


| ID |  | Task Name                                                              | Duration        | Start              | Finish             | 2018<br>H1 |
|----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 1  |                                                                                   | <b>UPDATED as of May 1, 2025</b>                                       |                 |                    |                    |            |
| 2  |                                                                                   | <b>SCE - Local RCI Solicitation</b>                                    | <b>679 days</b> | <b>Tue 8/21/18</b> | <b>Fri 3/26/21</b> |            |
| 3  |                                                                                   | SCE - RFA Preparation                                                  | 40 days         | Tue 8/21/18        | Mon 10/15/18       |            |
| 4  |                                                                                   | SCE - RFA Release                                                      | 1 day           | Fri 11/9/18        | Fri 11/9/18        |            |
| 5  |                                                                                   | SCE - RFA Abstract Creation Duration                                   | 30 days         | Sat 11/10/18       | Thu 12/20/18       |            |
| 6  |                                                                                   | SCE - RFA Evaluation                                                   | 82 days         | Fri 12/21/18       | Mon 4/15/19        |            |
| 7  |                                                                                   | SCE - RFA Review with EE PRG                                           | 1 day           | Tue 4/16/19        | Tue 4/16/19        |            |
| 8  |                                                                                   | SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 5/21/19        | Tue 5/21/19        |            |
| 9  |                                                                                   | SCE - RFP Preparation                                                  | 175 days        | Wed 5/22/19        | Tue 1/21/20        |            |
| 10 |                                                                                   | SCE - RFP Release                                                      | 1 day           | Wed 1/22/20        | Wed 1/22/20        |            |
| 11 |                                                                                   | SCE - RFP Proposal Creation Duration                                   | 25 days         | Thu 1/23/20        | Wed 2/26/20        |            |
| 12 |                                                                                   | SCE - RFP Evaluation                                                   | 38 days         | Thu 2/27/20        | Mon 4/20/20        |            |
| 13 |                                                                                   | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Thu 5/7/20         | Thu 5/7/20         |            |
| 14 |                                                                                   | SCE - RFP Review with EE PRG                                           | 1 day           | Tue 4/21/20        | Tue 4/21/20        |            |
| 15 |                                                                                   | SCE - Contract Negotiation and Development                             | 72 days         | Fri 5/8/20         | Mon 8/17/20        |            |
| 16 |                                                                                   | SCE - Contract Review with EE PRG                                      | 1 day           | Tue 8/18/20        | Tue 8/18/20        |            |
| 17 |                                                                                   | SCE - Final Award and Contract Signed                                  | 1 day           | Wed 9/30/20        | Wed 9/30/20        |            |
| 18 |                                                                                   | SCE - Submit Advice Letter                                             | 43 days         | Thu 10/1/20        | Mon 11/30/20       |            |
| 19 |                                                                                   | SCE - Advice Letter Approved                                           | 1 day           | Wed 12/30/20       | Wed 12/30/20       |            |
| 20 |                                                                                   | SCE - Implementation Plan                                              | 60 days         | Mon 1/4/21         | Fri 3/26/21        |            |
| 21 |                                                                                   | <b>SCE - SW Lighting</b>                                               | <b>518 days</b> | <b>Wed 4/3/19</b>  | <b>Fri 3/26/21</b> |            |
| 22 |                                                                                   | SCE - RFA Preparation                                                  | 55 days         | Wed 4/3/19         | Tue 6/18/19        |            |
| 23 |                                                                                   | SCE - RFA Release                                                      | 1 day           | Tue 7/2/19         | Tue 7/2/19         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID |  | Task Name                                                              | Duration        | Start              | Finish             | 2018<br>H1 |
|----|----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 24 |                                                                                  | SCE - RFA Abstract Creation Duration                                   | 20 days         | Wed 7/3/19         | Tue 7/30/19        |            |
| 25 |                                                                                  | SCE - RFA Evaluation                                                   | 34 days         | Wed 7/31/19        | Mon 9/16/19        |            |
| 26 |                                                                                  | SCE - RFA Review with EE PRG                                           | 1 day           | Tue 9/17/19        | Tue 9/17/19        |            |
| 27 |                                                                                  | SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 9/24/19        | Tue 9/24/19        |            |
| 28 |                                                                                  | SCE - RFP Preparation                                                  | 84 days         | Wed 9/25/19        | Mon 1/20/20        |            |
| 29 |                                                                                  | SCE - RFP Release                                                      | 1 day           | Thu 2/6/20         | Thu 2/6/20         |            |
| 30 |                                                                                  | SCE - RFP Proposal Creation Duration                                   | 27 days         | Fri 2/7/20         | Mon 3/16/20        |            |
| 31 |                                                                                  | SCE - RFP Evaluation                                                   | 25 days         | Tue 3/17/20        | Mon 4/20/20        |            |
| 32 |                                                                                  | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Thu 5/7/20         | Thu 5/7/20         |            |
| 33 |                                                                                  | SCE - RFP Review with EE PRG                                           | 1 day           | Tue 4/21/20        | Tue 4/21/20        |            |
| 34 |                                                                                  | SCE - Contract Negotiation and Development                             | 72 days         | Fri 5/8/20         | Mon 8/17/20        |            |
| 35 |                                                                                  | SCE - Contract Review with EE PRG                                      | 1 day           | Tue 8/18/20        | Tue 8/18/20        |            |
| 36 |                                                                                  | SCE - Final Award and Contract Signed                                  | 1 day           | Wed 9/30/20        | Wed 9/30/20        |            |
| 37 |                                                                                  | SCE - Submit Advice Letter                                             | 43 days         | Thu 10/1/20        | Mon 11/30/20       |            |
| 38 |                                                                                  | SCE - Advice Letter Approved                                           | 1 day           | Wed 12/23/20       | Wed 12/23/20       |            |
| 39 |                                                                                  | SCE - Implementation Plan                                              | 60 days         | Mon 1/4/21         | Fri 3/26/21        |            |
| 40 |                                                                                  | <b>SCE - Local Public Sector Solicitation</b>                          | <b>573 days</b> | <b>Mon 8/31/20</b> | <b>Wed 11/9/22</b> |            |
| 41 |                                                                                  | SCE - RFA Preparation                                                  | 33 days         | Mon 8/31/20        | Wed 10/14/20       |            |
| 42 |                                                                                  | SCE - RFA Release                                                      | 1 day           | Thu 11/5/20        | Thu 11/5/20        |            |
| 43 |                                                                                  | SCE - RFA Abstract Creation Duration                                   | 25 days         | Fri 11/6/20        | Thu 12/10/20       |            |
| 44 |                                                                                  | SCE - RFA Evaluation                                                   | 25 days         | Fri 12/11/20       | Thu 1/14/21        |            |
| 45 |                                                                                  | SCE - RFA Review with EE PRG                                           | 1 day           | Tue 1/19/21        | Tue 1/19/21        |            |
| 46 |                                                                                  | SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Thu 2/4/21         | Thu 2/4/21         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




| ID |  | Task Name                                                              | Duration        | Start              | Finish             | 2018<br>H1 |
|----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 47 |                                                                                   | SCE - RFP Preparation                                                  | 65 days         | Thu 12/10/20       | Wed 3/10/21        |            |
| 48 |                                                                                   | SCE - RFP Release                                                      | 1 day           | Thu 4/1/21         | Thu 4/1/21         |            |
| 49 |                                                                                   | SCE - RFP Proposal Creation Duration                                   | 30 days         | Fri 4/2/21         | Thu 5/13/21        |            |
| 50 |                                                                                   | SCE - RFP Evaluation                                                   | 20 days         | Fri 5/14/21        | Thu 6/10/21        |            |
| 51 |                                                                                   | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Mon 6/28/21        | Mon 6/28/21        |            |
| 52 |                                                                                   | SCE - RFP Review with EE PRG                                           | 1 day           | Tue 6/15/21        | Tue 6/15/21        |            |
| 53 |                                                                                   | SCE - Contract Negotiation and Development                             | 97 days         | Tue 6/29/21        | Wed 11/10/21       |            |
| 54 |                                                                                   | SCE - Contract Review with EE PRG                                      | 1 day           | Tue 11/16/21       | Tue 11/16/21       |            |
| 55 |                                                                                   | SCE - Final Award and Contract Signed                                  | 1 day           | Tue 12/14/21       | Tue 12/14/21       |            |
| 56 |                                                                                   | SCE - Submit Advice Letter                                             | 37 days         | Wed 12/15/21       | Thu 2/3/22         |            |
| 57 |                                                                                   | SCE - Submit Advice Letter                                             | 48 days         | Wed 12/15/21       | Fri 2/18/22        |            |
| 58 |                                                                                   | SCE - Advice Letter Approved                                           | 1 day           | Thu 8/18/22        | Thu 8/18/22        |            |
| 59 |                                                                                   | SCE - Implementation Plan                                              | 60 days         | Thu 8/18/22        | Wed 11/9/22        |            |
| 60 |                                                                                   | <b>SCE - Local Agriculture Solicitation</b>                            | <b>512 days</b> | <b>Mon 8/31/20</b> | <b>Tue 8/16/22</b> |            |
| 61 |                                                                                   | SCE - RFA Preparation                                                  | 33 days         | Mon 8/31/20        | Wed 10/14/20       |            |
| 62 |                                                                                   | SCE - RFA Release                                                      | 1 day           | Thu 11/5/20        | Thu 11/5/20        |            |
| 63 |                                                                                   | SCE - RFA Abstract Creation Duration                                   | 25 days         | Fri 11/6/20        | Thu 12/10/20       |            |
| 64 |                                                                                   | SCE - RFA Evaluation                                                   | 25 days         | Fri 12/11/20       | Thu 1/14/21        |            |
| 65 |                                                                                   | SCE - RFA Review with EE PRG                                           | 1 day           | Tue 1/19/21        | Tue 1/19/21        |            |
| 66 |                                                                                   | SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Thu 2/4/21         | Thu 2/4/21         |            |
| 67 |                                                                                   | SCE - RFP Preparation                                                  | 65 days         | Thu 12/10/20       | Wed 3/10/21        |            |
| 68 |                                                                                   | SCE - RFP Release                                                      | 1 day           | Thu 4/1/21         | Thu 4/1/21         |            |
| 69 |                                                                                   | SCE - RFP Proposal Creation Duration                                   | 30 days         | Fri 4/2/21         | Thu 5/13/21        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID |  | Task Name                                                              | Duration        | Start               | Finish              | 2018<br>H1 |
|----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|---------------------|---------------------|------------|
| 70 |                                                                                   | SCE - RFP Evaluation                                                   | 20 days         | Fri 5/14/21         | Thu 6/10/21         |            |
| 71 |                                                                                   | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Mon 6/28/21         | Mon 6/28/21         |            |
| 72 |                                                                                   | SCE - RFP Review with EE PRG                                           | 1 day           | Tue 6/15/21         | Tue 6/15/21         |            |
| 73 |                                                                                   | SCE - Contract Negotiation and Development                             | 97 days         | Tue 6/29/21         | Wed 11/10/21        |            |
| 74 |                                                                                   | SCE - Final Award and Contract Signed                                  | 1 day           | Mon 12/20/21        | Mon 12/20/21        |            |
| 75 |                                                                                   | SCE - Submit Advice Letter                                             | 33 days         | Tue 12/21/21        | Thu 2/3/22          |            |
| 76 |                                                                                   | SCE - Contract Review with EE PRG                                      | 1 day           | Tue 11/16/21        | Tue 11/16/21        |            |
| 77 |                                                                                   | SCE - Final Award and Contract Signed                                  | 1 day           | Wed 12/15/21        | Wed 12/15/21        |            |
| 78 |                                                                                   | SCE - Submit Advice Letter                                             | 56 days         | Thu 12/16/21        | Thu 3/3/22          |            |
| 79 |                                                                                   | SCE - Advice Letter Approved                                           | 1 day           | Fri 4/22/22         | Fri 4/22/22         |            |
| 80 |                                                                                   | SCE - Implementation Plan                                              | 60 days         | Sat 4/23/22         | Thu 7/14/22         |            |
| 81 |                                                                                   | <b>SCE - SW Water/Wastewater Solicitation</b>                          | <b>522 days</b> | <b>Mon 11/16/20</b> | <b>Tue 11/15/22</b> |            |
| 82 |                                                                                   | SCE - RFA Preparation                                                  | 70 days         | Mon 11/16/20        | Fri 2/19/21         |            |
| 83 |                                                                                   | SCE - RFA Release                                                      | 1 day           | Thu 3/4/21          | Thu 3/4/21          |            |
| 84 |                                                                                   | SCE - RFA Abstract Creation Duration                                   | 29 days         | Thu 3/4/21          | Tue 4/13/21         |            |
| 85 |                                                                                   | SCE - RFA Evaluation                                                   | 20 days         | Wed 4/14/21         | Tue 5/11/21         |            |
| 86 |                                                                                   | SCE - RFA Review with EE PRG                                           | 1 day           | Tue 5/18/21         | Tue 5/18/21         |            |
| 87 |                                                                                   | SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Thu 5/27/21         | Thu 5/27/21         |            |
| 88 |                                                                                   | SCE - RFP Preparation                                                  | 34 days         | Mon 4/19/21         | Thu 6/3/21          |            |
| 89 |                                                                                   | SCE - RFP Release                                                      | 1 day           | Thu 7/1/21          | Thu 7/1/21          |            |
| 90 |                                                                                   | SCE - RFP Proposal Creation Duration                                   | 25 days         | Fri 7/2/21          | Thu 8/5/21          |            |
| 91 |                                                                                   | SCE - RFP Evaluation                                                   | 41 days         | Fri 8/6/21          | Fri 10/1/21         |            |
| 92 |                                                                                   | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 10/26/21        | Tue 10/26/21        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration        | Start             | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|-------------------|--------------------|------------|
| 93  |                                                                                   | SCE - RFP Review with EE PRG                                           | 1 day           | Tue 10/19/21      | Tue 10/19/21       |            |
| 94  |                                                                                   | SCE - Contract Negotiation and Development                             | 94 days         | Wed 10/27/21      | Mon 3/7/22         |            |
| 95  |                                                                                   | SCE - Contract Review with EE PRG                                      | 1 day           | Tue 3/15/22       | Tue 3/15/22        |            |
| 96  |                                                                                   | SCE - Final Award and Contract Signed                                  | 1 day           | Tue 4/19/22       | Tue 4/19/22        |            |
| 97  |                                                                                   | SCE - Submit Advice Letter                                             | 40 days         | Wed 4/20/22       | Tue 6/14/22        |            |
| 98  |                                                                                   | SCE - Advice Letter Approved                                           | 26 days         | Wed 6/15/22       | Wed 7/20/22        |            |
| 99  |                                                                                   | SCE - Implementation Plan                                              | 44 days         | Thu 7/21/22       | Tue 9/20/22        |            |
| 100 |                                                                                   | <b>SCE - SW ETP Solicitation</b>                                       | <b>466 days</b> | <b>Fri 5/1/20</b> | <b>Fri 2/11/22</b> |            |
| 101 |                                                                                   | SCE - RFA Preparation                                                  | 57 days         | Fri 5/1/20        | Mon 7/20/20        |            |
| 102 |                                                                                   | SCE - RFA Release                                                      | 1 day           | Tue 8/4/20        | Tue 8/4/20         |            |
| 103 |                                                                                   | SCE - RFA Abstract Creation Duration                                   | 24 days         | Fri 8/7/20        | Wed 9/9/20         |            |
| 104 |                                                                                   | SCE - RFA Evaluation                                                   | 16 days         | Thu 9/10/20       | Thu 10/1/20        |            |
| 105 |                                                                                   | SCE - RFA Review with EE PRG                                           | 1 day           | Tue 10/20/20      | Tue 10/20/20       |            |
| 106 |                                                                                   | SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 10/27/20      | Tue 10/27/20       |            |
| 107 |                                                                                   | SCE - RFP Preparation                                                  | 42 days         | Tue 9/8/20        | Wed 11/4/20        |            |
| 108 |                                                                                   | SCE - RFP Release                                                      | 1 day           | Tue 1/5/21        | Tue 1/5/21         |            |
| 109 |                                                                                   | SCE - RFP Proposal Creation Duration                                   | 37 days         | Tue 1/5/21        | Wed 2/24/21        |            |
| 110 |                                                                                   | SCE - RFP Evaluation                                                   | 28 days         | Wed 2/24/21       | Fri 4/2/21         |            |
| 111 |                                                                                   | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 4/27/21       | Tue 4/27/21        |            |
| 112 |                                                                                   | SCE - RFP Review with EE PRG                                           | 1 day           | Tue 4/20/21       | Tue 4/20/21        |            |
| 113 |                                                                                   | SCE - Contract Negotiation and Development                             | 69 days         | Wed 4/21/21       | Mon 7/26/21        |            |
| 114 |                                                                                   | SCE - Contract Review with EE PRG                                      | 1 day           | Tue 8/17/21       | Tue 8/17/21        |            |
| 115 |                                                                                   | SCE - Final Award and Contract Signed                                  | 1 day           | Tue 9/14/21       | Tue 9/14/21        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration         | Start              | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------|--------------------|--------------------|------------|
| 116 |                                                                                   | SCE - Submit Advice Letter                                             | 18 days          | Wed 9/15/21        | Fri 10/8/21        |            |
| 117 |                                                                                   | SCE - Advice Letter Approved                                           | 1 day            | Tue 11/9/21        | Tue 11/9/21        |            |
| 118 |                                                                                   | SCE - Implementation Plan                                              | 60 days          | Wed 11/10/21       | Tue 2/1/22         |            |
| 119 |                                                                                   | <b>SCE - SW Higher-Education Solicitation</b>                          | <b>547 days?</b> | <b>Thu 10/1/20</b> | <b>Fri 11/4/22</b> |            |
| 120 |                                                                                   | SCE - RFA Preparation                                                  | 89 days          | Thu 10/1/20        | Tue 2/2/21         |            |
| 121 |                                                                                   | SCE - RFA Release                                                      | 1 day            | Thu 2/4/21         | Thu 2/4/21         |            |
| 122 |                                                                                   | SCE - RFA Abstract Creation Duration                                   | 19 days          | Fri 2/5/21         | Wed 3/3/21         |            |
| 123 |                                                                                   | SCE - RFA Evaluation                                                   | 31 days          | Thu 3/4/21         | Thu 4/15/21        |            |
| 124 |                                                                                   | SCE - RFA Review with EE PRG                                           | 1 day            | Tue 4/20/21        | Tue 4/20/21        |            |
| 125 |                                                                                   | SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Thu 4/29/21        | Thu 4/29/21        |            |
| 126 |                                                                                   | SCE - RFP Preparation                                                  | 39 days          | Mon 3/22/21        | Thu 5/13/21        |            |
| 127 |                                                                                   | SCE - RFP Release                                                      | 1 day            | Fri 5/28/21        | Fri 5/28/21        |            |
| 128 |                                                                                   | SCE - RFP Proposal Creation Duration                                   | 24 days          | Fri 6/4/21         | Wed 7/7/21         |            |
| 129 |                                                                                   | SCE - RFP Evaluation                                                   | 26 days          | Thu 7/8/21         | Thu 8/12/21        |            |
| 130 |                                                                                   | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Mon 8/30/21        | Mon 8/30/21        |            |
| 131 |                                                                                   | SCE - RFP Review with EE PRG                                           | 1 day            | Tue 8/17/21        | Tue 8/17/21        |            |
| 132 |                                                                                   | SCE - Contract Negotiation and Development                             | 95 days          | Fri 9/3/21         | Thu 1/13/22        |            |
| 133 |                                                                                   | SCE - Contract Review with EE PRG                                      | 1 day            | Tue 1/18/22        | Tue 1/18/22        |            |
| 134 |                                                                                   | SCE - Final Award and Contract Signed                                  | 1 day            | Sun 3/6/22         | Sun 3/6/22         |            |
| 135 |                                                                                   | SCE - Submit Advice Letter                                             | 1 day            | Tue 4/19/22        | Tue 4/19/22        |            |
| 136 |                                                                                   | SCE - Advice Letter Approved                                           | 1 day            | Mon 8/15/22        | Mon 8/15/22        |            |
| 137 |                                                                                   | SCE - Implementation Plan                                              | 60 days          | Mon 8/15/22        | Fri 11/4/22        |            |
| 138 |                                                                                   | <b>SCE - Local Equity Residential and SMB</b>                          | <b>384 days?</b> | <b>Tue 2/15/22</b> | <b>Fri 8/4/23</b>  |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration         | Start              | Finish              | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------|--------------------|---------------------|------------|
| 139 |                                                                                   | SCE - RFA Preparation                                                  | 35 days          | Tue 2/15/22        | Mon 4/4/22          |            |
| 140 |                                                                                   | SCE - RFA Release                                                      | 1 day            | Tue 4/5/22         | Tue 4/5/22          |            |
| 141 |                                                                                   | SCE - RFA Abstract Creation Duration                                   | 20 days          | Tue 4/5/22         | Mon 5/2/22          |            |
| 142 |                                                                                   | SCE - RFA Evaluation                                                   | 14 days          | Mon 5/9/22         | Thu 5/26/22         |            |
| 143 |                                                                                   | SCE - RFA Review with EE PRG                                           | 1 day            | Tue 5/31/22        | Tue 5/31/22         |            |
| 144 |                                                                                   | SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 6/7/22         | Tue 6/7/22          |            |
| 145 |                                                                                   | SCE - RFP Preparation                                                  | 62 days          | Mon 4/4/22         | Tue 6/28/22         |            |
| 146 |                                                                                   | SCE - RFP Release                                                      | 1 day            | Wed 6/29/22        | Wed 6/29/22         |            |
| 147 |                                                                                   | SCE - RFP Proposal Creation Duration                                   | 20 days          | Wed 6/29/22        | Tue 7/26/22         |            |
| 148 |                                                                                   | SCE - RFP Evaluation                                                   | 47 days          | Wed 7/27/22        | Thu 9/29/22         |            |
| 149 |                                                                                   | SCE - RFP Review with EE PRG                                           | 1 day?           | Tue 10/18/22       | Tue 10/18/22        |            |
| 150 |                                                                                   | RFP Estimated Notification of Successful and Unsuccessful Bidder       | 1 day            | Tue 11/1/22        | Tue 11/1/22         |            |
| 151 |                                                                                   | SCE - Contract Negotiation and Development                             | 65 days          | Wed 11/2/22        | Tue 1/31/23         |            |
| 152 |                                                                                   | SCE - Contract Review with EE PRG                                      | 1 day            | Tue 2/21/23        | Tue 2/21/23         |            |
| 153 |                                                                                   | SCE - Final Award and Contract Signed                                  | 1 day            | Thu 3/30/23        | Thu 3/30/23         |            |
| 154 |                                                                                   | SCE - Submit Advice Letter                                             | 22 days          | Sun 4/3/22         | Mon 5/2/22          |            |
| 155 |                                                                                   | SCE - Advice Letter Approved                                           | 28 days          | Tue 5/2/23         | Thu 6/8/23          |            |
| 156 |                                                                                   | SCE - Implementation Plan                                              | 45 days          | Thu 6/8/23         | Wed 8/9/23          |            |
| 157 |                                                                                   |                                                                        |                  |                    |                     |            |
| 158 |                                                                                   | <b>SCE - Local Equity SMB</b>                                          | <b>431 days?</b> | <b>Tue 2/15/22</b> | <b>Tue 10/10/23</b> |            |
| 159 |                                                                                   | SCE - RFA Preparation                                                  | 35 days          | Tue 2/15/22        | Mon 4/4/22          |            |
| 160 |                                                                                   | SCE - RFA Release                                                      | 1 day            | Tue 4/5/22         | Tue 4/5/22          |            |
| 161 |                                                                                   | SCE - RFA Abstract Creation Duration                                   | 20 days          | Tue 4/5/22         | Mon 5/2/22          |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration         | Start              | Finish            | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------|--------------------|-------------------|------------|
| 162 |                                                                                   | SCE - RFA Evaluation                                                   | 14 days          | Mon 5/9/22         | Thu 5/26/22       |            |
| 163 |                                                                                   | SCE - RFA Review with EE PRG                                           | 1 day            | Tue 5/31/22        | Tue 5/31/22       |            |
| 164 |                                                                                   | SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 6/7/22         | Tue 6/7/22        |            |
| 165 |                                                                                   | SCE - RFP Preparation                                                  | 62 days          | Mon 4/4/22         | Tue 6/28/22       |            |
| 166 |                                                                                   | SCE - RFP Release                                                      | 1 day            | Wed 6/29/22        | Wed 6/29/22       |            |
| 167 |                                                                                   | SCE - RFP Proposal Creation Duration                                   | 20 days          | Wed 6/29/22        | Tue 7/26/22       |            |
| 168 |                                                                                   | SCE - RFP Evaluation                                                   | 47 days          | Wed 7/27/22        | Thu 9/29/22       |            |
| 169 |                                                                                   | SCE - RFP Review with EE PRG                                           | 1 day?           | Tue 10/18/22       | Tue 10/18/22      |            |
| 170 |                                                                                   | RFP Estimated Notification of Successful and Unsuccessful Bidder       | 1 day            | Tue 11/1/22        | Tue 11/1/22       |            |
| 171 |                                                                                   | SCE - Contract Negotiation and Development                             | 108 days         | Wed 11/2/22        | Fri 3/31/23       |            |
| 172 |                                                                                   | SCE - Contract Review with EE PRG                                      | 1 day            | Tue 4/18/23        | Tue 4/18/23       |            |
| 173 |                                                                                   | SCE - Final Award and Contract Signed                                  | 1 day            | Wed 5/31/23        | Wed 5/31/23       |            |
| 174 |                                                                                   | SCE - Submit Advice Letter                                             | 22 days          | Mon 6/6/22         | Tue 7/5/22        |            |
| 175 |                                                                                   | SCE - Advice Letter Approved                                           | 24 days          | Thu 7/6/23         | Tue 8/8/23        |            |
| 176 |                                                                                   | SCE - Implementation Plan                                              | 45 days          | Wed 8/9/23         | Tue 10/10/23      |            |
| 177 |                                                                                   | <b>SCE - Local Strategic Energy Management Solicitation</b>            | <b>372 days?</b> | <b>Thu 12/1/22</b> | <b>Fri 5/3/24</b> |            |
| 178 |                                                                                   | SCE - RFP Preparation                                                  | 85 days          | Thu 12/1/22        | Wed 3/29/23       |            |
| 179 |                                                                                   | SCE - RFP Release                                                      | 1 day            | Fri 4/7/23         | Fri 4/7/23        |            |
| 180 |                                                                                   | SCE - RFP Proposal Creation Duration                                   | 35 days          | Fri 4/7/23         | Thu 5/25/23       |            |
| 181 |                                                                                   | SCE - RFP Evaluation                                                   | 22 days          | Thu 6/1/23         | Fri 6/30/23       |            |
| 182 |                                                                                   | SCE - RFP Review with EE PRG                                           | 1 day            | Tue 7/18/23        | Tue 7/18/23       |            |
| 183 |                                                                                   | SCE - Contract Negotiation and Development                             | 86 days          | Tue 8/1/23         | Tue 11/28/23      |            |
| 184 |                                                                                   | SCE - Contract Review with EE PRG                                      | 1 day            | Tue 12/19/23       | Tue 12/19/23      |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration         | Start              | Finish              | 2018<br>H1 |
|-----|----------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------|--------------------|---------------------|------------|
| 185 |                                                                                  | SCE - Final Award and Contract Signed                                  | 6 days           | Fri 1/19/24        | Fri 1/26/24         |            |
| 186 |                                                                                  | SCE - Submit Advice Letter                                             | 34 days          | Wed 1/31/24        | Mon 3/18/24         |            |
| 187 |                                                                                  | SCE - Advice Letter Approved                                           | 40 days          | Tue 3/19/24        | Mon 5/13/24         |            |
| 188 |                                                                                  | <b>SCE - Local Large Commercial Solicitation</b>                       | <b>488 days?</b> | <b>Mon 6/26/23</b> | <b>Wed 5/7/25</b>   |            |
| 189 |                                                                                  | SCE - RFP Preparation                                                  | 35 days          | Mon 6/26/23        | Fri 8/11/23         |            |
| 190 |                                                                                  | SCE - RFP Release                                                      | 1 day            | Thu 8/17/23        | Thu 8/17/23         |            |
| 191 |                                                                                  | SCE - RFP Proposal Creation Duration                                   | 41 days          | Thu 8/17/23        | Thu 10/12/23        |            |
| 192 |                                                                                  | SCE - RFP Paused                                                       | 1 day            | Fri 10/13/23       | Fri 10/13/23        |            |
| 193 |                                                                                  | <b>SCE - Residential Multifamily</b>                                   | <b>326 days?</b> | <b>Fri 9/1/23</b>  | <b>Fri 11/29/24</b> |            |
| 194 |                                                                                  | SCE - RFP Preparation                                                  | 47 days          | Fri 9/1/23         | Mon 11/6/23         |            |
| 195 |                                                                                  | SCE - RFP Release                                                      | 1 day            | Mon 11/6/23        | Mon 11/6/23         |            |
| 196 |                                                                                  | SCE - RFP Proposal Creation Duration                                   | 48 days          | Mon 11/6/23        | Wed 1/10/24         |            |
| 197 |                                                                                  | SCE - RFP Evaluation                                                   | 25 days          | Thu 1/11/24        | Wed 2/14/24         |            |
| 198 |                                                                                  | SCE - RFP Review with EE PRG                                           | 1 day            | Tue 2/20/24        | Tue 2/20/24         |            |
| 199 |                                                                                  | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Wed 2/28/24        | Wed 2/28/24         |            |
| 200 |                                                                                  | SCE - Contract Negotiation and Development                             | 70 days          | Mon 3/4/24         | Fri 6/7/24          |            |
| 201 |                                                                                  | SCE - Contract Review with EE PRG                                      | 1 day            | Tue 7/16/24        | Tue 7/16/24         |            |
| 202 |                                                                                  | SCE - Final Award and Contract Signed                                  | 15 days          | Mon 7/29/24        | Fri 8/16/24         |            |
| 203 |                                                                                  | SCE - Submit Advice Letter                                             | 30 days          | Mon 8/19/24        | Fri 9/27/24         |            |
| 204 |                                                                                  | SCE - Advice Letter Approved                                           | 1 day            | Mon 10/28/24       | Mon 10/28/24        |            |
| 205 |                                                                                  | <b>SCE - Local Large Industrial</b>                                    | <b>442 days</b>  | <b>Fri 11/3/23</b> | <b>Mon 7/14/25</b>  |            |
| 206 |                                                                                  | SCE - RFP Preparation                                                  | 17 days          | Fri 11/3/23        | Mon 11/27/23        |            |
| 207 |                                                                                  | SCE - RFP Release                                                      | 1 day            | Mon 12/11/23       | Mon 12/11/23        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration         | Start               | Finish            | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------|---------------------|-------------------|------------|
| 208 |                                                                                   | SCE - RFP Proposal Creation Duration                                   | 49 days          | Mon 12/11/23        | Thu 2/15/24       |            |
| 209 |                                                                                   | SCE - RFP Evaluation                                                   | 35 days          | Fri 2/16/24         | Thu 4/4/24        |            |
| 210 |                                                                                   | SCE - RFP Review with EE PRG                                           | 1 day            | Tue 4/16/24         | Tue 4/16/24       |            |
| 211 |                                                                                   | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 4/23/24         | Tue 4/23/24       |            |
| 212 |                                                                                   | SCE - Contract Negotiation and Development                             | 208 days         | Wed 4/24/24         | Fri 2/7/25        |            |
| 213 |                                                                                   | SCE - Contract Review with EE PRG                                      | 1 day            | Tue 4/29/25         | Tue 4/29/25       |            |
| 214 |                                                                                   | SCE - Final Award and Contract Signed                                  | 22 days          | Thu 5/1/25          | Fri 5/30/25       |            |
| 215 |                                                                                   | SCE - Submit Advice Letter                                             | 45 days          | Mon 6/2/25          | Fri 8/1/25        |            |
| 216 |                                                                                   | SCE - Advice Letter Approved                                           | 22 days          | Mon 8/4/25          | Tue 9/2/25        |            |
| 217 |                                                                                   | <b>SCE - MAP - All Sectors</b>                                         | <b>299 days?</b> | <b>Mon 11/20/23</b> | <b>Thu 1/9/25</b> |            |
| 218 |                                                                                   | SCE - RFP Preparation                                                  | 20 days          | Mon 11/20/23        | Fri 12/15/23      |            |
| 219 |                                                                                   | SCE - RFP Release                                                      | 1 day            | Mon 1/8/24          | Mon 1/8/24        |            |
| 220 |                                                                                   | SCE - RFP Proposal Creation Duration                                   | 40 days          | Mon 1/8/24          | Fri 3/1/24        |            |
| 221 |                                                                                   | SCE - RFP Evaluation                                                   | 30 days          | Mon 3/4/24          | Fri 4/12/24       |            |
| 222 |                                                                                   | SCE - RFP Review with EE PRG                                           | 1 day            | Tue 4/16/24         | Tue 4/16/24       |            |
| 223 |                                                                                   | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Wed 4/24/24         | Wed 4/24/24       |            |
| 224 |                                                                                   | SCE - Contract Negotiation and Development                             | 108 days         | Wed 5/1/24          | Fri 9/27/24       |            |
| 225 |                                                                                   | SCE - Contract Review with EE PRG                                      | 1 day            | Tue 10/15/24        | Tue 10/15/24      |            |
| 226 |                                                                                   | SCE - Final Award and Contract Signed                                  | 12 days          | Tue 10/29/24        | Wed 11/13/24      |            |
| 227 |                                                                                   | SCE - Submit Advice Letter                                             | 43 days          | Wed 11/13/24        | Fri 1/10/25       |            |
| 228 |                                                                                   | SCE - Advice Letter Approved                                           | 22 days          | Mon 1/13/25         | Tue 2/11/25       |            |
| 229 |                                                                                   | <b>SCE - Residential</b>                                               | <b>360 days?</b> | <b>Mon 11/20/23</b> | <b>Fri 4/4/25</b> |            |
| 230 |                                                                                   | SCE - RFP Preparation                                                  | 20 days          | Tue 1/16/24         | Mon 2/12/24       |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                        | Duration         | Start               | Finish            | 2018<br>H1 |
|-----|----------------------------------------------------------------------------------|----------------------------------------------------------------------------------|------------------|---------------------|-------------------|------------|
| 231 |                                                                                  | SCE - RFP Release                                                                | 1 day            | Thu 3/28/24         | Thu 3/28/24       |            |
| 232 |                                                                                  | SCE - RFP Proposal Creation Duration                                             | 41 days          | Thu 3/28/24         | Thu 5/23/24       |            |
| 233 |                                                                                  | SCE - RFP Evaluation                                                             | 35 days          | Fri 5/24/24         | Thu 7/11/24       |            |
| 234 |                                                                                  | SCE - RFP Review with EE PRG                                                     | 1 day            | Tue 7/16/24         | Tue 7/16/24       |            |
| 235 |                                                                                  | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder           | 1 day            | Mon 8/5/24          | Mon 8/5/24        |            |
| 236 |                                                                                  | SCE - Contract Negotiation and Development                                       | 80 days          | Mon 8/19/24         | Fri 12/6/24       |            |
| 237 |                                                                                  | SCE - Contract Review with EE PRG                                                | 1 day            | Tue 12/17/24        | Tue 12/17/24      |            |
| 238 |                                                                                  | SCE - Final Award and Contract Signed                                            | 11 days          | Mon 1/13/25         | Mon 1/27/25       |            |
| 239 |                                                                                  | SCE - Submit Advice Letter                                                       | 19 days          | Mon 2/3/25          | Thu 2/27/25       |            |
| 240 |                                                                                  | SCE - Advice Letter Approved                                                     | 1 day            | Tue 4/1/25          | Tue 4/1/25        |            |
| 241 |                                                                                  |                                                                                  |                  |                     |                   |            |
| 242 |                                                                                  | <b>SCE - Local Comprehensive Commercial Solicitation</b>                         | <b>431 days?</b> | <b>Mon 11/13/23</b> | <b>Mon 7/7/25</b> |            |
| 243 |                                                                                  | SCE - RFP Preparation                                                            | 73 days          | Mon 11/13/23        | Wed 2/21/24       |            |
| 244 |                                                                                  | SCE - RFP Release                                                                | 1 day            | Wed 2/28/24         | Wed 2/28/24       |            |
| 245 |                                                                                  | SCE - RFP Proposal Creation Duration                                             | 43 days          | Thu 2/29/24         | Mon 4/29/24       |            |
| 246 |                                                                                  | SCE - RFP Evaluation                                                             | 54 days          | Tue 4/30/24         | Fri 7/12/24       |            |
| 247 |                                                                                  | SCE - RFP Review with EE PRG                                                     | 1 day            | Tue 7/16/24         | Tue 7/16/24       |            |
| 248 |                                                                                  | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Phase 1 | 1 day            | Mon 7/29/24         | Mon 7/29/24       |            |
| 249 |                                                                                  | SCE - Contract Negotiation and Development - Phase 1                             | 81 days          | Tue 7/30/24         | Tue 11/19/24      |            |
| 250 |                                                                                  | SCE - Contract Review with EE PRG - Phase 1                                      | 1 day            | Tue 12/17/24        | Tue 12/17/24      |            |
| 251 |                                                                                  | SCE - Final Award and Contract Signed - Phase 1                                  | 1 day            | Tue 1/28/25         | Tue 1/28/25       |            |
| 252 |                                                                                  | SCE - Submit Advice Letter - Phase 1                                             | 23 days          | Tue 1/28/25         | Thu 2/27/25       |            |
| 253 |                                                                                  | SCE - Advice Letter Approved - Phase 1                                           | 1 day            | Tue 4/1/25          | Tue 4/1/25        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                        | Duration        | Start             | Finish            | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|----------------------------------------------------------------------------------|-----------------|-------------------|-------------------|------------|
| 254 |                                                                                   | SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Phase 1 | 1 day           | Mon 9/30/24       | Mon 9/30/24       |            |
| 255 |                                                                                   | SCE - Contract Negotiation and Development - Phase 2                             | 80 days         | Mon 12/2/24       | Fri 3/21/25       |            |
| 256 |                                                                                   | SCE - Contract Review with EE PRG - Phase 2                                      | 1 day           | Tue 4/29/25       | Tue 4/29/25       |            |
| 257 |                                                                                   | SCE - Final Award and Contract Signed - Phase 2                                  | 1 day           | Fri 5/30/25       | Fri 5/30/25       |            |
| 258 |                                                                                   | SCE - Submit Advice Letter - Phase 2                                             | 0 days          | N/A               | N/A               |            |
| 259 |                                                                                   | SCE - Advice Letter Approved - Phase 2                                           | 0 days          | N/A               | N/A               |            |
| 260 |                                                                                   |                                                                                  |                 |                   |                   |            |
| 261 |                                                                                   | <b>SCG - Local Single Family Solicitation</b>                                    | <b>660 days</b> | <b>Sun 7/1/18</b> | <b>Thu 1/7/21</b> |            |
| 262 |                                                                                   | SCG - RFA Preparation                                                            | 105 days        | Sun 7/1/18        | Thu 11/22/18      |            |
| 263 |                                                                                   | SCG - RFA Release                                                                | 1 day           | Mon 11/26/18      | Mon 11/26/18      |            |
| 264 |                                                                                   | SCG - RFA Abstract Creation Duration                                             | 30 days         | Tue 11/27/18      | Mon 1/7/19        |            |
| 265 |                                                                                   | SCG - RFA Evaluation                                                             | 39 days         | Mon 1/7/19        | Thu 2/28/19       |            |
| 266 |                                                                                   | SCG - RFA Review with EE PRG                                                     | 1 day           | Tue 3/5/19        | Tue 3/5/19        |            |
| 267 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder           | 1 day           | Mon 6/3/19        | Mon 6/3/19        |            |
| 268 |                                                                                   | SCG - RFP Preparation                                                            | 146 days        | Wed 1/2/19        | Wed 7/24/19       |            |
| 269 |                                                                                   | SCG - RFP Release                                                                | 1 day           | Wed 7/31/19       | Wed 7/31/19       |            |
| 270 |                                                                                   | SCG - RFP Proposal Creation Duration                                             | 30 days         | Thu 8/1/19        | Wed 9/11/19       |            |
| 271 |                                                                                   | SCG - RFP Evaluation                                                             | 37 days         | Wed 9/11/19       | Thu 10/31/19      |            |
| 272 |                                                                                   | SCG - RFP Review with EE PRG                                                     | 1 day           | Tue 11/5/19       | Tue 11/5/19       |            |
| 273 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder           | 1 day           | Tue 1/21/20       | Tue 1/21/20       |            |
| 274 |                                                                                   | SCG - Contract Negotiation and Development                                       | 69 days         | Mon 1/27/20       | Thu 4/30/20       |            |
| 275 |                                                                                   | SCG - Contract Review with EE PRG                                                | 14 days         | Tue 5/5/20        | Fri 5/22/20       |            |
| 276 |                                                                                   | SCG - Final Award and Contract Signed                                            | 8 days          | Mon 5/25/20       | Wed 6/3/20        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration        | Start             | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|-------------------|--------------------|------------|
| 277 |                                                                                   | SCG - Submit Advice Letter                                             | 96 days         | Mon 6/1/20        | Mon 10/12/20       |            |
| 278 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day           | Thu 11/12/20      | Thu 11/12/20       |            |
| 279 |                                                                                   | SCG - Implementation Plan                                              | 41 days         | Fri 11/13/20      | Fri 1/8/21         |            |
| 280 |                                                                                   | <b>SCG - Local Multi-family Solicitation</b>                           | <b>735 days</b> | <b>Sun 7/1/18</b> | <b>Thu 4/22/21</b> |            |
| 281 |                                                                                   | SCG - RFA Preparation                                                  | 105 days        | Sun 7/1/18        | Thu 11/22/18       |            |
| 282 |                                                                                   | SCG - RFA Release                                                      | 1 day           | Mon 11/26/18      | Mon 11/26/18       |            |
| 283 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 30 days         | Tue 11/27/18      | Mon 1/7/19         |            |
| 284 |                                                                                   | SCG - RFA Evaluation                                                   | 59 days         | Mon 1/7/19        | Thu 3/28/19        |            |
| 285 |                                                                                   | SCG - RFA Review with EE PRG                                           | 1 day           | Tue 4/2/19        | Tue 4/2/19         |            |
| 286 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Mon 6/3/19        | Mon 6/3/19         |            |
| 287 |                                                                                   | SCG - RFP Preparation                                                  | 146 days        | Wed 1/2/19        | Wed 7/24/19        |            |
| 288 |                                                                                   | SCG - RFP Release                                                      | 1 day           | Wed 7/31/19       | Wed 7/31/19        |            |
| 289 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 30 days         | Thu 8/1/19        | Wed 9/11/19        |            |
| 290 |                                                                                   | SCG - RFP Evaluation                                                   | 37 days         | Wed 9/11/19       | Thu 10/31/19       |            |
| 291 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day           | Tue 11/5/19       | Tue 11/5/19        |            |
| 292 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 1/21/20       | Tue 1/21/20        |            |
| 293 |                                                                                   | SCG - Contract Negotiation and Development                             | 155 days        | Mon 1/27/20       | Fri 8/28/20        |            |
| 294 |                                                                                   | SCG - Contract Review with EE PRG                                      | 99 days         | Tue 5/5/20        | Fri 9/18/20        |            |
| 295 |                                                                                   | SCG - Final Award and Contract Signed                                  | 8 days          | Mon 9/21/20       | Wed 9/30/20        |            |
| 296 |                                                                                   | SCG - Submit Advice Letter                                             | 37 days         | Thu 10/1/20       | Fri 11/20/20       |            |
| 297 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day           | Sun 5/2/21        | Sun 5/2/21         |            |
| 298 |                                                                                   | SCG - Implementation Plan                                              | 51 days         | Mon 5/3/21        | Mon 7/12/21        |            |
| 299 |                                                                                   | <b>SCG - Local Small/Medium Commercial Solicitation</b>                | <b>641 days</b> | <b>Tue 9/4/18</b> | <b>Tue 2/16/21</b> |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration        | Start             | Finish            | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|-------------------|-------------------|------------|
| 300 |                                                                                   | SCG - RFA Preparation                                                  | 104 days        | Tue 9/4/18        | Fri 1/25/19       |            |
| 301 |                                                                                   | SCG - RFA Release                                                      | 1 day           | Thu 1/31/19       | Thu 1/31/19       |            |
| 302 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 30 days         | Fri 2/1/19        | Thu 3/14/19       |            |
| 303 |                                                                                   | SCG - RFA Evaluation                                                   | 52 days         | Thu 3/14/19       | Fri 5/24/19       |            |
| 304 |                                                                                   | SCG - RFA Review with EE PRG                                           | 1 day           | Tue 6/4/19        | Tue 6/4/19        |            |
| 305 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Thu 8/1/19        | Thu 8/1/19        |            |
| 306 |                                                                                   | SCG - RFP Preparation                                                  | 37 days         | Wed 7/3/19        | Thu 8/22/19       |            |
| 307 |                                                                                   | SCG - RFP Release                                                      | 1 day           | Fri 8/23/19       | Fri 8/23/19       |            |
| 308 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 31 days         | Mon 8/26/19       | Mon 10/7/19       |            |
| 309 |                                                                                   | SCG - RFP Evaluation                                                   | 36 days         | Tue 10/8/19       | Tue 11/26/19      |            |
| 310 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day           | Tue 12/3/19       | Tue 12/3/19       |            |
| 311 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 1/21/20       | Tue 1/21/20       |            |
| 312 |                                                                                   | SCG - Contract Negotiation and Development                             | 135 days        | Mon 1/27/20       | Fri 7/31/20       |            |
| 313 |                                                                                   | SCG - Contract Review with EE PRG                                      | 14 days         | Tue 8/4/20        | Fri 8/21/20       |            |
| 314 |                                                                                   | SCG - Final Award and Contract Signed                                  | 6 days          | Mon 8/24/20       | Mon 8/31/20       |            |
| 315 |                                                                                   | SCG - Submit Advice Letter                                             | 59 days         | Tue 9/1/20        | Fri 11/20/20      |            |
| 316 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day           | Fri 12/18/20      | Fri 12/18/20      |            |
| 317 |                                                                                   | SCG - Implementation Plan                                              | 43 days         | Sat 12/19/20      | Tue 2/16/21       |            |
| 318 |                                                                                   | <b>SCG - Local Small/Medium Public Solicitation</b>                    | <b>631 days</b> | <b>Tue 9/4/18</b> | <b>Tue 2/2/21</b> |            |
| 319 |                                                                                   | SCG - RFA Preparation                                                  | 104 days        | Tue 9/4/18        | Fri 1/25/19       |            |
| 320 |                                                                                   | SCG - RFA Release                                                      | 1 day           | Thu 1/31/19       | Thu 1/31/19       |            |
| 321 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 30 days         | Fri 2/1/19        | Thu 3/14/19       |            |
| 322 |                                                                                   | SCG - RFA Evaluation                                                   | 52 days         | Thu 3/14/19       | Fri 5/24/19       |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration        | Start              | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 323 |                                                                                   | SCG - RFA Review with EE PRG                                           | 1 day           | Tue 6/4/19         | Tue 6/4/19         |            |
| 324 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Thu 8/1/19         | Thu 8/1/19         |            |
| 325 |                                                                                   | SCG - RFP Preparation                                                  | 37 days         | Wed 7/3/19         | Thu 8/22/19        |            |
| 326 |                                                                                   | SCG - RFP Release                                                      | 1 day           | Fri 8/23/19        | Fri 8/23/19        |            |
| 327 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 31 days         | Mon 8/26/19        | Mon 10/7/19        |            |
| 328 |                                                                                   | SCG - RFP Evaluation                                                   | 36 days         | Tue 10/8/19        | Tue 11/26/19       |            |
| 329 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day           | Tue 12/3/19        | Tue 12/3/19        |            |
| 330 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 1/21/20        | Tue 1/21/20        |            |
| 331 |                                                                                   | SCG - Contract Negotiation and Development                             | 135 days        | Mon 1/27/20        | Fri 7/31/20        |            |
| 332 |                                                                                   | SCG - Contract Review with EE PRG                                      | 14 days         | Tue 8/4/20         | Fri 8/21/20        |            |
| 333 |                                                                                   | SCG - Final Award and Contract Signed                                  | 6 days          | Mon 8/24/20        | Mon 8/31/20        |            |
| 334 |                                                                                   | SCG - Submit Advice Letter                                             | 49 days         | Tue 9/1/20         | Fri 11/6/20        |            |
| 335 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day           | Fri 12/4/20        | Fri 12/4/20        |            |
| 336 |                                                                                   | SCG - Implementation Plan                                              | 43 days         | Sat 12/5/20        | Tue 2/2/21         |            |
| 337 |                                                                                   | <b>SCG - Statewide POS Food Service Solicitation</b>                   | <b>605 days</b> | <b>Mon 1/21/19</b> | <b>Fri 5/14/21</b> |            |
| 338 |                                                                                   | SCG - RFA Preparation                                                  | 143 days        | Mon 1/21/19        | Wed 8/7/19         |            |
| 339 |                                                                                   | SCG - RFA Release                                                      | 0 days          | Mon 8/12/19        | Mon 8/12/19        |            |
| 340 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 34 days         | Tue 8/13/19        | Fri 9/27/19        |            |
| 341 |                                                                                   | SCG - RFA Evaluation                                                   | 34 days         | Mon 9/30/19        | Thu 11/14/19       |            |
| 342 |                                                                                   | SCG - RFA Review with EE PRG                                           | 0 days          | Tue 12/3/19        | Tue 12/3/19        |            |
| 343 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Fri 1/24/20        | Fri 1/24/20        |            |
| 344 |                                                                                   | SCG - RFP Preparation                                                  | 24 days         | Sat 10/26/19       | Wed 11/27/19       |            |
| 345 |                                                                                   | SCG - RFP Release                                                      | 0 days          | Wed 1/29/20        | Wed 1/29/20        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration        | Start              | Finish            | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|--------------------|-------------------|------------|
| 346 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 35 days         | Thu 1/30/20        | Wed 3/18/20       |            |
| 347 |                                                                                   | SCG - RFP Evaluation                                                   | 28 days         | Thu 3/19/20        | Mon 4/27/20       |            |
| 348 |                                                                                   | SCG - RFP Review with EE PRG                                           | 0 days          | Tue 5/5/20         | Tue 5/5/20        |            |
| 349 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Fri 5/15/20        | Fri 5/15/20       |            |
| 350 |                                                                                   | SCG - Contract Negotiation and Development                             | 90 days         | Mon 6/1/20         | Fri 10/2/20       |            |
| 351 |                                                                                   | SCG - Contract Review with EE PRG                                      | 14 days         | Tue 10/6/20        | Fri 10/23/20      |            |
| 352 |                                                                                   | SCG - Final Award and Contract Signed                                  | 5 days          | Mon 10/26/20       | Fri 10/30/20      |            |
| 353 |                                                                                   | SCG - Submit Advice Letter                                             | 32 days         | Mon 11/2/20        | Tue 12/15/20      |            |
| 354 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day           | Thu 1/14/21        | Thu 1/14/21       |            |
| 355 |                                                                                   | SCG - Implementation Plan                                              | 42 days         | Fri 1/15/21        | Mon 3/15/21       |            |
| 356 |                                                                                   | <b>SCG - Statewide Midstream Water Heating Solicitation</b>            | <b>597 days</b> | <b>Mon 1/21/19</b> | <b>Tue 5/4/21</b> |            |
| 357 |                                                                                   | SCG - RFA Preparation                                                  | 143 days        | Mon 1/21/19        | Wed 8/7/19        |            |
| 358 |                                                                                   | SCG - RFA Release                                                      | 0 days          | Mon 8/12/19        | Mon 8/12/19       |            |
| 359 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 34 days         | Tue 8/13/19        | Fri 9/27/19       |            |
| 360 |                                                                                   | SCG - RFA Evaluation                                                   | 34 days         | Mon 9/30/19        | Thu 11/14/19      |            |
| 361 |                                                                                   | SCG - RFA Review with EE PRG                                           | 0 days          | Tue 12/3/19        | Tue 12/3/19       |            |
| 362 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Fri 1/24/20        | Fri 1/24/20       |            |
| 363 |                                                                                   | SCG - RFP Preparation                                                  | 24 days         | Sat 10/26/19       | Wed 11/27/19      |            |
| 364 |                                                                                   | SCG - RFP Release                                                      | 0 days          | Wed 1/29/20        | Wed 1/29/20       |            |
| 365 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 35 days         | Thu 1/30/20        | Wed 3/18/20       |            |
| 366 |                                                                                   | SCG - RFP Evaluation                                                   | 28 days         | Thu 3/19/20        | Mon 4/27/20       |            |
| 367 |                                                                                   | SCG - RFP Review with EE PRG                                           | 0 days          | Tue 5/5/20         | Tue 5/5/20        |            |
| 368 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Fri 5/15/20        | Fri 5/15/20       |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration        | Start             | Finish              | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|-------------------|---------------------|------------|
| 369 |                                                                                   | SCG - Contract Negotiation and Development                             | 90 days         | Mon 6/1/20        | Fri 10/2/20         |            |
| 370 |                                                                                   | SCG - Contract Review with EE PRG                                      | 14 days         | Tue 10/6/20       | Fri 10/23/20        |            |
| 371 |                                                                                   | SCG - Final Award and Contract Signed                                  | 5 days          | Mon 10/26/20      | Fri 10/30/20        |            |
| 372 |                                                                                   | SCG - Submit Advice Letter                                             | 25 days         | Mon 11/2/20       | Fri 12/4/20         |            |
| 373 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day           | Thu 3/18/21       | Thu 3/18/21         |            |
| 374 |                                                                                   | SCG - Implementation Plan                                              | 22 days         | Fri 3/19/21       | Mon 4/19/21         |            |
| 375 |                                                                                   | <b>SCG - Statewide Gas Emerging Technology Solicitation</b>            | <b>738 days</b> | <b>Wed 1/2/19</b> | <b>Fri 10/29/21</b> |            |
| 376 |                                                                                   | SCG - RFA Preparation                                                  | 283 days        | Wed 1/2/19        | Fri 1/31/20         |            |
| 377 |                                                                                   | SCG - RFA Release                                                      | 1 day           | Wed 2/12/20       | Wed 2/12/20         |            |
| 378 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 30 days         | Thu 2/13/20       | Wed 3/25/20         |            |
| 379 |                                                                                   | SCG - RFA Evaluation                                                   | 26 days         | Thu 3/26/20       | Thu 4/30/20         |            |
| 380 |                                                                                   | SCG - RFA Review with EE PRG                                           | 1 day           | Tue 5/5/20        | Tue 5/5/20          |            |
| 381 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Fri 5/15/20       | Fri 5/15/20         |            |
| 382 |                                                                                   | SCG - RFP Preparation                                                  | 66 days         | Fri 5/1/20        | Fri 7/31/20         |            |
| 383 |                                                                                   | SCG - RFP Release                                                      | 1 day           | Fri 8/21/20       | Fri 8/21/20         |            |
| 384 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 30 days         | Mon 8/24/20       | Fri 10/2/20         |            |
| 385 |                                                                                   | SCG - RFP Evaluation                                                   | 38 days         | Mon 10/5/20       | Wed 11/25/20        |            |
| 386 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day           | Tue 12/1/20       | Tue 12/1/20         |            |
| 387 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Mon 12/7/20       | Mon 12/7/20         |            |
| 388 |                                                                                   | SCG - Contract Negotiation and Development                             | 85 days         | Mon 1/4/21        | Fri 4/30/21         |            |
| 389 |                                                                                   | SCG - Contract Review with EE PRG                                      | 9 days          | Tue 5/4/21        | Fri 5/14/21         |            |
| 390 |                                                                                   | SCG - Final Award and Contract Signed                                  | 29 days         | Mon 5/17/21       | Thu 6/24/21         |            |
| 391 |                                                                                   | SCG - Submit Advice Letter                                             | 23 days         | Sun 6/27/21       | Tue 7/27/21         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration        | Start              | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 392 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day           | Tue 8/24/21        | Tue 8/24/21        |            |
| 393 |                                                                                   | SCG - Implementation Plan                                              | 44 days         | Wed 8/25/21        | Sat 10/23/21       |            |
| 394 |                                                                                   | <b>SCG - Local Manufactured Housing Solicitation</b>                   | <b>341 days</b> | <b>Fri 11/1/19</b> | <b>Fri 2/19/21</b> |            |
| 395 |                                                                                   | SCG - RFA Preparation                                                  | 66 days         | Fri 11/1/19        | Fri 1/31/20        |            |
| 396 |                                                                                   | SCG - RFA Release                                                      | 0 days          | Fri 2/21/20        | Fri 2/21/20        |            |
| 397 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 30 days         | Mon 2/24/20        | Fri 4/3/20         |            |
| 398 |                                                                                   | SCG - RFA Evaluation                                                   | 35 days         | Mon 4/6/20         | Fri 5/22/20        |            |
| 399 |                                                                                   | SCG - RFA Review with EE PRG                                           | 0 days          | Tue 6/2/20         | Tue 6/2/20         |            |
| 400 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Mon 6/8/20         | Mon 6/8/20         |            |
| 401 |                                                                                   | SCG - RFP Preparation                                                  | 43 days         | Wed 4/1/20         | Fri 5/29/20        |            |
| 402 |                                                                                   | SCG - RFP Release                                                      | 0 days          | Fri 6/12/20        | Fri 6/12/20        |            |
| 403 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 30 days         | Mon 6/15/20        | Fri 7/24/20        |            |
| 404 |                                                                                   | SCG - RFP Evaluation                                                   | 50 days         | Mon 7/27/20        | Fri 10/2/20        |            |
| 405 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day           | Tue 10/6/20        | Tue 10/6/20        |            |
| 406 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 10/13/20       | Tue 10/13/20       |            |
| 407 |                                                                                   | SCG - Contract Negotiation and Development                             | 28 days         | Mon 10/19/20       | Wed 11/25/20       |            |
| 408 |                                                                                   | SCG - Contract Review with EE PRG                                      | 7 days          | Tue 12/1/20        | Wed 12/9/20        |            |
| 409 |                                                                                   | SCG - Final Award and Contract Signed                                  | 9 days          | Thu 12/10/20       | Tue 12/22/20       |            |
| 410 |                                                                                   | SCG - Submit Advice Letter                                             | 0 days          | N/A                | N/A                |            |
| 411 |                                                                                   | SCG - Advice Letter Approved                                           | 0 days          | N/A                | N/A                |            |
| 412 |                                                                                   | SCG - Implementation Plan                                              | 44 days         | Tue 12/22/20       | Fri 2/19/21        |            |
| 413 |                                                                                   | <b>SCG - Local Large Commercial Solicitation</b>                       | <b>434 days</b> | <b>Fri 11/1/19</b> | <b>Wed 6/30/21</b> |            |
| 414 |                                                                                   | SCG - RFA Preparation                                                  | 66 days         | Fri 11/1/19        | Fri 1/31/20        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration        | Start              | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 415 |                                                                                   | SCG - RFA Release                                                      | 1 day           | Fri 2/21/20        | Fri 2/21/20        |            |
| 416 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 30 days         | Mon 2/24/20        | Fri 4/3/20         |            |
| 417 |                                                                                   | SCG - RFA Evaluation                                                   | 35 days         | Mon 4/6/20         | Fri 5/22/20        |            |
| 418 |                                                                                   | SCG - RFA Review with EE PRG                                           | 1 day           | Tue 6/2/20         | Tue 6/2/20         |            |
| 419 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Mon 6/8/20         | Mon 6/8/20         |            |
| 420 |                                                                                   | SCG - RFP Preparation                                                  | 43 days         | Wed 4/1/20         | Fri 5/29/20        |            |
| 421 |                                                                                   | SCG - RFP Release                                                      | 1 day           | Fri 6/12/20        | Fri 6/12/20        |            |
| 422 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 30 days         | Mon 6/15/20        | Fri 7/24/20        |            |
| 423 |                                                                                   | SCG - RFP Evaluation                                                   | 50 days         | Mon 7/27/20        | Fri 10/2/20        |            |
| 424 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day           | Tue 10/6/20        | Tue 10/6/20        |            |
| 425 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 10/13/20       | Tue 10/13/20       |            |
| 426 |                                                                                   | SCG - Contract Negotiation and Development                             | 28 days         | Mon 10/19/20       | Wed 11/25/20       |            |
| 427 |                                                                                   | SCG - Contract Review with EE PRG                                      | 7 days          | Tue 12/1/20        | Wed 12/9/20        |            |
| 428 |                                                                                   | SCG - Final Award and Contract Signed                                  | 10 days         | Thu 12/10/20       | Wed 12/23/20       |            |
| 429 |                                                                                   | SCG - Submit Advice Letter                                             | 64 days         | Fri 1/1/21         | Wed 3/31/21        |            |
| 430 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day           | Fri 6/4/21         | Fri 6/4/21         |            |
| 431 |                                                                                   | SCG - Implementation Plan                                              | 43 days         | Sat 6/5/21         | Tue 8/3/21         |            |
| 432 |                                                                                   | <b>SCG - Local Agricultural Solicitation</b>                           | <b>434 days</b> | <b>Fri 11/1/19</b> | <b>Wed 6/30/21</b> |            |
| 433 |                                                                                   | SCG - RFA Preparation                                                  | 66 days         | Fri 11/1/19        | Fri 1/31/20        |            |
| 434 |                                                                                   | SCG - RFA Release                                                      | 1 day           | Fri 2/21/20        | Fri 2/21/20        |            |
| 435 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 30 days         | Mon 2/24/20        | Fri 4/3/20         |            |
| 436 |                                                                                   | SCG - RFA Evaluation                                                   | 35 days         | Mon 4/6/20         | Fri 5/22/20        |            |
| 437 |                                                                                   | SCG - RFA Review with EE PRG                                           | 1 day           | Tue 6/2/20         | Tue 6/2/20         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration         | Start             | Finish              | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------|-------------------|---------------------|------------|
| 438 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Mon 6/8/20        | Mon 6/8/20          |            |
| 439 |                                                                                   | SCG - RFP Preparation                                                  | 43 days          | Wed 4/1/20        | Fri 5/29/20         |            |
| 440 |                                                                                   | SCG - RFP Release                                                      | 1 day            | Fri 6/12/20       | Fri 6/12/20         |            |
| 441 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 30 days          | Mon 6/15/20       | Fri 7/24/20         |            |
| 442 |                                                                                   | SCG - RFP Evaluation                                                   | 50 days          | Mon 7/27/20       | Fri 10/2/20         |            |
| 443 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day            | Tue 10/6/20       | Tue 10/6/20         |            |
| 444 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 10/13/20      | Tue 10/13/20        |            |
| 445 |                                                                                   | SCG - Contract Negotiation and Development                             | 28 days          | Mon 10/19/20      | Wed 11/25/20        |            |
| 446 |                                                                                   | SCG - Contract Review with EE PRG                                      | 7 days           | Tue 12/1/20       | Wed 12/9/20         |            |
| 447 |                                                                                   | SCG - Final Award and Contract Signed                                  | 2 days           | Fri 12/11/20      | Mon 12/14/20        |            |
| 448 |                                                                                   | SCG - Submit Advice Letter                                             | 41 days          | Fri 1/1/21        | Fri 2/26/21         |            |
| 449 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day            | Wed 4/7/21        | Wed 4/7/21          |            |
| 450 |                                                                                   | SCG - Implementation Plan                                              | 43 days          | Thu 4/8/21        | Mon 6/7/21          |            |
| 451 |                                                                                   | <b>SCG - Local Behavioral Solicitation - Residential</b>               | <b>413 days?</b> | <b>Fri 5/1/20</b> | <b>Tue 11/30/21</b> |            |
| 452 |                                                                                   | SCG - RFA Preparation                                                  | 66 days          | Fri 5/1/20        | Fri 7/31/20         |            |
| 453 |                                                                                   | SCG - RFA Release                                                      | 1 day            | Fri 8/21/20       | Fri 8/21/20         |            |
| 454 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 25 days          | Mon 8/24/20       | Fri 9/25/20         |            |
| 455 |                                                                                   | SCG - RFA Evaluation                                                   | 25 days          | Mon 9/28/20       | Fri 10/30/20        |            |
| 456 |                                                                                   | SCG - RFA Review with EE PRG                                           | 1 day            | Tue 11/3/20       | Tue 11/3/20         |            |
| 457 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Wed 11/18/20      | Wed 11/18/20        |            |
| 458 |                                                                                   | SCG - RFP Preparation                                                  | 66 days          | Thu 10/1/20       | Thu 12/31/20        |            |
| 459 |                                                                                   | SCG - RFP Release                                                      | 1 day            | Fri 1/15/21       | Fri 1/15/21         |            |
| 460 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 26 days          | Mon 1/18/21       | Mon 2/22/21         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration         | Start             | Finish              | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------|-------------------|---------------------|------------|
| 461 |                                                                                   | SCG - RFP Evaluation                                                   | 29 days          | Tue 2/23/21       | Fri 4/2/21          |            |
| 462 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day            | Tue 4/6/21        | Tue 4/6/21          |            |
| 463 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 4/13/21       | Tue 4/13/21         |            |
| 464 |                                                                                   | SCG - Contract Negotiation and Development                             | 95 days          | Mon 4/26/21       | Fri 9/3/21          |            |
| 465 |                                                                                   | SCG - Contract Review with EE PRG                                      | 9 days           | Tue 9/7/21        | Fri 9/17/21         |            |
| 466 |                                                                                   | SCG - Final Award and Contract Signed                                  | 30 days          | Mon 9/20/21       | Fri 10/29/21        |            |
| 467 |                                                                                   | SCG - Submit Advice Letter                                             | 21 days          | Mon 11/1/21       | Mon 11/29/21        |            |
| 468 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day            | Wed 12/22/21      | Wed 12/22/21        |            |
| 469 |                                                                                   | SCG - Implementation Plan                                              | 43 days          | Thu 12/23/21      | Sun 2/20/22         |            |
| 470 |                                                                                   | <b>SCG - Local Behavioral Solicitation - Commercial</b>                | <b>413 days?</b> | <b>Fri 5/1/20</b> | <b>Tue 11/30/21</b> |            |
| 471 |                                                                                   | SCG - RFA Preparation                                                  | 66 days          | Fri 5/1/20        | Fri 7/31/20         |            |
| 472 |                                                                                   | SCG - RFA Release                                                      | 1 day            | Fri 8/21/20       | Fri 8/21/20         |            |
| 473 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 25 days          | Mon 8/24/20       | Fri 9/25/20         |            |
| 474 |                                                                                   | SCG - RFA Evaluation                                                   | 25 days          | Mon 9/28/20       | Fri 10/30/20        |            |
| 475 |                                                                                   | SCG - RFA Review with EE PRG                                           | 1 day            | Tue 11/3/20       | Tue 11/3/20         |            |
| 476 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Wed 11/18/20      | Wed 11/18/20        |            |
| 477 |                                                                                   | SCG - RFP Preparation                                                  | 66 days          | Thu 10/1/20       | Thu 12/31/20        |            |
| 478 |                                                                                   | SCG - RFP Release                                                      | 1 day            | Fri 1/22/21       | Fri 1/22/21         |            |
| 479 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 26 days          | Mon 1/25/21       | Mon 3/1/21          |            |
| 480 |                                                                                   | SCG - RFP Evaluation                                                   | 24 days          | Tue 3/2/21        | Fri 4/2/21          |            |
| 481 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day            | Tue 4/6/21        | Tue 4/6/21          |            |
| 482 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Fri 11/12/21      | Fri 11/12/21        |            |
| 483 |                                                                                   | SCG - Contract Negotiation and Development                             | 132 days         | Mon 11/29/21      | Tue 5/31/22         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                              | Duration         | Start              | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------|--------------------|--------------------|------------|
| 484 |                                                                                   | SCG - Contract Review with EE PRG                                      | 8 days           | Sun 6/5/22         | Tue 6/14/22        |            |
| 485 |                                                                                   | SCG - Final Award and Contract Signed                                  | 109 days         | Fri 7/1/22         | Wed 11/30/22       |            |
| 486 |                                                                                   | SCG - Submit Advice Letter                                             | 23 days          | N/A                | N/A                |            |
| 487 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day            | N/A                | N/A                |            |
| 488 |                                                                                   | SCG - Implementation Plan                                              | 43 days          | Thu 12/1/22        | Sun 1/29/23        |            |
| 489 |                                                                                   | <b>SCG - Local Industrial Solicitation</b>                             | <b>434 days?</b> | <b>Tue 12/1/20</b> | <b>Fri 7/29/22</b> |            |
| 490 |                                                                                   | SCG - RFA Preparation                                                  | 63 days?         | Tue 12/1/20        | Thu 2/25/21        |            |
| 491 |                                                                                   | SCG - RFA Release                                                      | 1 day?           | Fri 3/19/21        | Fri 3/19/21        |            |
| 492 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 25 days?         | Mon 3/22/21        | Fri 4/23/21        |            |
| 493 |                                                                                   | SCG - RFA Evaluation                                                   | 25 days?         | Mon 4/26/21        | Fri 5/28/21        |            |
| 494 |                                                                                   | SCG - RFA Review with EE PRG                                           | 1 day?           | Tue 6/1/21         | Tue 6/1/21         |            |
| 495 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day?           | Tue 6/8/21         | Tue 6/8/21         |            |
| 496 |                                                                                   | SCG - RFP Preparation                                                  | 67 days?         | Thu 4/1/21         | Fri 7/2/21         |            |
| 497 |                                                                                   | SCG - RFP Release                                                      | 1 day?           | Fri 7/16/21        | Fri 7/16/21        |            |
| 498 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 30 days?         | Mon 7/19/21        | Fri 8/27/21        |            |
| 499 |                                                                                   | SCG - RFP Evaluation                                                   | 25 days?         | Mon 8/30/21        | Fri 10/1/21        |            |
| 500 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day?           | Tue 10/5/21        | Tue 10/5/21        |            |
| 501 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day?           | Tue 12/14/21       | Tue 12/14/21       |            |
| 502 |                                                                                   | SCG - Contract Negotiation and Development                             | 127 days?        | Thu 2/3/22         | Fri 7/29/22        |            |
| 503 |                                                                                   | SCG - Contract Review with EE PRG                                      | 9 days?          | Tue 8/2/22         | Fri 8/12/22        |            |
| 504 |                                                                                   | SCG - Final Award and Contract Signed                                  | 21 days?         | Fri 7/29/22        | Fri 8/26/22        |            |
| 505 |                                                                                   | SCG - Submit Advice Letter                                             | 1 day?           | Sun 10/30/22       | Sun 10/30/22       |            |
| 506 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day?           | Mon 1/30/23        | Mon 1/30/23        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID  |  | Task Name                                                              | Duration        | Start             | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------|-------------------|--------------------|------------|
| 507 |                                                                                   | SCG - Implementation Plan                                              | 45 days?        | Tue 1/31/23       | Sat 4/1/23         |            |
| 508 |                                                                                   | <b>SCG - Large Public Sector Solicitation (re-Bid)</b>                 | <b>412 days</b> | <b>Mon 1/4/21</b> | <b>Tue 8/2/22</b>  |            |
| 509 |                                                                                   | SCG - RFA Preparation                                                  | 65 days         | Mon 1/4/21        | Fri 4/2/21         |            |
| 510 |                                                                                   | SCG - RFA Release                                                      | 1 day           | Fri 7/16/21       | Fri 7/16/21        |            |
| 511 |                                                                                   | SCG - RFA Abstract Creation Duration                                   | 20 days         | Mon 7/19/21       | Fri 8/13/21        |            |
| 512 |                                                                                   | SCG - RFA Evaluation                                                   | 15 days         | Mon 8/16/21       | Fri 9/3/21         |            |
| 513 |                                                                                   | SCG - RFA Review with EE PRG                                           | 1 day           | Tue 9/7/21        | Tue 9/7/21         |            |
| 514 |                                                                                   | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 9/14/21       | Tue 9/14/21        |            |
| 515 |                                                                                   | SCG - RFP Preparation                                                  | 35 days         | Mon 9/13/21       | Fri 10/29/21       |            |
| 516 |                                                                                   | SCG - RFP Release                                                      | 1 day           | Mon 11/8/21       | Mon 11/8/21        |            |
| 517 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 29 days         | Tue 11/9/21       | Fri 12/17/21       |            |
| 518 |                                                                                   | SCG - RFP Evaluation                                                   | 30 days         | Mon 12/20/21      | Fri 1/28/22        |            |
| 519 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day           | Tue 2/1/22        | Tue 2/1/22         |            |
| 520 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 3/8/22        | Tue 3/8/22         |            |
| 521 |                                                                                   | SCG - Contract Negotiation and Development                             | 79 days         | Mon 3/14/22       | Thu 6/30/22        |            |
| 522 |                                                                                   | SCG - Contract Review with EE PRG                                      | 9 days          | Tue 7/5/22        | Fri 7/15/22        |            |
| 523 |                                                                                   | SCG - Final Award and Contract Signed                                  | 63 days         | Mon 7/18/22       | Wed 10/12/22       |            |
| 524 |                                                                                   | SCG - Submit Advice Letter                                             | 23 days         | N/A               | N/A                |            |
| 525 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day           | N/A               | N/A                |            |
| 526 |                                                                                   | SCG - Implementation Plan                                              | 44 days         | Wed 10/12/22      | Sat 12/10/22       |            |
| 527 |                                                                                   | <b>SCG - Outreach Solicitation</b>                                     | <b>434 days</b> | <b>Mon 2/1/21</b> | <b>Thu 9/29/22</b> |            |
| 528 |                                                                                   | SCG - RFA Preparation                                                  | 65 days         | Mon 2/1/21        | Fri 4/30/21        |            |
| 529 |                                                                                   | SCG - RFA Release                                                      | 1 day           | Fri 5/21/21       | Fri 5/21/21        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID  |  | Task Name                                                              | Duration         | Start             | Finish              | 2018<br>H1 |
|-----|----------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------|-------------------|---------------------|------------|
| 530 |                                                                                  | SCG - RFA Abstract Creation Duration                                   | 25 days          | Mon 5/24/21       | Fri 6/25/21         |            |
| 531 |                                                                                  | SCG - RFA Evaluation                                                   | 25 days          | Mon 6/28/21       | Fri 7/30/21         |            |
| 532 |                                                                                  | SCG - RFA Review with EE PRG                                           | 1 day            | Tue 8/3/21        | Tue 8/3/21          |            |
| 533 |                                                                                  | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 8/10/21       | Tue 8/10/21         |            |
| 534 |                                                                                  | SCG - RFP Preparation                                                  | 69 days          | Tue 6/1/21        | Fri 9/3/21          |            |
| 535 |                                                                                  | SCG - RFP Release                                                      | 1 day            | Fri 9/17/21       | Fri 9/17/21         |            |
| 536 |                                                                                  | SCG - RFP Proposal Creation Duration                                   | 30 days          | Mon 9/20/21       | Fri 10/29/21        |            |
| 537 |                                                                                  | SCG - RFP Evaluation                                                   | 25 days          | Mon 11/1/21       | Fri 12/3/21         |            |
| 538 |                                                                                  | SCG - RFP Review with EE PRG                                           | 1 day            | Tue 12/7/21       | Tue 12/7/21         |            |
| 539 |                                                                                  | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 12/14/21      | Tue 12/14/21        |            |
| 540 |                                                                                  | SCG - Contract Negotiation and Development                             | 54 days          | Mon 1/17/22       | Thu 3/31/22         |            |
| 541 |                                                                                  | SCG - Contract Review with EE PRG                                      | 9 days           | Tue 4/5/22        | Fri 4/15/22         |            |
| 542 |                                                                                  | SCG - Final Award and Contract Signed                                  | 10 days          | Mon 4/18/22       | Fri 4/29/22         |            |
| 543 |                                                                                  | SCG - Submit Advice Letter                                             | 21 days          | N/A               | N/A                 |            |
| 544 |                                                                                  | SCG - Advice Letter Approved                                           | 1 day            | N/A               | N/A                 |            |
| 545 |                                                                                  | SCG - Implementation Plan                                              | 43 days          | Sat 4/30/22       | Tue 6/28/22         |            |
| 546 |                                                                                  | <b>SCG - Marketplace Solicitation</b>                                  | <b>436 days?</b> | <b>Mon 3/1/21</b> | <b>Mon 10/31/22</b> |            |
| 547 |                                                                                  | SCG - RFA Preparation                                                  | 64 days          | Sat 5/1/21        | Wed 7/28/21         |            |
| 548 |                                                                                  | SCG - RFA Release                                                      | 1 day            | Fri 8/20/21       | Fri 8/20/21         |            |
| 549 |                                                                                  | SCG - RFA Abstract Creation Duration                                   | 25 days          | Mon 8/23/21       | Fri 9/24/21         |            |
| 550 |                                                                                  | SCG - RFA Evaluation                                                   | 25 days          | Mon 9/27/21       | Fri 10/29/21        |            |
| 551 |                                                                                  | SCG - RFA Review with EE PRG                                           | 1 day            | Tue 11/2/21       | Tue 11/2/21         |            |
| 552 |                                                                                  | SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 11/9/21       | Tue 11/9/21         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




| ID  |  | Task Name                                                              | Duration         | Start             | Finish              | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------------|------------------|-------------------|---------------------|------------|
| 553 |                                                                                   | SCG - RFP Preparation                                                  | 91 days          | Thu 8/26/21       | Thu 12/30/21        |            |
| 554 |                                                                                   | SCG - RFP Release                                                      | 1 day            | Fri 1/14/22       | Fri 1/14/22         |            |
| 555 |                                                                                   | SCG - RFP Proposal Creation Duration                                   | 30 days          | Mon 1/17/22       | Fri 2/25/22         |            |
| 556 |                                                                                   | SCG - RFP Evaluation                                                   | 25 days          | Mon 2/28/22       | Fri 4/1/22          |            |
| 557 |                                                                                   | SCG - RFP Review with EE PRG                                           | 1 day            | Tue 5/3/22        | Tue 5/3/22          |            |
| 558 |                                                                                   | SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Wed 5/11/22       | Wed 5/11/22         |            |
| 559 |                                                                                   | SCG - Contract Negotiation and Development                             | 117 days         | Wed 6/22/22       | Thu 12/1/22         |            |
| 560 |                                                                                   | SCG - Contract Review with EE PRG                                      | 9 days           | Tue 12/6/22       | Fri 12/16/22        |            |
| 561 |                                                                                   | SCG - Final Award and Contract Signed                                  | 10 days          | Mon 12/19/22      | Fri 12/30/22        |            |
| 562 |                                                                                   | SCG - Submit Advice Letter                                             | 20 days          | Tue 1/3/23        | Mon 1/30/23         |            |
| 563 |                                                                                   | SCG - Advice Letter Approved                                           | 1 day            | Tue 5/2/23        | Tue 5/2/23          |            |
| 564 |                                                                                   | SCG - Implementation Plan                                              | 44 days          | Wed 5/3/23        | Sun 7/2/23          |            |
| 565 |                                                                                   | <b>SCG - Residential Multi-Family - Whole Building</b>                 | <b>436 days?</b> | <b>Mon 3/1/21</b> | <b>Mon 10/31/22</b> |            |
| 566 |                                                                                   | RFA Preparation                                                        | 40 days          | Mon 1/10/22       | Fri 3/4/22          |            |
| 567 |                                                                                   | RFA Release                                                            | 1 day            | Fri 3/25/22       | Fri 3/25/22         |            |
| 568 |                                                                                   | RFA Abstract Creation Duration                                         | 25 days          | Mon 3/28/22       | Fri 4/29/22         |            |
| 569 |                                                                                   | RFA Evaluation                                                         | 25 days          | Mon 5/2/22        | Fri 6/3/22          |            |
| 570 |                                                                                   | RFA Review with EE PRG                                                 | 1 day            | Tue 6/7/22        | Tue 6/7/22          |            |
| 571 |                                                                                   | RFA Estimated Notification of Successful and Unsuccessful Bidder       | 1 day            | Tue 6/14/22       | Tue 6/14/22         |            |
| 572 |                                                                                   | RFP Preparation                                                        | 28 days          | Sun 5/1/22        | Tue 6/7/22          |            |
| 573 |                                                                                   | RFP Release                                                            | 1 day            | Fri 6/24/22       | Fri 6/24/22         |            |
| 574 |                                                                                   | RFP Proposal Creation Duration                                         | 52 days          | Mon 6/27/22       | Tue 9/6/22          |            |
| 575 |                                                                                   | RFP Evaluation                                                         | 11 days          | Fri 9/9/22        | Fri 9/23/22         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                        | Duration            | Start                 | Finish                | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------|---------------------|-----------------------|-----------------------|------------|
| 576 |                                                                                   | RFP Review with EE PRG                                           | 1 day               | Thu 10/6/22           | Thu 10/6/22           |            |
| 577 |                                                                                   | RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day               | Tue 10/11/22          | Tue 10/11/22          |            |
| 578 |                                                                                   | Contract Negotiation and Development                             | 39 days             | Tue 10/11/22          | Fri 12/2/22           |            |
| 579 |                                                                                   | Contract Review with EE PRG                                      | 1 day               | Tue 12/6/22           | Tue 12/6/22           |            |
| 580 |                                                                                   | Final Award and Contract Signed                                  | 10 days             | Mon 12/19/22          | Fri 12/30/22          |            |
| 581 |                                                                                   | Submit Advice Letter                                             | 22 days             | Mon 1/2/23            | Tue 1/31/23           |            |
| 582 |                                                                                   | Advice Letter Approved                                           | 1 day               | Fri 3/31/23           | Fri 3/31/23           |            |
| 583 |                                                                                   | Implementation Plan                                              | 43 days             | Sat 4/1/23            | Tue 5/30/23           |            |
| 584 |                                                                                   | <del>SCG—Youth Education Outreach Solicitation</del>             | <del>331 days</del> | <del>Tue 3/1/22</del> | <del>Tue 6/6/23</del> |            |
| 585 |                                                                                   | <b>SCG - HERS Rater Training Solicitation</b>                    | <b>436 days?</b>    | <b>Mon 3/1/21</b>     | <b>Mon 10/31/22</b>   |            |
| 586 |                                                                                   | RFP Preparation                                                  | 43 days             | Tue 3/1/22            | Thu 4/28/22           |            |
| 587 |                                                                                   | RFP Release                                                      | 1 day               | Fri 5/13/22           | Fri 5/13/22           |            |
| 588 |                                                                                   | RFP Proposal Creation Duration                                   | 20 days             | Mon 5/16/22           | Fri 6/10/22           |            |
| 589 |                                                                                   | RFP Evaluation                                                   | 59 days             | Mon 6/13/22           | Thu 9/1/22            |            |
| 590 |                                                                                   | RFP Review with EE PRG                                           | 1 day               | Tue 9/6/22            | Tue 9/6/22            |            |
| 591 |                                                                                   | RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day               | Wed 8/31/22           | Wed 8/31/22           |            |
| 592 |                                                                                   | Contract Negotiation and Development                             | 53 days             | Fri 9/16/22           | Tue 11/29/22          |            |
| 593 |                                                                                   | Contract Review with EE PRG                                      | 9 days              | Tue 12/6/22           | Fri 12/16/22          |            |
| 594 |                                                                                   | Final Award and Contract Signed                                  | 9 days              | Mon 12/19/22          | Thu 12/29/22          |            |
| 595 |                                                                                   | Submit Advice Letter                                             | N/A                 | N/A                   | N/A                   |            |
| 596 |                                                                                   | Advice Letter Approved                                           | N/A                 | N/A                   | N/A                   |            |
| 597 |                                                                                   | Implementation Plan                                              | 42 days             | Fri 12/30/22          | Mon 2/27/23           |            |
| 598 |                                                                                   | <b>SCG - Retail Partnering Solicitation</b>                      | <b>29 days?</b>     | Tue 9/27/22           | Fri 11/4/22           |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                        | Duration         | Start             | Finish              | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------|------------------|-------------------|---------------------|------------|
| 599 |                                                                                   | RFP Preparation                                                  | 43 days          | Tue 3/1/22        | Thu 4/28/22         |            |
| 600 |                                                                                   | RFP Release                                                      | 1 day            | Fri 6/17/22       | Fri 6/17/22         |            |
| 601 |                                                                                   | RFP Proposal Creation Duration                                   | 30 days          | Mon 6/20/22       | Fri 7/29/22         |            |
| 602 |                                                                                   | RFP Evaluation                                                   | 24 days          | Mon 8/1/22        | Thu 9/1/22          |            |
| 603 |                                                                                   | RFP Review with EE PRG                                           | 1 day            | Tue 9/6/22        | Tue 9/6/22          |            |
| 604 |                                                                                   | RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 9/13/22       | Tue 9/13/22         |            |
| 605 |                                                                                   | Contract Negotiation and Development                             | 29 days          | Mon 9/19/22       | Thu 10/27/22        |            |
| 606 |                                                                                   | Contract Review with EE PRG                                      | 9 days           | Tue 11/1/22       | Fri 11/11/22        |            |
| 607 |                                                                                   | Final Award and Contract Signed                                  | 13 days          | Mon 11/14/22      | Wed 11/30/22        |            |
| 608 |                                                                                   | Submit Advice Letter                                             | N/A              | N/A               | N/A                 |            |
| 609 |                                                                                   | Advice Letter Approved                                           | N/A              | N/A               | N/A                 |            |
| 610 |                                                                                   | Implementation Plan                                              | 43 days          | Sat 10/1/22       | Tue 11/29/22        |            |
| 611 |                                                                                   | <b>SCG - Non-Residential EE Advisor Solicitation</b>             | <b>436 days?</b> | <b>Mon 3/1/21</b> | <b>Mon 10/31/22</b> |            |
| 612 |                                                                                   | RFP Preparation                                                  | 46 days          | Fri 4/1/22        | Fri 6/3/22          |            |
| 613 |                                                                                   | RFP Release                                                      | 1 day            | Fri 8/26/22       | Fri 8/26/22         |            |
| 614 |                                                                                   | RFP Proposal Creation Duration                                   | 20 days          | Mon 8/29/22       | Fri 9/23/22         |            |
| 615 |                                                                                   | RFP Evaluation                                                   | 16 days          | Sat 9/24/22       | Fri 10/14/22        |            |
| 616 |                                                                                   | RFP Review with EE PRG                                           | 5 days           | Mon 10/17/22      | Fri 10/21/22        |            |
| 617 |                                                                                   | RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 10/25/22      | Tue 10/25/22        |            |
| 618 |                                                                                   | Contract Negotiation and Development                             | 32 days          | Sun 10/30/22      | Mon 12/12/22        |            |
| 619 |                                                                                   | Contract Review with EE PRG                                      | 9 days           | Tue 12/13/22      | Fri 12/23/22        |            |
| 620 |                                                                                   | Final Award and Contract Signed                                  | 4 days           | Tue 12/27/22      | Fri 12/30/22        |            |
| 621 |                                                                                   | Submit Advice Letter                                             | N/A              | N/A               | N/A                 |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                        | Duration         | Start              | Finish              | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------|------------------|--------------------|---------------------|------------|
| 622 |                                                                                   | Advice Letter Approved                                           | N/A              | N/A                | N/A                 |            |
| 623 |                                                                                   | Implementation Plan                                              | 44 days          | Sun 1/1/23         | Wed 3/1/23          |            |
| 624 |                                                                                   | <b>SCG - Residential EE Kits Solicitation</b>                    | <b>436 days?</b> | <b>Mon 3/1/21</b>  | <b>Mon 10/31/22</b> |            |
| 625 |                                                                                   | RFP Preparation                                                  | 46 days          | Fri 4/1/22         | Fri 6/3/22          |            |
| 626 |                                                                                   | RFP Release                                                      | 1 day            | Mon 7/25/22        | Mon 7/25/22         |            |
| 627 |                                                                                   | RFP Proposal Creation Duration                                   | 16 days          | Tue 7/26/22        | Tue 8/16/22         |            |
| 628 |                                                                                   | RFP Evaluation                                                   | 12 days          | Wed 8/17/22        | Thu 9/1/22          |            |
| 629 |                                                                                   | RFP Review with EE PRG                                           | 1 day            | Tue 8/2/22         | Tue 8/2/22          |            |
| 630 |                                                                                   | RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 8/9/22         | Tue 8/9/22          |            |
| 631 |                                                                                   | Contract Negotiation and Development                             | 30 days          | Mon 8/22/22        | Fri 9/30/22         |            |
| 632 |                                                                                   | Contract Review with EE PRG                                      | 9 days           | Tue 10/4/22        | Fri 10/14/22        |            |
| 633 |                                                                                   | Final Award and Contract Signed                                  | 10 days          | Mon 10/17/22       | Fri 10/28/22        |            |
| 634 |                                                                                   | Submit Advice Letter                                             | N/A              | N/A                | N/A                 |            |
| 635 |                                                                                   | Advice Letter Approved                                           | N/A              | N/A                | N/A                 |            |
| 636 |                                                                                   | Implementation Plan                                              | 43 days          | Sat 10/29/22       | Tue 12/27/22        |            |
| 637 |                                                                                   | <b>SCG - IDEEA 365</b>                                           | <b>230 days</b>  | <b>Mon 2/13/23</b> | <b>Fri 12/29/23</b> |            |
| 638 |                                                                                   | RFP Preparation                                                  | 23 days          | Mon 2/13/23        | Wed 3/15/23         |            |
| 639 |                                                                                   | RFP Release                                                      | 20 days          | Thu 4/20/23        | Wed 5/17/23         |            |
| 640 |                                                                                   | RFP Proposal Creation Duration                                   | 43 days          | Wed 5/3/23         | Fri 6/30/23         |            |
| 641 |                                                                                   | RFP Evaluation                                                   | 12 days          | Fri 7/14/23        | Mon 7/31/23         |            |
| 642 |                                                                                   | RFP Review with EE PRG                                           | 1 day            | Tue 8/1/23         | Tue 8/1/23          |            |
| 643 |                                                                                   | RFP Estimated Notification of Successful and Unsuccessful Bidder | 23 days          | Tue 8/1/23         | Thu 8/31/23         |            |
| 644 |                                                                                   | Contract Negotiation and Development                             | 21 days          | Fri 9/1/23         | Fri 9/29/23         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                        | Duration         | Start              | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|------------------------------------------------------------------|------------------|--------------------|--------------------|------------|
| 645 |                                                                                   | Contract Review with EE PRG                                      | 32 days          | Mon 9/18/23        | Tue 10/31/23       |            |
| 646 |                                                                                   | Final Award and Contract Signed                                  | 17 days          | Mon 10/9/23        | Tue 10/31/23       |            |
| 647 |                                                                                   | Submit Advice Letter                                             | 10 days          | Wed 11/1/23        | Tue 11/14/23       |            |
| 648 |                                                                                   | Advice Letter Approved                                           | 11 days          | Wed 11/22/23       | Wed 12/6/23        |            |
| 649 |                                                                                   | Implementation Plan                                              | 9 days           | Tue 12/19/23       | Fri 12/29/23       |            |
| 650 |                                                                                   | <b>SCG - Commercial SEM</b>                                      | <b>110 days?</b> | <b>Tue 8/1/23</b>  | <b>Mon 1/1/24</b>  |            |
| 651 |                                                                                   | RFP Preparation                                                  | 22 days          | Tue 8/1/23         | Wed 8/30/23        |            |
| 652 |                                                                                   | RFP Release                                                      | 13 days          | Wed 9/13/23        | Fri 9/29/23        |            |
| 653 |                                                                                   | RFP Proposal Creation Duration                                   | 11 days          | Mon 10/2/23        | Mon 10/16/23       |            |
| 654 |                                                                                   | RFP Evaluation                                                   | 5 days           | Wed 10/25/23       | Tue 10/31/23       |            |
| 655 |                                                                                   | RFP Review with EE PRG                                           | 2 days           | Tue 10/31/23       | Wed 11/1/23        |            |
| 656 |                                                                                   | RFP Estimated Notification of Successful and Unsuccessful Bidder | 5 days           | Thu 11/2/23        | Wed 11/8/23        |            |
| 657 |                                                                                   | Contract Negotiation and Development                             | 16 days          | Wed 10/25/23       | Wed 11/15/23       |            |
| 658 |                                                                                   | Contract Review with EE PRG                                      | 1 day            | Tue 12/5/23        | Tue 12/5/23        |            |
| 659 |                                                                                   | Final Award and Contract Signed                                  | 6 days           | Wed 12/13/23       | Wed 12/20/23       |            |
| 660 |                                                                                   | Submit Advice Letter                                             | 5 days           | Mon 12/18/23       | Fri 12/22/23       |            |
| 661 |                                                                                   | Advice Letter Approved                                           | 1 day            | Fri 12/29/23       | Fri 12/29/23       |            |
| 662 |                                                                                   | Implementation Plan                                              | 1 day            | Mon 1/1/24         | Mon 1/1/24         |            |
| 663 |                                                                                   | <b>SCG - Market Access Program</b>                               | <b>333 days?</b> | <b>Sat 3/16/24</b> | <b>Tue 6/24/25</b> |            |
| 664 |                                                                                   | RFP Preparation                                                  | 75 days          | Sat 3/16/24        | Thu 6/27/24        |            |
| 665 |                                                                                   | RFP Release                                                      | 1 day            | Fri 6/21/24        | Fri 6/21/24        |            |
| 666 |                                                                                   | RFP Proposal Creation Duration                                   | 53 days          | Mon 6/24/24        | Wed 9/4/24         |            |
| 667 |                                                                                   | RFP Evaluation                                                   | 38 days          | Mon 8/19/24        | Wed 10/9/24        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |



| ID  |  | Task Name                                                                                                     | Duration         | Start               | Finish            | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------|------------------|---------------------|-------------------|------------|
| 668 |                                                                                   | RFP Review with EE PRG                                                                                        | 1 day            | Tue 10/1/24         | Tue 10/1/24       |            |
| 669 |                                                                                   | RFP Estimated Notification of Successful and Unsuccessful Bidder                                              | 1 day            | Tue 10/8/24         | Tue 10/8/24       |            |
| 670 |                                                                                   | Contract Negotiation and Development                                                                          | 78 days          | Mon 10/14/24        | Wed 1/29/25       |            |
| 671 |                                                                                   | Contract Review with EE PRG                                                                                   | 10 days          | Tue 1/7/25          | Mon 1/20/25       |            |
| 672 |                                                                                   | Final Award and Contract Signed                                                                               | 11 days          | Mon 1/20/25         | Mon 2/3/25        |            |
| 673 |                                                                                   | Submit Advice Letter                                                                                          | N/A              | Wed 1/1/25          |                   |            |
| 674 |                                                                                   | Advice Letter Approved                                                                                        | N/A              | Mon 3/3/25          |                   |            |
| 675 |                                                                                   | Implementation Plan                                                                                           | 59 days          | Thu 4/3/25          | Tue 6/24/25       |            |
| 676 |                                                                                   | <b>SCG - IDEEA 365 (Round 3)</b>                                                                              | <b>230 days?</b> | <b>Tue 10/15/24</b> | <b>Mon 9/1/25</b> |            |
| 677 |                                                                                   | RFP Preparation                                                                                               | 23 days          | Tue 10/15/24        | Thu 11/14/24      |            |
| 678 |                                                                                   | RFP Release                                                                                                   | 20 days          | Fri 11/15/24        | Thu 12/12/24      |            |
| 679 |                                                                                   | RFP Proposal Creation Duration                                                                                | 43 days          | Fri 12/13/24        | Tue 2/11/25       |            |
| 680 |                                                                                   | RFP Evaluation                                                                                                | 12 days          | Wed 2/12/25         | Thu 2/27/25       |            |
| 681 |                                                                                   | RFP Review with EE PRG                                                                                        | 1 day            | Fri 2/28/25         | Fri 2/28/25       |            |
| 682 |                                                                                   | RFP Estimated Notification of Successful and Unsuccessful Bidder                                              | 23 days          | Mon 3/3/25          | Wed 4/2/25        |            |
| 683 |                                                                                   | Contract Negotiation and Development                                                                          | 21 days          | Thu 4/3/25          | Thu 5/1/25        |            |
| 684 |                                                                                   | Contract Review with EE PRG                                                                                   | 32 days          | Fri 5/2/25          | Mon 6/16/25       |            |
| 685 |                                                                                   | Final Award and Contract Signed                                                                               | 17 days          | Tue 6/17/25         | Wed 7/9/25        |            |
| 686 |                                                                                   | Submit Advice Letter                                                                                          | 10 days          | Thu 7/10/25         | Wed 7/23/25       |            |
| 687 |                                                                                   | Advice Letter Approved                                                                                        | 11 days          | Thu 7/24/25         | Thu 8/7/25        |            |
| 688 |                                                                                   | Implementation Plan                                                                                           | 9 days           | Fri 8/8/25          | Wed 8/20/25       |            |
| 689 |                                                                                   |                                                                                                               |                  |                     |                   |            |
| 690 |                                                                                   | <b>Please note the SDG&amp;E Solicitations marked with an * are estimated dates and are subject to change</b> |                  |                     |                   |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                | Duration        | Start             | Finish             | 2018<br>H1                                                                          |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|-------------------|--------------------|-------------------------------------------------------------------------------------|
| 691 |                                                                                   | <b>SDG&amp;E - Small Commercial (&lt;20kW) Solicitation</b>              | <b>612 days</b> | <b>Wed 8/1/18</b> | <b>Thu 12/3/20</b> |  |
| 692 |                                                                                   | SDG&E - RFA Preparation                                                  | 69 days         | Wed 8/1/18        | Mon 11/5/18        |                                                                                     |
| 693 |                                                                                   | SDG&E - RFA Release                                                      | 0 days          | Mon 11/5/18       | Mon 11/5/18        |                                                                                     |
| 694 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 25 days         | Mon 11/5/18       | Fri 12/7/18        |                                                                                     |
| 695 |                                                                                   | SDG&E - RFA Evaluation                                                   | 28 days         | Fri 12/7/18       | Tue 1/15/19        |                                                                                     |
| 696 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 0 days          | Sat 2/2/19        | Sat 2/2/19         |                                                                                     |
| 697 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Mon 4/1/19        | Mon 4/1/19         |                                                                                     |
| 698 |                                                                                   | SDG&E - RFP Preparation                                                  | 55 days         | Tue 4/2/19        | Mon 6/17/19        |                                                                                     |
| 699 |                                                                                   | SDG&E - RFP Release                                                      | 0 days          | Tue 6/18/19       | Tue 6/18/19        |                                                                                     |
| 700 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 51 days         | Tue 6/18/19       | Tue 8/27/19        |                                                                                     |
| 701 |                                                                                   | SDG&E - RFP Evaluation                                                   | 48 days         | Wed 8/28/19       | Fri 11/1/19        |                                                                                     |
| 702 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Wed 1/1/20        | Wed 1/1/20         |                                                                                     |
| 703 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 0 days          | Tue 2/11/20       | Tue 2/11/20        |                                                                                     |
| 704 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 55 days         | Mon 2/17/20       | Fri 5/1/20         |                                                                                     |
| 705 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 0 days          | Tue 6/9/20        | Tue 6/9/20         |                                                                                     |
| 706 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 0 days          | Tue 6/30/20       | Tue 6/30/20        |                                                                                     |
| 707 |                                                                                   | SDG&E - Submit Advice Letter                                             | 0 days          | Wed 8/12/20       | Wed 8/12/20        |                                                                                     |
| 708 |                                                                                   | SDG&E - Advice Letter Approved                                           | 23 days         | Wed 8/12/20       | Fri 9/11/20        |                                                                                     |
| 709 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days         | Fri 9/11/20       | Thu 12/3/20        |                                                                                     |
| 710 |                                                                                   | <b>SDG&amp;E - Large Commercial (&gt;20kW) Solicitation</b>              | <b>612 days</b> | <b>Wed 8/1/18</b> | <b>Thu 12/3/20</b> |  |
| 711 |                                                                                   | SDG&E - RFA Preparation                                                  | 69 days         | Wed 8/1/18        | Mon 11/5/18        |                                                                                     |
| 712 |                                                                                   | SDG&E - RFA Release                                                      | 0 days          | Mon 11/5/18       | Mon 11/5/18        |                                                                                     |
| 713 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 25 days         | Mon 11/5/18       | Fri 12/7/18        |                                                                                     |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                | Duration        | Start             | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|-------------------|--------------------|------------|
| 714 |                                                                                   | SDG&E - RFA Evaluation                                                   | 28 days         | Fri 12/7/18       | Tue 1/15/19        |            |
| 715 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 0 days          | Sat 2/2/19        | Sat 2/2/19         |            |
| 716 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Mon 4/1/19        | Mon 4/1/19         |            |
| 717 |                                                                                   | SDG&E - RFP Preparation                                                  | 55 days         | Tue 4/2/19        | Mon 6/17/19        |            |
| 718 |                                                                                   | SDG&E - RFP Release                                                      | 0 days          | Tue 6/18/19       | Tue 6/18/19        |            |
| 719 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 51 days         | Tue 6/18/19       | Tue 8/27/19        |            |
| 720 |                                                                                   | SDG&E - RFP Evaluation                                                   | 48 days         | Wed 8/28/19       | Fri 11/1/19        |            |
| 721 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Wed 1/1/20        | Wed 1/1/20         |            |
| 722 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 0 days          | Tue 2/11/20       | Tue 2/11/20        |            |
| 723 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 55 days         | Mon 2/17/20       | Fri 5/1/20         |            |
| 724 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 0 days          | Tue 5/12/20       | Tue 5/12/20        |            |
| 725 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 0 days          | Tue 6/30/20       | Tue 6/30/20        |            |
| 726 |                                                                                   | SDG&E - Submit Advice Letter                                             | 0 days          | Wed 8/12/20       | Wed 8/12/20        |            |
| 727 |                                                                                   | SDG&E - Advice Letter Approved                                           | 23 days         | Wed 8/12/20       | Fri 9/11/20        |            |
| 728 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days         | Fri 9/11/20       | Thu 12/3/20        |            |
| 729 |                                                                                   | <b>SDG&amp;E - Residential Multi-Family Solicitation</b>                 | <b>586 days</b> | <b>Thu 9/6/18</b> | <b>Thu 12/3/20</b> |            |
| 730 |                                                                                   | SDG&E - RFA Preparation                                                  | 64 days         | Thu 9/6/18        | Tue 12/4/18        |            |
| 731 |                                                                                   | SDG&E - RFA Release                                                      | 23 days         | Tue 12/4/18       | Thu 1/3/19         |            |
| 732 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 49 days         | Tue 9/11/18       | Fri 11/16/18       |            |
| 733 |                                                                                   | SDG&E - RFA Evaluation                                                   | 21 days         | Mon 1/7/19        | Mon 2/4/19         |            |
| 734 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 0 days          | Tue 11/13/18      | Tue 11/13/18       |            |
| 735 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Wed 3/20/19       | Wed 3/20/19        |            |
| 736 |                                                                                   | SDG&E - RFP Preparation                                                  | 63 days         | Fri 3/22/19       | Tue 6/18/19        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                | Duration        | Start              | Finish            | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|--------------------|-------------------|------------|
| 737 |                                                                                   | SDG&E - RFP Release                                                      | 52 days         | Tue 6/18/19        | Wed 8/28/19       |            |
| 738 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 36 days         | Mon 3/25/19        | Mon 5/13/19       |            |
| 739 |                                                                                   | SDG&E - RFP Evaluation                                                   | 30 days         | Thu 8/29/19        | Wed 10/9/19       |            |
| 740 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 6 days          | Thu 12/12/19       | Thu 12/19/19      |            |
| 741 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 0 days          | Tue 3/10/20        | Tue 3/10/20       |            |
| 742 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 35 days         | Mon 4/13/20        | Fri 5/29/20       |            |
| 743 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 10 days         | Thu 6/4/20         | Wed 6/17/20       |            |
| 744 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 0 days          | Mon 6/22/20        | Mon 6/22/20       |            |
| 745 |                                                                                   | SDG&E - Submit Advice Letter                                             | 0 days          | Wed 8/12/20        | Wed 8/12/20       |            |
| 746 |                                                                                   | SDG&E - Advice Letter Approved                                           | 23 days         | Wed 8/12/20        | Fri 9/11/20       |            |
| 747 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days         | Fri 9/11/20        | Thu 12/3/20       |            |
| 748 |                                                                                   | <b>SDG&amp;E - SW HVAC Solicitation</b>                                  | <b>593 days</b> | <b>Thu 11/1/18</b> | <b>Tue 2/9/21</b> |            |
| 749 |                                                                                   | SDG&E - RFA Preparation                                                  | 48 days         | Thu 11/1/18        | Mon 1/7/19        |            |
| 750 |                                                                                   | SDG&E - RFA Release                                                      | 0 days          | Mon 1/7/19         | Mon 1/7/19        |            |
| 751 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 24 days         | Mon 1/7/19         | Thu 2/7/19        |            |
| 752 |                                                                                   | SDG&E - RFA Evaluation                                                   | 37 days         | Fri 2/8/19         | Sun 3/31/19       |            |
| 753 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 0 days          | Tue 4/9/19         | Tue 4/9/19        |            |
| 754 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Wed 4/17/19        | Wed 4/17/19       |            |
| 755 |                                                                                   | SDG&E - RFP Preparation                                                  | 73 days         | Thu 4/18/19        | Mon 7/29/19       |            |
| 756 |                                                                                   | SDG&E - RFP Release                                                      | 0 days          | Tue 9/3/19         | Tue 9/3/19        |            |
| 757 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 30 days         | Tue 9/3/19         | Mon 10/14/19      |            |
| 758 |                                                                                   | SDG&E - RFP Evaluation                                                   | 33 days         | Mon 10/14/19       | Wed 11/27/19      |            |
| 759 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Tue 1/21/20        | Tue 1/21/20       |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                | Duration        | Start              | Finish            | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|--------------------|-------------------|------------|
| 760 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 0 days          | Tue 3/10/20        | Tue 3/10/20       |            |
| 761 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 88 days         | Wed 3/25/20        | Fri 7/24/20       |            |
| 762 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 0 days          | Tue 9/8/20         | Tue 9/8/20        |            |
| 763 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 0 days          | Fri 10/30/20       | Fri 10/30/20      |            |
| 764 |                                                                                   | SDG&E - Submit Advice Letter                                             | 0 days          | Thu 11/12/20       | Thu 11/12/20      |            |
| 765 |                                                                                   | SDG&E - Advice Letter Approved                                           | 0 days          | Fri 12/11/20       | Fri 12/11/20      |            |
| 766 |                                                                                   | SDG&E - Implementation Plan                                              | 0 days          | Tue 2/9/21         | Tue 2/9/21        |            |
| 767 |                                                                                   | <b>SDG&amp;E - SW PLA Solicitation</b>                                   | <b>853 days</b> | <b>Mon 1/28/19</b> | <b>Wed 5/4/22</b> |            |
| 768 |                                                                                   | SDG&E - RFA Preparation                                                  | 75 days         | Mon 1/28/19        | Fri 5/10/19       |            |
| 769 |                                                                                   | SDG&E - RFA Release                                                      | 0 days          | Fri 5/10/19        | Fri 5/10/19       |            |
| 770 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 31 days         | Fri 5/10/19        | Fri 6/21/19       |            |
| 771 |                                                                                   | SDG&E - RFA Evaluation                                                   | 65 days         | Mon 6/24/19        | Fri 9/20/19       |            |
| 772 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 0 days          | Tue 9/10/19        | Tue 9/10/19       |            |
| 773 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Fri 9/20/19        | Fri 9/20/19       |            |
| 774 |                                                                                   | SDG&E - RFP Preparation                                                  | 52 days         | Fri 9/20/19        | Mon 12/2/19       |            |
| 775 |                                                                                   | SDG&E - RFP Release                                                      | 0 days          | Mon 1/27/20        | Mon 1/27/20       |            |
| 776 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 31 days         | Mon 1/27/20        | Mon 3/9/20        |            |
| 777 |                                                                                   | SDG&E - RFP Evaluation                                                   | 82 days         | Mon 3/9/20         | Tue 6/30/20       |            |
| 778 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Mon 8/17/20        | Mon 8/17/20       |            |
| 779 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 66 days         | Tue 10/13/20       | Tue 1/12/21       |            |
| 780 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 197 days        | Fri 1/29/21        | Mon 11/1/21       |            |
| 781 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 0 days          | Tue 11/9/21        | Tue 11/9/21       |            |
| 782 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 0 days          | Fri 1/7/22         | Fri 1/7/22        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                | Duration        | Start              | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 783 |                                                                                   | SDG&E - Submit Advice Letter                                             | 0 days          | Mon 1/10/22        | Mon 1/10/22        |            |
| 784 |                                                                                   | SDG&E - Advice Letter Approved                                           | 0 days          | Thu 2/10/22        | Thu 2/10/22        |            |
| 785 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days         | Thu 2/10/22        | Wed 5/4/22         |            |
| 786 |                                                                                   | <b>SDG&amp;E - Residential Single-Family 2.0 Solicitation</b>            | <b>467 days</b> | <b>Tue 1/19/21</b> | <b>Wed 11/2/22</b> |            |
| 787 |                                                                                   | SDG&E - RFA Preparation                                                  | 43 days         | Tue 1/19/21        | Thu 3/18/21        |            |
| 788 |                                                                                   | SDG&E - RFA Release                                                      | 0 days          | Mon 3/22/21        | Mon 3/22/21        |            |
| 789 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 22 days         | Mon 3/22/21        | Tue 4/20/21        |            |
| 790 |                                                                                   | SDG&E - RFA Evaluation                                                   | 38 days         | Wed 4/21/21        | Fri 6/11/21        |            |
| 791 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 7 days          | Thu 6/3/21         | Fri 6/11/21        |            |
| 792 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Tue 6/15/21        | Tue 6/15/21        |            |
| 793 |                                                                                   | SDG&E - RFP Preparation                                                  | 43 days         | Wed 6/16/21        | Fri 8/13/21        |            |
| 794 |                                                                                   | SDG&E - RFP Release                                                      | 0 days          | Wed 8/18/21        | Wed 8/18/21        |            |
| 795 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 32 days         | Wed 8/18/21        | Thu 9/30/21        |            |
| 796 |                                                                                   | SDG&E - RFP Evaluation                                                   | 44 days         | Fri 10/1/21        | Wed 12/1/21        |            |
| 797 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Tue 12/14/21       | Tue 12/14/21       |            |
| 798 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 7 days          | Thu 12/2/21        | Fri 12/10/21       |            |
| 799 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 96 days         | Mon 12/20/21       | Mon 5/2/22         |            |
| 800 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 7 days          | Thu 5/5/22         | Fri 5/13/22        |            |
| 801 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 0 days          | Tue 5/31/22        | Tue 5/31/22        |            |
| 802 |                                                                                   | SDG&E - Submit Advice Letter                                             | 0 days          | Fri 6/24/22        | Fri 6/24/22        |            |
| 803 |                                                                                   | SDG&E - Advice Letter Approved                                           | 0 days          | Thu 8/11/22        | Thu 8/11/22        |            |
| 804 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days         | Thu 8/11/22        | Wed 11/2/22        |            |
| 805 |                                                                                   | <b>SDG&amp;E - Residential Single-Family Solicitation</b>                | <b>501 days</b> | <b>Mon 7/1/19</b>  | <b>Tue 6/1/21</b>  |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                | Duration        | Start             | Finish              | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|-------------------|---------------------|------------|
| 806 |                                                                                   | SDG&E - RFA Preparation                                                  | 80 days         | Mon 7/1/19        | Fri 10/18/19        |            |
| 807 |                                                                                   | SDG&E - RFA Release                                                      | 35 days         | Fri 10/18/19      | Thu 12/5/19         |            |
| 808 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 53 days         | Mon 7/22/19       | Wed 10/2/19         |            |
| 809 |                                                                                   | SDG&E - RFA Evaluation                                                   | 29 days         | Fri 12/6/19       | Wed 1/15/20         |            |
| 810 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 0 days          | Tue 10/8/19       | Tue 10/8/19         |            |
| 811 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Thu 2/27/20       | Thu 2/27/20         |            |
| 812 |                                                                                   | SDG&E - RFP Preparation                                                  | 48 days         | Fri 2/28/20       | Tue 5/5/20          |            |
| 813 |                                                                                   | SDG&E - RFP Release                                                      | 0 days          | Mon 4/27/20       | Mon 4/27/20         |            |
| 814 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 32 days         | Mon 4/27/20       | Tue 6/9/20          |            |
| 815 |                                                                                   | SDG&E - RFP Evaluation                                                   | 16 days         | Wed 6/10/20       | Wed 7/1/20          |            |
| 816 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 2 days          | Thu 7/23/20       | Fri 7/24/20         |            |
| 817 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 7 days          | Thu 8/6/20        | Fri 8/14/20         |            |
| 818 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 60 days         | Mon 8/17/20       | Fri 11/6/20         |            |
| 819 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 10 days         | Tue 12/8/20       | Mon 12/21/20        |            |
| 820 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 0 days          | Fri 1/29/21       | Fri 1/29/21         |            |
| 821 |                                                                                   | SDG&E - Submit Advice Letter                                             | 0 days          | Mon 3/1/21        | Mon 3/1/21          |            |
| 822 |                                                                                   | SDG&E - Advice Letter Approved                                           |                 |                   |                     |            |
| 823 |                                                                                   | SDG&E - Implementation Plan                                              | 0 days          | Tue 6/1/21        | Tue 6/1/21          |            |
| 824 |                                                                                   | <b>SDG&amp;E - Public Sector: Federal Solicitation</b>                   | <b>625 days</b> | <b>Mon 7/1/19</b> | <b>Fri 11/19/21</b> |            |
| 825 |                                                                                   | SDG&E - RFA Preparation                                                  | 78 days         | Mon 7/1/19        | Wed 10/16/19        |            |
| 826 |                                                                                   | SDG&E - RFA Release                                                      | 0 days          | Wed 10/16/19      | Wed 10/16/19        |            |
| 827 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 31 days         | Wed 10/16/19      | Wed 11/27/19        |            |
| 828 |                                                                                   | SDG&E - RFA Evaluation                                                   | 39 days         | Tue 12/3/19       | Fri 1/24/20         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                | Duration        | Start             | Finish              | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|-------------------|---------------------|------------|
| 829 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 0 days          | Tue 3/10/20       | Tue 3/10/20         |            |
| 830 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Mon 3/23/20       | Mon 3/23/20         |            |
| 831 |                                                                                   | SDG&E - RFP Preparation                                                  | 22 days         | Thu 3/26/20       | Fri 4/24/20         |            |
| 832 |                                                                                   | SDG&E - RFP Release                                                      | 0 days          | Fri 5/22/20       | Fri 5/22/20         |            |
| 833 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 40 days         | Fri 5/22/20       | Thu 7/16/20         |            |
| 834 |                                                                                   | SDG&E - RFP Evaluation                                                   | 30 days         | Fri 7/17/20       | Thu 8/27/20         |            |
| 835 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Wed 11/18/20      | Wed 11/18/20        |            |
| 836 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 0 days          | Tue 11/10/20      | Tue 11/10/20        |            |
| 837 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 53 days         | Wed 2/17/21       | Fri 4/30/21         |            |
| 838 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 0 days          | Tue 5/11/21       | Tue 5/11/21         |            |
| 839 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 0 days          | Thu 7/1/21        | Thu 7/1/21          |            |
| 840 |                                                                                   | SDG&E - Submit Advice Letter                                             | 0 days          | Wed 7/21/21       | Wed 7/21/21         |            |
| 841 |                                                                                   | SDG&E - Advice Letter Approved                                           | 0 days          | Fri 8/27/21       | Fri 8/27/21         |            |
| 842 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days         | Mon 8/30/21       | Fri 11/19/21        |            |
| 843 |                                                                                   | <b>SDG&amp;E - Public Sector: K-12 Solicitation</b>                      | <b>625 days</b> | <b>Mon 7/1/19</b> | <b>Fri 11/19/21</b> |            |
| 844 |                                                                                   | SDG&E - RFA Preparation                                                  | 78 days         | Mon 7/1/19        | Wed 10/16/19        |            |
| 845 |                                                                                   | SDG&E - RFA Release                                                      | 0 days          | Wed 10/16/19      | Wed 10/16/19        |            |
| 846 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 31 days         | Wed 10/16/19      | Wed 11/27/19        |            |
| 847 |                                                                                   | SDG&E - RFA Evaluation                                                   | 39 days         | Tue 12/3/19       | Fri 1/24/20         |            |
| 848 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 0 days          | Tue 3/10/20       | Tue 3/10/20         |            |
| 849 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Mon 3/23/20       | Mon 3/23/20         |            |
| 850 |                                                                                   | SDG&E - RFP Preparation                                                  | 22 days         | Thu 3/26/20       | Fri 4/24/20         |            |
| 851 |                                                                                   | SDG&E - RFP Release                                                      | 1 day           | Fri 5/22/20       | Fri 5/22/20         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                | Duration        | Start        | Finish             | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|--------------|--------------------|------------|
| 852 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 40 days         | Fri 5/22/20  | Thu 7/16/20        |            |
| 853 |                                                                                   | SDG&E - RFP Evaluation                                                   | 30 days         | Fri 7/17/20  | Thu 8/27/20        |            |
| 854 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Wed 11/18/20 | Wed 11/18/20       |            |
| 855 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 0 days          | Tue 11/10/20 | Tue 11/10/20       |            |
| 856 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 117 days        | Thu 11/19/20 | Fri 4/30/21        |            |
| 857 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 0 days          | Tue 5/11/21  | Tue 5/11/21        |            |
| 858 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 0 days          | Thu 7/1/21   | Thu 7/1/21         |            |
| 859 |                                                                                   | SDG&E - Submit Advice Letter                                             | 0 days          | Wed 7/21/21  | Wed 7/21/21        |            |
| 860 |                                                                                   | SDG&E - Advice Letter Approved                                           | 0 days          | Fri 8/27/21  | Fri 8/27/21        |            |
| 861 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days         | Mon 8/30/21  | Fri 11/19/21       |            |
| 862 |                                                                                   | <b>SDG&amp;E - Public Sector: Local Government Solicitation</b>          | <b>338 days</b> | Tue 10/13/20 | <b>Thu 1/27/22</b> |            |
| 863 |                                                                                   | SDG&E - RFA Preparation                                                  | 10 days         | Fri 10/23/20 | Thu 11/5/20        |            |
| 864 |                                                                                   | SDG&E - RFA Release                                                      | 1 day           | Wed 1/27/21  | Wed 1/27/21        |            |
| 865 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 20 days         | Thu 1/28/21  | Wed 2/24/21        |            |
| 866 |                                                                                   | SDG&E - RFA Evaluation                                                   | 18 days         | Fri 2/26/21  | Tue 3/23/21        |            |
| 867 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 7 days          | Thu 4/8/21   | Fri 4/16/21        |            |
| 868 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Wed 4/21/21  | Wed 4/21/21        |            |
| 869 |                                                                                   | SDG&E - RFP Preparation                                                  | 51 days         | Fri 3/19/21  | Fri 5/28/21        |            |
| 870 |                                                                                   | SDG&E - RFP Release                                                      | 1 day           | Tue 6/1/21   | Tue 6/1/21         |            |
| 871 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 26 days         | Wed 6/2/21   | Wed 7/7/21         |            |
| 872 |                                                                                   | SDG&E - RFP Evaluation                                                   | 26 days         | Thu 7/8/21   | Thu 8/12/21        |            |
| 873 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Mon 10/25/21 | Mon 10/25/21       |            |
| 874 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 7 days          | Tue 10/12/21 | Wed 10/20/21       |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID  |  | Task Name                                                                | Duration        | Start             | Finish              | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|-------------------|---------------------|------------|
| 875 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 41 days         | Fri 11/5/21       | Fri 12/31/21        |            |
| 876 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 7 days          | Thu 1/6/22        | Fri 1/14/22         |            |
| 877 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 9 days          | Mon 1/17/22       | Thu 1/27/22         |            |
| 878 |                                                                                   | SDG&E - Submit Advice Letter                                             | 13 days         | Wed 6/1/22        | Fri 6/17/22         |            |
| 879 |                                                                                   | SDG&E - Advice Letter Approved                                           | 40 days         | Fri 6/17/22       | Thu 8/11/22         |            |
| 880 |                                                                                   | SDG&E - Implementation Plan                                              | 42 days         | Mon 8/15/22       | Tue 10/11/22        |            |
| 881 |                                                                                   | <b>SDG&amp;E - Agricultural Sector: Local Agriculture Solicitation</b>   | <b>447 days</b> | <b>Mon 3/1/21</b> | <b>Tue 11/15/22</b> |            |
| 882 |                                                                                   | SDG&E - RFA Preparation                                                  | 56 days         | Mon 3/1/21        | Mon 5/17/21         |            |
| 883 |                                                                                   | SDG&E - RFA Release                                                      | 0 days          | Mon 4/26/21       | Mon 4/26/21         |            |
| 884 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 20 days         | Tue 4/27/21       | Mon 5/24/21         |            |
| 885 |                                                                                   | SDG&E - RFA Evaluation                                                   | 36 days         | Tue 6/1/21        | Tue 7/20/21         |            |
| 886 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 0 days          | Thu 7/8/21        | Thu 7/8/21          |            |
| 887 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Tue 7/20/21       | Tue 7/20/21         |            |
| 888 |                                                                                   | SDG&E - RFP Preparation                                                  | 48 days         | Tue 7/20/21       | Thu 9/23/21         |            |
| 889 |                                                                                   | SDG&E - RFP Release                                                      | 0 days          | Thu 9/23/21       | Thu 9/23/21         |            |
| 890 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 25 days         | Fri 9/24/21       | Thu 10/28/21        |            |
| 891 |                                                                                   | SDG&E - RFP Evaluation                                                   | 23 days         | Thu 10/28/21      | Mon 11/29/21        |            |
| 892 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 0 days          | Tue 2/1/22        | Tue 2/1/22          |            |
| 893 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 0 days          | Tue 2/8/22        | Tue 2/8/22          |            |
| 894 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 83 days         | Tue 2/1/22        | Thu 5/26/22         |            |
| 895 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 0 days          | Tue 6/14/22       | Tue 6/14/22         |            |
| 896 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 10 days         | Fri 6/18/21       | Thu 7/1/21          |            |
| 897 |                                                                                   | SDG&E - Submit Advice Letter                                             | 0 days          | Fri 7/22/22       | Fri 7/22/22         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID  |  | Task Name                                                                | Duration        | Start             | Finish              | 2018<br>H1 |
|-----|----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|-------------------|---------------------|------------|
| 898 |                                                                                  | SDG&E - Advice Letter Approved                                           | 0 days          | Tue 8/30/22       | Tue 8/30/22         |            |
| 899 |                                                                                  | SDG&E - Implementation Plan                                              | 44 days         | Wed 8/31/22       | Sat 10/29/22        |            |
| 900 |                                                                                  | <b>*SDG&amp;E - Industrial Solicitation</b>                              | <b>426 days</b> | <b>Thu 4/1/21</b> | <b>Thu 11/17/22</b> |            |
| 901 |                                                                                  | SDG&E - RFA Preparation                                                  | 56 days         | Thu 4/1/21        | Thu 6/17/21         |            |
| 902 |                                                                                  | SDG&E - RFA Release                                                      | 1 day           | Fri 6/18/21       | Fri 6/18/21         |            |
| 903 |                                                                                  | SDG&E - RFA Abstract Creation Duration                                   | 24 days         | Mon 6/21/21       | Thu 7/22/21         |            |
| 904 |                                                                                  | SDG&E - RFA Evaluation                                                   | 29 days         | Fri 7/23/21       | Wed 9/1/21          |            |
| 905 |                                                                                  | SDG&E - RFA Review with EE PRG                                           | 7 days          | Thu 9/2/21        | Fri 9/10/21         |            |
| 906 |                                                                                  | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 9/21/21       | Tue 9/21/21         |            |
| 907 |                                                                                  | SDG&E - RFP Preparation                                                  | 41 days         | Wed 9/22/21       | Wed 11/17/21        |            |
| 908 |                                                                                  | SDG&E - RFP Release                                                      | 1 day           | Thu 11/18/21      | Thu 11/18/21        |            |
| 909 |                                                                                  | SDG&E - RFP Proposal Creation Duration                                   | 37 days         | Thu 11/18/21      | Fri 1/7/22          |            |
| 910 |                                                                                  | SDG&E - RFP Evaluation                                                   | 26 days         | Mon 1/10/22       | Mon 2/14/22         |            |
| 911 |                                                                                  | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Fri 3/25/22       | Fri 3/25/22         |            |
| 912 |                                                                                  | SDG&E - Selection Review with EE PRG                                     | 7 days          | Thu 3/17/22       | Fri 3/25/22         |            |
| 913 |                                                                                  | SDG&E - Contract Negotiation and Development                             | 87 days         | Mon 3/28/22       | Tue 7/26/22         |            |
| 914 |                                                                                  | SDG&E - Contract Review with EE PRG                                      | 1 day           | Wed 7/27/22       | Wed 7/27/22         |            |
| 915 |                                                                                  | SDG&E - Final Award and Contract Signed                                  | 18 days         | Mon 8/8/22        | Wed 8/31/22         |            |
| 916 |                                                                                  | SDG&E - Submit Advice Letter                                             | 1 day           | Wed 9/21/22       | Wed 9/21/22         |            |
| 917 |                                                                                  | SDG&E - Advice Letter Approved                                           | 1 day           | Fri 12/9/22       | Fri 12/9/22         |            |
| 918 |                                                                                  | SDG&E - Implementation Plan                                              | 60 days         | Fri 12/9/22       | Thu 3/2/23          |            |
| 919 |                                                                                  | <b>*SDG&amp;E - Industrial-Port Tenants Solicitation</b>                 | <b>426 days</b> | <b>Thu 4/1/21</b> | <b>Thu 11/17/22</b> |            |
| 920 |                                                                                  | SDG&E - RFA Preparation                                                  | 56 days         | Thu 4/1/21        | Thu 6/17/21         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




| ID  |  | Task Name                                                                | Duration        | Start             | Finish              | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|-------------------|---------------------|------------|
| 921 |                                                                                   | SDG&E - RFA Release                                                      | 1 day           | Fri 6/18/21       | Fri 6/18/21         |            |
| 922 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 24 days         | Mon 6/21/21       | Thu 7/22/21         |            |
| 923 |                                                                                   | SDG&E - RFA Evaluation                                                   | 29 days         | Fri 7/23/21       | Wed 9/1/21          |            |
| 924 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 7 days          | Thu 9/2/21        | Fri 9/10/21         |            |
| 925 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 9/21/21       | Tue 9/21/21         |            |
| 926 |                                                                                   | SDG&E - RFP Preparation                                                  | 41 days         | Wed 9/22/21       | Wed 11/17/21        |            |
| 927 |                                                                                   | SDG&E - RFP Release                                                      | 1 day           | Thu 11/18/21      | Thu 11/18/21        |            |
| 928 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 37 days         | Thu 11/18/21      | Fri 1/7/22          |            |
| 929 |                                                                                   | SDG&E - RFP Evaluation                                                   | 26 days         | Mon 1/10/22       | Mon 2/14/22         |            |
| 930 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Fri 3/25/22       | Fri 3/25/22         |            |
| 931 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 7 days          | Thu 3/17/22       | Fri 3/25/22         |            |
| 932 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 87 days         | Mon 3/28/22       | Tue 7/26/22         |            |
| 933 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 1 day           | Wed 7/27/22       | Wed 7/27/22         |            |
| 934 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 18 days         | Mon 8/8/22        | Wed 8/31/22         |            |
| 935 |                                                                                   | SDG&E - Submit Advice Letter                                             | 1 day           | Wed 9/21/22       | Wed 9/21/22         |            |
| 936 |                                                                                   | SDG&E - Advice Letter Approved                                           | 1 day           | Fri 12/9/22       | Fri 12/9/22         |            |
| 937 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days         | Fri 12/9/22       | Thu 3/2/23          |            |
| 938 |                                                                                   | <b>*SDG&amp;E - SW Residential HVAC QI/QM Solicitation</b>               | <b>377 days</b> | <b>Mon 7/5/21</b> | <b>Tue 12/13/22</b> |            |
| 939 |                                                                                   | SDG&E - RFA Preparation                                                  | 48 days         | Mon 7/5/21        | Wed 9/8/21          |            |
| 940 |                                                                                   | SDG&E - RFA Release                                                      | 1 day           | Wed 9/29/21       | Wed 9/29/21         |            |
| 941 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 22 days         | Wed 9/29/21       | Thu 10/28/21        |            |
| 942 |                                                                                   | SDG&E - RFA Evaluation                                                   | 21 days         | Fri 10/29/21      | Fri 11/26/21        |            |
| 943 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 6 days          | Fri 12/10/21      | Fri 12/17/21        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                | Duration        | Start              | Finish            | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|--------------------|-------------------|------------|
| 944 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Wed 12/22/21       | Wed 12/22/21      |            |
| 945 |                                                                                   | SDG&E - RFP Preparation                                                  | 56 days         | Tue 1/4/22         | Tue 3/22/22       |            |
| 946 |                                                                                   | SDG&E - RFP Release                                                      | 1 day           | Tue 3/22/22        | Tue 3/22/22       |            |
| 947 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 23 days         | Wed 3/23/22        | Fri 4/22/22       |            |
| 948 |                                                                                   | SDG&E - RFP Evaluation                                                   | 20 days         | Mon 4/25/22        | Fri 5/20/22       |            |
| 949 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 6/21/22        | Tue 6/21/22       |            |
| 950 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 0 days          | Fri 6/17/22        | Fri 6/17/22       |            |
| 951 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 83 days         | Wed 7/20/22        | Fri 11/11/22      |            |
| 952 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 6 days          | Mon 11/14/22       | Mon 11/21/22      |            |
| 953 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 1 day           | Mon 1/10/22        | Mon 1/10/22       |            |
| 954 |                                                                                   | SDG&E - Submit Advice Letter                                             | 22 days         | Sun 1/15/23        | Mon 2/13/23       |            |
| 955 |                                                                                   | SDG&E - Advice Letter Approved                                           | 1 day           | Fri 4/28/23        | Fri 4/28/23       |            |
| 956 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days         | Fri 4/28/23        | Thu 7/20/23       |            |
| 957 |                                                                                   | <b>*SDG&amp;E - Local/Residential Behavioral Solicitation</b>            | <b>472 days</b> | <b>Mon 4/19/21</b> | <b>Tue 2/7/23</b> |            |
| 958 |                                                                                   | SDG&E - RFA Preparation                                                  | 53 days         | Mon 4/19/21        | Wed 6/30/21       |            |
| 959 |                                                                                   | SDG&E - RFA Release                                                      | 1 day           | Mon 7/26/21        | Mon 7/26/21       |            |
| 960 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 21 days         | Mon 7/26/21        | Mon 8/23/21       |            |
| 961 |                                                                                   | SDG&E - RFA Evaluation                                                   | 30 days         | Tue 8/24/21        | Mon 10/4/21       |            |
| 962 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 7 days          | Thu 10/7/21        | Fri 10/15/21      |            |
| 963 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 10/19/21       | Tue 10/19/21      |            |
| 964 |                                                                                   | SDG&E - RFP Preparation                                                  | 28 days         | Thu 10/21/21       | Mon 11/29/21      |            |
| 965 |                                                                                   | SDG&E - RFP Release                                                      | 1 day           | Wed 12/22/21       | Wed 12/22/21      |            |
| 966 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 20 days         | Wed 12/22/21       | Tue 1/18/22       |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID  |  | Task Name                                                                | Duration         | Start              | Finish            | 2018<br>H1 |
|-----|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|------------------|--------------------|-------------------|------------|
| 967 |                                                                                   | SDG&E - RFP Evaluation                                                   | 28 days          | Wed 1/19/22        | Fri 2/25/22       |            |
| 968 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 3/15/22        | Tue 3/15/22       |            |
| 969 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 7 days           | Thu 3/3/22         | Fri 3/11/22       |            |
| 970 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 119 days         | Fri 3/18/22        | Wed 8/31/22       |            |
| 971 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 7 days           | Thu 9/8/22         | Fri 9/16/22       |            |
| 972 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 1 day            | Fri 10/21/22       | Fri 10/21/22      |            |
| 973 |                                                                                   | SDG&E - Submit Advice Letter                                             | 1 day            | Wed 11/16/22       | Wed 11/16/22      |            |
| 974 |                                                                                   | SDG&E - Advice Letter Approved                                           | 1 day            | Fri 12/16/22       | Fri 12/16/22      |            |
| 975 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days          | Wed 11/16/22       | Tue 2/7/23        |            |
| 976 |                                                                                   | <b>*SDG&amp;E - Small Business Outreach Solicitation</b>                 | <b>298 days?</b> | <b>Wed 4/13/22</b> | <b>Fri 6/2/23</b> |            |
| 977 |                                                                                   | SDG&E - RFA Preparation                                                  | 53 days          | Wed 4/13/22        | Fri 6/24/22       |            |
| 978 |                                                                                   | SDG&E - RFA Release                                                      | 1 day            | Thu 7/7/22         | Thu 7/7/22        |            |
| 979 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 21 days          | Fri 7/8/22         | Fri 8/5/22        |            |
| 980 |                                                                                   | SDG&E - RFA Evaluation                                                   | 30 days          | Mon 8/8/22         | Fri 9/16/22       |            |
| 981 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 5 days           | Mon 9/19/22        | Fri 9/23/22       |            |
| 982 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 9/27/22        | Tue 9/27/22       |            |
| 983 |                                                                                   | SDG&E - RFP Preparation                                                  | 28 days          | Mon 8/8/22         | Wed 9/14/22       |            |
| 984 |                                                                                   | SDG&E - RFP Release                                                      | 1 day            | Tue 10/18/22       | Tue 10/18/22      |            |
| 985 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 31 days          | Tue 10/18/22       | Tue 11/29/22      |            |
| 986 |                                                                                   | SDG&E - RFP Evaluation                                                   | 38 days          | Wed 11/30/22       | Fri 1/20/23       |            |
| 987 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 2/28/23        | Tue 2/28/23       |            |
| 988 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 7 days           | Thu 2/16/23        | Fri 2/24/23       |            |
| 989 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 79 days          | Tue 2/28/23        | Fri 6/16/23       |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                                                       | Duration         | Start              | Finish             | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------|------------------|--------------------|--------------------|------------|
| 990  |                                                                                   | SDG&E - Contract Review with EE PRG                                                             | 4 days           | Wed 6/21/23        | Mon 6/26/23        |            |
| 991  |                                                                                   | SDG&E - Final Award and Contract Signed                                                         | 1 day            | Tue 8/29/23        | Tue 8/29/23        |            |
| 992  |                                                                                   | SDG&E - Submit Advice Letter                                                                    | 1 day            | Fri 9/15/23        | Fri 9/15/23        |            |
| 993  |                                                                                   | SDG&E - Advice Letter Approved                                                                  | 1 day            | Mon 10/16/23       | Mon 10/16/23       |            |
| 994  |                                                                                   | SDG&E - Implementation Plan                                                                     | 46 days          | Mon 10/16/23       | Mon 12/18/23       |            |
| 995  |                                                                                   | <b>*SDG&amp;E - Workforce Education &amp; Training /Integrated Energy Education Solicitatio</b> | <b>353 days?</b> | <b>Mon 1/16/23</b> | <b>Wed 5/22/24</b> |            |
| 996  |                                                                                   | SDG&E - RFP Release                                                                             | 1 day?           | Thu 2/2/23         | Thu 2/2/23         |            |
| 997  |                                                                                   | SDG&E - RFP Evaluation                                                                          | 25 days          | Fri 3/17/23        | Thu 4/20/23        |            |
| 998  |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder                        | 1 day            | Tue 5/16/23        | Tue 5/16/23        |            |
| 999  |                                                                                   | SDG&E - Selection Review with EE PRG                                                            | 5 days           | Tue 5/9/23         | Mon 5/15/23        |            |
| 1000 |                                                                                   | SDG&E - Contract Negotiation and Development                                                    | 94 days          | Fri 5/5/23         | Wed 9/13/23        |            |
| 1001 |                                                                                   | SDG&E - Contract Review with EE PRG                                                             | 7 days           | Tue 10/10/23       | Wed 10/18/23       |            |
| 1002 |                                                                                   | SDG&E - Final Award and Contract Signed                                                         | 1 day            | Tue 11/14/23       | Tue 11/14/23       |            |
| 1003 |                                                                                   | SDG&E - Submit Advice Letter                                                                    | 1 day            | Fri 1/12/24        | Fri 1/12/24        |            |
| 1004 |                                                                                   | SDG&E - Advice Letter Approved                                                                  | 1 day            | Mon 2/12/24        | Mon 2/12/24        |            |
| 1005 |                                                                                   | SDG&E - Implementation Plan                                                                     | 60 days          | Mon 2/12/24        | Fri 5/3/24         |            |
| 1006 |                                                                                   | <b>*SDG&amp;E - Residential Equity Education &amp; Outreach Solicitation</b>                    | <b>331 days?</b> | <b>Fri 1/13/23</b> | <b>Fri 4/19/24</b> |            |
| 1007 |                                                                                   | SDG&E - RFA Release                                                                             | 1 day            | Thu 3/2/23         | Thu 3/2/23         |            |
| 1008 |                                                                                   | SDG&E - RFA Evaluation                                                                          | 21 days          | Wed 4/12/23        | Wed 5/10/23        |            |
| 1009 |                                                                                   | SDG&E - RFA Review with EE PRG                                                                  | 7 days           | Fri 5/19/23        | Mon 5/29/23        |            |
| 1010 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder                        | 1 day            | Tue 5/30/23        | Tue 5/30/23        |            |
| 1011 |                                                                                   | SDG&E - RFP Release                                                                             | 1 day            | Thu 6/1/23         | Thu 6/1/23         |            |
| 1012 |                                                                                   | SDG&E - RFP Evaluation                                                                          | 27 days          | Mon 7/17/23        | Tue 8/22/23        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                                | Duration        | Start              | Finish             | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 1013 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Mon 8/28/23        | Mon 8/28/23        |            |
| 1014 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 7 days          | Wed 8/30/23        | Thu 9/7/23         |            |
| 1015 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 32 days         | Thu 11/2/23        | Fri 12/15/23       |            |
| 1016 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 7 days          | Tue 1/9/24         | Wed 1/17/24        |            |
| 1017 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 1 day           | Mon 2/12/24        | Mon 2/12/24        |            |
| 1018 |                                                                                   | SDG&E - Submit Advice Letter                                             | 1 day           | Mon 2/26/24        | Mon 2/26/24        |            |
| 1019 |                                                                                   | SDG&E - Advice Letter Approved                                           | 1 day           | Mon 4/8/24         | Mon 4/8/24         |            |
| 1020 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days         | Tue 4/9/24         | Mon 7/1/24         |            |
| 1021 |                                                                                   | <b>*SDG&amp;E - Non-Residential Behavioral Solicitation</b>              | <b>398 days</b> | <b>Mon 8/15/22</b> | <b>Wed 2/21/24</b> |            |
| 1022 |                                                                                   | SDG&E - RFA Preparation                                                  | 67 days         | Mon 8/15/22        | Tue 11/15/22       |            |
| 1023 |                                                                                   | SDG&E - RFA Release                                                      | 1 day           | Mon 10/24/22       | Mon 10/24/22       |            |
| 1024 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 27 days         | Tue 8/23/22        | Wed 9/28/22        |            |
| 1025 |                                                                                   | SDG&E - RFA Evaluation                                                   | 16 days         | Tue 11/29/22       | Tue 12/20/22       |            |
| 1026 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 7 days          | Thu 1/5/23         | Fri 1/13/23        |            |
| 1027 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Wed 1/18/23        | Wed 1/18/23        |            |
| 1028 |                                                                                   | SDG&E - RFP Preparation                                                  | 26 days         | Mon 11/14/22       | Mon 12/19/22       |            |
| 1029 |                                                                                   | SDG&E - RFP Release                                                      | 1 day           | Mon 1/23/23        | Mon 1/23/23        |            |
| 1030 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 26 days         | Mon 1/23/23        | Mon 2/27/23        |            |
| 1031 |                                                                                   | SDG&E - RFP Evaluation                                                   | 58 days         | Tue 2/28/23        | Thu 5/18/23        |            |
| 1032 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 6/20/23        | Tue 6/20/23        |            |
| 1033 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 7 days          | Thu 6/8/23         | Fri 6/16/23        |            |
| 1034 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 60 days         | Wed 6/21/23        | Tue 9/12/23        |            |
| 1035 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 7 days          | Thu 10/5/23        | Fri 10/13/23       |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                                | Duration        | Start              | Finish              | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|--------------------|---------------------|------------|
| 1036 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 1 day           | Thu 12/21/23       | Thu 12/21/23        |            |
| 1037 |                                                                                   | SDG&E - Submit Advice Letter                                             | 1 day           | Fri 1/12/24        | Fri 1/12/24         |            |
| 1038 |                                                                                   | SDG&E - Advice Letter Approved                                           | 1 day           | Mon 2/12/24        | Mon 2/12/24         |            |
| 1039 |                                                                                   | SDG&E - Implementation Plan                                              | 60 days         | Mon 2/12/24        | Fri 5/3/24          |            |
| 1040 |                                                                                   | <b>*SDG&amp;E - Retail Offices and Wholesale Solicitation</b>            | <b>419 days</b> | <b>Wed 5/10/23</b> | <b>Mon 12/16/24</b> |            |
| 1041 |                                                                                   | SDG&E - RFA Preparation                                                  | 33 days         | Wed 5/10/23        | Fri 6/23/23         |            |
| 1042 |                                                                                   | SDG&E - RFA Release                                                      | 1 day           | Mon 7/3/23         | Mon 7/3/23          |            |
| 1043 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 31 days         | Tue 7/4/23         | Tue 8/15/23         |            |
| 1044 |                                                                                   | SDG&E - RFA Evaluation                                                   | 19 days         | Wed 8/16/23        | Mon 9/11/23         |            |
| 1045 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 3 days          | Mon 9/18/23        | Wed 9/20/23         |            |
| 1046 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Mon 9/25/23        | Mon 9/25/23         |            |
| 1047 |                                                                                   | SDG&E - RFP Preparation                                                  | 33 days         | Wed 7/5/23         | Fri 8/18/23         |            |
| 1048 |                                                                                   | SDG&E - RFP Release                                                      | 1 day           | Fri 9/29/23        | Fri 9/29/23         |            |
| 1049 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 33 days         | Mon 10/2/23        | Wed 11/15/23        |            |
| 1050 |                                                                                   | SDG&E - RFP Evaluation                                                   | 25 days         | Thu 11/16/23       | Wed 12/20/23        |            |
| 1051 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Mon 2/19/24        | Mon 2/19/24         |            |
| 1052 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 7 days          | Thu 2/8/24         | Fri 2/16/24         |            |
| 1053 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 96 days         | Mon 2/26/24        | Mon 7/8/24          |            |
| 1054 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 6 days          | Wed 7/17/24        | Wed 7/24/24         |            |
| 1055 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 1 day           | Tue 8/27/24        | Tue 8/27/24         |            |
| 1056 |                                                                                   | SDG&E - Submit Advice Letter                                             | 1 day           | Mon 9/16/24        | Mon 9/16/24         |            |
| 1057 |                                                                                   | SDG&E - Advice Letter Approved                                           | 1 day           | Wed 10/16/24       | Wed 10/16/24        |            |
| 1058 |                                                                                   | SDG&E - Implementation Plan                                              | 44 days         | Wed 10/16/24       | Mon 12/16/24        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                                | Duration        | Start              | Finish             | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 1059 |                                                                                   | <b>*SDG&amp;E - Groceries, Restaurants and Food Storage Solicitation</b> | <b>467 days</b> | <b>Wed 6/14/23</b> | <b>Thu 3/27/25</b> |            |
| 1060 |                                                                                   | SDG&E - RFA Preparation                                                  | 33 days         | Wed 6/14/23        | Fri 7/28/23        |            |
| 1061 |                                                                                   | SDG&E - RFA Release                                                      | 1 day           | Tue 8/15/23        | Tue 8/15/23        |            |
| 1062 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 21 days         | Wed 8/16/23        | Wed 9/13/23        |            |
| 1063 |                                                                                   | SDG&E - RFA Evaluation                                                   | 15 days         | Thu 9/14/23        | Wed 10/4/23        |            |
| 1064 |                                                                                   | SDG&E - RFA Review with EE PRG                                           | 5 days          | Wed 10/18/23       | Tue 10/24/23       |            |
| 1065 |                                                                                   | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Mon 10/30/23       | Mon 10/30/23       |            |
| 1066 |                                                                                   | SDG&E - RFP Preparation                                                  | 16 days         | Mon 10/9/23        | Mon 10/30/23       |            |
| 1067 |                                                                                   | SDG&E - RFP Release                                                      | 1 day           | Mon 11/6/23        | Mon 11/6/23        |            |
| 1068 |                                                                                   | SDG&E - RFP Proposal Creation Duration                                   | 40 days         | Mon 11/6/23        | Fri 12/29/23       |            |
| 1069 |                                                                                   | SDG&E - RFP Evaluation                                                   | 34 days         | Fri 12/29/23       | Wed 2/14/24        |            |
| 1070 |                                                                                   | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Wed 3/6/24         | Wed 3/6/24         |            |
| 1071 |                                                                                   | SDG&E - Selection Review with EE PRG                                     | 7 days          | Thu 2/29/24        | Fri 3/8/24         |            |
| 1072 |                                                                                   | SDG&E - Contract Negotiation and Development                             | 144 days        | Wed 3/13/24        | Mon 9/30/24        |            |
| 1073 |                                                                                   | SDG&E - Contract Review with EE PRG                                      | 6 days          | Tue 10/8/24        | Tue 10/15/24       |            |
| 1074 |                                                                                   | SDG&E - Final Award and Contract Signed                                  | 1 day           | Tue 11/26/24       | Tue 11/26/24       |            |
| 1075 |                                                                                   | SDG&E - Submit Advice Letter                                             | 1 day           | Fri 12/27/24       | Fri 12/27/24       |            |
| 1076 |                                                                                   | SDG&E - Advice Letter Approved                                           | 1 day           | Mon 1/27/25        | Mon 1/27/25        |            |
| 1077 |                                                                                   | SDG&E - Implementation Plan                                              | 44 days         | Mon 1/27/25        | Thu 3/27/25        |            |
| 1078 |                                                                                   | <b>*SDG&amp;E - Private Institutions and Healthcare Solicitation</b>     | <b>399 days</b> | <b>Thu 10/5/23</b> | <b>Tue 4/15/25</b> |            |
| 1079 |                                                                                   | SDG&E - RFA Preparation                                                  | 33 days         | Thu 10/5/23        | Mon 11/20/23       |            |
| 1080 |                                                                                   | SDG&E - RFA Release                                                      | 1 day           | Mon 11/27/23       | Mon 11/27/23       |            |
| 1081 |                                                                                   | SDG&E - RFA Abstract Creation Duration                                   | 35 days         | Mon 11/27/23       | Fri 1/12/24        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                                | Duration        | Start               | Finish             | 2018<br>H1 |
|------|----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|---------------------|--------------------|------------|
| 1082 |                                                                                  | SDG&E - RFA Evaluation                                                   | 30 days         | Mon 1/15/24         | Fri 2/23/24        |            |
| 1083 |                                                                                  | SDG&E - RFA Review with EE PRG                                           | 5 days          | Mon 2/26/24         | Fri 3/1/24         |            |
| 1084 |                                                                                  | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Mon 3/4/24          | Mon 3/4/24         |            |
| 1085 |                                                                                  | SDG&E - RFP Preparation                                                  | 54 days         | Mon 11/27/23        | Thu 2/8/24         |            |
| 1086 |                                                                                  | SDG&E - RFP Release                                                      | 1 day           | Fri 3/8/24          | Fri 3/8/24         |            |
| 1087 |                                                                                  | SDG&E - RFP Proposal Creation Duration                                   | 34 days         | Fri 3/8/24          | Wed 4/24/24        |            |
| 1088 |                                                                                  | SDG&E - RFP Evaluation                                                   | 42 days         | Thu 4/25/24         | Fri 6/21/24        |            |
| 1089 |                                                                                  | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 7/2/24          | Tue 7/2/24         |            |
| 1090 |                                                                                  | SDG&E - Selection Review with EE PRG                                     | 7 days          | Fri 6/21/24         | Mon 7/1/24         |            |
| 1091 |                                                                                  | SDG&E - Contract Negotiation and Development                             | 61 days         | Wed 7/31/24         | Wed 10/23/24       |            |
| 1092 |                                                                                  | SDG&E - Contract Review with EE PRG                                      | 4 days          | Tue 11/12/24        | Fri 11/15/24       |            |
| 1093 |                                                                                  | SDG&E - Final Award and Contract Signed                                  | 1 day           | Tue 12/17/24        | Tue 12/17/24       |            |
| 1094 |                                                                                  | SDG&E - Submit Advice Letter                                             | 1 day           | Wed 1/15/25         | Wed 1/15/25        |            |
| 1095 |                                                                                  | SDG&E - Advice Letter Approved                                           | 1 day           | Fri 2/14/25         | Fri 2/14/25        |            |
| 1096 |                                                                                  | SDG&E - Implementation Plan                                              | 43 days         | Fri 2/14/25         | Tue 4/15/25        |            |
| 1097 |                                                                                  | <b>*SDG&amp;E - Lodging: Hotels/Motels Solicitation</b>                  | <b>400 days</b> | <b>Tue 10/10/23</b> | <b>Mon 4/21/25</b> |            |
| 1098 |                                                                                  | SDG&E - RFA Preparation                                                  | 33 days         | Tue 10/10/23        | Thu 11/23/23       |            |
| 1099 |                                                                                  | SDG&E - RFA Release                                                      | 1 day           | Fri 12/8/23         | Fri 12/8/23        |            |
| 1100 |                                                                                  | SDG&E - RFA Abstract Creation Duration                                   | 35 days         | Fri 12/8/23         | Thu 1/25/24        |            |
| 1101 |                                                                                  | SDG&E - RFA Evaluation                                                   | 22 days         | Mon 1/22/24         | Tue 2/20/24        |            |
| 1102 |                                                                                  | SDG&E - RFA Review with EE PRG                                           | 7 days          | Tue 3/12/24         | Wed 3/20/24        |            |
| 1103 |                                                                                  | SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 3/19/24         | Tue 3/19/24        |            |
| 1104 |                                                                                  | SDG&E - RFP Preparation                                                  | 48 days         | Tue 1/23/24         | Thu 3/28/24        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                                | Duration        | Start              | Finish             | 2018<br>H1 |
|------|----------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 1105 |                                                                                  | SDG&E - RFP Release                                                      | 1 day           | Thu 3/21/24        | Thu 3/21/24        |            |
| 1106 |                                                                                  | SDG&E - RFP Proposal Creation Duration                                   | 29 days         | Thu 3/21/24        | Tue 4/30/24        |            |
| 1107 |                                                                                  | SDG&E - RFP Evaluation                                                   | 23 days         | Mon 5/6/24         | Wed 6/5/24         |            |
| 1108 |                                                                                  | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 6/18/24        | Tue 6/18/24        |            |
| 1109 |                                                                                  | SDG&E - Selection Review with EE PRG                                     | 7 days          | Thu 6/20/24        | Fri 6/28/24        |            |
| 1110 |                                                                                  | SDG&E - Contract Negotiation and Development                             | 61 days         | Wed 7/31/24        | Wed 10/23/24       |            |
| 1111 |                                                                                  | SDG&E - Contract Review with EE PRG                                      | 4 days          | Tue 11/12/24       | Fri 11/15/24       |            |
| 1112 |                                                                                  | SDG&E - Final Award and Contract Signed                                  | 1 day           | Tue 12/17/24       | Tue 12/17/24       |            |
| 1113 |                                                                                  | SDG&E - Submit Advice Letter                                             | 1 day           | Thu 1/16/25        | Thu 1/16/25        |            |
| 1114 |                                                                                  | SDG&E - Advice Letter Approved                                           | 1 day           | Thu 2/20/25        | Thu 2/20/25        |            |
| 1115 |                                                                                  | SDG&E - Implementation Plan                                              | 43 days         | Thu 2/20/25        | Mon 4/21/25        |            |
| 1116 |                                                                                  | <b>*SDG&amp;E - Market Access Program (MAP)</b>                          | <b>326 days</b> | <b>Wed 3/13/24</b> | <b>Wed 6/11/25</b> |            |
| 1117 |                                                                                  | SDG&E - RFP Preparation                                                  | 38 days         | Wed 3/13/24        | Fri 5/3/24         |            |
| 1118 |                                                                                  | SDG&E - RFP Release                                                      | 1 day           | Tue 5/7/24         | Tue 5/7/24         |            |
| 1119 |                                                                                  | SDG&E - RFP Proposal Creation Duration                                   | 31 days         | Tue 5/7/24         | Tue 6/18/24        |            |
| 1120 |                                                                                  | SDG&E - RFP Evaluation                                                   | 43 days         | Wed 6/19/24        | Fri 8/16/24        |            |
| 1121 |                                                                                  | SDG&E - Selection Review with EE PRG                                     | 7 days          | Thu 9/5/24         | Fri 9/13/24        |            |
| 1122 |                                                                                  | SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day           | Tue 9/17/24        | Tue 9/17/24        |            |
| 1123 |                                                                                  | SDG&E - Contract Negotiation and Development                             | 60 days         | Fri 9/27/24        | Thu 12/19/24       |            |
| 1124 |                                                                                  | SDG&E - Contract Review with EE PRG                                      | 3 days          | Tue 12/10/24       | Thu 12/12/24       |            |
| 1125 |                                                                                  | SDG&E - Final Award and Contract Signed                                  | 1 day           | Fri 1/31/25        | Fri 1/31/25        |            |
| 1126 |                                                                                  | SDG&E - Submit Advice Letter                                             | 1 day           | Wed 3/12/25        | Wed 3/12/25        |            |
| 1127 |                                                                                  | SDG&E - Advice Letter Approved                                           | 1 day           | Fri 4/11/25        | Fri 4/11/25        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                                                          | Duration         | Start              | Finish             | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------|------------------|--------------------|--------------------|------------|
| 1128 |                                                                                   | SDG&E - Implementation Plan                                                                        | 44 days          | Fri 4/11/25        | Wed 6/11/25        |            |
| 1129 |                                                                                   | Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change |                  |                    |                    |            |
| 1130 |                                                                                   |                                                                                                    |                  |                    |                    |            |
| 1131 |                                                                                   | <b>PG&amp;E - Local Government Partnerships (non-resource programs) Solicitation</b>               | <b>376 days?</b> | <b>Fri 3/22/19</b> | <b>Fri 8/28/20</b> |            |
| 1132 |                                                                                   | PG&E - RFA Preparation                                                                             | 42 days          | Fri 3/22/19        | Mon 5/20/19        |            |
| 1133 |                                                                                   | PG&E - RFA Release                                                                                 | 1 day            | Thu 5/23/19        | Thu 5/23/19        |            |
| 1134 |                                                                                   | PG&E - RFA Abstract Creation Duration                                                              | 22 days          | Thu 5/23/19        | Fri 6/21/19        |            |
| 1135 |                                                                                   | PG&E - RFA Evaluation                                                                              | 15 days          | Mon 6/24/19        | Fri 7/12/19        |            |
| 1136 |                                                                                   | PG&E - RFA Review with EE PRG                                                                      | 4 days           | Tue 7/23/19        | Fri 7/26/19        |            |
| 1137 |                                                                                   | PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder                            | 5 days           | Mon 8/5/19         | Fri 8/9/19         |            |
| 1138 |                                                                                   | PG&E - RFP Preparation                                                                             | 45 days          | Tue 8/27/19        | Mon 10/28/19       |            |
| 1139 |                                                                                   | PG&E - RFP Release                                                                                 | 1 day            | Mon 11/4/19        | Mon 11/4/19        |            |
| 1140 |                                                                                   | PG&E - RFP Proposal Creation Duration                                                              | 33 days          | Mon 11/4/19        | Wed 12/18/19       |            |
| 1141 |                                                                                   | PG&E - RFP Evaluation                                                                              | 18 days          | Mon 1/6/20         | Wed 1/29/20        |            |
| 1142 |                                                                                   | PG&E - RFP Review with EE PRG                                                                      | 4 days           | Tue 2/25/20        | Fri 2/28/20        |            |
| 1143 |                                                                                   | PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder                            | 5 days           | Mon 3/2/20         | Fri 3/6/20         |            |
| 1144 |                                                                                   | PG&E - Contract Negotiation and Development                                                        | 58 days          | Fri 2/28/20        | Tue 5/19/20        |            |
| 1145 |                                                                                   | PG&E - Contract Review with EE PRG                                                                 | 7 days           | Tue 5/26/20        | Wed 6/3/20         |            |
| 1146 |                                                                                   | PG&E - Final Award and Contract Signed                                                             | 22 days          | Fri 5/29/20        | Mon 6/29/20        |            |
| 1147 |                                                                                   | PG&E - Submit Advice Letter                                                                        |                  | N/A                | N/A                |            |
| 1148 |                                                                                   | PG&E - Advice Letter Approved                                                                      |                  |                    |                    |            |
| 1149 |                                                                                   | PG&E - Implementation Plan                                                                         | 24 days          | Tue 7/28/20        | Fri 8/28/20        |            |
| 1150 |                                                                                   | <b>PG&amp;E - Statewide Codes &amp; Standards (RFP only) Solicitation</b>                          | <b>221 days?</b> | <b>Mon 7/8/19</b>  | <b>Mon 5/11/20</b> |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                               | Duration         | Start              | Finish             | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|-------------------------------------------------------------------------|------------------|--------------------|--------------------|------------|
| 1151 |                                                                                   | PG&E - RFA Preparation                                                  |                  | N/A                | N/A                |            |
| 1152 |                                                                                   | PG&E - RFA Release                                                      |                  | N/A                | N/A                |            |
| 1153 |                                                                                   | PG&E - RFA Abstract Creation Duration                                   |                  | N/A                | N/A                |            |
| 1154 |                                                                                   | PG&E - RFA Evaluation                                                   |                  | N/A                | N/A                |            |
| 1155 |                                                                                   | PG&E - RFA Review with EE PRG                                           |                  | N/A                | N/A                |            |
| 1156 |                                                                                   | PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder |                  | N/A                | N/A                |            |
| 1157 |                                                                                   | PG&E - RFP Preparation                                                  | 36 days          | Mon 7/8/19         | Mon 8/26/19        |            |
| 1158 |                                                                                   | PG&E - RFP Release                                                      | 1 day            | Tue 9/10/19        | Tue 9/10/19        |            |
| 1159 |                                                                                   | PG&E - RFP Proposal Creation Duration                                   | 24 days          | Tue 9/10/19        | Fri 10/11/19       |            |
| 1160 |                                                                                   | PG&E - RFP Evaluation                                                   | 10 days          | Mon 10/14/19       | Fri 10/25/19       |            |
| 1161 |                                                                                   | PG&E - RFP Review with EE PRG                                           | 4 days           | Thu 11/21/19       | Tue 11/26/19       |            |
| 1162 |                                                                                   | PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 3 days           | Wed 11/27/19       | Fri 11/29/19       |            |
| 1163 |                                                                                   | PG&E - Contract Negotiation and Development                             | 35 days          | Mon 12/2/19        | Fri 1/17/20        |            |
| 1164 |                                                                                   | PG&E - Contract Review with EE PRG                                      | 4 days           | Tue 1/21/20        | Fri 1/24/20        |            |
| 1165 |                                                                                   | PG&E - Final Award and Contract Signed                                  | 32 days          | Wed 1/29/20        | Thu 3/12/20        |            |
| 1166 |                                                                                   | PG&E - Submit Advice Letter                                             |                  | N/A                | N/A                |            |
| 1167 |                                                                                   | PG&E - Advice Letter Approved                                           |                  |                    |                    |            |
| 1168 |                                                                                   | PG&E - Implementation Plan                                              | 32 days          | Fri 3/27/20        | Mon 5/11/20        |            |
| 1169 |                                                                                   | <b>PG&amp;E - Local Multi-Sector (40% outsource) Solicitation</b>       | <b>251 days?</b> | <b>Tue 4/28/20</b> | <b>Tue 4/13/21</b> |            |
| 1170 |                                                                                   | PG&E - RFA Preparation                                                  |                  | N/A                | N/A                |            |
| 1171 |                                                                                   | PG&E - RFA Release                                                      |                  | N/A                | N/A                |            |
| 1172 |                                                                                   | PG&E - RFA Abstract Creation Duration                                   |                  | N/A                | N/A                |            |
| 1173 |                                                                                   | PG&E - RFA Evaluation                                                   |                  | N/A                | N/A                |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                                    | Duration        | Start              | Finish             | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|------------------------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 1174 |                                                                                   | PG&E - RFA Review with EE PRG                                                |                 | N/A                | N/A                |            |
| 1175 |                                                                                   | PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder      |                 | N/A                | N/A                |            |
| 1176 |                                                                                   | PG&E - RFP Preparation                                                       |                 | N/A                | N/A                |            |
| 1177 |                                                                                   | PG&E - RFP Release                                                           |                 | N/A                | N/A                |            |
| 1178 |                                                                                   | PG&E - RFP Proposal Creation Duration                                        |                 | N/A                | N/A                |            |
| 1179 |                                                                                   | PG&E - RFP Evaluation                                                        |                 | N/A                | N/A                |            |
| 1180 |                                                                                   | PG&E - RFP Review with EE PRG                                                | 4 days          | Tue 4/28/20        | Fri 5/1/20         |            |
| 1181 |                                                                                   | PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder      |                 |                    |                    |            |
| 1182 |                                                                                   | PG&E - Contract Negotiation and Development                                  | 81 days         | Thu 7/2/20         | Thu 10/22/20       |            |
| 1183 |                                                                                   | PG&E - Contract Review with EE PRG                                           | 24 days         | Thu 10/22/20       | Tue 11/24/20       |            |
| 1184 |                                                                                   | PG&E - Final Award and Contract Signed                                       | 23 days         | Mon 11/30/20       | Wed 12/30/20       |            |
| 1185 |                                                                                   | PG&E - Submit Advice Letter                                                  | 1 day           | Wed 1/13/21        | Wed 1/13/21        |            |
| 1186 |                                                                                   | PG&E - Advice Letter Approved                                                | 1 day?          | Fri 2/12/21        | Fri 2/12/21        |            |
| 1187 |                                                                                   | PG&E - Implementation Plan                                                   | 43 days         | Sat 2/13/21        | Tue 4/13/21        |            |
| 1188 |                                                                                   | <b>PG&amp;E - Statewide New Constructions (Non-Residential) Solicitation</b> | <b>591 days</b> | <b>Mon 3/25/19</b> | <b>Sun 6/27/21</b> |            |
| 1189 |                                                                                   | PG&E - RFA Preparation                                                       | 45 days         | Mon 3/25/19        | Fri 5/24/19        |            |
| 1190 |                                                                                   | PG&E - RFA Release                                                           | 1 day           | Tue 5/28/19        | Tue 5/28/19        |            |
| 1191 |                                                                                   | PG&E - RFA Abstract Creation Duration                                        | 24 days         | Tue 5/28/19        | Fri 6/28/19        |            |
| 1192 |                                                                                   | PG&E - RFA Evaluation                                                        | 19 days         | Tue 7/2/19         | Fri 7/26/19        |            |
| 1193 |                                                                                   | PG&E - RFA Review with EE PRG                                                | 4 days          | Tue 8/20/19        | Fri 8/23/19        |            |
| 1194 |                                                                                   | PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder      | 4 days          | Tue 8/27/19        | Fri 8/30/19        |            |
| 1195 |                                                                                   | PG&E - RFP Preparation                                                       | 45 days         | Fri 12/27/19       | Thu 2/27/20        |            |
| 1196 |                                                                                   | PG&E - RFP Release                                                           | 1 day           | Mon 3/16/20        | Mon 3/16/20        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID   |  | Task Name                                                               | Duration         | Start              | Finish            | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|-------------------------------------------------------------------------|------------------|--------------------|-------------------|------------|
| 1197 |                                                                                   | PG&E - RFP Proposal Creation Duration                                   | 40 days          | Tue 3/17/20        | Mon 5/11/20       |            |
| 1198 |                                                                                   | PG&E - RFP Evaluation                                                   | 52 days          | Tue 5/12/20        | Wed 7/22/20       |            |
| 1199 |                                                                                   | PG&E - RFP Review with EE PRG                                           | 8 days           | Fri 7/24/20        | Tue 8/4/20        |            |
| 1200 |                                                                                   | PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 6 days           | Wed 8/5/20         | Wed 8/12/20       |            |
| 1201 |                                                                                   | PG&E - Contract Negotiation and Development                             | 49 days          | Mon 8/17/20        | Thu 10/22/20      |            |
| 1202 |                                                                                   | PG&E - Contract Review with EE PRG                                      | 24 days          | Thu 10/22/20       | Tue 11/24/20      |            |
| 1203 |                                                                                   | PG&E - Final Award and Contract Signed                                  | 23 days          | Mon 11/30/20       | Wed 12/30/20      |            |
| 1204 |                                                                                   | PG&E - Submit Advice Letter                                             | 1 day            | Fri 2/19/21        | Fri 2/19/21       |            |
| 1205 |                                                                                   | PG&E - Advice Letter Approved                                           | 1 day            | Wed 4/28/21        | Wed 4/28/21       |            |
| 1206 |                                                                                   | PG&E - Implementation Plan                                              | 43 days          | Thu 4/29/21        | Sun 6/27/21       |            |
| 1207 |                                                                                   | <b>PG&amp;E - Statewide New Construction (Residential) Solicitation</b> | <b>640 days?</b> | <b>Mon 3/25/19</b> | <b>Fri 9/3/21</b> |            |
| 1208 |                                                                                   | PG&E - RFA Preparation                                                  | 45 days          | Mon 3/25/19        | Fri 5/24/19       |            |
| 1209 |                                                                                   | PG&E - RFA Release                                                      | 1 day            | Tue 5/28/19        | Tue 5/28/19       |            |
| 1210 |                                                                                   | PG&E - RFA Abstract Creation Duration                                   | 24 days          | Tue 5/28/19        | Fri 6/28/19       |            |
| 1211 |                                                                                   | PG&E - RFA Evaluation                                                   | 19 days          | Tue 7/2/19         | Fri 7/26/19       |            |
| 1212 |                                                                                   | PG&E - RFA Review with EE PRG                                           | 4 days           | Tue 8/20/19        | Fri 8/23/19       |            |
| 1213 |                                                                                   | PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 4 days           | Tue 8/27/19        | Fri 8/30/19       |            |
| 1214 |                                                                                   | PG&E - RFP Preparation                                                  | 45 days          | Fri 12/27/19       | Thu 2/27/20       |            |
| 1215 |                                                                                   | PG&E - RFP Release                                                      | 1 day            | Mon 3/16/20        | Mon 3/16/20       |            |
| 1216 |                                                                                   | PG&E - RFP Proposal Creation Duration                                   | 40 days          | Tue 3/17/20        | Mon 5/11/20       |            |
| 1217 |                                                                                   | PG&E - RFP Evaluation                                                   | 52 days          | Tue 5/12/20        | Wed 7/22/20       |            |
| 1218 |                                                                                   | PG&E - RFP Review with EE PRG                                           | 8 days           | Fri 7/24/20        | Tue 8/4/20        |            |
| 1219 |                                                                                   | PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 6 days           | Wed 8/5/20         | Wed 8/12/20       |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID   |  | Task Name                                                               | Duration         | Start             | Finish            | 2018<br>H1 |
|------|----------------------------------------------------------------------------------|-------------------------------------------------------------------------|------------------|-------------------|-------------------|------------|
| 1220 |                                                                                  | PG&E - Contract Negotiation and Development                             | 177 days         | Mon 8/17/20       | Tue 4/20/21       |            |
| 1221 |                                                                                  | PG&E - Contract Review with EE PRG                                      | 16 days          | Thu 4/22/21       | Thu 5/13/21       |            |
| 1222 |                                                                                  | PG&E - Final Award and Contract Signed                                  | 32 days          | Sat 5/15/21       | Mon 6/28/21       |            |
| 1223 |                                                                                  | PG&E - Submit Advice Letter                                             | 1 day            | Mon 7/12/21       | Mon 7/12/21       |            |
| 1224 |                                                                                  | PG&E - Advice Letter Approved (all electric)                            | 1 day            | Wed 8/11/21       | Wed 8/11/21       |            |
| 1225 |                                                                                  | PG&E - Advice Letter Approved (mixed fuel)                              | 1 day            | Wed 9/15/21       | Wed 9/15/21       |            |
| 1226 |                                                                                  | PG&E - Implementation Plan (all electric)                               | 43 days          | Thu 8/12/21       | Mon 10/11/21      |            |
| 1227 |                                                                                  | PG&E - Implementation Plan (mixed fuel)                                 | 43 days          | Thu 9/16/21       | Sun 11/14/21      |            |
| 1228 |                                                                                  | <b>PG&amp;E - Statewide WE&amp;T Career Connections Solicitation</b>    | <b>410 days?</b> | <b>Tue 1/7/20</b> | <b>Mon 8/2/21</b> |            |
| 1229 |                                                                                  | PG&E - RFA Preparation                                                  | 54 days          | Tue 1/7/20        | Fri 3/20/20       |            |
| 1230 |                                                                                  | PG&E - RFA Release                                                      | 1 day            | Mon 4/6/20        | Mon 4/6/20        |            |
| 1231 |                                                                                  | PG&E - RFA Abstract Creation Duration                                   | 29 days          | Tue 4/7/20        | Fri 5/15/20       |            |
| 1232 |                                                                                  | PG&E - RFA Evaluation                                                   | 20 days          | Mon 5/18/20       | Fri 6/12/20       |            |
| 1233 |                                                                                  | PG&E - RFA Review with EE PRG                                           | 8 days           | Fri 6/19/20       | Tue 6/30/20       |            |
| 1234 |                                                                                  | PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder | 4 days           | Fri 7/3/20        | Wed 7/8/20        |            |
| 1235 |                                                                                  | PG&E - RFP Preparation                                                  | 45 days          | Mon 6/15/20       | Fri 8/14/20       |            |
| 1236 |                                                                                  | PG&E - RFP Release                                                      | 1 day            | Fri 9/4/20        | Fri 9/4/20        |            |
| 1237 |                                                                                  | PG&E - RFP Proposal Creation Duration                                   | 20 days          | Mon 9/7/20        | Fri 10/2/20       |            |
| 1238 |                                                                                  | PG&E - RFP Evaluation                                                   | 14 days          | Tue 10/6/20       | Fri 10/23/20      |            |
| 1239 |                                                                                  | PG&E - RFP Review with EE PRG                                           | 8 days           | Fri 10/23/20      | Tue 11/3/20       |            |
| 1240 |                                                                                  | PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder | 1 day            | Tue 11/10/20      | Tue 11/10/20      |            |
| 1241 |                                                                                  | PG&E - Contract Negotiation and Development                             | 71 days          | Mon 12/7/20       | Mon 3/15/21       |            |
| 1242 |                                                                                  | PG&E - Contract Review with EE PRG                                      | 6 days           | Tue 3/23/21       | Tue 3/30/21       |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone



Finish-only



| ID   |  | Task Name                                                                        | Duration         | Start             | Finish            | 2018<br>H1 |
|------|----------------------------------------------------------------------------------|----------------------------------------------------------------------------------|------------------|-------------------|-------------------|------------|
| 1243 |                                                                                  | PG&E - Final Award and Contract Signed                                           | 22 days          | Thu 4/1/21        | Fri 4/30/21       |            |
| 1244 |                                                                                  | PG&E - Submit Advice Letter                                                      | 1 day            | Fri 5/28/21       | Fri 5/28/21       |            |
| 1245 |                                                                                  | PG&E - Advice Letter Approved                                                    | 1 day            | Fri 6/25/21       | Fri 6/25/21       |            |
| 1246 |                                                                                  | PG&E - Implementation Plan                                                       | 43 days          | Sat 6/26/21       | Tue 8/24/21       |            |
| 1247 |                                                                                  | <b>PG&amp;E - Statewide WE&amp;T Career and Workforce Readiness Solicitation</b> | <b>410 days?</b> | <b>Tue 1/7/20</b> | <b>Mon 8/2/21</b> |            |
| 1248 |                                                                                  | PG&E - RFA Preparation                                                           | 54 days          | Tue 1/7/20        | Fri 3/20/20       |            |
| 1249 |                                                                                  | PG&E - RFA Release                                                               | 1 day            | Mon 4/6/20        | Mon 4/6/20        |            |
| 1250 |                                                                                  | PG&E - RFA Abstract Creation Duration                                            | 29 days          | Tue 4/7/20        | Fri 5/15/20       |            |
| 1251 |                                                                                  | PG&E - RFA Evaluation                                                            | 20 days          | Mon 5/18/20       | Fri 6/12/20       |            |
| 1252 |                                                                                  | PG&E - RFA Review with EE PRG                                                    | 8 days           | Fri 6/19/20       | Tue 6/30/20       |            |
| 1253 |                                                                                  | PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder          | 4 days           | Fri 7/3/20        | Wed 7/8/20        |            |
| 1254 |                                                                                  | PG&E - RFP Preparation                                                           | 45 days          | Mon 6/15/20       | Fri 8/14/20       |            |
| 1255 |                                                                                  | PG&E - RFP Release                                                               | 1 day            | Fri 9/4/20        | Fri 9/4/20        |            |
| 1256 |                                                                                  | PG&E - RFP Proposal Creation Duration                                            | 20 days          | Mon 9/7/20        | Fri 10/2/20       |            |
| 1257 |                                                                                  | PG&E - RFP Evaluation                                                            | 14 days          | Tue 10/6/20       | Fri 10/23/20      |            |
| 1258 |                                                                                  | PG&E - RFP Review with EE PRG                                                    | 8 days           | Fri 10/23/20      | Tue 11/3/20       |            |
| 1259 |                                                                                  | PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder          | 1 day            | Tue 11/10/20      | Tue 11/10/20      |            |
| 1260 |                                                                                  | PG&E - Contract Negotiation and Development                                      | 71 days          | Mon 12/7/20       | Mon 3/15/21       |            |
| 1261 |                                                                                  | PG&E - Contract Review with EE PRG                                               | 6 days           | Tue 3/23/21       | Tue 3/30/21       |            |
| 1262 |                                                                                  | PG&E - Final Award and Contract Signed                                           | 22 days          | Thu 4/1/21        | Fri 4/30/21       |            |
| 1263 |                                                                                  | PG&E - Submit Advice Letter                                                      | 1 day            | Fri 5/28/21       | Fri 5/28/21       |            |
| 1264 |                                                                                  | PG&E - Advice Letter Approved                                                    | 1 day            | Fri 6/25/21       | Fri 6/25/21       |            |
| 1265 |                                                                                  | PG&E - Implementation Plan                                                       | 43 days          | Sat 6/26/21       | Tue 8/24/21       |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




| ID   |  | Task Name                                                                      | Duration         | Start             | Finish              | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|--------------------------------------------------------------------------------|------------------|-------------------|---------------------|------------|
| 1266 |                                                                                   | <b>PG&amp;E - Statewide State of CA (Dept. of Corrections) Solicitation</b>    | <b>348 days?</b> | <b>Sun 3/1/20</b> | <b>Tue 6/29/21</b>  |            |
| 1267 |                                                                                   | PG&E - RFA Preparation                                                         | 46 days          | Sun 3/1/20        | Fri 5/1/20          |            |
| 1268 |                                                                                   | PG&E - RFA Release                                                             | 1 day            | Wed 5/13/20       | Wed 5/13/20         |            |
| 1269 |                                                                                   | PG&E - RFA Abstract Creation Duration                                          | 31 days          | Wed 5/13/20       | Wed 6/24/20         |            |
| 1270 |                                                                                   | PG&E - RFA Evaluation                                                          | 15 days          | Mon 6/29/20       | Fri 7/17/20         |            |
| 1271 |                                                                                   | PG&E - RFA Review with EE PRG                                                  | 5 days           | Tue 7/28/20       | Mon 8/3/20          |            |
| 1272 |                                                                                   | PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder        | 5 days           | Mon 8/3/20        | Fri 8/7/20          |            |
| 1273 |                                                                                   | PG&E - RFP Preparation                                                         | 20 days          | Mon 8/3/20        | Fri 8/28/20         |            |
| 1274 |                                                                                   | PG&E - RFP Release                                                             | 1 day            | Wed 9/9/20        | Wed 9/9/20          |            |
| 1275 |                                                                                   | PG&E - RFP Proposal Creation Duration                                          | 31 days          | Wed 9/9/20        | Wed 10/21/20        |            |
| 1276 |                                                                                   | PG&E - RFP Evaluation                                                          | 31 days          | Fri 10/23/20      | Fri 12/4/20         |            |
| 1277 |                                                                                   | PG&E - RFP Review with EE PRG                                                  | 6 days           | Tue 12/22/20      | Tue 12/29/20        |            |
| 1278 |                                                                                   | PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder        | 3 days           | Wed 1/6/21        | Fri 1/8/21          |            |
| 1279 |                                                                                   | PG&E - Contract Negotiation and Development                                    | 65 days          | Wed 1/20/21       | Tue 4/20/21         |            |
| 1280 |                                                                                   | PG&E - Contract Review with EE PRG                                             | 7 days           | Thu 4/22/21       | Fri 4/30/21         |            |
| 1281 |                                                                                   | PG&E - Final Award and Contract Signed                                         | 22 days          | Sat 5/1/21        | Mon 5/31/21         |            |
| 1282 |                                                                                   | PG&E - Submit Advice Letter                                                    | 1 day            | Thu 6/24/21       | Thu 6/24/21         |            |
| 1283 |                                                                                   | PG&E - Advice Letter Approved                                                  | 1 day            | Wed 7/28/21       | Wed 7/28/21         |            |
| 1284 |                                                                                   | PG&E - Implementation Plan                                                     | 43 days          | Thu 7/29/21       | Sun 9/26/21         |            |
| 1285 |                                                                                   | <b>PG&amp;E - Local (Micro and Small Business Equity Program) Solicitation</b> | <b>403 days?</b> | <b>Tue 6/1/21</b> | <b>Thu 12/15/22</b> |            |
| 1286 |                                                                                   | PG&E - RFA Preparation                                                         | 38 days          | Tue 6/1/21        | Thu 7/22/21         |            |
| 1287 |                                                                                   | PG&E - RFA Release                                                             | 1 day            | Tue 9/7/21        | Tue 9/7/21          |            |
| 1288 |                                                                                   | PG&E - RFA Abstract Creation Duration                                          | 34 days          | Wed 9/8/21        | Mon 10/25/21        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                             | Duration        | Start             | Finish              | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|-----------------------------------------------------------------------|-----------------|-------------------|---------------------|------------|
| 1289 |                                                                                   | PG&E - RFA Evaluation                                                 | 18 days         | Tue 10/26/21      | Thu 11/18/21        |            |
| 1290 |                                                                                   | PG&E - RFP Release                                                    | 1 day           | Wed 12/8/21       | Wed 12/8/21         |            |
| 1291 |                                                                                   | PG&E - RFP Proposal Creation Duration                                 | 46 days         | Wed 12/8/21       | Wed 2/9/22          |            |
| 1292 |                                                                                   | PG&E - RFP Evaluation                                                 | 21 days         | Thu 2/10/22       | Thu 3/10/22         |            |
| 1293 |                                                                                   | PG&E - RFP Review with EE PRG                                         | 6 days          | Thu 3/17/22       | Thu 3/24/22         |            |
| 1294 |                                                                                   | PG&E - RFP Estimated Bidder Notification                              | 1 day           | Wed 3/30/22       | Wed 3/30/22         |            |
| 1295 |                                                                                   | PG&E - Contract Negotiation and Development                           | 71 days         | Thu 4/7/22        | Thu 7/14/22         |            |
| 1296 |                                                                                   | PG&E - Contract Review with EE PRG                                    | 6 days          | Fri 7/22/22       | Fri 7/29/22         |            |
| 1297 |                                                                                   | PG&E - Final Award and Contract Signed                                | 45 days         | Mon 8/8/22        | Fri 10/7/22         |            |
| 1298 |                                                                                   | PG&E - Submit Advice Letter                                           | 1 day           | Wed 10/12/22      | Wed 10/12/22        |            |
| 1299 |                                                                                   | PG&E - Advice Letter Approved                                         | 1 day           | Fri 11/11/22      | Fri 11/11/22        |            |
| 1300 |                                                                                   | PG&E - Implementation Plan                                            | 31 days         | Fri 11/11/22      | Fri 12/23/22        |            |
| 1301 |                                                                                   | <b>PG&amp;E - Local (C&amp;S Compliance Improvement) Solicitation</b> | <b>436 days</b> | <b>Tue 3/1/22</b> | <b>Tue 10/31/23</b> |            |
| 1302 |                                                                                   | PG&E - RFA Preparation                                                | 34 days         | Tue 3/1/22        | Fri 4/15/22         |            |
| 1303 |                                                                                   | PG&E - RFA Release                                                    | 1 day           | Mon 5/16/22       | Mon 5/16/22         |            |
| 1304 |                                                                                   | PG&E - RFA Abstract Creation Duration                                 | 25 days         | Tue 5/17/22       | Mon 6/20/22         |            |
| 1305 |                                                                                   | PG&E - RFA Evaluation                                                 | 28 days         | Tue 6/21/22       | Thu 7/28/22         |            |
| 1306 |                                                                                   | PG&E - RFA Review with EE PRG                                         | 1 day           | Tue 8/9/22        | Tue 8/9/22          |            |
| 1307 |                                                                                   | PG&E - RFA Estimated Bidder Notification                              | 1 day           | Wed 8/31/22       | Wed 8/31/22         |            |
| 1308 |                                                                                   | PG&E - RFP Preparation                                                | 24 days         | Mon 8/1/22        | Thu 9/1/22          |            |
| 1309 |                                                                                   | PG&E - RFP Release                                                    | 1 day           | Tue 9/13/22       | Tue 9/13/22         |            |
| 1310 |                                                                                   | PG&E - RFP Proposal Creation Duration                                 | 26 days         | Tue 9/13/22       | Tue 10/18/22        |            |
| 1311 |                                                                                   | PG&E - RFP Evaluation                                                 | 45 days         | Wed 10/19/22      | Tue 12/20/22        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                                 | Duration        | Start             | Finish             | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|---------------------------------------------------------------------------|-----------------|-------------------|--------------------|------------|
| 1312 |                                                                                   | PG&E - RFP Review with EE PRG                                             | 1 day           | Tue 1/24/23       | Tue 1/24/23        |            |
| 1313 |                                                                                   | PG&E - RFP Estimated Bidder Notification                                  | 1 day           | Fri 2/10/23       | Fri 2/10/23        |            |
| 1314 |                                                                                   | PG&E - Contract Negotiation and Development                               | 47 days         | Mon 2/13/23       | Tue 4/18/23        |            |
| 1315 |                                                                                   | PG&E - Contract Review with EE PRG                                        | 26 days         | Tue 5/23/23       | Tue 6/27/23        |            |
| 1316 |                                                                                   | PG&E - Final Award and Contract Signed                                    | 48 days         | Wed 6/28/23       | Fri 9/1/23         |            |
| 1317 |                                                                                   | PG&E - Submit Advice Letter                                               |                 | N/A               |                    |            |
| 1318 |                                                                                   | PG&E - Advice Letter Approved                                             |                 | N/A               |                    |            |
| 1319 |                                                                                   | PG&E - Implementation Plan                                                | 1 day           | Tue 10/31/23      | Tue 10/31/23       |            |
| 1320 |                                                                                   | <b>PG&amp;E - Residential Electrification Equity Program Solicitation</b> | <b>595 days</b> | <b>Mon 8/1/22</b> | <b>Fri 11/8/24</b> |            |
| 1321 |                                                                                   | PG&E - RFA Preparation                                                    | 59 days         | Mon 8/1/22        | Thu 10/20/22       |            |
| 1322 |                                                                                   | PG&E - RFA Release                                                        | 1 day           | Tue 11/29/22      | Tue 11/29/22       |            |
| 1323 |                                                                                   | PG&E - RFA Abstract Creation Duration                                     | 46 days         | Tue 11/29/22      | Tue 1/31/23        |            |
| 1324 |                                                                                   | PG&E - RFA Evaluation                                                     | 17 days         | Sun 2/5/23        | Sun 2/26/23        |            |
| 1325 |                                                                                   | PG&E - RFA Review with EE PRG                                             | 6 days          | Mon 2/27/23       | Mon 3/6/23         |            |
| 1326 |                                                                                   | PG&E - RFA Estimated Bidder Notification                                  | 3 days          | Mon 3/6/23        | Wed 3/8/23         |            |
| 1327 |                                                                                   | PG&E - RFP Preparation                                                    | 46 days         | Mon 1/9/23        | Mon 3/13/23        |            |
| 1328 |                                                                                   | PG&E - RFP Release                                                        | 1 day           | Tue 4/11/23       | Tue 4/11/23        |            |
| 1329 |                                                                                   | PG&E - RFP Proposal Creation Duration                                     | 26 days         | Tue 4/11/23       | Tue 5/16/23        |            |
| 1330 |                                                                                   | PG&E - RFP Evaluation                                                     | 18 days         | Fri 5/19/23       | Tue 6/13/23        |            |
| 1331 |                                                                                   | PG&E - RFP Review with EE PRG                                             | 1 day           | Tue 6/27/23       | Tue 6/27/23        |            |
| 1332 |                                                                                   | PG&E - RFP Estimated Bidder Notification                                  | 1 day           | Tue 7/11/23       | Tue 7/11/23        |            |
| 1333 |                                                                                   | PG&E - Contract Negotiation and Development                               | 233 days        | Tue 8/1/23        | Thu 6/20/24        |            |
| 1334 |                                                                                   | PG&E - Contract Review with EE PRG                                        | 8 days          | Fri 6/21/24       | Tue 7/2/24         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                 | Duration        | Start             | Finish             | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|-----------------------------------------------------------|-----------------|-------------------|--------------------|------------|
| 1335 |                                                                                   | PG&E - Final Award and Contract Signed                    | 21 days         | Fri 7/5/24        | Fri 8/2/24         |            |
| 1336 |                                                                                   | PG&E - Submit Advice Letter                               | 1 day           | Fri 8/9/24        | Fri 8/9/24         |            |
| 1337 |                                                                                   | PG&E - Advice Letter Approved                             | 1 day           | Mon 9/9/24        | Mon 9/9/24         |            |
| 1338 |                                                                                   | PG&E - Implementation Plan                                | 1 day           | Fri 11/8/24       | Fri 11/8/24        |            |
| 1339 |                                                                                   | <b>PG&amp;E - Statewide C&amp;S Advocacy Solicitation</b> | <b>641 days</b> | <b>Tue 2/1/22</b> | <b>Tue 7/16/24</b> |            |
| 1340 |                                                                                   | PG&E - RFA Preparation                                    | 54 days         | Tue 2/1/22        | Fri 4/15/22        |            |
| 1341 |                                                                                   | PG&E - RFA Release                                        | 1 day           | Mon 5/30/22       | Mon 5/30/22        |            |
| 1342 |                                                                                   | PG&E - RFA Abstract Creation Duration                     | 24 days         | Tue 5/31/22       | Fri 7/1/22         |            |
| 1343 |                                                                                   | PG&E - RFA Evaluation                                     | 14 days         | Fri 7/1/22        | Wed 7/20/22        |            |
| 1344 |                                                                                   | PG&E - RFA Review with EE PRG                             | 6 days          | Fri 7/22/22       | Fri 7/29/22        |            |
| 1345 |                                                                                   | PG&E - RFA Estimated Bidder Notification                  | 1 day           | Mon 8/1/22        | Mon 8/1/22         |            |
| 1346 |                                                                                   | PG&E - RFP Preparation                                    | 36 days         | Fri 4/1/22        | Fri 5/20/22        |            |
| 1347 |                                                                                   | PG&E - RFP Release                                        | 1 day           | Tue 6/7/22        | Tue 6/7/22         |            |
| 1348 |                                                                                   | PG&E - RFP Proposal Creation Duration                     | 31 days         | Tue 6/7/22        | Tue 7/19/22        |            |
| 1349 |                                                                                   | PG&E - RFP Evaluation                                     | 50 days         | Wed 7/20/22       | Tue 9/27/22        |            |
| 1350 |                                                                                   | PG&E - RFP Review with EE PRG                             | 1 day           | Wed 10/5/22       | Wed 10/5/22        |            |
| 1351 |                                                                                   | PG&E - RFP Estimated Bidder Notification                  | 1 day           | Mon 10/24/22      | Mon 10/24/22       |            |
| 1352 |                                                                                   | PG&E - Contract Negotiation and Development               | 73 days         | Mon 11/14/22      | Wed 2/22/23        |            |
| 1353 |                                                                                   | PG&E - Contract Review with EE PRG - Wave 1               | 1 day           | Tue 4/25/23       | Tue 4/25/23        |            |
| 1354 |                                                                                   | PG&E - Final Award and Contract Signed                    | 18 days         | Mon 7/17/23       | Wed 8/9/23         |            |
| 1355 |                                                                                   | PG&E - Submit Advice Letter (wave 1)                      | 1 day           | Thu 9/21/23       | Thu 9/21/23        |            |
| 1356 |                                                                                   | PG&E - Advice Letter Approved                             | 1 day           | Wed 10/25/23      | Wed 10/25/23       |            |
| 1357 |                                                                                   | PG&E - Implementation Plan                                | 1 day           | Thu 12/7/23       | Thu 12/7/23        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                    | Duration        | Start              | Finish              | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|--------------------------------------------------------------|-----------------|--------------------|---------------------|------------|
| 1358 |                                                                                   | PG&E - Contract Review with EE PRG - Wave 2                  | 1 day           | Wed 12/20/23       | Wed 12/20/23        |            |
| 1359 |                                                                                   | PG&E - Final Award and Contract Signed                       | 1 day           | Fri 3/29/24        | Fri 3/29/24         |            |
| 1360 |                                                                                   | PG&E - Submit Advice Letter                                  | 1 day           | Wed 4/17/24        | Wed 4/17/24         |            |
| 1361 |                                                                                   | PG&E - Advice Letter Approved                                | 1 day           | Fri 5/17/24        | Fri 5/17/24         |            |
| 1362 |                                                                                   | PG&E - Implementation Plan                                   | 1 day           | Tue 7/16/24        | Tue 7/16/24         |            |
| 1363 |                                                                                   | <b>PG&amp;E - Zonal Electrification Solicitation</b>         | <b>495 days</b> | <b>Thu 12/1/22</b> | <b>Wed 10/23/24</b> |            |
| 1364 |                                                                                   | PG&E - RFP Preparation                                       | 88 days         | Thu 12/1/22        | Mon 4/3/23          |            |
| 1365 |                                                                                   | PG&E - RFP Release                                           | 1 day           | Tue 4/18/23        | Tue 4/18/23         |            |
| 1366 |                                                                                   | PG&E - RFP Proposal Creation Duration                        | 53 days         | Tue 4/18/23        | Thu 6/29/23         |            |
| 1367 |                                                                                   | PG&E - RFP Evaluation (including interviews)                 | 40 days         | Mon 7/10/23        | Fri 9/1/23          |            |
| 1368 |                                                                                   | PG&E - RFP Review with EE PRG                                | 1 day           | Tue 9/26/23        | Tue 9/26/23         |            |
| 1369 |                                                                                   | PG&E - RFP Estimated Bidder Notification                     | 1 day           | Mon 10/2/23        | Mon 10/2/23         |            |
| 1370 |                                                                                   | PG&E - Contract Negotiation and Development                  | 135 days        | Mon 10/9/23        | Fri 4/12/24         |            |
| 1371 |                                                                                   | PG&E - Contract Review with EE PRG                           | 1 day           | Tue 4/23/24        | Tue 4/23/24         |            |
| 1372 |                                                                                   | PG&E - Final Award and Contract Signed                       | 43 days         | Wed 5/1/24         | Fri 6/28/24         |            |
| 1373 |                                                                                   | PG&E - Submit Advice Letter                                  | 1 day           | Wed 7/3/24         | Wed 7/3/24          |            |
| 1374 |                                                                                   | PG&E - Advice Letter Approved                                | 1 day           | Wed 8/28/24        | Wed 8/28/24         |            |
| 1375 |                                                                                   | PG&E - Implementation Plan                                   | 1 day           | Wed 10/23/24       | Wed 10/23/24        |            |
| 1376 |                                                                                   | <b>PG&amp;E - Residential Whole Home Load Management RFP</b> | <b>453 days</b> | <b>Tue 8/15/23</b> | <b>Thu 5/8/25</b>   |            |
| 1377 |                                                                                   | PG&E - RFP Preparation                                       | 1 day           | Tue 8/15/23        | Tue 8/15/23         |            |
| 1378 |                                                                                   | PG&E - RFP Release                                           | 1 day           | Tue 8/15/23        | Tue 8/15/23         |            |
| 1379 |                                                                                   | PG&E - RFP Proposal Creation Duration                        | 51 days         | Tue 8/15/23        | Tue 10/24/23        |            |
| 1380 |                                                                                   | PG&E - RFP Evaluation                                        | 36 days         | Thu 10/26/23       | Thu 12/14/23        |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                            | Duration         | Start              | Finish             | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|----------------------------------------------------------------------|------------------|--------------------|--------------------|------------|
| 1381 |                                                                                   | PG&E - RFP Review with EE PRG                                        | 1 day            | Fri 2/16/24        | Fri 2/16/24        |            |
| 1382 |                                                                                   | PG&E - RFP Estimated Bidder Notification                             | 1 day            | Tue 2/27/24        | Tue 2/27/24        |            |
| 1383 |                                                                                   | PG&E - Contract Negotiation and Development                          | 155 days         | Wed 3/13/24        | Tue 10/15/24       |            |
| 1384 |                                                                                   | PG&E - Contract Review with EE PRG                                   | 8 days           | Tue 11/5/24        | Thu 11/14/24       |            |
| 1385 |                                                                                   | PG&E - Final Award and Contract Signed                               | 53 days          | Thu 11/14/24       | Mon 1/27/25        |            |
| 1386 |                                                                                   | PG&E - Submit Advice Letter                                          | 1 day            | Fri 2/7/25         | Fri 2/7/25         |            |
| 1387 |                                                                                   | PG&E - Advice Letter Approved                                        | 1 day            | Mon 3/10/25        | Mon 3/10/25        |            |
| 1388 |                                                                                   | PG&E - Implementation Plan                                           | 1 day            | Thu 5/8/25         | Thu 5/8/25         |            |
| 1389 |                                                                                   | <b>PG&amp;E - 2024 Summer Reliability Platform Administrator RFP</b> | <b>337 days?</b> | <b>Tue 4/18/23</b> | <b>Wed 7/31/24</b> |            |
| 1390 |                                                                                   | PG&E - RFP Preparation                                               | 30 days          | Mon 5/1/23         | Fri 6/9/23         |            |
| 1391 |                                                                                   | PG&E - RFP Release                                                   | 1 day            | Fri 9/1/23         | Fri 9/1/23         |            |
| 1392 |                                                                                   | PG&E - RFP Proposal Creation Duration                                | 31 days          | Fri 9/1/23         | Fri 10/13/23       |            |
| 1393 |                                                                                   | PG&E - RFP Evaluation                                                | 22 days          | Tue 10/17/23       | Wed 11/15/23       |            |
| 1394 |                                                                                   | PG&E - RFP Review with EE PRG                                        | 1 day            | Tue 11/28/23       | Tue 11/28/23       |            |
| 1395 |                                                                                   | PG&E - RFP Estimated Bidder Notification                             | 1 day            | Tue 12/5/23        | Tue 12/5/23        |            |
| 1396 |                                                                                   | PG&E - Contract Negotiation and Development                          | 68 days          | Mon 1/8/24         | Wed 4/10/24        |            |
| 1397 |                                                                                   | PG&E - Contract Review with EE PRG                                   | 1 day            | Tue 4/23/24        | Tue 4/23/24        |            |
| 1398 |                                                                                   | PG&E - Final Award and Contract Signed                               | 22 days          | Wed 5/1/24         | Thu 5/30/24        |            |
| 1399 |                                                                                   | PG&E - Submit Advice Letter                                          | 1 day            | Fri 5/31/24        | Fri 5/31/24        |            |
| 1400 |                                                                                   | PG&E - Advice Letter Approved                                        | 1 day            | Mon 7/1/24         | Mon 7/1/24         |            |
| 1401 |                                                                                   | PG&E - Implementation Plan                                           | 1 day            | Wed 7/31/24        | Wed 7/31/24        |            |
| 1402 |                                                                                   | <b>PG&amp;E - C&amp;S Code Readiness RFP</b>                         | <b>393 days?</b> | <b>Wed 2/1/23</b>  | <b>Fri 8/2/24</b>  |            |
| 1403 |                                                                                   | PG&E - RFP Preparation                                               | 113 days         | Wed 2/1/23         | Fri 7/7/23         |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                               | Duration        | Start             | Finish             | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|-------------------------------------------------------------------------|-----------------|-------------------|--------------------|------------|
| 1404 |                                                                                   | PG&E - RFP Release                                                      | 1 day           | Wed 7/12/23       | Wed 7/12/23        |            |
| 1405 |                                                                                   | PG&E - RFP Proposal Creation Duration                                   | 30 days         | Thu 7/13/23       | Wed 8/23/23        |            |
| 1406 |                                                                                   | PG&E - RFP Evaluation                                                   | 36 days         | Mon 8/28/23       | Mon 10/16/23       |            |
| 1407 |                                                                                   | PG&E - RFP Review with EE PRG                                           | 1 day           | Tue 10/24/23      | Tue 10/24/23       |            |
| 1408 |                                                                                   | PG&E - RFP Estimated Bidder Notification                                | 1 day           | Mon 11/6/23       | Mon 11/6/23        |            |
| 1409 |                                                                                   | PG&E - Contract Negotiation and Development                             | 65 days         | Wed 11/15/23      | Tue 2/13/24        |            |
| 1410 |                                                                                   | PG&E - Contract Review with EE PRG                                      | 1 day           | Tue 2/27/24       | Tue 2/27/24        |            |
| 1411 |                                                                                   | PG&E - Final Award and Contract Signed                                  | 1 day           | Fri 4/12/24       | Fri 4/12/24        |            |
| 1412 |                                                                                   | PG&E - Submit Advice Letter                                             | 1 day           | Tue 5/7/24        | Tue 5/7/24         |            |
| 1413 |                                                                                   | PG&E - Advice Letter Approved                                           | 1 day           | Thu 6/6/24        | Thu 6/6/24         |            |
| 1414 |                                                                                   | PG&E - Implementation Plan                                              | 1 day           | Fri 8/2/24        | Fri 8/2/24         |            |
| 1415 |                                                                                   | <b>PG&amp;E - Residential Electrification - Single Point of Contact</b> | <b>414 days</b> | <b>Tue 8/1/23</b> | <b>Fri 2/28/25</b> |            |
| 1416 |                                                                                   | PG&E - RFP Preparation                                                  | 133 days        | Tue 8/1/23        | Thu 2/1/24         |            |
| 1417 |                                                                                   | PG&E - RFP Release                                                      | 1 day           | Wed 2/28/24       | Wed 2/28/24        |            |
| 1418 |                                                                                   | PG&E - RFP Proposal Creation Duration                                   | 33 days         | Wed 2/28/24       | Fri 4/12/24        |            |
| 1419 |                                                                                   | PG&E - RFP Evaluation                                                   | 66 days         | Mon 4/15/24       | Mon 7/15/24        |            |
| 1420 |                                                                                   | PG&E - RFP Review with EE PRG                                           | 6 days          | Fri 7/19/24       | Fri 7/26/24        |            |
| 1421 |                                                                                   | PG&E - RFP Estimated Bidder Notification                                | 1 day           | Wed 8/7/24        | Wed 8/7/24         |            |
| 1422 |                                                                                   | PG&E - Contract Negotiation and Development                             | 62 days         |                   |                    |            |
| 1423 |                                                                                   | PG&E - Contract Review with EE PRG                                      | 6 days          |                   |                    |            |
| 1424 |                                                                                   | PG&E - Final Award and Contract Signed                                  | 25 days         |                   |                    |            |
| 1425 |                                                                                   | PG&E - Submit Advice Letter                                             | 1 day           |                   |                    |            |
| 1426 |                                                                                   | PG&E - Advice Letter Approved                                           | 1 day           |                   |                    |            |

Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |


| ID   |  | Task Name                                                      | Duration        | Start              | Finish             | 2018<br>H1 |
|------|-----------------------------------------------------------------------------------|----------------------------------------------------------------|-----------------|--------------------|--------------------|------------|
| 1427 |                                                                                   | PG&E - Implementation Plan                                     | 1 day           |                    |                    |            |
| 1428 |                                                                                   | <b>PG&amp;E - Commercial SEM FP</b>                            | <b>430 days</b> | <b>Thu 8/3/23</b>  | <b>Wed 3/26/25</b> |            |
| 1429 |                                                                                   | PG&E - RFP Preparation                                         | 16 days         | Thu 8/3/23         | Thu 8/24/23        |            |
| 1430 |                                                                                   | PG&E - RFP Release                                             | 1 day           | Fri 11/3/23        | Fri 11/3/23        |            |
| 1431 |                                                                                   | PG&E - RFP Proposal Creation Duration                          | 55 days         | Fri 11/3/23        | Thu 1/18/24        |            |
| 1432 |                                                                                   | PG&E - RFP Evaluation                                          | 58 days         | Tue 1/23/24        | Thu 4/11/24        |            |
| 1433 |                                                                                   | PG&E - RFP Review with EE PRG                                  | 1 day           | Wed 4/17/24        | Wed 4/17/24        |            |
| 1434 |                                                                                   | PG&E - RFP Estimated Bidder Notification                       | 4 days          | Tue 4/23/24        | Fri 4/26/24        |            |
| 1435 |                                                                                   | PG&E - Contract Negotiation and Development                    | 90 days         | Thu 5/2/24         | Wed 9/4/24         |            |
| 1436 |                                                                                   | PG&E - Contract Review with EE PRG                             | 8 days          | Mon 9/16/24        | Wed 9/25/24        |            |
| 1437 |                                                                                   | PG&E - Final Award and Contract Signed                         | 58 days         | Thu 9/26/24        | Mon 12/16/24       |            |
| 1438 |                                                                                   | PG&E - Submit Advice Letter                                    | 1 day           | Thu 12/19/24       | Thu 12/19/24       |            |
| 1439 |                                                                                   | PG&E - Advice Letter Approved                                  | 0 days          | Thu 1/30/25        | Thu 1/30/25        |            |
| 1440 |                                                                                   | PG&E - Implementation Plan                                     | 1 day           | Wed 3/26/25        | Wed 3/26/25        |            |
| 1441 |                                                                                   | <b>PG&amp;E - SW WE&amp;T Career &amp; Workforce Readiness</b> | <b>460 days</b> | <b>Tue 10/8/24</b> | <b>Mon 7/13/26</b> |            |
| 1442 |                                                                                   | PG&E - RFP Preparation                                         | 199 days        | Tue 10/8/24        | Fri 7/11/25        |            |
| 1443 |                                                                                   | PG&E - RFP Release                                             | 1 day           | Thu 7/17/25        | Thu 7/17/25        |            |
| 1444 |                                                                                   | PG&E - RFP Proposal Creation Duration                          | 31 days         | Thu 7/17/25        | Thu 8/28/25        |            |
| 1445 |                                                                                   | PG&E - RFP Evaluation                                          | 34 days         | Tue 9/2/25         | Fri 10/17/25       |            |
| 1446 |                                                                                   | PG&E - RFP Review with EE PRG                                  | 11 days         | Mon 10/20/25       | Mon 11/3/25        |            |
| 1447 |                                                                                   | PG&E - RFP Estimated Bidder Notification                       | 1 day           | Thu 11/13/25       | Thu 11/13/25       |            |
| 1448 |                                                                                   | PG&E - Contract Negotiation and Development                    | 65 days         | Wed 10/29/25       | Tue 1/27/26        |            |
| 1449 |                                                                                   | PG&E - Contract Review with EE PRG                             | 11 days         | Fri 1/30/26        | Fri 2/13/26        |            |

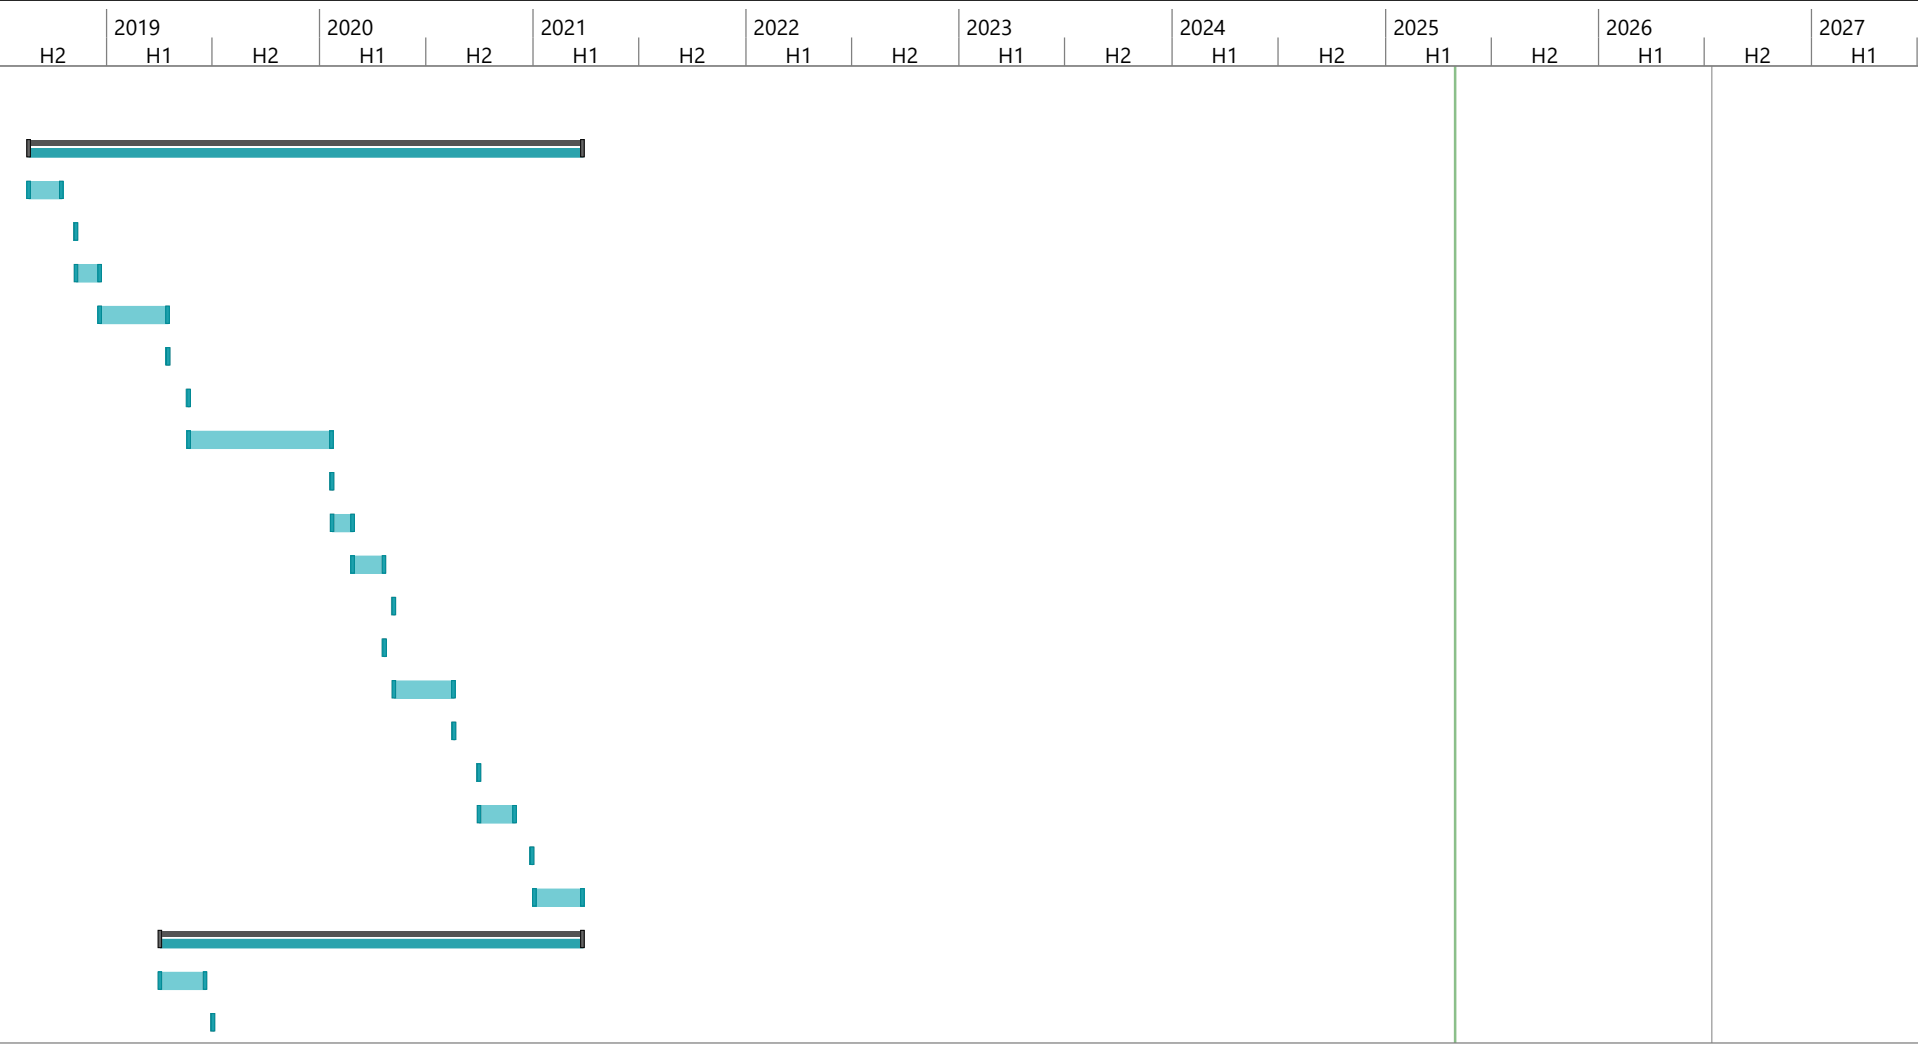
Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID   |  | Task Name                              | Duration | Start       | Finish      | 2018<br>H1 |  |
|------|----------------------------------------------------------------------------------|----------------------------------------|----------|-------------|-------------|------------|--|
| 1450 |                                                                                  | PG&E - Final Award and Contract Signed | 36 days  | Wed 2/18/26 | Wed 4/8/26  |            |  |
| 1451 |                                                                                  | PG&E - Submit Advice Letter            | 1 day    | Wed 4/15/26 | Wed 4/15/26 |            |  |
| 1452 |                                                                                  | PG&E - Advice Letter Approved          | 1 day    | Fri 5/15/26 | Fri 5/15/26 |            |  |
| 1453 |                                                                                  | PG&E - Implementation Plan             | 1 day    | Mon 7/13/26 | Mon 7/13/26 |            |  |

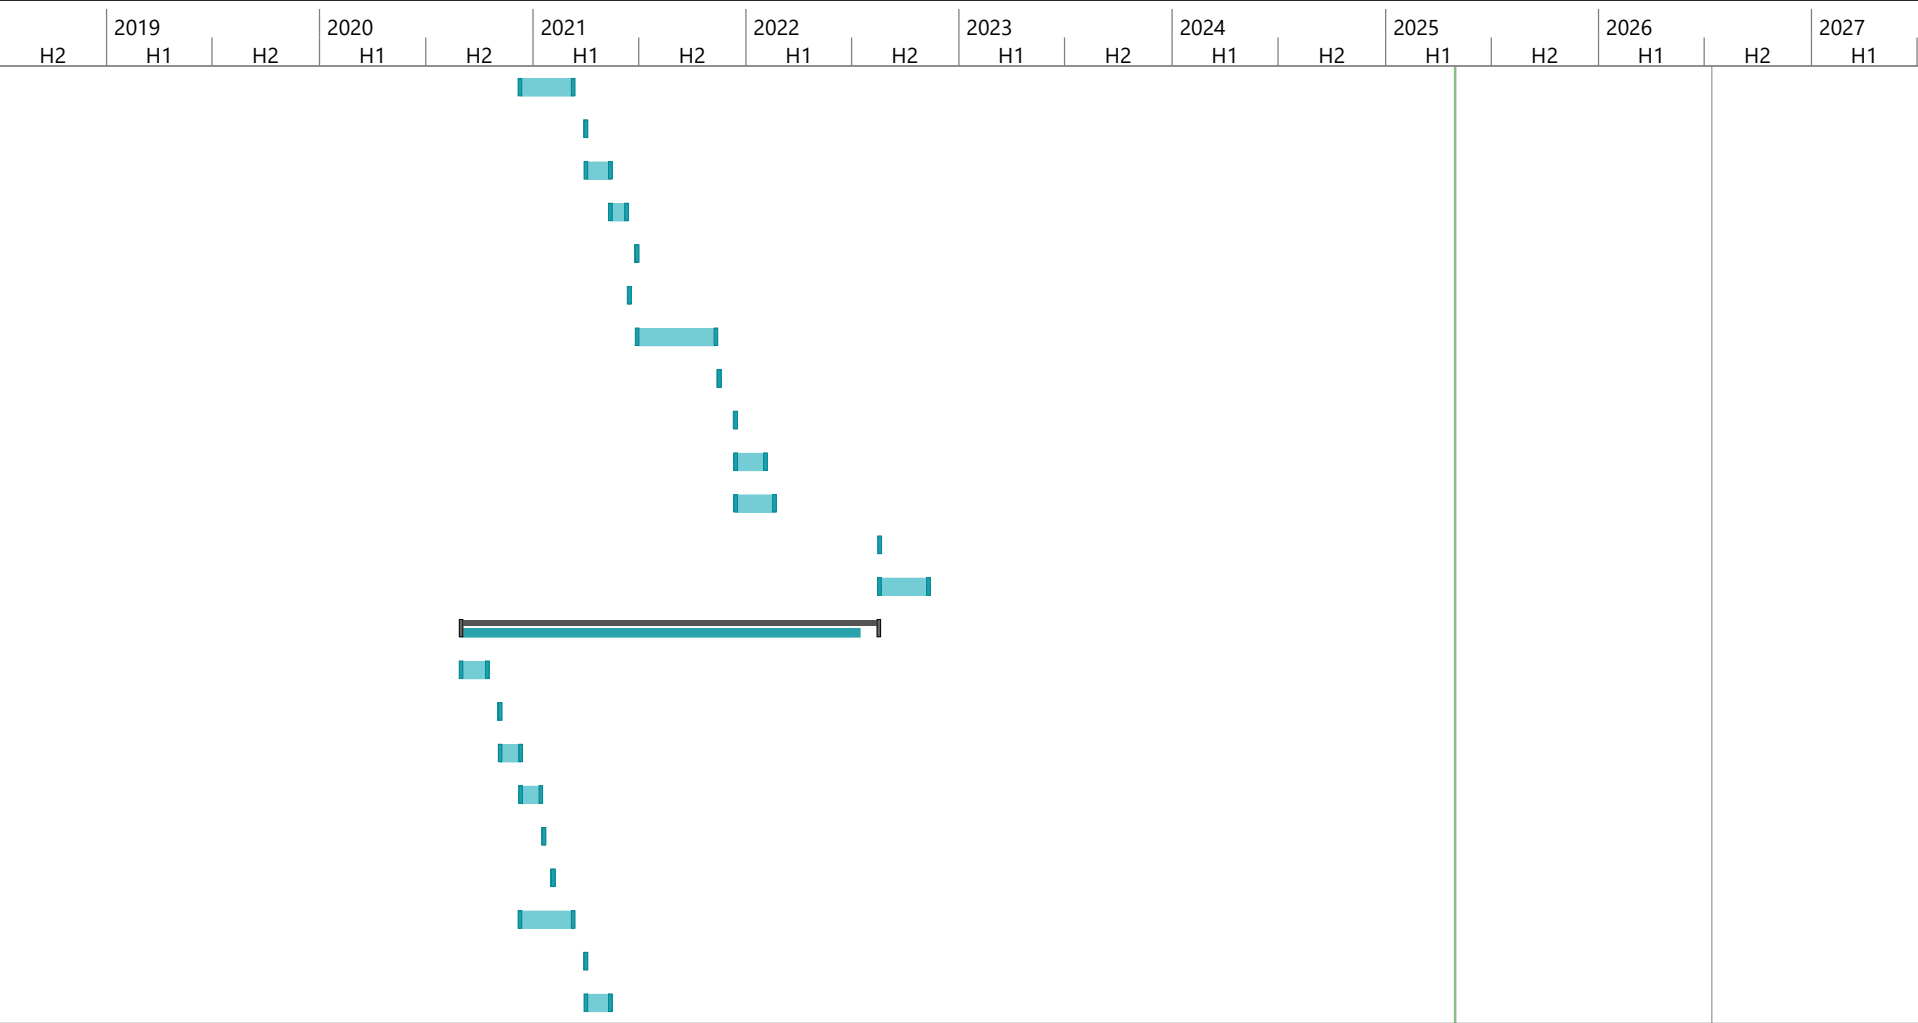
Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |



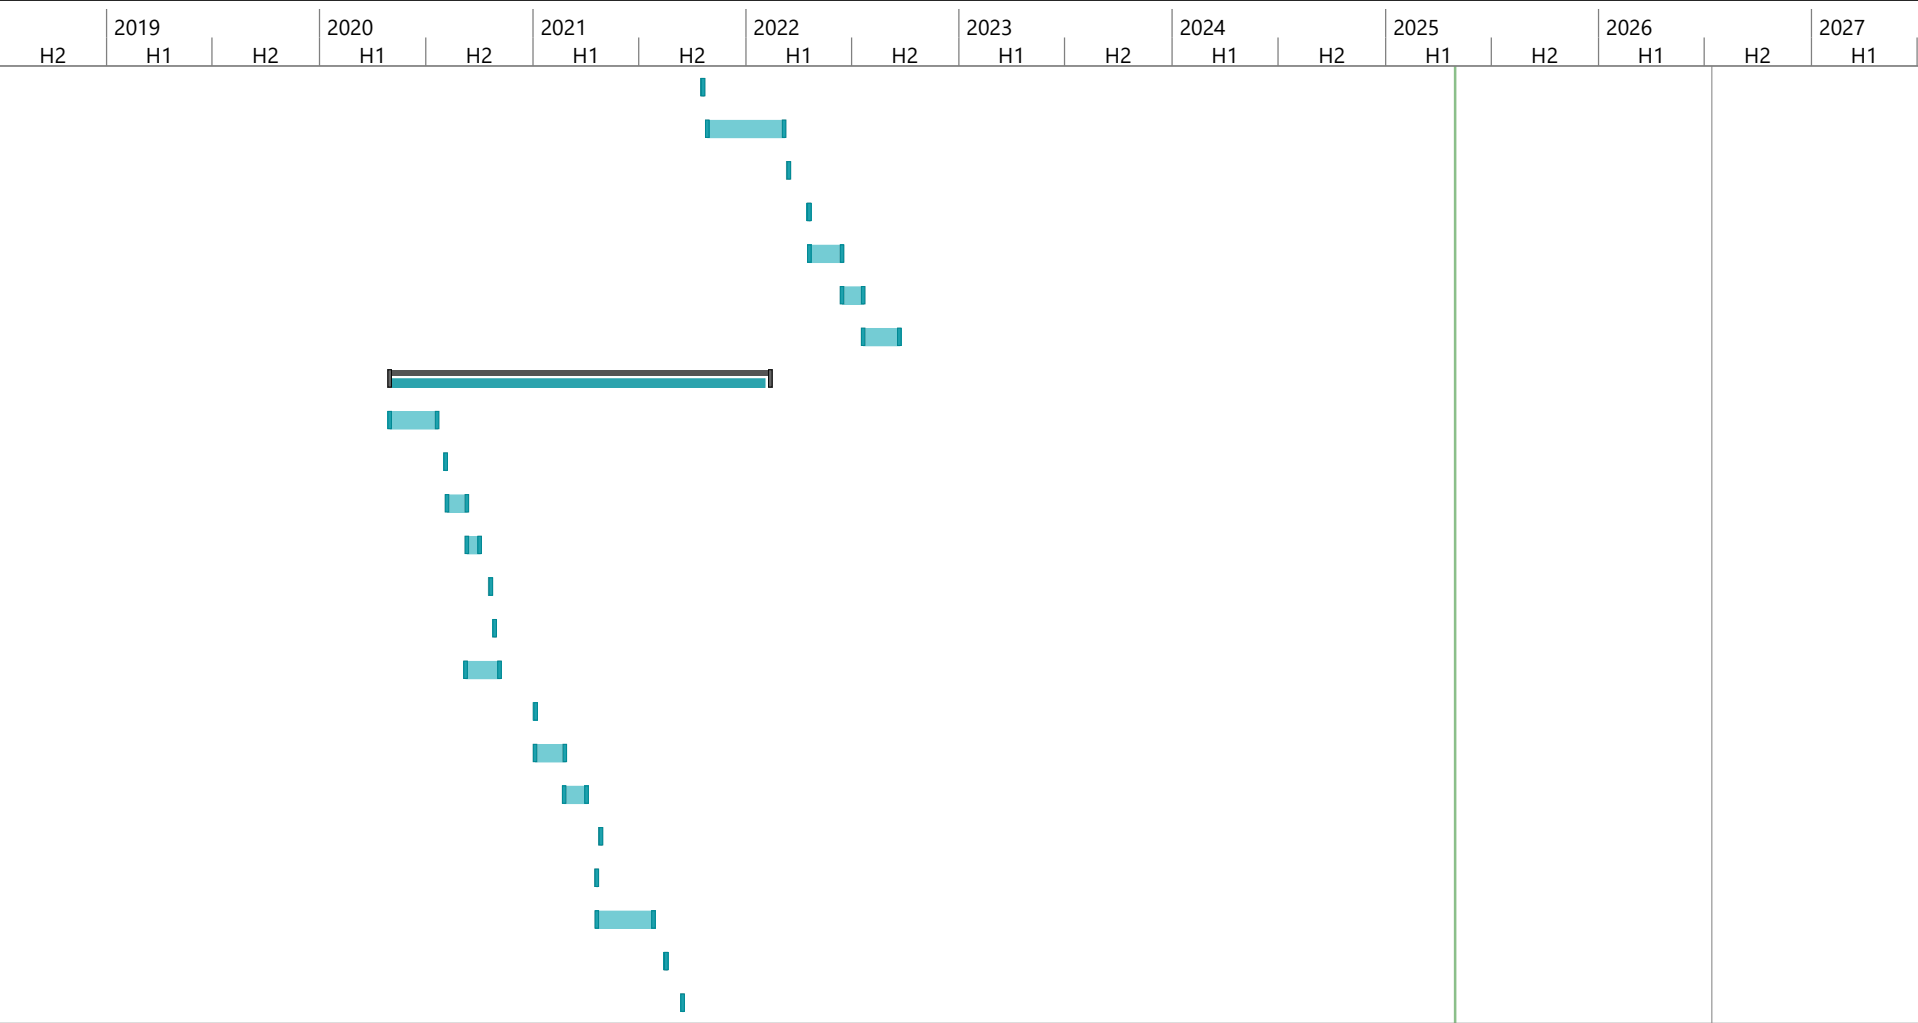
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |



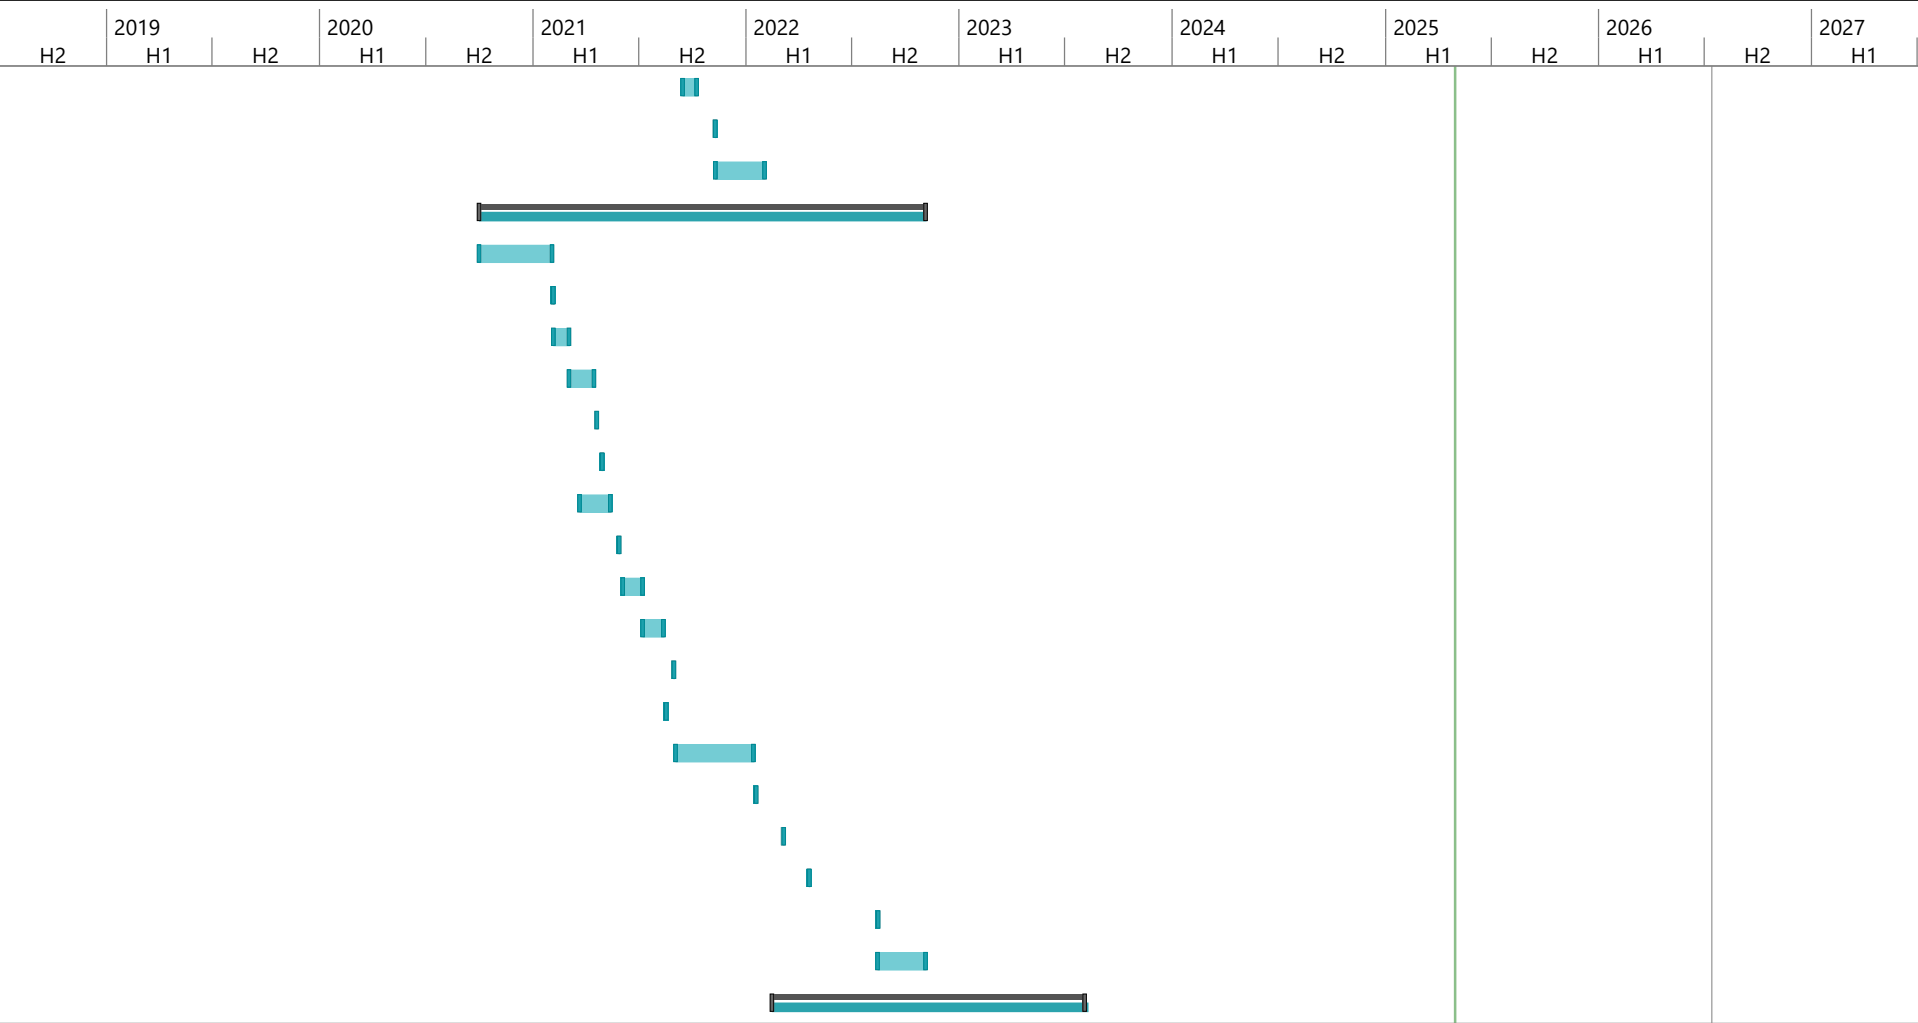


|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |

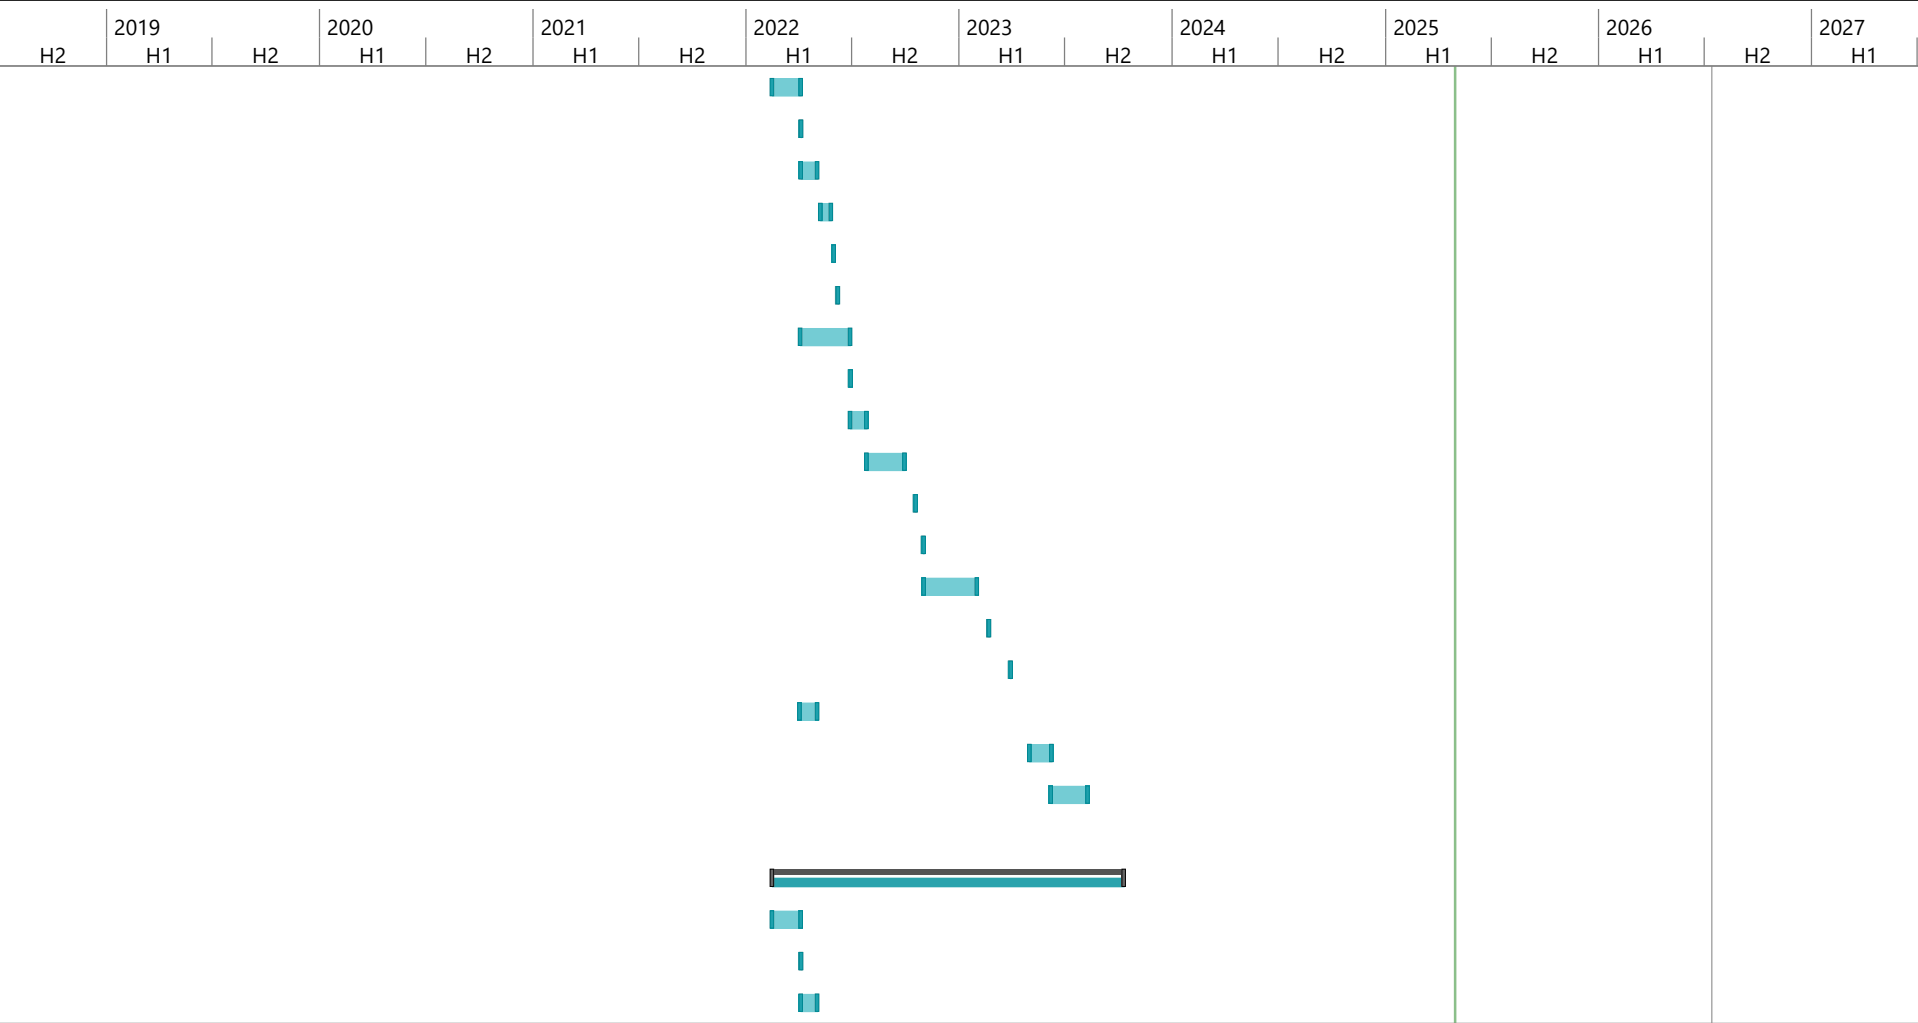




|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |



|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |



Project: IOU Master Task Timeli  
Date: Wed 4/30/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

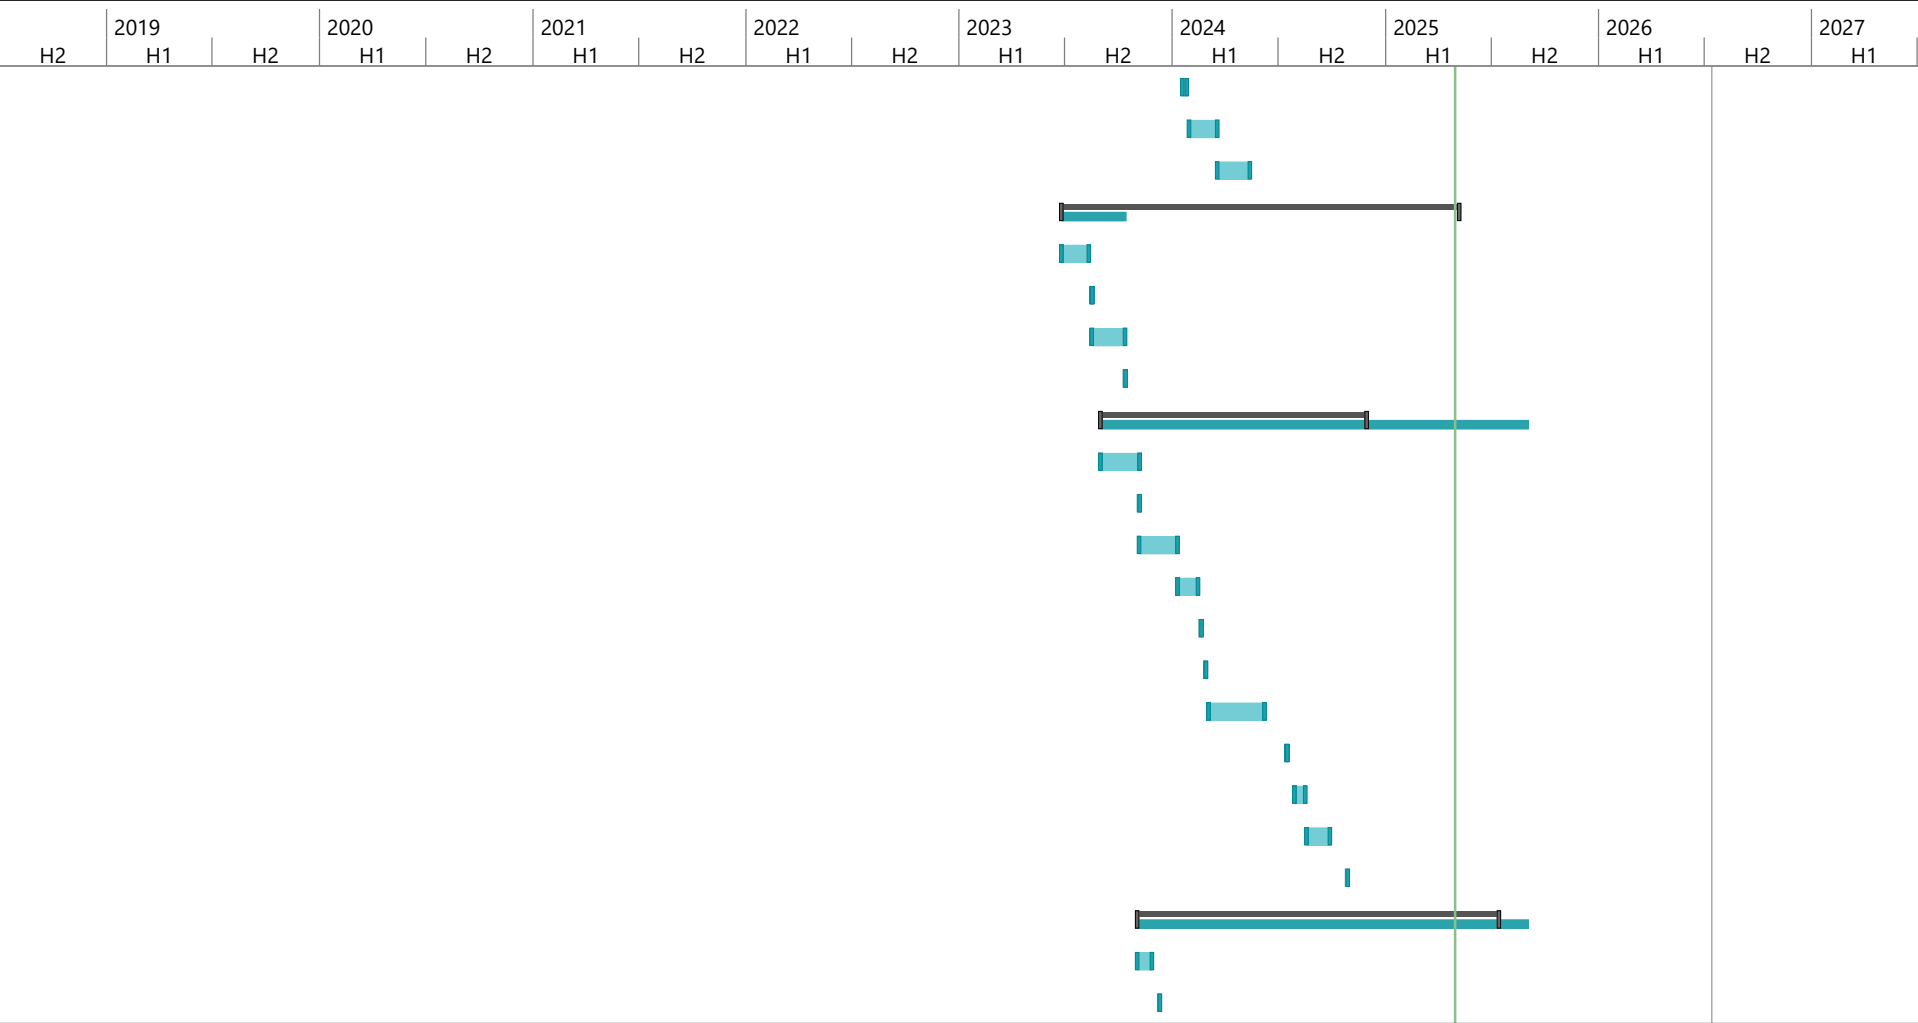
Deadline

Progress

Manual Progress

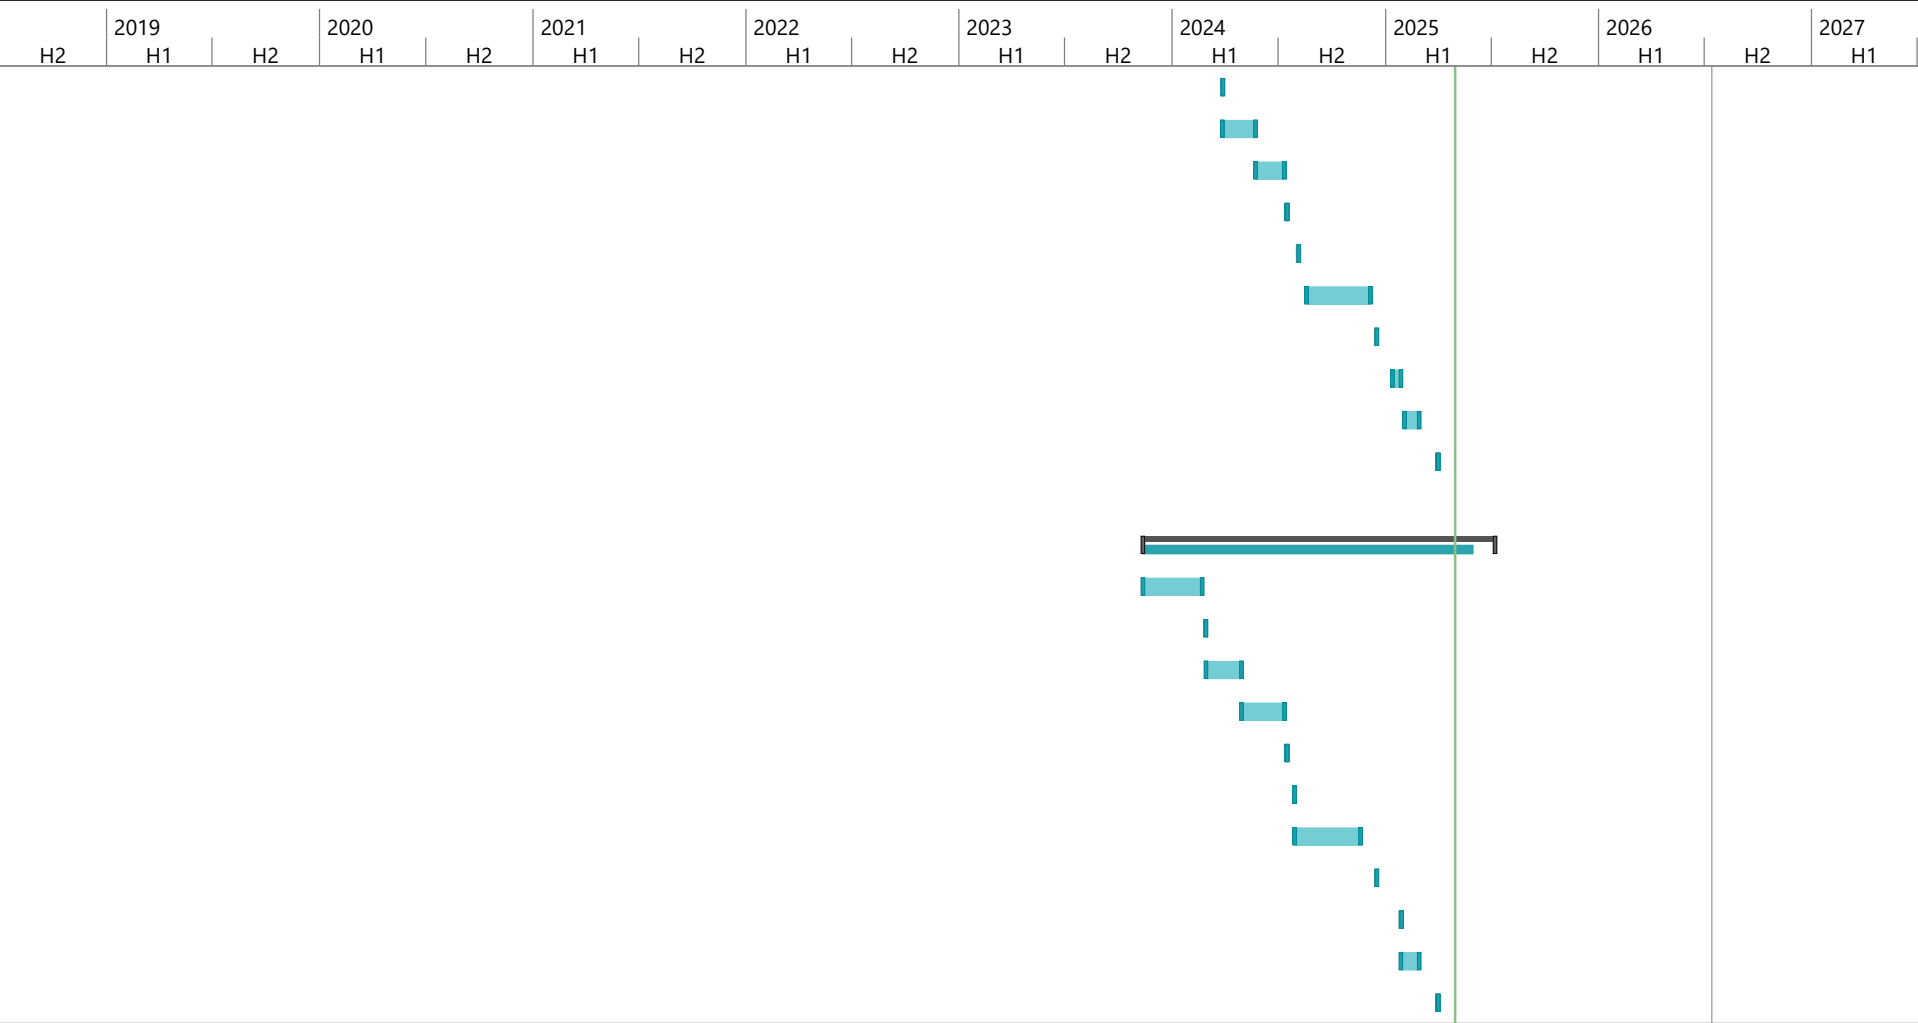
Page 71





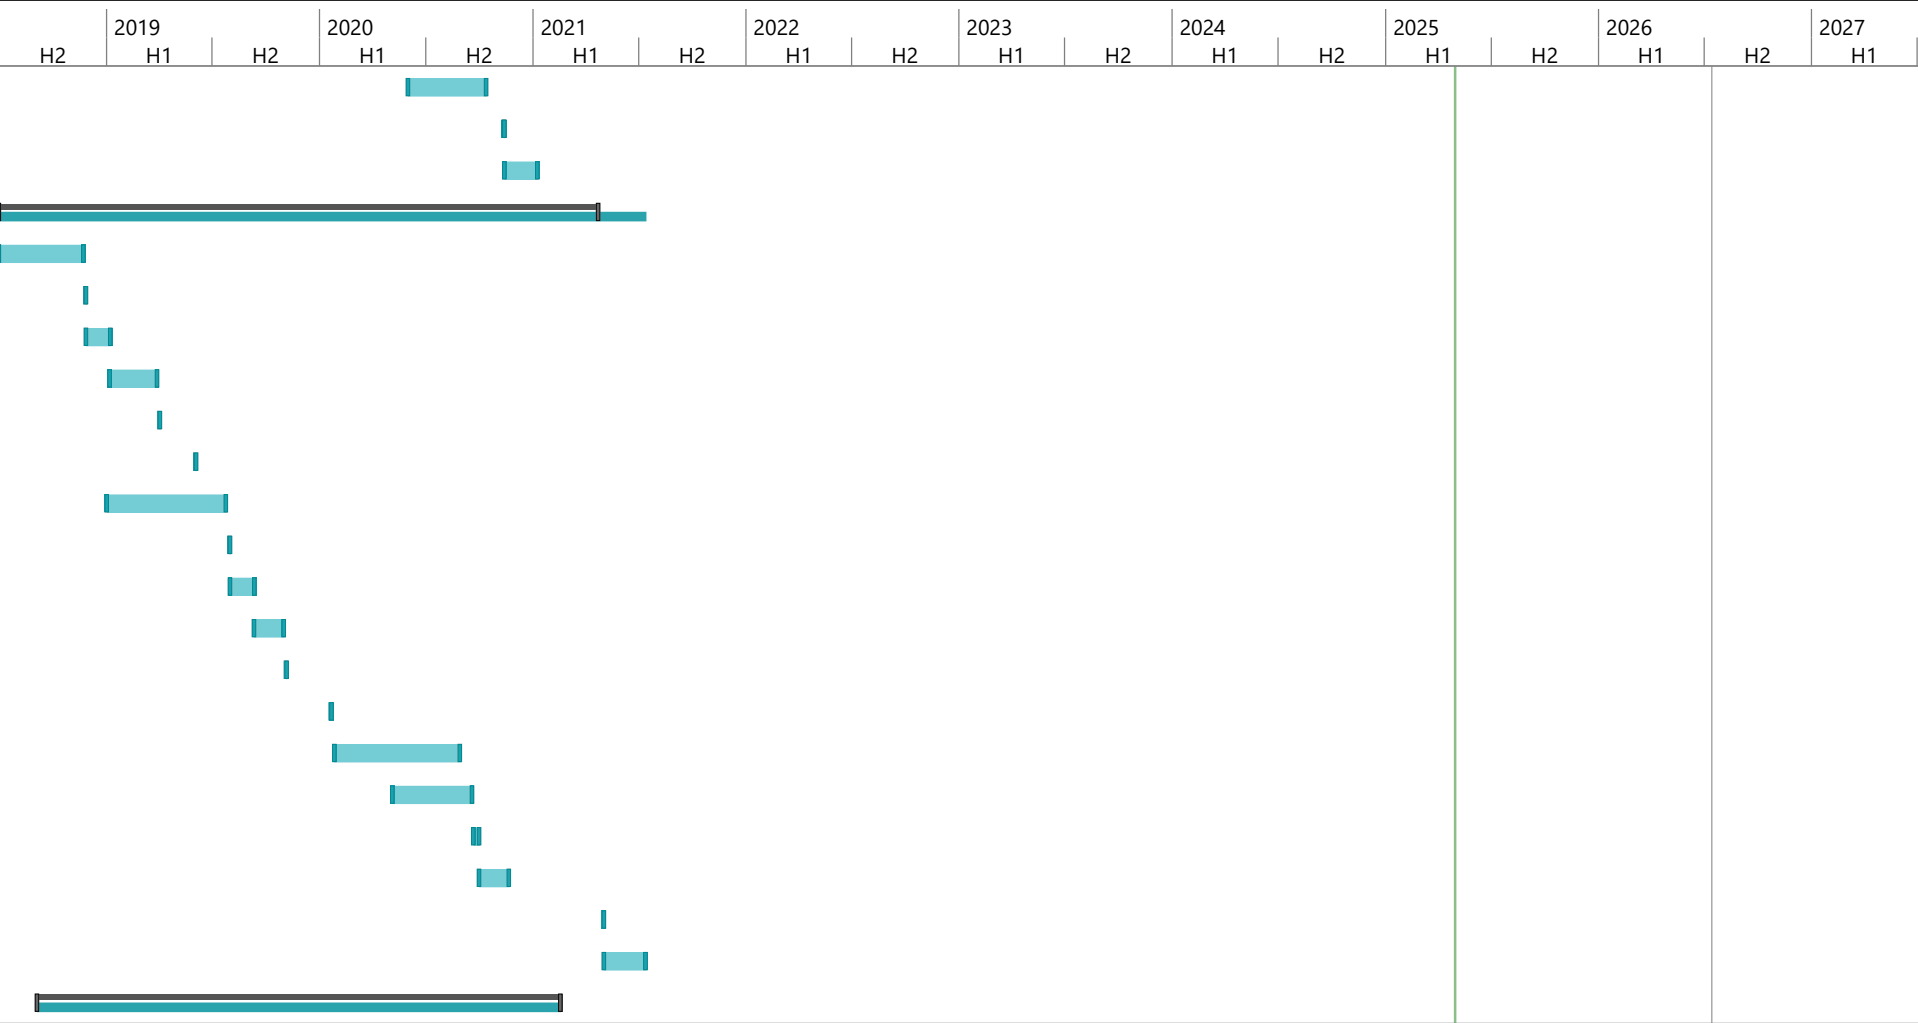
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |



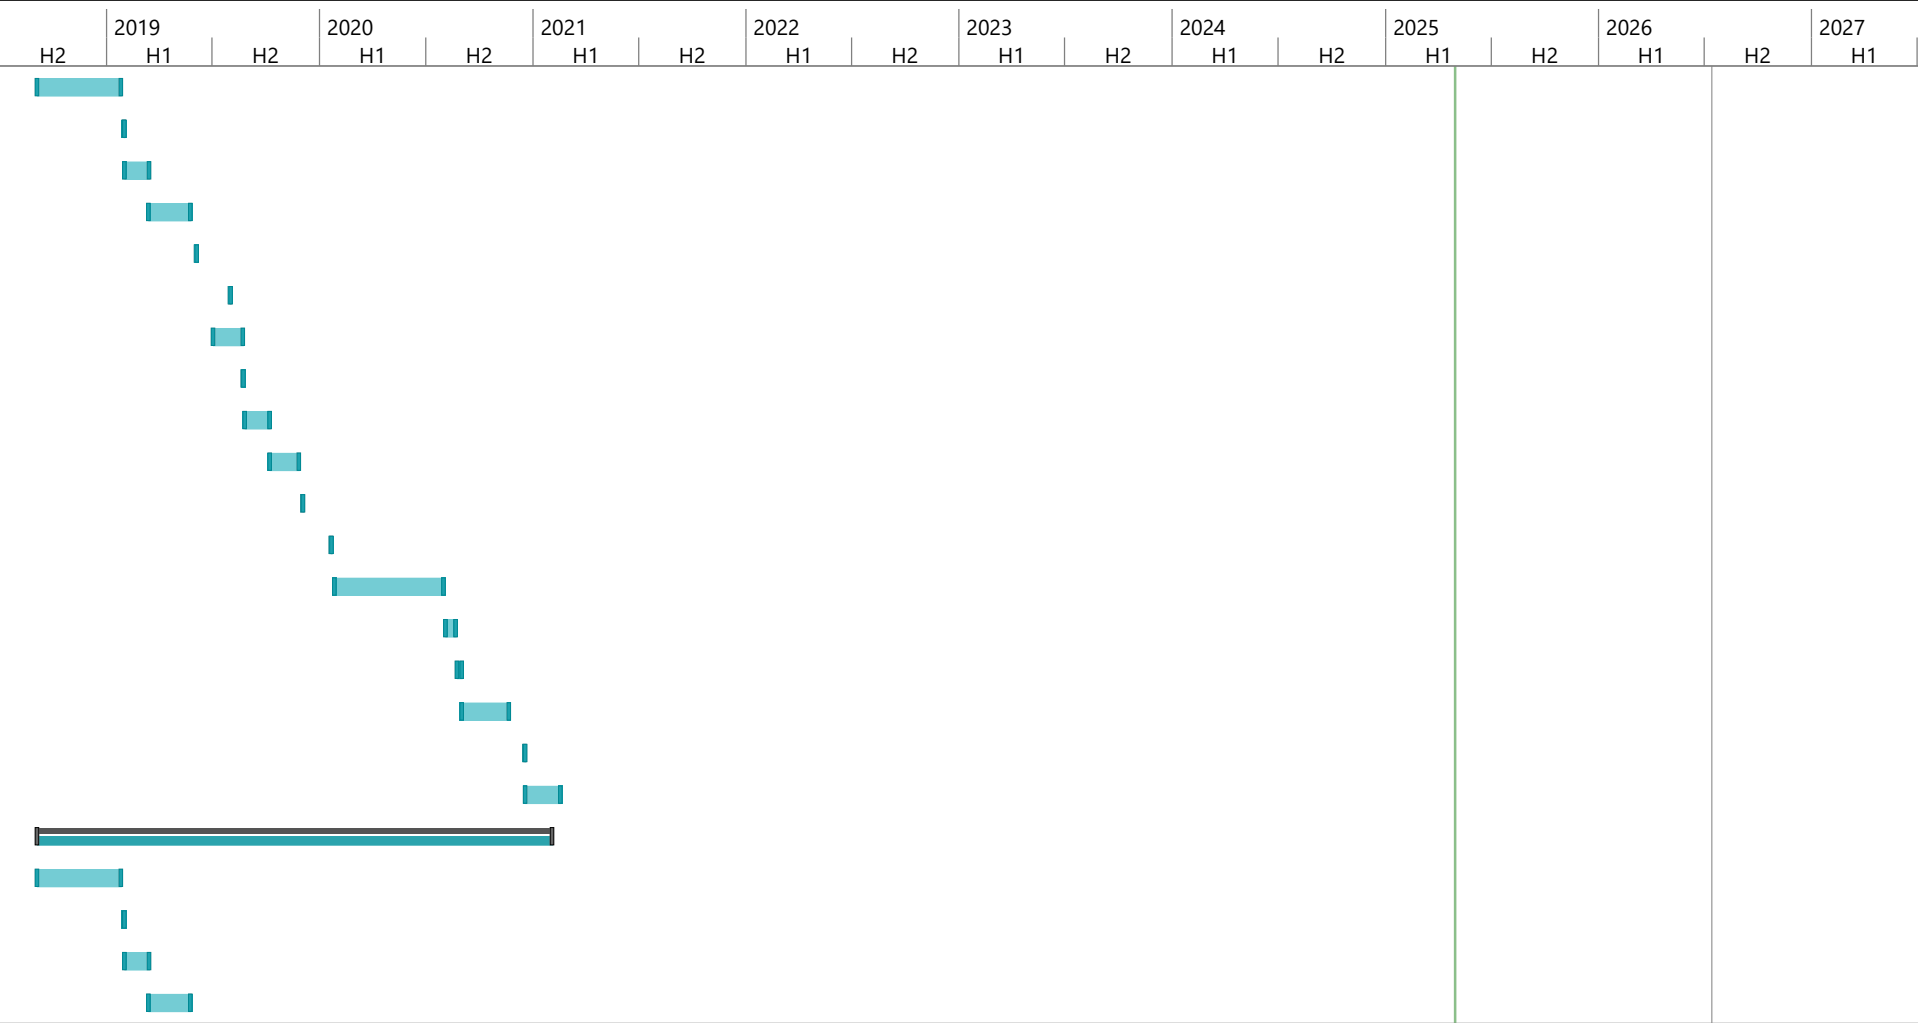


|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |

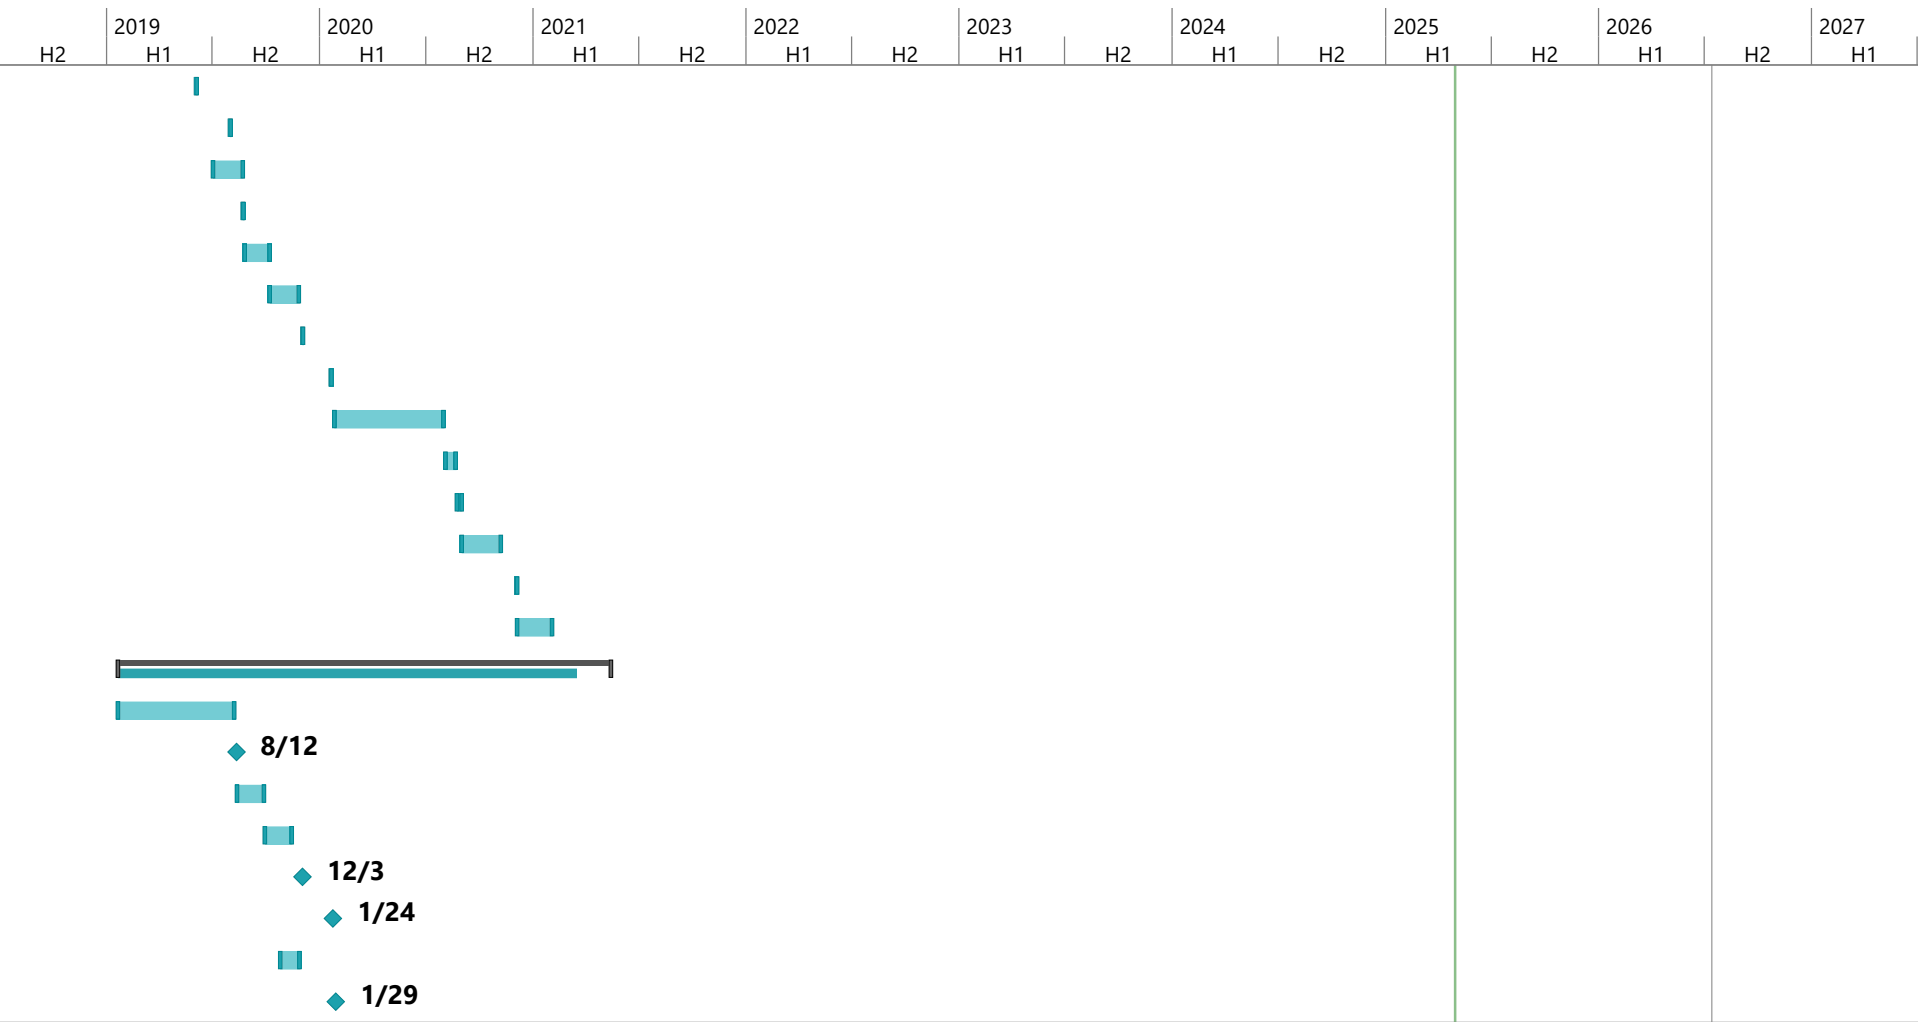




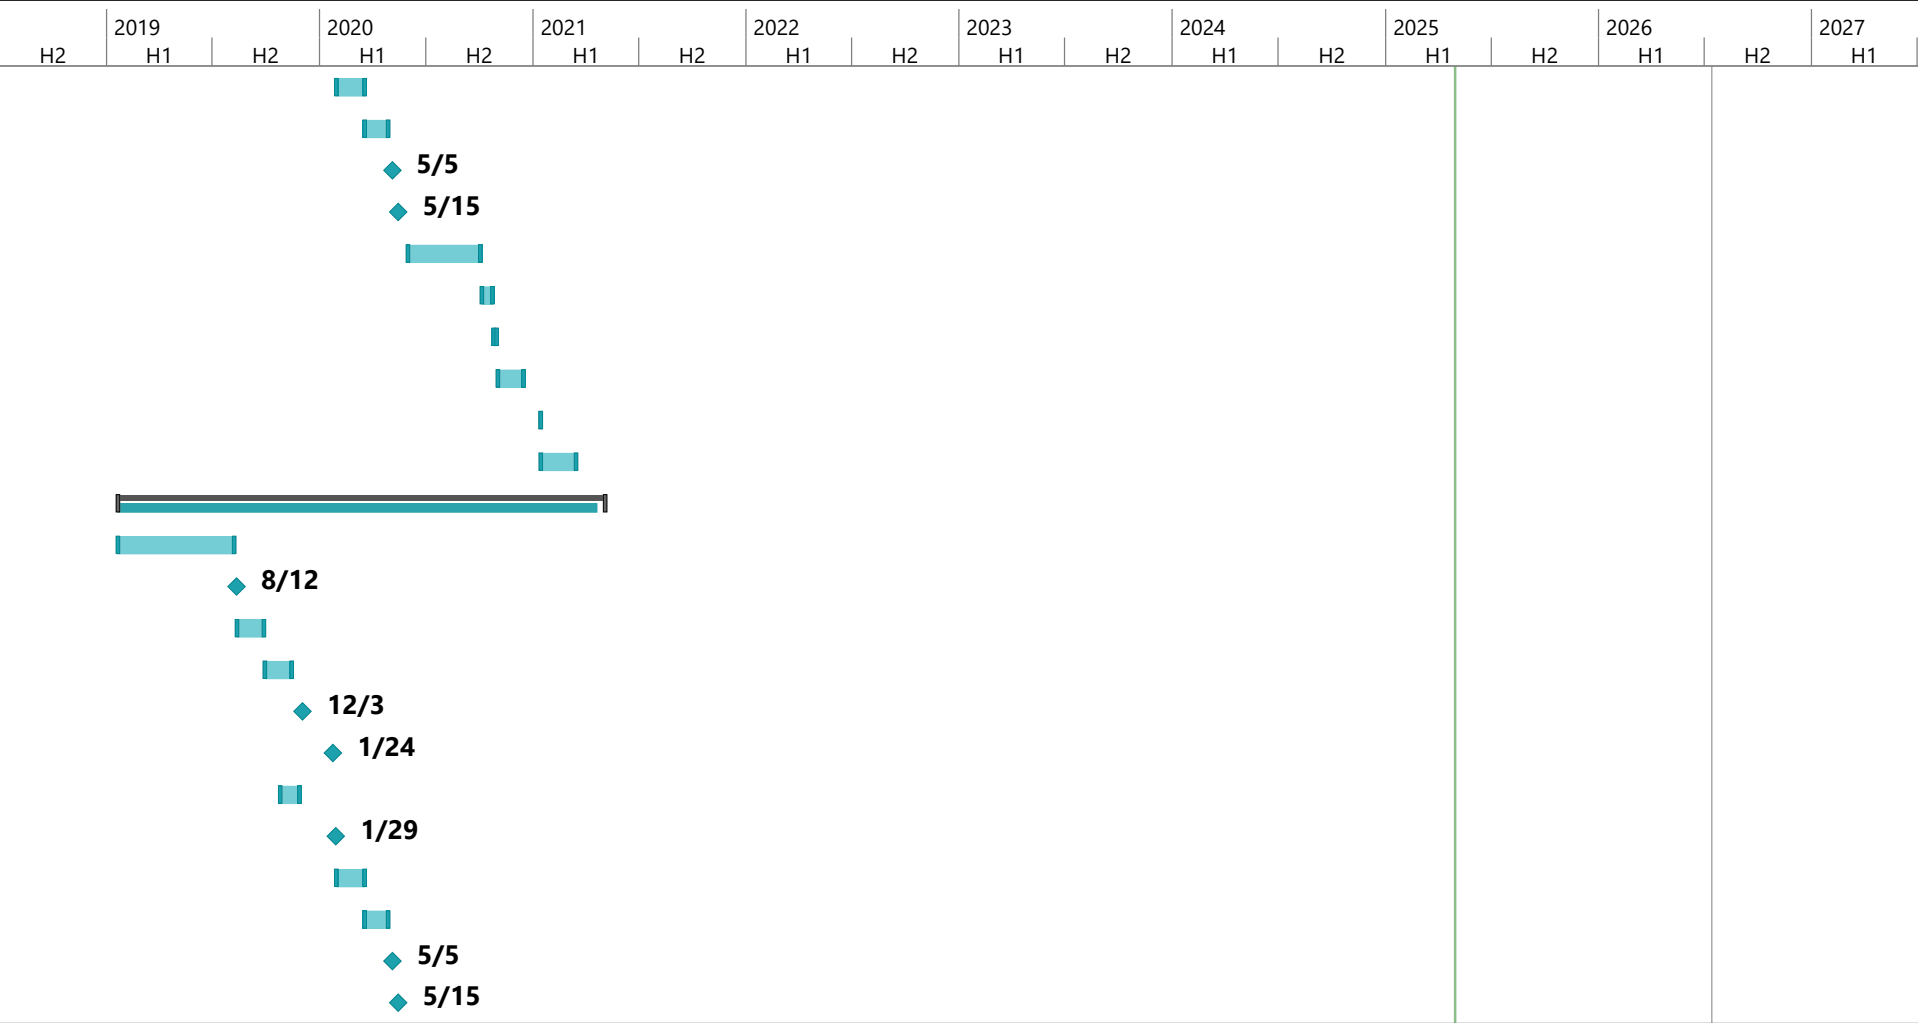
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |



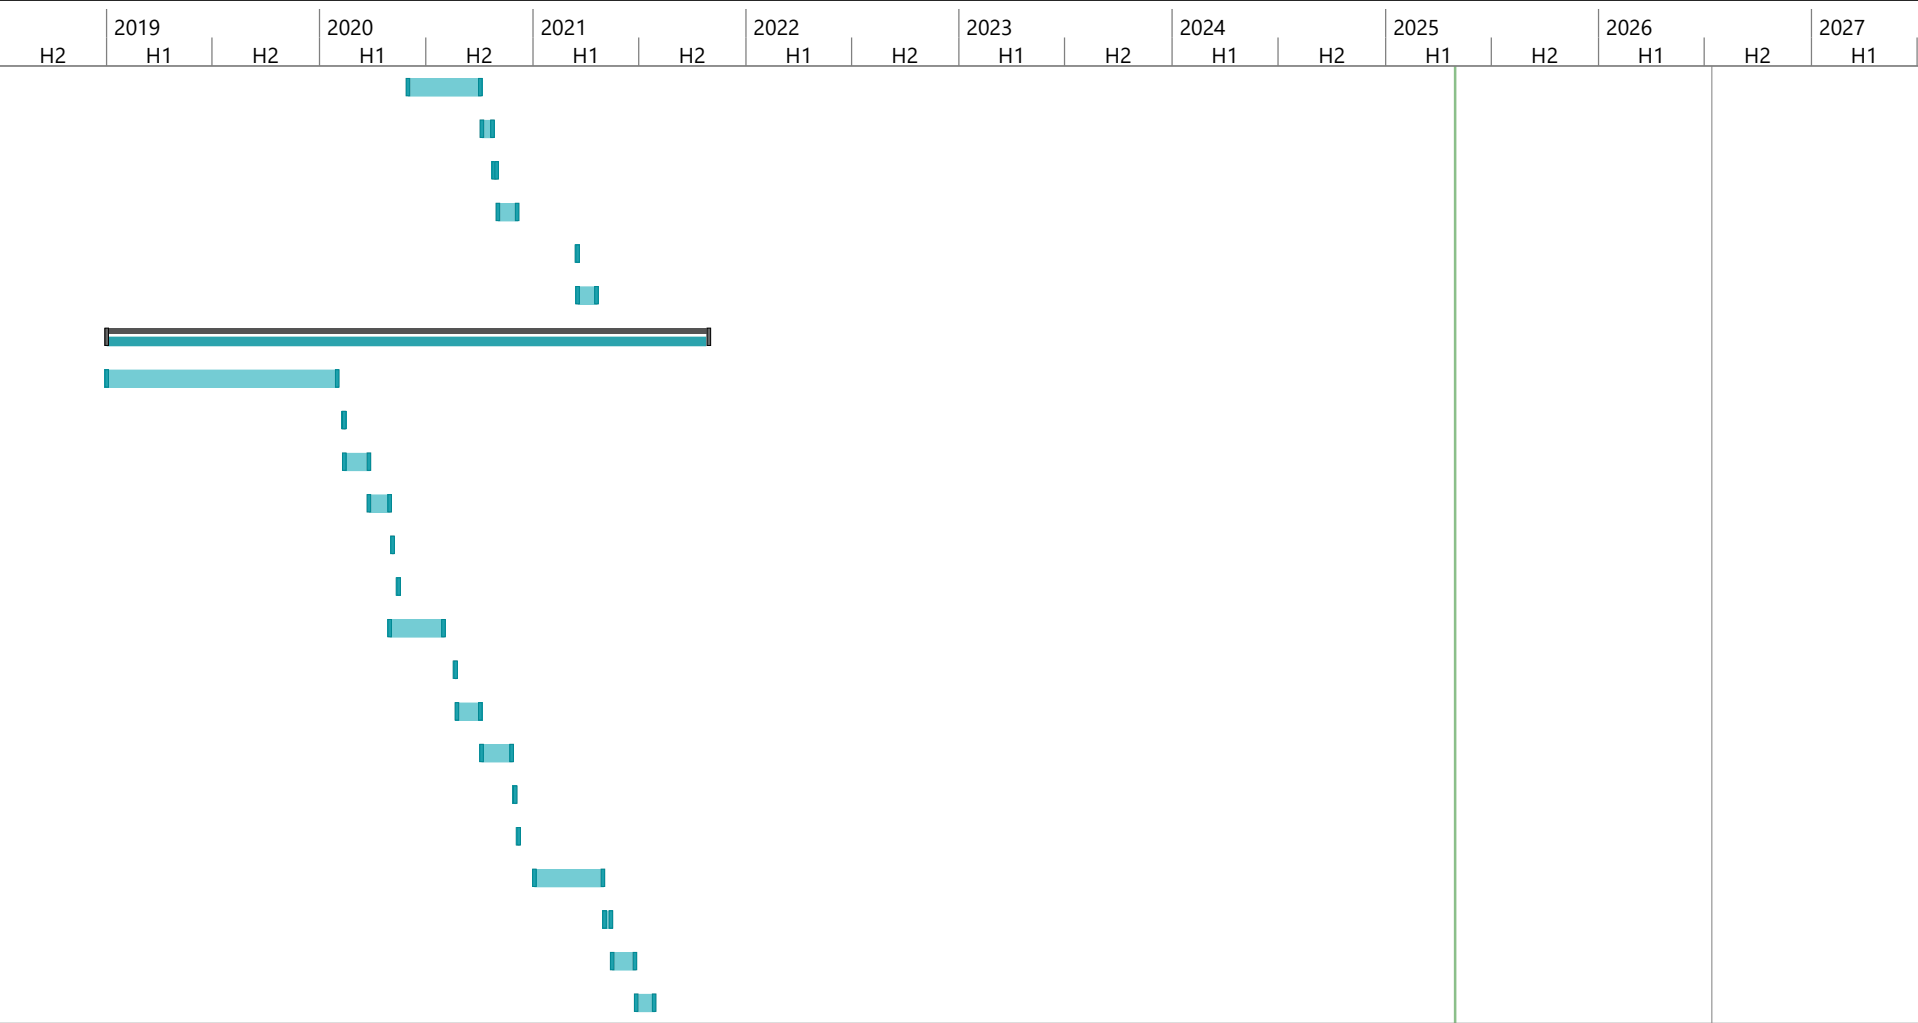
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |



|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |

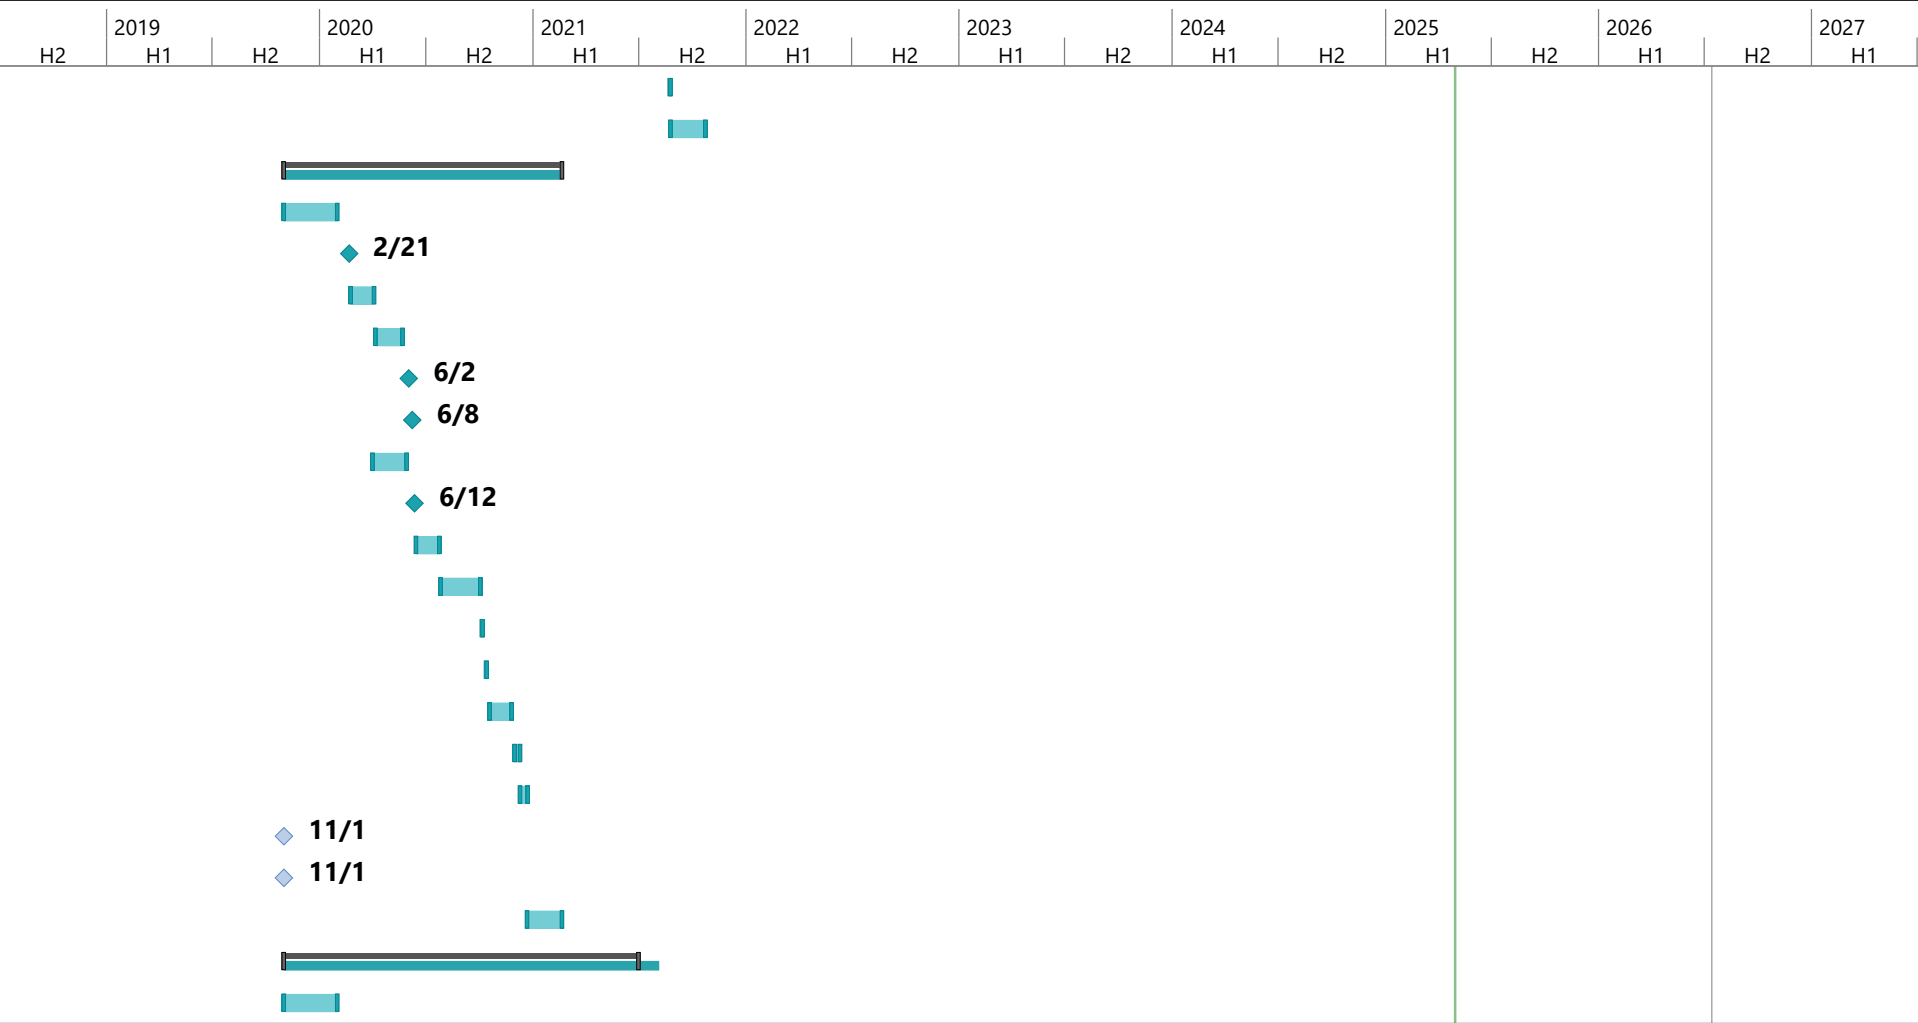


|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |

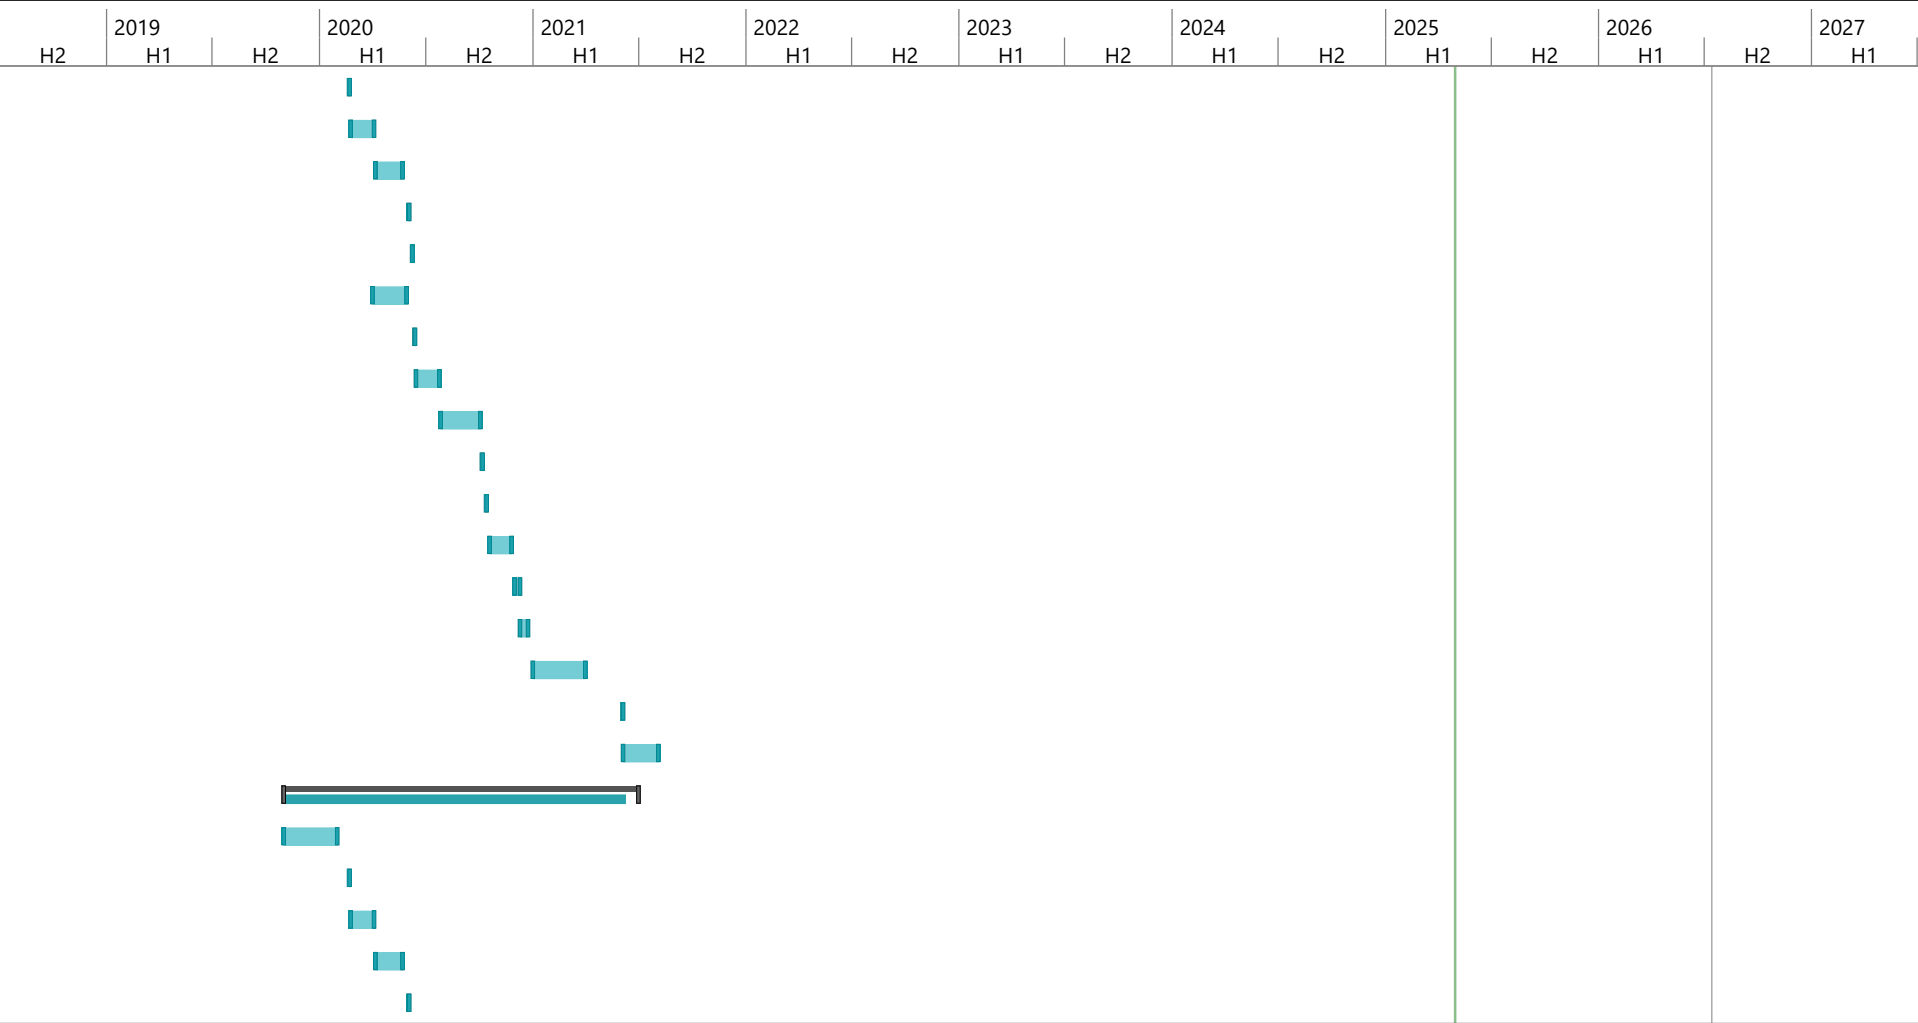


Project: IOU Master Task Timeli  
Date: Wed 4/30/25

|                    |  |                       |  |                    |  |
|--------------------|--|-----------------------|--|--------------------|--|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |  |
| Inactive Milestone |  | Finish-only           |  |                    |  |



|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |

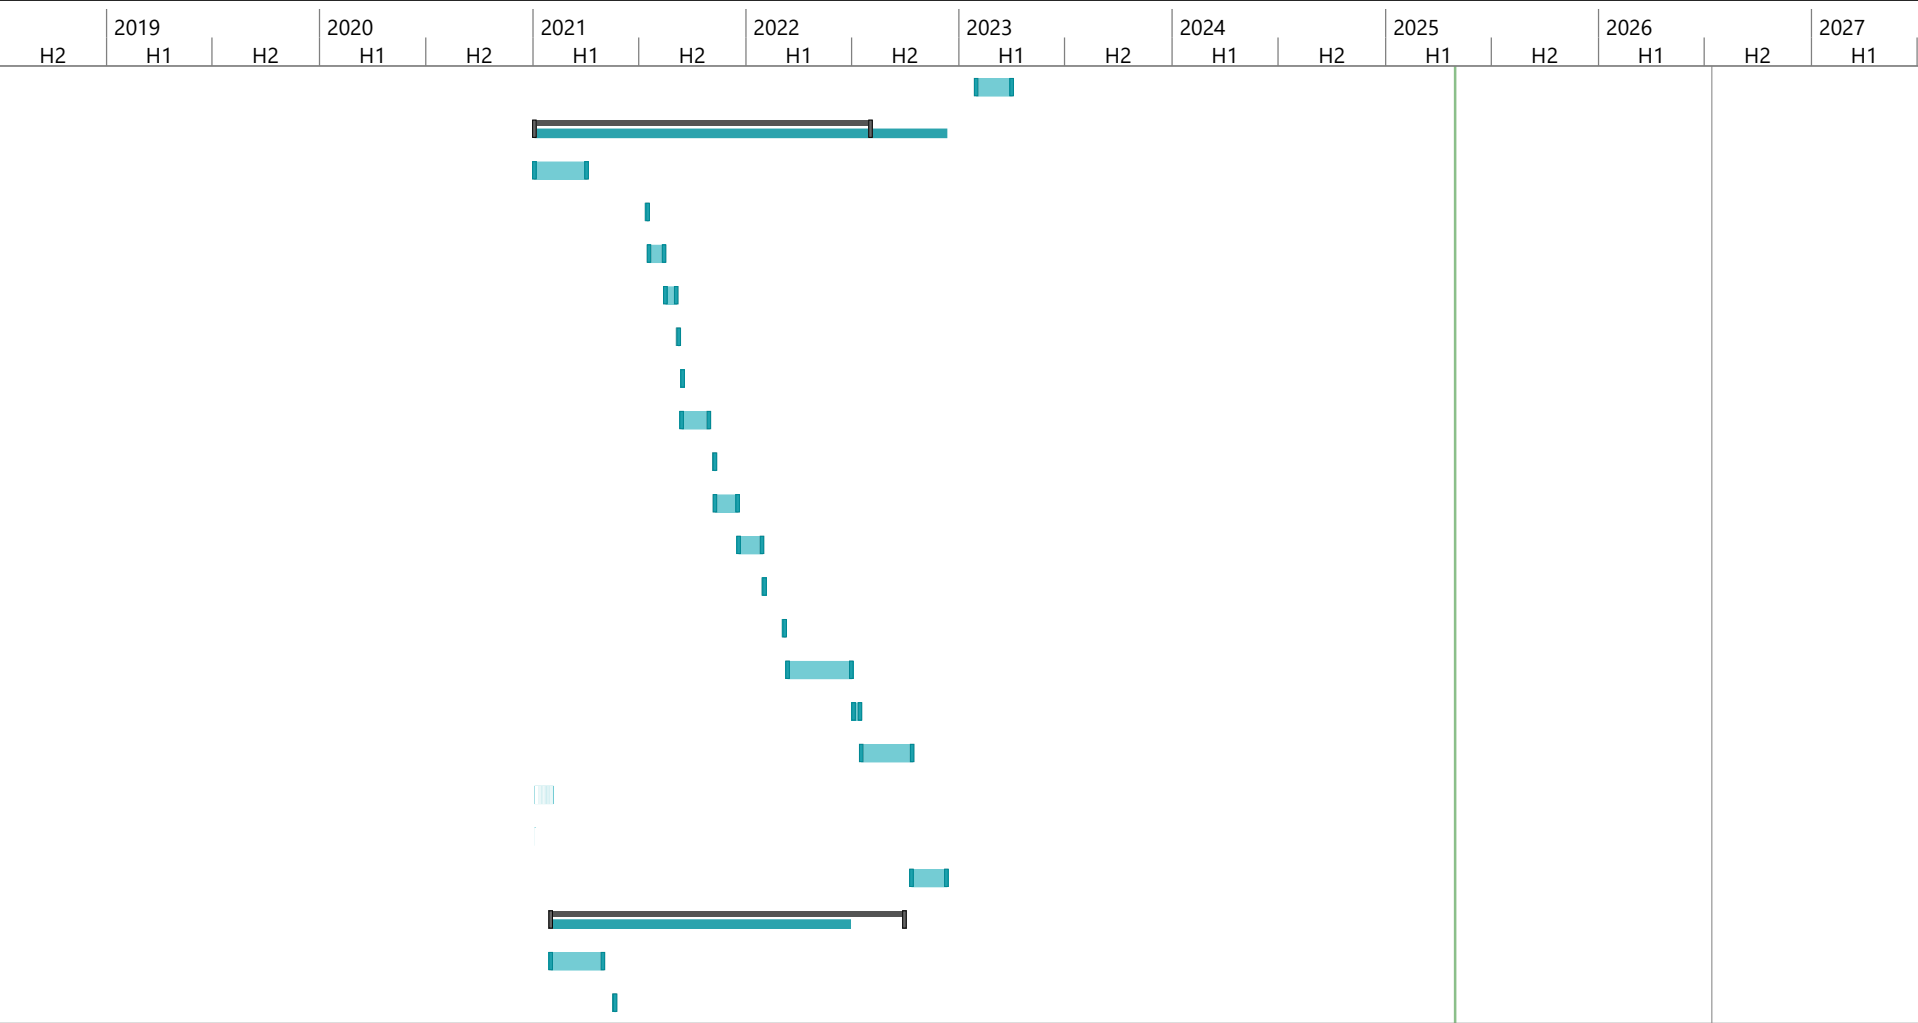


|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |









Project: IOU Master Task Timeli  
Date: Wed 4/30/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

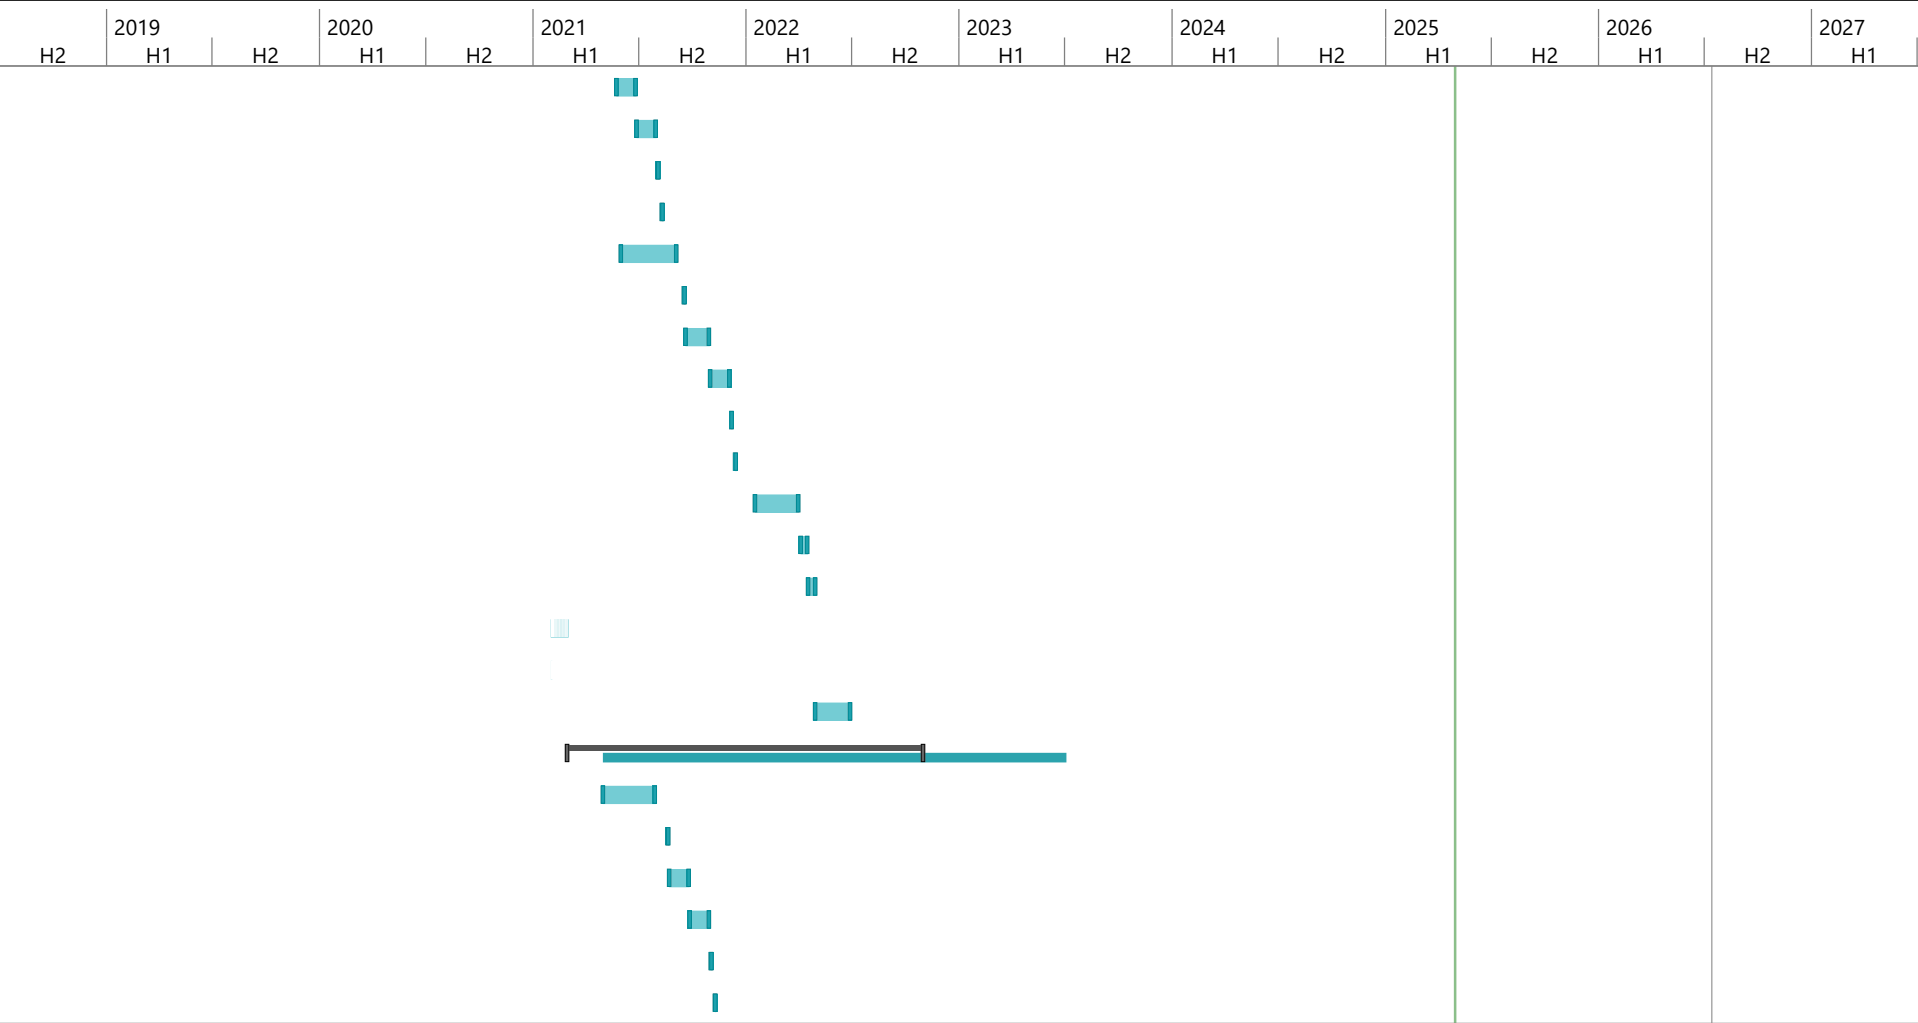
External Milestone

Deadline

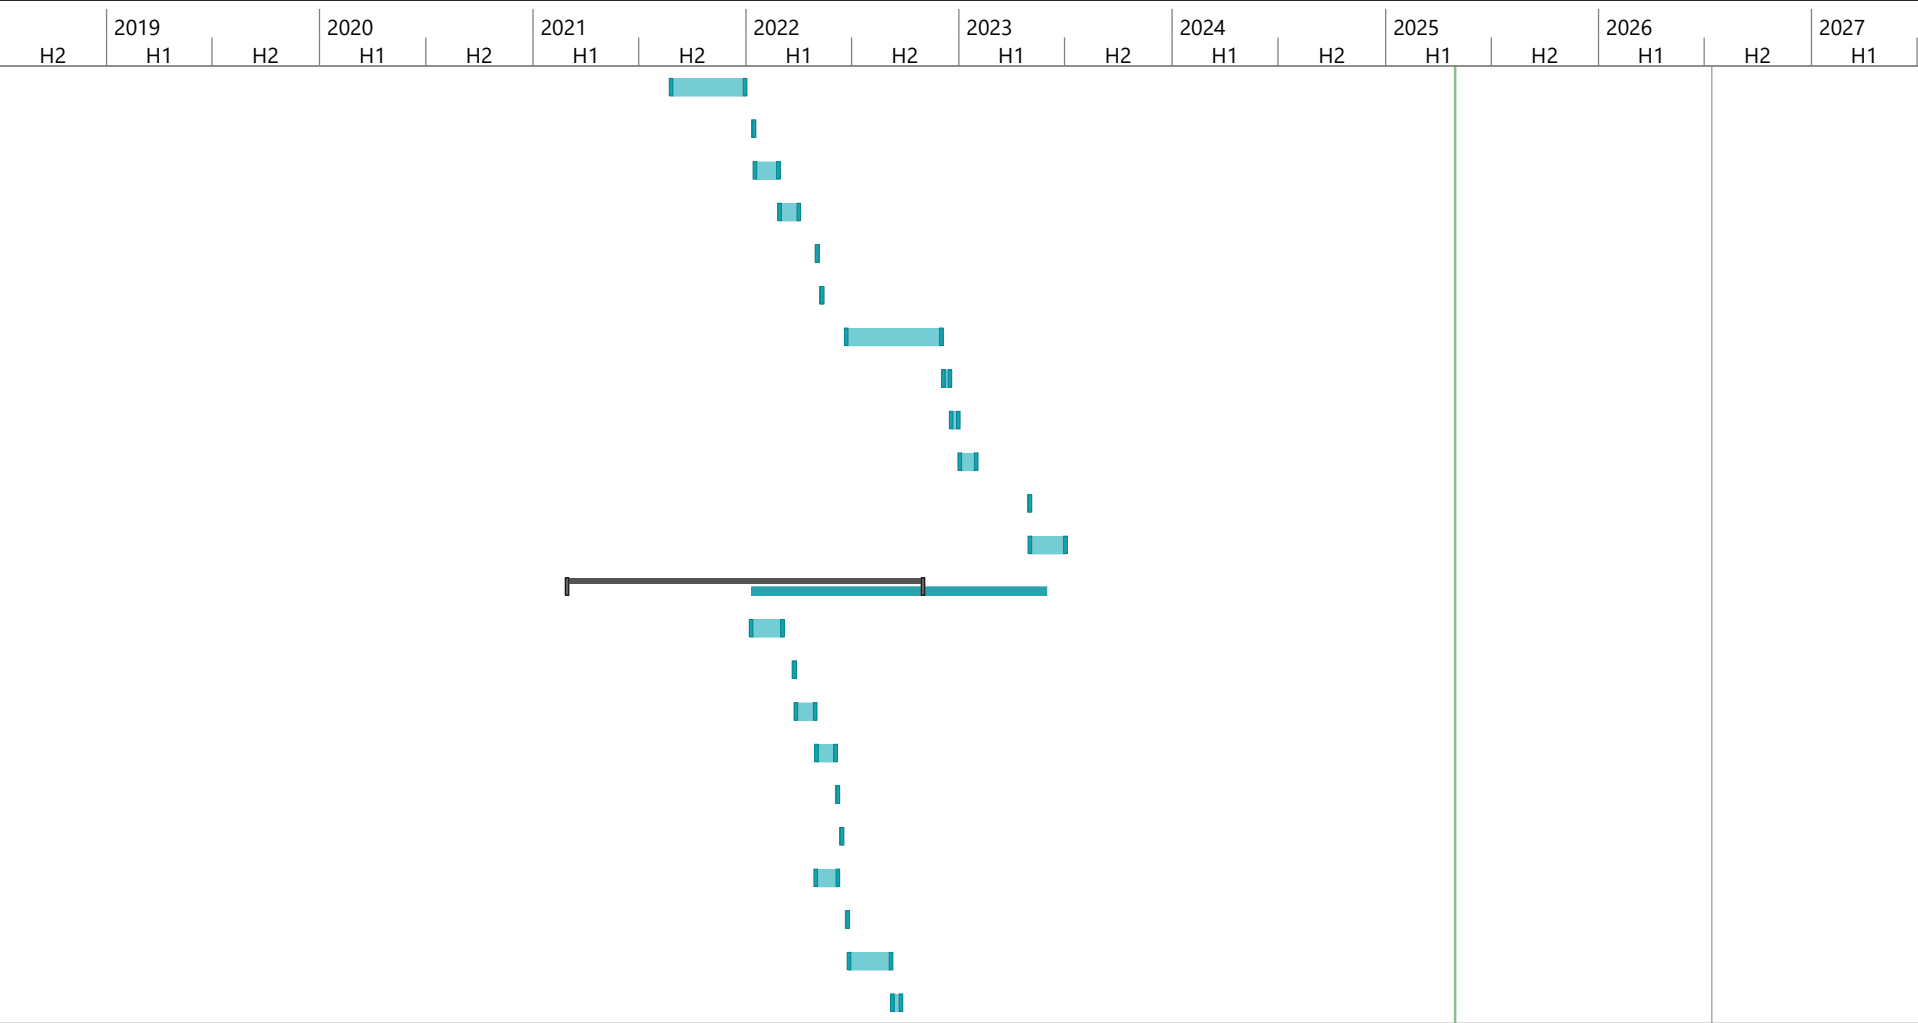
Progress

Manual Progress

Page 87



|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |



Project: IOU Master Task Timeli  
Date: Wed 4/30/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

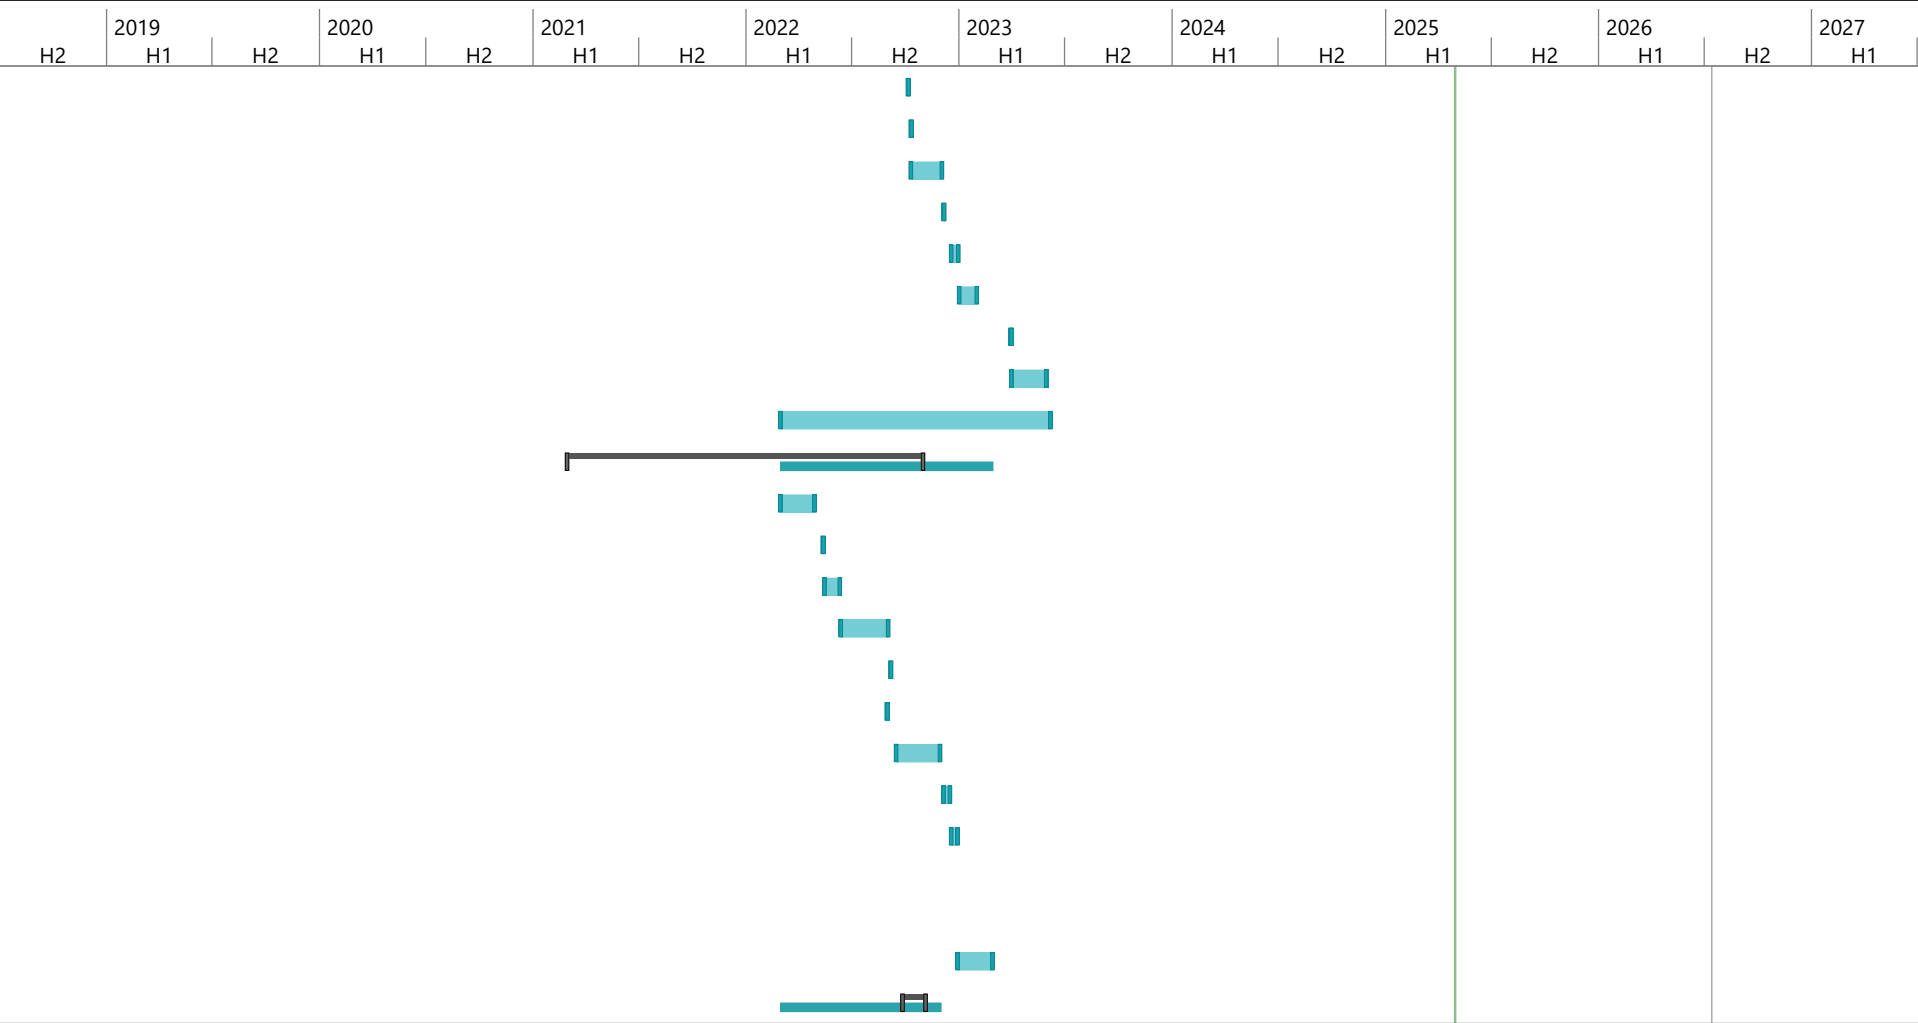
External Milestone

Deadline

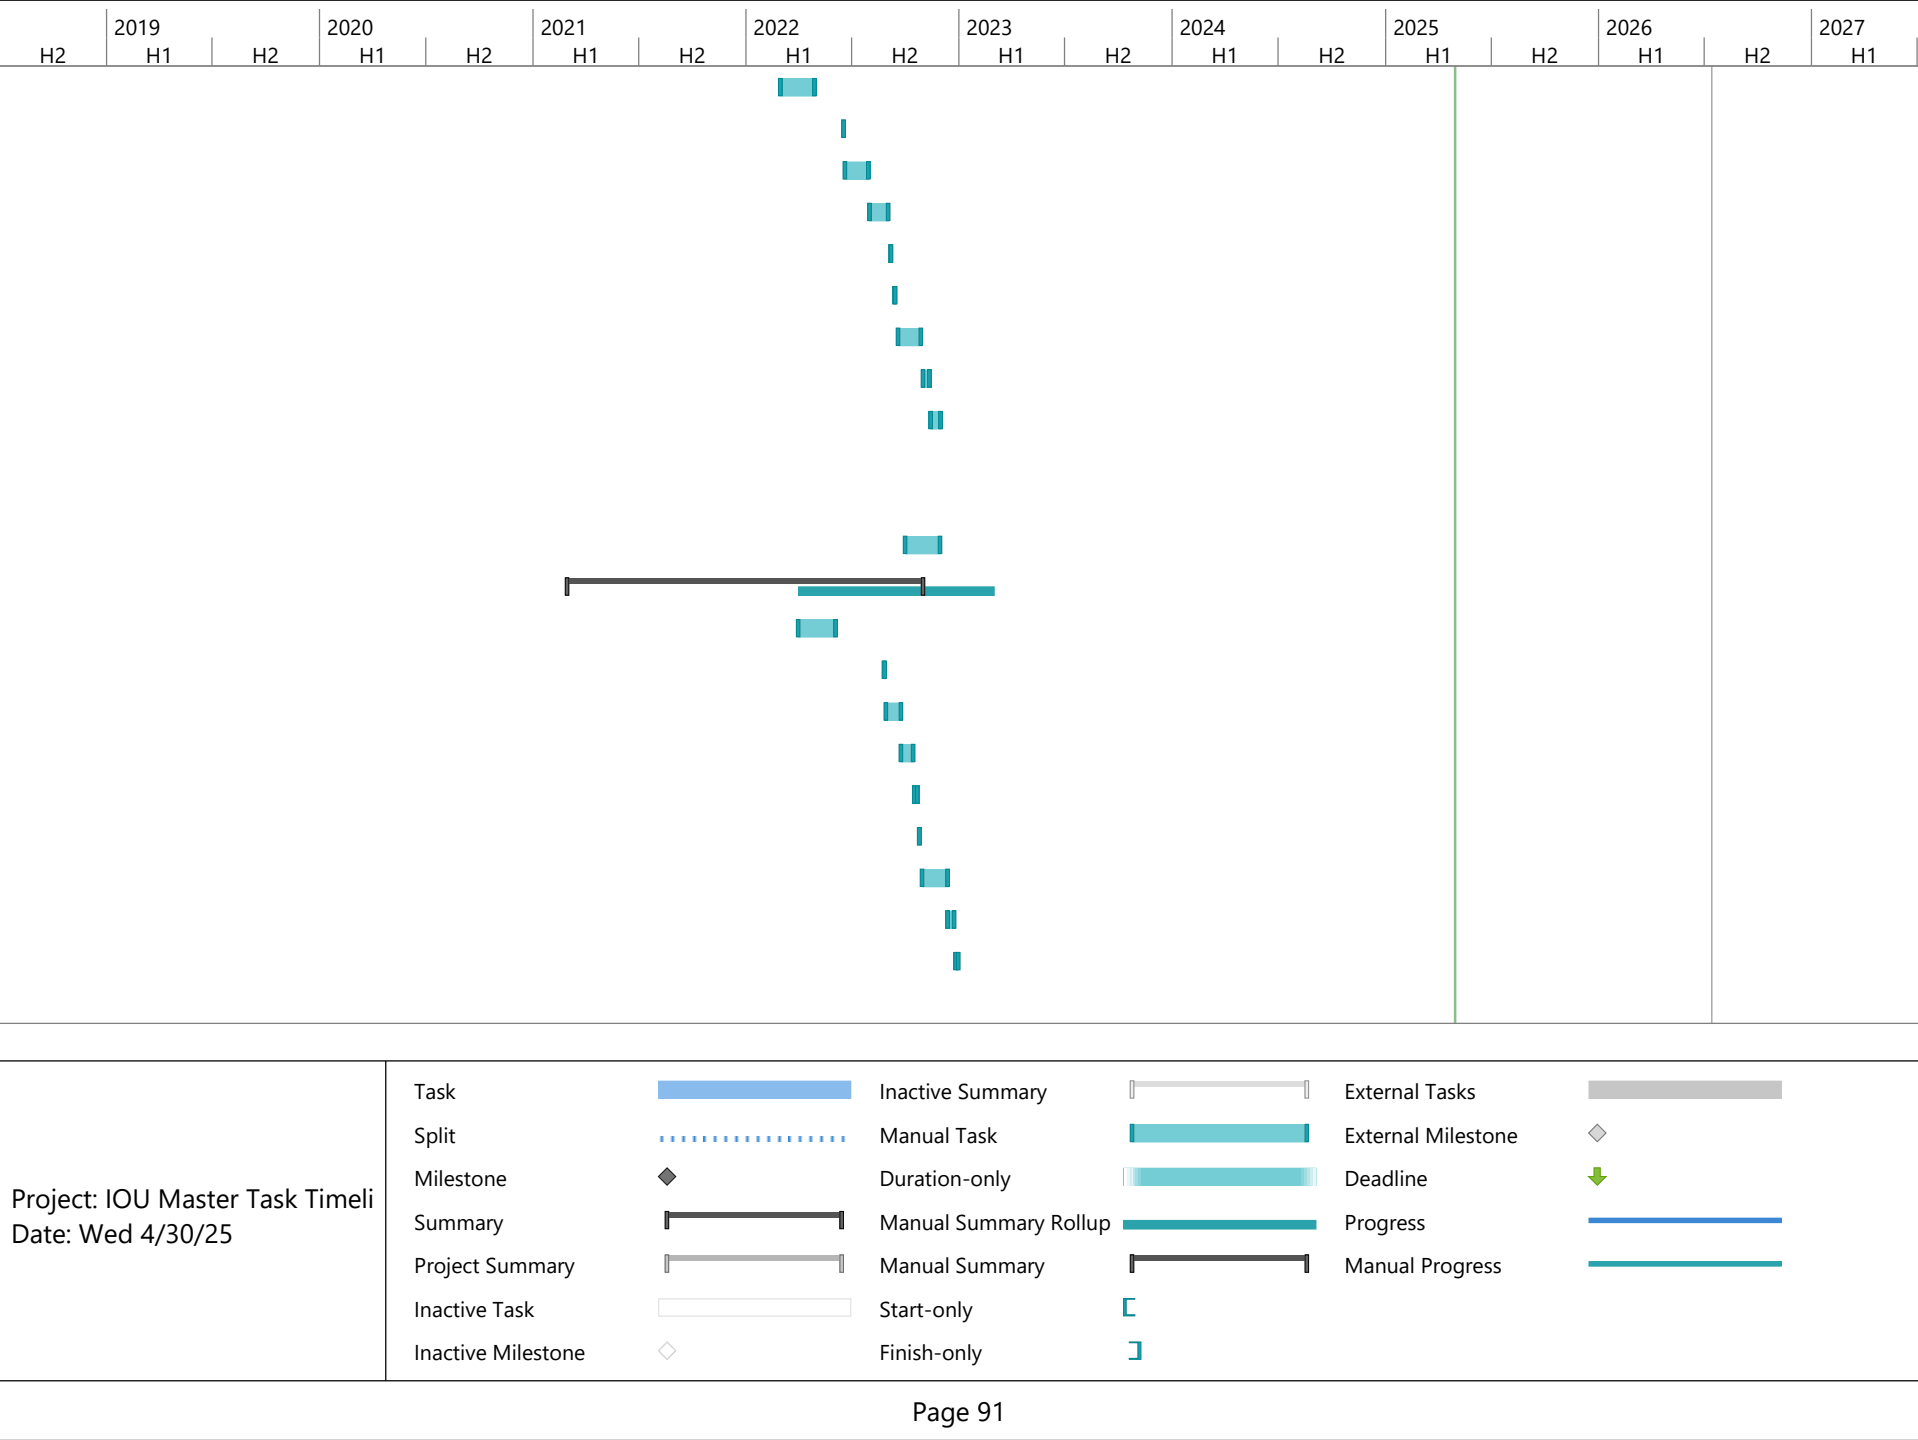
Progress

Manual Progress

Page 89

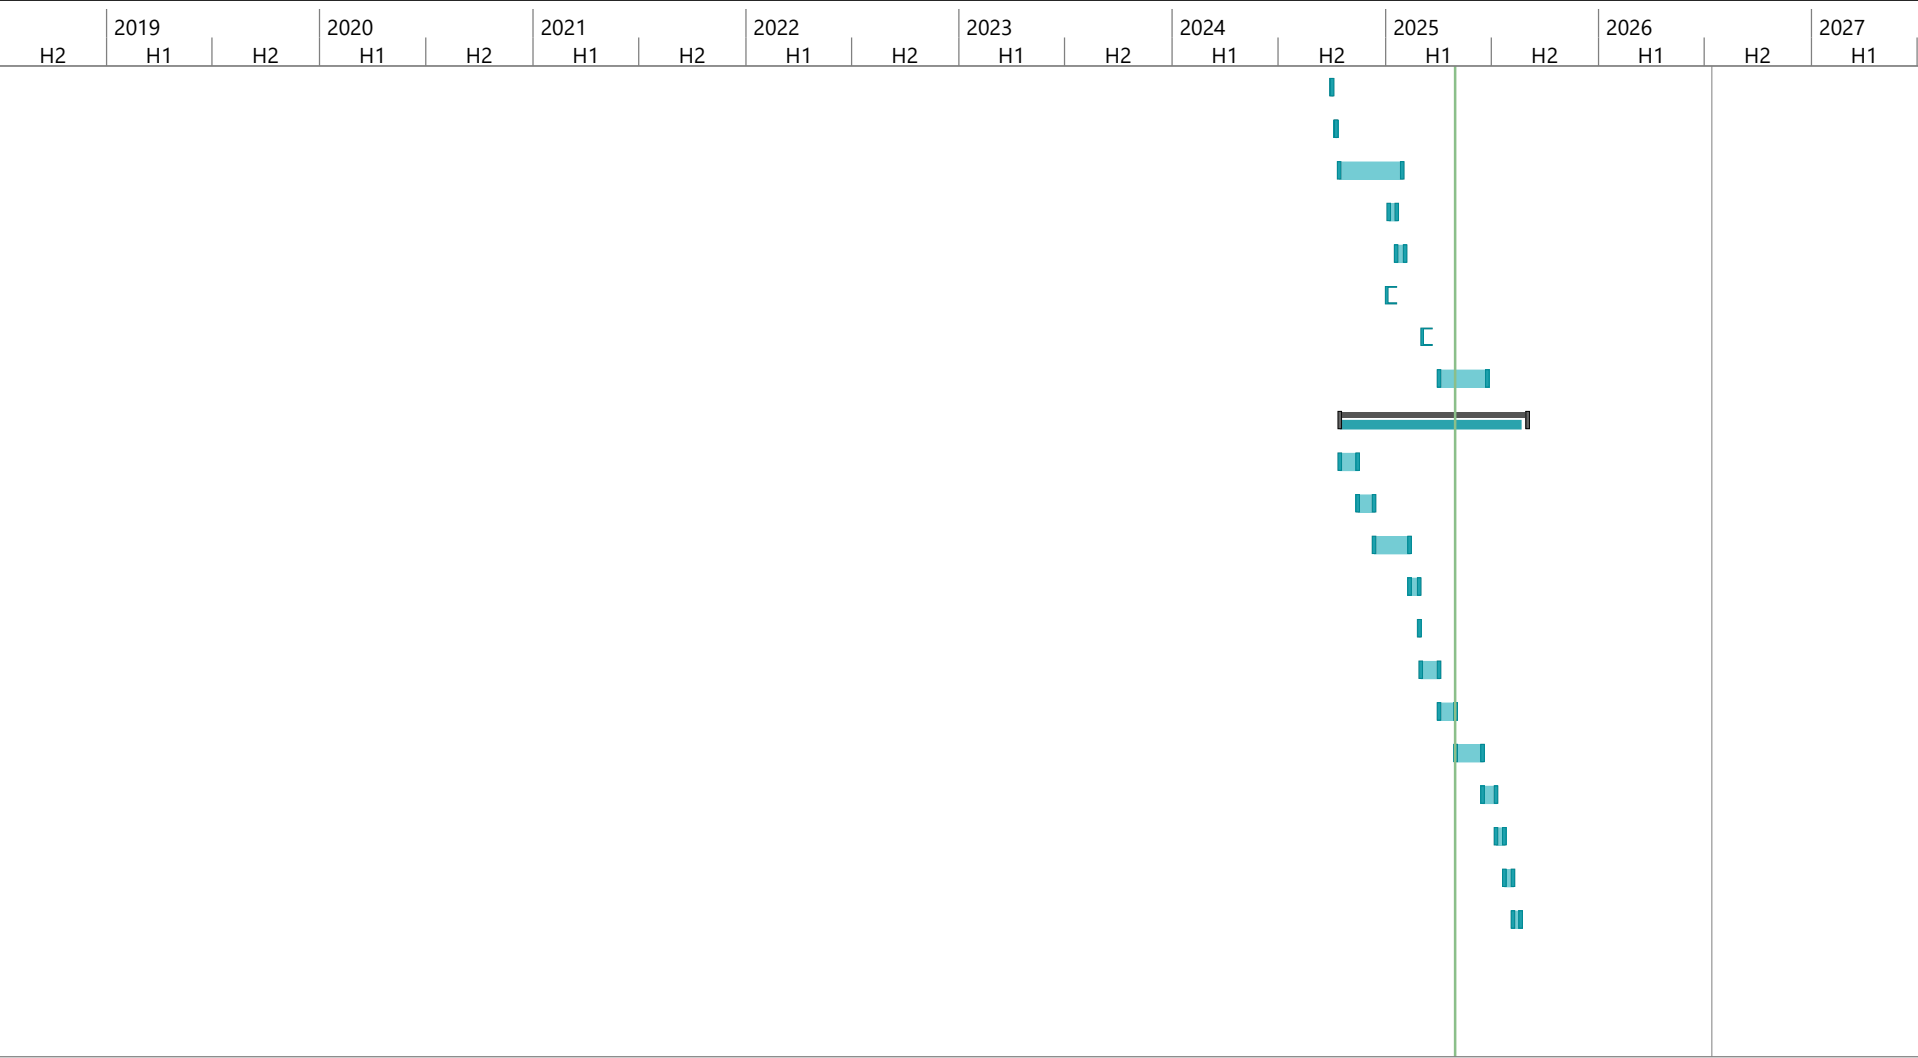


|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |

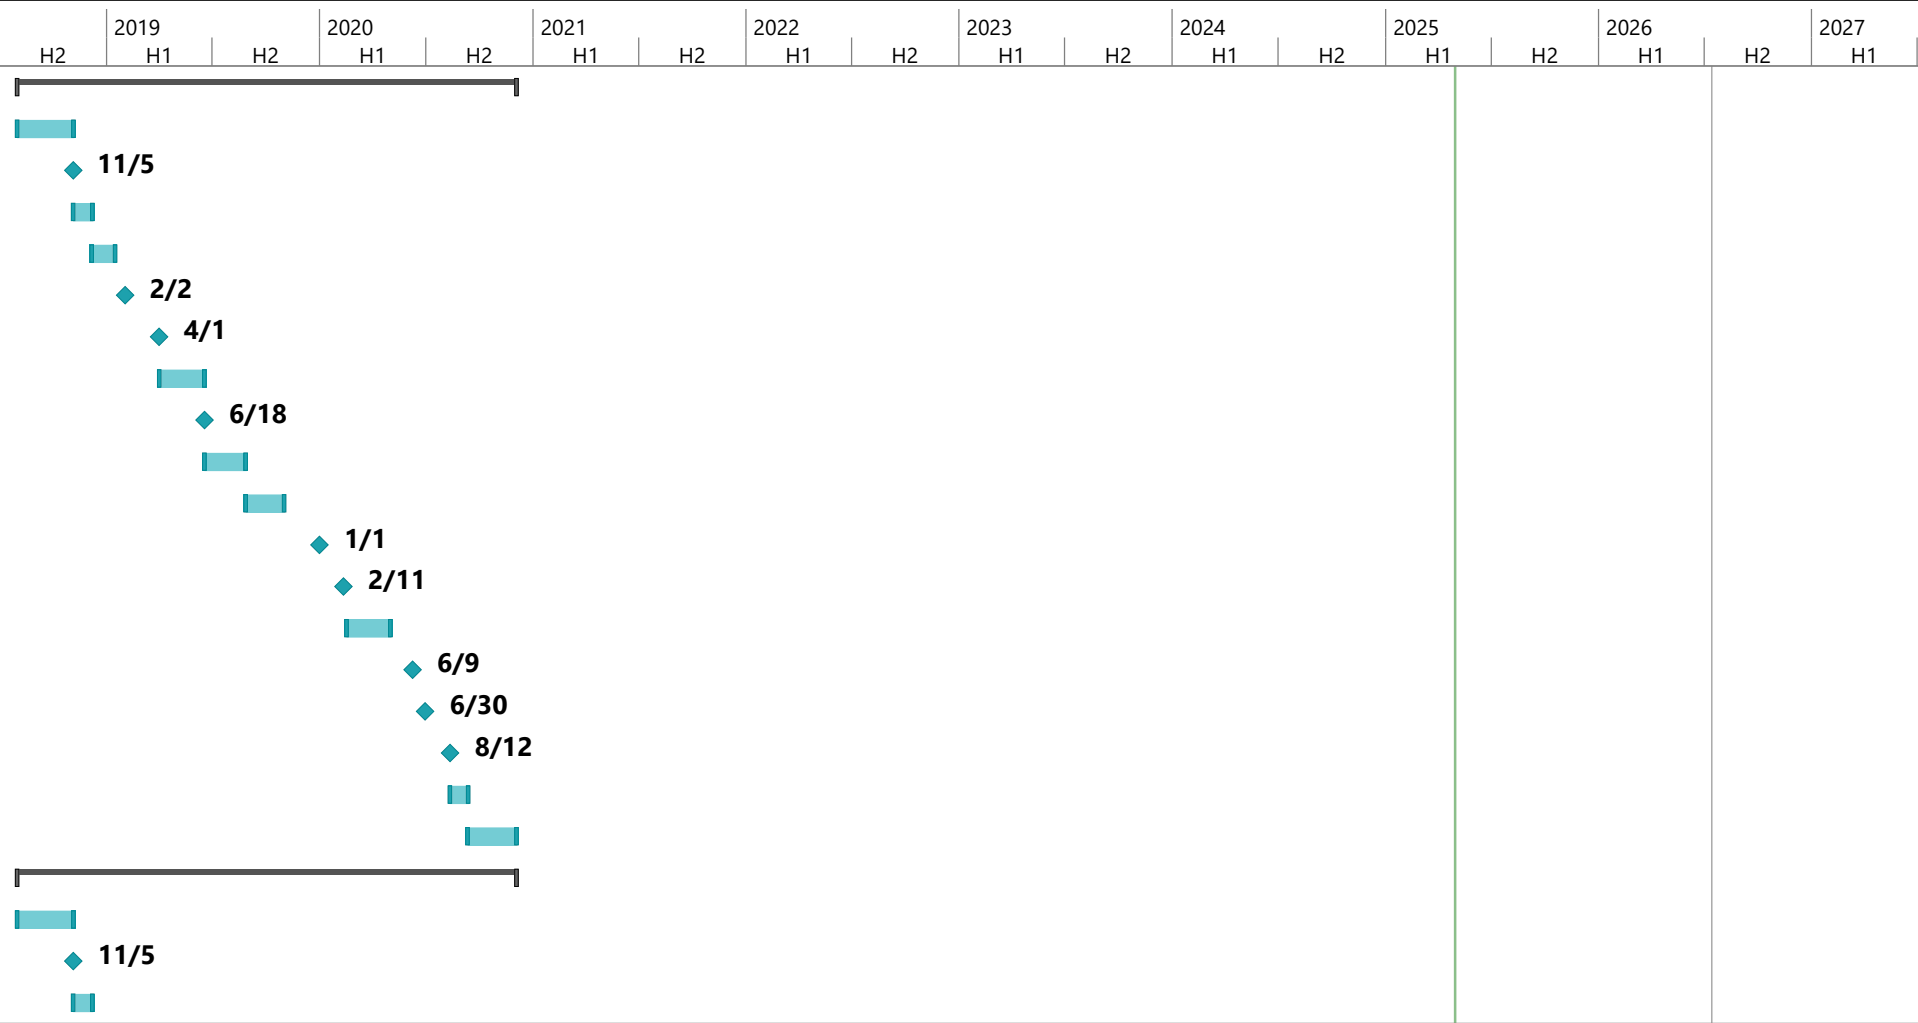




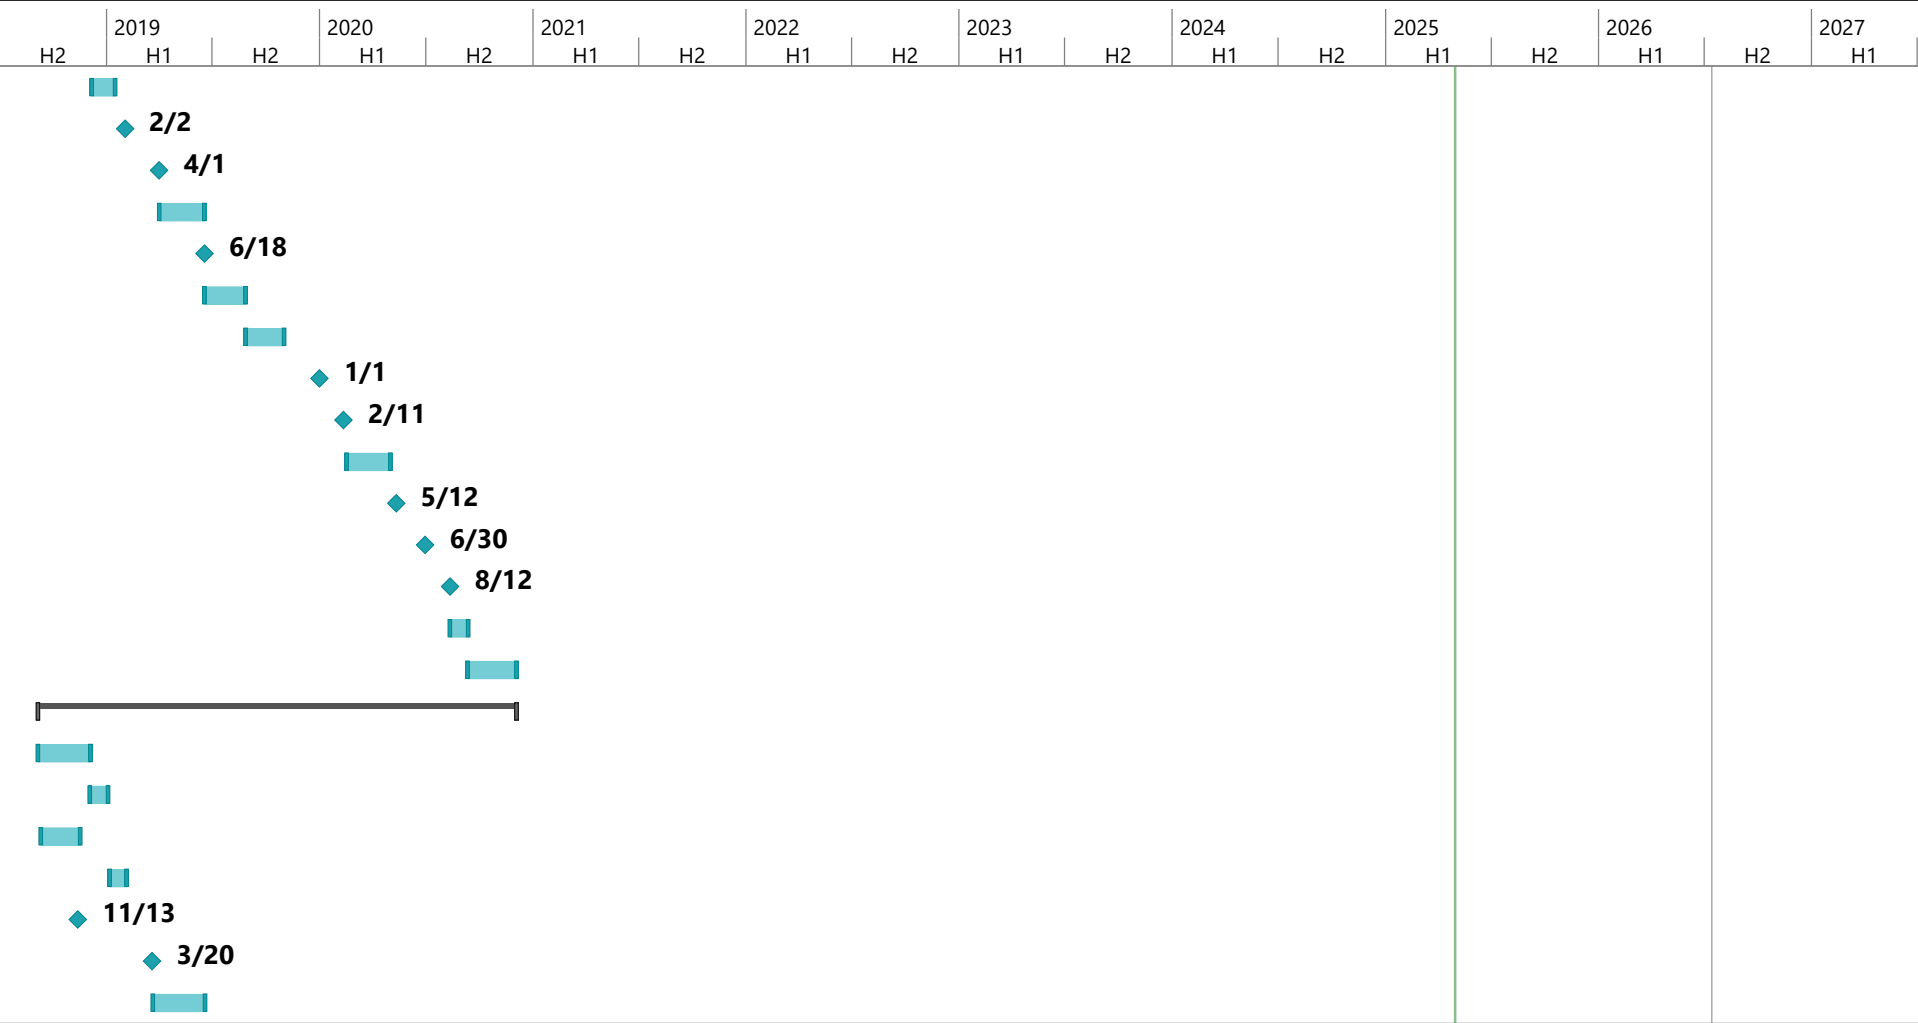




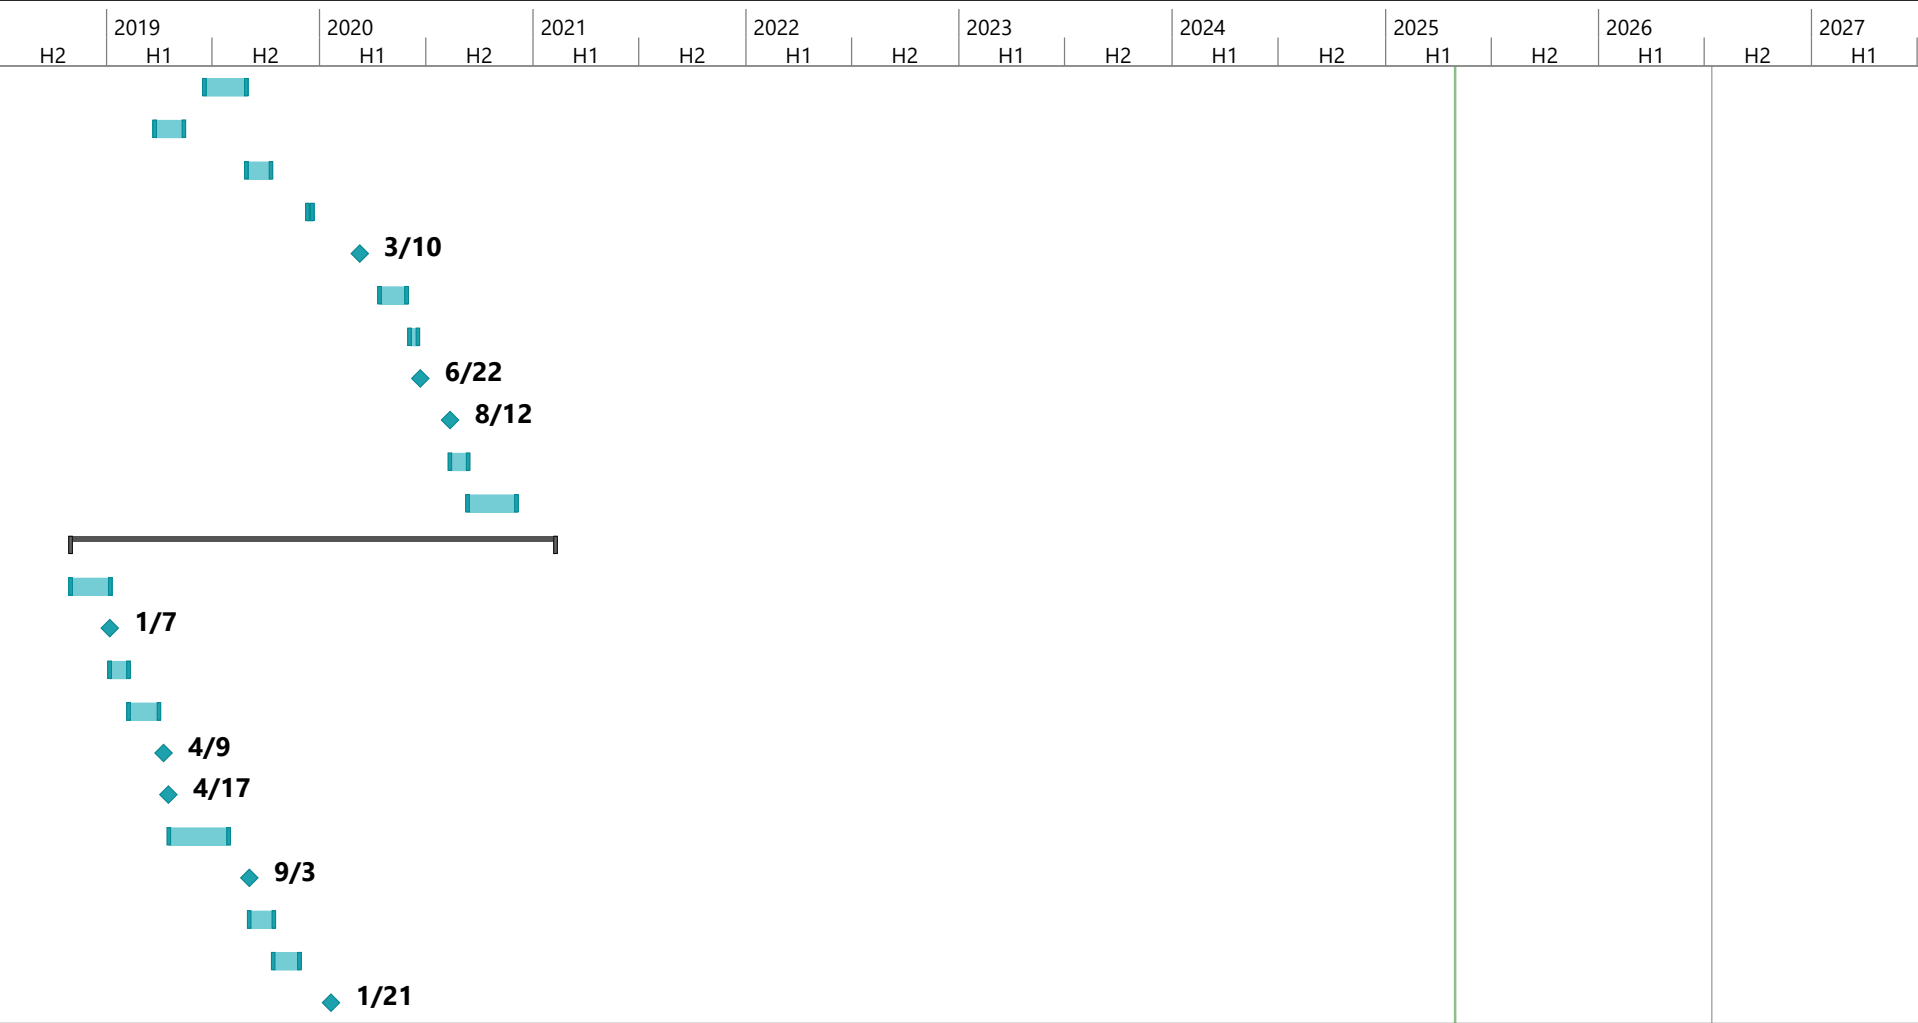
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |



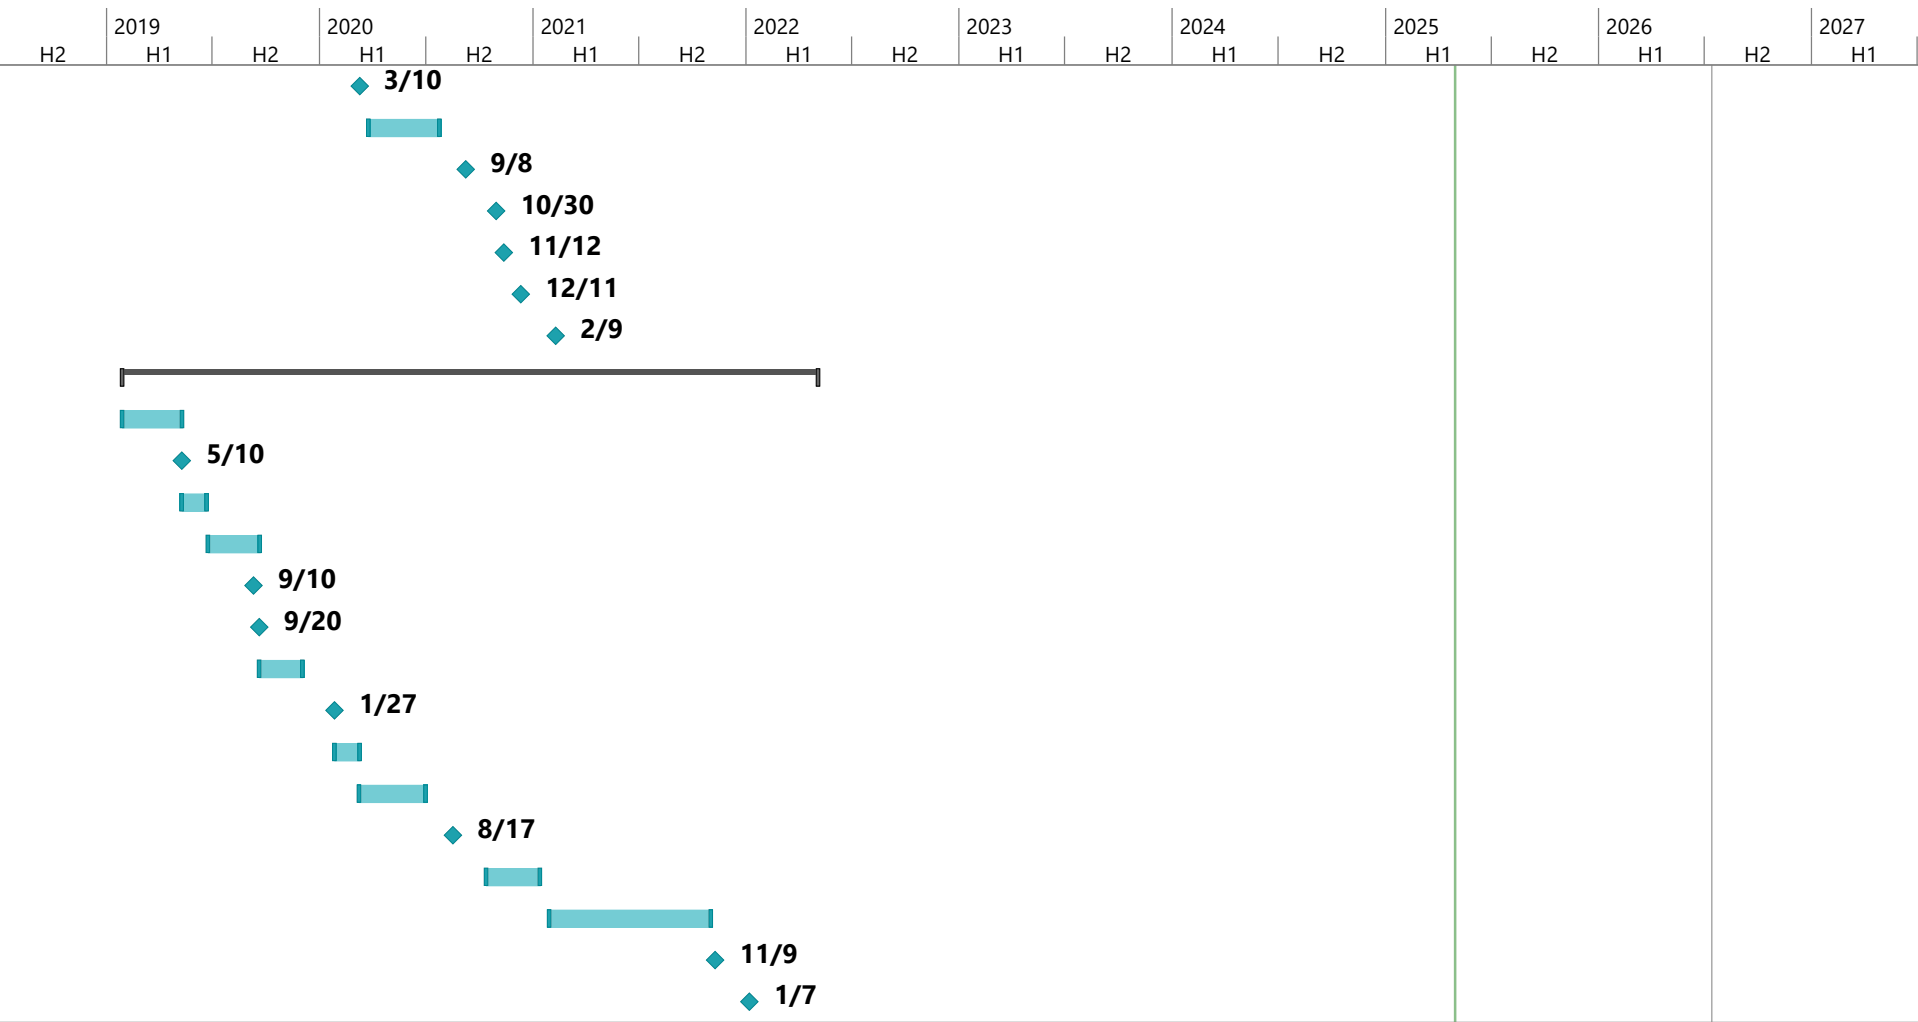
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |



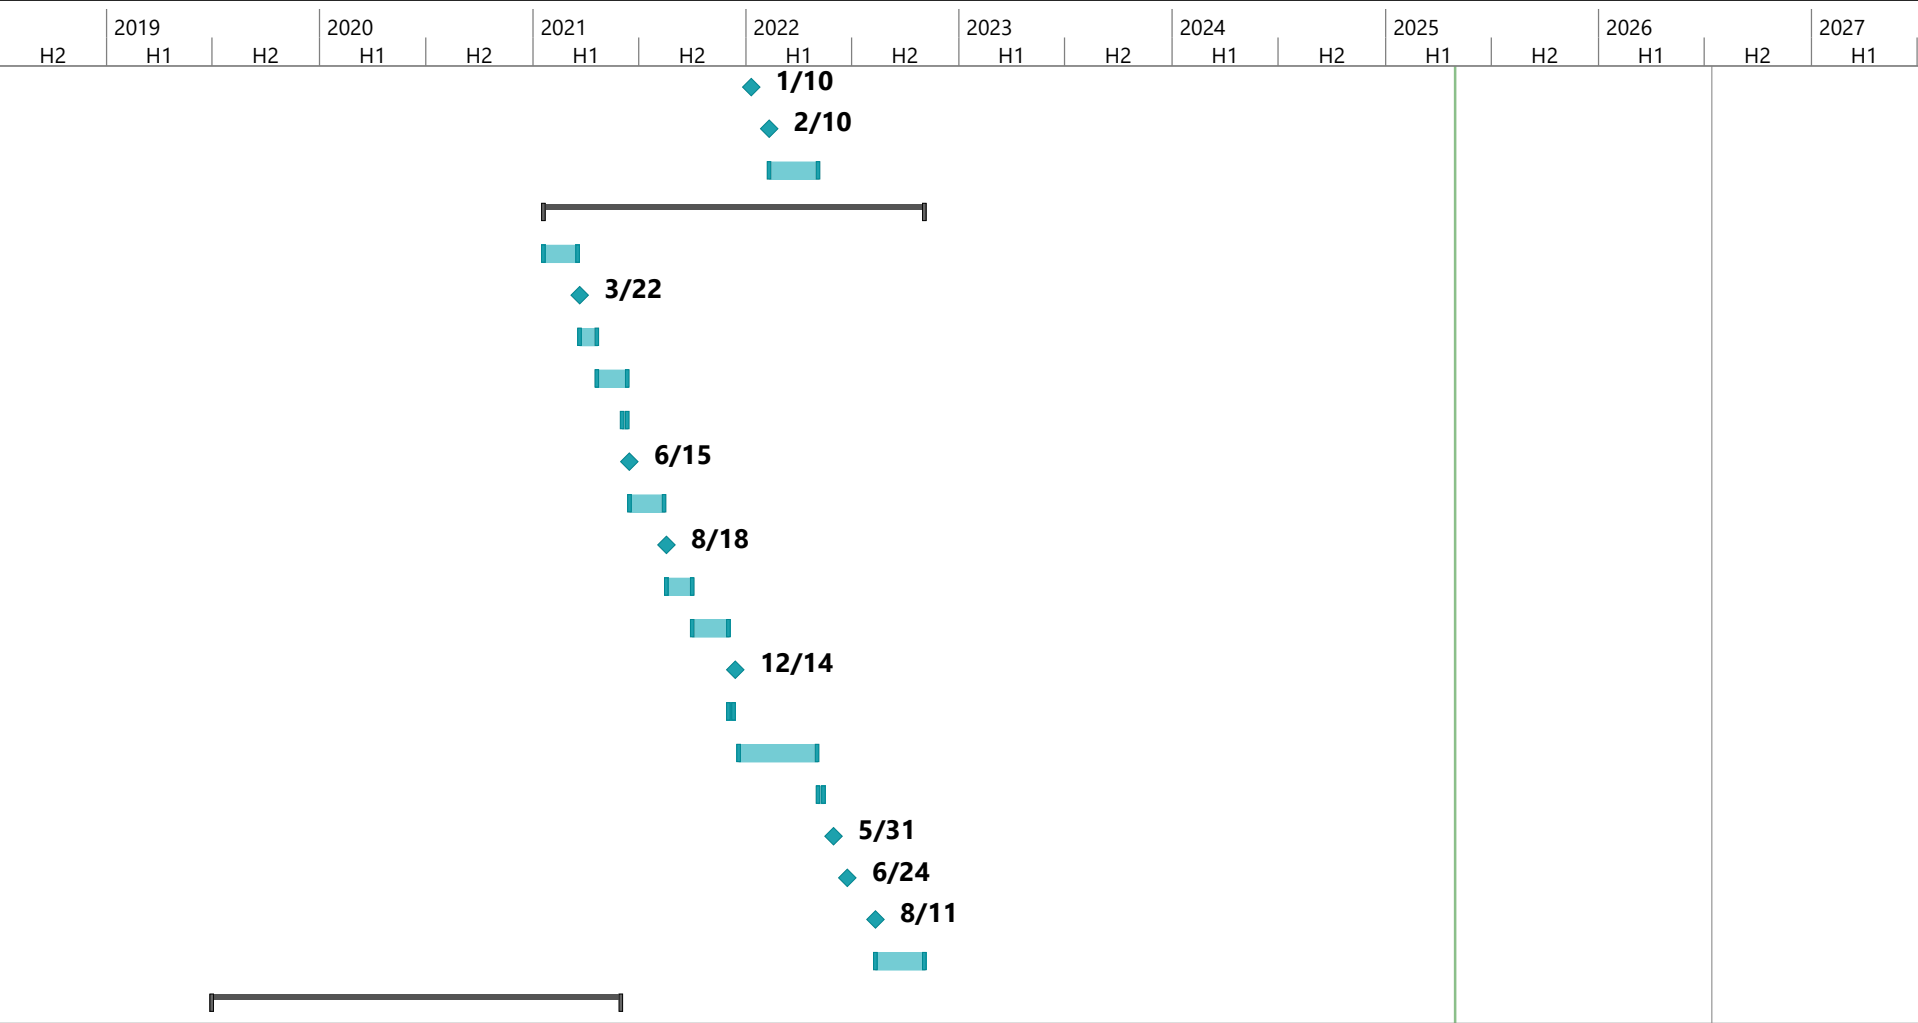
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |



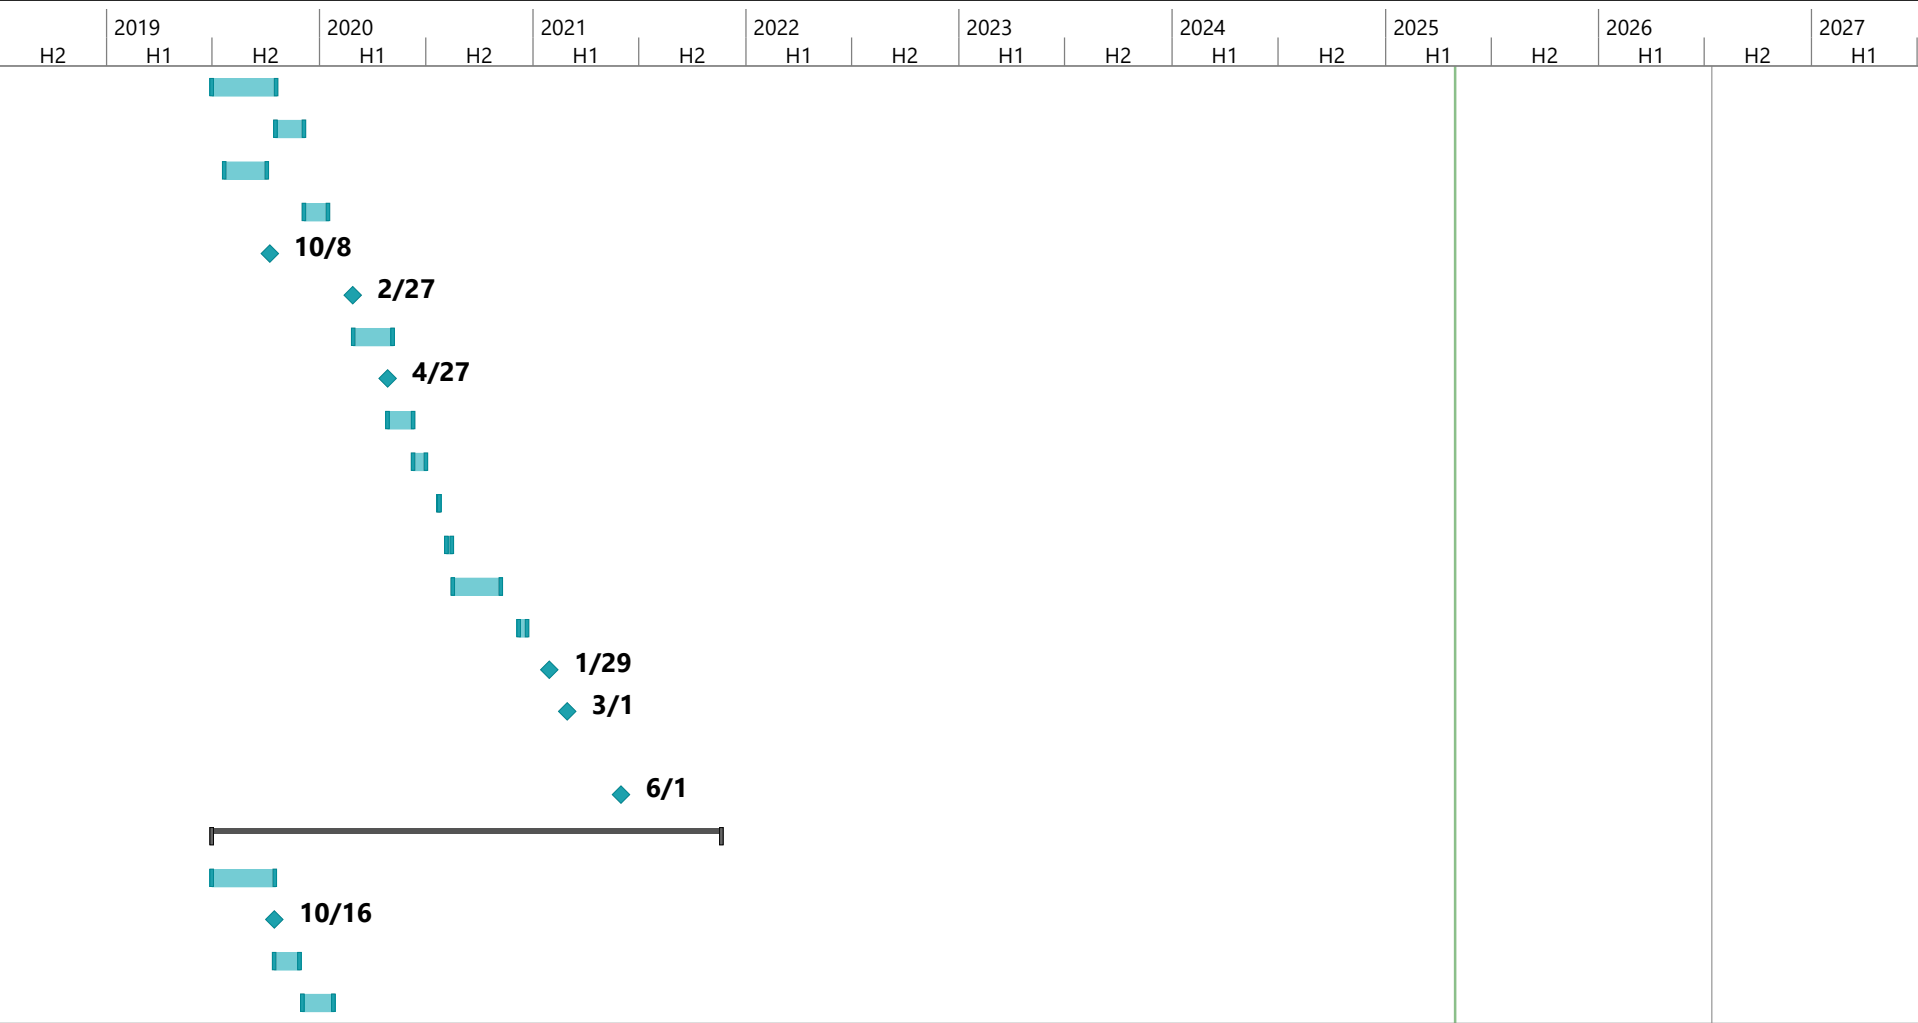
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |



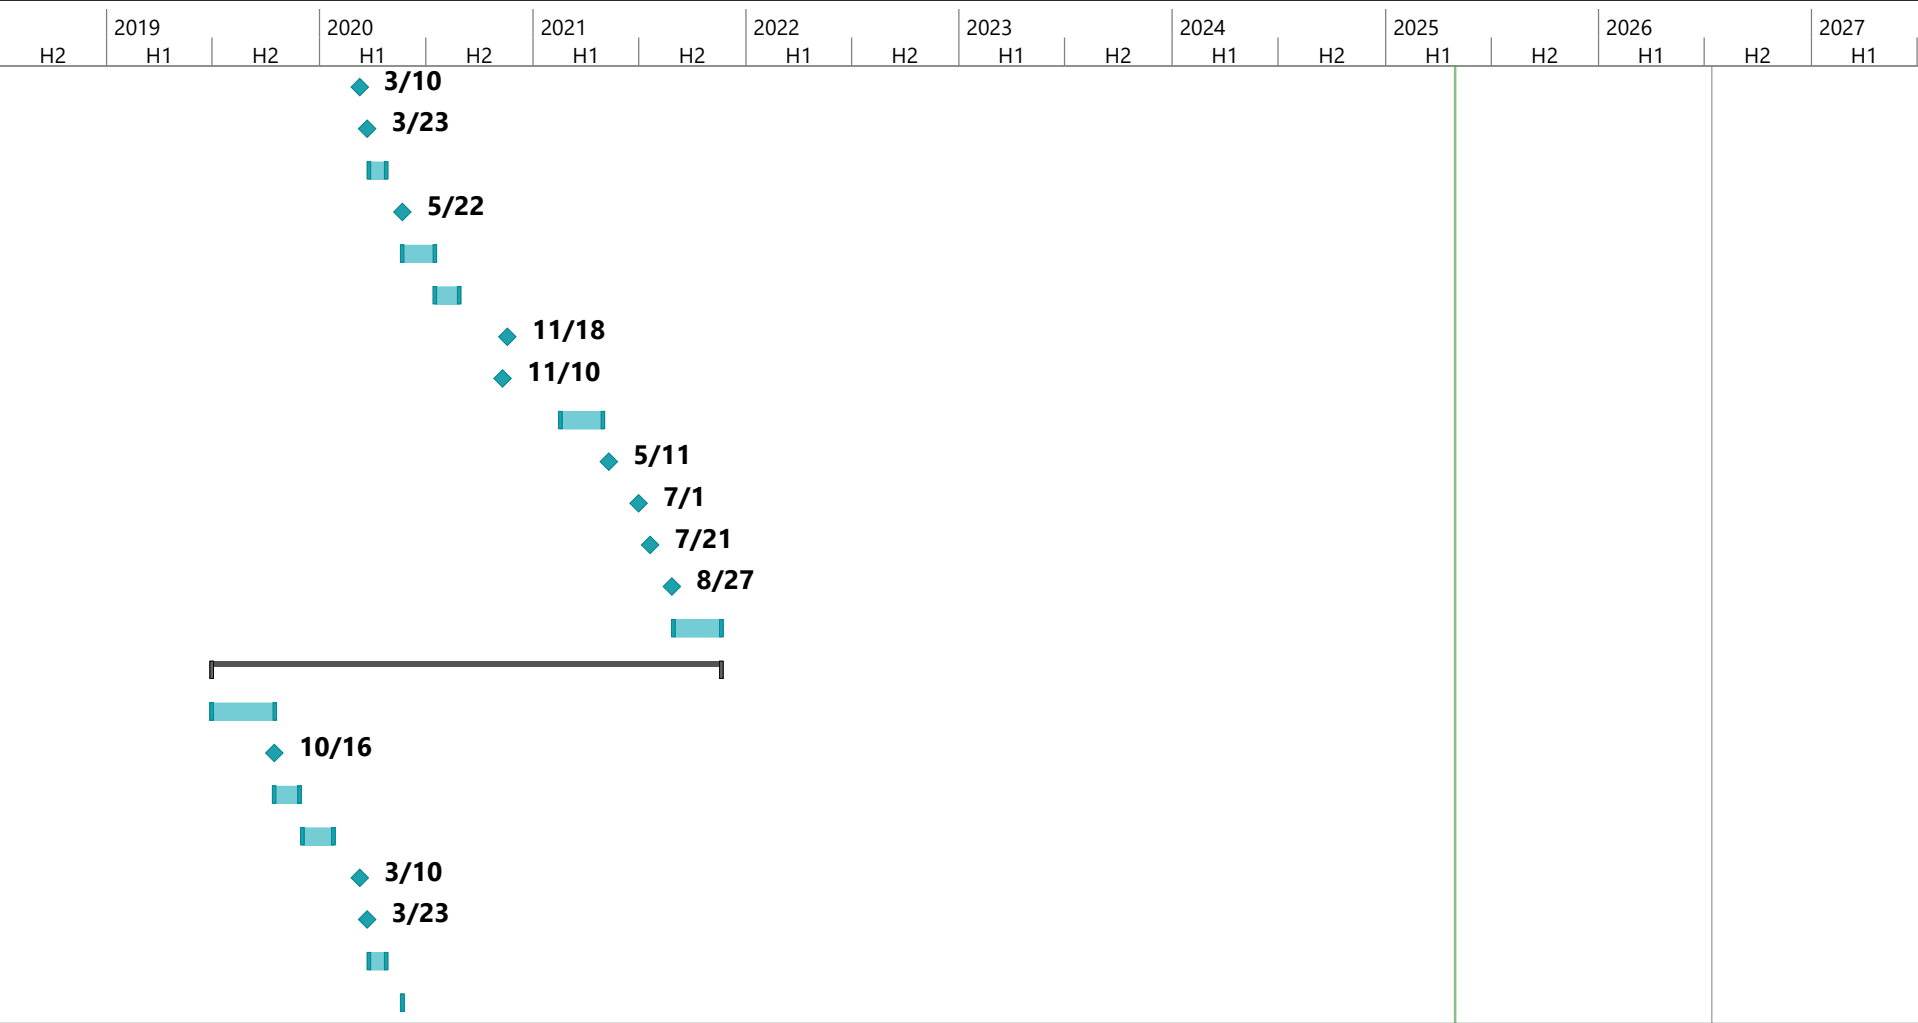
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |



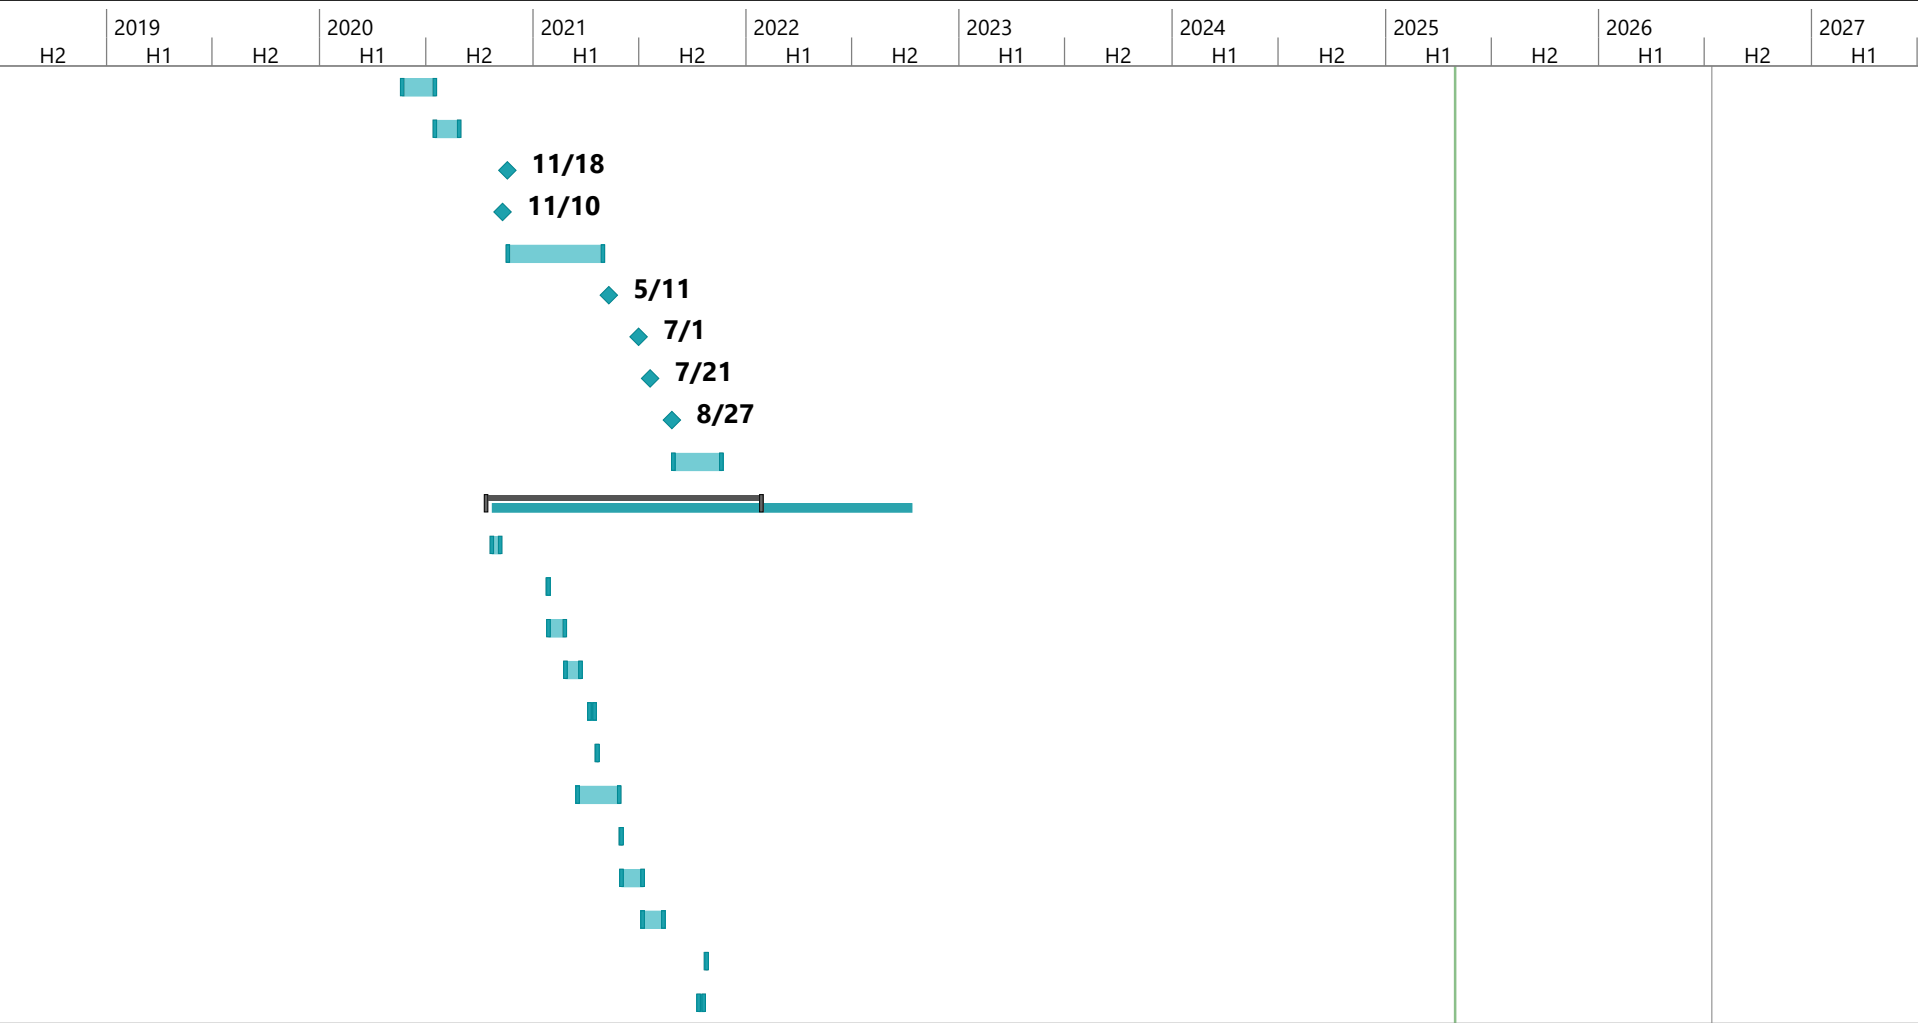
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |



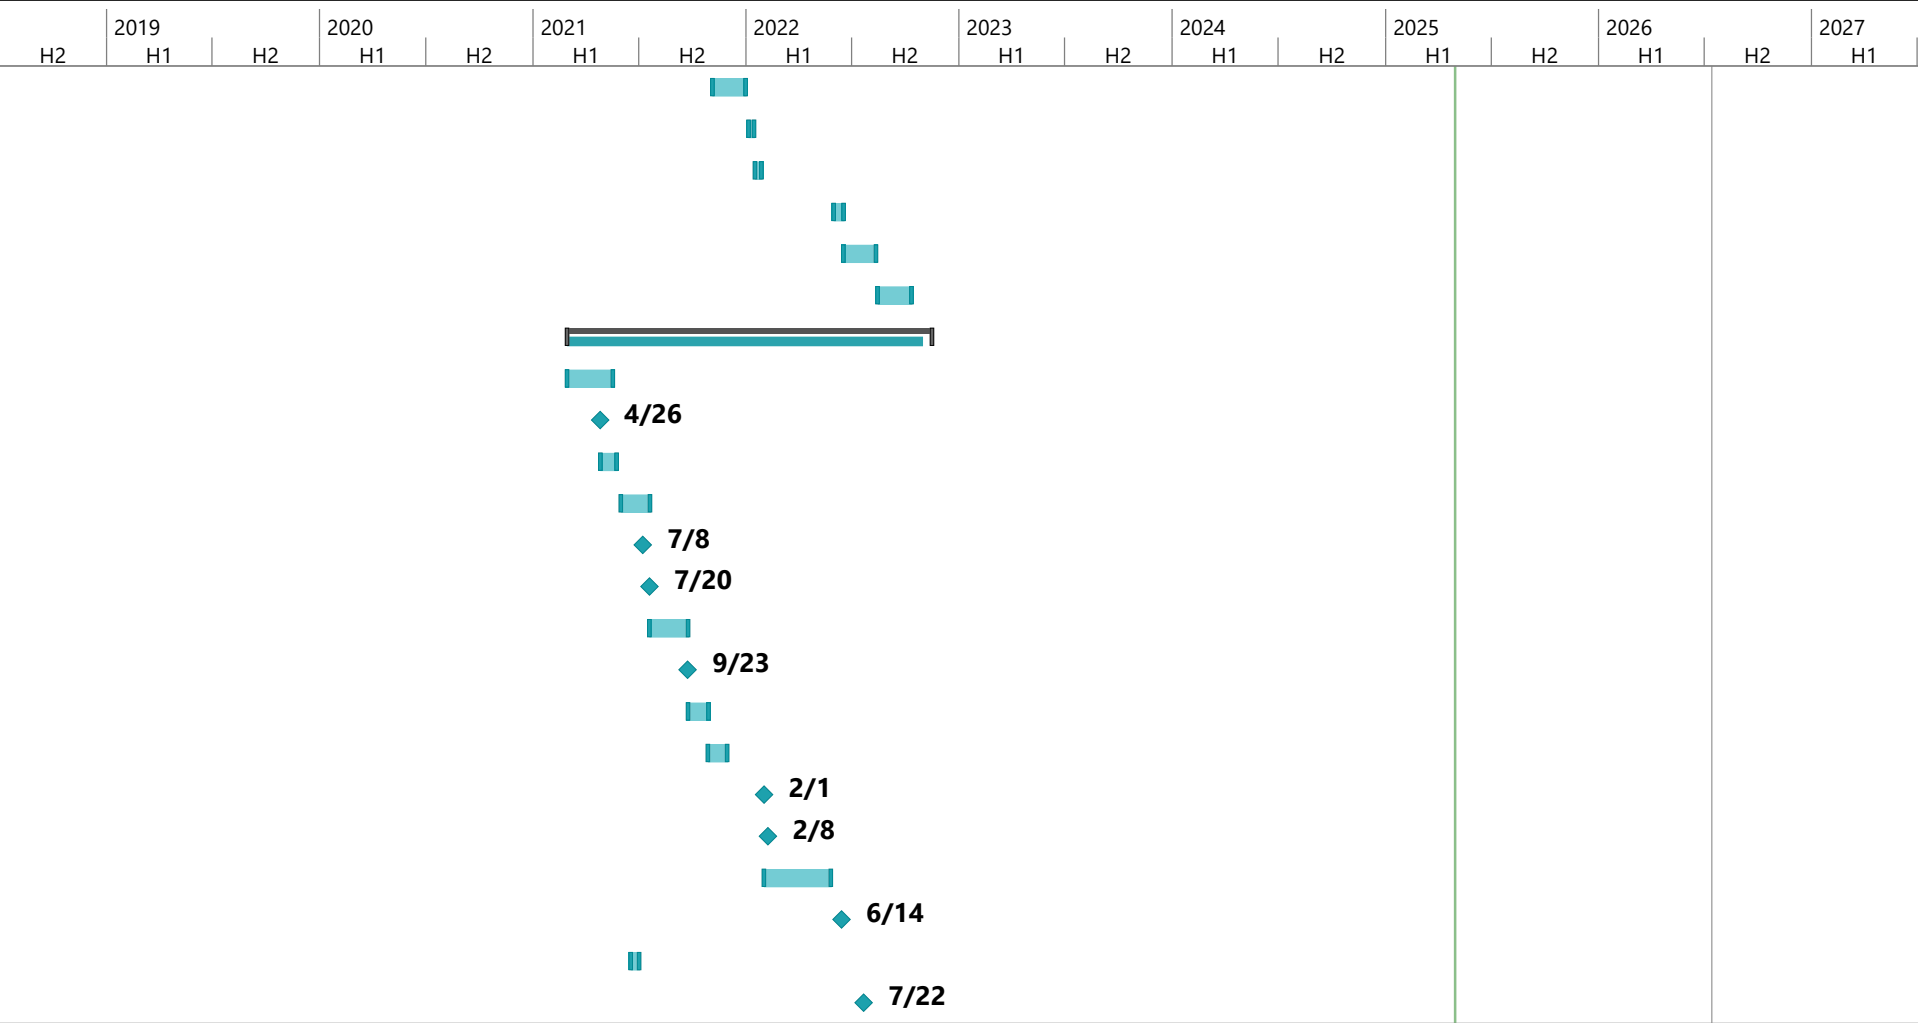
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |



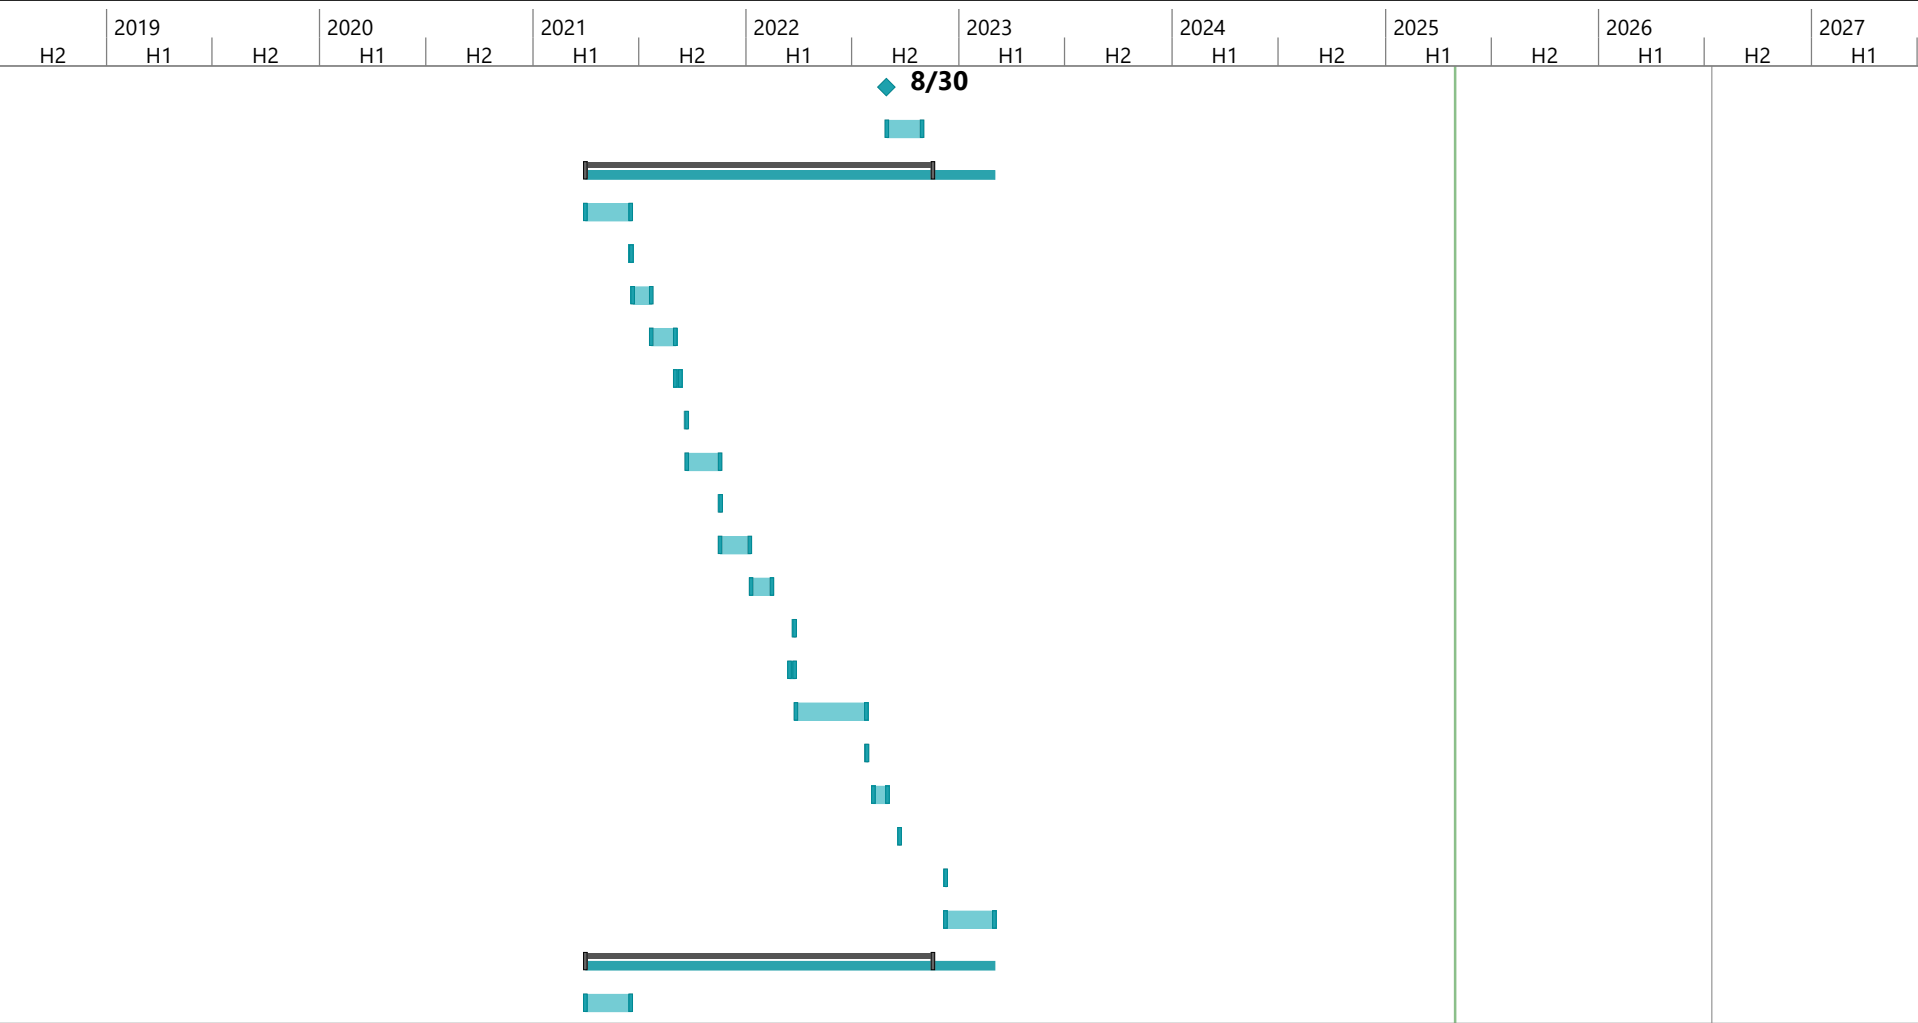
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |




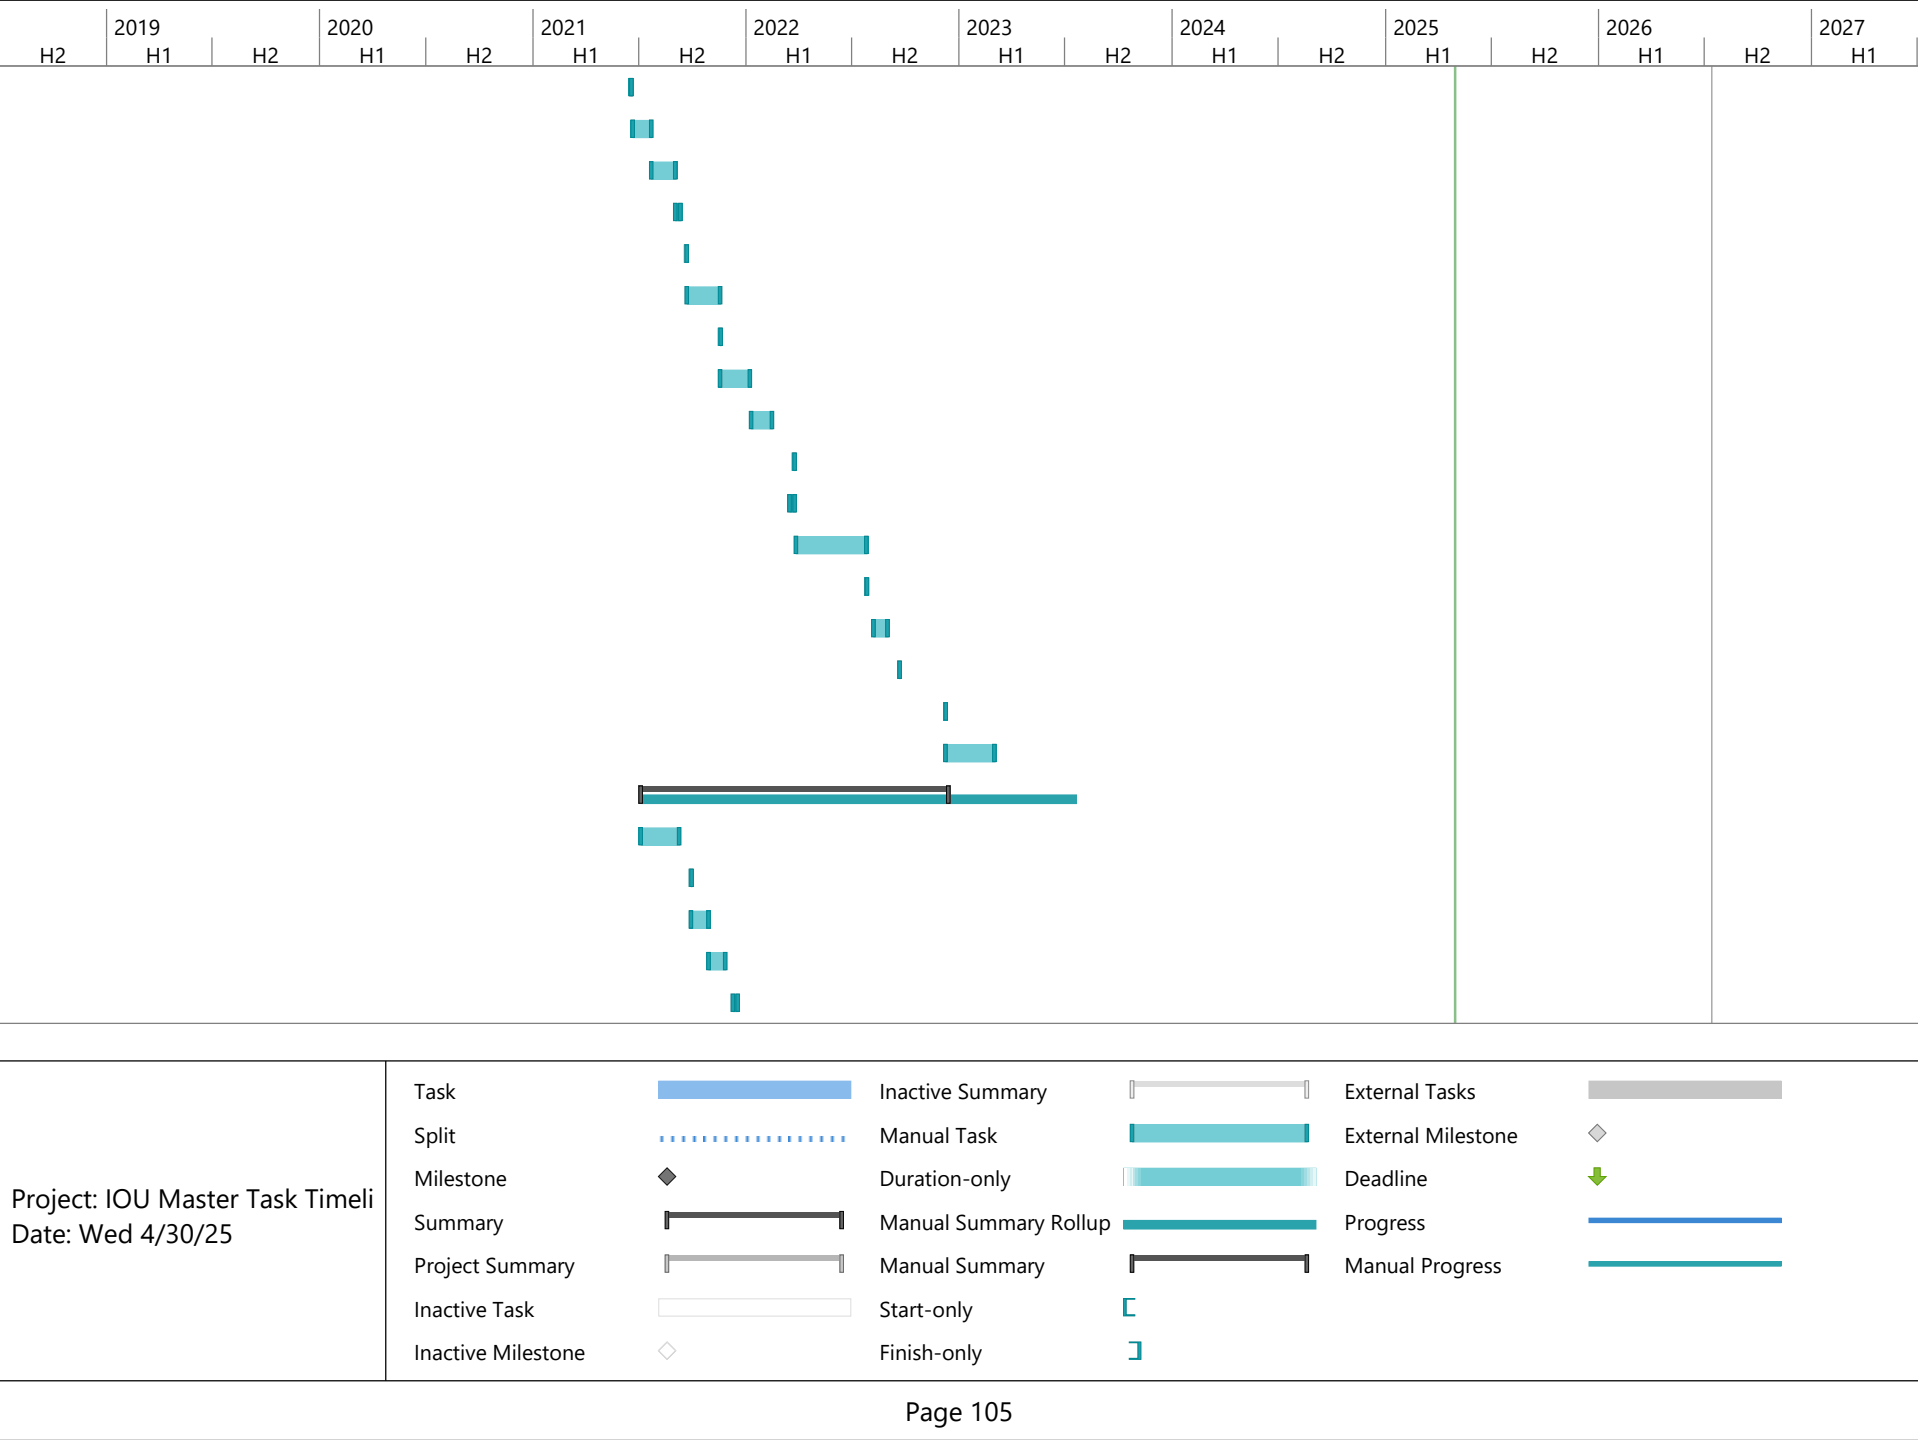
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |

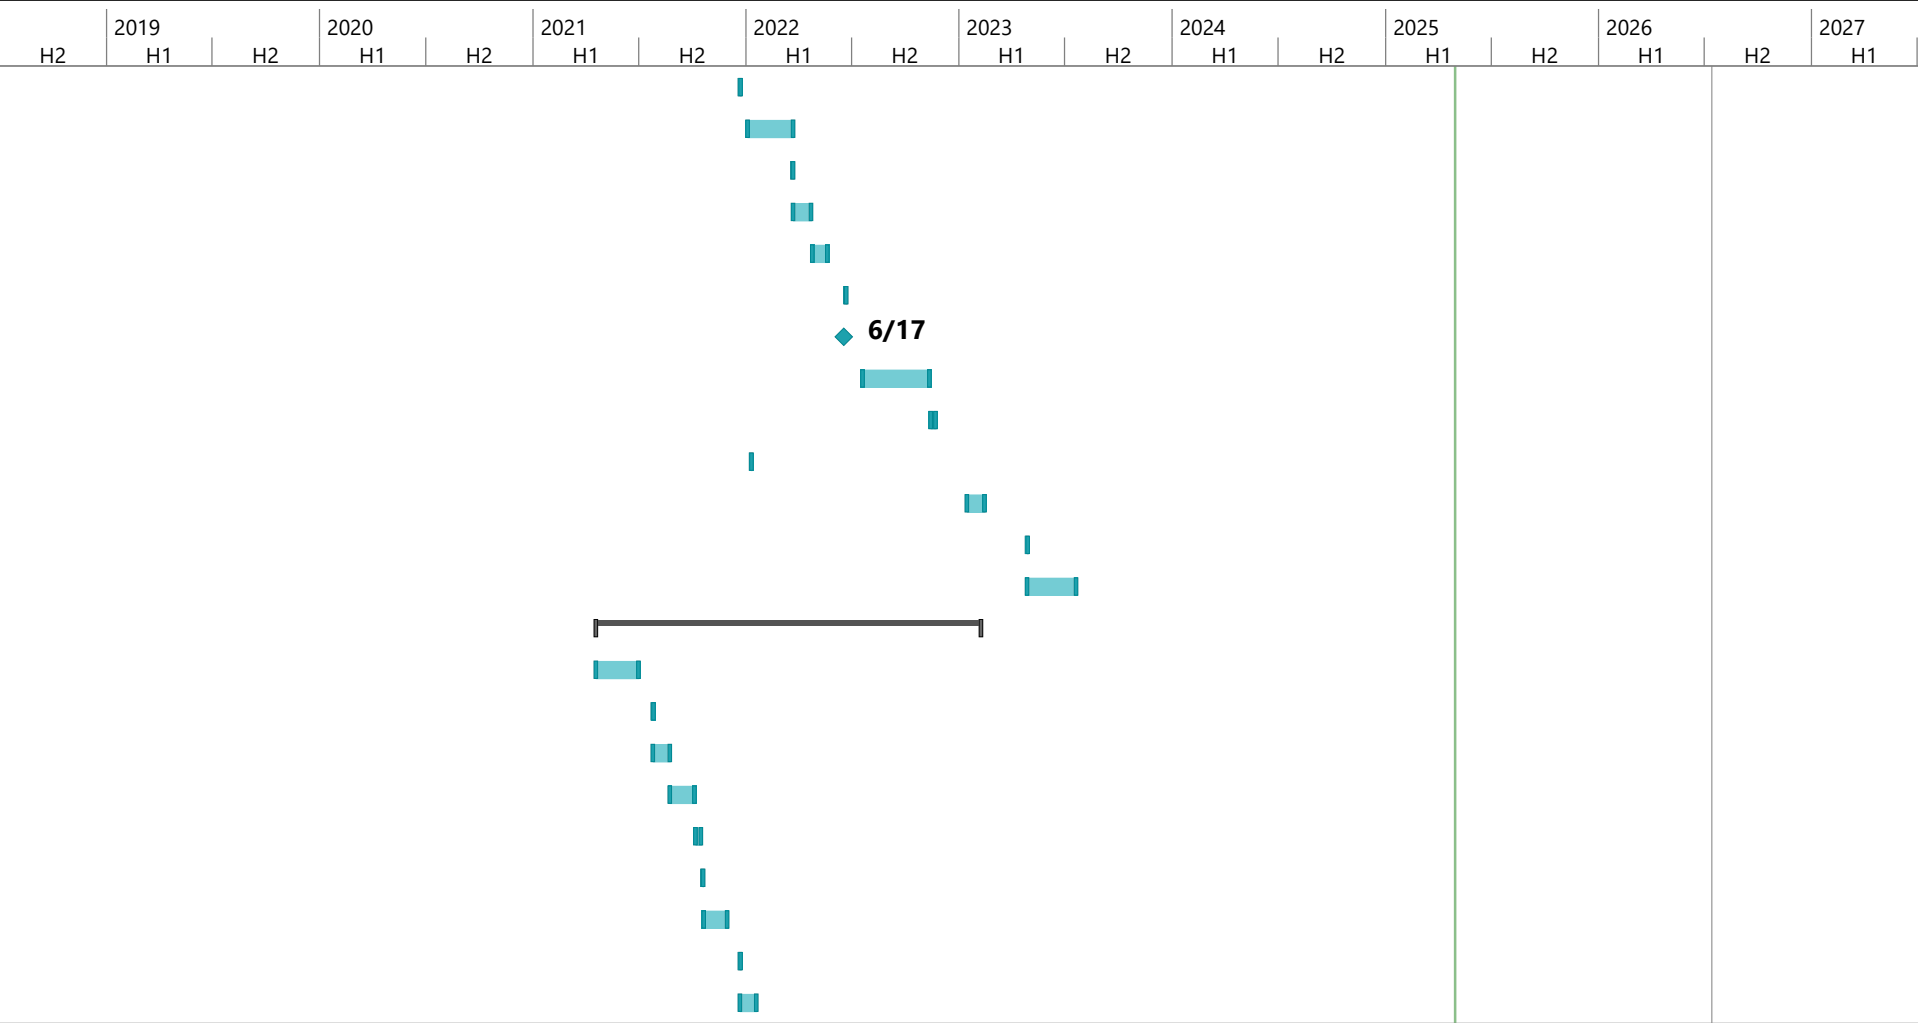


|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |



|                                                      |                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|------------------------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |                                                                                       |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |





Project: IOU Master Task Timeli  
Date: Wed 4/30/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

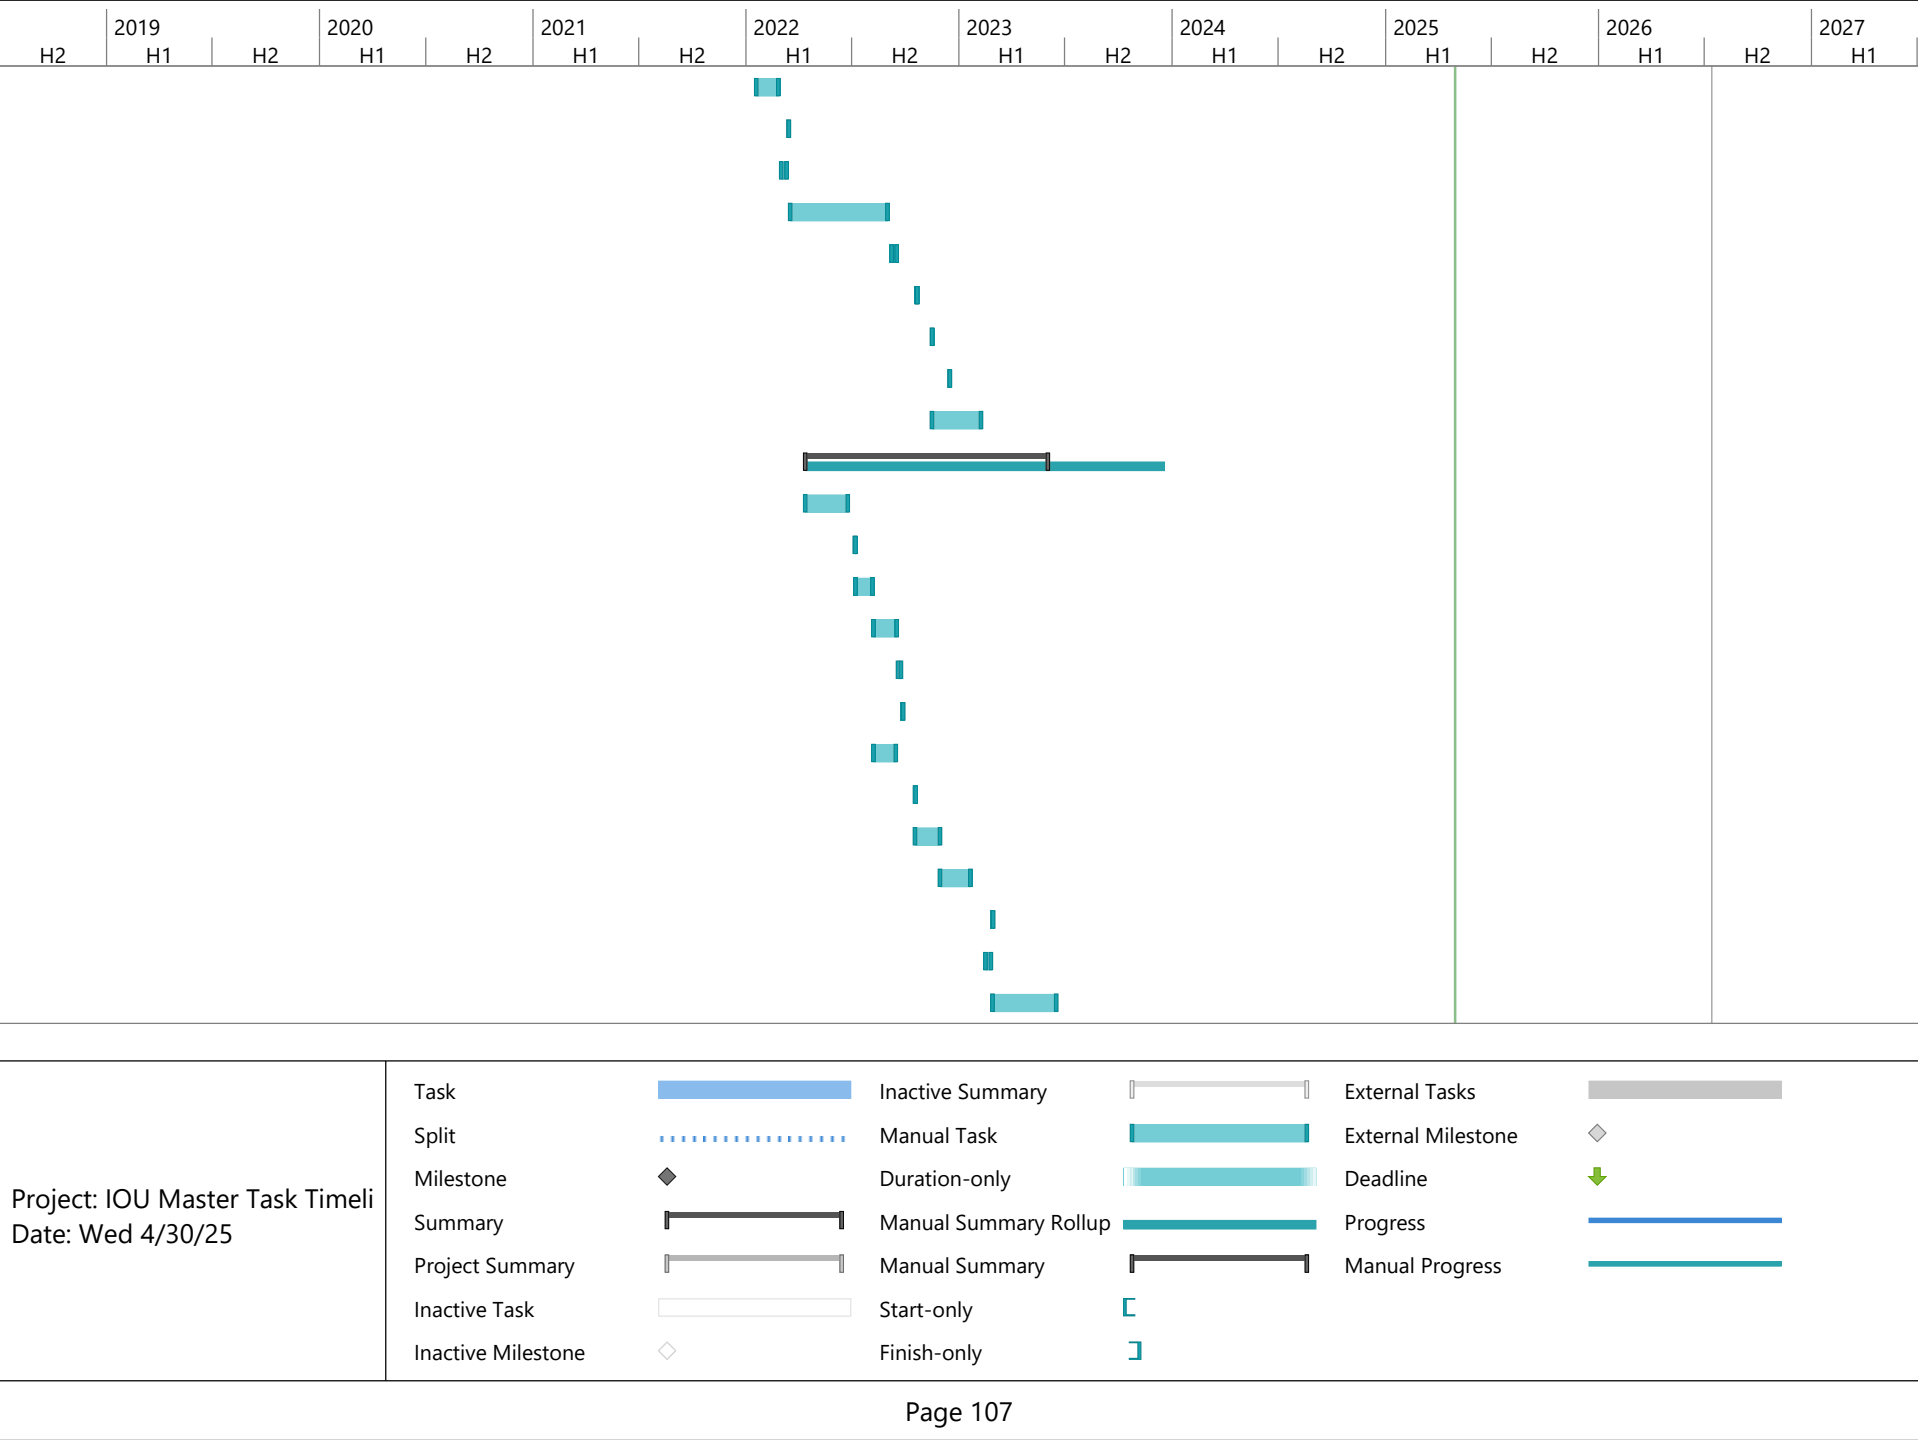
External Milestone

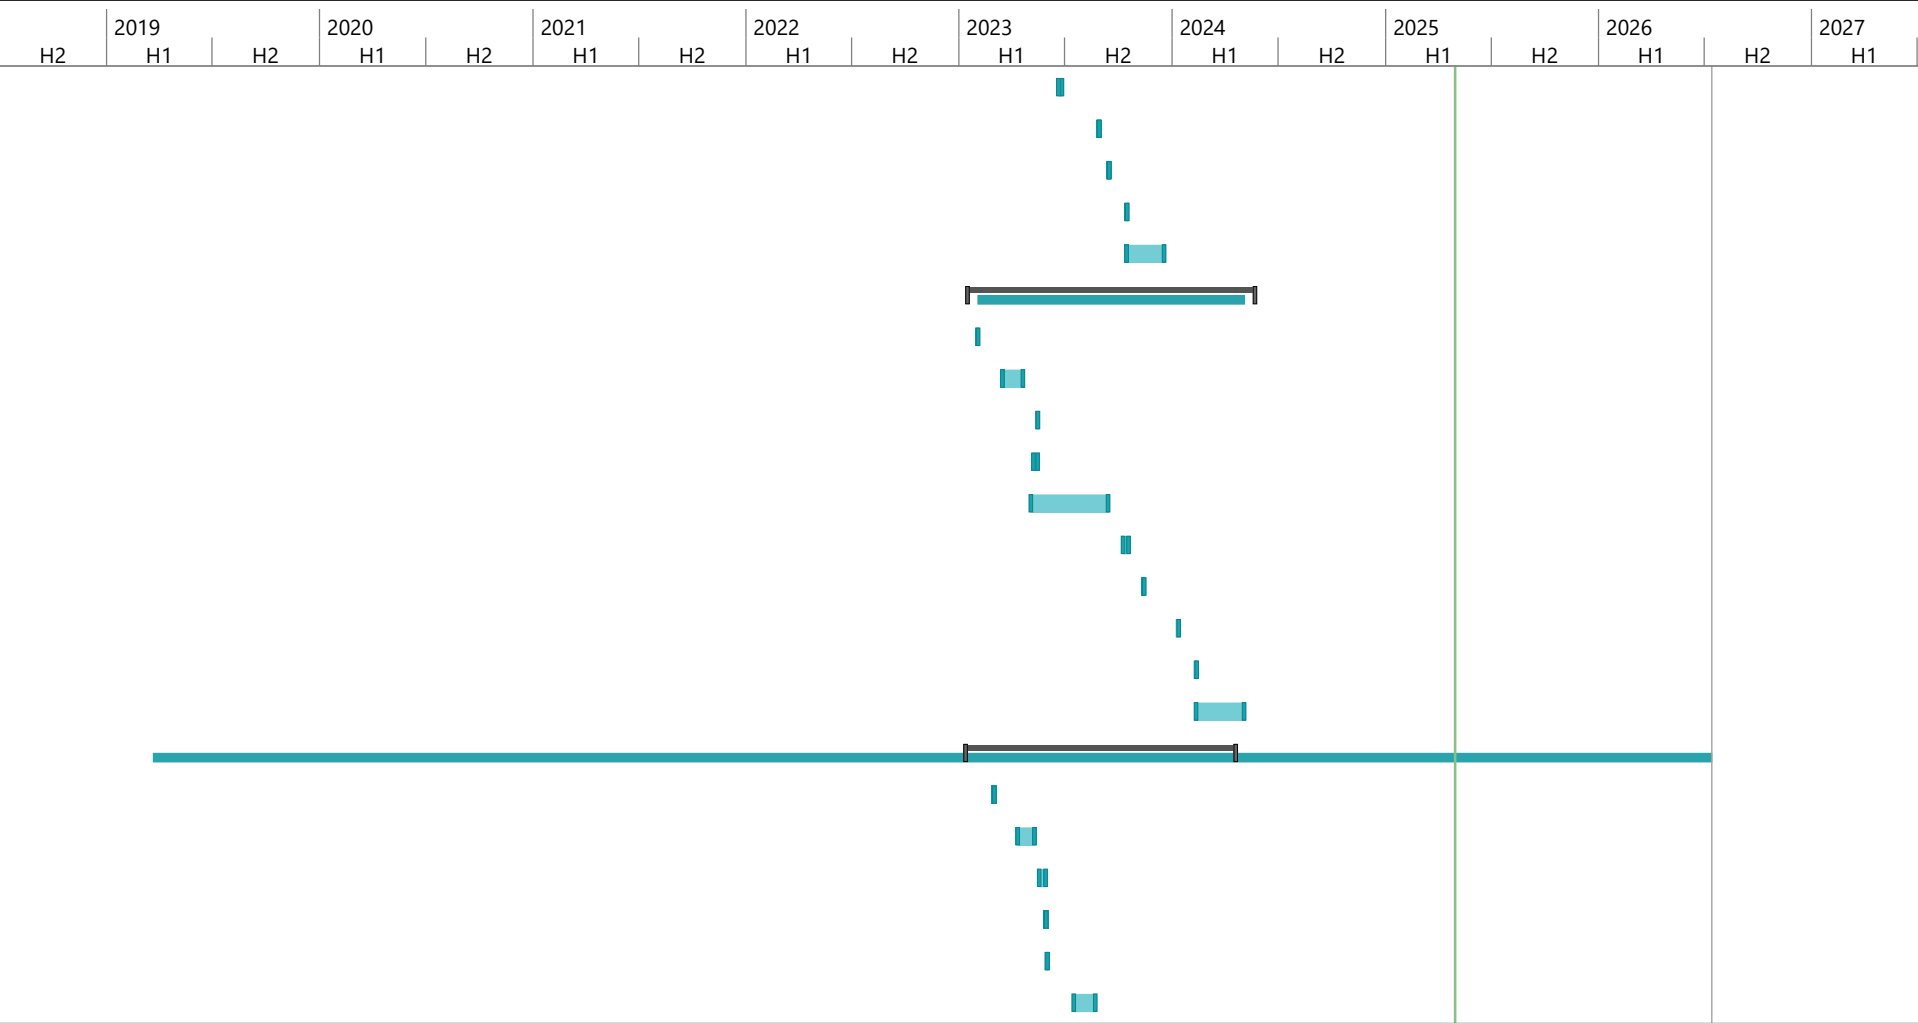
Deadline

Progress

Manual Progress

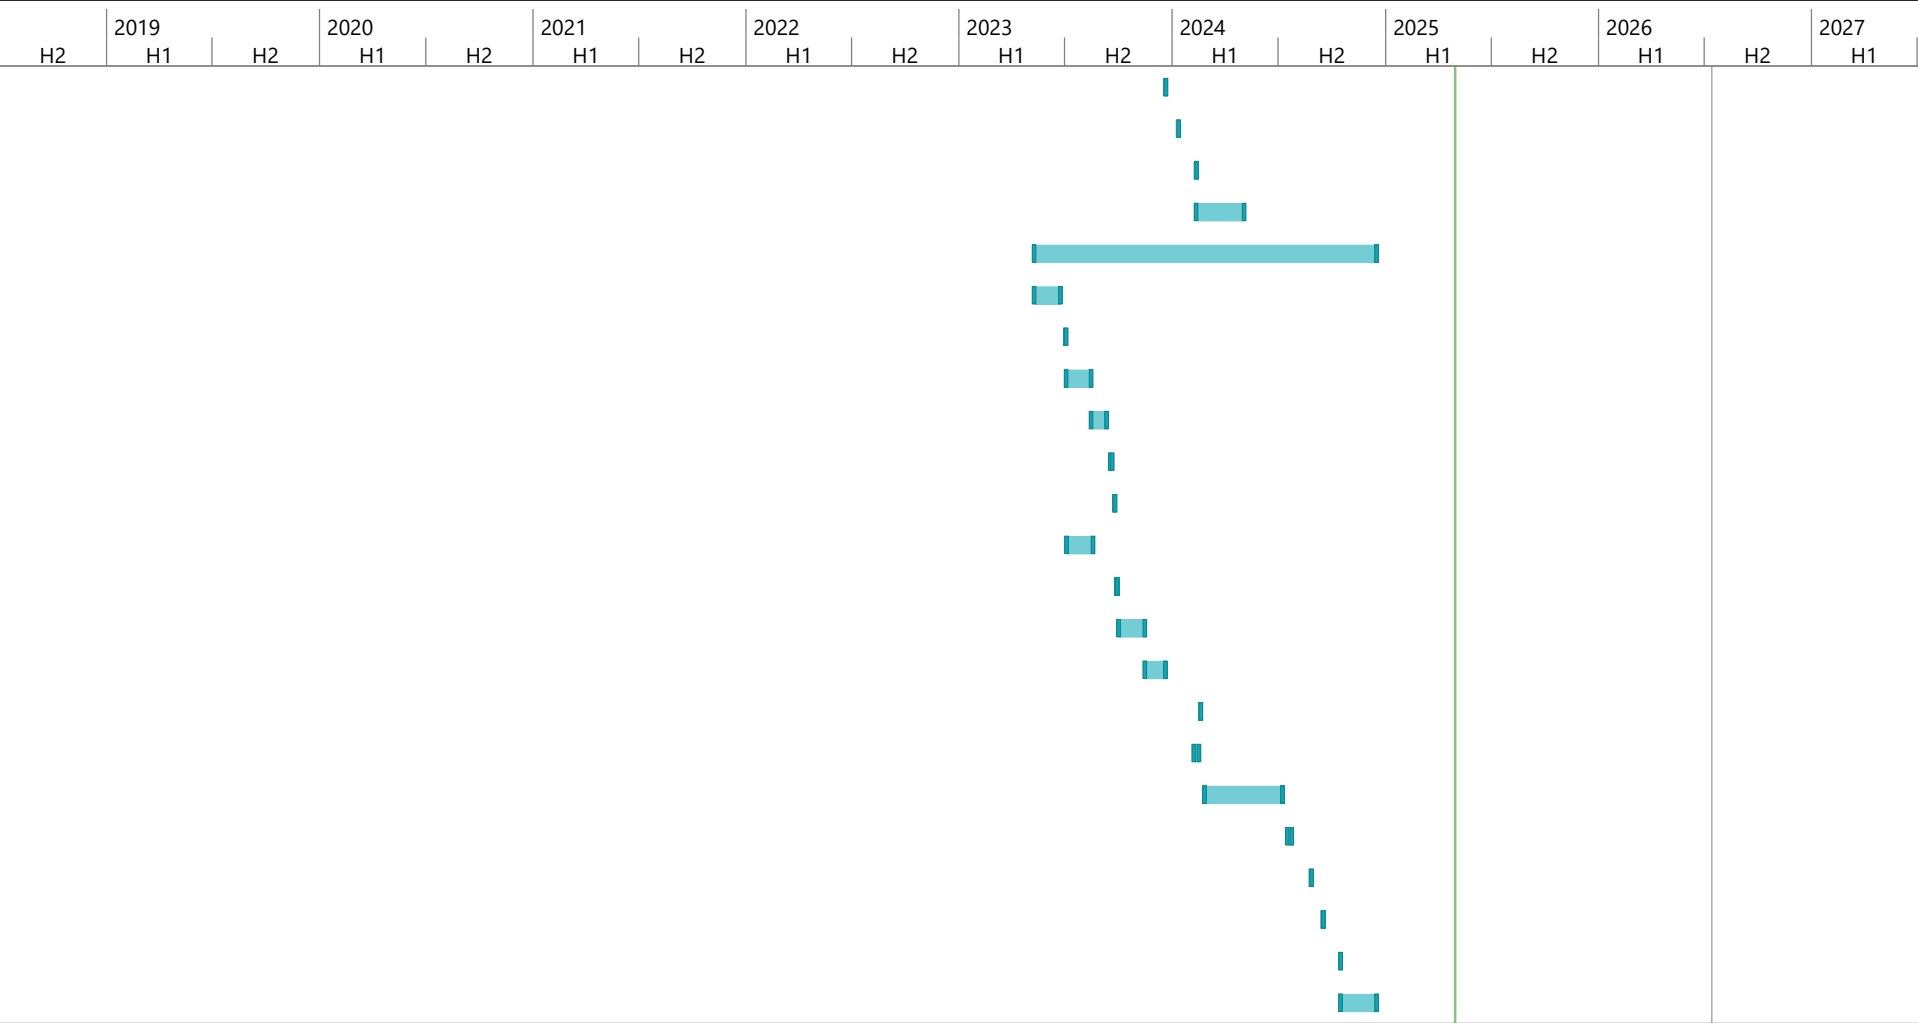
Page 106





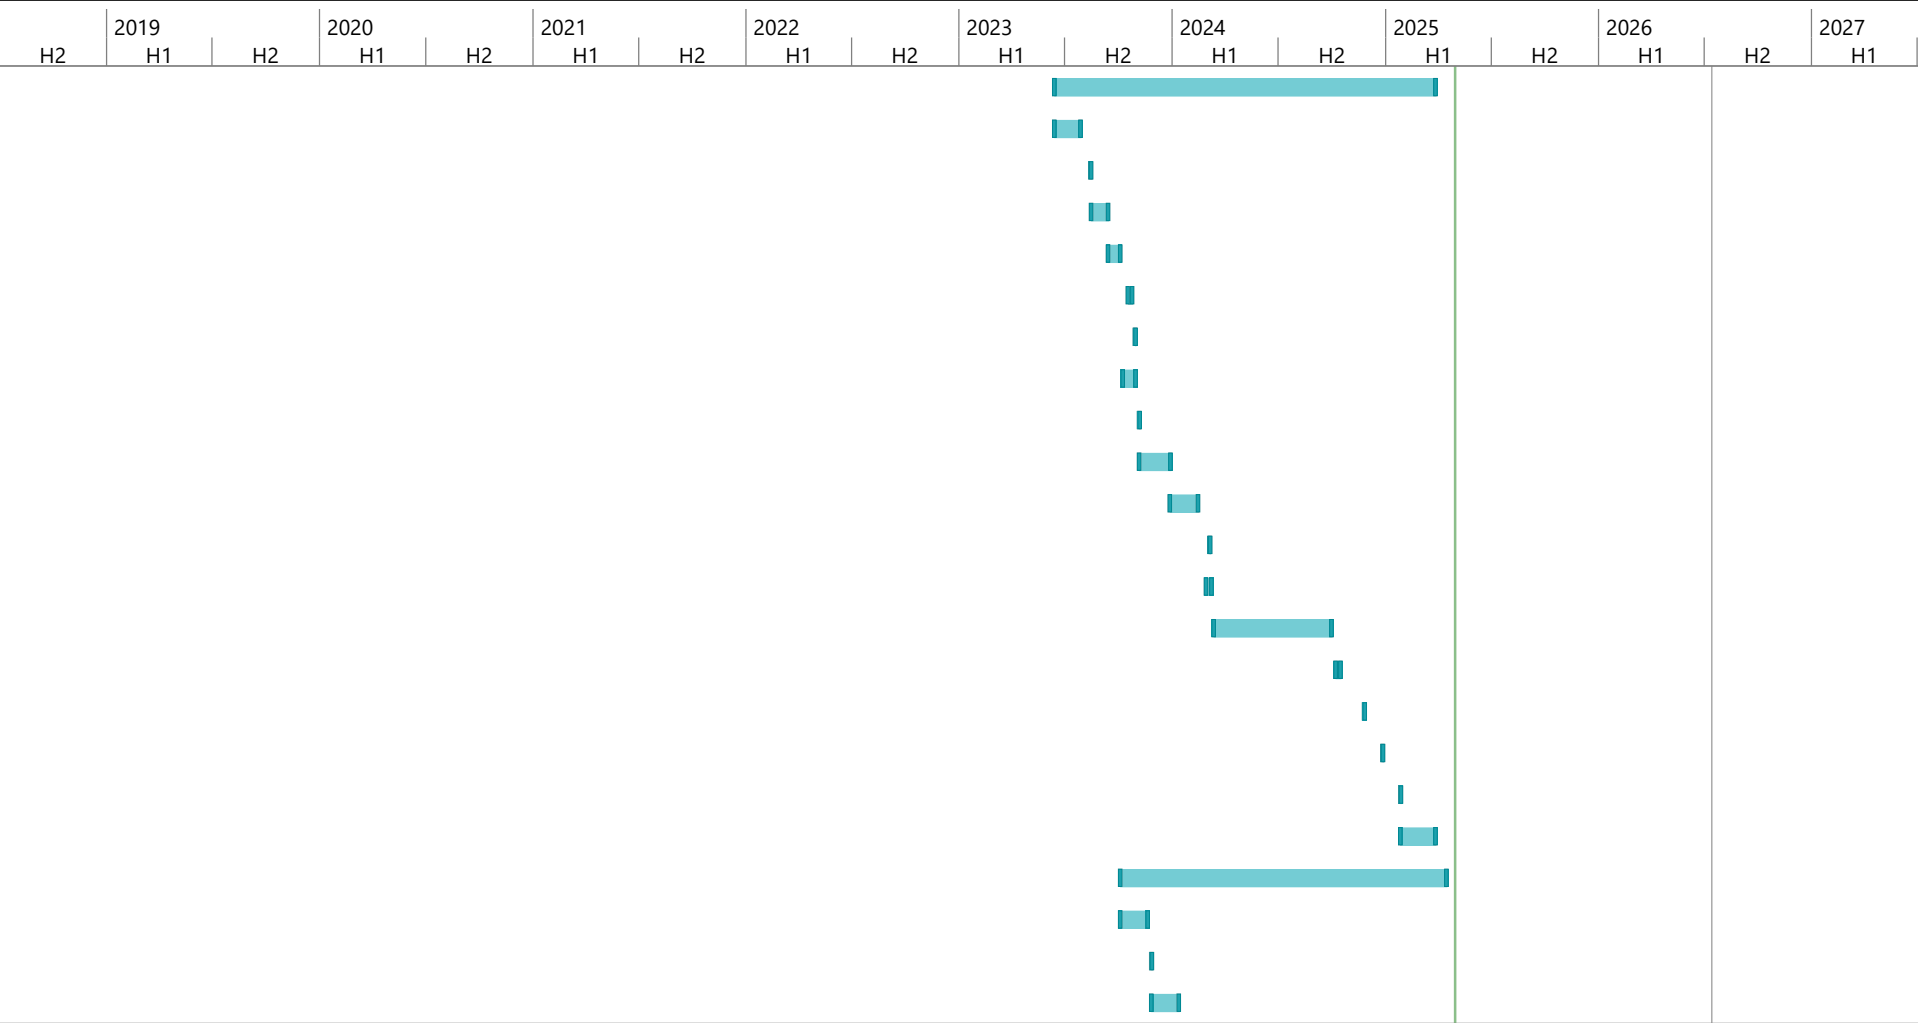
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |



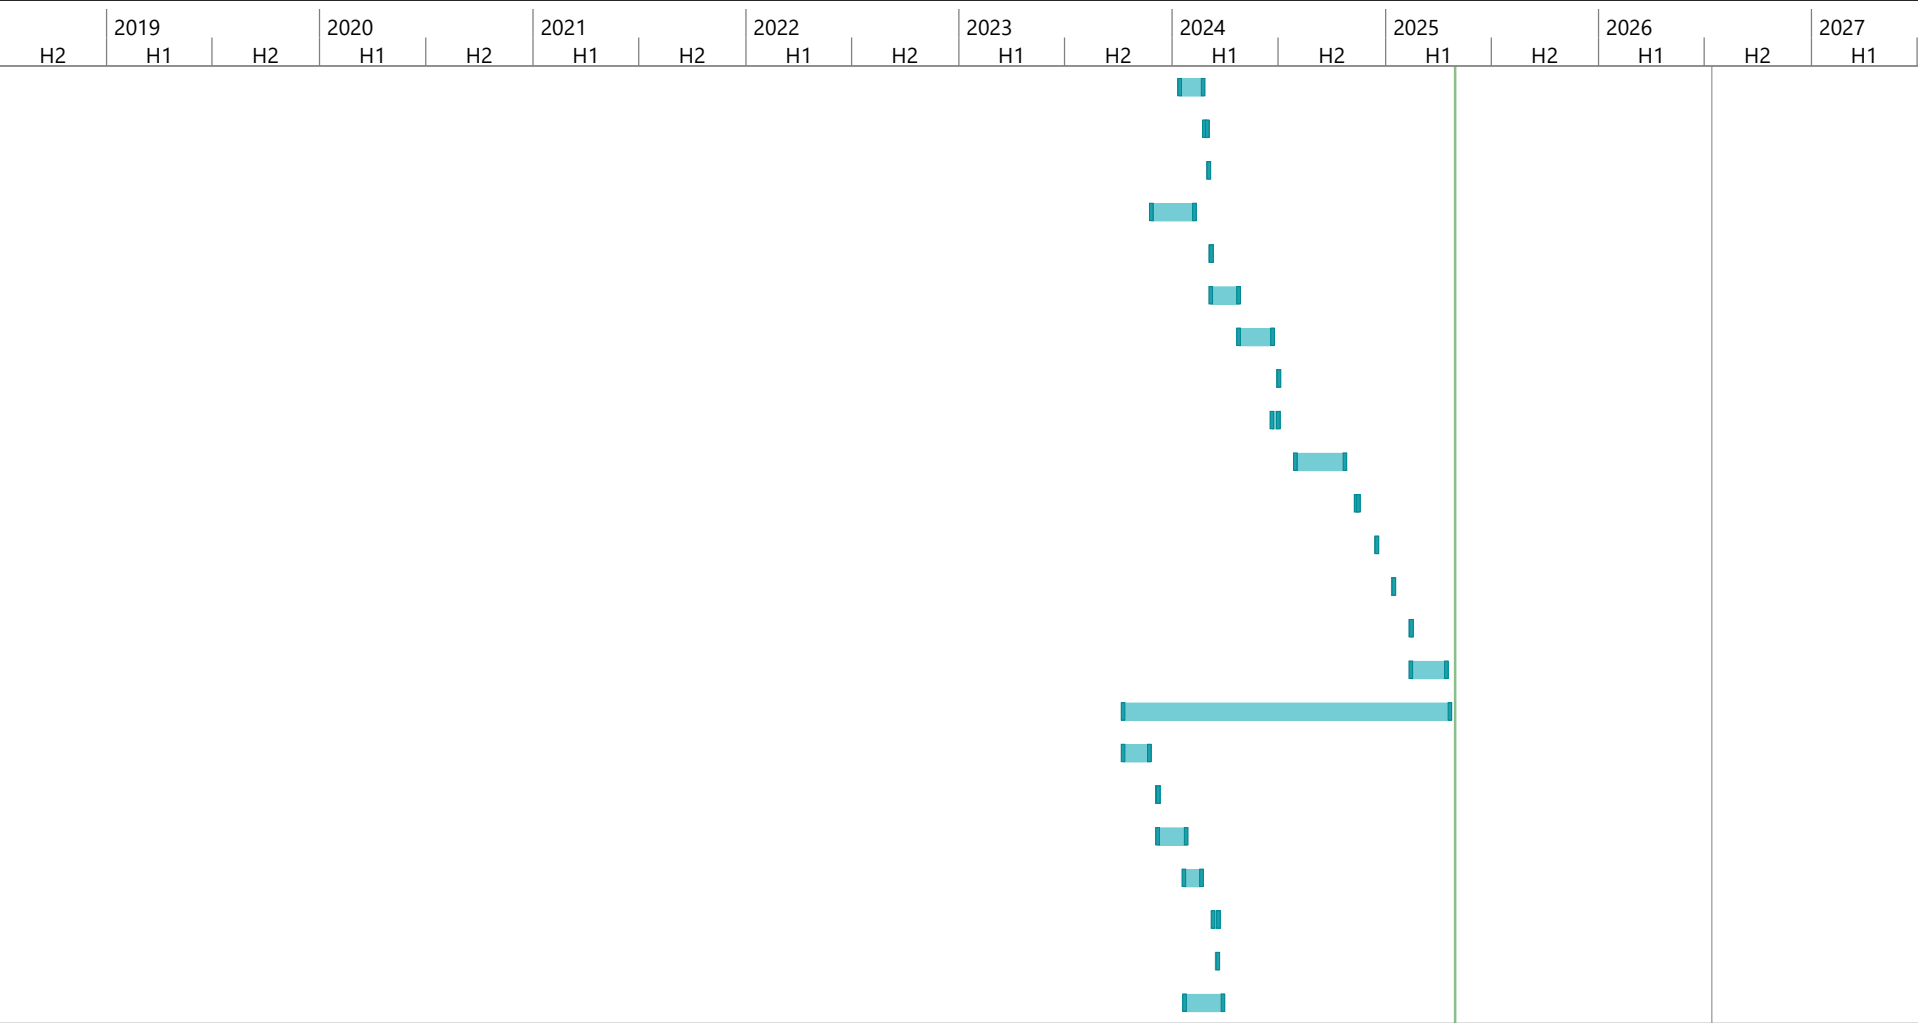


Project: IOU Master Task Timeli  
Date: Wed 4/30/25

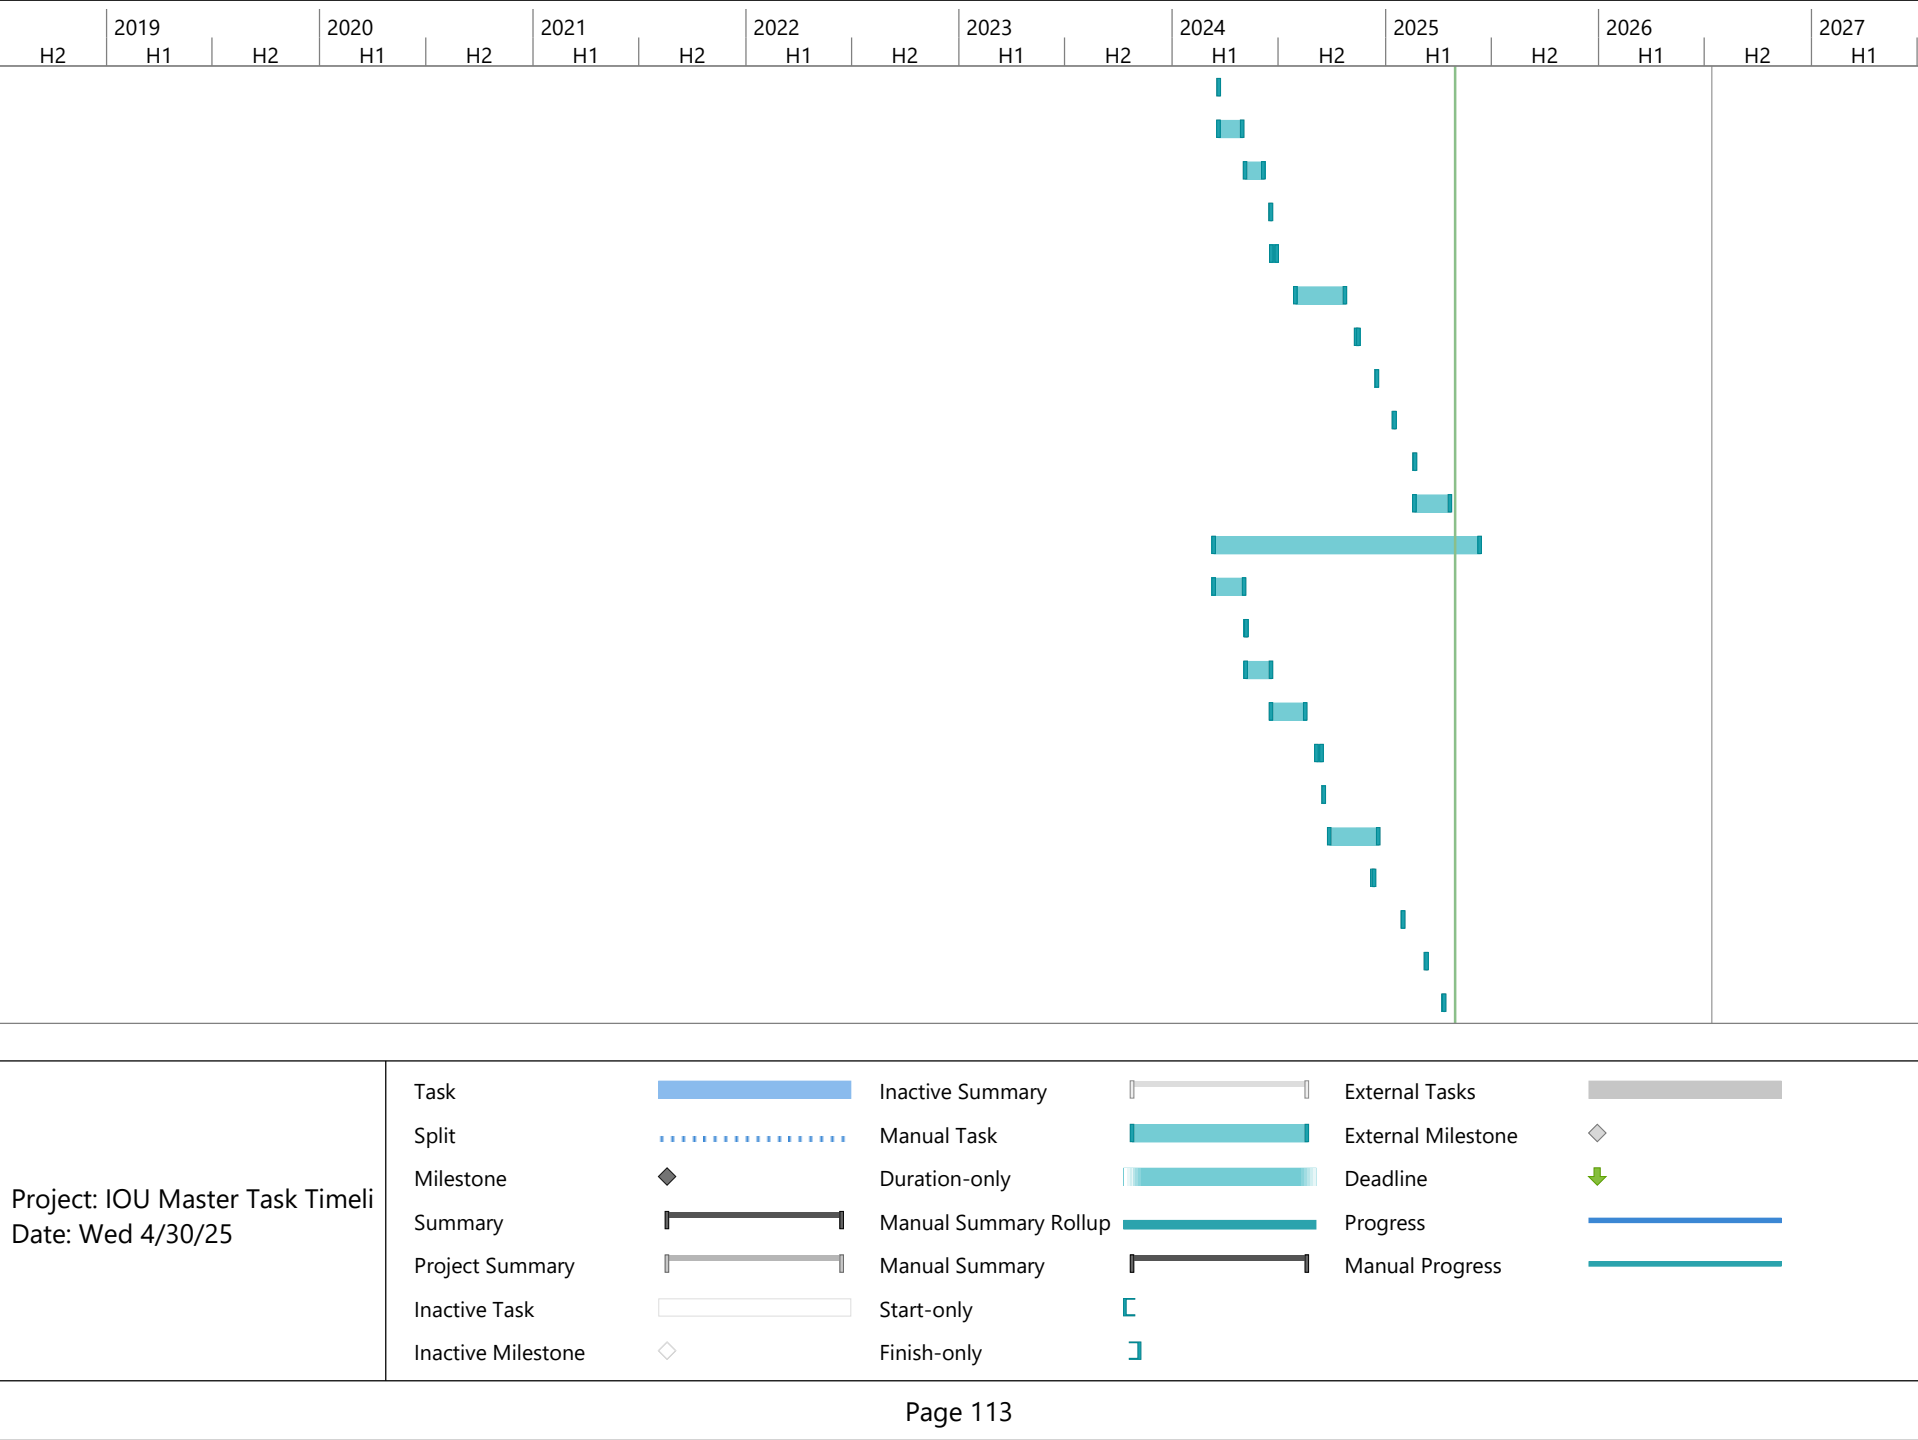
|                    |  |                       |  |                    |  |
|--------------------|--|-----------------------|--|--------------------|--|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |  |
| Inactive Milestone |  | Finish-only           |  |                    |  |



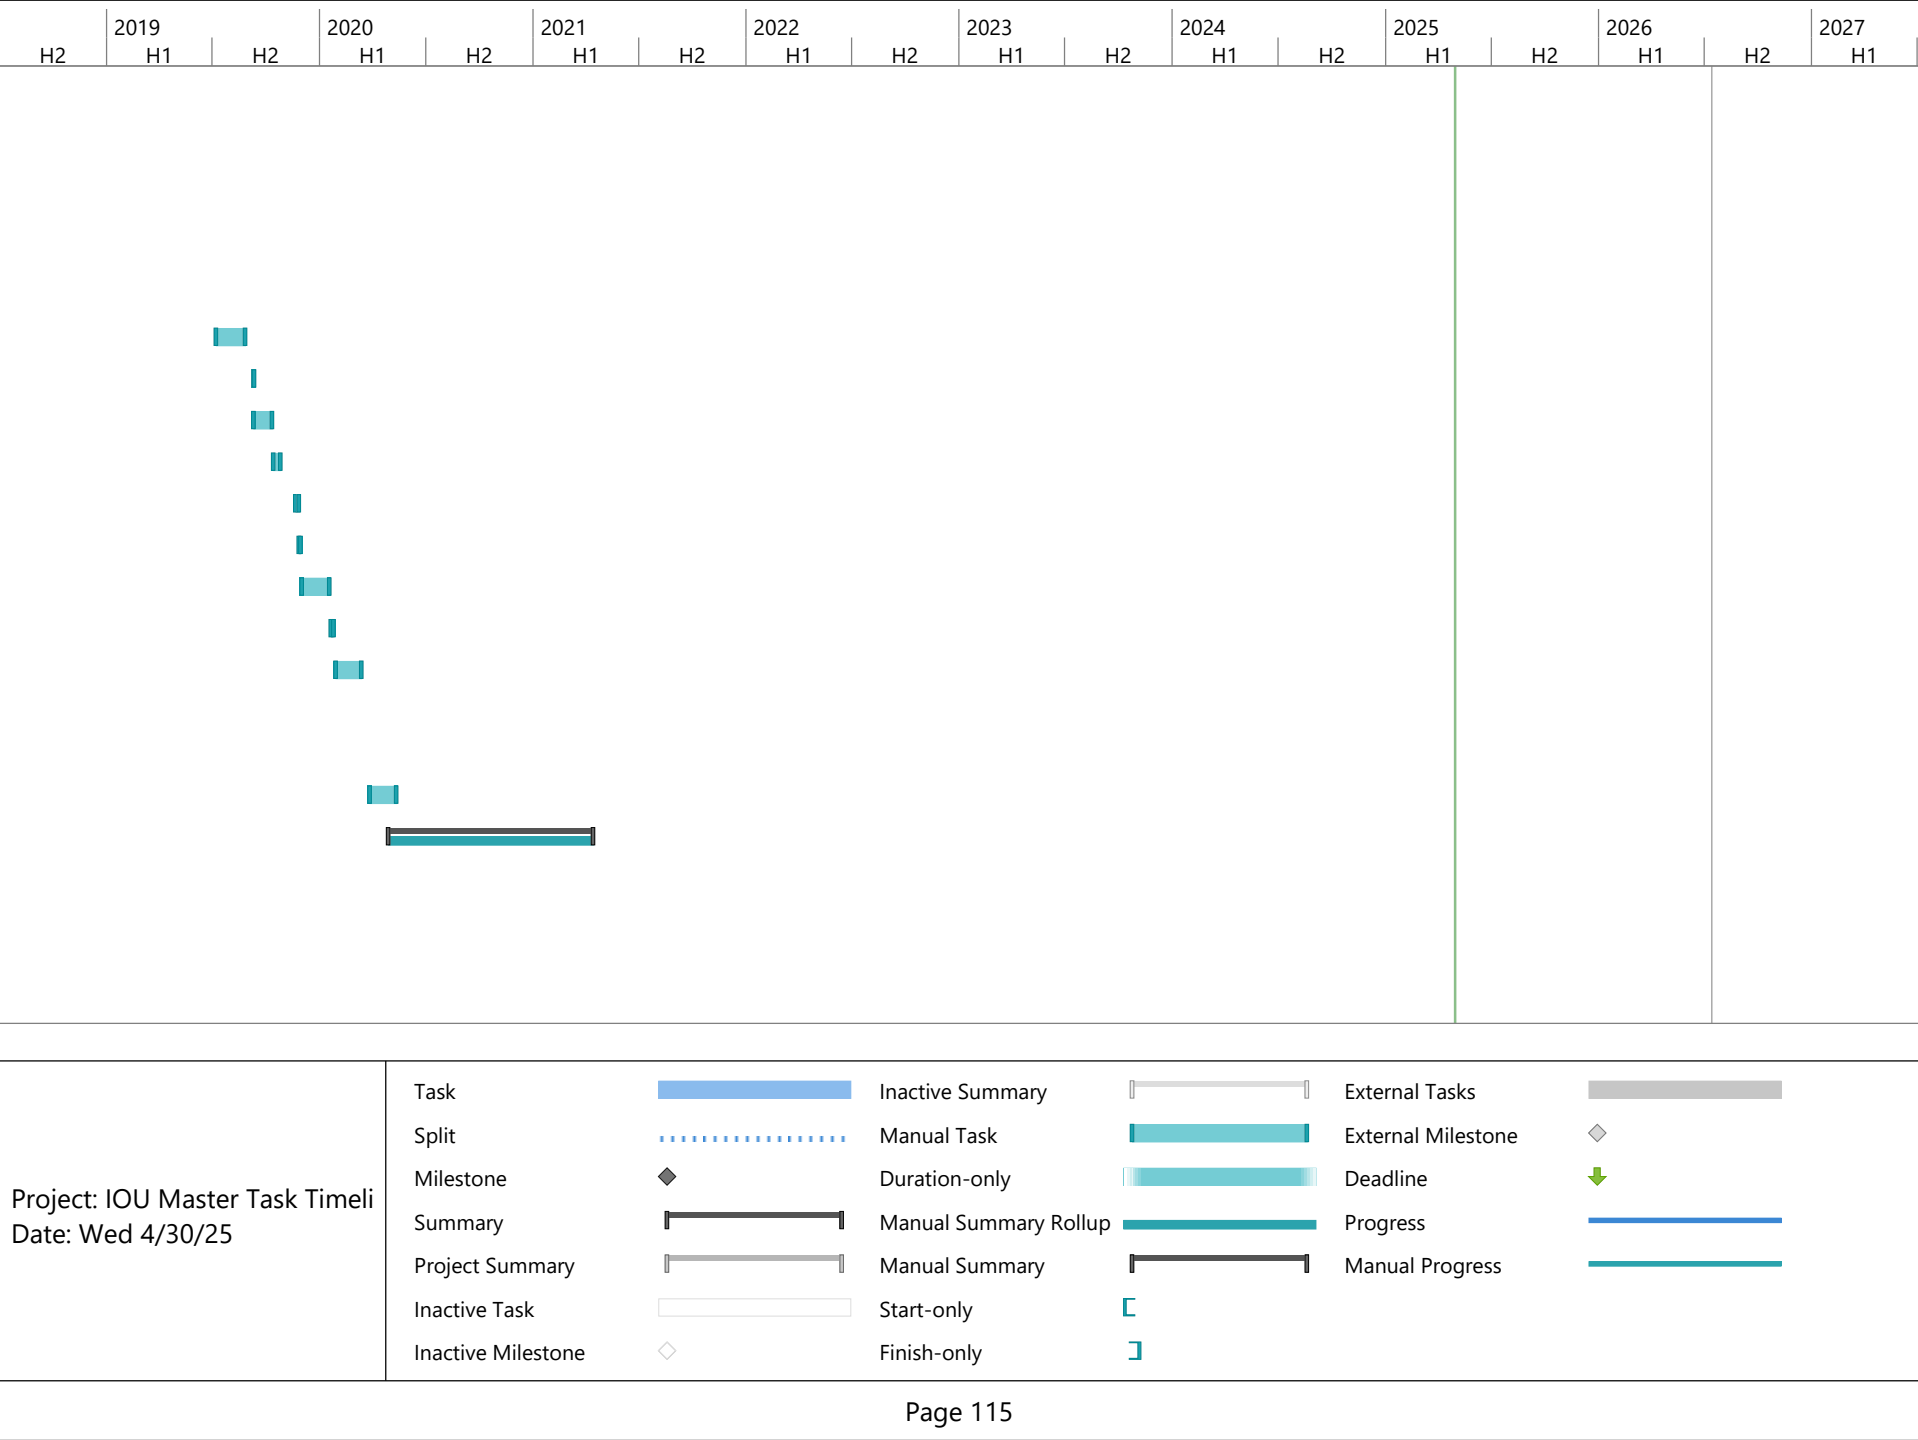
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |



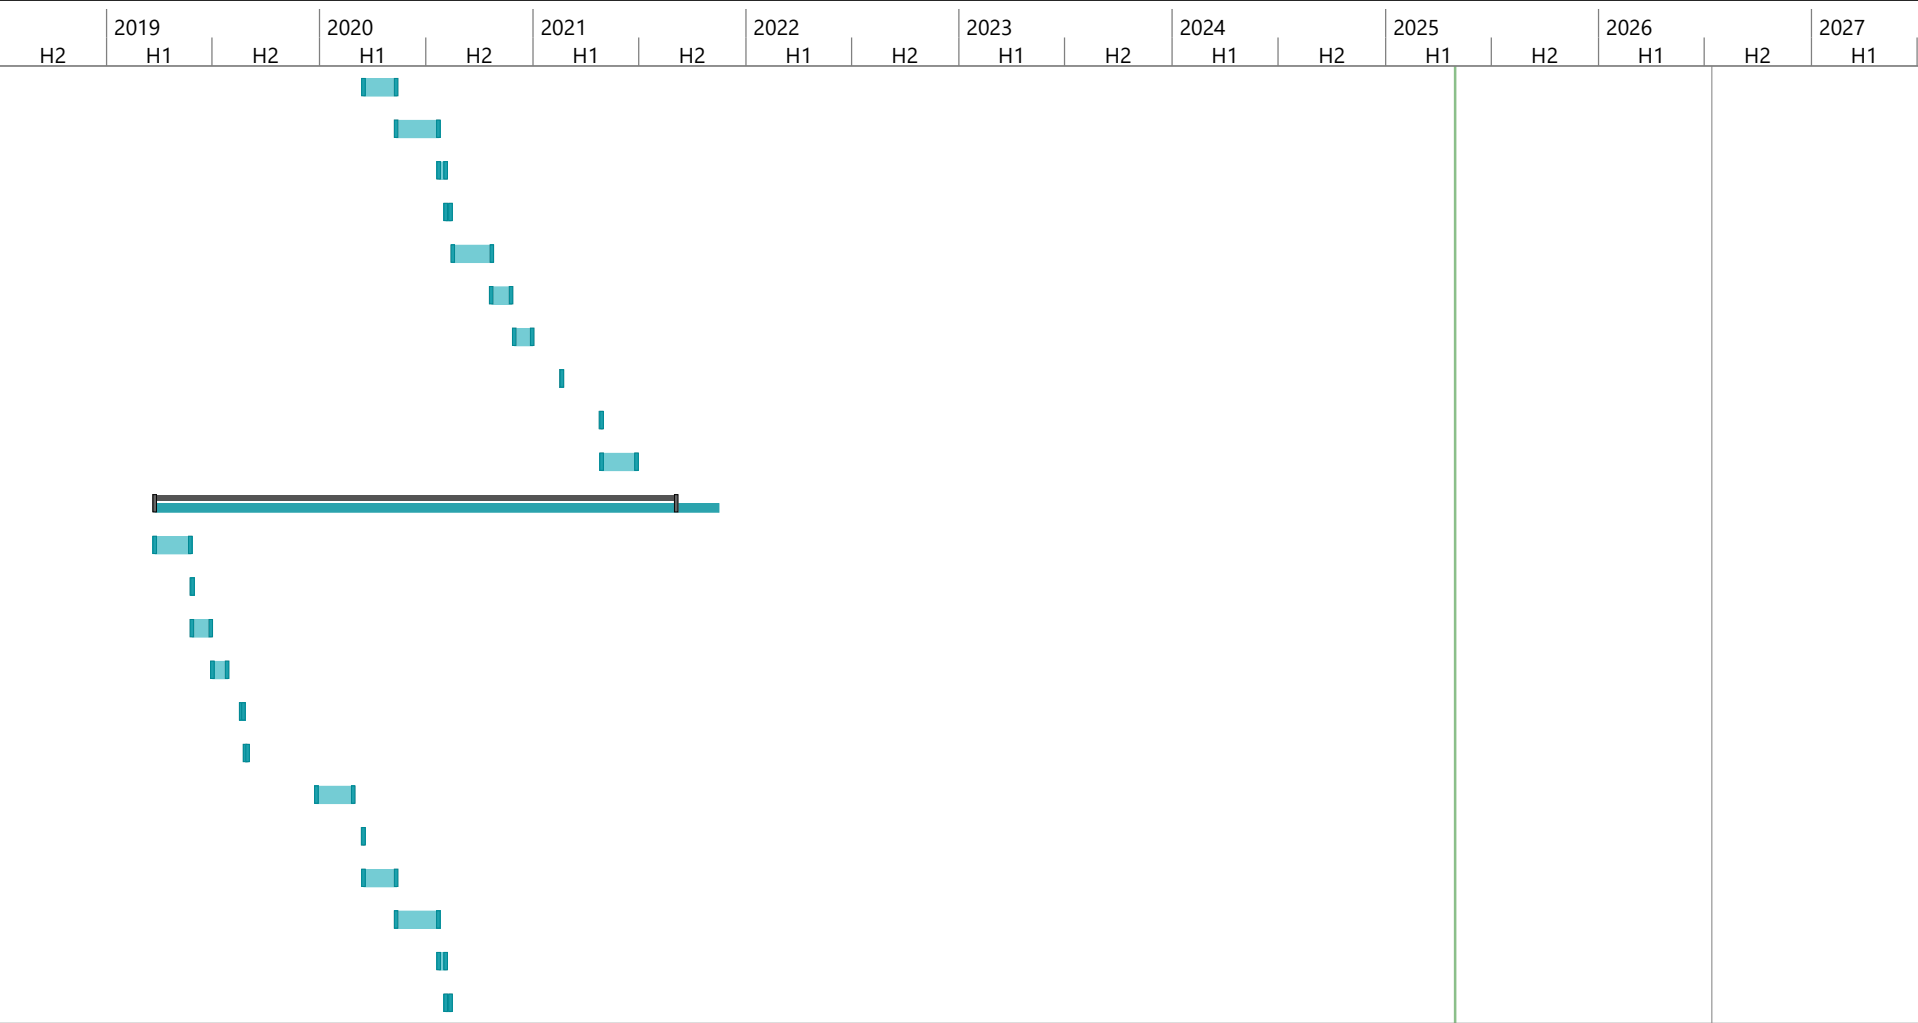
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |





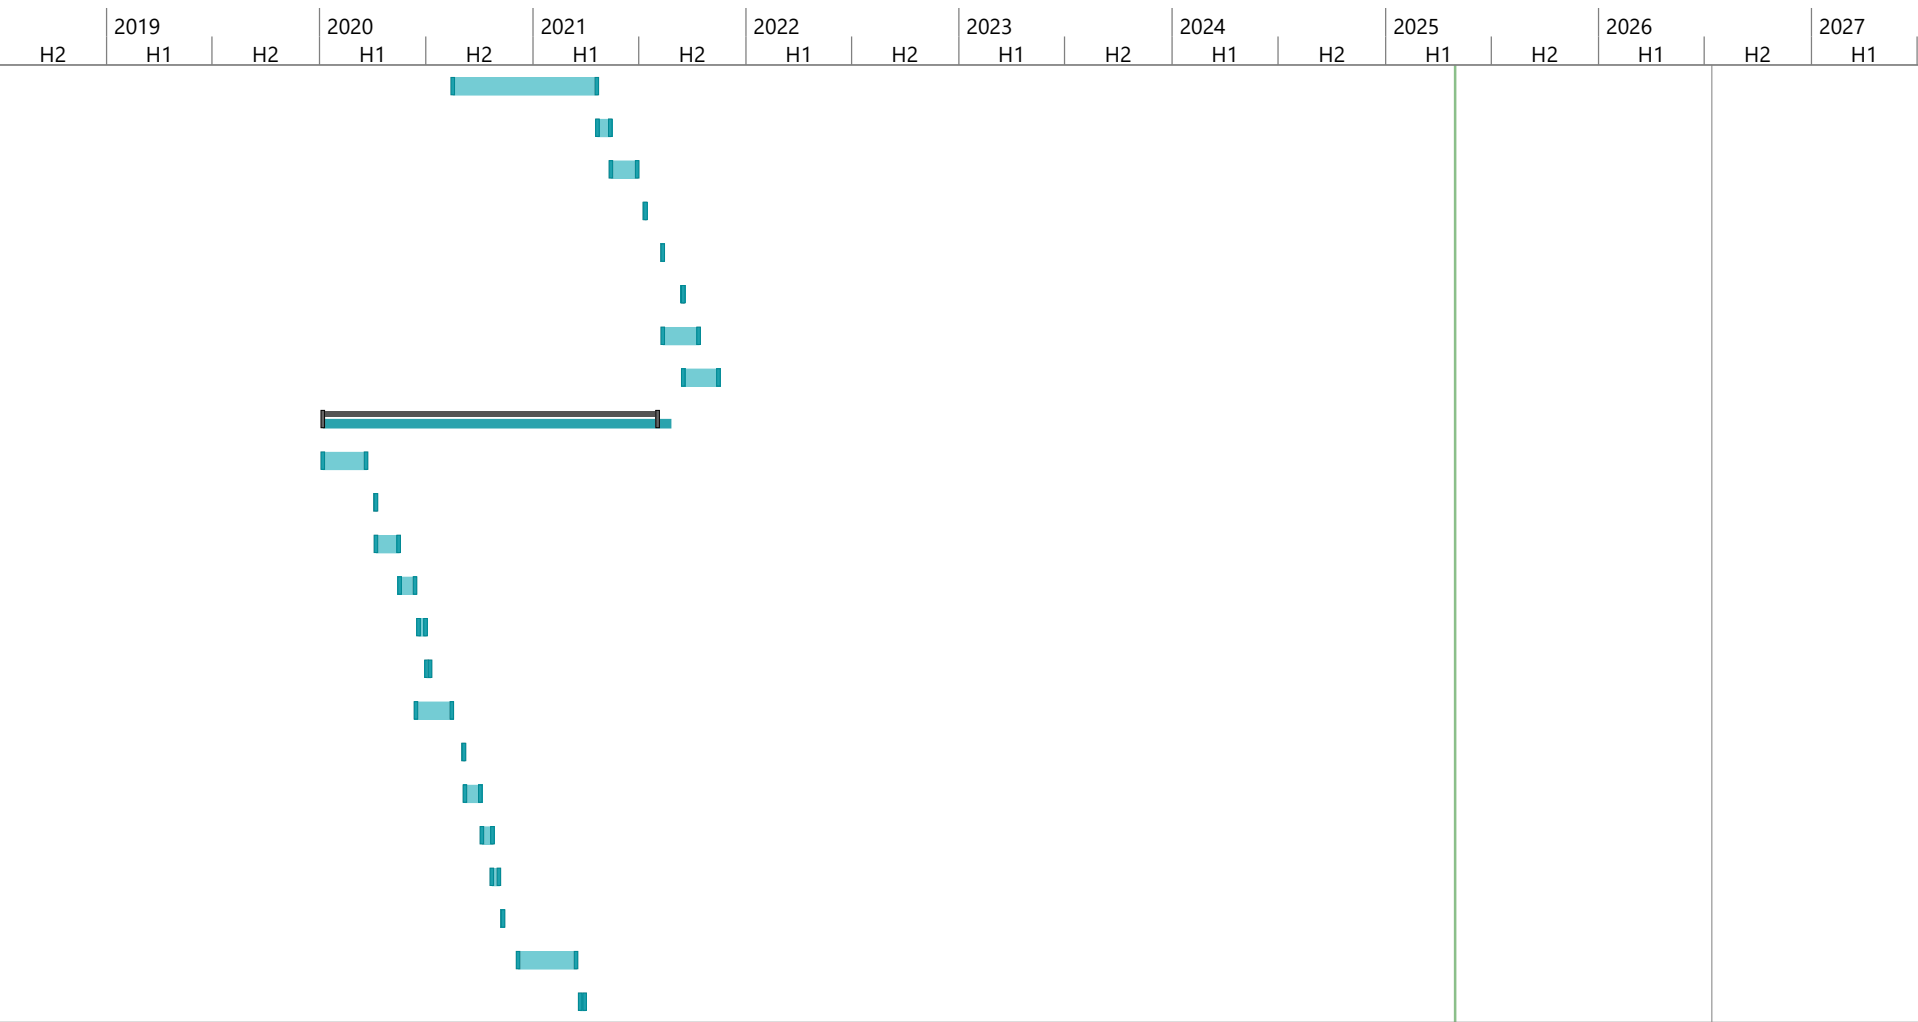






Project: IOU Master Task Timeli  
Date: Wed 4/30/25

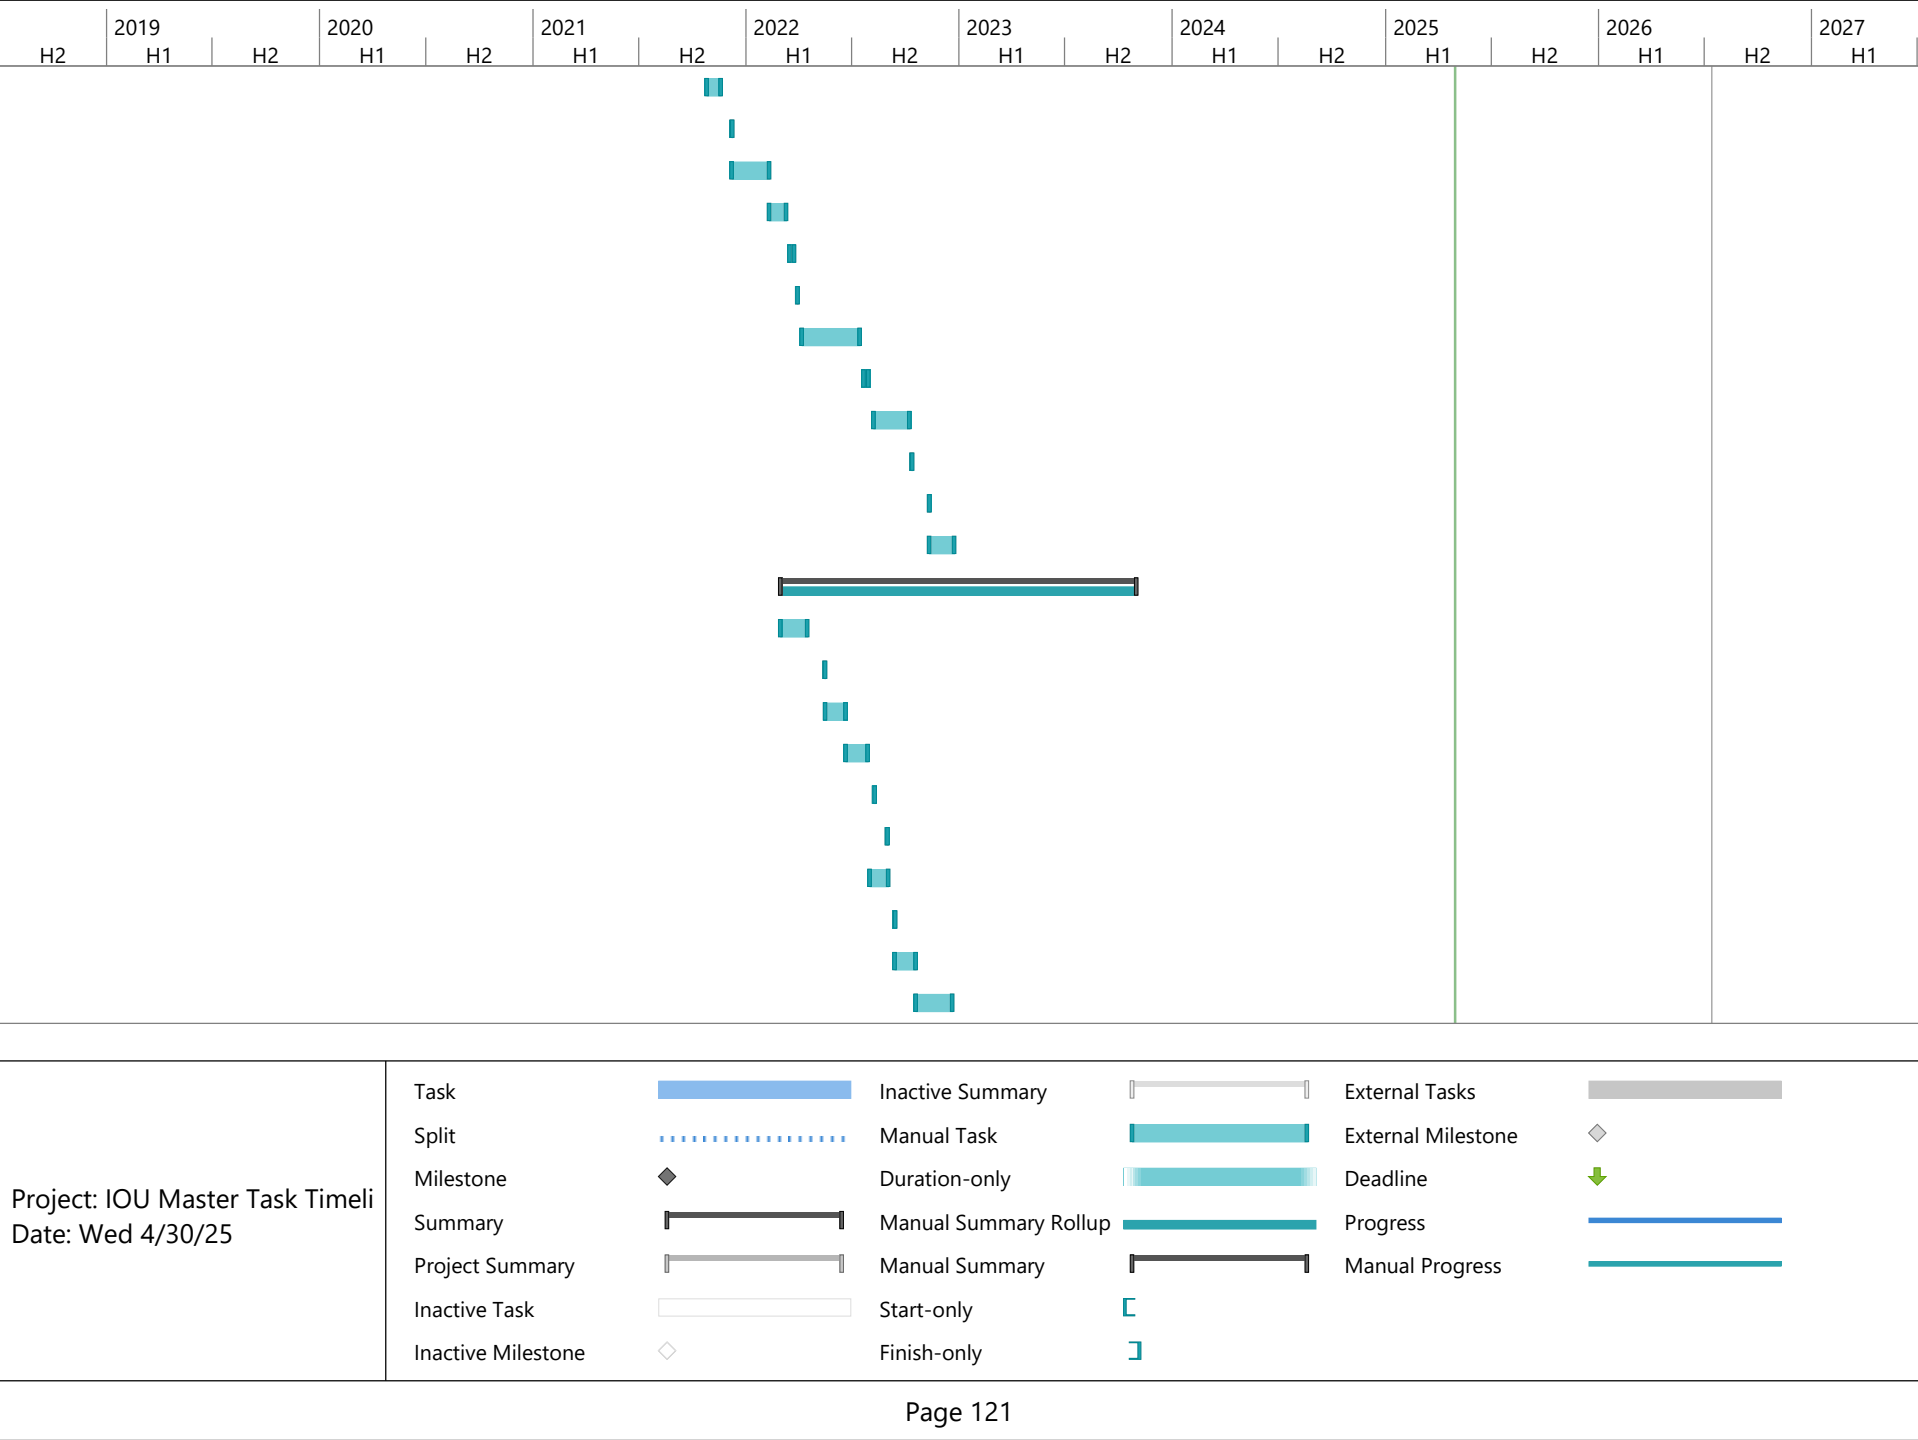
|                    |  |                       |  |                    |  |
|--------------------|--|-----------------------|--|--------------------|--|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |  |
| Inactive Milestone |  | Finish-only           |  |                    |  |

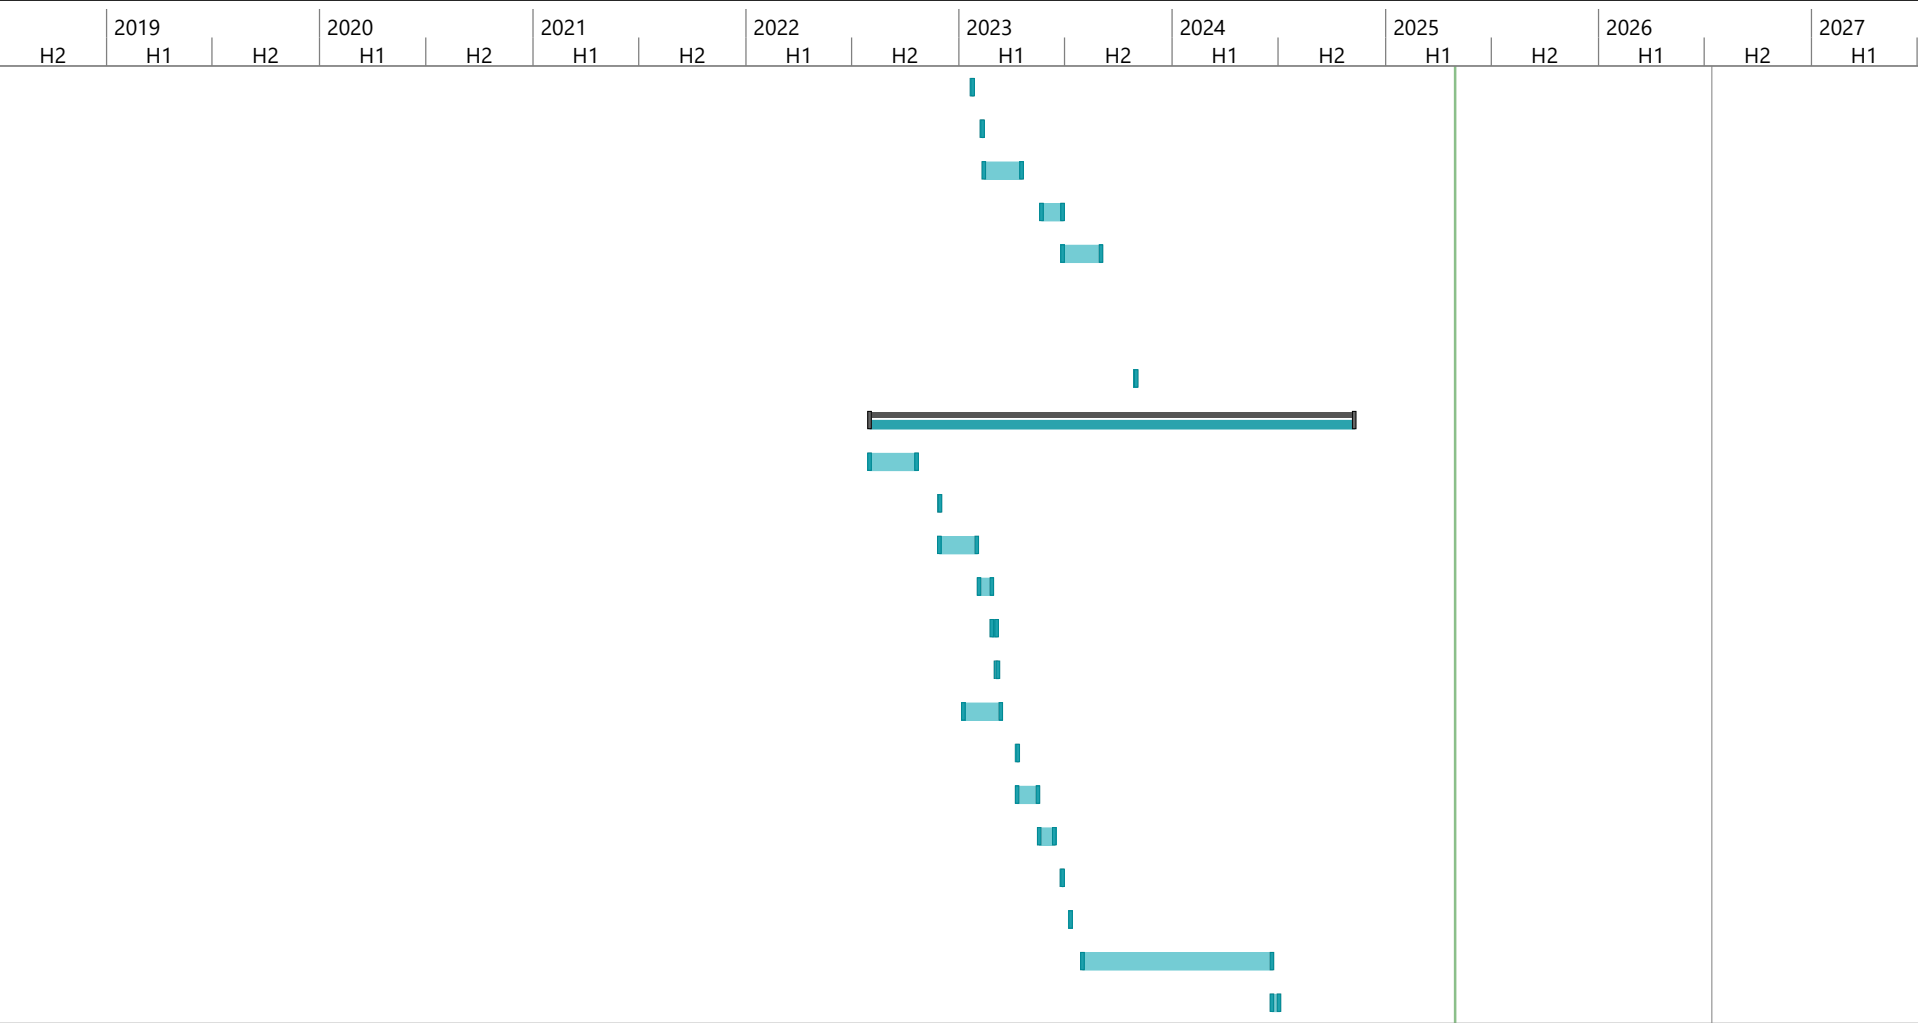


|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |

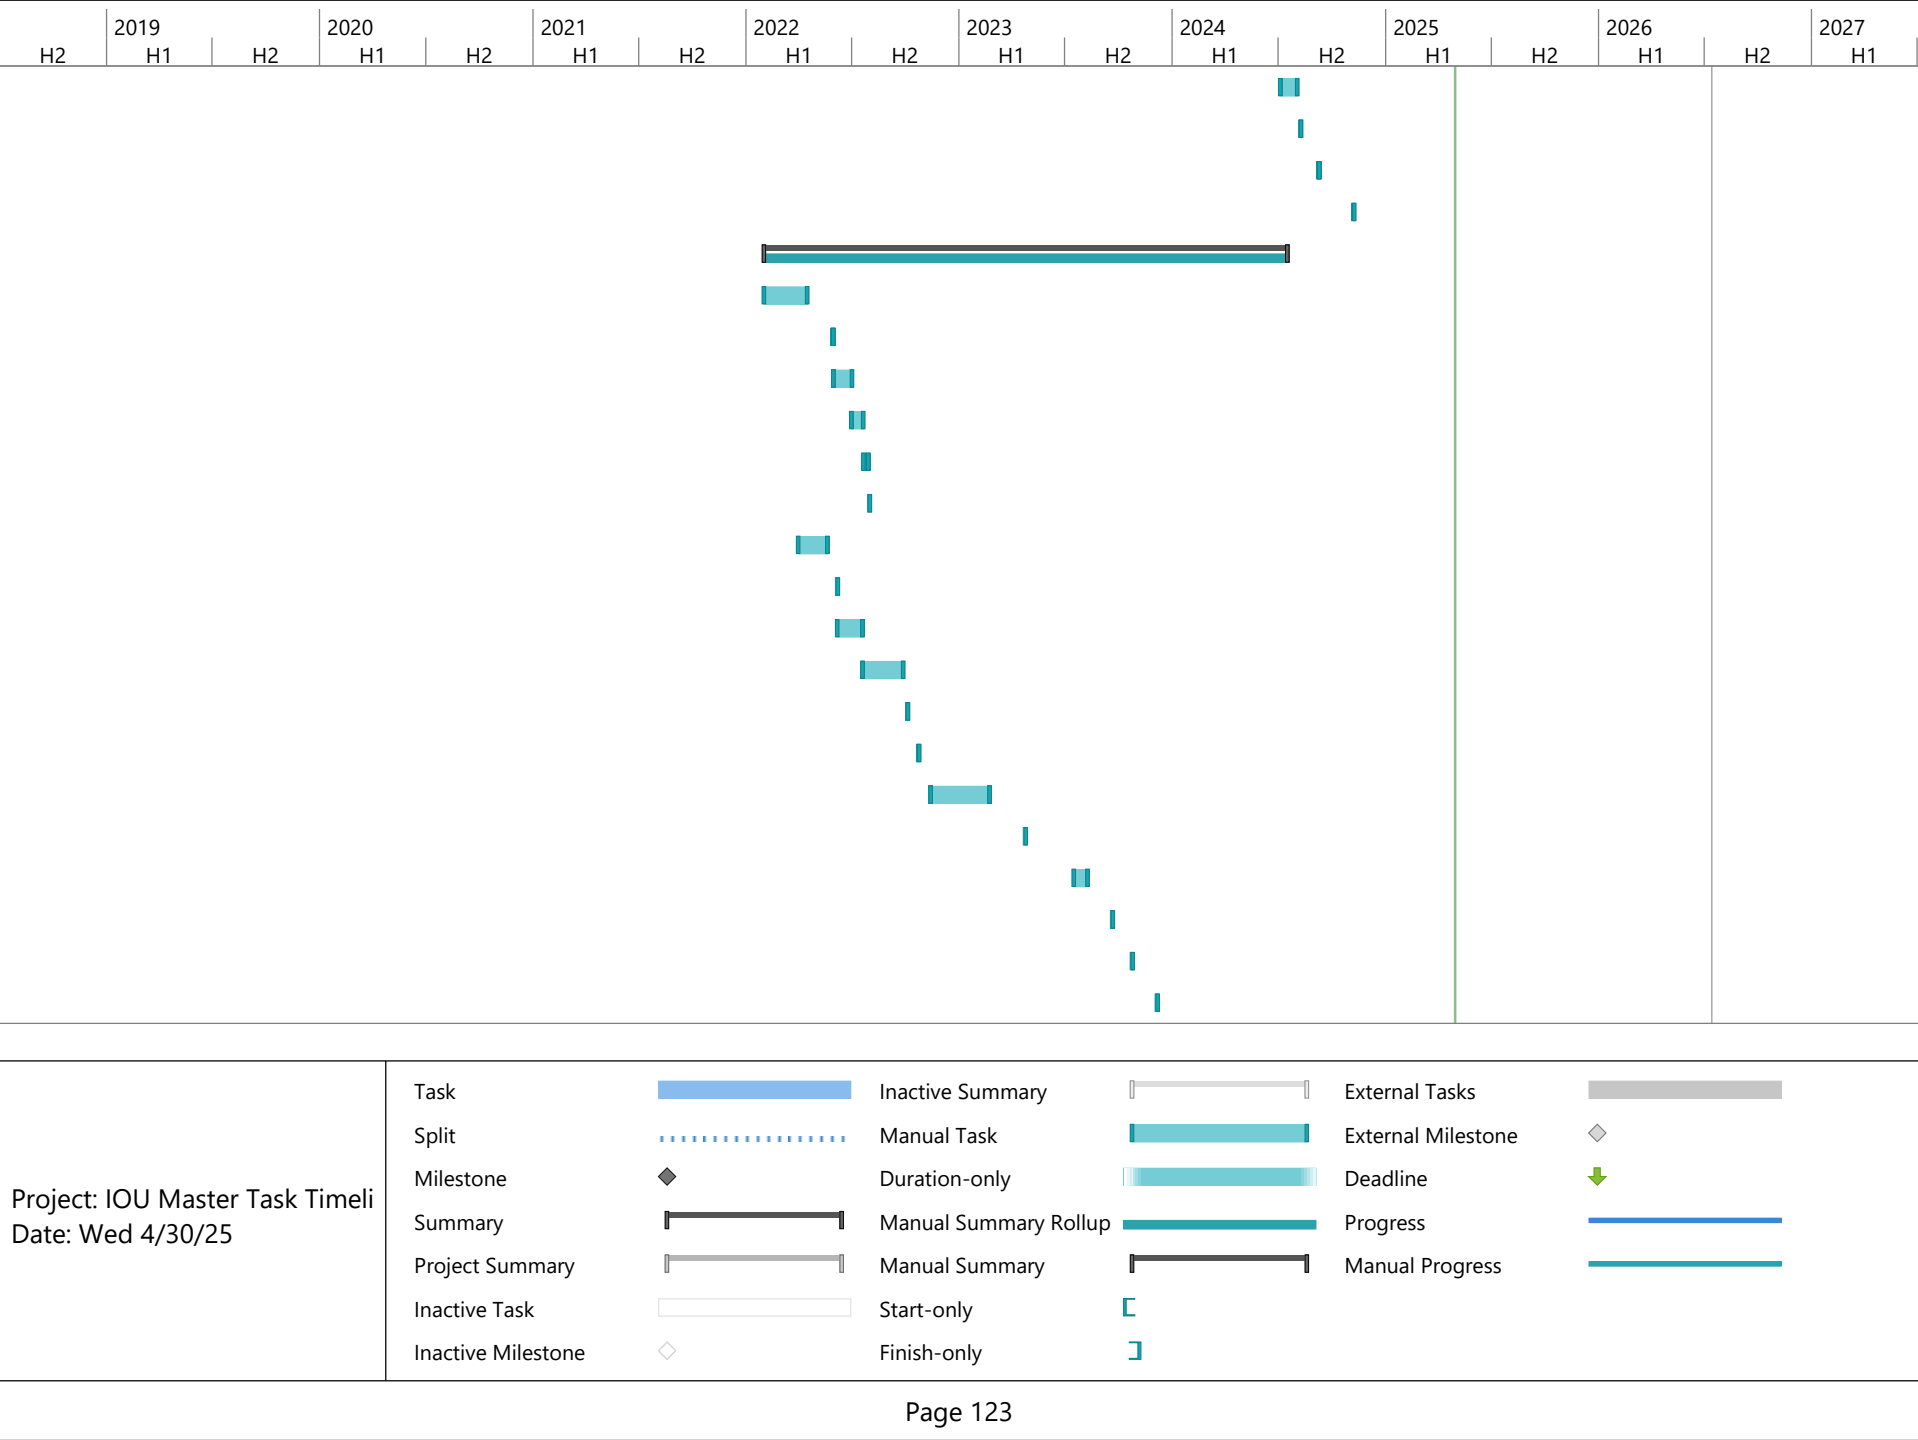




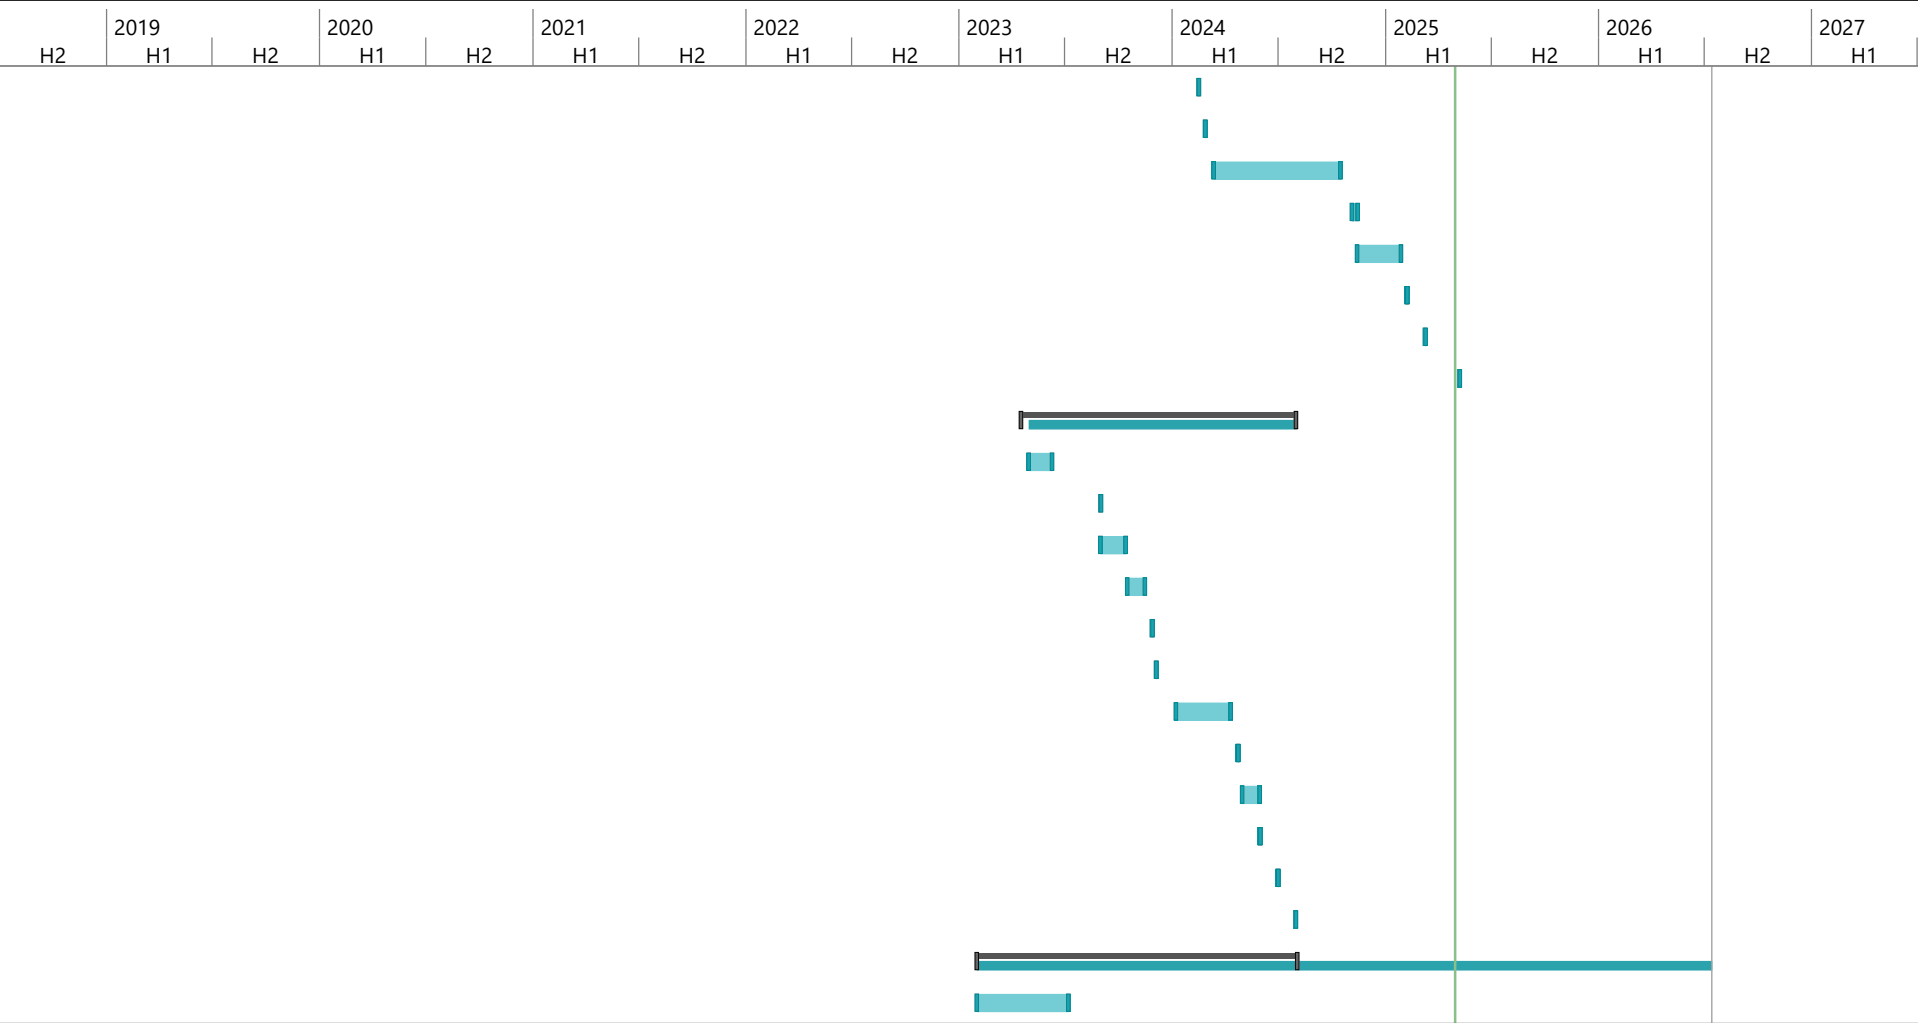




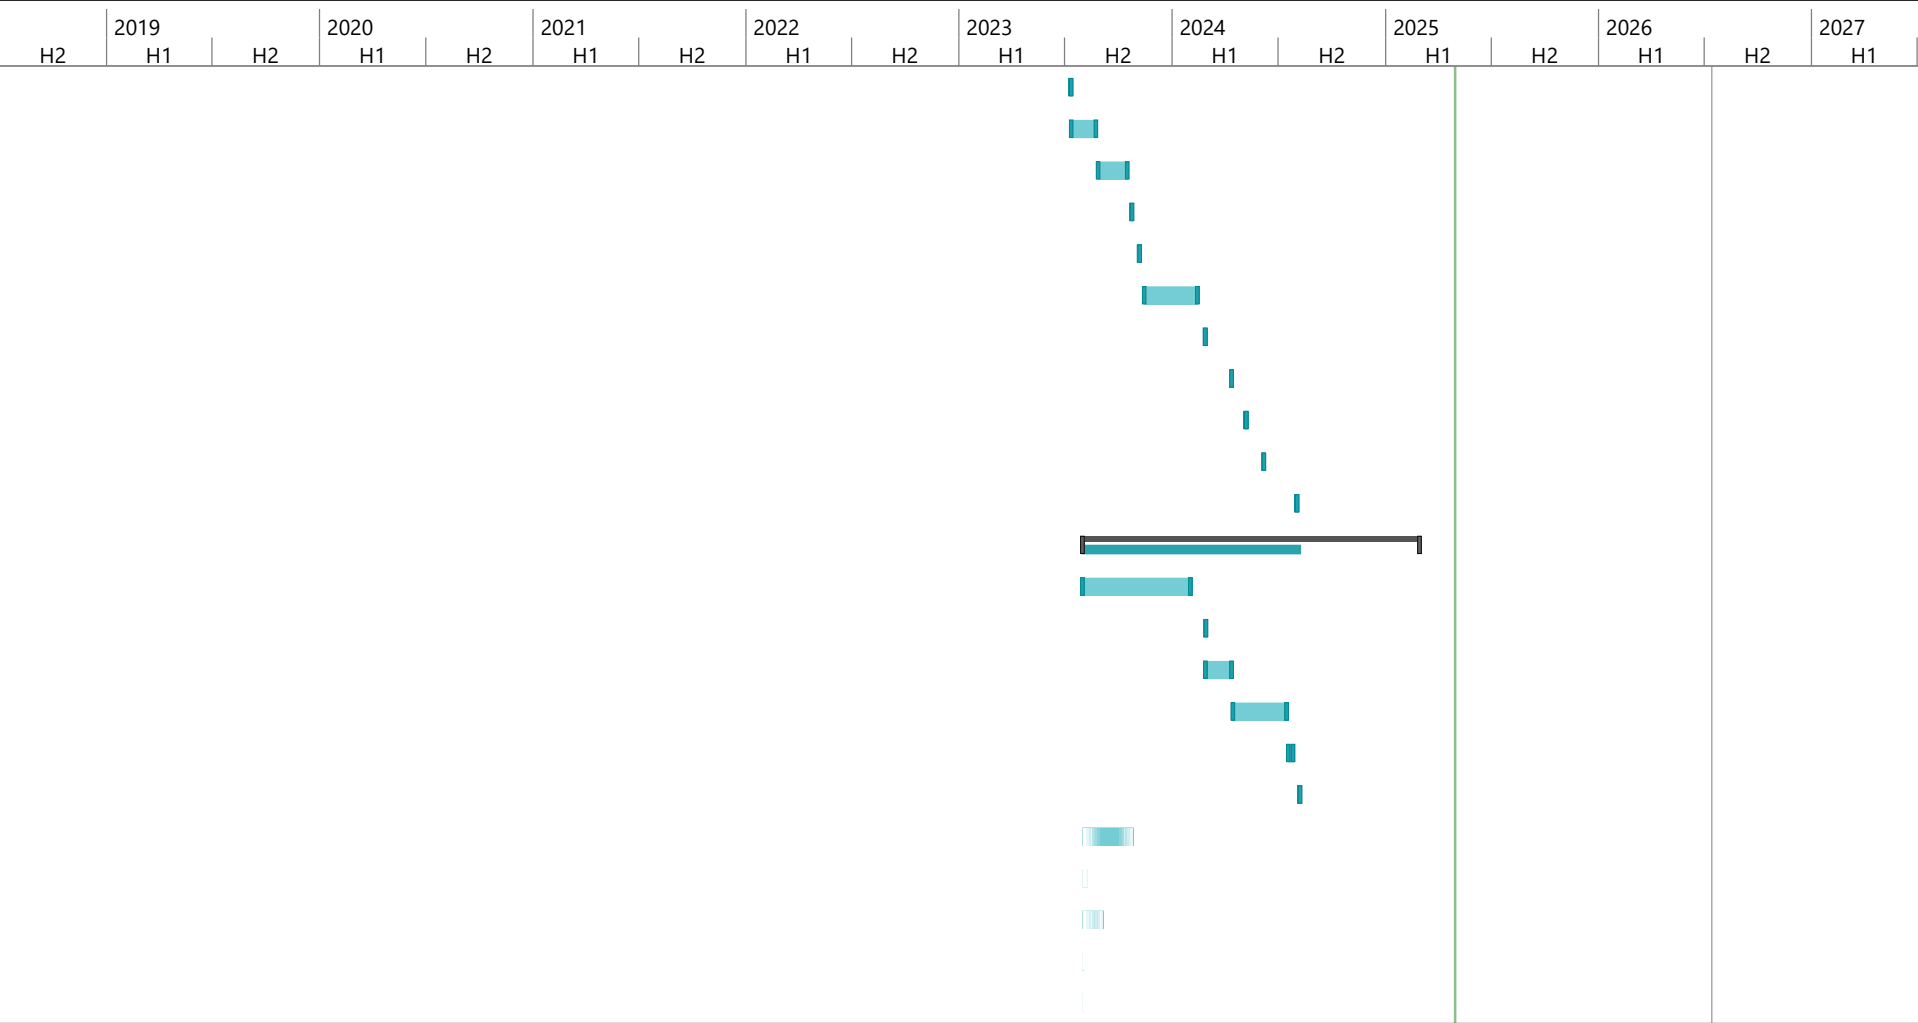
|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |



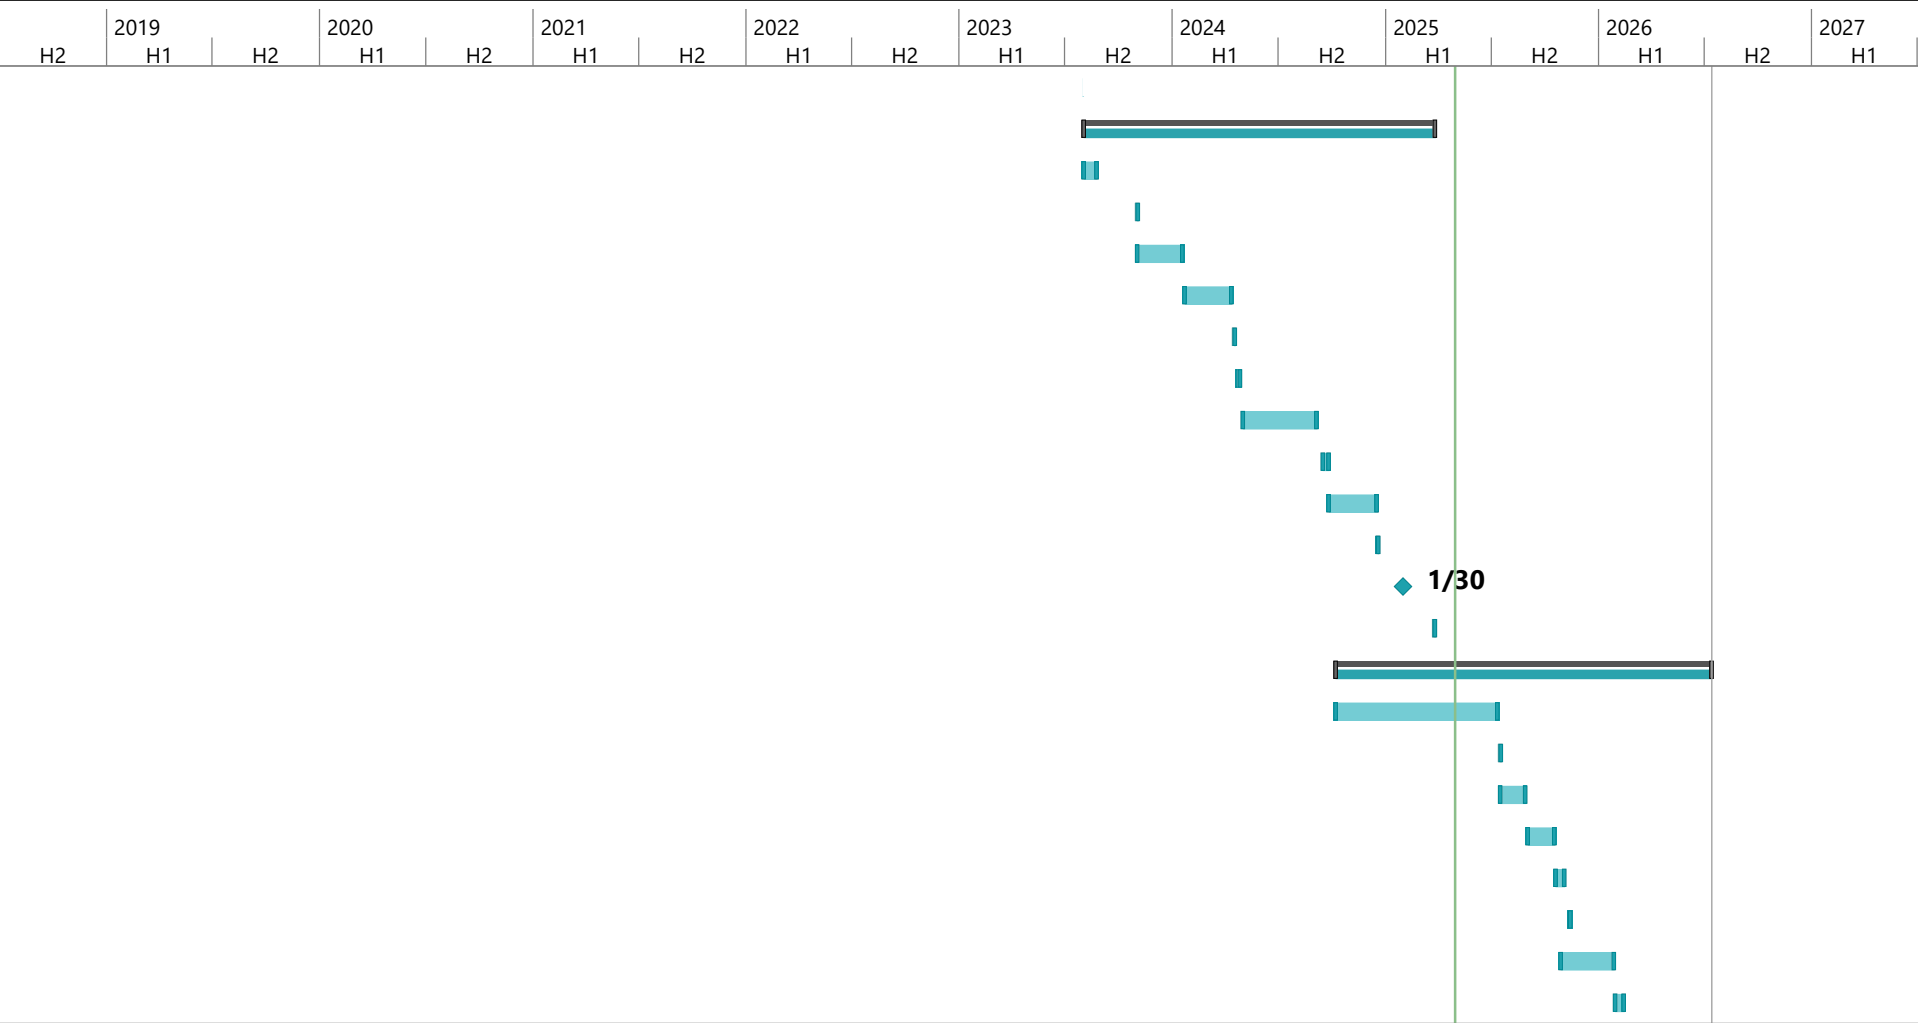




|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |



|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |



|                                                      |                    |  |                       |  |                    |  |
|------------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: IOU Master Task Timeli<br>Date: Wed 4/30/25 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                      | Split              |  | Manual Task           |  | External Milestone |  |
|                                                      | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                      | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                      | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                      | Inactive Task      |  | Start-only            |  |                    |  |
|                                                      | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                      |                    |  |                       |  |                    |  |

