




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1	<b>UPDATED as of July 1, 2026</b>					
2	<b>SCE - Local RCI Solicitation</b>	<b>679 days</b>	<b>Tue 8/21/18</b>	<b>Fri 3/26/21</b>		
3	SCE - RFA Preparation	40 days	Tue 8/21/18	Mon 10/15/18		
4	SCE - RFA Release	1 day	Fri 11/9/18	Fri 11/9/18		
5	SCE - RFA Abstract Creation Duration	30 days	Sat 11/10/18	Thu 12/20/18		
6	SCE - RFA Evaluation	82 days	Fri 12/21/18	Mon 4/15/19		
7	SCE - RFA Review with EE PRG	1 day	Tue 4/16/19	Tue 4/16/19		
8	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/21/19	Tue 5/21/19		
9	SCE - RFP Preparation	175 days	Wed 5/22/19	Tue 1/21/20		
10	SCE - RFP Release	1 day	Wed 1/22/20	Wed 1/22/20		
11	SCE - RFP Proposal Creation Duration	25 days	Thu 1/23/20	Wed 2/26/20		
12	SCE - RFP Evaluation	38 days	Thu 2/27/20	Mon 4/20/20		
13	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20		
14	SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20		
15	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20		
16	SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20		
17	SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20		
18	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20		
19	SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20		
20	SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21		
21	<b>SCE - SW Lighting</b>	<b>518 days</b>	<b>Wed 4/3/19</b>	<b>Fri 3/26/21</b>		
22	SCE - RFA Preparation	55 days	Wed 4/3/19	Tue 6/18/19		
23	SCE - RFA Release	1 day	Tue 7/2/19	Tue 7/2/19		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
24	SCE - RFA Abstract Creation Duration	20 days	Wed 7/3/19	Tue 7/30/19		
25	SCE - RFA Evaluation	34 days	Wed 7/31/19	Mon 9/16/19		
26	SCE - RFA Review with EE PRG	1 day	Tue 9/17/19	Tue 9/17/19		
27	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/24/19	Tue 9/24/19		
28	SCE - RFP Preparation	84 days	Wed 9/25/19	Mon 1/20/20		
29	SCE - RFP Release	1 day	Thu 2/6/20	Thu 2/6/20		
30	SCE - RFP Proposal Creation Duration	27 days	Fri 2/7/20	Mon 3/16/20		
31	SCE - RFP Evaluation	25 days	Tue 3/17/20	Mon 4/20/20		
32	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20		
33	SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20		
34	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20		
35	SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20		
36	SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20		
37	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20		
38	SCE - Advice Letter Approved	1 day	Wed 12/23/20	Wed 12/23/20		
39	SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21		
40	<b>SCE - Local Public Sector Solicitation</b>	<b>573 days</b>	<b>Mon 8/31/20</b>	<b>Wed 11/9/22</b>		
41	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20		
42	SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20		
43	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20		
44	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21		
45	SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21		
46	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
47	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21		
48	SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21		
49	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21		
50	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21		
51	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21		
52	SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21		
53	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21		
54	SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21		
55	SCE - Final Award and Contract Signed	1 day	Tue 12/14/21	Tue 12/14/21		
56	SCE - Submit Advice Letter	37 days	Wed 12/15/21	Thu 2/3/22		
57	SCE - Submit Advice Letter	48 days	Wed 12/15/21	Fri 2/18/22		
58	SCE - Advice Letter Approved	1 day	Thu 8/18/22	Thu 8/18/22		
59	SCE - Implementation Plan	60 days	Thu 8/18/22	Wed 11/9/22		
60	<b>SCE - Local Agriculture Solicitation</b>	<b>512 days</b>	<b>Mon 8/31/20</b>	<b>Tue 8/16/22</b>		
61	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20		
62	SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20		
63	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20		
64	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21		
65	SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21		
66	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21		
67	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21		
68	SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21		
69	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
70	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21		
71	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21		
72	SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21		
73	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21		
74	SCE - Final Award and Contract Signed	1 day	Mon 12/20/21	Mon 12/20/21		
75	SCE - Submit Advice Letter	33 days	Tue 12/21/21	Thu 2/3/22		
76	SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21		
77	SCE - Final Award and Contract Signed	1 day	Wed 12/15/21	Wed 12/15/21		
78	SCE - Submit Advice Letter	56 days	Thu 12/16/21	Thu 3/3/22		
79	SCE - Advice Letter Approved	1 day	Fri 4/22/22	Fri 4/22/22		
80	SCE - Implementation Plan	60 days	Sat 4/23/22	Thu 7/14/22		
81	<b>SCE - SW Water/Wastewater Solicitation</b>	<b>522 days</b>	<b>Mon 11/16/20</b>	<b>Tue 11/15/22</b>		
82	SCE - RFA Preparation	70 days	Mon 11/16/20	Fri 2/19/21		
83	SCE - RFA Release	1 day	Thu 3/4/21	Thu 3/4/21		
84	SCE - RFA Abstract Creation Duration	29 days	Thu 3/4/21	Tue 4/13/21		
85	SCE - RFA Evaluation	20 days	Wed 4/14/21	Tue 5/11/21		
86	SCE - RFA Review with EE PRG	1 day	Tue 5/18/21	Tue 5/18/21		
87	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/27/21	Thu 5/27/21		
88	SCE - RFP Preparation	34 days	Mon 4/19/21	Thu 6/3/21		
89	SCE - RFP Release	1 day	Thu 7/1/21	Thu 7/1/21		
90	SCE - RFP Proposal Creation Duration	25 days	Fri 7/2/21	Thu 8/5/21		
91	SCE - RFP Evaluation	41 days	Fri 8/6/21	Fri 10/1/21		
92	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/26/21	Tue 10/26/21		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
93	SCE - RFP Review with EE PRG	1 day	Tue 10/19/21	Tue 10/19/21		
94	SCE - Contract Negotiation and Development	94 days	Wed 10/27/21	Mon 3/7/22		
95	SCE - Contract Review with EE PRG	1 day	Tue 3/15/22	Tue 3/15/22		
96	SCE - Final Award and Contract Signed	1 day	Tue 4/19/22	Tue 4/19/22		
97	SCE - Submit Advice Letter	40 days	Wed 4/20/22	Tue 6/14/22		
98	SCE - Advice Letter Approved	26 days	Wed 6/15/22	Wed 7/20/22		
99	SCE - Implementation Plan	44 days	Thu 7/21/22	Tue 9/20/22		
100	<b>SCE - SW ETP Solicitation</b>	<b>466 days</b>	<b>Fri 5/1/20</b>	<b>Fri 2/11/22</b>		
101	SCE - RFA Preparation	57 days	Fri 5/1/20	Mon 7/20/20		
102	SCE - RFA Release	1 day	Tue 8/4/20	Tue 8/4/20		
103	SCE - RFA Abstract Creation Duration	24 days	Fri 8/7/20	Wed 9/9/20		
104	SCE - RFA Evaluation	16 days	Thu 9/10/20	Thu 10/1/20		
105	SCE - RFA Review with EE PRG	1 day	Tue 10/20/20	Tue 10/20/20		
106	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/27/20	Tue 10/27/20		
107	SCE - RFP Preparation	42 days	Tue 9/8/20	Wed 11/4/20		
108	SCE - RFP Release	1 day	Tue 1/5/21	Tue 1/5/21		
109	SCE - RFP Proposal Creation Duration	37 days	Tue 1/5/21	Wed 2/24/21		
110	SCE - RFP Evaluation	28 days	Wed 2/24/21	Fri 4/2/21		
111	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/27/21	Tue 4/27/21		
112	SCE - RFP Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21		
113	SCE - Contract Negotiation and Development	69 days	Wed 4/21/21	Mon 7/26/21		
114	SCE - Contract Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21		
115	SCE - Final Award and Contract Signed	1 day	Tue 9/14/21	Tue 9/14/21		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
116	SCE - Submit Advice Letter	18 days	Wed 9/15/21	Fri 10/8/21		
117	SCE - Advice Letter Approved	1 day	Tue 11/9/21	Tue 11/9/21		
118	SCE - Implementation Plan	60 days	Wed 11/10/21	Tue 2/1/22		
119	<b>SCE - SW Higher-Education Solicitation</b>	<b>547 days?</b>	<b>Thu 10/1/20</b>	<b>Fri 11/4/22</b>		
120	SCE - RFA Preparation	89 days	Thu 10/1/20	Tue 2/2/21		
121	SCE - RFA Release	1 day	Thu 2/4/21	Thu 2/4/21		
122	SCE - RFA Abstract Creation Duration	19 days	Fri 2/5/21	Wed 3/3/21		
123	SCE - RFA Evaluation	31 days	Thu 3/4/21	Thu 4/15/21		
124	SCE - RFA Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21		
125	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 4/29/21	Thu 4/29/21		
126	SCE - RFP Preparation	39 days	Mon 3/22/21	Thu 5/13/21		
127	SCE - RFP Release	1 day	Fri 5/28/21	Fri 5/28/21		
128	SCE - RFP Proposal Creation Duration	24 days	Fri 6/4/21	Wed 7/7/21		
129	SCE - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21		
130	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/30/21	Mon 8/30/21		
131	SCE - RFP Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21		
132	SCE - Contract Negotiation and Development	95 days	Fri 9/3/21	Thu 1/13/22		
133	SCE - Contract Review with EE PRG	1 day	Tue 1/18/22	Tue 1/18/22		
134	SCE - Final Award and Contract Signed	1 day	Sun 3/6/22	Sun 3/6/22		
135	SCE - Submit Advice Letter	1 day	Tue 4/19/22	Tue 4/19/22		
136	SCE - Advice Letter Approved	1 day	Mon 8/15/22	Mon 8/15/22		
137	SCE - Implementation Plan	60 days	Mon 8/15/22	Fri 11/4/22		
138	<b>SCE - Local Equity Residential and SMB</b>	<b>384 days?</b>	<b>Tue 2/15/22</b>	<b>Fri 8/4/23</b>		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1	H2
139	SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22		
140	SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22		
141	SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22		
142	SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22		
143	SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22		
144	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22		
145	SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22		
146	SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22		
147	SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22		
148	SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22		
149	SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22		
150	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22		
151	SCE - Contract Negotiation and Development	65 days	Wed 11/2/22	Tue 1/31/23		
152	SCE - Contract Review with EE PRG	1 day	Tue 2/21/23	Tue 2/21/23		
153	SCE - Final Award and Contract Signed	1 day	Thu 3/30/23	Thu 3/30/23		
154	SCE - Submit Advice Letter	22 days	Sun 4/3/22	Mon 5/2/22		
155	SCE - Advice Letter Approved	28 days	Tue 5/2/23	Thu 6/8/23		
156	SCE - Implementation Plan	45 days	Thu 6/8/23	Wed 8/9/23		
157						
158	<b>SCE - Local Equity SMB</b>	<b>431 days?</b>	<b>Tue 2/15/22</b>	<b>Tue 10/10/23</b>		
159	SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22		
160	SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22		
161	SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
162	SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22		
163	SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22		
164	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22		
165	SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22		
166	SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22		
167	SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22		
168	SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22		
169	SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22		
170	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22		
171	SCE - Contract Negotiation and Development	108 days	Wed 11/2/22	Fri 3/31/23		
172	SCE - Contract Review with EE PRG	1 day	Tue 4/18/23	Tue 4/18/23		
173	SCE - Final Award and Contract Signed	1 day	Wed 5/31/23	Wed 5/31/23		
174	SCE - Submit Advice Letter	22 days	Mon 6/6/22	Tue 7/5/22		
175	SCE - Advice Letter Approved	24 days	Thu 7/6/23	Tue 8/8/23		
176	SCE - Implementation Plan	45 days	Wed 8/9/23	Tue 10/10/23		
177	<b>SCE - Local Strategic Energy Management Solicitation</b>	<b>372 days?</b>	<b>Thu 12/1/22</b>	<b>Fri 5/3/24</b>		
178	SCE - RFP Preparation	85 days	Thu 12/1/22	Wed 3/29/23		
179	SCE - RFP Release	1 day	Fri 4/7/23	Fri 4/7/23		
180	SCE - RFP Proposal Creation Duration	35 days	Fri 4/7/23	Thu 5/25/23		
181	SCE - RFP Evaluation	22 days	Thu 6/1/23	Fri 6/30/23		
182	SCE - RFP Review with EE PRG	1 day	Tue 7/18/23	Tue 7/18/23		
183	SCE - Contract Negotiation and Development	86 days	Tue 8/1/23	Tue 11/28/23		
184	SCE - Contract Review with EE PRG	1 day	Tue 12/19/23	Tue 12/19/23		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
185	SCE - Final Award and Contract Signed	6 days	Fri 1/19/24	Fri 1/26/24		
186	SCE - Submit Advice Letter	34 days	Wed 1/31/24	Mon 3/18/24		
187	SCE - Advice Letter Approved	40 days	Tue 3/19/24	Mon 5/13/24		
188	<b>SCE - Local Large Commercial Solicitation</b>	<b>488 days?</b>	<b>Mon 6/26/23</b>	<b>Wed 5/7/25</b>		
189	SCE - RFP Preparation	35 days	Mon 6/26/23	Fri 8/11/23		
190	SCE - RFP Release	1 day	Thu 8/17/23	Thu 8/17/23		
191	SCE - RFP Proposal Creation Duration	41 days	Thu 8/17/23	Thu 10/12/23		
192	SCE - RFP Paused	1 day	Fri 10/13/23	Fri 10/13/23		
193	<b>SCE - Residential Multifamily</b>	<b>326 days?</b>	<b>Fri 9/1/23</b>	<b>Fri 11/29/24</b>		
194	SCE - RFP Preparation	47 days	Fri 9/1/23	Mon 11/6/23		
195	SCE - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23		
196	SCE - RFP Proposal Creation Duration	48 days	Mon 11/6/23	Wed 1/10/24		
197	SCE - RFP Evaluation	25 days	Thu 1/11/24	Wed 2/14/24		
198	SCE - RFP Review with EE PRG	1 day	Tue 2/20/24	Tue 2/20/24		
199	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 2/28/24	Wed 2/28/24		
200	SCE - Contract Negotiation and Development	70 days	Mon 3/4/24	Fri 6/7/24		
201	SCE - Contract Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
202	SCE - Final Award and Contract Signed	15 days	Mon 7/29/24	Fri 8/16/24		
203	SCE - Submit Advice Letter	30 days	Mon 8/19/24	Fri 9/27/24		
204	SCE - Advice Letter Approved	1 day	Mon 10/28/24	Mon 10/28/24		
205	<b>SCE - Local Large Industrial</b>	<b>499 days</b>	<b>Fri 11/3/23</b>	<b>Wed 10/1/25</b>		
206	SCE - RFP Preparation	17 days	Fri 11/3/23	Mon 11/27/23		
207	SCE - RFP Release	1 day	Mon 12/11/23	Mon 12/11/23		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
208	SCE - RFP Proposal Creation Duration	49 days	Mon 12/11/23	Thu 2/15/24		
209	SCE - RFP Evaluation	35 days	Fri 2/16/24	Thu 4/4/24		
210	SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24		
211	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/23/24	Tue 4/23/24		
212	SCE - Contract Negotiation and Development	208 days	Wed 4/24/24	Fri 2/7/25		
213	SCE - Contract Review with EE PRG	1 day	Tue 4/29/25	Tue 4/29/25		
214	SCE - Final Award and Contract Signed	42 days	Thu 5/1/25	Fri 6/27/25		
215	SCE - Submit Advice Letter	35 days	Mon 6/30/25	Fri 8/15/25		
216	SCE - Advice Letter Approved	33 days	Mon 8/18/25	Wed 10/1/25		
217	<b>SCE - MAP - All Sectors</b>	<b>299 days?</b>	<b>Mon 11/20/23</b>	<b>Thu 1/9/25</b>		
218	SCE - RFP Preparation	20 days	Mon 11/20/23	Fri 12/15/23		
219	SCE - RFP Release	1 day	Mon 1/8/24	Mon 1/8/24		
220	SCE - RFP Proposal Creation Duration	40 days	Mon 1/8/24	Fri 3/1/24		
221	SCE - RFP Evaluation	30 days	Mon 3/4/24	Fri 4/12/24		
222	SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24		
223	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/24/24	Wed 4/24/24		
224	SCE - Contract Negotiation and Development	108 days	Wed 5/1/24	Fri 9/27/24		
225	SCE - Contract Review with EE PRG	1 day	Tue 10/15/24	Tue 10/15/24		
226	SCE - Final Award and Contract Signed	12 days	Tue 10/29/24	Wed 11/13/24		
227	SCE - Submit Advice Letter	43 days	Wed 11/13/24	Fri 1/10/25		
228	SCE - Advice Letter Approved	22 days	Mon 1/13/25	Tue 2/11/25		
229	<b>SCE - Residential</b>	<b>360 days?</b>	<b>Mon 11/20/23</b>	<b>Fri 4/4/25</b>		
230	SCE - RFP Preparation	20 days	Tue 1/16/24	Mon 2/12/24		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1	H2
231	SCE - RFP Release	1 day	Thu 3/28/24	Thu 3/28/24		
232	SCE - RFP Proposal Creation Duration	41 days	Thu 3/28/24	Thu 5/23/24		
233	SCE - RFP Evaluation	35 days	Fri 5/24/24	Thu 7/11/24		
234	SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
235	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/5/24	Mon 8/5/24		
236	SCE - Contract Negotiation and Development	80 days	Mon 8/19/24	Fri 12/6/24		
237	SCE - Contract Review with EE PRG	1 day	Tue 12/17/24	Tue 12/17/24		
238	SCE - Final Award and Contract Signed	11 days	Mon 1/13/25	Mon 1/27/25		
239	SCE - Submit Advice Letter	19 days	Mon 2/3/25	Thu 2/27/25		
240	SCE - Advice Letter Approved	1 day	Tue 4/1/25	Tue 4/1/25		
241						
242	<b>SCE - Local Comprehensive Commercial Solicitation</b>	<b>431 days?</b>	<b>Mon 11/13/23</b>	<b>Mon 7/7/25</b>		
243	SCE - RFP Preparation	73 days	Mon 11/13/23	Wed 2/21/24		
244	SCE - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24		
245	SCE - RFP Proposal Creation Duration	43 days	Thu 2/29/24	Mon 4/29/24		
246	SCE - RFP Evaluation	54 days	Tue 4/30/24	Fri 7/12/24		
247	SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
248	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Phase 1	1 day	Mon 7/29/24	Mon 7/29/24		
249	SCE - Contract Negotiation and Development - Phase 1	81 days	Tue 7/30/24	Tue 11/19/24		
250	SCE - Contract Review with EE PRG - Phase 1	1 day	Tue 12/17/24	Tue 12/17/24		
251	SCE - Final Award and Contract Signed - Phase 1	1 day	Tue 1/28/25	Tue 1/28/25		
252	SCE - Submit Advice Letter - Phase 1	23 days	Tue 1/28/25	Thu 2/27/25		
253	SCE - Advice Letter Approved - Phase 1	1 day	Tue 4/1/25	Tue 4/1/25		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
254	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Pha	1 day	Mon 9/30/24	Mon 9/30/24		
255	SCE - Contract Negotiation and Development - Phase 2	80 days	Mon 12/2/24	Fri 3/21/25		
256	SCE - Contract Review with EE PRG - Phase 2	1 day	Tue 4/29/25	Tue 4/29/25		
257	SCE - Final Award and Contract Signed - Phase 2	1 day	Tue 5/20/25	Tue 5/20/25		
258	SCE - Submit Advice Letter - Phase 2	0 days	N/A	N/A		
259	SCE - Advice Letter Approved - Phase 2	0 days	N/A	N/A		
260	<b>SCE - SW ETP Solicitation</b>	<b>505 days</b>	<b>Wed 2/25/26</b>	<b>Tue 2/1/28</b>		
261	SCE - RFA Preparation	63 days	Wed 2/25/26	Fri 5/22/26		
262	SCE - RFA Release	1 day	Tue 5/26/26	Tue 5/26/26		
263	SCE - RFA Abstract Creation Duration	34 days	Tue 5/26/26	Fri 7/10/26		
264	SCE - RFA Evaluation	19 days	Tue 7/21/26	Fri 8/14/26		
265	SCE - RFA Review with EE PRG	1 day	Tue 8/18/26	Tue 8/18/26		
266	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/25/26	Tue 8/25/26		
267	SCE - RFP Preparation	42 days	Mon 7/6/26	Tue 9/1/26		
268	SCE - RFP Release	1 day	Mon 11/2/26	Mon 11/2/26		
269	SCE - RFP Proposal Creation Duration	37 days	Mon 11/2/26	Tue 12/22/26		
270	SCE - RFP Evaluation	25 days	Wed 1/6/27	Tue 2/9/27		
271	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/16/27	Tue 2/16/27		
272	SCE - RFP Review with EE PRG	1 day	Tue 2/23/27	Tue 2/23/27		
273	SCE - Contract Negotiation and Development	80 days	Tue 3/2/27	Mon 6/21/27		
274	SCE - Contract Review with EE PRG	1 day	Tue 7/20/27	Tue 7/20/27		
275	SCE - Final Award and Contract Signed	1 day	Wed 7/28/27	Wed 7/28/27		
276	SCE - Submit Advice Letter	23 days	Thu 8/5/27	Mon 9/6/27		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
277	SCE - Advice Letter Approved	46 days	Tue 9/7/27	Tue 11/9/27		
278	SCE - Implementation Plan	60 days	Wed 11/10/27	Tue 2/1/28		
279						
280	<b>SCG - Local Single Family Solicitation</b>	<b>660 days</b>	<b>Sun 7/1/18</b>	<b>Thu 1/7/21</b>		
281	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18		
282	SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18		
283	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19		
284	SCG - RFA Evaluation	39 days	Mon 1/7/19	Thu 2/28/19		
285	SCG - RFA Review with EE PRG	1 day	Tue 3/5/19	Tue 3/5/19		
286	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19		
287	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19		
288	SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19		
289	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19		
290	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19		
291	SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19		
292	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
293	SCG - Contract Negotiation and Development	69 days	Mon 1/27/20	Thu 4/30/20		
294	SCG - Contract Review with EE PRG	14 days	Tue 5/5/20	Fri 5/22/20		
295	SCG - Final Award and Contract Signed	8 days	Mon 5/25/20	Wed 6/3/20		
296	SCG - Submit Advice Letter	96 days	Mon 6/1/20	Mon 10/12/20		
297	SCG - Advice Letter Approved	1 day	Thu 11/12/20	Thu 11/12/20		
298	SCG - Implementation Plan	41 days	Fri 11/13/20	Fri 1/8/21		
299	<b>SCG - Local Multi-family Solicitation</b>	<b>735 days</b>	<b>Sun 7/1/18</b>	<b>Thu 4/22/21</b>		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
300	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18		
301	SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18		
302	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19		
303	SCG - RFA Evaluation	59 days	Mon 1/7/19	Thu 3/28/19		
304	SCG - RFA Review with EE PRG	1 day	Tue 4/2/19	Tue 4/2/19		
305	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19		
306	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19		
307	SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19		
308	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19		
309	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19		
310	SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19		
311	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
312	SCG - Contract Negotiation and Development	155 days	Mon 1/27/20	Fri 8/28/20		
313	SCG - Contract Review with EE PRG	99 days	Tue 5/5/20	Fri 9/18/20		
314	SCG - Final Award and Contract Signed	8 days	Mon 9/21/20	Wed 9/30/20		
315	SCG - Submit Advice Letter	37 days	Thu 10/1/20	Fri 11/20/20		
316	SCG - Advice Letter Approved	1 day	Sun 5/2/21	Sun 5/2/21		
317	SCG - Implementation Plan	51 days	Mon 5/3/21	Mon 7/12/21		
318	<b>SCG - Local Small/Medium Commercial Solicitation</b>	<b>641 days</b>	<b>Tue 9/4/18</b>	<b>Tue 2/16/21</b>		
319	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19		
320	SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19		
321	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19		
322	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
323	SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19		
324	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19		
325	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19		
326	SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19		
327	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19		
328	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19		
329	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19		
330	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
331	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20		
332	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20		
333	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20		
334	SCG - Submit Advice Letter	59 days	Tue 9/1/20	Fri 11/20/20		
335	SCG - Advice Letter Approved	1 day	Fri 12/18/20	Fri 12/18/20		
336	SCG - Implementation Plan	43 days	Sat 12/19/20	Tue 2/16/21		
337	<b>SCG - Local Small/Medium Public Solicitation</b>	<b>631 days</b>	<b>Tue 9/4/18</b>	<b>Tue 2/2/21</b>		
338	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19		
339	SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19		
340	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19		
341	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19		
342	SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19		
343	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19		
344	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19		
345	SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
346	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19		
347	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19		
348	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19		
349	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
350	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20		
351	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20		
352	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20		
353	SCG - Submit Advice Letter	49 days	Tue 9/1/20	Fri 11/6/20		
354	SCG - Advice Letter Approved	1 day	Fri 12/4/20	Fri 12/4/20		
355	SCG - Implementation Plan	43 days	Sat 12/5/20	Tue 2/2/21		
356	<b>SCG - Statewide POS Food Service Solicitation</b>	<b>605 days</b>	<b>Mon 1/21/19</b>	<b>Fri 5/14/21</b>		
357	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19		
358	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19		
359	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19		
360	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19		
361	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19		
362	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20		
363	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19		
364	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20		
365	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20		
366	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20		
367	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20		
368	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
369	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20		
370	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20		
371	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20		
372	SCG - Submit Advice Letter	32 days	Mon 11/2/20	Tue 12/15/20		
373	SCG - Advice Letter Approved	1 day	Thu 1/14/21	Thu 1/14/21		
374	SCG - Implementation Plan	42 days	Fri 1/15/21	Mon 3/15/21		
375	<b>SCG - Statewide Midstream Water Heating Solicitation</b>	<b>597 days</b>	<b>Mon 1/21/19</b>	<b>Tue 5/4/21</b>		
376	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19		
377	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19		
378	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19		
379	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19		
380	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19		
381	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20		
382	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19		
383	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20		
384	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20		
385	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20		
386	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20		
387	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20		
388	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20		
389	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20		
390	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20		
391	SCG - Submit Advice Letter	25 days	Mon 11/2/20	Fri 12/4/20		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
392	SCG - Advice Letter Approved	1 day	Thu 3/18/21	Thu 3/18/21		
393	SCG - Implementation Plan	22 days	Fri 3/19/21	Mon 4/19/21		
394	<b>SCG - Statewide Gas Emerging Technology Solicitation</b>	<b>738 days</b>	<b>Wed 1/2/19</b>	<b>Fri 10/29/21</b>		
395	SCG - RFA Preparation	283 days	Wed 1/2/19	Fri 1/31/20		
396	SCG - RFA Release	1 day	Wed 2/12/20	Wed 2/12/20		
397	SCG - RFA Abstract Creation Duration	30 days	Thu 2/13/20	Wed 3/25/20		
398	SCG - RFA Evaluation	26 days	Thu 3/26/20	Thu 4/30/20		
399	SCG - RFA Review with EE PRG	1 day	Tue 5/5/20	Tue 5/5/20		
400	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 5/15/20	Fri 5/15/20		
401	SCG - RFP Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
402	SCG - RFP Release	1 day	Fri 8/21/20	Fri 8/21/20		
403	SCG - RFP Proposal Creation Duration	30 days	Mon 8/24/20	Fri 10/2/20		
404	SCG - RFP Evaluation	38 days	Mon 10/5/20	Wed 11/25/20		
405	SCG - RFP Review with EE PRG	1 day	Tue 12/1/20	Tue 12/1/20		
406	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 12/7/20	Mon 12/7/20		
407	SCG - Contract Negotiation and Development	85 days	Mon 1/4/21	Fri 4/30/21		
408	SCG - Contract Review with EE PRG	9 days	Tue 5/4/21	Fri 5/14/21		
409	SCG - Final Award and Contract Signed	29 days	Mon 5/17/21	Thu 6/24/21		
410	SCG - Submit Advice Letter	23 days	Sun 6/27/21	Tue 7/27/21		
411	SCG - Advice Letter Approved	1 day	Tue 8/24/21	Tue 8/24/21		
412	SCG - Implementation Plan	44 days	Wed 8/25/21	Sat 10/23/21		
413	<b>SCG - Local Manufactured Housing Solicitation</b>	<b>341 days</b>	<b>Fri 11/1/19</b>	<b>Fri 2/19/21</b>		
414	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
415	SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20		
416	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
417	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
418	SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20		
419	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20		
420	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
421	SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20		
422	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
423	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
424	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
425	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
426	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
427	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
428	SCG - Final Award and Contract Signed	9 days	Thu 12/10/20	Tue 12/22/20		
429	SCG - Submit Advice Letter	0 days	N/A	N/A		
430	SCG - Advice Letter Approved	0 days	N/A	N/A		
431	SCG - Implementation Plan	44 days	Tue 12/22/20	Fri 2/19/21		
432	<b>SCG - Local Large Commercial Solicitation</b>	<b>434 days</b>	<b>Fri 11/1/19</b>	<b>Wed 6/30/21</b>		
433	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		
434	SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20		
435	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
436	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
437	SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1	H2
438	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20		
439	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
440	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20		
441	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
442	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
443	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
444	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
445	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
446	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
447	SCG - Final Award and Contract Signed	10 days	Thu 12/10/20	Wed 12/23/20		
448	SCG - Submit Advice Letter	64 days	Fri 1/1/21	Wed 3/31/21		
449	SCG - Advice Letter Approved	1 day	Fri 6/4/21	Fri 6/4/21		
450	SCG - Implementation Plan	43 days	Sat 6/5/21	Tue 8/3/21		
451	<b>SCG - Local Agricultural Solicitation</b>	<b>434 days</b>	<b>Fri 11/1/19</b>	<b>Wed 6/30/21</b>		
452	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		
453	SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20		
454	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
455	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
456	SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20		
457	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20		
458	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
459	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20		
460	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
461	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
462	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
463	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
464	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
465	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
466	SCG - Final Award and Contract Signed	2 days	Fri 12/11/20	Mon 12/14/20		
467	SCG - Submit Advice Letter	41 days	Fri 1/1/21	Fri 2/26/21		
468	SCG - Advice Letter Approved	1 day	Wed 4/7/21	Wed 4/7/21		
469	SCG - Implementation Plan	43 days	Thu 4/8/21	Mon 6/7/21		
470	<b>SCG - Local Behavioral Solicitation - Residential</b>	<b>413 days?</b>	<b>Fri 5/1/20</b>	<b>Tue 11/30/21</b>		
471	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
472	SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20		
473	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20		
474	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20		
475	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20		
476	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20		
477	SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20		
478	SCG - RFP Release	1 day	Fri 1/15/21	Fri 1/15/21		
479	SCG - RFP Proposal Creation Duration	26 days	Mon 1/18/21	Mon 2/22/21		
480	SCG - RFP Evaluation	29 days	Tue 2/23/21	Fri 4/2/21		
481	SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21		
482	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/13/21	Tue 4/13/21		
483	SCG - Contract Negotiation and Development	95 days	Mon 4/26/21	Fri 9/3/21		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
484	SCG - Contract Review with EE PRG	9 days	Tue 9/7/21	Fri 9/17/21		
485	SCG - Final Award and Contract Signed	30 days	Mon 9/20/21	Fri 10/29/21		
486	SCG - Submit Advice Letter	21 days	Mon 11/1/21	Mon 11/29/21		
487	SCG - Advice Letter Approved	1 day	Wed 12/22/21	Wed 12/22/21		
488	SCG - Implementation Plan	43 days	Thu 12/23/21	Sun 2/20/22		
489	<b>SCG - Local Behavioral Solicitation - Commercial</b>	<b>413 days?</b>	<b>Fri 5/1/20</b>	<b>Tue 11/30/21</b>		
490	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
491	SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20		
492	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20		
493	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20		
494	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20		
495	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20		
496	SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20		
497	SCG - RFP Release	1 day	Fri 1/22/21	Fri 1/22/21		
498	SCG - RFP Proposal Creation Duration	26 days	Mon 1/25/21	Mon 3/1/21		
499	SCG - RFP Evaluation	24 days	Tue 3/2/21	Fri 4/2/21		
500	SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21		
501	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 11/12/21	Fri 11/12/21		
502	SCG - Contract Negotiation and Development	132 days	Mon 11/29/21	Tue 5/31/22		
503	SCG - Contract Review with EE PRG	8 days	Sun 6/5/22	Tue 6/14/22		
504	SCG - Final Award and Contract Signed	109 days	Fri 7/1/22	Wed 11/30/22		
505	SCG - Submit Advice Letter	23 days	N/A	N/A		
506	SCG - Advice Letter Approved	1 day	N/A	N/A		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
507	SCG - Implementation Plan	43 days	Thu 12/1/22	Sun 1/29/23		
508	<b>SCG - Local Industrial Solicitation</b>	<b>434 days?</b>	<b>Tue 12/1/20</b>	<b>Fri 7/29/22</b>		
509	SCG - RFA Preparation	63 days?	Tue 12/1/20	Thu 2/25/21		
510	SCG - RFA Release	1 day?	Fri 3/19/21	Fri 3/19/21		
511	SCG - RFA Abstract Creation Duration	25 days?	Mon 3/22/21	Fri 4/23/21		
512	SCG - RFA Evaluation	25 days?	Mon 4/26/21	Fri 5/28/21		
513	SCG - RFA Review with EE PRG	1 day?	Tue 6/1/21	Tue 6/1/21		
514	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 6/8/21	Tue 6/8/21		
515	SCG - RFP Preparation	67 days?	Thu 4/1/21	Fri 7/2/21		
516	SCG - RFP Release	1 day?	Fri 7/16/21	Fri 7/16/21		
517	SCG - RFP Proposal Creation Duration	30 days?	Mon 7/19/21	Fri 8/27/21		
518	SCG - RFP Evaluation	25 days?	Mon 8/30/21	Fri 10/1/21		
519	SCG - RFP Review with EE PRG	1 day?	Tue 10/5/21	Tue 10/5/21		
520	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 12/14/21	Tue 12/14/21		
521	SCG - Contract Negotiation and Development	127 days?	Thu 2/3/22	Fri 7/29/22		
522	SCG - Contract Review with EE PRG	9 days?	Tue 8/2/22	Fri 8/12/22		
523	SCG - Final Award and Contract Signed	21 days?	Fri 7/29/22	Fri 8/26/22		
524	SCG - Submit Advice Letter	1 day?	Sun 10/30/22	Sun 10/30/22		
525	SCG - Advice Letter Approved	1 day?	Mon 1/30/23	Mon 1/30/23		
526	SCG - Implementation Plan	45 days?	Tue 1/31/23	Sat 4/1/23		
527	<b>SCG - Large Public Sector Solicitation (re-Bid)</b>	<b>412 days</b>	<b>Mon 1/4/21</b>	<b>Tue 8/2/22</b>		
528	SCG - RFA Preparation	65 days	Mon 1/4/21	Fri 4/2/21		
529	SCG - RFA Release	1 day	Fri 7/16/21	Fri 7/16/21		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
530	SCG - RFA Abstract Creation Duration	20 days	Mon 7/19/21	Fri 8/13/21		
531	SCG - RFA Evaluation	15 days	Mon 8/16/21	Fri 9/3/21		
532	SCG - RFA Review with EE PRG	1 day	Tue 9/7/21	Tue 9/7/21		
533	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/14/21	Tue 9/14/21		
534	SCG - RFP Preparation	35 days	Mon 9/13/21	Fri 10/29/21		
535	SCG - RFP Release	1 day	Mon 11/8/21	Mon 11/8/21		
536	SCG - RFP Proposal Creation Duration	29 days	Tue 11/9/21	Fri 12/17/21		
537	SCG - RFP Evaluation	30 days	Mon 12/20/21	Fri 1/28/22		
538	SCG - RFP Review with EE PRG	1 day	Tue 2/1/22	Tue 2/1/22		
539	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/8/22	Tue 3/8/22		
540	SCG - Contract Negotiation and Development	79 days	Mon 3/14/22	Thu 6/30/22		
541	SCG - Contract Review with EE PRG	9 days	Tue 7/5/22	Fri 7/15/22		
542	SCG - Final Award and Contract Signed	63 days	Mon 7/18/22	Wed 10/12/22		
543	SCG - Submit Advice Letter	23 days	N/A	N/A		
544	SCG - Advice Letter Approved	1 day	N/A	N/A		
545	SCG - Implementation Plan	44 days	Wed 10/12/22	Sat 12/10/22		
546	<b>SCG - Outreach Solicitation</b>	<b>434 days</b>	<b>Mon 2/1/21</b>	<b>Thu 9/29/22</b>		
547	SCG - RFA Preparation	65 days	Mon 2/1/21	Fri 4/30/21		
548	SCG - RFA Release	1 day	Fri 5/21/21	Fri 5/21/21		
549	SCG - RFA Abstract Creation Duration	25 days	Mon 5/24/21	Fri 6/25/21		
550	SCG - RFA Evaluation	25 days	Mon 6/28/21	Fri 7/30/21		
551	SCG - RFA Review with EE PRG	1 day	Tue 8/3/21	Tue 8/3/21		
552	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/10/21	Tue 8/10/21		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
553	SCG - RFP Preparation	69 days	Tue 6/1/21	Fri 9/3/21		
554	SCG - RFP Release	1 day	Fri 9/17/21	Fri 9/17/21		
555	SCG - RFP Proposal Creation Duration	30 days	Mon 9/20/21	Fri 10/29/21		
556	SCG - RFP Evaluation	25 days	Mon 11/1/21	Fri 12/3/21		
557	SCG - RFP Review with EE PRG	1 day	Tue 12/7/21	Tue 12/7/21		
558	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 12/14/21	Tue 12/14/21		
559	SCG - Contract Negotiation and Development	54 days	Mon 1/17/22	Thu 3/31/22		
560	SCG - Contract Review with EE PRG	9 days	Tue 4/5/22	Fri 4/15/22		
561	SCG - Final Award and Contract Signed	10 days	Mon 4/18/22	Fri 4/29/22		
562	SCG - Submit Advice Letter	21 days	N/A	N/A		
563	SCG - Advice Letter Approved	1 day	N/A	N/A		
564	SCG - Implementation Plan	43 days	Sat 4/30/22	Tue 6/28/22		
565	<b>SCG - Marketplace Solicitation</b>	<b>436 days?</b>	<b>Mon 3/1/21</b>	<b>Mon 10/31/22</b>		
566	SCG - RFA Preparation	64 days	Sat 5/1/21	Wed 7/28/21		
567	SCG - RFA Release	1 day	Fri 8/20/21	Fri 8/20/21		
568	SCG - RFA Abstract Creation Duration	25 days	Mon 8/23/21	Fri 9/24/21		
569	SCG - RFA Evaluation	25 days	Mon 9/27/21	Fri 10/29/21		
570	SCG - RFA Review with EE PRG	1 day	Tue 11/2/21	Tue 11/2/21		
571	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/9/21	Tue 11/9/21		
572	SCG - RFP Preparation	91 days	Thu 8/26/21	Thu 12/30/21		
573	SCG - RFP Release	1 day	Fri 1/14/22	Fri 1/14/22		
574	SCG - RFP Proposal Creation Duration	30 days	Mon 1/17/22	Fri 2/25/22		
575	SCG - RFP Evaluation	25 days	Mon 2/28/22	Fri 4/1/22		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
576	SCG - RFP Review with EE PRG	1 day	Tue 5/3/22	Tue 5/3/22		
577	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 5/11/22	Wed 5/11/22		
578	SCG - Contract Negotiation and Development	117 days	Wed 6/22/22	Thu 12/1/22		
579	SCG - Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22		
580	SCG - Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22		
581	SCG - Submit Advice Letter	20 days	Tue 1/3/23	Mon 1/30/23		
582	SCG - Advice Letter Approved	1 day	Tue 5/2/23	Tue 5/2/23		
583	SCG - Implementation Plan	44 days	Wed 5/3/23	Sun 7/2/23		
584	<b>SCG - Residential Multi-Family - Whole Building</b>	<b>436 days?</b>	<b>Mon 3/1/21</b>	<b>Mon 10/31/22</b>		
585	RFA Preparation	40 days	Mon 1/10/22	Fri 3/4/22		
586	RFA Release	1 day	Fri 3/25/22	Fri 3/25/22		
587	RFA Abstract Creation Duration	25 days	Mon 3/28/22	Fri 4/29/22		
588	RFA Evaluation	25 days	Mon 5/2/22	Fri 6/3/22		
589	RFA Review with EE PRG	1 day	Tue 6/7/22	Tue 6/7/22		
590	RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/14/22	Tue 6/14/22		
591	RFP Preparation	28 days	Sun 5/1/22	Tue 6/7/22		
592	RFP Release	1 day	Fri 6/24/22	Fri 6/24/22		
593	RFP Proposal Creation Duration	52 days	Mon 6/27/22	Tue 9/6/22		
594	RFP Evaluation	11 days	Fri 9/9/22	Fri 9/23/22		
595	RFP Review with EE PRG	1 day	Thu 10/6/22	Thu 10/6/22		
596	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/11/22	Tue 10/11/22		
597	Contract Negotiation and Development	39 days	Tue 10/11/22	Fri 12/2/22		
598	Contract Review with EE PRG	1 day	Tue 12/6/22	Tue 12/6/22		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
599	Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22		
600	Submit Advice Letter	22 days	Mon 1/2/23	Tue 1/31/23		
601	Advice Letter Approved	1 day	Fri 3/31/23	Fri 3/31/23		
602	Implementation Plan	43 days	Sat 4/1/23	Tue 5/30/23		
603	<del>SCG – Youth Education Outreach Solicitation</del>	<del>331 days</del>	<del>Tue 3/1/22</del>	<del>Tue 6/6/23</del>		
604	<b>SCG - HERS Rater Training Solicitation</b>	<b>436 days?</b>	<b>Mon 3/1/21</b>	<b>Mon 10/31/22</b>		
605	RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22		
606	RFP Release	1 day	Fri 5/13/22	Fri 5/13/22		
607	RFP Proposal Creation Duration	20 days	Mon 5/16/22	Fri 6/10/22		
608	RFP Evaluation	59 days	Mon 6/13/22	Thu 9/1/22		
609	RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22		
610	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 8/31/22	Wed 8/31/22		
611	Contract Negotiation and Development	53 days	Fri 9/16/22	Tue 11/29/22		
612	Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22		
613	Final Award and Contract Signed	9 days	Mon 12/19/22	Thu 12/29/22		
614	Submit Advice Letter	N/A	N/A	N/A		
615	Advice Letter Approved	N/A	N/A	N/A		
616	Implementation Plan	42 days	Fri 12/30/22	Mon 2/27/23		
617	<b>SCG - Retail Partnering Solicitation</b>	<b>29 days?</b>	Tue 9/27/22	Fri 11/4/22		
618	RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22		
619	RFP Release	1 day	Fri 6/17/22	Fri 6/17/22		
620	RFP Proposal Creation Duration	30 days	Mon 6/20/22	Fri 7/29/22		
621	RFP Evaluation	24 days	Mon 8/1/22	Thu 9/1/22		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
622	RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22		
623	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/13/22	Tue 9/13/22		
624	Contract Negotiation and Development	29 days	Mon 9/19/22	Thu 10/27/22		
625	Contract Review with EE PRG	9 days	Tue 11/1/22	Fri 11/11/22		
626	Final Award and Contract Signed	13 days	Mon 11/14/22	Wed 11/30/22		
627	Submit Advice Letter	N/A	N/A	N/A		
628	Advice Letter Approved	N/A	N/A	N/A		
629	Implementation Plan	43 days	Sat 10/1/22	Tue 11/29/22		
630	<b>SCG - Non-Residential EE Advisor Solicitation</b>	<b>436 days?</b>	<b>Mon 3/1/21</b>	<b>Mon 10/31/22</b>		
631	RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22		
632	RFP Release	1 day	Fri 8/26/22	Fri 8/26/22		
633	RFP Proposal Creation Duration	20 days	Mon 8/29/22	Fri 9/23/22		
634	RFP Evaluation	16 days	Sat 9/24/22	Fri 10/14/22		
635	RFP Review with EE PRG	5 days	Mon 10/17/22	Fri 10/21/22		
636	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/25/22	Tue 10/25/22		
637	Contract Negotiation and Development	32 days	Sun 10/30/22	Mon 12/12/22		
638	Contract Review with EE PRG	9 days	Tue 12/13/22	Fri 12/23/22		
639	Final Award and Contract Signed	4 days	Tue 12/27/22	Fri 12/30/22		
640	Submit Advice Letter	N/A	N/A	N/A		
641	Advice Letter Approved	N/A	N/A	N/A		
642	Implementation Plan	44 days	Sun 1/1/23	Wed 3/1/23		
643	<b>SCG - Residential EE Kits Solicitation</b>	<b>436 days?</b>	<b>Mon 3/1/21</b>	<b>Mon 10/31/22</b>		
644	RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
645	RFP Release	1 day	Mon 7/25/22	Mon 7/25/22		
646	RFP Proposal Creation Duration	16 days	Tue 7/26/22	Tue 8/16/22		
647	RFP Evaluation	12 days	Wed 8/17/22	Thu 9/1/22		
648	RFP Review with EE PRG	1 day	Tue 8/2/22	Tue 8/2/22		
649	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/9/22	Tue 8/9/22		
650	Contract Negotiation and Development	30 days	Mon 8/22/22	Fri 9/30/22		
651	Contract Review with EE PRG	9 days	Tue 10/4/22	Fri 10/14/22		
652	Final Award and Contract Signed	10 days	Mon 10/17/22	Fri 10/28/22		
653	Submit Advice Letter	N/A	N/A	N/A		
654	Advice Letter Approved	N/A	N/A	N/A		
655	Implementation Plan	43 days	Sat 10/29/22	Tue 12/27/22		
656	<b>SCG - IDEEA 365</b>	<b>230 days</b>	<b>Mon 2/13/23</b>	<b>Fri 12/29/23</b>		
657	RFP Preparation	23 days	Mon 2/13/23	Wed 3/15/23		
658	RFP Release	20 days	Thu 4/20/23	Wed 5/17/23		
659	RFP Proposal Creation Duration	43 days	Wed 5/3/23	Fri 6/30/23		
660	RFP Evaluation	12 days	Fri 7/14/23	Mon 7/31/23		
661	RFP Review with EE PRG	1 day	Tue 8/1/23	Tue 8/1/23		
662	RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Tue 8/1/23	Thu 8/31/23		
663	Contract Negotiation and Development	21 days	Fri 9/1/23	Fri 9/29/23		
664	Contract Review with EE PRG	32 days	Mon 9/18/23	Tue 10/31/23		
665	Final Award and Contract Signed	17 days	Mon 10/9/23	Tue 10/31/23		
666	Submit Advice Letter	10 days	Wed 11/1/23	Tue 11/14/23		
667	Advice Letter Approved	11 days	Wed 11/22/23	Wed 12/6/23		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
668	Implementation Plan	9 days	Tue 12/19/23	Fri 12/29/23		
669	<b>SCG - Commercial SEM</b>	<b>110 days?</b>	<b>Tue 8/1/23</b>	<b>Mon 1/1/24</b>		
670	RFP Preparation	22 days	Tue 8/1/23	Wed 8/30/23		
671	RFP Release	13 days	Wed 9/13/23	Fri 9/29/23		
672	RFP Proposal Creation Duration	11 days	Mon 10/2/23	Mon 10/16/23		
673	RFP Evaluation	5 days	Wed 10/25/23	Tue 10/31/23		
674	RFP Review with EE PRG	2 days	Tue 10/31/23	Wed 11/1/23		
675	RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Thu 11/2/23	Wed 11/8/23		
676	Contract Negotiation and Development	16 days	Wed 10/25/23	Wed 11/15/23		
677	Contract Review with EE PRG	1 day	Tue 12/5/23	Tue 12/5/23		
678	Final Award and Contract Signed	6 days	Wed 12/13/23	Wed 12/20/23		
679	Submit Advice Letter	5 days	Mon 12/18/23	Fri 12/22/23		
680	Advice Letter Approved	1 day	Fri 12/29/23	Fri 12/29/23		
681	Implementation Plan	1 day	Mon 1/1/24	Mon 1/1/24		
682	<b>SCG - Market Access Program</b>	<b>333 days?</b>	<b>Sat 3/16/24</b>	<b>Tue 6/24/25</b>		
683	RFP Preparation	75 days	Sat 3/16/24	Thu 6/27/24		
684	RFP Release	1 day	Fri 6/21/24	Fri 6/21/24		
685	RFP Proposal Creation Duration	53 days	Mon 6/24/24	Wed 9/4/24		
686	RFP Evaluation	38 days	Mon 8/19/24	Wed 10/9/24		
687	RFP Review with EE PRG	1 day	Tue 10/1/24	Tue 10/1/24		
688	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/8/24	Tue 10/8/24		
689	Contract Negotiation and Development	78 days	Mon 10/14/24	Wed 1/29/25		
690	Contract Review with EE PRG	10 days	Tue 1/7/25	Mon 1/20/25		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
691	Final Award and Contract Signed	11 days	Mon 1/20/25	Mon 2/3/25		
692	Submit Advice Letter	N/A	Wed 1/1/25			
693	Advice Letter Approved	N/A	Mon 3/3/25			
694	Implementation Plan	59 days	Thu 4/3/25	Tue 6/24/25		
695	<b>SCG - IDEEA 365 (Round 3)</b>	<b>230 days?</b>	<b>Tue 10/15/24</b>	<b>Mon 9/1/25</b>		
696	RFP Preparation	23 days	Tue 10/15/24	Thu 11/14/24		
697	RFP Release	20 days	Fri 11/15/24	Thu 12/12/24		
698	RFP Proposal Creation Duration	43 days	Fri 12/13/24	Tue 2/11/25		
699	RFP Evaluation	12 days	Wed 2/12/25	Thu 2/27/25		
700	RFP Review with EE PRG	1 day	Fri 2/28/25	Fri 2/28/25		
701	RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Mon 3/3/25	Wed 4/2/25		
702	Contract Negotiation and Development	21 days	Thu 4/3/25	Thu 5/1/25		
703	Contract Review with EE PRG	32 days	Fri 5/2/25	Mon 6/16/25		
704	Final Award and Contract Signed	17 days	Tue 6/17/25	Wed 7/9/25		
705	Submit Advice Letter	10 days	Thu 7/10/25	Wed 7/23/25		
706	Advice Letter Approved	11 days	Thu 7/24/25	Thu 8/7/25		
707	Implementation Plan	9 days	Fri 8/8/25	Wed 8/20/25		
708						
709	<i>Please note the SDG&amp;E Solicitations marked with an * are estimated dates and are subject to change</i>					
710	<b>SDG&amp;E - Small Commercial (&lt;20kW) Solicitation</b>	<b>612 days</b>	<b>Wed 8/1/18</b>	<b>Thu 12/3/20</b>		
711	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18		
712	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18		
713	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
714	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19		
715	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19		
716	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19		
717	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19		
718	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19		
719	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19		
720	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19		
721	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20		
722	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20		
723	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20		
724	SDG&E - Contract Review with EE PRG	0 days	Tue 6/9/20	Tue 6/9/20		
725	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20		
726	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
727	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
728	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
729	<b>SDG&amp;E - Large Commercial (&gt;20kW) Solicitation</b>	<b>612 days</b>	<b>Wed 8/1/18</b>	<b>Thu 12/3/20</b>		
730	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18		
731	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18		
732	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18		
733	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19		
734	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19		
735	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19		
736	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
737	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19		
738	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19		
739	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19		
740	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20		
741	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20		
742	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20		
743	SDG&E - Contract Review with EE PRG	0 days	Tue 5/12/20	Tue 5/12/20		
744	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20		
745	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
746	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
747	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
748	<b>SDG&amp;E - Residential Multi-Family Solicitation</b>	<b>586 days</b>	<b>Thu 9/6/18</b>	<b>Thu 12/3/20</b>		
749	SDG&E - RFA Preparation	64 days	Thu 9/6/18	Tue 12/4/18		
750	SDG&E - RFA Release	23 days	Tue 12/4/18	Thu 1/3/19		
751	SDG&E - RFA Abstract Creation Duration	49 days	Tue 9/11/18	Fri 11/16/18		
752	SDG&E - RFA Evaluation	21 days	Mon 1/7/19	Mon 2/4/19		
753	SDG&E - RFA Review with EE PRG	0 days	Tue 11/13/18	Tue 11/13/18		
754	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 3/20/19	Wed 3/20/19		
755	SDG&E - RFP Preparation	63 days	Fri 3/22/19	Tue 6/18/19		
756	SDG&E - RFP Release	52 days	Tue 6/18/19	Wed 8/28/19		
757	SDG&E - RFP Proposal Creation Duration	36 days	Mon 3/25/19	Mon 5/13/19		
758	SDG&E - RFP Evaluation	30 days	Thu 8/29/19	Wed 10/9/19		
759	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Thu 12/12/19	Thu 12/19/19		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
760	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
761	SDG&E - Contract Negotiation and Development	35 days	Mon 4/13/20	Fri 5/29/20		
762	SDG&E - Contract Review with EE PRG	10 days	Thu 6/4/20	Wed 6/17/20		
763	SDG&E - Final Award and Contract Signed	0 days	Mon 6/22/20	Mon 6/22/20		
764	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
765	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
766	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
767	<b>SDG&amp;E - SW HVAC Solicitation</b>	<b>593 days</b>	<b>Thu 11/1/18</b>	<b>Tue 2/9/21</b>		
768	SDG&E - RFA Preparation	48 days	Thu 11/1/18	Mon 1/7/19		
769	SDG&E - RFA Release	0 days	Mon 1/7/19	Mon 1/7/19		
770	SDG&E - RFA Abstract Creation Duration	24 days	Mon 1/7/19	Thu 2/7/19		
771	SDG&E - RFA Evaluation	37 days	Fri 2/8/19	Sun 3/31/19		
772	SDG&E - RFA Review with EE PRG	0 days	Tue 4/9/19	Tue 4/9/19		
773	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 4/17/19	Wed 4/17/19		
774	SDG&E - RFP Preparation	73 days	Thu 4/18/19	Mon 7/29/19		
775	SDG&E - RFP Release	0 days	Tue 9/3/19	Tue 9/3/19		
776	SDG&E - RFP Proposal Creation Duration	30 days	Tue 9/3/19	Mon 10/14/19		
777	SDG&E - RFP Evaluation	33 days	Mon 10/14/19	Wed 11/27/19		
778	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20		
779	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
780	SDG&E - Contract Negotiation and Development	88 days	Wed 3/25/20	Fri 7/24/20		
781	SDG&E - Contract Review with EE PRG	0 days	Tue 9/8/20	Tue 9/8/20		
782	SDG&E - Final Award and Contract Signed	0 days	Fri 10/30/20	Fri 10/30/20		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1	H2
783	SDG&E - Submit Advice Letter	0 days	Thu 11/12/20	Thu 11/12/20		
784	SDG&E - Advice Letter Approved	0 days	Fri 12/11/20	Fri 12/11/20		
785	SDG&E - Implementation Plan	0 days	Tue 2/9/21	Tue 2/9/21		
786	<b>SDG&amp;E - SW PLA Solicitation</b>	<b>853 days</b>	<b>Mon 1/28/19</b>	<b>Wed 5/4/22</b>		
787	SDG&E - RFA Preparation	75 days	Mon 1/28/19	Fri 5/10/19		
788	SDG&E - RFA Release	0 days	Fri 5/10/19	Fri 5/10/19		
789	SDG&E - RFA Abstract Creation Duration	31 days	Fri 5/10/19	Fri 6/21/19		
790	SDG&E - RFA Evaluation	65 days	Mon 6/24/19	Fri 9/20/19		
791	SDG&E - RFA Review with EE PRG	0 days	Tue 9/10/19	Tue 9/10/19		
792	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 9/20/19	Fri 9/20/19		
793	SDG&E - RFP Preparation	52 days	Fri 9/20/19	Mon 12/2/19		
794	SDG&E - RFP Release	0 days	Mon 1/27/20	Mon 1/27/20		
795	SDG&E - RFP Proposal Creation Duration	31 days	Mon 1/27/20	Mon 3/9/20		
796	SDG&E - RFP Evaluation	82 days	Mon 3/9/20	Tue 6/30/20		
797	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/17/20	Mon 8/17/20		
798	SDG&E - Selection Review with EE PRG	66 days	Tue 10/13/20	Tue 1/12/21		
799	SDG&E - Contract Negotiation and Development	197 days	Fri 1/29/21	Mon 11/1/21		
800	SDG&E - Contract Review with EE PRG	0 days	Tue 11/9/21	Tue 11/9/21		
801	SDG&E - Final Award and Contract Signed	0 days	Fri 1/7/22	Fri 1/7/22		
802	SDG&E - Submit Advice Letter	0 days	Mon 1/10/22	Mon 1/10/22		
803	SDG&E - Advice Letter Approved	0 days	Thu 2/10/22	Thu 2/10/22		
804	SDG&E - Implementation Plan	60 days	Thu 2/10/22	Wed 5/4/22		
805	<b>SDG&amp;E - Residential Single-Family 2.0 Solicitation</b>	<b>467 days</b>	<b>Tue 1/19/21</b>	<b>Wed 11/2/22</b>		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
806	SDG&E - RFA Preparation	43 days	Tue 1/19/21	Thu 3/18/21		
807	SDG&E - RFA Release	0 days	Mon 3/22/21	Mon 3/22/21		
808	SDG&E - RFA Abstract Creation Duration	22 days	Mon 3/22/21	Tue 4/20/21		
809	SDG&E - RFA Evaluation	38 days	Wed 4/21/21	Fri 6/11/21		
810	SDG&E - RFA Review with EE PRG	7 days	Thu 6/3/21	Fri 6/11/21		
811	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 6/15/21	Tue 6/15/21		
812	SDG&E - RFP Preparation	43 days	Wed 6/16/21	Fri 8/13/21		
813	SDG&E - RFP Release	0 days	Wed 8/18/21	Wed 8/18/21		
814	SDG&E - RFP Proposal Creation Duration	32 days	Wed 8/18/21	Thu 9/30/21		
815	SDG&E - RFP Evaluation	44 days	Fri 10/1/21	Wed 12/1/21		
816	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 12/14/21	Tue 12/14/21		
817	SDG&E - Selection Review with EE PRG	7 days	Thu 12/2/21	Fri 12/10/21		
818	SDG&E - Contract Negotiation and Development	96 days	Mon 12/20/21	Mon 5/2/22		
819	SDG&E - Contract Review with EE PRG	7 days	Thu 5/5/22	Fri 5/13/22		
820	SDG&E - Final Award and Contract Signed	0 days	Tue 5/31/22	Tue 5/31/22		
821	SDG&E - Submit Advice Letter	0 days	Fri 6/24/22	Fri 6/24/22		
822	SDG&E - Advice Letter Approved	0 days	Thu 8/11/22	Thu 8/11/22		
823	SDG&E - Implementation Plan	60 days	Thu 8/11/22	Wed 11/2/22		
824	<b>SDG&amp;E - Residential Single-Family Solicitation</b>	<b>501 days</b>	<b>Mon 7/1/19</b>	<b>Tue 6/1/21</b>		
825	SDG&E - RFA Preparation	80 days	Mon 7/1/19	Fri 10/18/19		
826	SDG&E - RFA Release	35 days	Fri 10/18/19	Thu 12/5/19		
827	SDG&E - RFA Abstract Creation Duration	53 days	Mon 7/22/19	Wed 10/2/19		
828	SDG&E - RFA Evaluation	29 days	Fri 12/6/19	Wed 1/15/20		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
829	SDG&E - RFA Review with EE PRG	0 days	Tue 10/8/19	Tue 10/8/19		
830	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 2/27/20	Thu 2/27/20		
831	SDG&E - RFP Preparation	48 days	Fri 2/28/20	Tue 5/5/20		
832	SDG&E - RFP Release	0 days	Mon 4/27/20	Mon 4/27/20		
833	SDG&E - RFP Proposal Creation Duration	32 days	Mon 4/27/20	Tue 6/9/20		
834	SDG&E - RFP Evaluation	16 days	Wed 6/10/20	Wed 7/1/20		
835	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 7/23/20	Fri 7/24/20		
836	SDG&E - Selection Review with EE PRG	7 days	Thu 8/6/20	Fri 8/14/20		
837	SDG&E - Contract Negotiation and Development	60 days	Mon 8/17/20	Fri 11/6/20		
838	SDG&E - Contract Review with EE PRG	10 days	Tue 12/8/20	Mon 12/21/20		
839	SDG&E - Final Award and Contract Signed	0 days	Fri 1/29/21	Fri 1/29/21		
840	SDG&E - Submit Advice Letter	0 days	Mon 3/1/21	Mon 3/1/21		
841	SDG&E - Advice Letter Approved					
842	SDG&E - Implementation Plan	0 days	Tue 6/1/21	Tue 6/1/21		
843	<b>SDG&amp;E - Public Sector: Federal Solicitation</b>	<b>625 days</b>	<b>Mon 7/1/19</b>	<b>Fri 11/19/21</b>		
844	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19		
845	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19		
846	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19		
847	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20		
848	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
849	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20		
850	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20		
851	SDG&E - RFP Release	0 days	Fri 5/22/20	Fri 5/22/20		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
852	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20		
853	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20		
854	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20		
855	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20		
856	SDG&E - Contract Negotiation and Development	53 days	Wed 2/17/21	Fri 4/30/21		
857	SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21		
858	SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21		
859	SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21		
860	SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21		
861	SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21		
862	<b>SDG&amp;E - Public Sector: K-12 Solicitation</b>	<b>625 days</b>	<b>Mon 7/1/19</b>	<b>Fri 11/19/21</b>		
863	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19		
864	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19		
865	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19		
866	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20		
867	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
868	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20		
869	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20		
870	SDG&E - RFP Release	1 day	Fri 5/22/20	Fri 5/22/20		
871	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20		
872	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20		
873	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20		
874	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
875	SDG&E - Contract Negotiation and Development	117 days	Thu 11/19/20	Fri 4/30/21		
876	SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21		
877	SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21		
878	SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21		
879	SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21		
880	SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21		
881	<b>SDG&amp;E - Public Sector: Local Government Solicitation</b>	<b>338 days</b>	Tue 10/13/20	<b>Thu 1/27/22</b>		
882	SDG&E - RFA Preparation	10 days	Fri 10/23/20	Thu 11/5/20		
883	SDG&E - RFA Release	1 day	Wed 1/27/21	Wed 1/27/21		
884	SDG&E - RFA Abstract Creation Duration	20 days	Thu 1/28/21	Wed 2/24/21		
885	SDG&E - RFA Evaluation	18 days	Fri 2/26/21	Tue 3/23/21		
886	SDG&E - RFA Review with EE PRG	7 days	Thu 4/8/21	Fri 4/16/21		
887	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/21/21	Wed 4/21/21		
888	SDG&E - RFP Preparation	51 days	Fri 3/19/21	Fri 5/28/21		
889	SDG&E - RFP Release	1 day	Tue 6/1/21	Tue 6/1/21		
890	SDG&E - RFP Proposal Creation Duration	26 days	Wed 6/2/21	Wed 7/7/21		
891	SDG&E - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21		
892	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/25/21	Mon 10/25/21		
893	SDG&E - Selection Review with EE PRG	7 days	Tue 10/12/21	Wed 10/20/21		
894	SDG&E - Contract Negotiation and Development	41 days	Fri 11/5/21	Fri 12/31/21		
895	SDG&E - Contract Review with EE PRG	7 days	Thu 1/6/22	Fri 1/14/22		
896	SDG&E - Final Award and Contract Signed	9 days	Mon 1/17/22	Thu 1/27/22		
897	SDG&E - Submit Advice Letter	13 days	Wed 6/1/22	Fri 6/17/22		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
898	SDG&E - Advice Letter Approved	40 days	Fri 6/17/22	Thu 8/11/22		
899	SDG&E - Implementation Plan	42 days	Mon 8/15/22	Tue 10/11/22		
900	<b>SDG&amp;E - Agricultural Sector: Local Agriculture Solicitation</b>	<b>447 days</b>	<b>Mon 3/1/21</b>	<b>Tue 11/15/22</b>		
901	SDG&E - RFA Preparation	56 days	Mon 3/1/21	Mon 5/17/21		
902	SDG&E - RFA Release	0 days	Mon 4/26/21	Mon 4/26/21		
903	SDG&E - RFA Abstract Creation Duration	20 days	Tue 4/27/21	Mon 5/24/21		
904	SDG&E - RFA Evaluation	36 days	Tue 6/1/21	Tue 7/20/21		
905	SDG&E - RFA Review with EE PRG	0 days	Thu 7/8/21	Thu 7/8/21		
906	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 7/20/21	Tue 7/20/21		
907	SDG&E - RFP Preparation	48 days	Tue 7/20/21	Thu 9/23/21		
908	SDG&E - RFP Release	0 days	Thu 9/23/21	Thu 9/23/21		
909	SDG&E - RFP Proposal Creation Duration	25 days	Fri 9/24/21	Thu 10/28/21		
910	SDG&E - RFP Evaluation	23 days	Thu 10/28/21	Mon 11/29/21		
911	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 2/1/22	Tue 2/1/22		
912	SDG&E - Selection Review with EE PRG	0 days	Tue 2/8/22	Tue 2/8/22		
913	SDG&E - Contract Negotiation and Development	83 days	Tue 2/1/22	Thu 5/26/22		
914	SDG&E - Contract Review with EE PRG	0 days	Tue 6/14/22	Tue 6/14/22		
915	SDG&E - Final Award and Contract Signed	10 days	Fri 6/18/21	Thu 7/1/21		
916	SDG&E - Submit Advice Letter	0 days	Fri 7/22/22	Fri 7/22/22		
917	SDG&E - Advice Letter Approved	0 days	Tue 8/30/22	Tue 8/30/22		
918	SDG&E - Implementation Plan	44 days	Wed 8/31/22	Sat 10/29/22		
919	<b>*SDG&amp;E - Industrial Solicitation</b>	<b>426 days</b>	<b>Thu 4/1/21</b>	<b>Thu 11/17/22</b>		
920	SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
921	SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21		
922	SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21		
923	SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21		
924	SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21		
925	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21		
926	SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21		
927	SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21		
928	SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22		
929	SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22		
930	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22		
931	SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22		
932	SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22		
933	SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22		
934	SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22		
935	SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22		
936	SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22		
937	SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23		
938	<b>*SDG&amp;E - Industrial-Port Tenants Solicitation</b>	<b>426 days</b>	<b>Thu 4/1/21</b>	<b>Thu 11/17/22</b>		
939	SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21		
940	SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21		
941	SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21		
942	SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21		
943	SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
944	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21		
945	SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21		
946	SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21		
947	SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22		
948	SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22		
949	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22		
950	SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22		
951	SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22		
952	SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22		
953	SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22		
954	SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22		
955	SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22		
956	SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23		
957	<b>*SDG&amp;E - SW Residential HVAC QI/QM Solicitation</b>	<b>377 days</b>	<b>Mon 7/5/21</b>	<b>Tue 12/13/22</b>		
958	SDG&E - RFA Preparation	48 days	Mon 7/5/21	Wed 9/8/21		
959	SDG&E - RFA Release	1 day	Wed 9/29/21	Wed 9/29/21		
960	SDG&E - RFA Abstract Creation Duration	22 days	Wed 9/29/21	Thu 10/28/21		
961	SDG&E - RFA Evaluation	21 days	Fri 10/29/21	Fri 11/26/21		
962	SDG&E - RFA Review with EE PRG	6 days	Fri 12/10/21	Fri 12/17/21		
963	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 12/22/21	Wed 12/22/21		
964	SDG&E - RFP Preparation	56 days	Tue 1/4/22	Tue 3/22/22		
965	SDG&E - RFP Release	1 day	Tue 3/22/22	Tue 3/22/22		
966	SDG&E - RFP Proposal Creation Duration	23 days	Wed 3/23/22	Fri 4/22/22		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
967	SDG&E - RFP Evaluation	20 days	Mon 4/25/22	Fri 5/20/22		
968	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/21/22	Tue 6/21/22		
969	SDG&E - Selection Review with EE PRG	0 days	Fri 6/17/22	Fri 6/17/22		
970	SDG&E - Contract Negotiation and Development	83 days	Wed 7/20/22	Fri 11/11/22		
971	SDG&E - Contract Review with EE PRG	6 days	Mon 11/14/22	Mon 11/21/22		
972	SDG&E - Final Award and Contract Signed	1 day	Mon 1/10/22	Mon 1/10/22		
973	SDG&E - Submit Advice Letter	22 days	Sun 1/15/23	Mon 2/13/23		
974	SDG&E - Advice Letter Approved	1 day	Fri 4/28/23	Fri 4/28/23		
975	SDG&E - Implementation Plan	60 days	Fri 4/28/23	Thu 7/20/23		
976	<b>*SDG&amp;E - Local/Residential Behavioral Solicitation</b>	<b>472 days</b>	<b>Mon 4/19/21</b>	<b>Tue 2/7/23</b>		
977	SDG&E - RFA Preparation	53 days	Mon 4/19/21	Wed 6/30/21		
978	SDG&E - RFA Release	1 day	Mon 7/26/21	Mon 7/26/21		
979	SDG&E - RFA Abstract Creation Duration	21 days	Mon 7/26/21	Mon 8/23/21		
980	SDG&E - RFA Evaluation	30 days	Tue 8/24/21	Mon 10/4/21		
981	SDG&E - RFA Review with EE PRG	7 days	Thu 10/7/21	Fri 10/15/21		
982	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/19/21	Tue 10/19/21		
983	SDG&E - RFP Preparation	28 days	Thu 10/21/21	Mon 11/29/21		
984	SDG&E - RFP Release	1 day	Wed 12/22/21	Wed 12/22/21		
985	SDG&E - RFP Proposal Creation Duration	20 days	Wed 12/22/21	Tue 1/18/22		
986	SDG&E - RFP Evaluation	28 days	Wed 1/19/22	Fri 2/25/22		
987	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/15/22	Tue 3/15/22		
988	SDG&E - Selection Review with EE PRG	7 days	Thu 3/3/22	Fri 3/11/22		
989	SDG&E - Contract Negotiation and Development	119 days	Fri 3/18/22	Wed 8/31/22		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
990	SDG&E - Contract Review with EE PRG	7 days	Thu 9/8/22	Fri 9/16/22		
991	SDG&E - Final Award and Contract Signed	1 day	Fri 10/21/22	Fri 10/21/22		
992	SDG&E - Submit Advice Letter	1 day	Wed 11/16/22	Wed 11/16/22		
993	SDG&E - Advice Letter Approved	1 day	Fri 12/16/22	Fri 12/16/22		
994	SDG&E - Implementation Plan	60 days	Wed 11/16/22	Tue 2/7/23		
995	<b>*SDG&amp;E - Small Business Outreach Solicitation</b>	<b>298 days?</b>	<b>Wed 4/13/22</b>	<b>Fri 6/2/23</b>		
996	SDG&E - RFA Preparation	53 days	Wed 4/13/22	Fri 6/24/22		
997	SDG&E - RFA Release	1 day	Thu 7/7/22	Thu 7/7/22		
998	SDG&E - RFA Abstract Creation Duration	21 days	Fri 7/8/22	Fri 8/5/22		
999	SDG&E - RFA Evaluation	30 days	Mon 8/8/22	Fri 9/16/22		
1000	SDG&E - RFA Review with EE PRG	5 days	Mon 9/19/22	Fri 9/23/22		
1001	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/27/22	Tue 9/27/22		
1002	SDG&E - RFP Preparation	28 days	Mon 8/8/22	Wed 9/14/22		
1003	SDG&E - RFP Release	1 day	Tue 10/18/22	Tue 10/18/22		
1004	SDG&E - RFP Proposal Creation Duration	31 days	Tue 10/18/22	Tue 11/29/22		
1005	SDG&E - RFP Evaluation	38 days	Wed 11/30/22	Fri 1/20/23		
1006	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/28/23	Tue 2/28/23		
1007	SDG&E - Selection Review with EE PRG	7 days	Thu 2/16/23	Fri 2/24/23		
1008	SDG&E - Contract Negotiation and Development	79 days	Tue 2/28/23	Fri 6/16/23		
1009	SDG&E - Contract Review with EE PRG	4 days	Wed 6/21/23	Mon 6/26/23		
1010	SDG&E - Final Award and Contract Signed	1 day	Tue 8/29/23	Tue 8/29/23		
1011	SDG&E - Submit Advice Letter	1 day	Fri 9/15/23	Fri 9/15/23		
1012	SDG&E - Advice Letter Approved	1 day	Mon 10/16/23	Mon 10/16/23		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1013	SDG&E - Implementation Plan	46 days	Mon 10/16/23	Mon 12/18/23		
1014	<b>*SDG&amp;E - Workforce Education &amp; Training /Integrated Energy Education Solicitatio</b>	<b>353 days?</b>	<b>Mon 1/16/23</b>	<b>Wed 5/22/24</b>		
1015	SDG&E - RFP Release	1 day?	Thu 2/2/23	Thu 2/2/23		
1016	SDG&E - RFP Evaluation	25 days	Fri 3/17/23	Thu 4/20/23		
1017	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/16/23	Tue 5/16/23		
1018	SDG&E - Selection Review with EE PRG	5 days	Tue 5/9/23	Mon 5/15/23		
1019	SDG&E - Contract Negotiation and Development	94 days	Fri 5/5/23	Wed 9/13/23		
1020	SDG&E - Contract Review with EE PRG	7 days	Tue 10/10/23	Wed 10/18/23		
1021	SDG&E - Final Award and Contract Signed	1 day	Tue 11/14/23	Tue 11/14/23		
1022	SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24		
1023	SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24		
1024	SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24		
1025	<b>*SDG&amp;E - Residential Equity Education &amp; Outreach Solicitation</b>	<b>331 days?</b>	<b>Fri 1/13/23</b>	<b>Fri 4/19/24</b>		
1026	SDG&E - RFA Release	1 day	Thu 3/2/23	Thu 3/2/23		
1027	SDG&E - RFA Evaluation	21 days	Wed 4/12/23	Wed 5/10/23		
1028	SDG&E - RFA Review with EE PRG	7 days	Fri 5/19/23	Mon 5/29/23		
1029	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/30/23	Tue 5/30/23		
1030	SDG&E - RFP Release	1 day	Thu 6/1/23	Thu 6/1/23		
1031	SDG&E - RFP Evaluation	27 days	Mon 7/17/23	Tue 8/22/23		
1032	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/28/23	Mon 8/28/23		
1033	SDG&E - Selection Review with EE PRG	7 days	Wed 8/30/23	Thu 9/7/23		
1034	SDG&E - Contract Negotiation and Development	32 days	Thu 11/2/23	Fri 12/15/23		
1035	SDG&E - Contract Review with EE PRG	7 days	Tue 1/9/24	Wed 1/17/24		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1036	SDG&E - Final Award and Contract Signed	1 day	Mon 2/12/24	Mon 2/12/24		
1037	SDG&E - Submit Advice Letter	1 day	Mon 2/26/24	Mon 2/26/24		
1038	SDG&E - Advice Letter Approved	1 day	Mon 4/8/24	Mon 4/8/24		
1039	SDG&E - Implementation Plan	60 days	Tue 4/9/24	Mon 7/1/24		
1040	<b>*SDG&amp;E - Non-Residential Behavioral Solicitation</b>	<b>398 days</b>	<b>Mon 8/15/22</b>	<b>Wed 2/21/24</b>		
1041	SDG&E - RFA Preparation	67 days	Mon 8/15/22	Tue 11/15/22		
1042	SDG&E - RFA Release	1 day	Mon 10/24/22	Mon 10/24/22		
1043	SDG&E - RFA Abstract Creation Duration	27 days	Tue 8/23/22	Wed 9/28/22		
1044	SDG&E - RFA Evaluation	16 days	Tue 11/29/22	Tue 12/20/22		
1045	SDG&E - RFA Review with EE PRG	7 days	Thu 1/5/23	Fri 1/13/23		
1046	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 1/18/23	Wed 1/18/23		
1047	SDG&E - RFP Preparation	26 days	Mon 11/14/22	Mon 12/19/22		
1048	SDG&E - RFP Release	1 day	Mon 1/23/23	Mon 1/23/23		
1049	SDG&E - RFP Proposal Creation Duration	26 days	Mon 1/23/23	Mon 2/27/23		
1050	SDG&E - RFP Evaluation	58 days	Tue 2/28/23	Thu 5/18/23		
1051	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/20/23	Tue 6/20/23		
1052	SDG&E - Selection Review with EE PRG	7 days	Thu 6/8/23	Fri 6/16/23		
1053	SDG&E - Contract Negotiation and Development	60 days	Wed 6/21/23	Tue 9/12/23		
1054	SDG&E - Contract Review with EE PRG	7 days	Thu 10/5/23	Fri 10/13/23		
1055	SDG&E - Final Award and Contract Signed	1 day	Thu 12/21/23	Thu 12/21/23		
1056	SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24		
1057	SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24		
1058	SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1059	<b>*SDG&amp;E - Retail Offices and Wholesale Solicitation</b>	<b>419 days</b>	<b>Wed 5/10/23</b>	<b>Mon 12/16/24</b>		
1060	SDG&E - RFA Preparation	33 days	Wed 5/10/23	Fri 6/23/23		
1061	SDG&E - RFA Release	1 day	Mon 7/3/23	Mon 7/3/23		
1062	SDG&E - RFA Abstract Creation Duration	31 days	Tue 7/4/23	Tue 8/15/23		
1063	SDG&E - RFA Evaluation	19 days	Wed 8/16/23	Mon 9/11/23		
1064	SDG&E - RFA Review with EE PRG	3 days	Mon 9/18/23	Wed 9/20/23		
1065	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 9/25/23	Mon 9/25/23		
1066	SDG&E - RFP Preparation	33 days	Wed 7/5/23	Fri 8/18/23		
1067	SDG&E - RFP Release	1 day	Fri 9/29/23	Fri 9/29/23		
1068	SDG&E - RFP Proposal Creation Duration	33 days	Mon 10/2/23	Wed 11/15/23		
1069	SDG&E - RFP Evaluation	25 days	Thu 11/16/23	Wed 12/20/23		
1070	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 2/19/24	Mon 2/19/24		
1071	SDG&E - Selection Review with EE PRG	7 days	Thu 2/8/24	Fri 2/16/24		
1072	SDG&E - Contract Negotiation and Development	96 days	Mon 2/26/24	Mon 7/8/24		
1073	SDG&E - Contract Review with EE PRG	6 days	Wed 7/17/24	Wed 7/24/24		
1074	SDG&E - Final Award and Contract Signed	1 day	Tue 8/27/24	Tue 8/27/24		
1075	SDG&E - Submit Advice Letter	1 day	Mon 9/16/24	Mon 9/16/24		
1076	SDG&E - Advice Letter Approved	1 day	Wed 10/16/24	Wed 10/16/24		
1077	SDG&E - Implementation Plan	44 days	Wed 10/16/24	Mon 12/16/24		
1078	<b>*SDG&amp;E - Groceries, Restaurants and Food Storage Solicitation</b>	<b>467 days</b>	<b>Wed 6/14/23</b>	<b>Thu 3/27/25</b>		
1079	SDG&E - RFA Preparation	33 days	Wed 6/14/23	Fri 7/28/23		
1080	SDG&E - RFA Release	1 day	Tue 8/15/23	Tue 8/15/23		
1081	SDG&E - RFA Abstract Creation Duration	21 days	Wed 8/16/23	Wed 9/13/23		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1082	SDG&E - RFA Evaluation	15 days	Thu 9/14/23	Wed 10/4/23		
1083	SDG&E - RFA Review with EE PRG	5 days	Wed 10/18/23	Tue 10/24/23		
1084	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/30/23	Mon 10/30/23		
1085	SDG&E - RFP Preparation	16 days	Mon 10/9/23	Mon 10/30/23		
1086	SDG&E - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23		
1087	SDG&E - RFP Proposal Creation Duration	40 days	Mon 11/6/23	Fri 12/29/23		
1088	SDG&E - RFP Evaluation	34 days	Fri 12/29/23	Wed 2/14/24		
1089	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 3/6/24	Wed 3/6/24		
1090	SDG&E - Selection Review with EE PRG	7 days	Thu 2/29/24	Fri 3/8/24		
1091	SDG&E - Contract Negotiation and Development	144 days	Wed 3/13/24	Mon 9/30/24		
1092	SDG&E - Contract Review with EE PRG	6 days	Tue 10/8/24	Tue 10/15/24		
1093	SDG&E - Final Award and Contract Signed	1 day	Tue 11/26/24	Tue 11/26/24		
1094	SDG&E - Submit Advice Letter	1 day	Fri 12/27/24	Fri 12/27/24		
1095	SDG&E - Advice Letter Approved	1 day	Mon 1/27/25	Mon 1/27/25		
1096	SDG&E - Implementation Plan	44 days	Mon 1/27/25	Thu 3/27/25		
1097	<b>*SDG&amp;E - Private Institutions and Healthcare Solicitation</b>	<b>399 days</b>	<b>Thu 10/5/23</b>	<b>Tue 4/15/25</b>		
1098	SDG&E - RFA Preparation	33 days	Thu 10/5/23	Mon 11/20/23		
1099	SDG&E - RFA Release	1 day	Mon 11/27/23	Mon 11/27/23		
1100	SDG&E - RFA Abstract Creation Duration	35 days	Mon 11/27/23	Fri 1/12/24		
1101	SDG&E - RFA Evaluation	30 days	Mon 1/15/24	Fri 2/23/24		
1102	SDG&E - RFA Review with EE PRG	5 days	Mon 2/26/24	Fri 3/1/24		
1103	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 3/4/24	Mon 3/4/24		
1104	SDG&E - RFP Preparation	54 days	Mon 11/27/23	Thu 2/8/24		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1105	SDG&E - RFP Release	1 day	Fri 3/8/24	Fri 3/8/24		
1106	SDG&E - RFP Proposal Creation Duration	34 days	Fri 3/8/24	Wed 4/24/24		
1107	SDG&E - RFP Evaluation	42 days	Thu 4/25/24	Fri 6/21/24		
1108	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 7/2/24	Tue 7/2/24		
1109	SDG&E - Selection Review with EE PRG	7 days	Fri 6/21/24	Mon 7/1/24		
1110	SDG&E - Contract Negotiation and Development	61 days	Wed 7/31/24	Wed 10/23/24		
1111	SDG&E - Contract Review with EE PRG	4 days	Tue 11/12/24	Fri 11/15/24		
1112	SDG&E - Final Award and Contract Signed	1 day	Tue 12/17/24	Tue 12/17/24		
1113	SDG&E - Submit Advice Letter	1 day	Wed 1/15/25	Wed 1/15/25		
1114	SDG&E - Advice Letter Approved	1 day	Fri 2/14/25	Fri 2/14/25		
1115	SDG&E - Implementation Plan	43 days	Fri 2/14/25	Tue 4/15/25		
1116	<b>*SDG&amp;E - Lodging: Hotels/Motels Solicitation</b>	<b>400 days</b>	<b>Tue 10/10/23</b>	<b>Mon 4/21/25</b>		
1117	SDG&E - RFA Preparation	33 days	Tue 10/10/23	Thu 11/23/23		
1118	SDG&E - RFA Release	1 day	Fri 12/8/23	Fri 12/8/23		
1119	SDG&E - RFA Abstract Creation Duration	35 days	Fri 12/8/23	Thu 1/25/24		
1120	SDG&E - RFA Evaluation	22 days	Mon 1/22/24	Tue 2/20/24		
1121	SDG&E - RFA Review with EE PRG	7 days	Tue 3/12/24	Wed 3/20/24		
1122	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/19/24	Tue 3/19/24		
1123	SDG&E - RFP Preparation	48 days	Tue 1/23/24	Thu 3/28/24		
1124	SDG&E - RFP Release	1 day	Thu 3/21/24	Thu 3/21/24		
1125	SDG&E - RFP Proposal Creation Duration	29 days	Thu 3/21/24	Tue 4/30/24		
1126	SDG&E - RFP Evaluation	23 days	Mon 5/6/24	Wed 6/5/24		
1127	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/18/24	Tue 6/18/24		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1128	SDG&E - Selection Review with EE PRG	7 days	Thu 6/20/24	Fri 6/28/24		
1129	SDG&E - Contract Negotiation and Development	61 days	Wed 7/31/24	Wed 10/23/24		
1130	SDG&E - Contract Review with EE PRG	4 days	Tue 11/12/24	Fri 11/15/24		
1131	SDG&E - Final Award and Contract Signed	1 day	Tue 12/17/24	Tue 12/17/24		
1132	SDG&E - Submit Advice Letter	1 day	Thu 1/16/25	Thu 1/16/25		
1133	SDG&E - Advice Letter Approved	1 day	Thu 2/20/25	Thu 2/20/25		
1134	SDG&E - Implementation Plan	43 days	Thu 2/20/25	Mon 4/21/25		
1135	<b>*SDG&amp;E - Market Access Program (MAP)</b>	<b>326 days</b>	<b>Wed 3/13/24</b>	<b>Wed 6/11/25</b>		
1136	SDG&E - RFP Preparation	38 days	Wed 3/13/24	Fri 5/3/24		
1137	SDG&E - RFP Release	1 day	Tue 5/7/24	Tue 5/7/24		
1138	SDG&E - RFP Proposal Creation Duration	31 days	Tue 5/7/24	Tue 6/18/24		
1139	SDG&E - RFP Evaluation	43 days	Wed 6/19/24	Fri 8/16/24		
1140	SDG&E - Selection Review with EE PRG	7 days	Thu 9/5/24	Fri 9/13/24		
1141	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/17/24	Tue 9/17/24		
1142	SDG&E - Contract Negotiation and Development	60 days	Fri 9/27/24	Thu 12/19/24		
1143	SDG&E - Contract Review with EE PRG	3 days	Tue 12/10/24	Thu 12/12/24		
1144	SDG&E - Final Award and Contract Signed	1 day	Fri 1/31/25	Fri 1/31/25		
1145	SDG&E - Submit Advice Letter	1 day	Wed 3/12/25	Wed 3/12/25		
1146	SDG&E - Advice Letter Approved	1 day	Fri 4/11/25	Fri 4/11/25		
1147	SDG&E - Implementation Plan	44 days	Fri 4/11/25	Wed 6/11/25		
1148	Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change					
1149						
1150	<b>PG&amp;E - Local Government Partnerships (non-resource programs) Solicitation</b>	<b>376 days?</b>	<b>Fri 3/22/19</b>	<b>Fri 8/28/20</b>		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1151	PG&E - RFA Preparation	42 days	Fri 3/22/19	Mon 5/20/19		
1152	PG&E - RFA Release	1 day	Thu 5/23/19	Thu 5/23/19		
1153	PG&E - RFA Abstract Creation Duration	22 days	Thu 5/23/19	Fri 6/21/19		
1154	PG&E - RFA Evaluation	15 days	Mon 6/24/19	Fri 7/12/19		
1155	PG&E - RFA Review with EE PRG	4 days	Tue 7/23/19	Fri 7/26/19		
1156	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/5/19	Fri 8/9/19		
1157	PG&E - RFP Preparation	45 days	Tue 8/27/19	Mon 10/28/19		
1158	PG&E - RFP Release	1 day	Mon 11/4/19	Mon 11/4/19		
1159	PG&E - RFP Proposal Creation Duration	33 days	Mon 11/4/19	Wed 12/18/19		
1160	PG&E - RFP Evaluation	18 days	Mon 1/6/20	Wed 1/29/20		
1161	PG&E - RFP Review with EE PRG	4 days	Tue 2/25/20	Fri 2/28/20		
1162	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/2/20	Fri 3/6/20		
1163	PG&E - Contract Negotiation and Development	58 days	Fri 2/28/20	Tue 5/19/20		
1164	PG&E - Contract Review with EE PRG	7 days	Tue 5/26/20	Wed 6/3/20		
1165	PG&E - Final Award and Contract Signed	22 days	Fri 5/29/20	Mon 6/29/20		
1166	PG&E - Submit Advice Letter		N/A	N/A		
1167	PG&E - Advice Letter Approved					
1168	PG&E - Implementation Plan	24 days	Tue 7/28/20	Fri 8/28/20		
1169	<b>PG&amp;E - Statewide Codes &amp; Standards (RFP only) Solicitation</b>	<b>221 days?</b>	<b>Mon 7/8/19</b>	<b>Mon 5/11/20</b>		
1170	PG&E - RFA Preparation		N/A	N/A		
1171	PG&E - RFA Release		N/A	N/A		
1172	PG&E - RFA Abstract Creation Duration		N/A	N/A		
1173	PG&E - RFA Evaluation		N/A	N/A		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1174	PG&E - RFA Review with EE PRG		N/A	N/A		
1175	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A		
1176	PG&E - RFP Preparation	36 days	Mon 7/8/19	Mon 8/26/19		
1177	PG&E - RFP Release	1 day	Tue 9/10/19	Tue 9/10/19		
1178	PG&E - RFP Proposal Creation Duration	24 days	Tue 9/10/19	Fri 10/11/19		
1179	PG&E - RFP Evaluation	10 days	Mon 10/14/19	Fri 10/25/19		
1180	PG&E - RFP Review with EE PRG	4 days	Thu 11/21/19	Tue 11/26/19		
1181	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 11/27/19	Fri 11/29/19		
1182	PG&E - Contract Negotiation and Development	35 days	Mon 12/2/19	Fri 1/17/20		
1183	PG&E - Contract Review with EE PRG	4 days	Tue 1/21/20	Fri 1/24/20		
1184	PG&E - Final Award and Contract Signed	32 days	Wed 1/29/20	Thu 3/12/20		
1185	PG&E - Submit Advice Letter		N/A	N/A		
1186	PG&E - Advice Letter Approved					
1187	PG&E - Implementation Plan	32 days	Fri 3/27/20	Mon 5/11/20		
1188	<b>PG&amp;E - Local Multi-Sector (40% outsource) Solicitation</b>	<b>251 days?</b>	<b>Tue 4/28/20</b>	<b>Tue 4/13/21</b>		
1189	PG&E - RFA Preparation		N/A	N/A		
1190	PG&E - RFA Release		N/A	N/A		
1191	PG&E - RFA Abstract Creation Duration		N/A	N/A		
1192	PG&E - RFA Evaluation		N/A	N/A		
1193	PG&E - RFA Review with EE PRG		N/A	N/A		
1194	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A		
1195	PG&E - RFP Preparation		N/A	N/A		
1196	PG&E - RFP Release		N/A	N/A		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1197	PG&E - RFP Proposal Creation Duration		N/A	N/A		
1198	PG&E - RFP Evaluation		N/A	N/A		
1199	PG&E - RFP Review with EE PRG	4 days	Tue 4/28/20	Fri 5/1/20		
1200	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder					
1201	PG&E - Contract Negotiation and Development	81 days	Thu 7/2/20	Thu 10/22/20		
1202	PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20		
1203	PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20		
1204	PG&E - Submit Advice Letter	1 day	Wed 1/13/21	Wed 1/13/21		
1205	PG&E - Advice Letter Approved	1 day?	Fri 2/12/21	Fri 2/12/21		
1206	PG&E - Implementation Plan	43 days	Sat 2/13/21	Tue 4/13/21		
1207	<b>PG&amp;E - Statewide New Constructions (Non-Residential) Solicitation</b>	<b>591 days</b>	<b>Mon 3/25/19</b>	<b>Sun 6/27/21</b>		
1208	PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19		
1209	PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19		
1210	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19		
1211	PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19		
1212	PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19		
1213	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19		
1214	PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20		
1215	PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20		
1216	PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20		
1217	PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20		
1218	PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20		
1219	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1220	PG&E - Contract Negotiation and Development	49 days	Mon 8/17/20	Thu 10/22/20		
1221	PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20		
1222	PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20		
1223	PG&E - Submit Advice Letter	1 day	Fri 2/19/21	Fri 2/19/21		
1224	PG&E - Advice Letter Approved	1 day	Wed 4/28/21	Wed 4/28/21		
1225	PG&E - Implementation Plan	43 days	Thu 4/29/21	Sun 6/27/21		
1226	<b>PG&amp;E - Statewide New Construction (Residential) Solicitation</b>	<b>640 days?</b>	<b>Mon 3/25/19</b>	<b>Fri 9/3/21</b>		
1227	PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19		
1228	PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19		
1229	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19		
1230	PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19		
1231	PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19		
1232	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19		
1233	PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20		
1234	PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20		
1235	PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20		
1236	PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20		
1237	PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20		
1238	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20		
1239	PG&E - Contract Negotiation and Development	177 days	Mon 8/17/20	Tue 4/20/21		
1240	PG&E - Contract Review with EE PRG	16 days	Thu 4/22/21	Thu 5/13/21		
1241	PG&E - Final Award and Contract Signed	32 days	Sat 5/15/21	Mon 6/28/21		
1242	PG&E - Submit Advice Letter	1 day	Mon 7/12/21	Mon 7/12/21		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1243	PG&E - Advice Letter Approved (all electric)	1 day	Wed 8/11/21	Wed 8/11/21		
1244	PG&E - Advice Letter Approved (mixed fuel)	1 day	Wed 9/15/21	Wed 9/15/21		
1245	PG&E - Implementation Plan (all electric)	43 days	Thu 8/12/21	Mon 10/11/21		
1246	PG&E - Implementation Plan (mixed fuel)	43 days	Thu 9/16/21	Sun 11/14/21		
1247	<b>PG&amp;E - Statewide WE&amp;T Career Connections Solicitation</b>	<b>410 days?</b>	<b>Tue 1/7/20</b>	<b>Mon 8/2/21</b>		
1248	PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20		
1249	PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20		
1250	PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20		
1251	PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20		
1252	PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20		
1253	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20		
1254	PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20		
1255	PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20		
1256	PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20		
1257	PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20		
1258	PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20		
1259	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20		
1260	PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21		
1261	PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21		
1262	PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21		
1263	PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21		
1264	PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21		
1265	PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1266	<b>PG&amp;E - Statewide WE&amp;T Career and Workforce Readiness Solicitation</b>	<b>410 days?</b>	<b>Tue 1/7/20</b>	<b>Mon 8/2/21</b>		
1267	PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20		
1268	PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20		
1269	PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20		
1270	PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20		
1271	PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20		
1272	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20		
1273	PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20		
1274	PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20		
1275	PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20		
1276	PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20		
1277	PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20		
1278	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20		
1279	PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21		
1280	PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21		
1281	PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21		
1282	PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21		
1283	PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21		
1284	PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21		
1285	<b>PG&amp;E - Statewide State of CA (Dept. of Corrections) Solicitation</b>	<b>348 days?</b>	<b>Sun 3/1/20</b>	<b>Tue 6/29/21</b>		
1286	PG&E - RFA Preparation	46 days	Sun 3/1/20	Fri 5/1/20		
1287	PG&E - RFA Release	1 day	Wed 5/13/20	Wed 5/13/20		
1288	PG&E - RFA Abstract Creation Duration	31 days	Wed 5/13/20	Wed 6/24/20		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1289	PG&E - RFA Evaluation	15 days	Mon 6/29/20	Fri 7/17/20		
1290	PG&E - RFA Review with EE PRG	5 days	Tue 7/28/20	Mon 8/3/20		
1291	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/3/20	Fri 8/7/20		
1292	PG&E - RFP Preparation	20 days	Mon 8/3/20	Fri 8/28/20		
1293	PG&E - RFP Release	1 day	Wed 9/9/20	Wed 9/9/20		
1294	PG&E - RFP Proposal Creation Duration	31 days	Wed 9/9/20	Wed 10/21/20		
1295	PG&E - RFP Evaluation	31 days	Fri 10/23/20	Fri 12/4/20		
1296	PG&E - RFP Review with EE PRG	6 days	Tue 12/22/20	Tue 12/29/20		
1297	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 1/6/21	Fri 1/8/21		
1298	PG&E - Contract Negotiation and Development	65 days	Wed 1/20/21	Tue 4/20/21		
1299	PG&E - Contract Review with EE PRG	7 days	Thu 4/22/21	Fri 4/30/21		
1300	PG&E - Final Award and Contract Signed	22 days	Sat 5/1/21	Mon 5/31/21		
1301	PG&E - Submit Advice Letter	1 day	Thu 6/24/21	Thu 6/24/21		
1302	PG&E - Advice Letter Approved	1 day	Wed 7/28/21	Wed 7/28/21		
1303	PG&E - Implementation Plan	43 days	Thu 7/29/21	Sun 9/26/21		
1304	<b>PG&amp;E - Local (Micro and Small Business Equity Program) Solicitation</b>	<b>403 days?</b>	<b>Tue 6/1/21</b>	<b>Thu 12/15/22</b>		
1305	PG&E - RFA Preparation	38 days	Tue 6/1/21	Thu 7/22/21		
1306	PG&E - RFA Release	1 day	Tue 9/7/21	Tue 9/7/21		
1307	PG&E - RFA Abstract Creation Duration	34 days	Wed 9/8/21	Mon 10/25/21		
1308	PG&E - RFA Evaluation	18 days	Tue 10/26/21	Thu 11/18/21		
1309	PG&E - RFP Release	1 day	Wed 12/8/21	Wed 12/8/21		
1310	PG&E - RFP Proposal Creation Duration	46 days	Wed 12/8/21	Wed 2/9/22		
1311	PG&E - RFP Evaluation	21 days	Thu 2/10/22	Thu 3/10/22		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1	H2
1312	PG&E - RFP Review with EE PRG	6 days	Thu 3/17/22	Thu 3/24/22		
1313	PG&E - RFP Estimated Bidder Notification	1 day	Wed 3/30/22	Wed 3/30/22		
1314	PG&E - Contract Negotiation and Development	71 days	Thu 4/7/22	Thu 7/14/22		
1315	PG&E - Contract Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22		
1316	PG&E - Final Award and Contract Signed	45 days	Mon 8/8/22	Fri 10/7/22		
1317	PG&E - Submit Advice Letter	1 day	Wed 10/12/22	Wed 10/12/22		
1318	PG&E - Advice Letter Approved	1 day	Fri 11/11/22	Fri 11/11/22		
1319	PG&E - Implementation Plan	31 days	Fri 11/11/22	Fri 12/23/22		
1320	<b>PG&amp;E - Local (C&amp;S Compliance Improvement) Solicitation</b>	<b>436 days</b>	<b>Tue 3/1/22</b>	<b>Tue 10/31/23</b>		
1321	PG&E - RFA Preparation	34 days	Tue 3/1/22	Fri 4/15/22		
1322	PG&E - RFA Release	1 day	Mon 5/16/22	Mon 5/16/22		
1323	PG&E - RFA Abstract Creation Duration	25 days	Tue 5/17/22	Mon 6/20/22		
1324	PG&E - RFA Evaluation	28 days	Tue 6/21/22	Thu 7/28/22		
1325	PG&E - RFA Review with EE PRG	1 day	Tue 8/9/22	Tue 8/9/22		
1326	PG&E - RFA Estimated Bidder Notification	1 day	Wed 8/31/22	Wed 8/31/22		
1327	PG&E - RFP Preparation	24 days	Mon 8/1/22	Thu 9/1/22		
1328	PG&E - RFP Release	1 day	Tue 9/13/22	Tue 9/13/22		
1329	PG&E - RFP Proposal Creation Duration	26 days	Tue 9/13/22	Tue 10/18/22		
1330	PG&E - RFP Evaluation	45 days	Wed 10/19/22	Tue 12/20/22		
1331	PG&E - RFP Review with EE PRG	1 day	Tue 1/24/23	Tue 1/24/23		
1332	PG&E - RFP Estimated Bidder Notification	1 day	Fri 2/10/23	Fri 2/10/23		
1333	PG&E - Contract Negotiation and Development	47 days	Mon 2/13/23	Tue 4/18/23		
1334	PG&E - Contract Review with EE PRG	26 days	Tue 5/23/23	Tue 6/27/23		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1335	PG&E - Final Award and Contract Signed	48 days	Wed 6/28/23	Fri 9/1/23		
1336	PG&E - Submit Advice Letter		N/A			
1337	PG&E - Advice Letter Approved		N/A			
1338	PG&E - Implementation Plan	1 day	Tue 10/31/23	Tue 10/31/23		
1339	<b>PG&amp;E - Residential Electrification Equity Program Solicitation</b>	<b>595 days</b>	<b>Mon 8/1/22</b>	<b>Fri 11/8/24</b>		
1340	PG&E - RFA Preparation	59 days	Mon 8/1/22	Thu 10/20/22		
1341	PG&E - RFA Release	1 day	Tue 11/29/22	Tue 11/29/22		
1342	PG&E - RFA Abstract Creation Duration	46 days	Tue 11/29/22	Tue 1/31/23		
1343	PG&E - RFA Evaluation	17 days	Sun 2/5/23	Sun 2/26/23		
1344	PG&E - RFA Review with EE PRG	6 days	Mon 2/27/23	Mon 3/6/23		
1345	PG&E - RFA Estimated Bidder Notification	3 days	Mon 3/6/23	Wed 3/8/23		
1346	PG&E - RFP Preparation	46 days	Mon 1/9/23	Mon 3/13/23		
1347	PG&E - RFP Release	1 day	Tue 4/11/23	Tue 4/11/23		
1348	PG&E - RFP Proposal Creation Duration	26 days	Tue 4/11/23	Tue 5/16/23		
1349	PG&E - RFP Evaluation	18 days	Fri 5/19/23	Tue 6/13/23		
1350	PG&E - RFP Review with EE PRG	1 day	Tue 6/27/23	Tue 6/27/23		
1351	PG&E - RFP Estimated Bidder Notification	1 day	Tue 7/11/23	Tue 7/11/23		
1352	PG&E - Contract Negotiation and Development	233 days	Tue 8/1/23	Thu 6/20/24		
1353	PG&E - Contract Review with EE PRG	8 days	Fri 6/21/24	Tue 7/2/24		
1354	PG&E - Final Award and Contract Signed	21 days	Fri 7/5/24	Fri 8/2/24		
1355	PG&E - Submit Advice Letter	1 day	Fri 8/9/24	Fri 8/9/24		
1356	PG&E - Advice Letter Approved	1 day	Mon 9/9/24	Mon 9/9/24		
1357	PG&E - Implementation Plan	1 day	Fri 11/8/24	Fri 11/8/24		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1358	<b>PG&amp;E - Statewide C&amp;S Advocacy Solicitation</b>	<b>641 days</b>	<b>Tue 2/1/22</b>	<b>Tue 7/16/24</b>		
1359	PG&E - RFA Preparation	54 days	Tue 2/1/22	Fri 4/15/22		
1360	PG&E - RFA Release	1 day	Mon 5/30/22	Mon 5/30/22		
1361	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/31/22	Fri 7/1/22		
1362	PG&E - RFA Evaluation	14 days	Fri 7/1/22	Wed 7/20/22		
1363	PG&E - RFA Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22		
1364	PG&E - RFA Estimated Bidder Notification	1 day	Mon 8/1/22	Mon 8/1/22		
1365	PG&E - RFP Preparation	36 days	Fri 4/1/22	Fri 5/20/22		
1366	PG&E - RFP Release	1 day	Tue 6/7/22	Tue 6/7/22		
1367	PG&E - RFP Proposal Creation Duration	31 days	Tue 6/7/22	Tue 7/19/22		
1368	PG&E - RFP Evaluation	50 days	Wed 7/20/22	Tue 9/27/22		
1369	PG&E - RFP Review with EE PRG	1 day	Wed 10/5/22	Wed 10/5/22		
1370	PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/24/22	Mon 10/24/22		
1371	PG&E - Contract Negotiation and Development	73 days	Mon 11/14/22	Wed 2/22/23		
1372	PG&E - Contract Review with EE PRG - Wave 1	1 day	Tue 4/25/23	Tue 4/25/23		
1373	PG&E - Final Award and Contract Signed	18 days	Mon 7/17/23	Wed 8/9/23		
1374	PG&E - Submit Advice Letter (wave 1)	1 day	Thu 9/21/23	Thu 9/21/23		
1375	PG&E - Advice Letter Approved	1 day	Wed 10/25/23	Wed 10/25/23		
1376	PG&E - Implementation Plan	1 day	Thu 12/7/23	Thu 12/7/23		
1377	PG&E - Contract Review with EE PRG - Wave 2	1 day	Wed 12/20/23	Wed 12/20/23		
1378	PG&E - Final Award and Contract Signed	1 day	Fri 3/29/24	Fri 3/29/24		
1379	PG&E - Submit Advice Letter	1 day	Wed 4/17/24	Wed 4/17/24		
1380	PG&E - Advice Letter Approved	1 day	Fri 5/17/24	Fri 5/17/24		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1381	PG&E - Implementation Plan	1 day	Tue 7/16/24	Tue 7/16/24		
1382	<b>PG&amp;E - Zonal Electrification Solicitation</b>	<b>495 days</b>	<b>Thu 12/1/22</b>	<b>Wed 10/23/24</b>		
1383	PG&E - RFP Preparation	88 days	Thu 12/1/22	Mon 4/3/23		
1384	PG&E - RFP Release	1 day	Tue 4/18/23	Tue 4/18/23		
1385	PG&E - RFP Proposal Creation Duration	53 days	Tue 4/18/23	Thu 6/29/23		
1386	PG&E - RFP Evaluation (including interviews)	40 days	Mon 7/10/23	Fri 9/1/23		
1387	PG&E - RFP Review with EE PRG	1 day	Tue 9/26/23	Tue 9/26/23		
1388	PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/2/23	Mon 10/2/23		
1389	PG&E - Contract Negotiation and Development	135 days	Mon 10/9/23	Fri 4/12/24		
1390	PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24		
1391	PG&E - Final Award and Contract Signed	43 days	Wed 5/1/24	Fri 6/28/24		
1392	PG&E - Submit Advice Letter	1 day	Wed 7/3/24	Wed 7/3/24		
1393	PG&E - Advice Letter Approved	1 day	Wed 8/28/24	Wed 8/28/24		
1394	PG&E - Implementation Plan	1 day	Wed 10/23/24	Wed 10/23/24		
1395	<b>PG&amp;E - Residential Whole Home Load Management RFP</b>	<b>453 days</b>	<b>Tue 8/15/23</b>	<b>Thu 5/8/25</b>		
1396	PG&E - RFP Preparation	1 day	Tue 8/15/23	Tue 8/15/23		
1397	PG&E - RFP Release	1 day	Tue 8/15/23	Tue 8/15/23		
1398	PG&E - RFP Proposal Creation Duration	51 days	Tue 8/15/23	Tue 10/24/23		
1399	PG&E - RFP Evaluation	36 days	Thu 10/26/23	Thu 12/14/23		
1400	PG&E - RFP Review with EE PRG	1 day	Fri 2/16/24	Fri 2/16/24		
1401	PG&E - RFP Estimated Bidder Notification	1 day	Tue 2/27/24	Tue 2/27/24		
1402	PG&E - Contract Negotiation and Development	155 days	Wed 3/13/24	Tue 10/15/24		
1403	PG&E - Contract Review with EE PRG	8 days	Tue 11/5/24	Thu 11/14/24		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1404	PG&E - Final Award and Contract Signed	53 days	Thu 11/14/24	Mon 1/27/25		
1405	PG&E - Submit Advice Letter	1 day	Fri 2/7/25	Fri 2/7/25		
1406	PG&E - Advice Letter Approved	1 day	Mon 3/10/25	Mon 3/10/25		
1407	PG&E - Implementation Plan	1 day	Thu 5/8/25	Thu 5/8/25		
1408	<b>PG&amp;E - 2024 Summer Reliability Platform Administrator RFP</b>	<b>337 days?</b>	<b>Tue 4/18/23</b>	<b>Wed 7/31/24</b>		
1409	PG&E - RFP Preparation	30 days	Mon 5/1/23	Fri 6/9/23		
1410	PG&E - RFP Release	1 day	Fri 9/1/23	Fri 9/1/23		
1411	PG&E - RFP Proposal Creation Duration	31 days	Fri 9/1/23	Fri 10/13/23		
1412	PG&E - RFP Evaluation	22 days	Tue 10/17/23	Wed 11/15/23		
1413	PG&E - RFP Review with EE PRG	1 day	Tue 11/28/23	Tue 11/28/23		
1414	PG&E - RFP Estimated Bidder Notification	1 day	Tue 12/5/23	Tue 12/5/23		
1415	PG&E - Contract Negotiation and Development	68 days	Mon 1/8/24	Wed 4/10/24		
1416	PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24		
1417	PG&E - Final Award and Contract Signed	22 days	Wed 5/1/24	Thu 5/30/24		
1418	PG&E - Submit Advice Letter	1 day	Fri 5/31/24	Fri 5/31/24		
1419	PG&E - Advice Letter Approved	1 day	Mon 7/1/24	Mon 7/1/24		
1420	PG&E - Implementation Plan	1 day	Wed 7/31/24	Wed 7/31/24		
1421	<b>PG&amp;E - C&amp;S Code Readiness RFP</b>	<b>393 days?</b>	<b>Wed 2/1/23</b>	<b>Fri 8/2/24</b>		
1422	PG&E - RFP Preparation	113 days	Wed 2/1/23	Fri 7/7/23		
1423	PG&E - RFP Release	1 day	Wed 7/12/23	Wed 7/12/23		
1424	PG&E - RFP Proposal Creation Duration	30 days	Thu 7/13/23	Wed 8/23/23		
1425	PG&E - RFP Evaluation	36 days	Mon 8/28/23	Mon 10/16/23		
1426	PG&E - RFP Review with EE PRG	1 day	Tue 10/24/23	Tue 10/24/23		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1427	PG&E - RFP Estimated Bidder Notification	1 day	Mon 11/6/23	Mon 11/6/23		
1428	PG&E - Contract Negotiation and Development	65 days	Wed 11/15/23	Tue 2/13/24		
1429	PG&E - Contract Review with EE PRG	1 day	Tue 2/27/24	Tue 2/27/24		
1430	PG&E - Final Award and Contract Signed	1 day	Fri 4/12/24	Fri 4/12/24		
1431	PG&E - Submit Advice Letter	1 day	Tue 5/7/24	Tue 5/7/24		
1432	PG&E - Advice Letter Approved	1 day	Thu 6/6/24	Thu 6/6/24		
1433	PG&E - Implementation Plan	1 day	Fri 8/2/24	Fri 8/2/24		
1434	<b>PG&amp;E - Residential Electrification - Single Point of Contact</b>	<b>414 days</b>	<b>Tue 8/1/23</b>	<b>Fri 2/28/25</b>		
1435	PG&E - RFP Preparation	133 days	Tue 8/1/23	Thu 2/1/24		
1436	PG&E - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24		
1437	PG&E - RFP Proposal Creation Duration	33 days	Wed 2/28/24	Fri 4/12/24		
1438	PG&E - RFP Evaluation	66 days	Mon 4/15/24	Mon 7/15/24		
1439	PG&E - RFP Review with EE PRG	6 days	Fri 7/19/24	Fri 7/26/24		
1440	PG&E - RFP Estimated Bidder Notification	1 day	Wed 8/7/24	Wed 8/7/24		
1441	PG&E - Contract Negotiation and Development	62 days				
1442	PG&E - Contract Review with EE PRG	6 days				
1443	PG&E - Final Award and Contract Signed	25 days				
1444	PG&E - Submit Advice Letter	1 day				
1445	PG&E - Advice Letter Approved	1 day				
1446	PG&E - Implementation Plan	1 day				
1447	<b>PG&amp;E - Commercial SEM FP</b>	<b>430 days</b>	<b>Thu 8/3/23</b>	<b>Wed 3/26/25</b>		
1448	PG&E - RFP Preparation	16 days	Thu 8/3/23	Thu 8/24/23		
1449	PG&E - RFP Release	1 day	Fri 11/3/23	Fri 11/3/23		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1	H2
1450	PG&E - RFP Proposal Creation Duration	55 days	Fri 11/3/23	Thu 1/18/24		
1451	PG&E - RFP Evaluation	58 days	Tue 1/23/24	Thu 4/11/24		
1452	PG&E - RFP Review with EE PRG	1 day	Wed 4/17/24	Wed 4/17/24		
1453	PG&E - RFP Estimated Bidder Notification	4 days	Tue 4/23/24	Fri 4/26/24		
1454	PG&E - Contract Negotiation and Development	90 days	Thu 5/2/24	Wed 9/4/24		
1455	PG&E - Contract Review with EE PRG	8 days	Mon 9/16/24	Wed 9/25/24		
1456	PG&E - Final Award and Contract Signed	58 days	Thu 9/26/24	Mon 12/16/24		
1457	PG&E - Submit Advice Letter	1 day	Thu 12/19/24	Thu 12/19/24		
1458	PG&E - Advice Letter Approved	0 days	Thu 1/30/25	Thu 1/30/25		
1459	PG&E - Implementation Plan	1 day	Wed 3/26/25	Wed 3/26/25		
1460	<b>PG&amp;E - SW WE&amp;T Career &amp; Workforce Readiness</b>	<b>610 days</b>	<b>Tue 10/8/24</b>	<b>Mon 2/8/27</b>		
1461	PG&E - RFP Preparation	199 days	Tue 10/8/24	Fri 7/11/25		
1462	PG&E - RFP Release	1 day	Thu 7/17/25	Thu 7/17/25		
1463	PG&E - RFP Proposal Creation Duration	41 days	Thu 7/17/25	Thu 9/11/25		
1464	PG&E - RFP Evaluation	50 days	Mon 9/15/25	Fri 11/21/25		
1465	PG&E - RFP Review with EE PRG	4 days	Fri 12/5/25	Wed 12/10/25		
1466	PG&E - RFP Estimated Bidder Notification	4 days	Wed 12/10/25	Mon 12/15/25		
1467	PG&E - Contract Negotiation and Development	157 days	Wed 1/7/26	Thu 8/13/26		
1468	PG&E - Contract Review with EE PRG	14 days	Thu 8/13/26	Tue 9/1/26		
1469	PG&E - Final Award and Contract Signed	45 days	Tue 9/1/26	Sun 11/1/26		
1470	PG&E - Submit Advice Letter	1 day	Tue 11/10/26	Tue 11/10/26		
1471	PG&E - Advice Letter Approved	1 day	Thu 12/10/26	Thu 12/10/26		
1472	PG&E - Implementation Plan	43 days	Thu 12/10/26	Mon 2/8/27		


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1	H2
1473	<b>PG&amp;E - Statewide HVAC</b>	<b>454 days</b>	<b>Fri 5/2/25</b>	<b>Wed 1/27/27</b>		
1474	PG&E - RFP Preparation	122 days	Fri 5/2/25	Mon 10/20/25		
1475	PG&E - RFP Release	1 day	Wed 10/22/25	Wed 10/22/25		
1476	PG&E - RFP Proposal Creation Duration	41 days	Wed 10/22/25	Wed 12/17/25		
1477	PG&E - RFP Evaluation	32 days	Thu 12/18/25	Fri 1/30/26		
1478	PG&E - RFP Review with EE PRG	1 day	Thu 3/26/26	Thu 3/26/26		
1479	PG&E - RFP Estimated Bidder Notification	1 day	Mon 4/6/26	Mon 4/6/26		
1480	PG&E - Contract Negotiation and Development	90 days	Tue 4/7/26	Mon 8/10/26		
1481	PG&E - Contract Review with EE PRG	2 days	Tue 8/25/26	Wed 8/26/26		
1482	PG&E - Final Award and Contract Signed	1 day	Mon 10/26/26	Mon 10/26/26		
1483	PG&E - Submit Advice Letter	1 day	Tue 10/27/26	Tue 10/27/26		
1484	PG&E - Advice Letter Approved	1 day	Fri 11/27/26	Fri 11/27/26		
1485	PG&E - Implementation Plan	44 days	Fri 11/27/26	Wed 1/27/27		

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

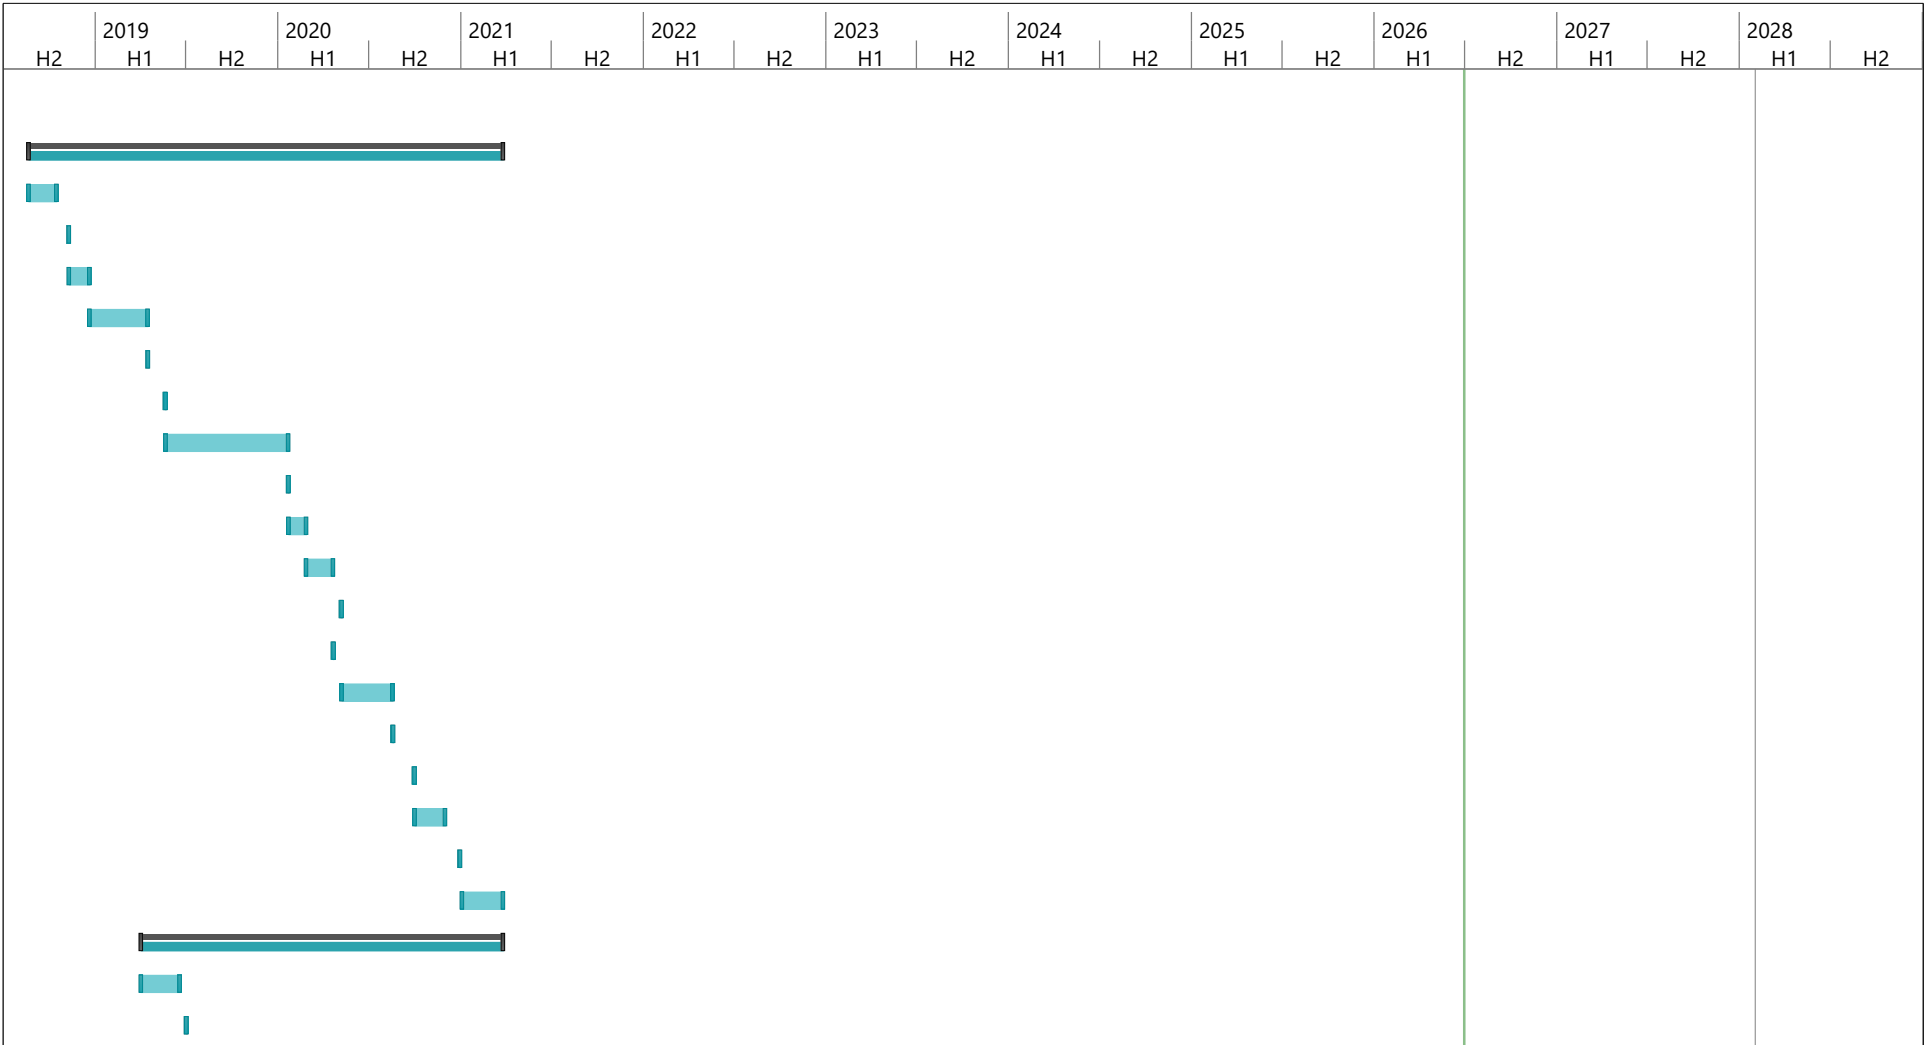


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

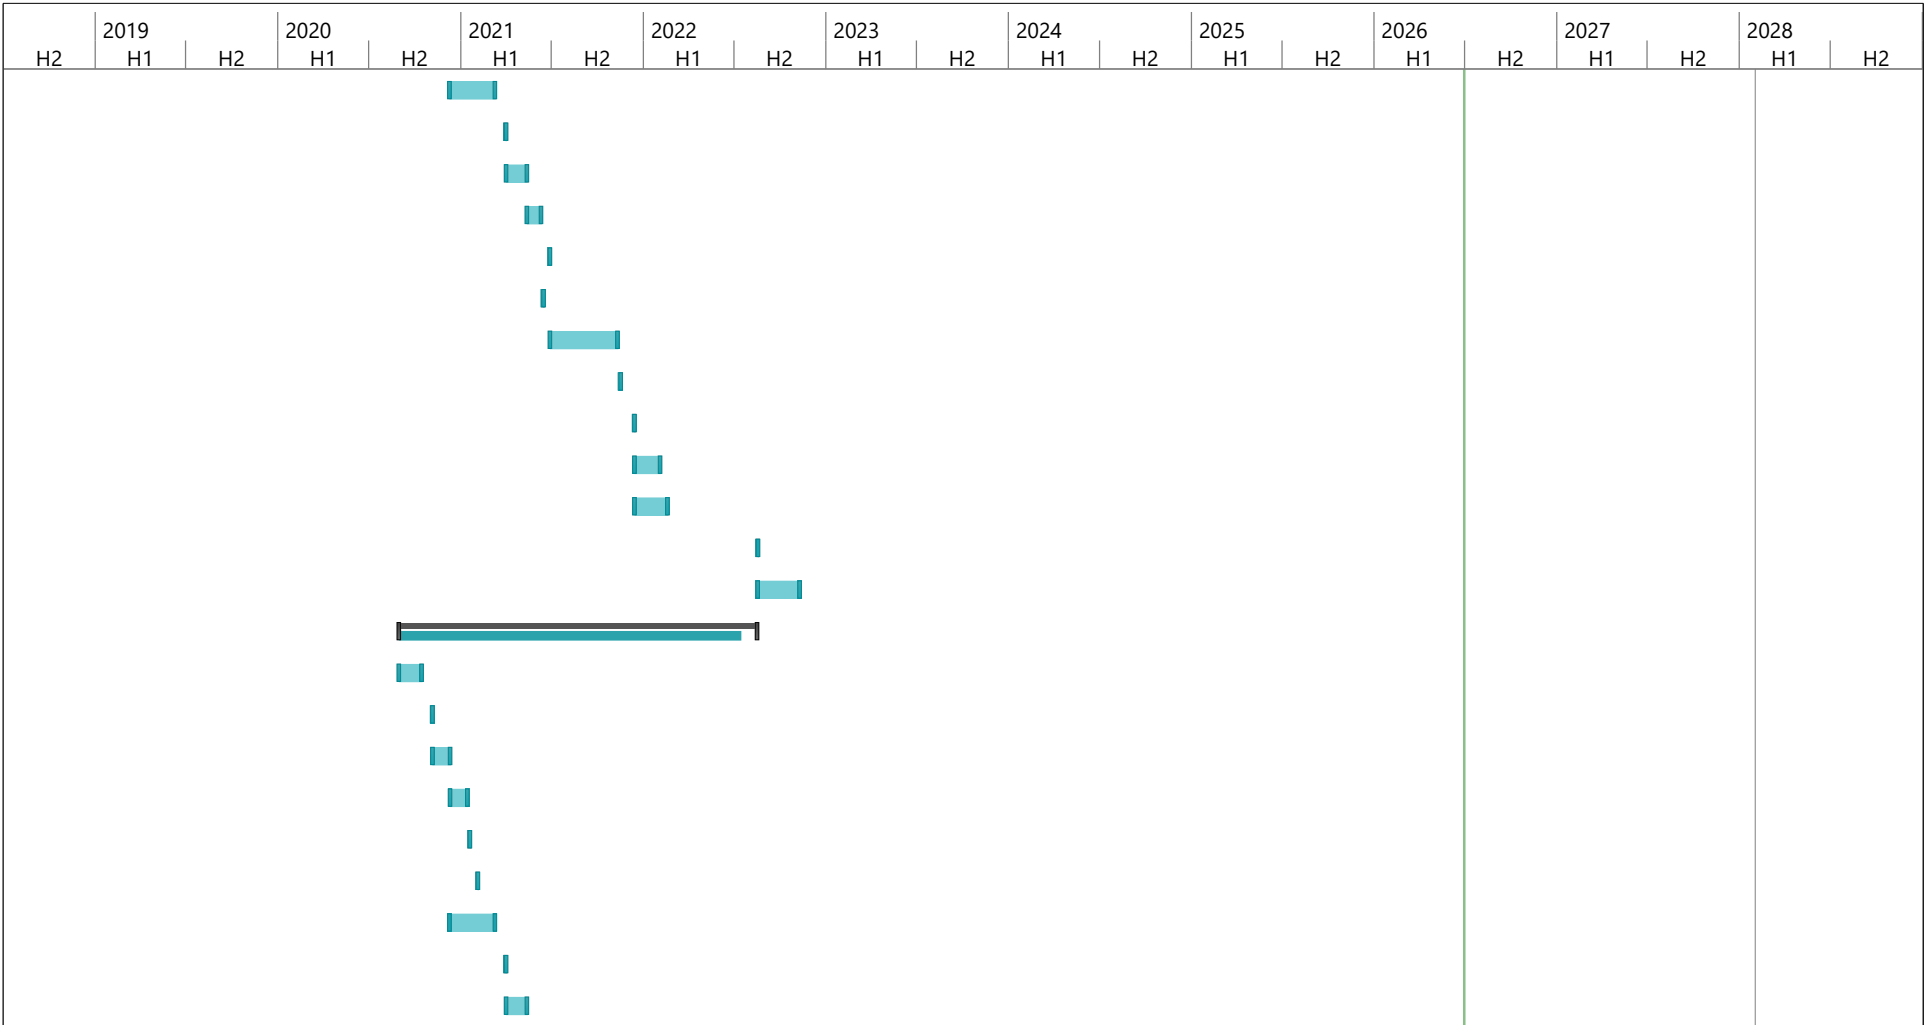


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

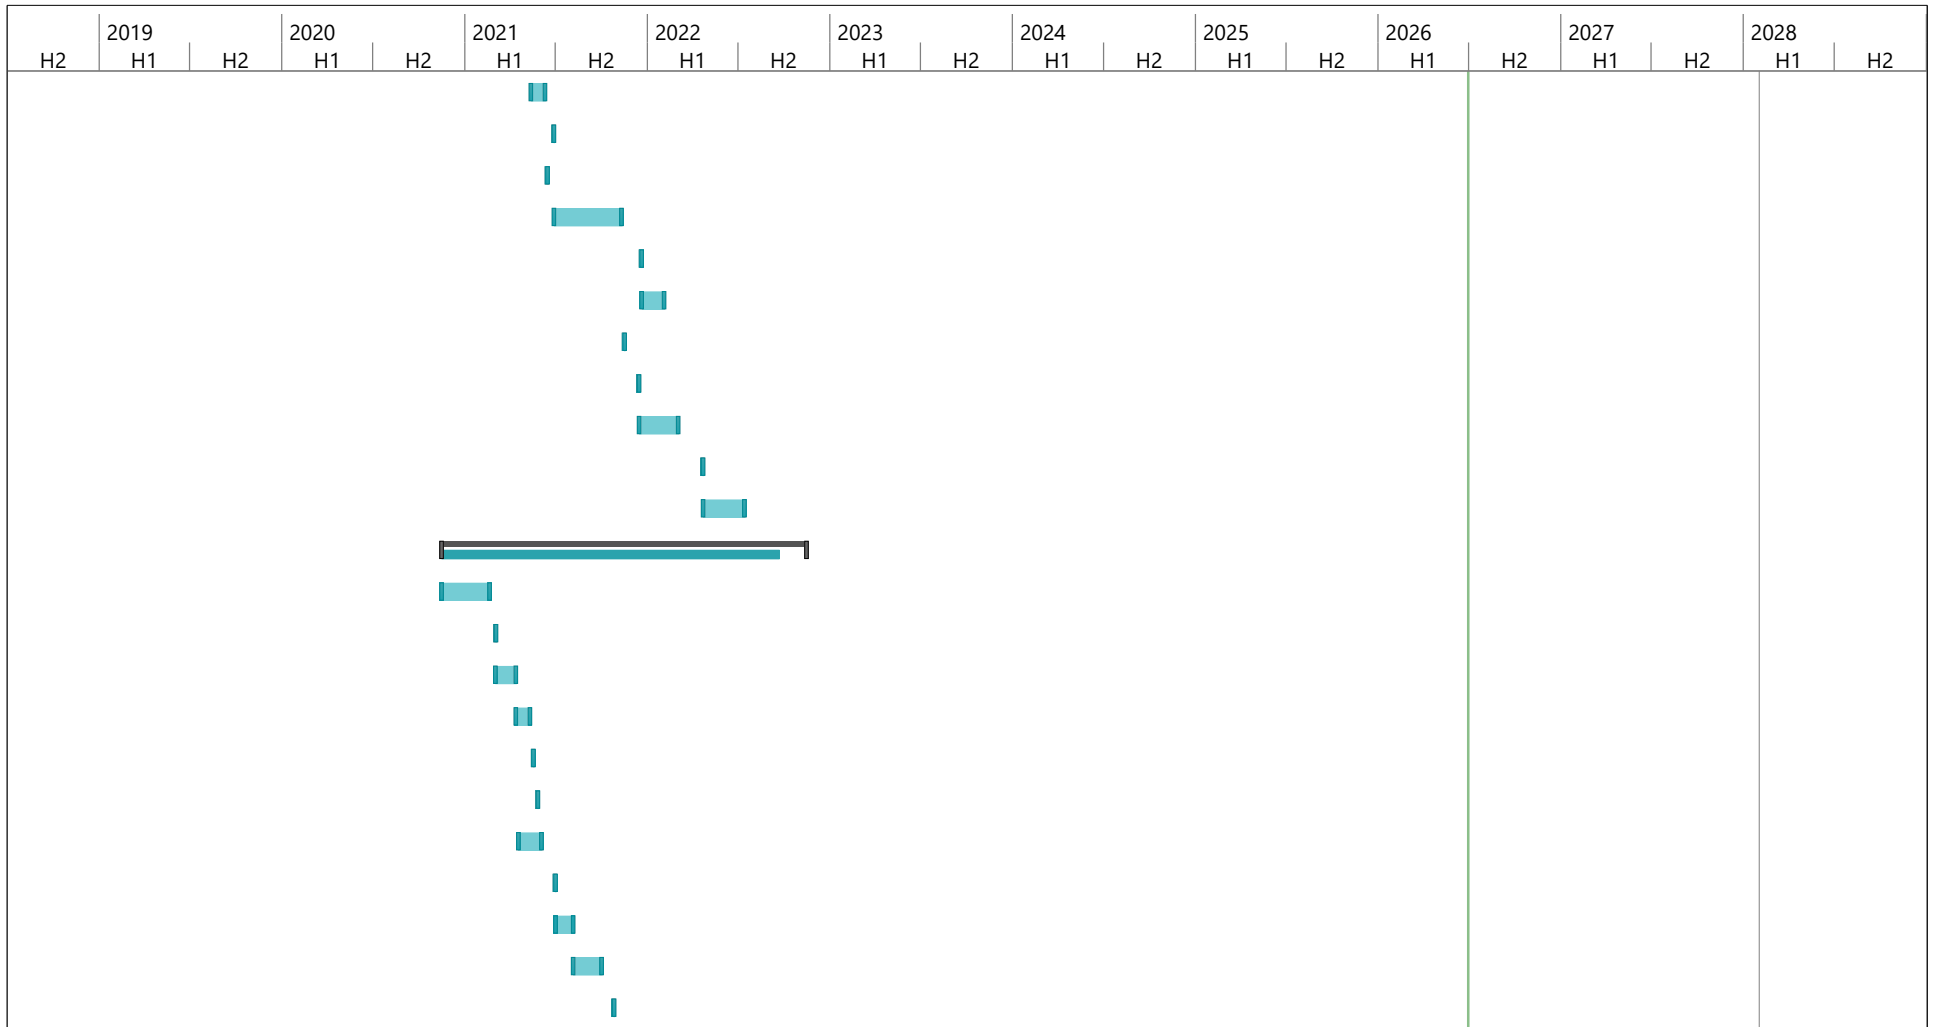


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

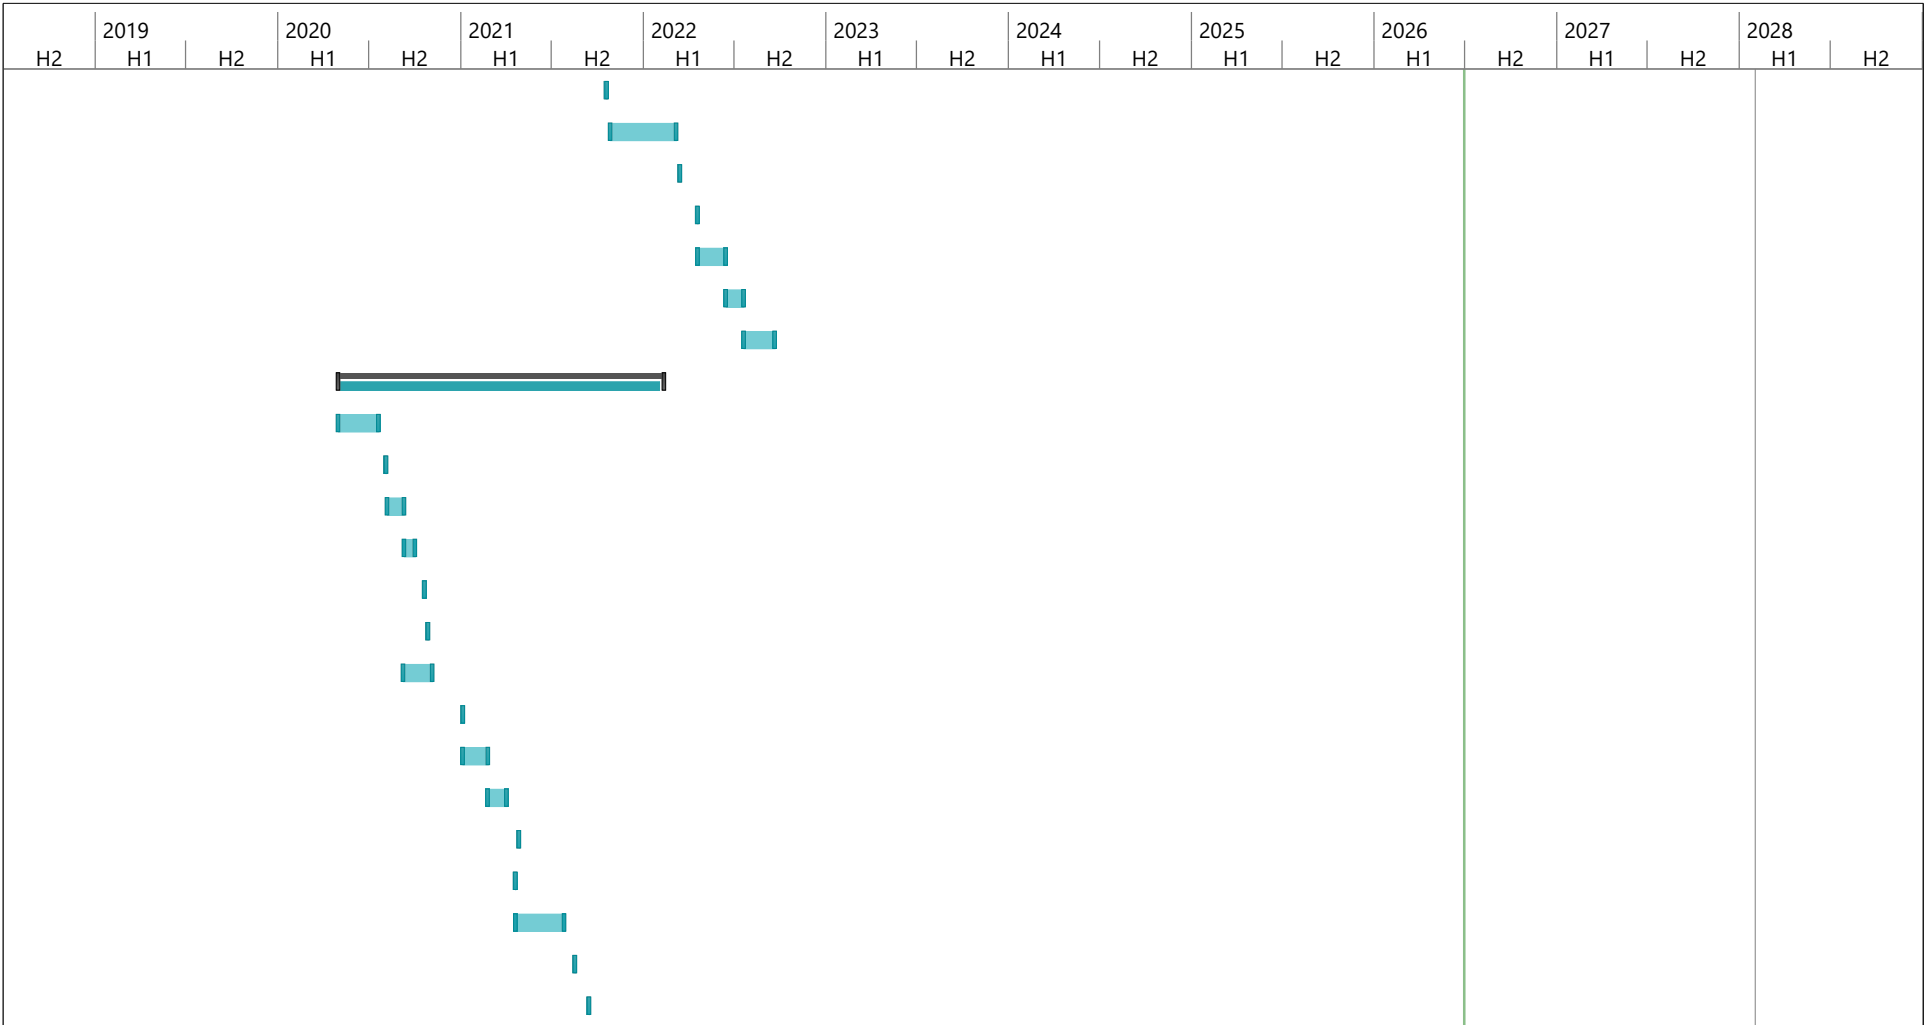


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

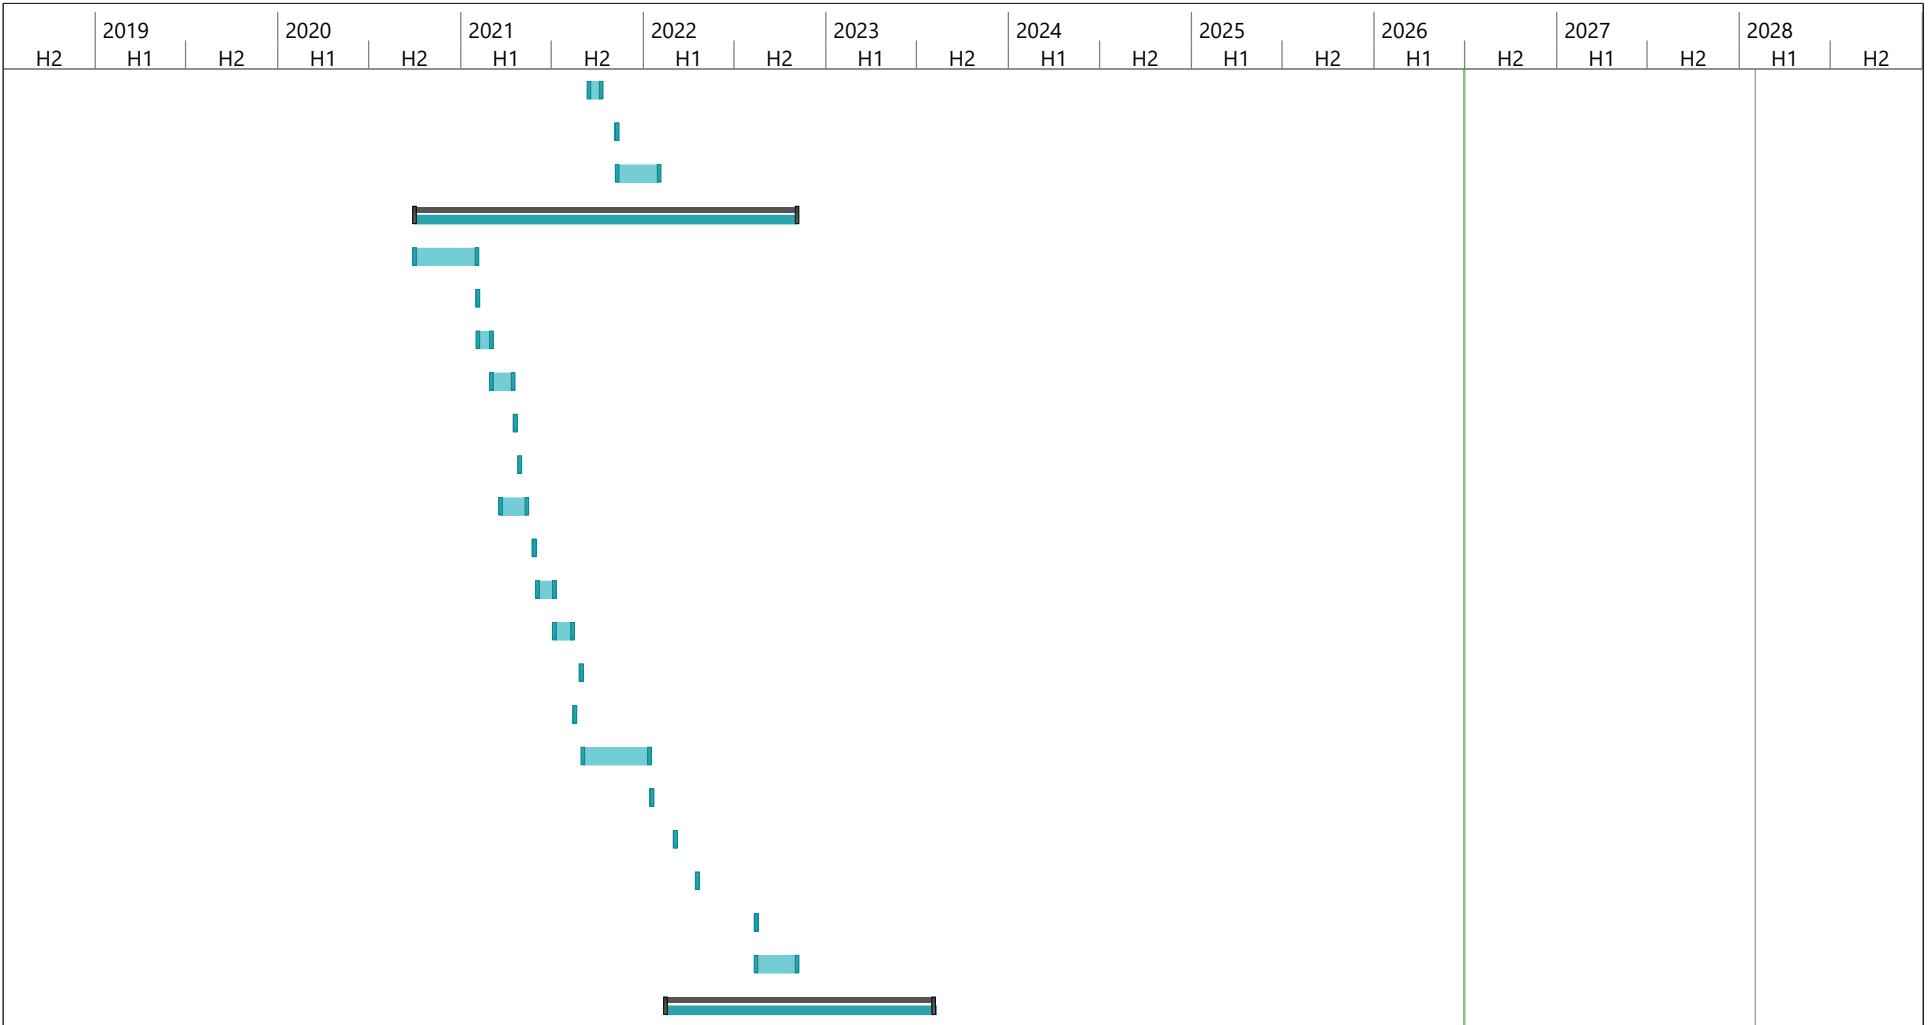


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

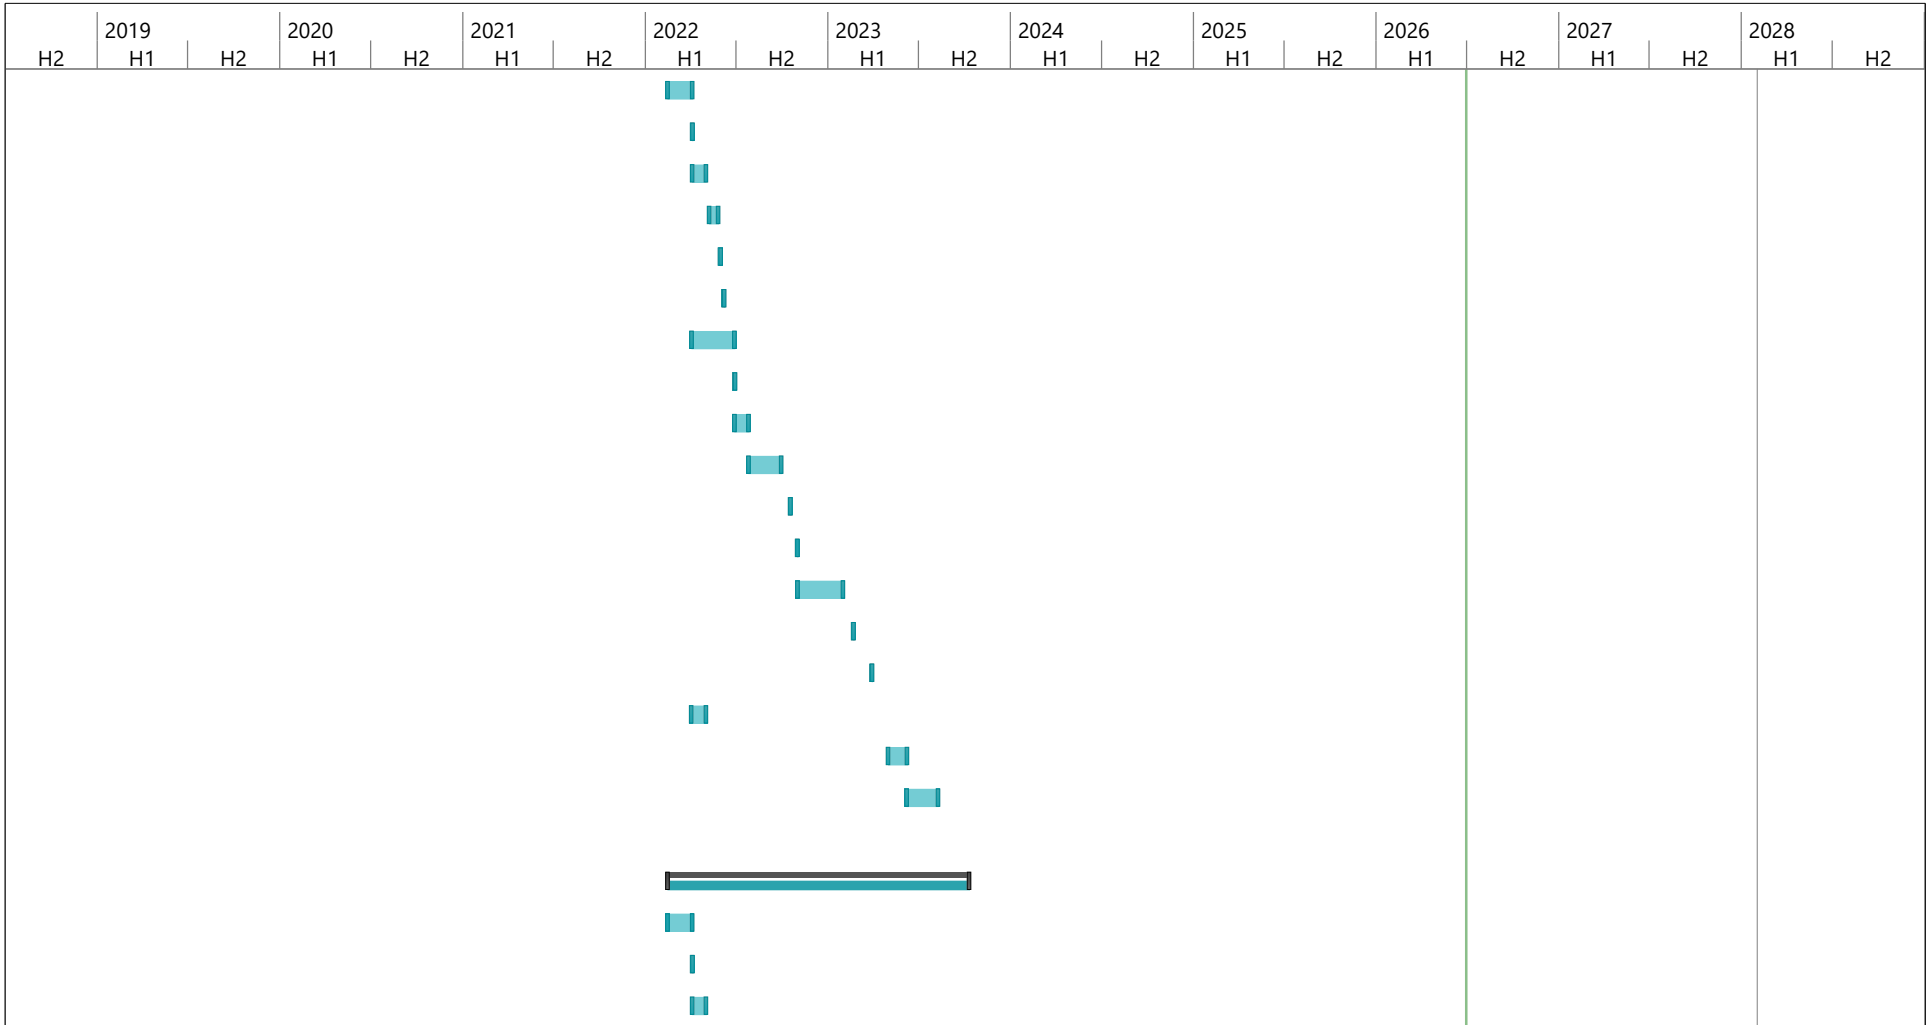


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

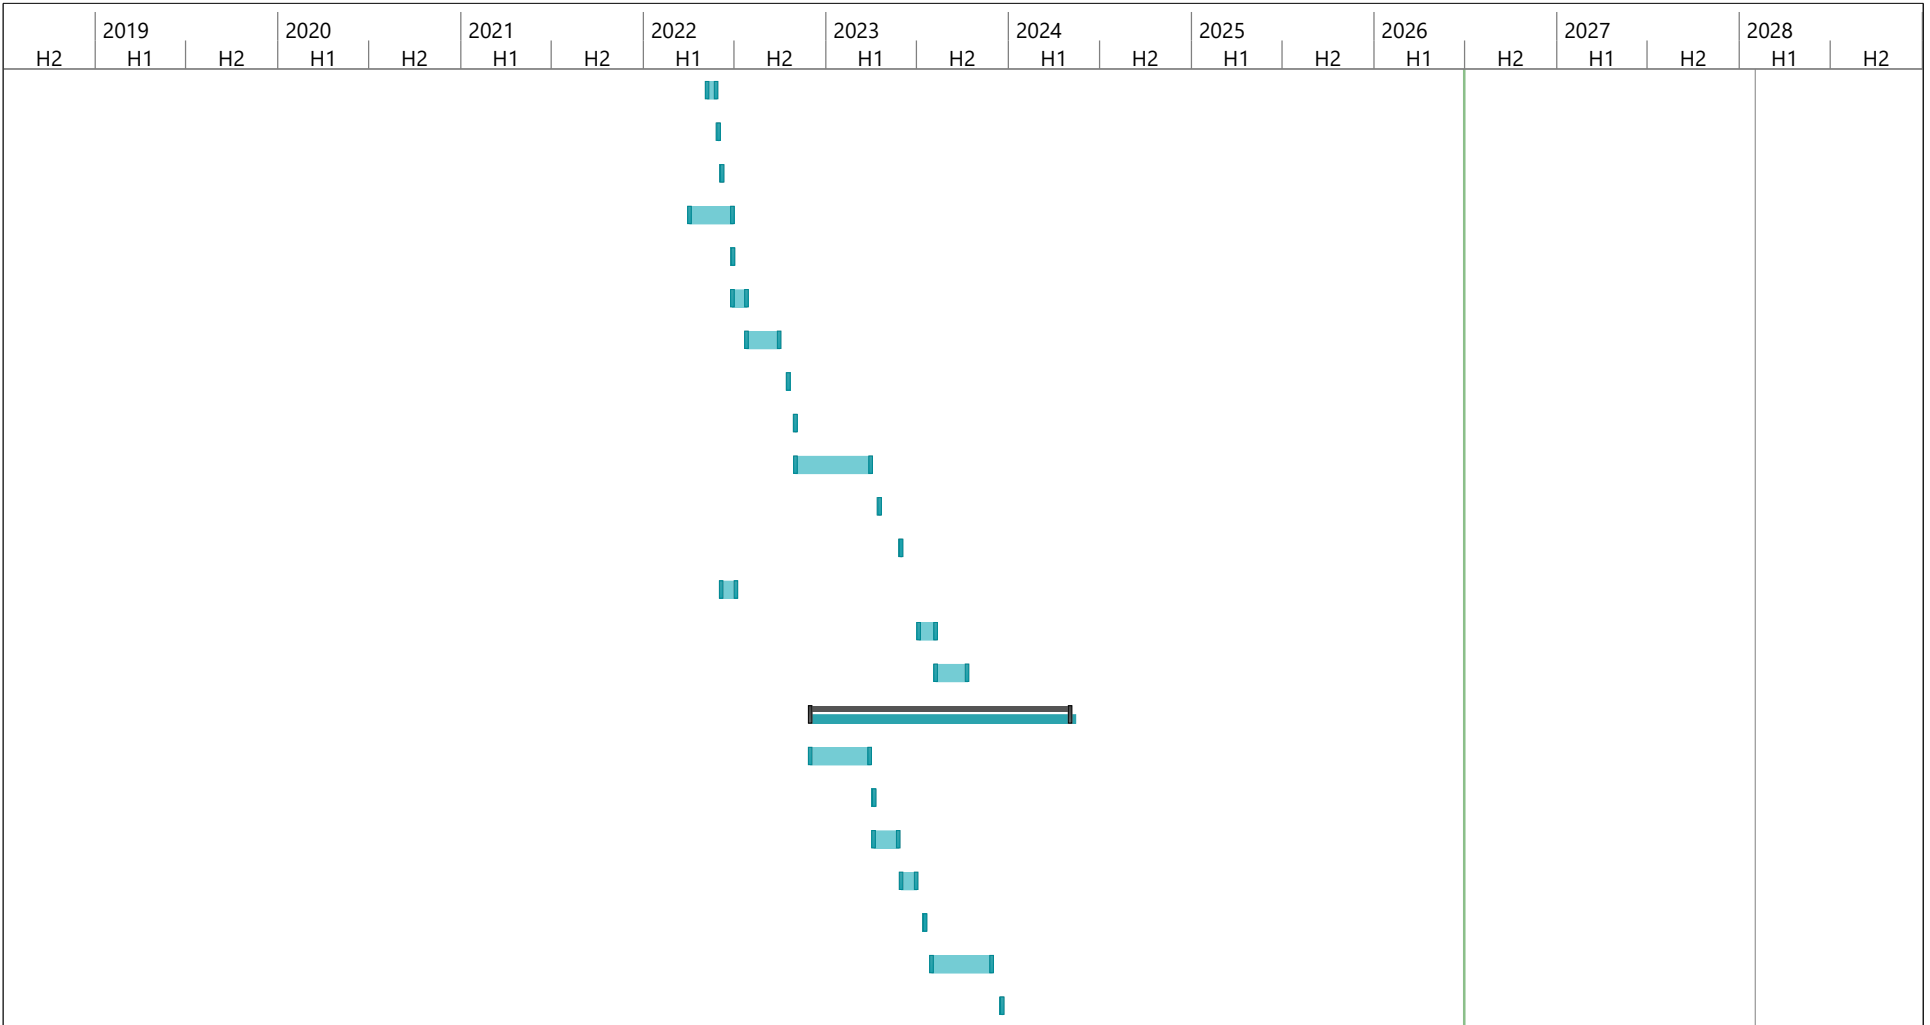


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

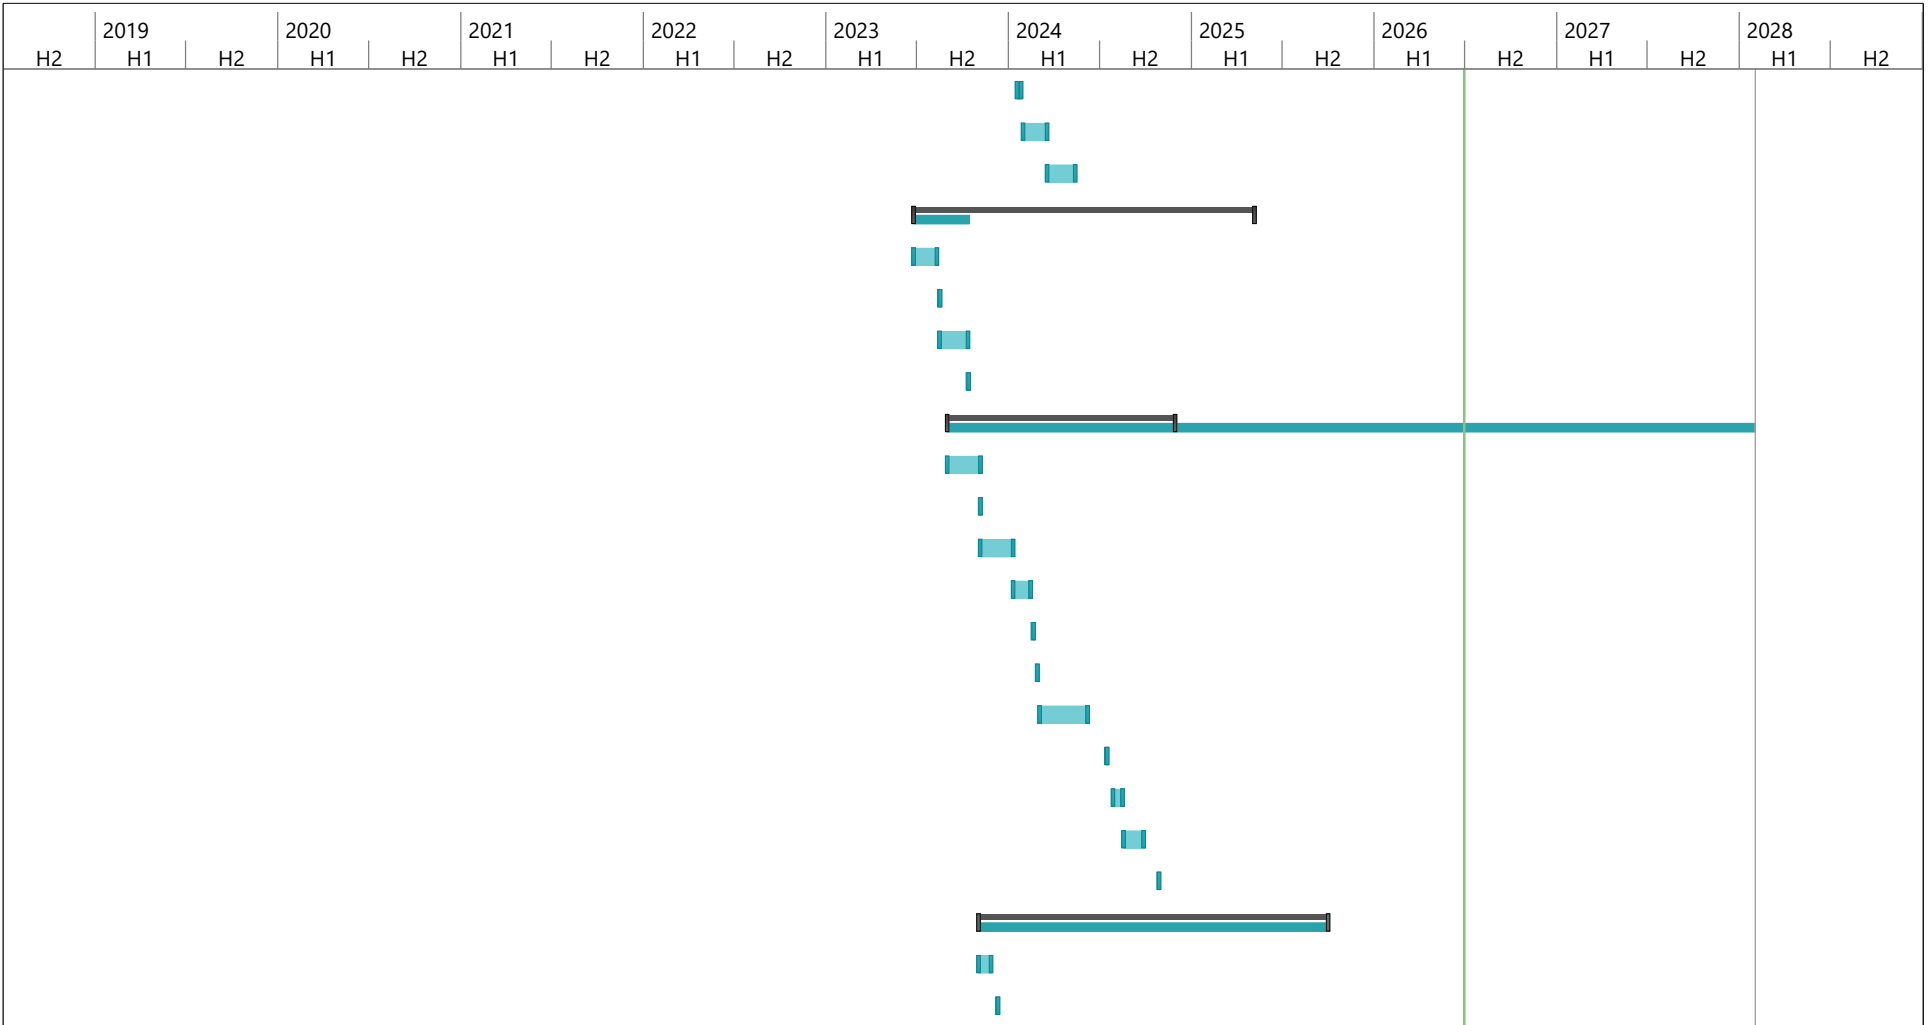


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

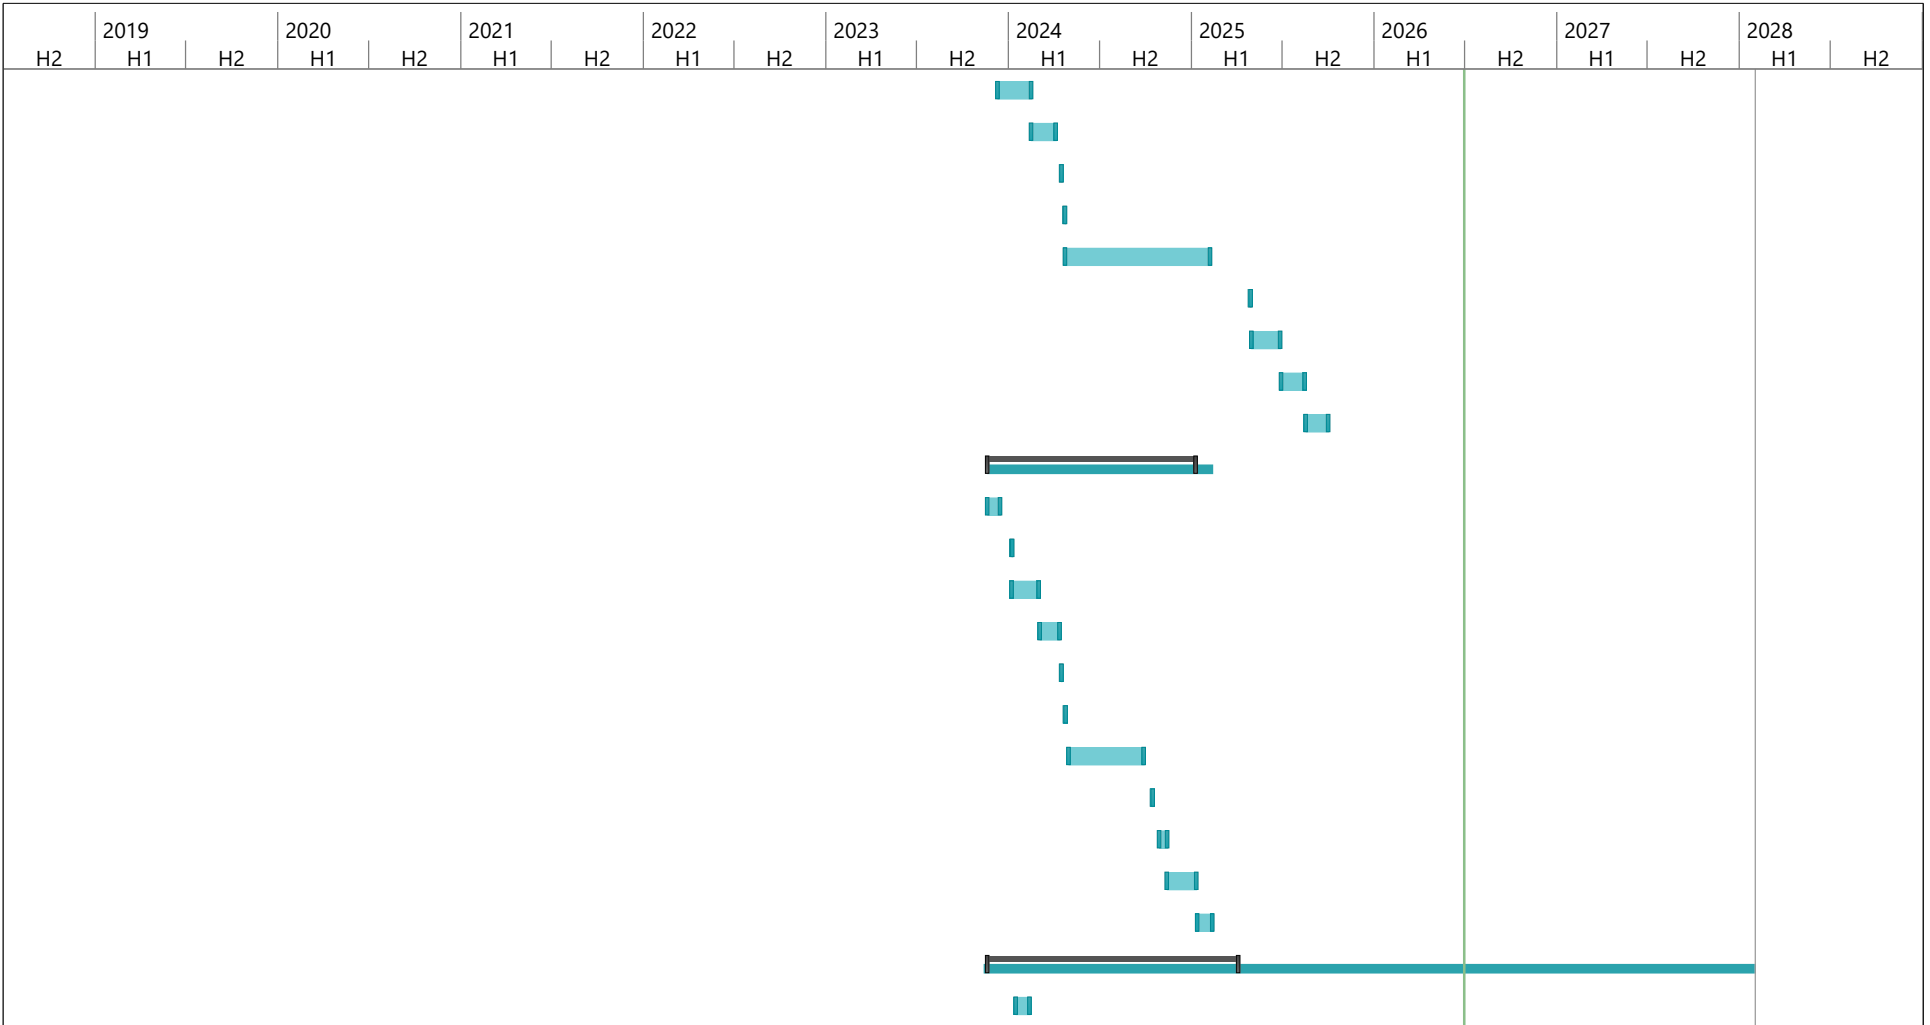


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

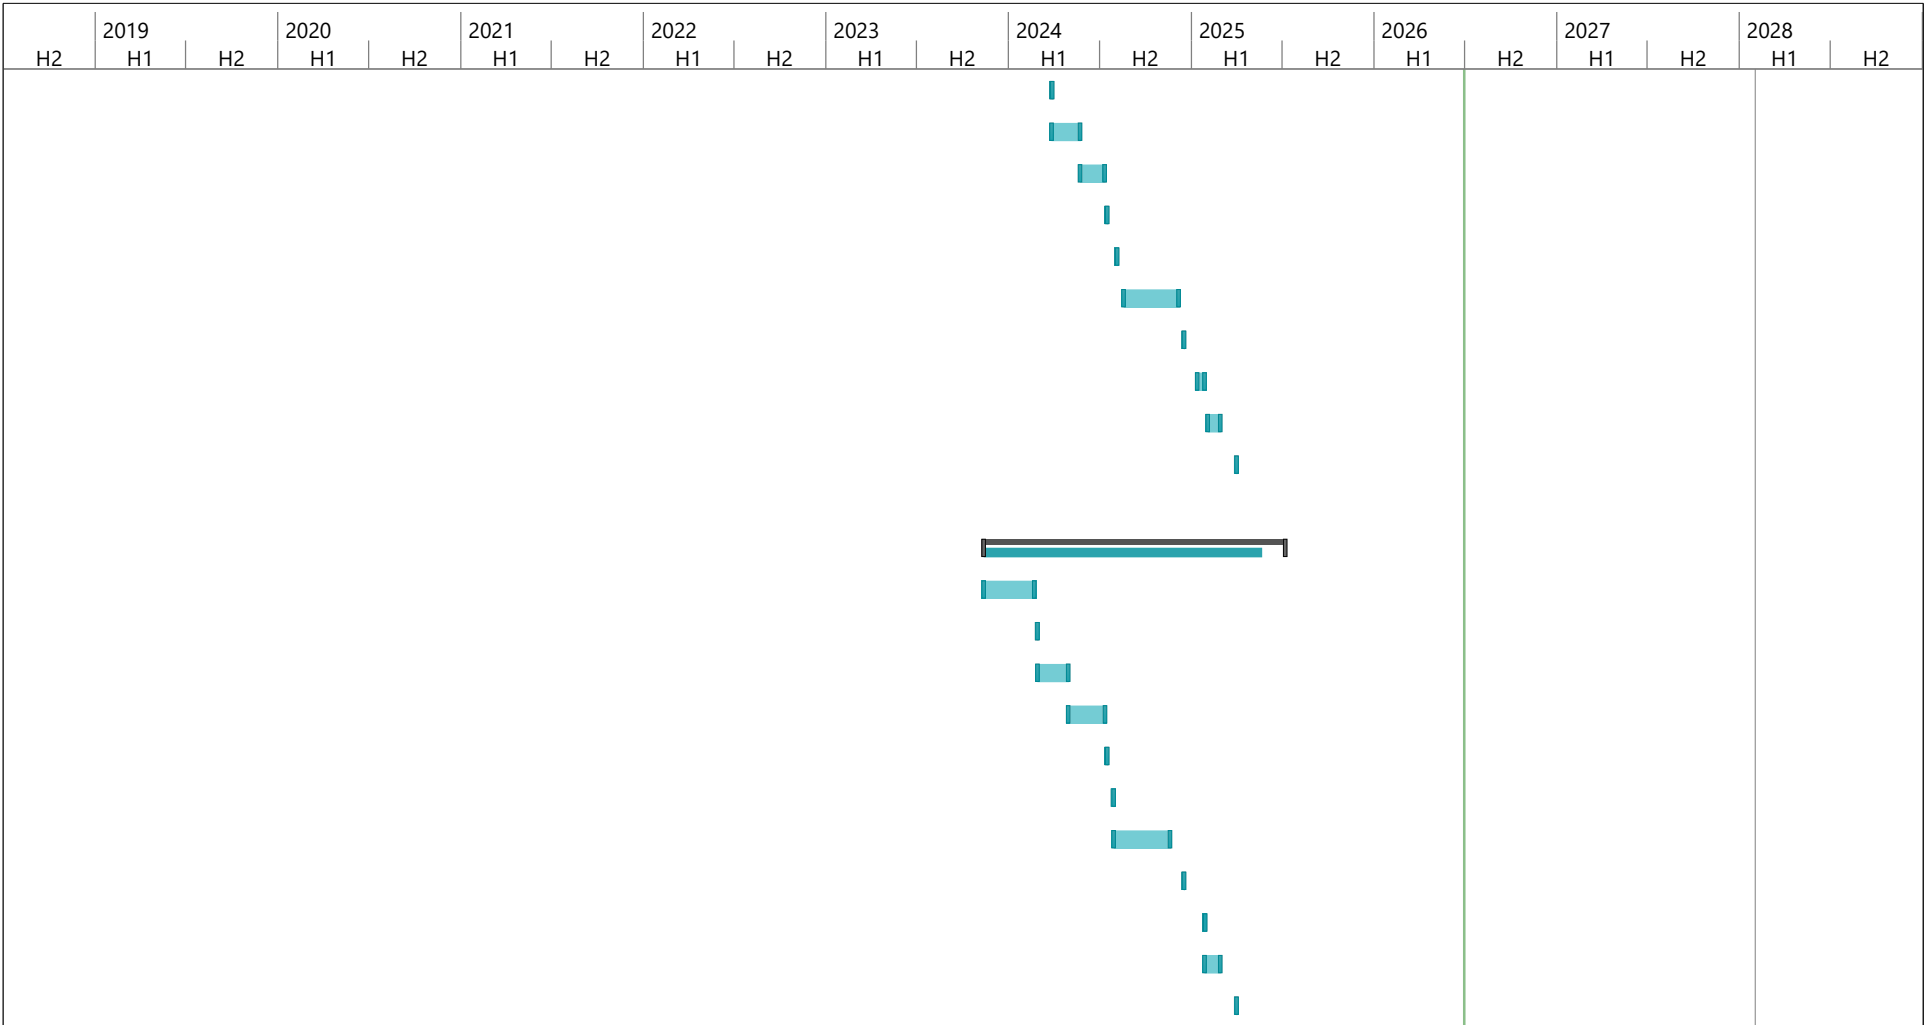


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

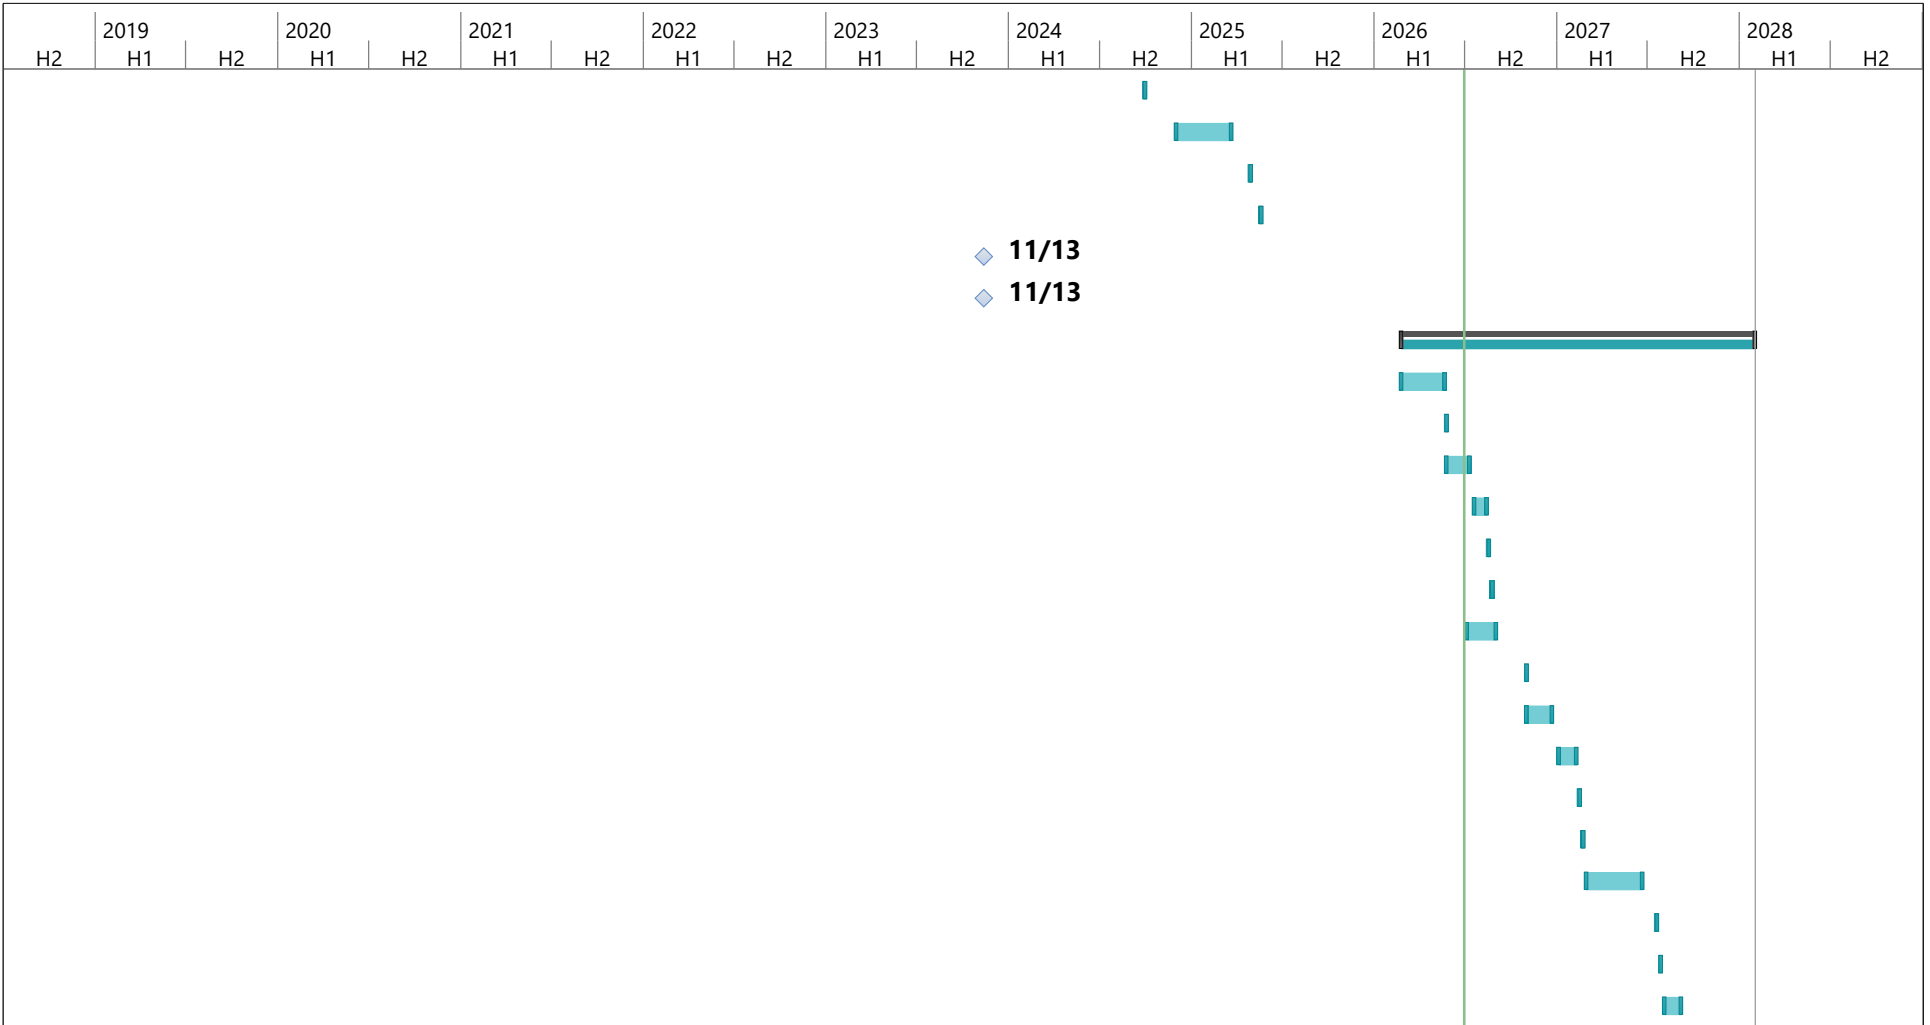


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

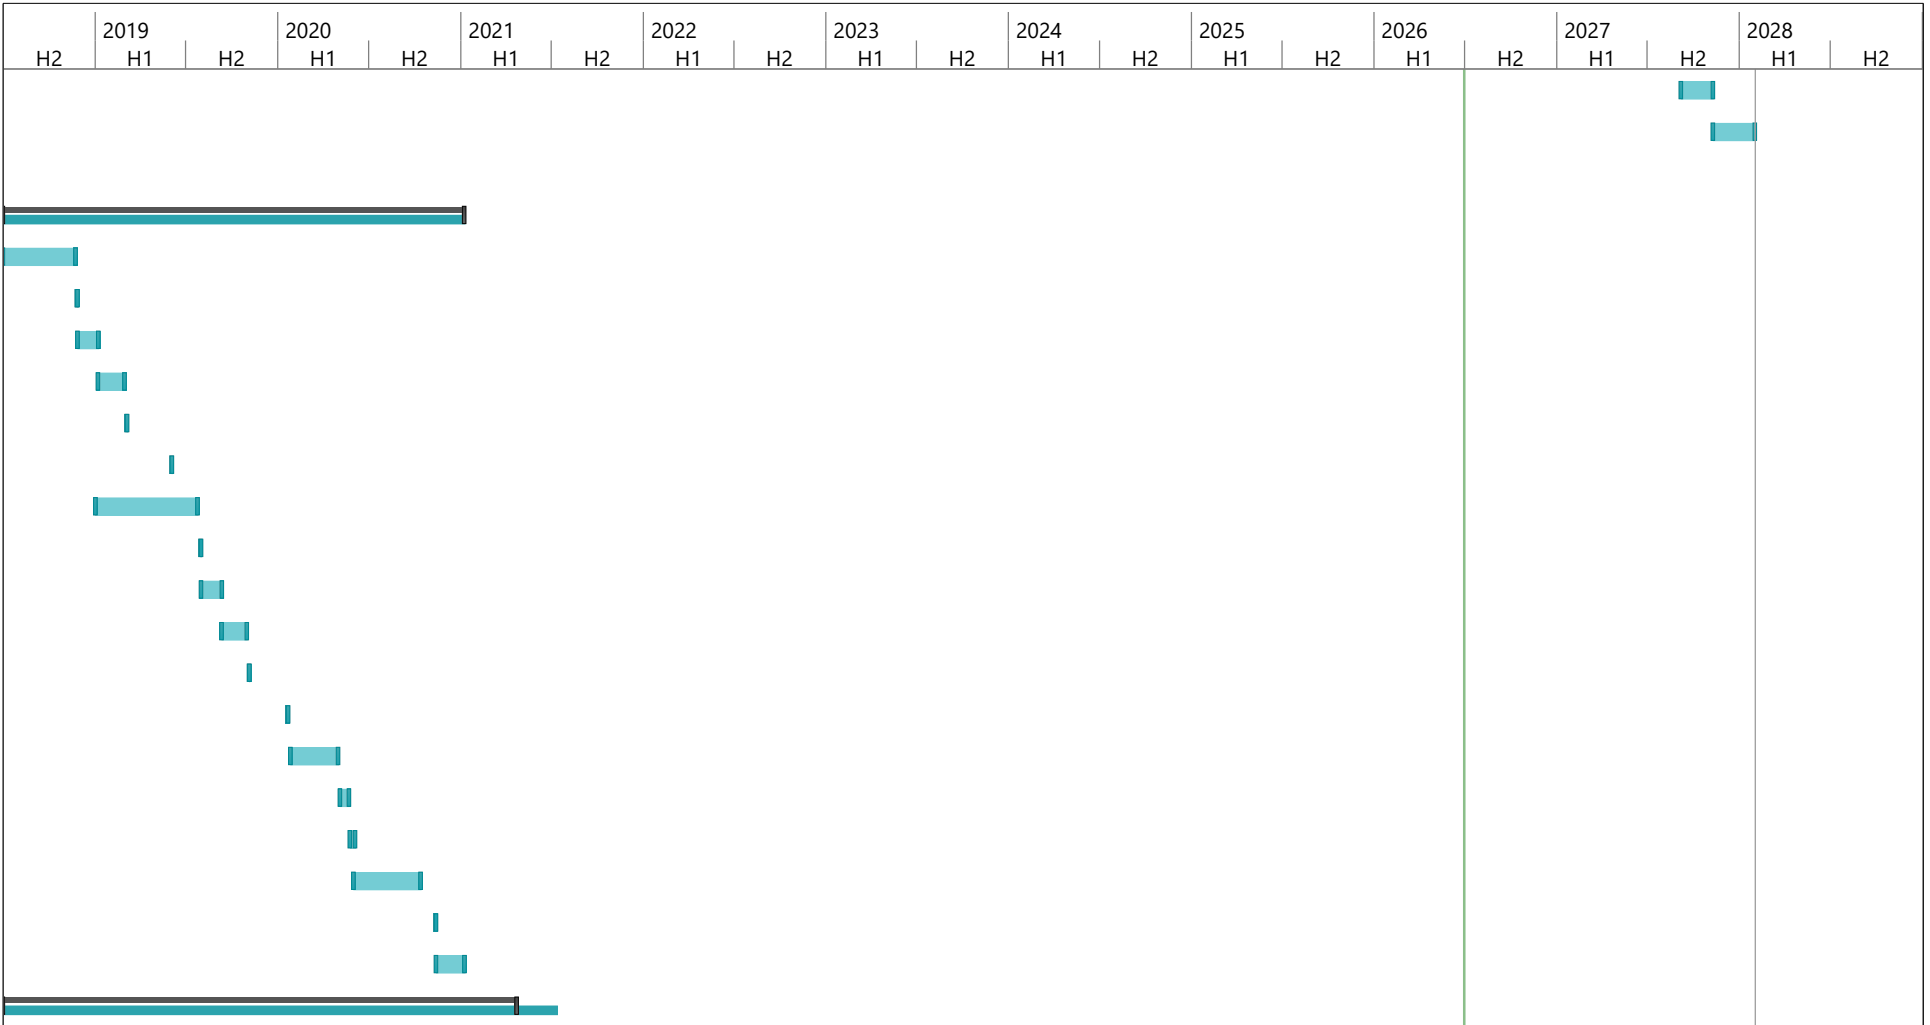


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

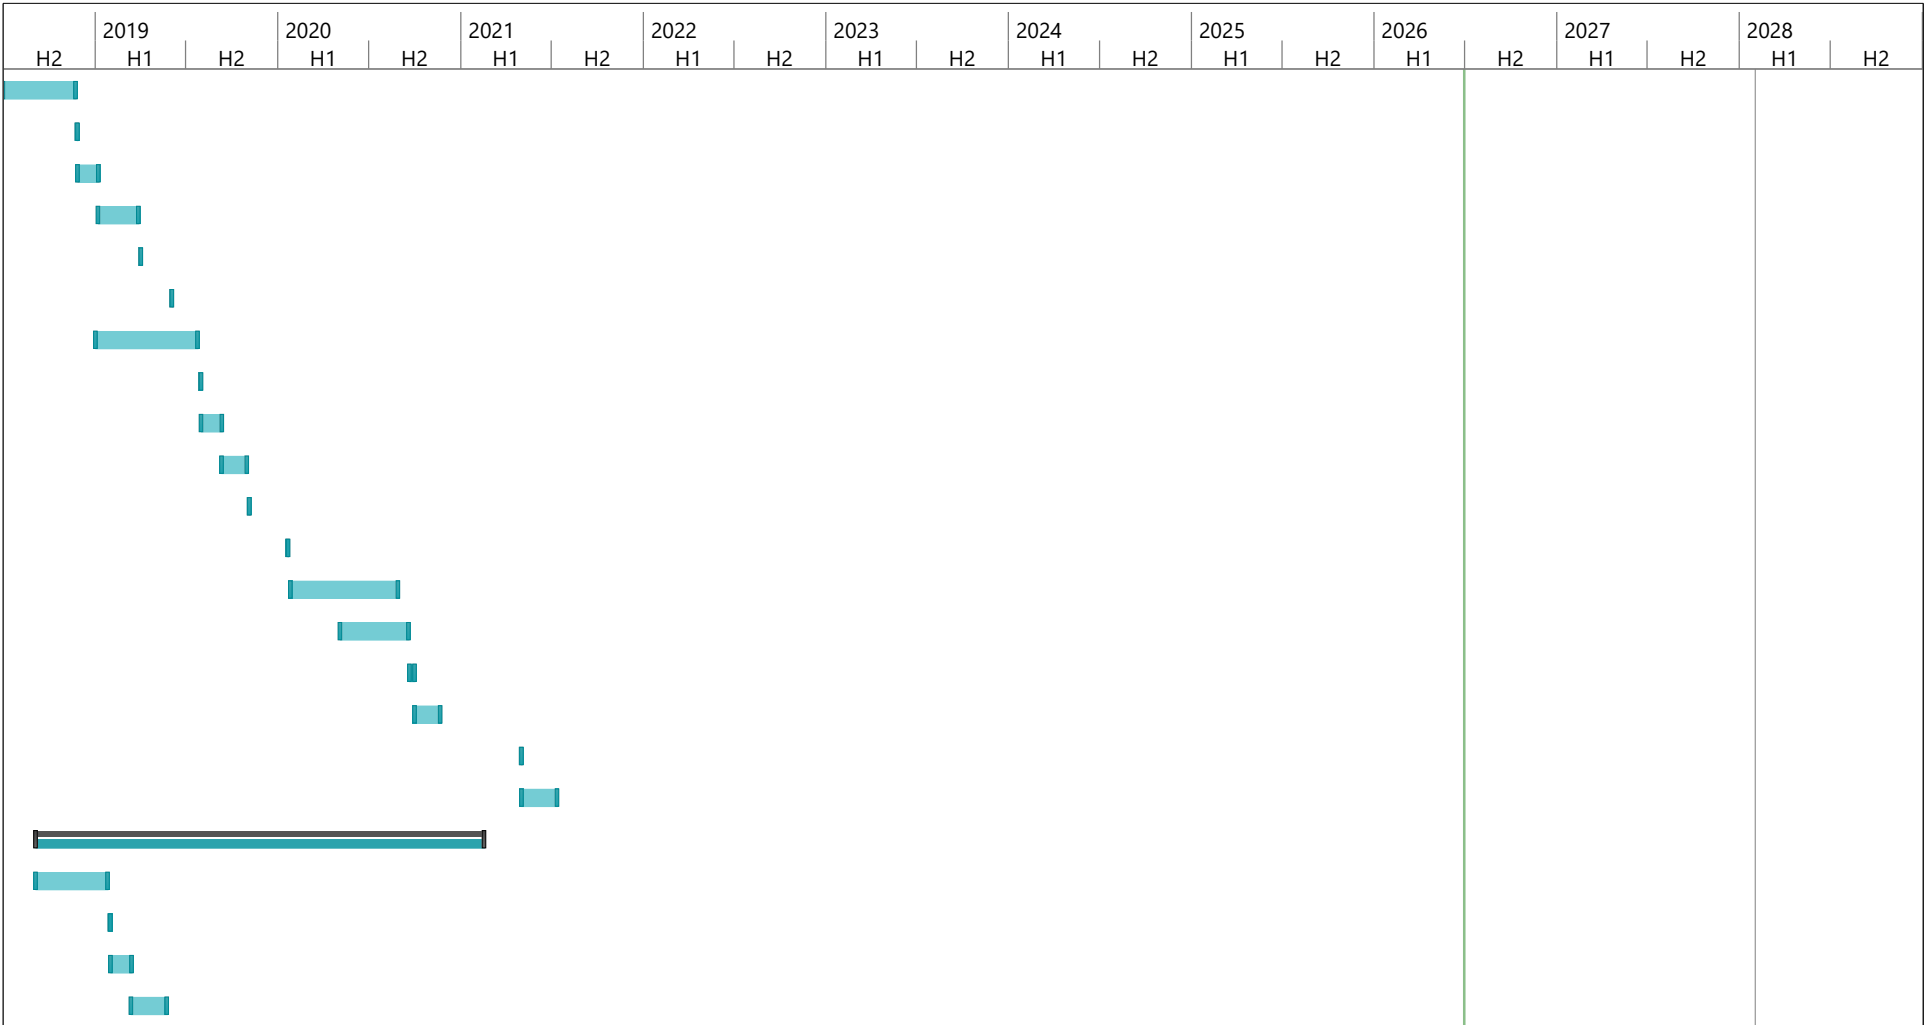


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

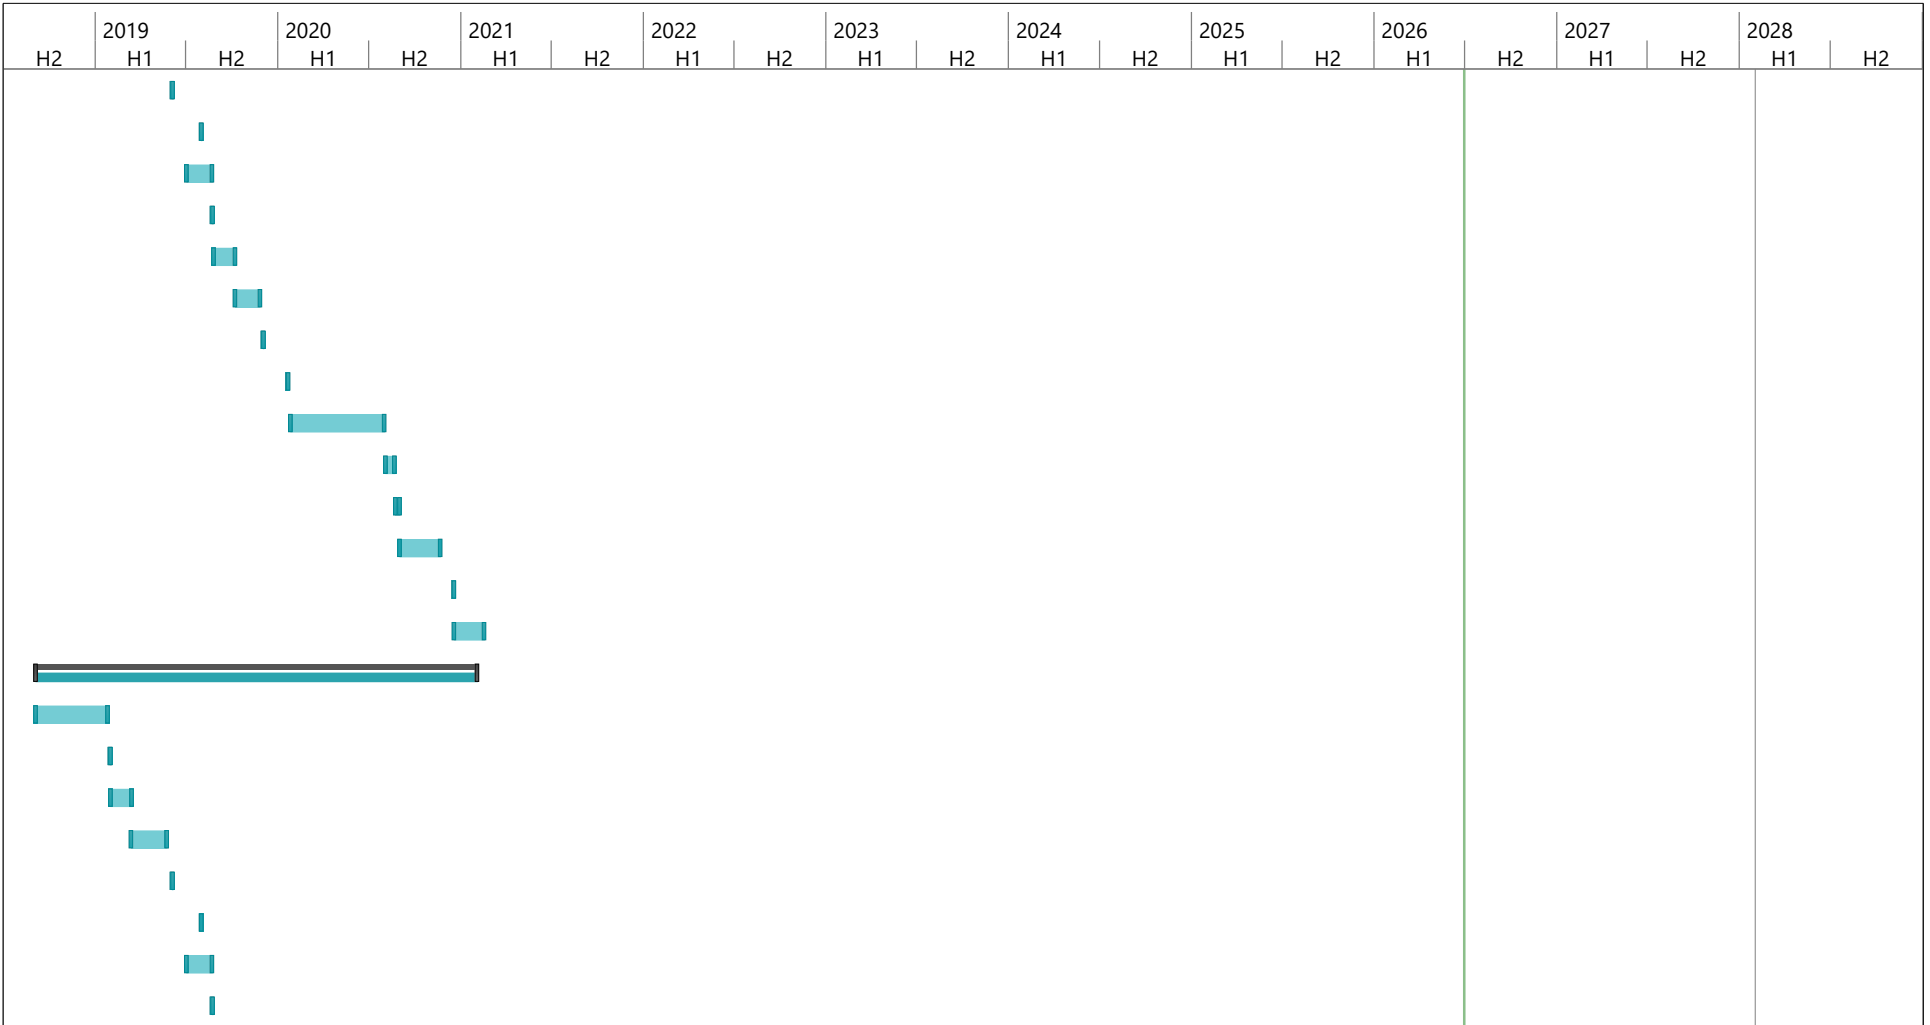


Project: IOU Master Task Timeli  
 Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

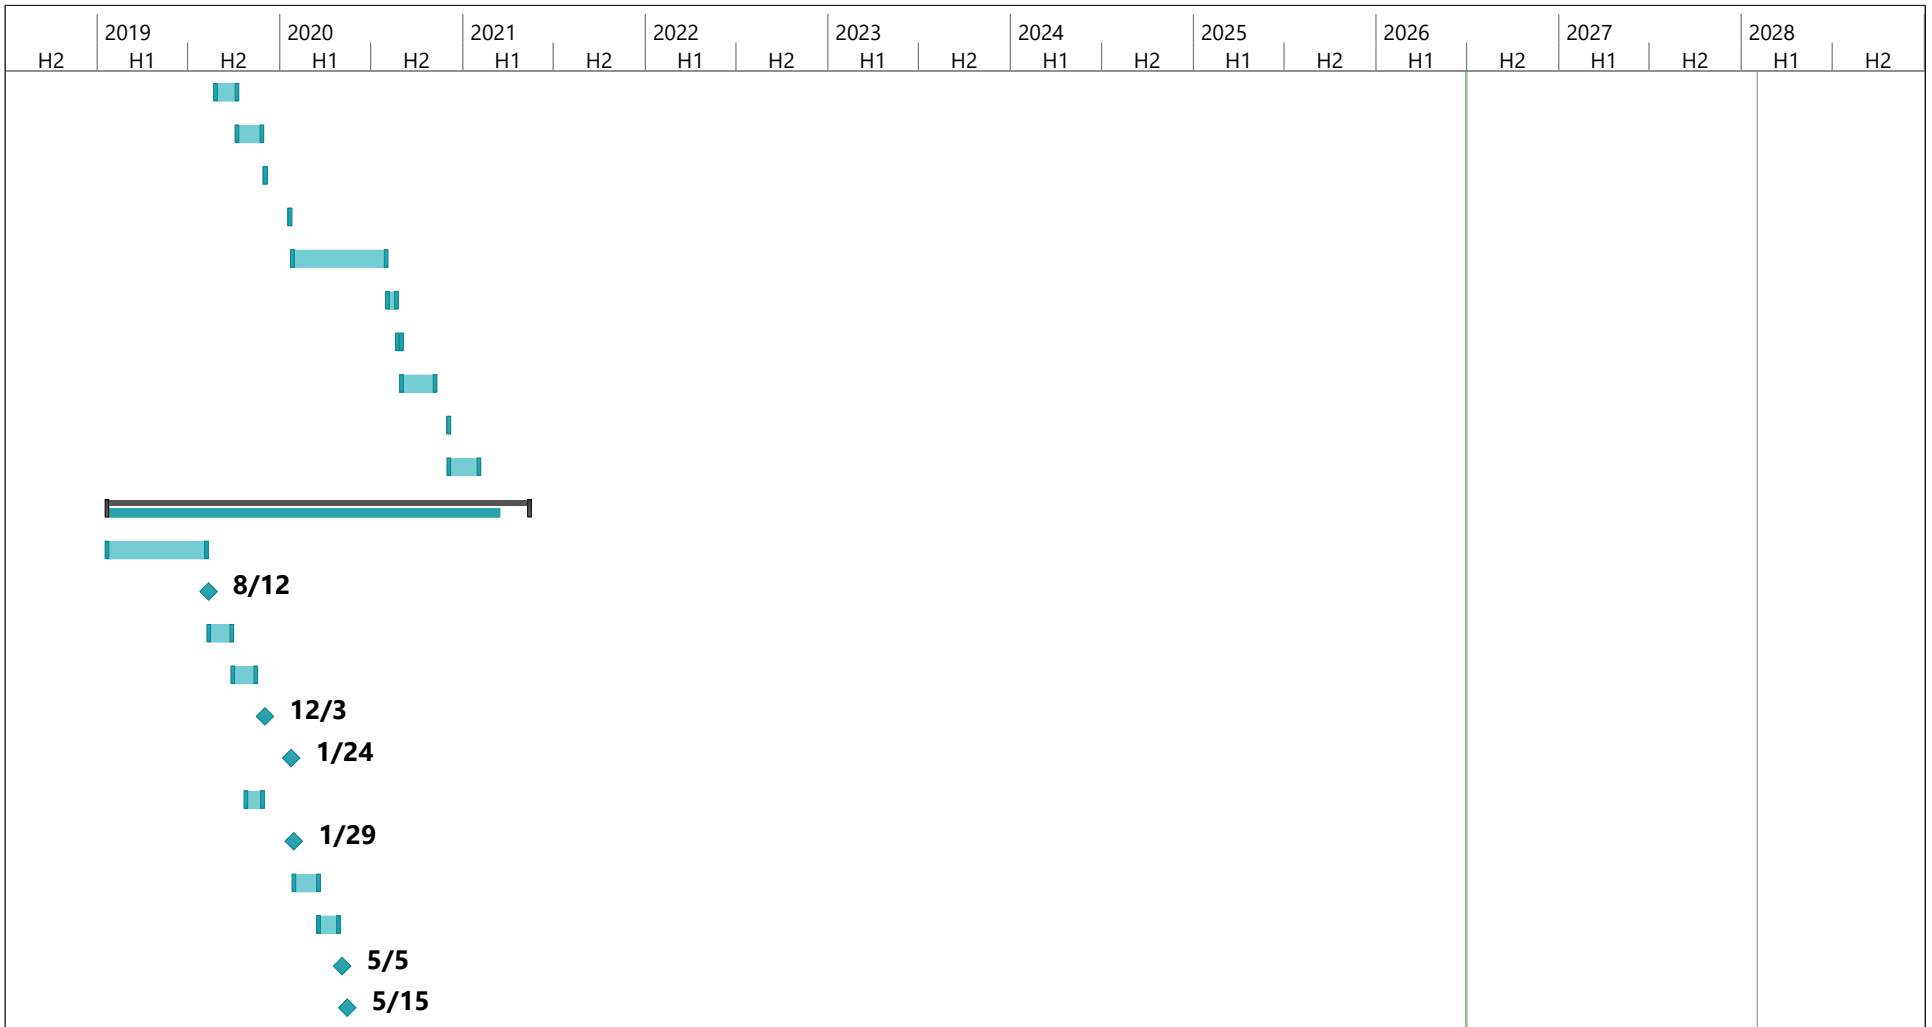


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

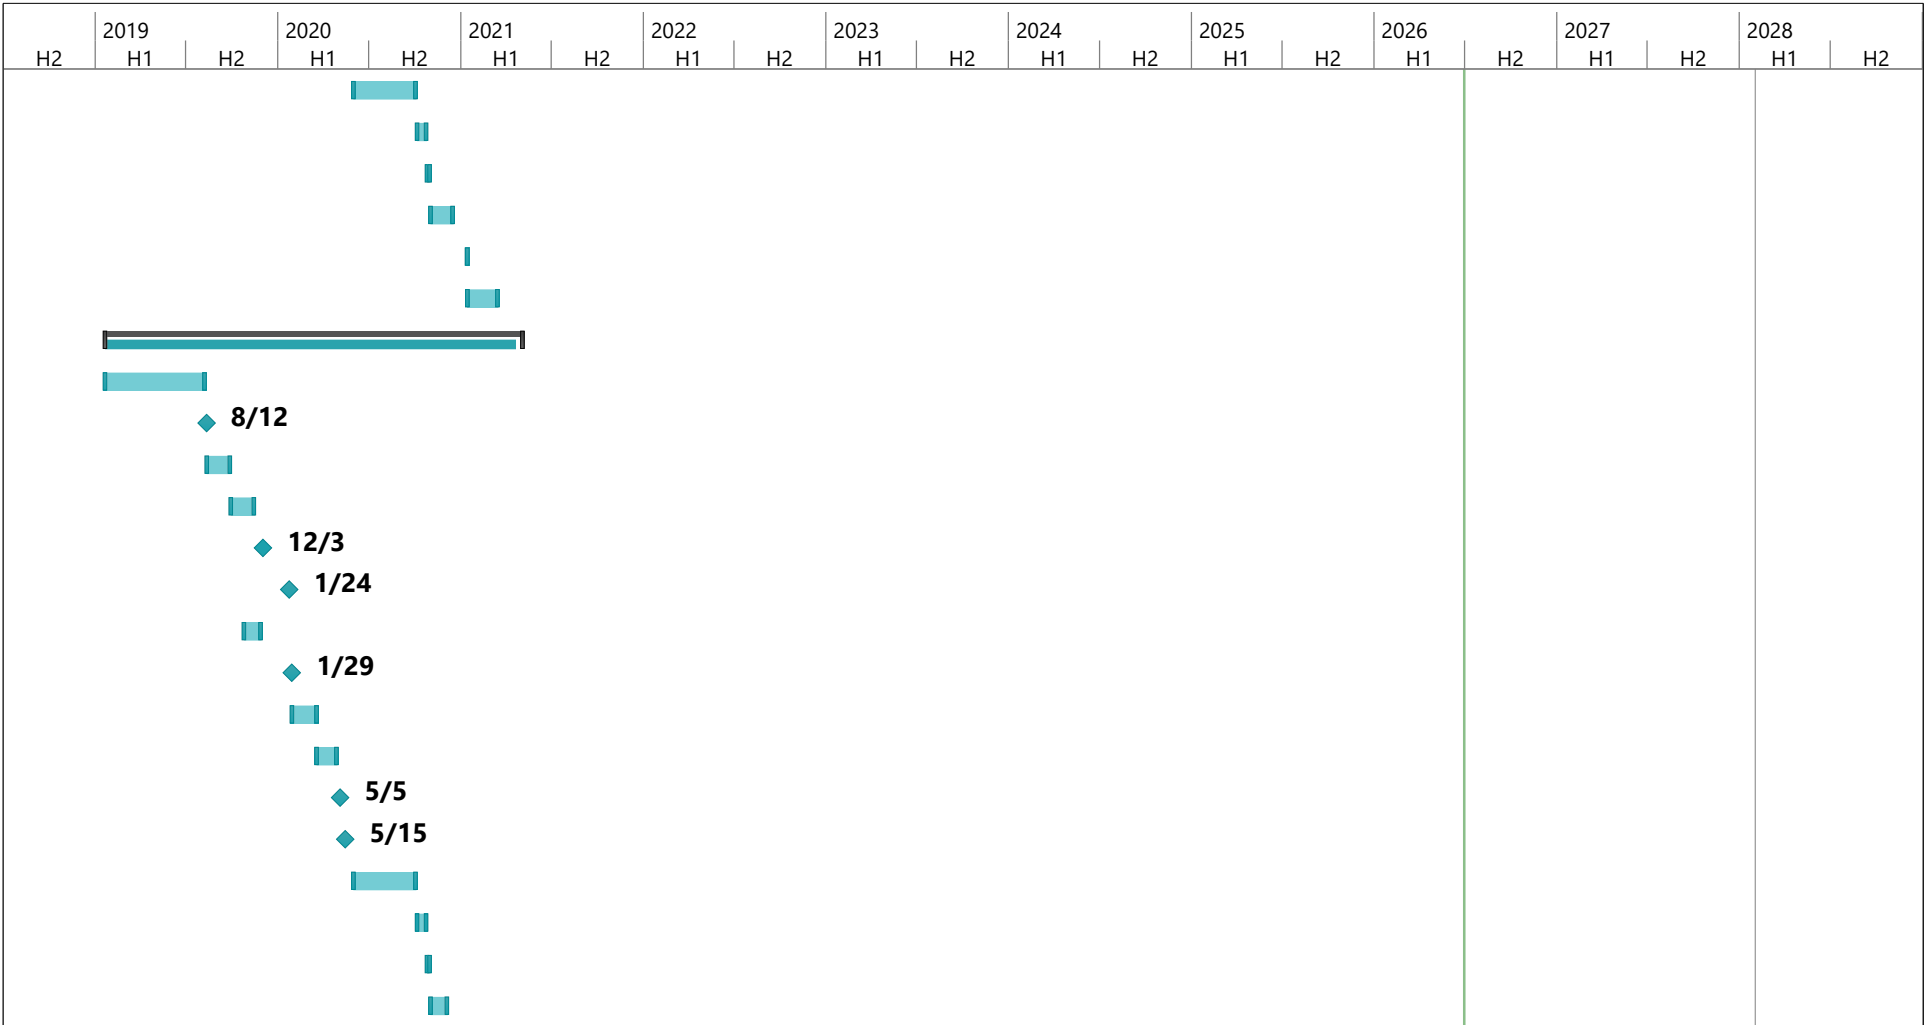


Project: IOU Master Task Timeli  
 Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

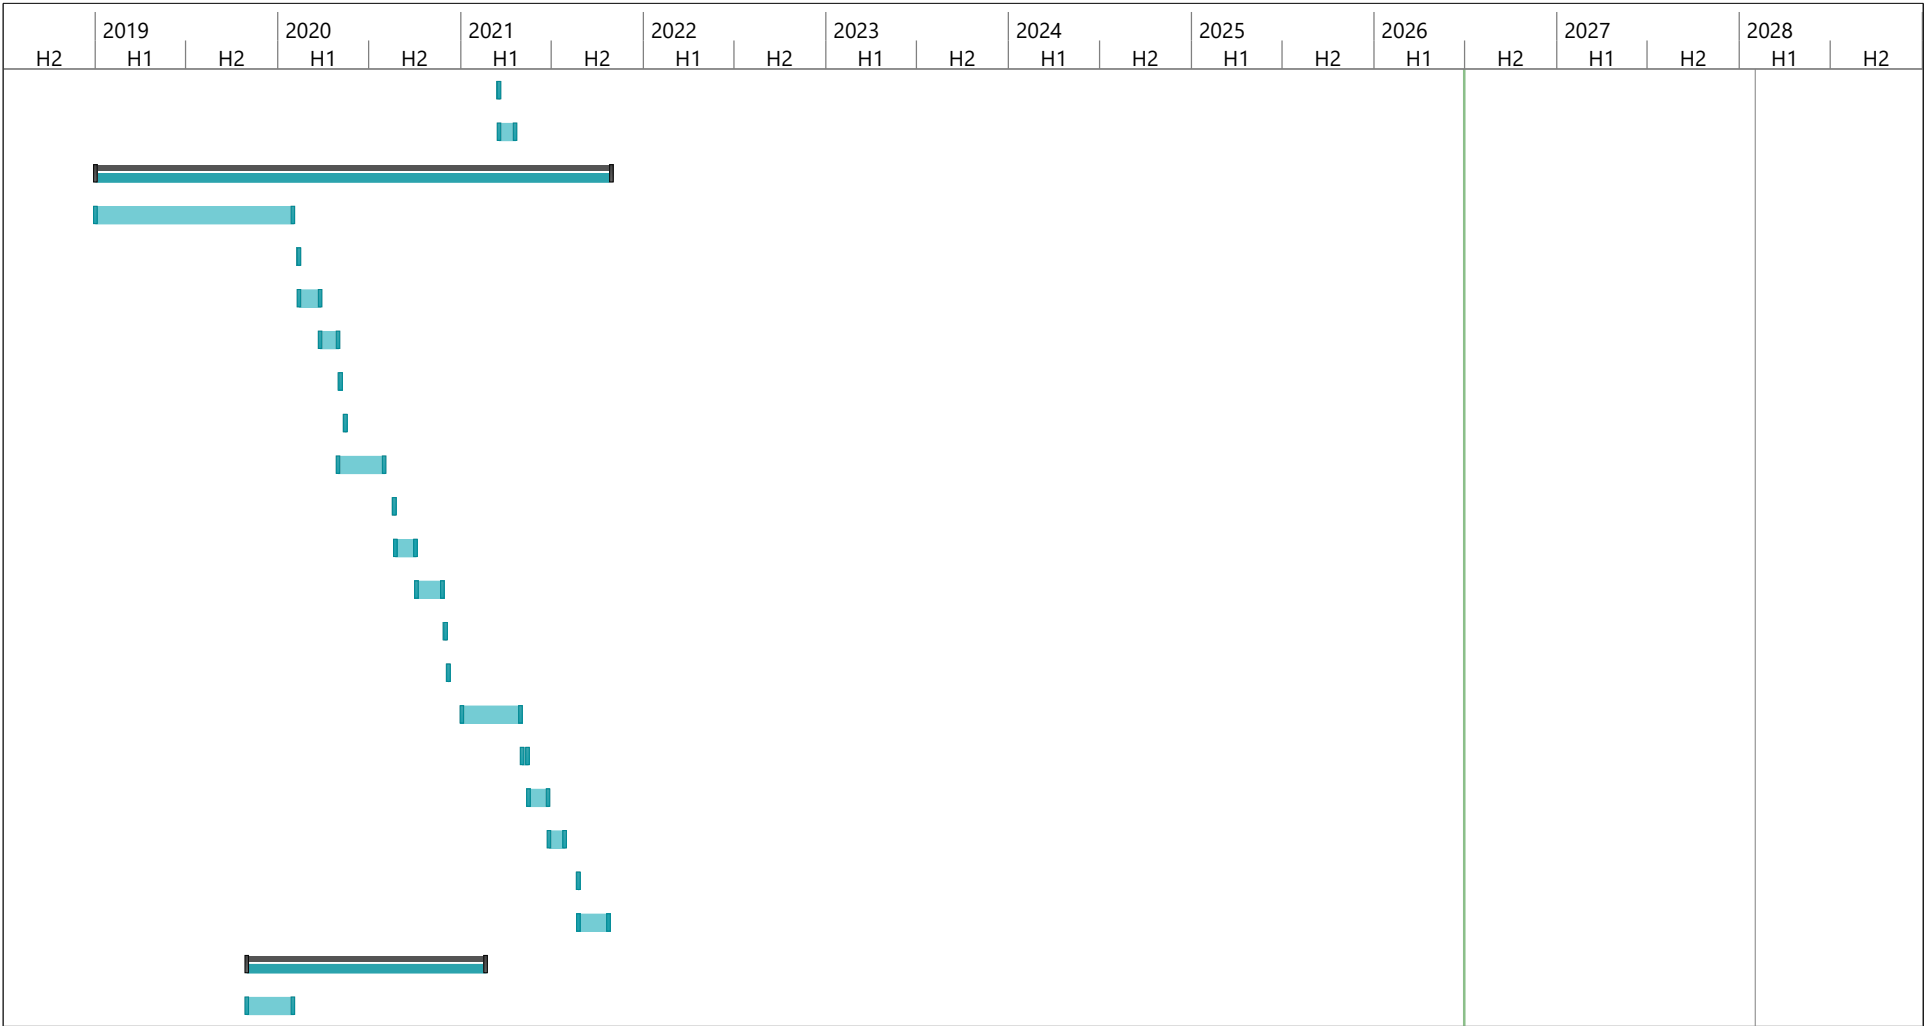


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

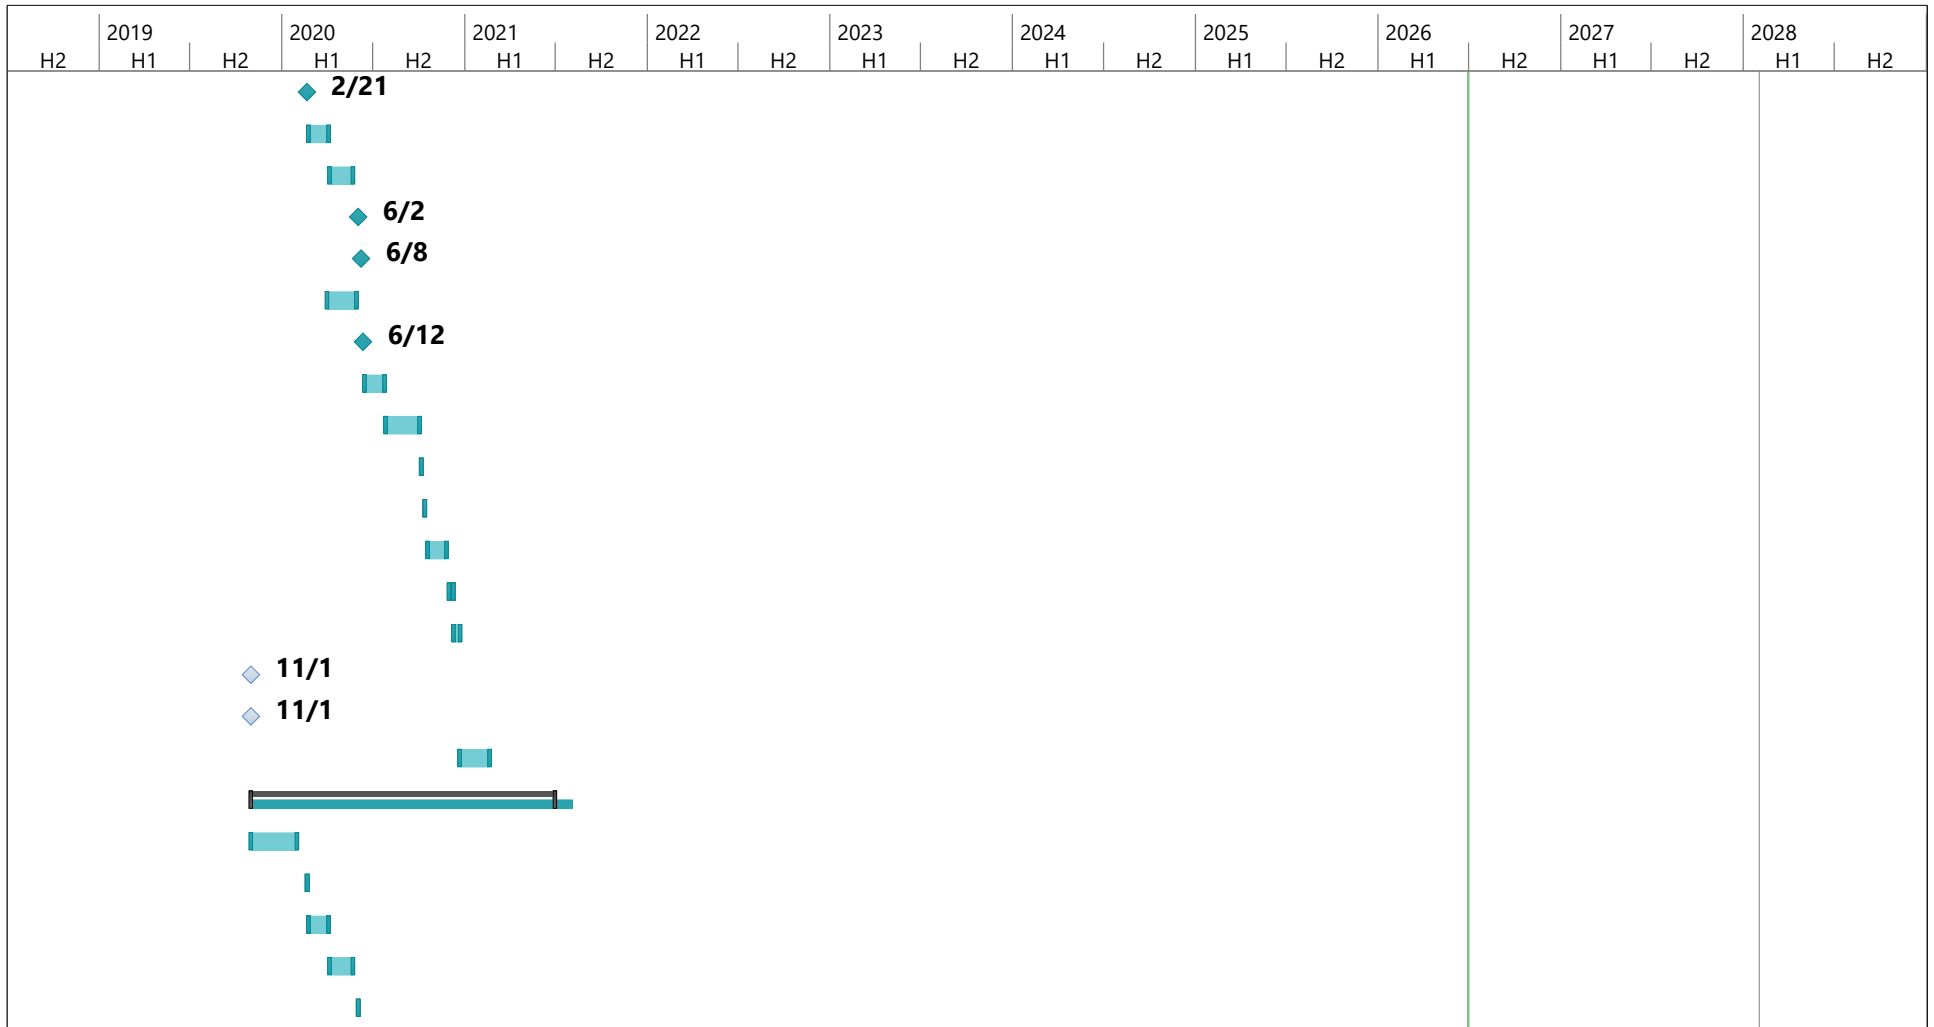


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

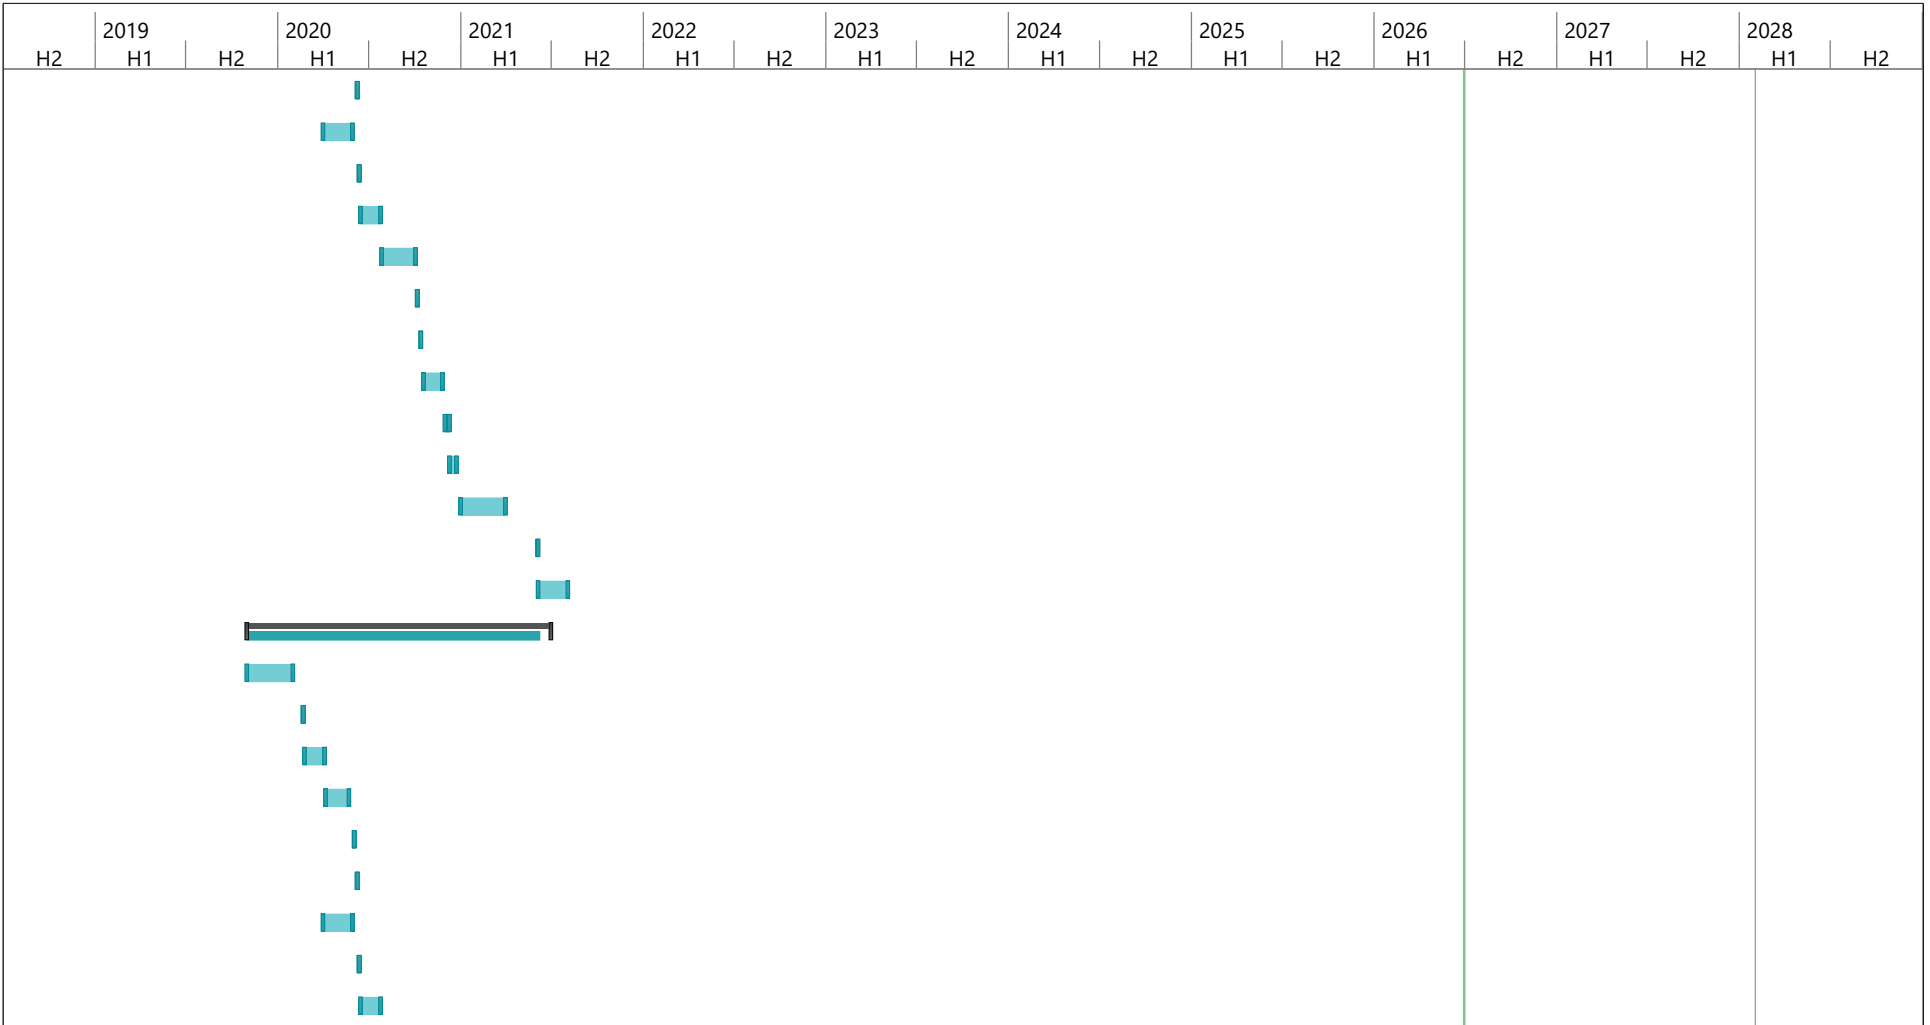


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

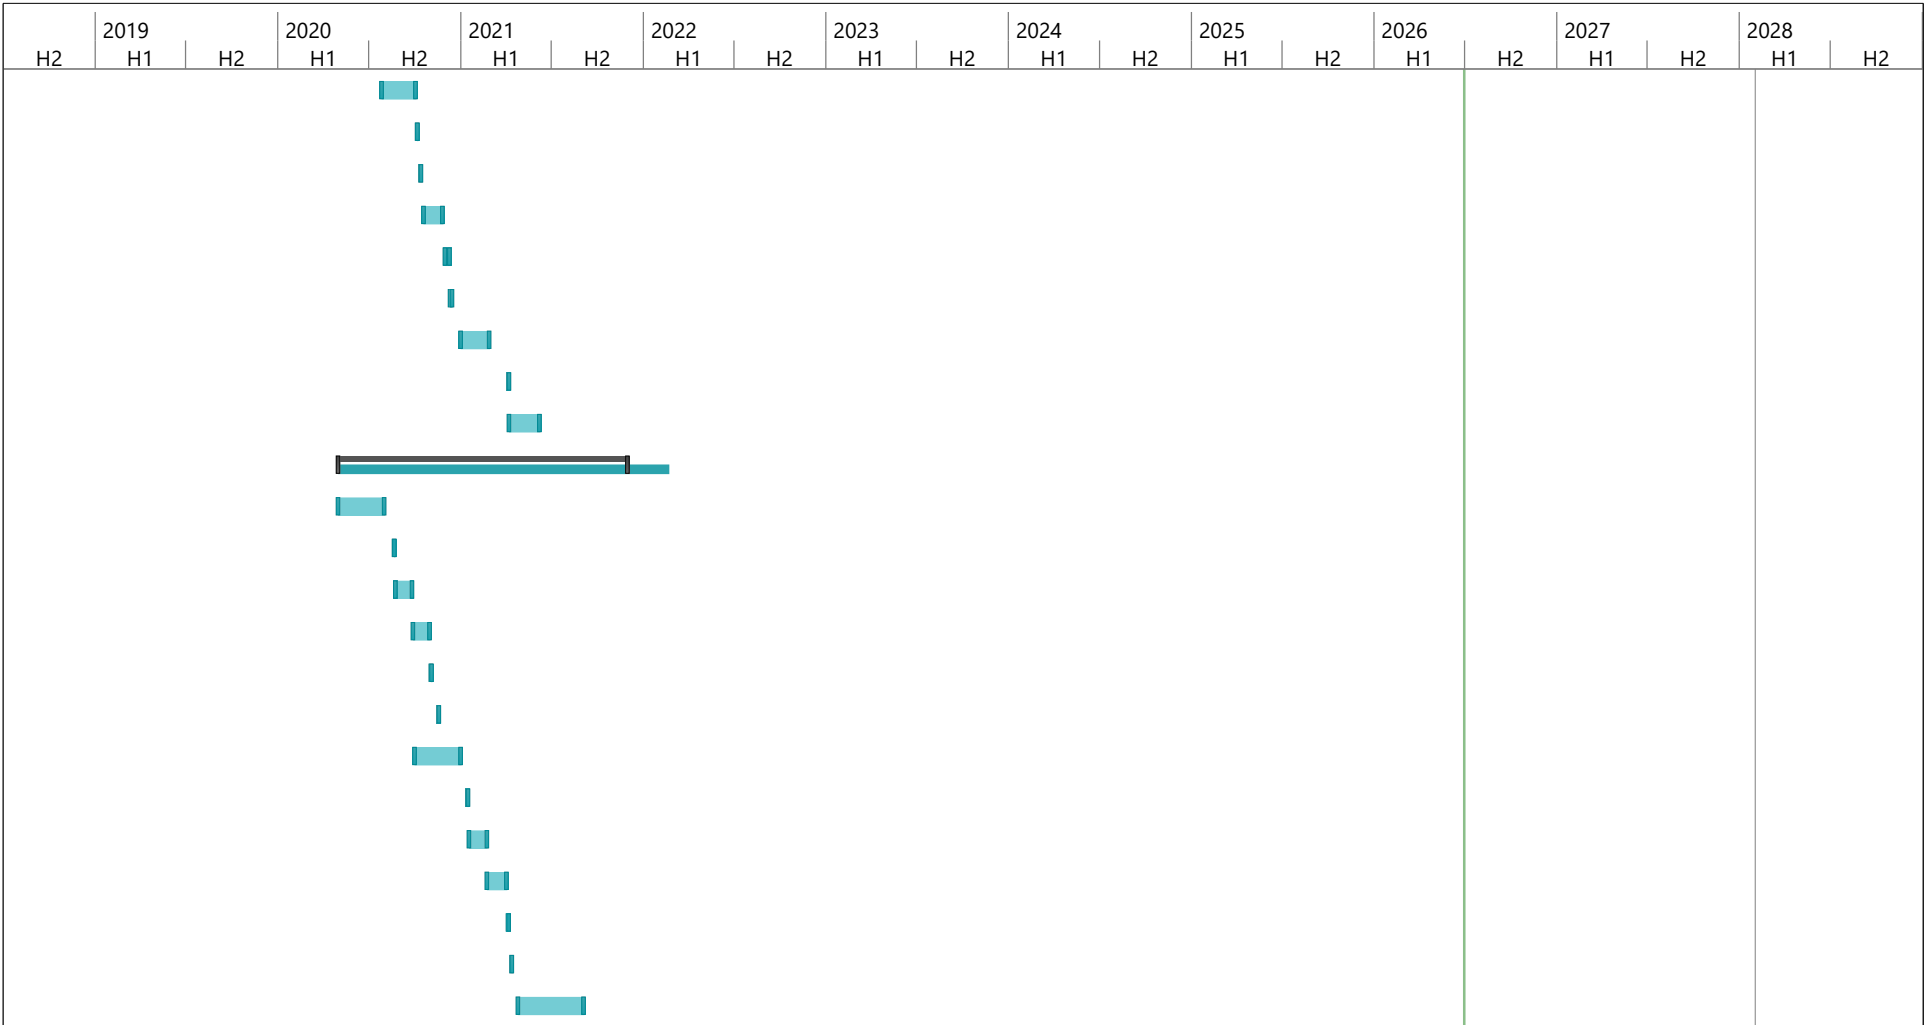


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

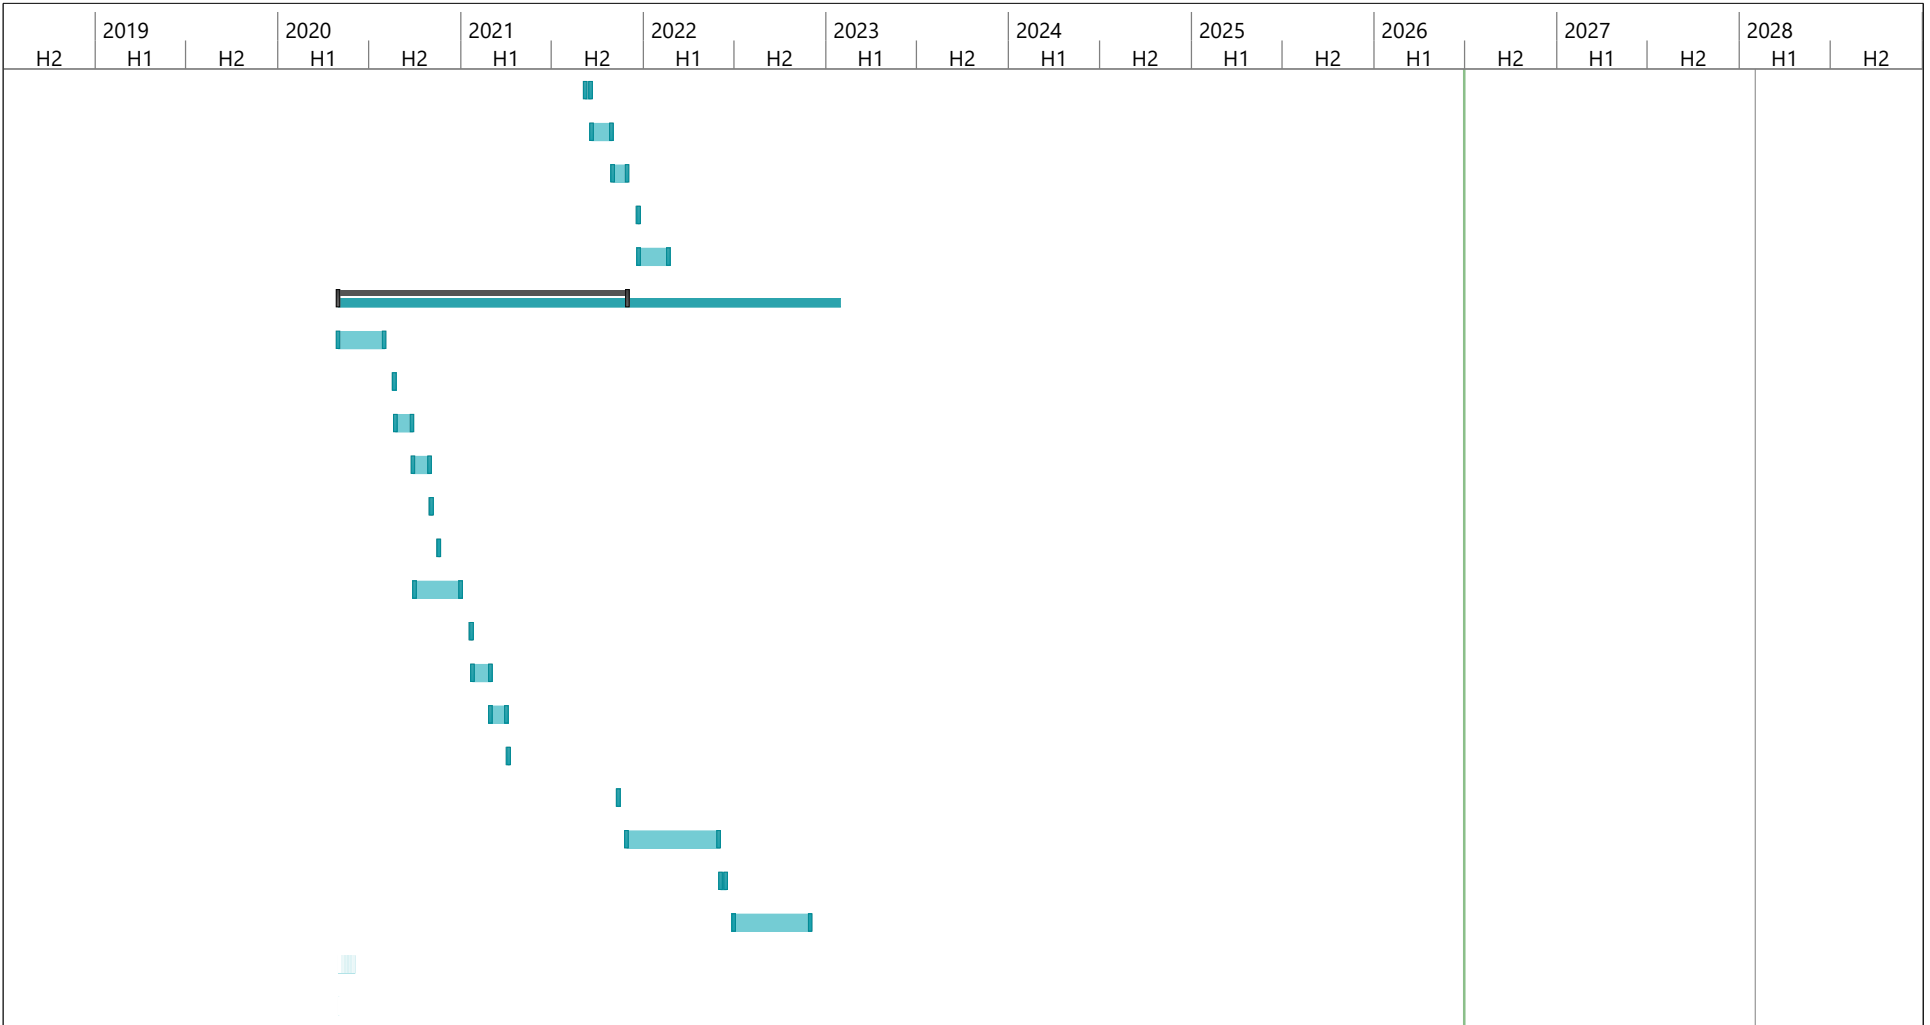


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

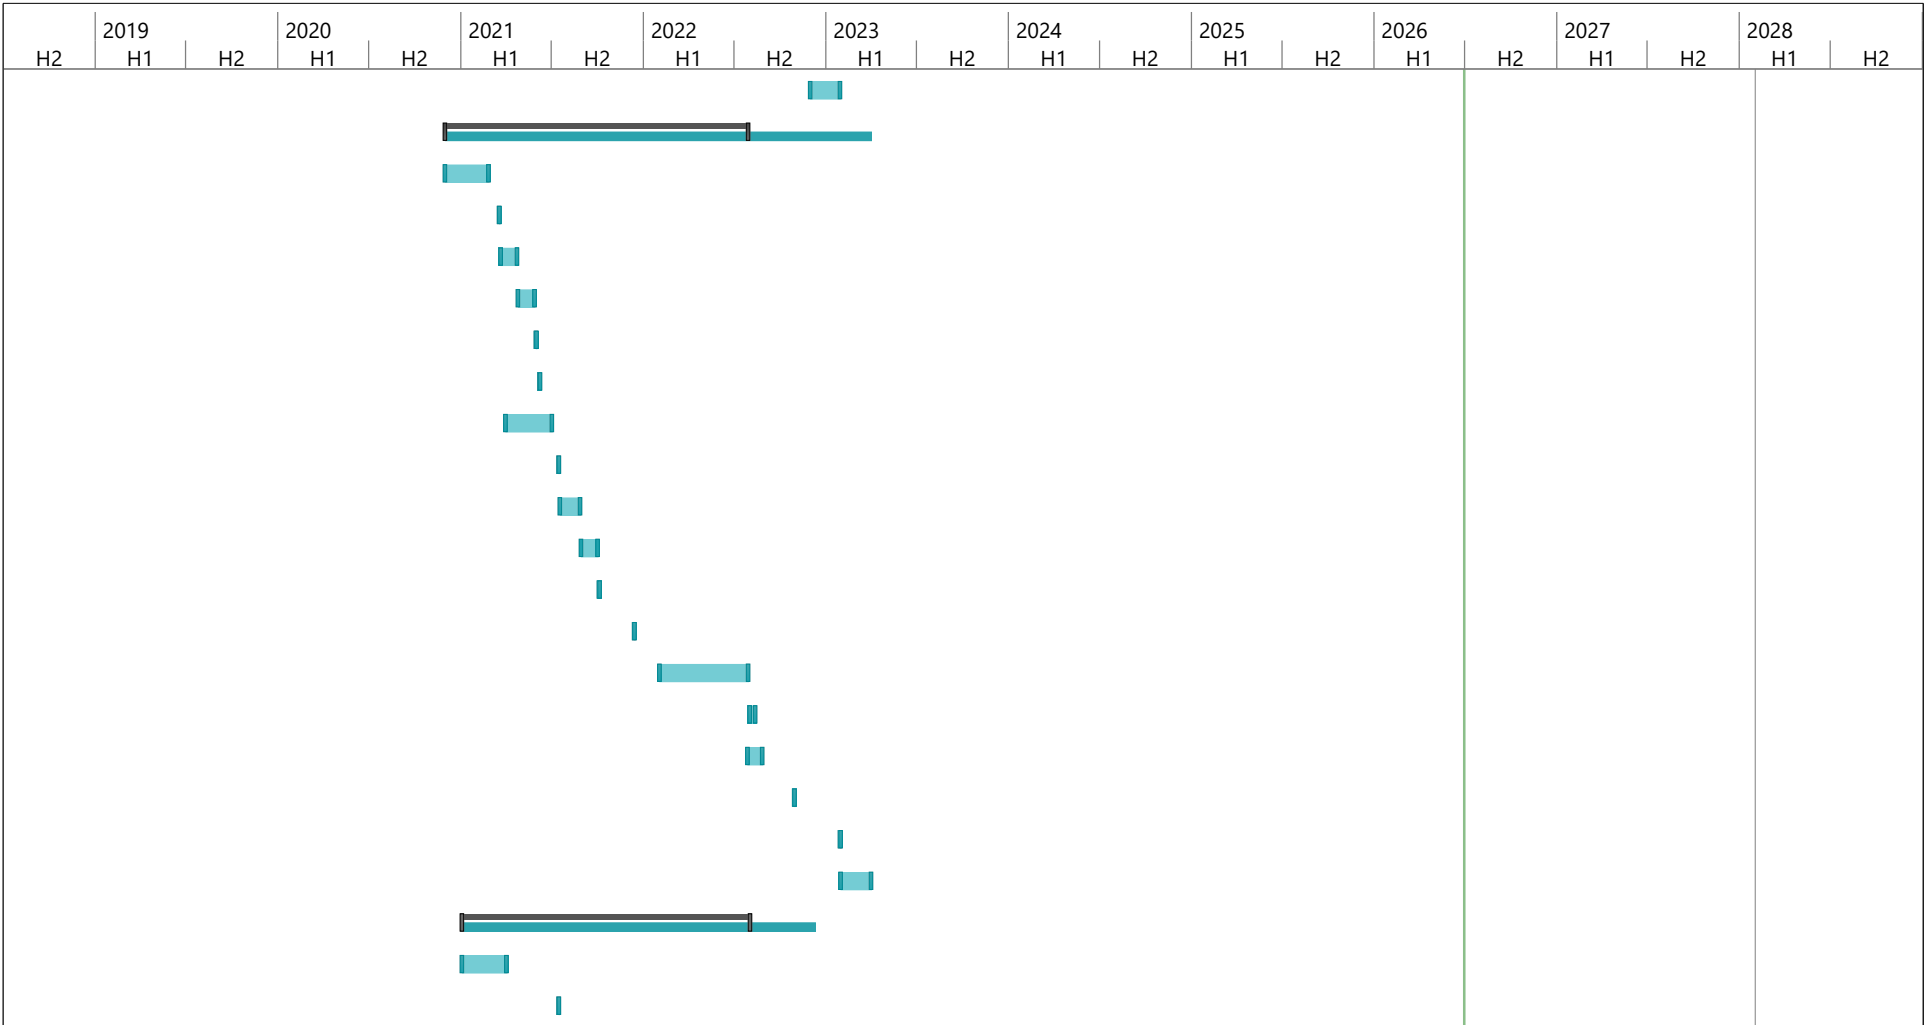


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

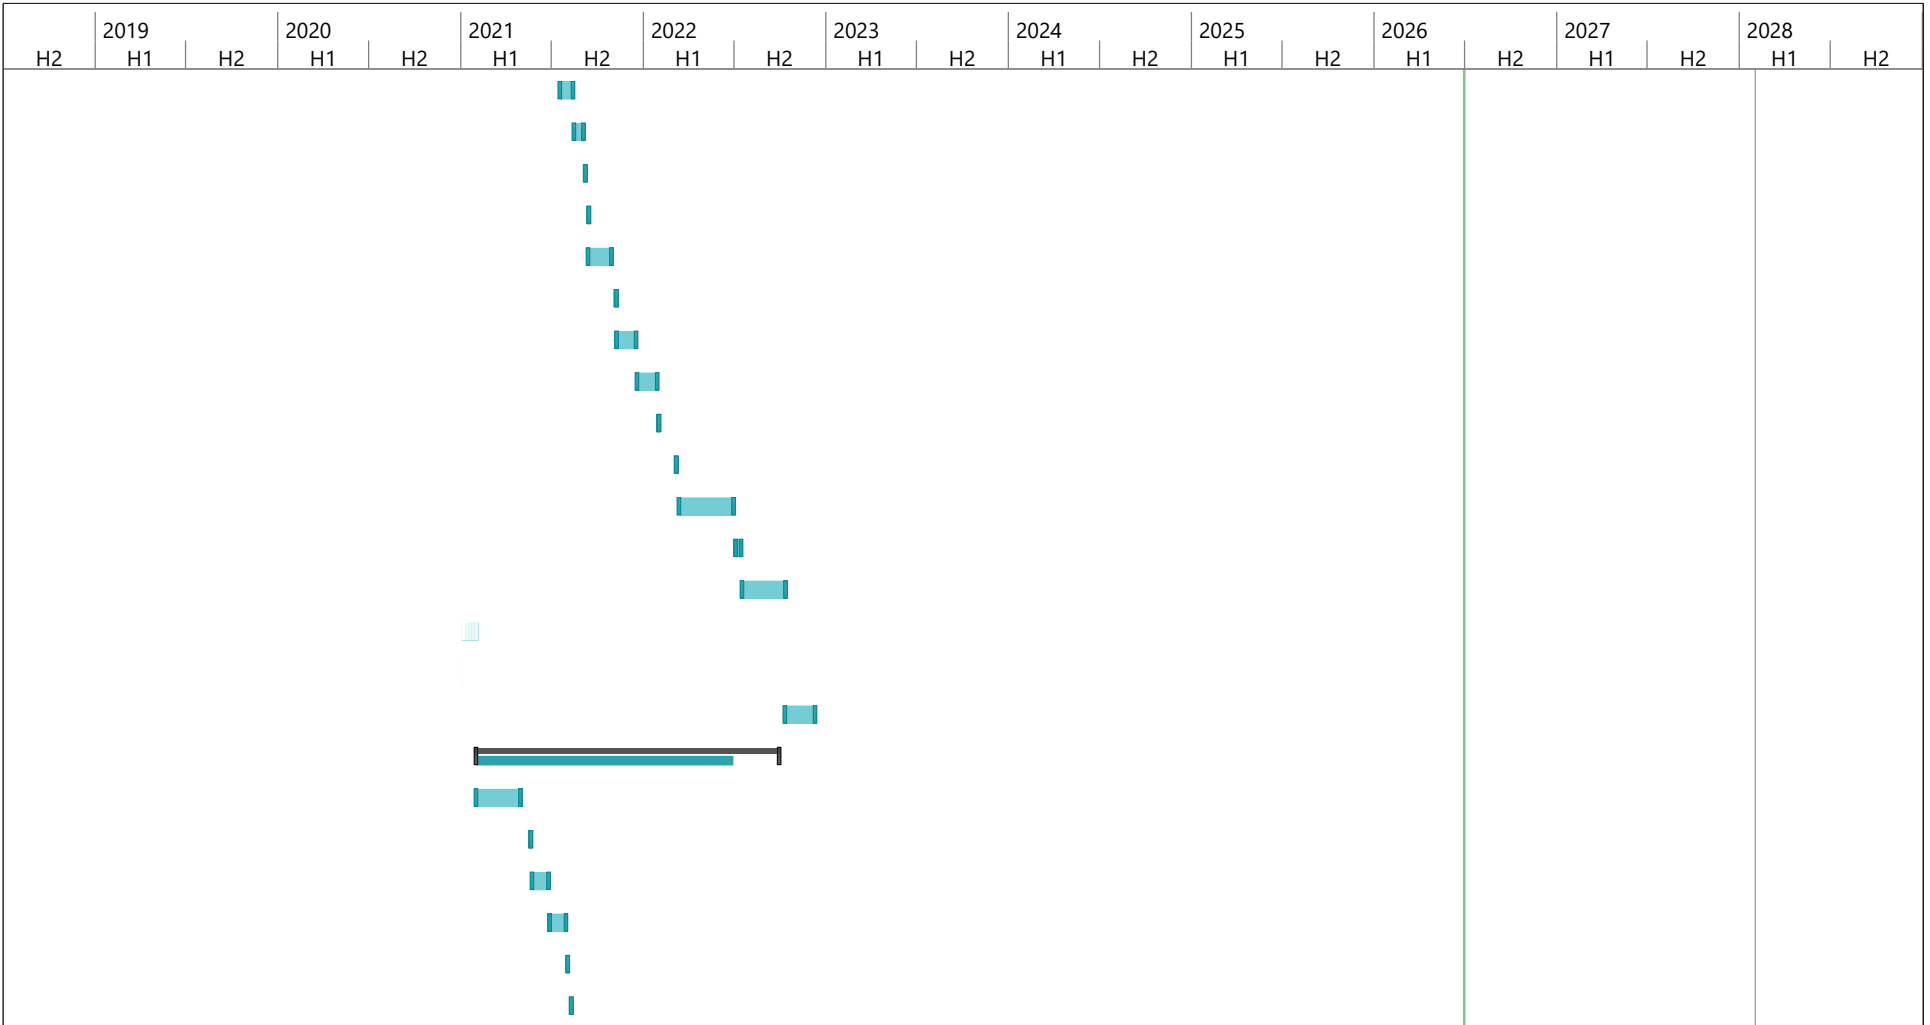


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

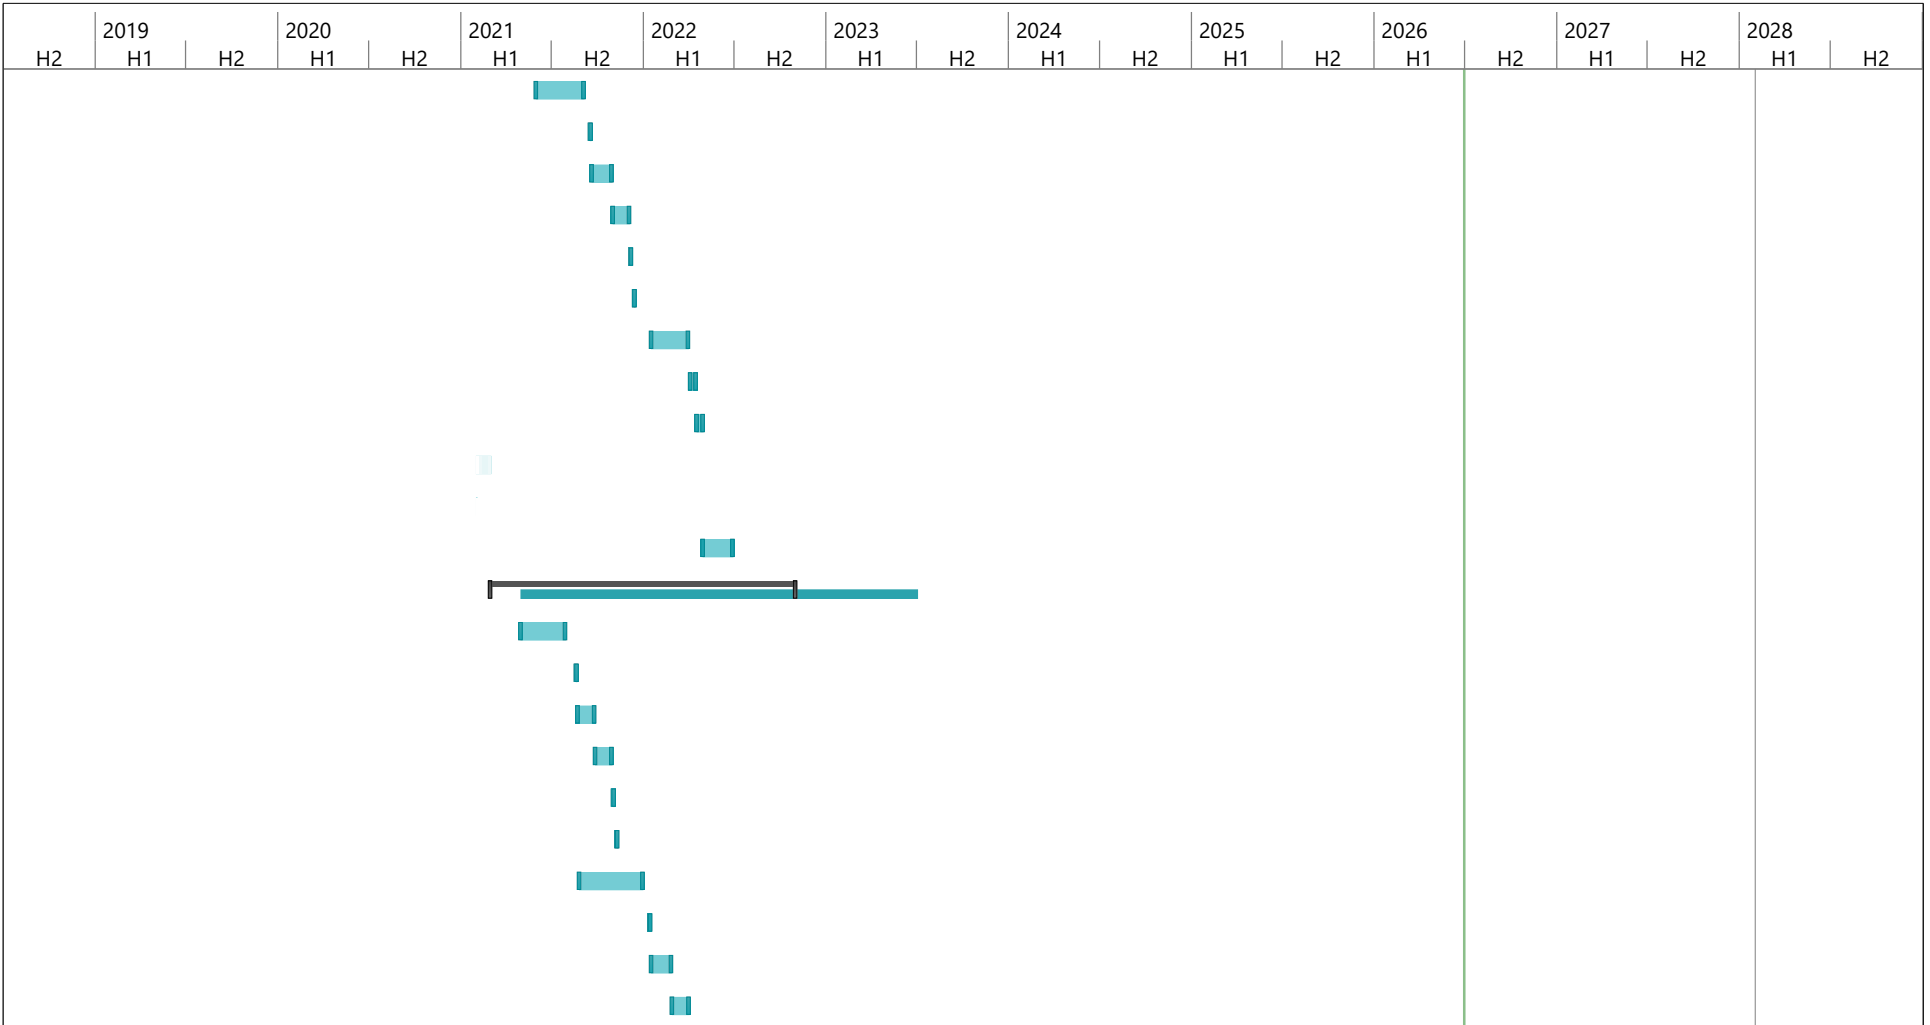


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

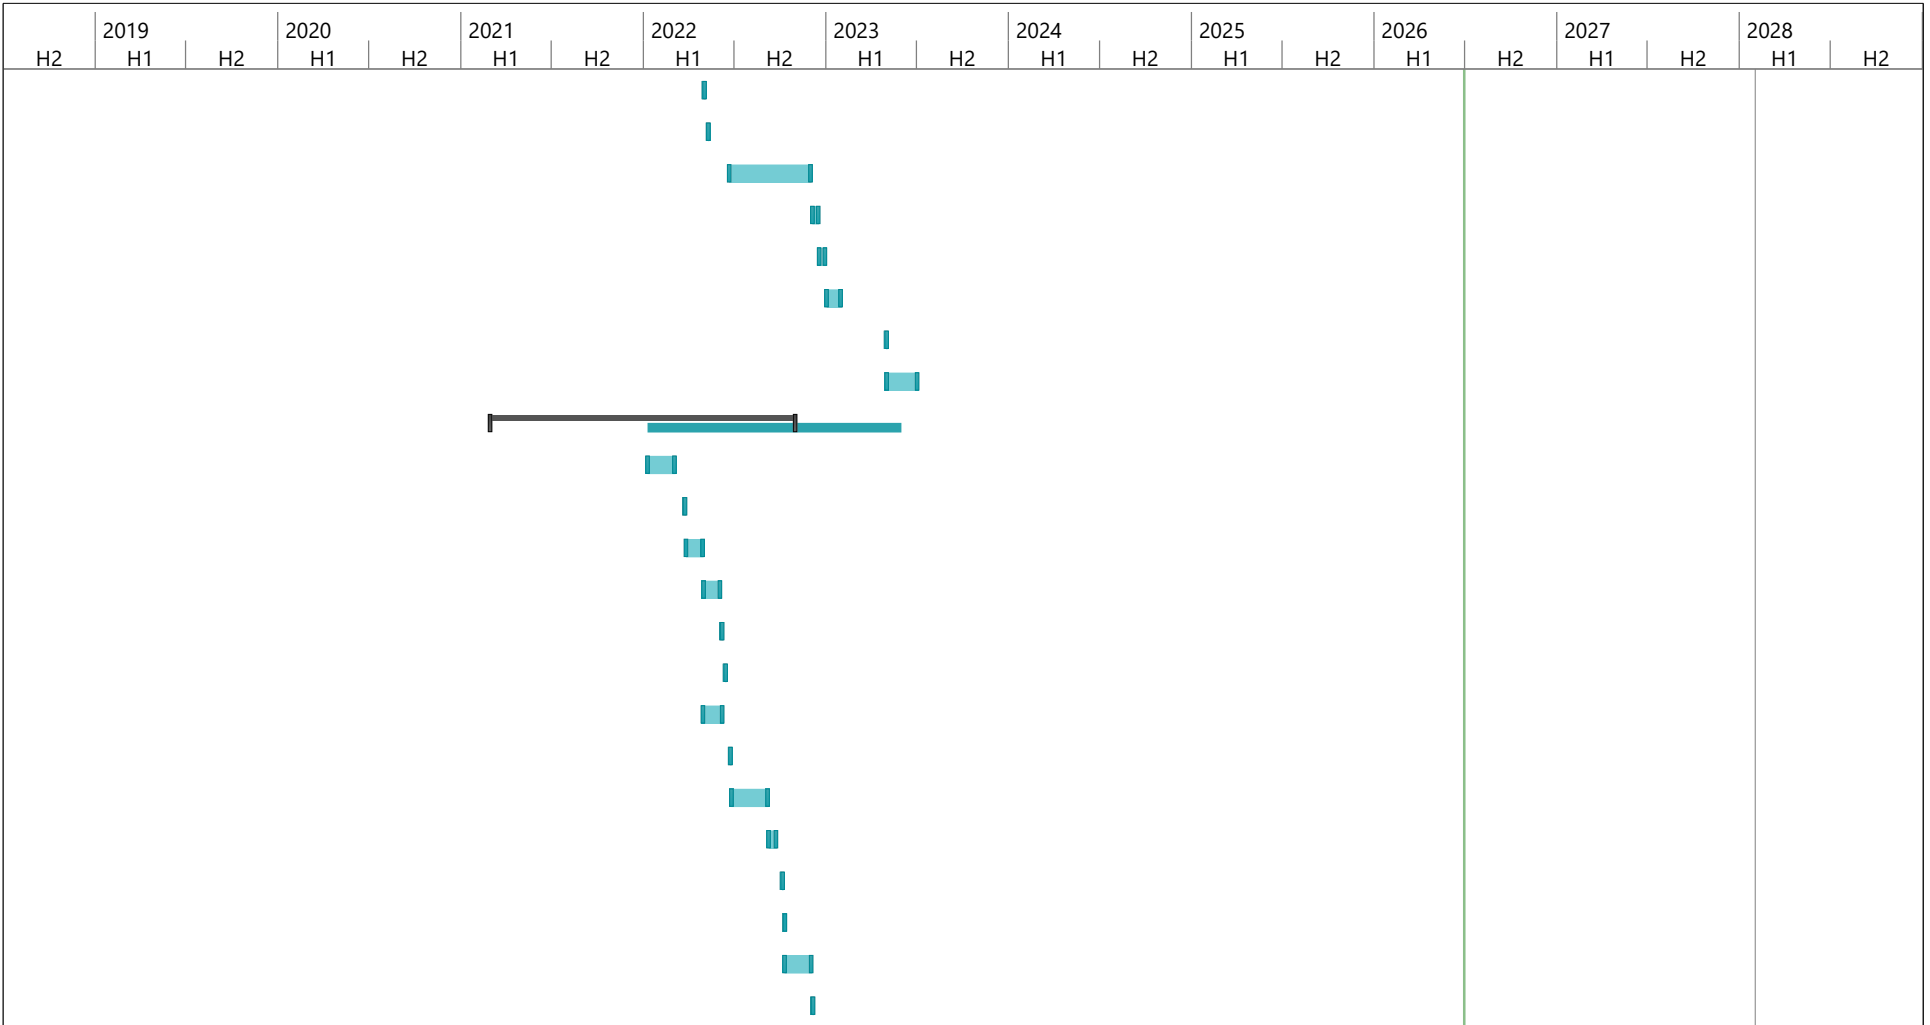


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

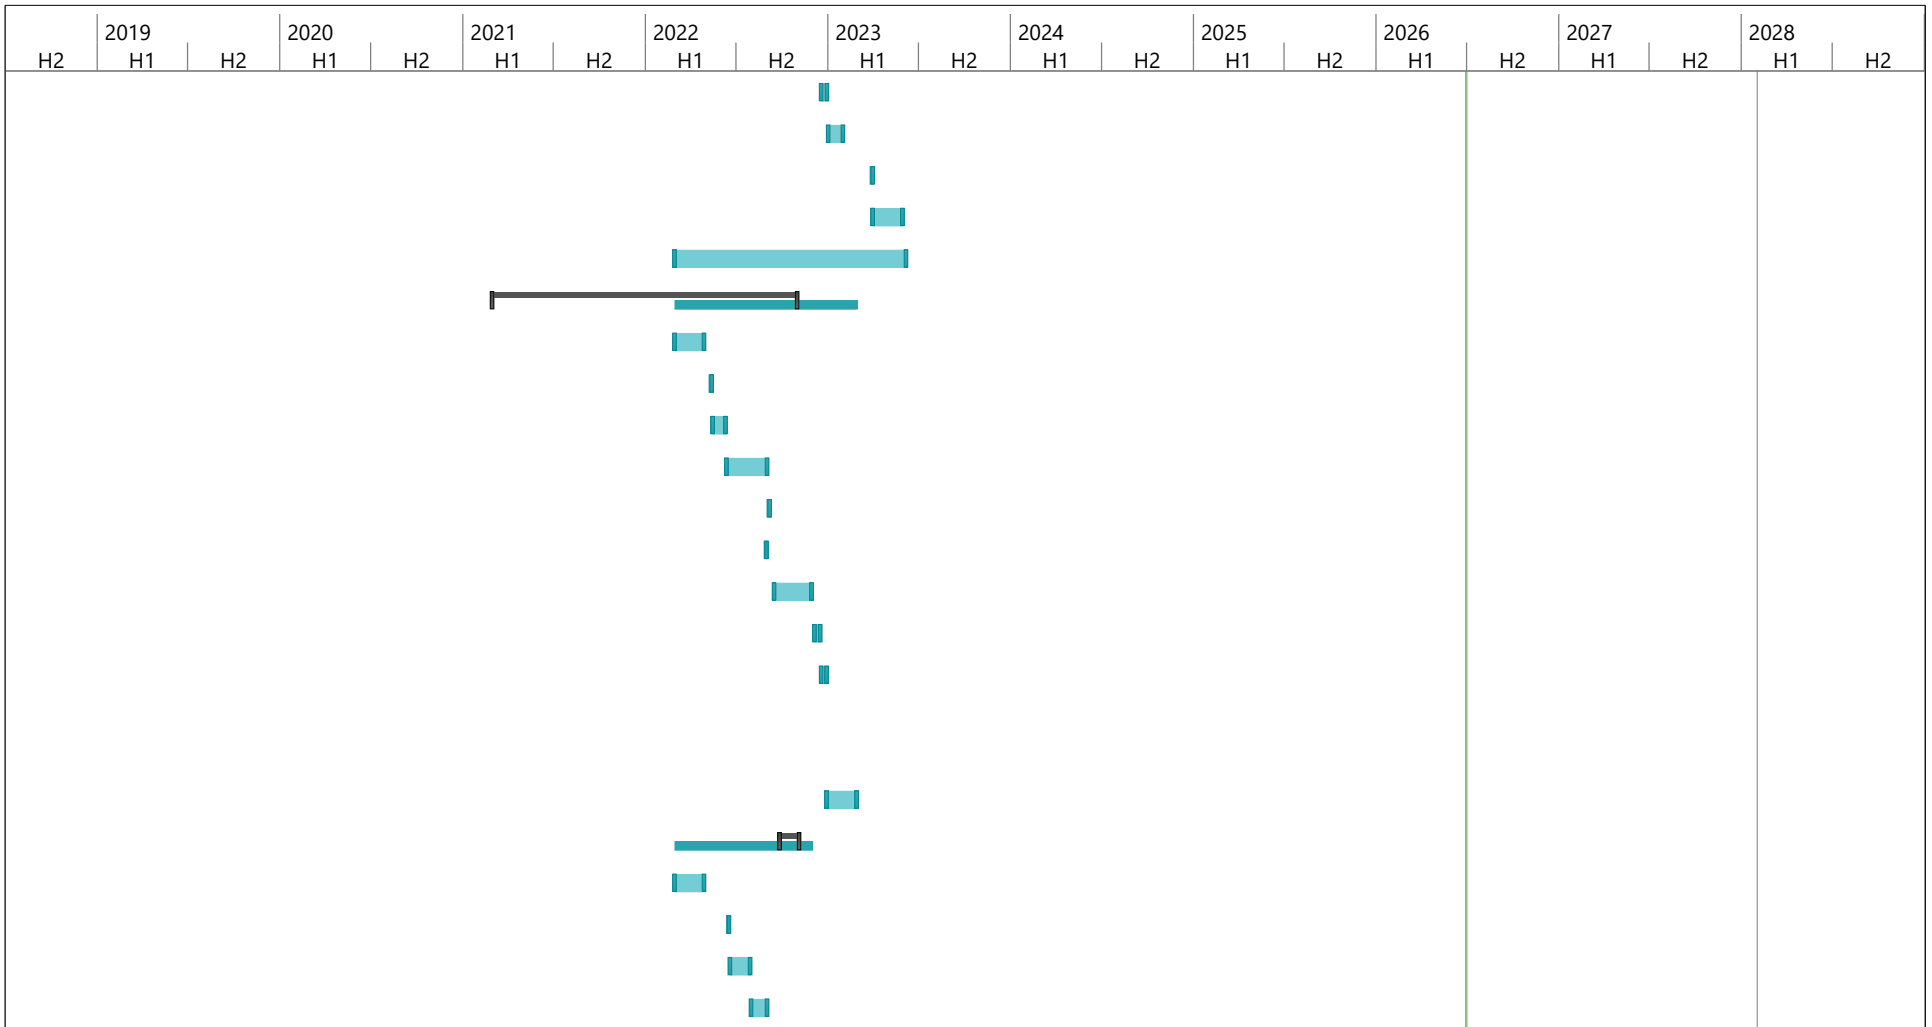


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

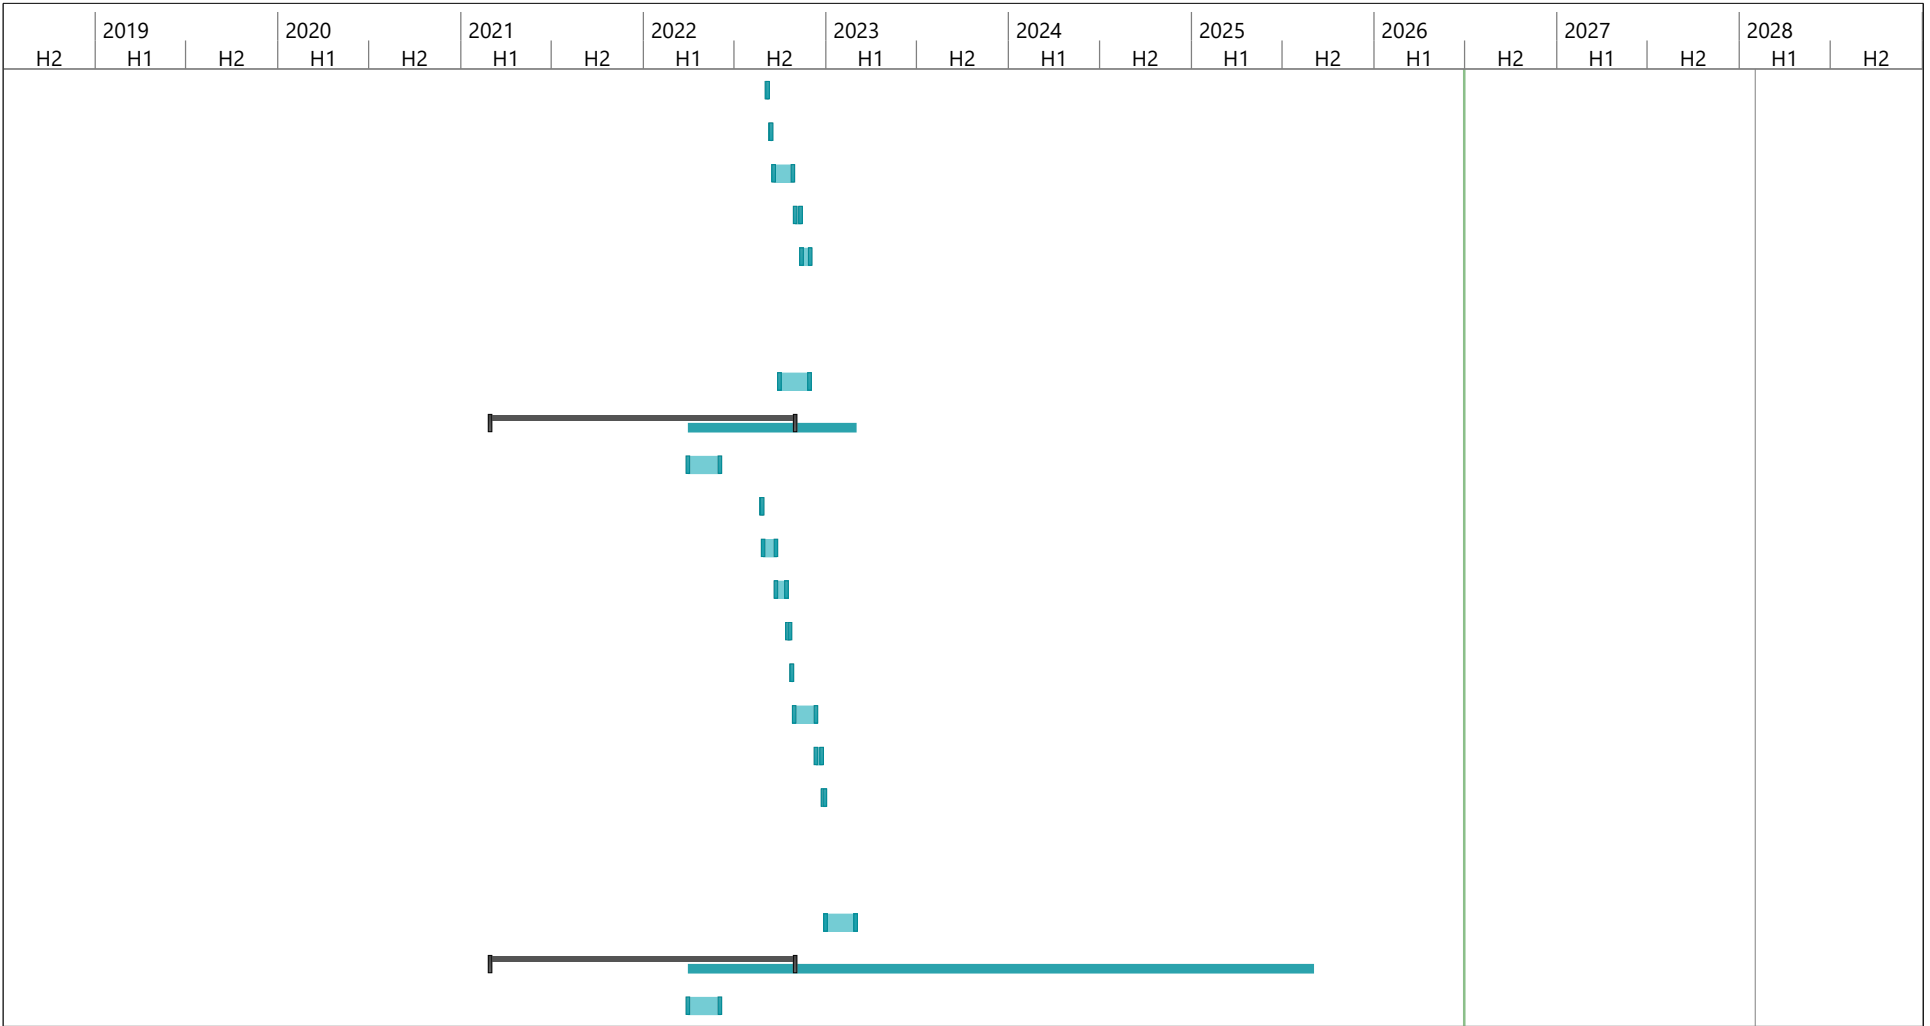


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

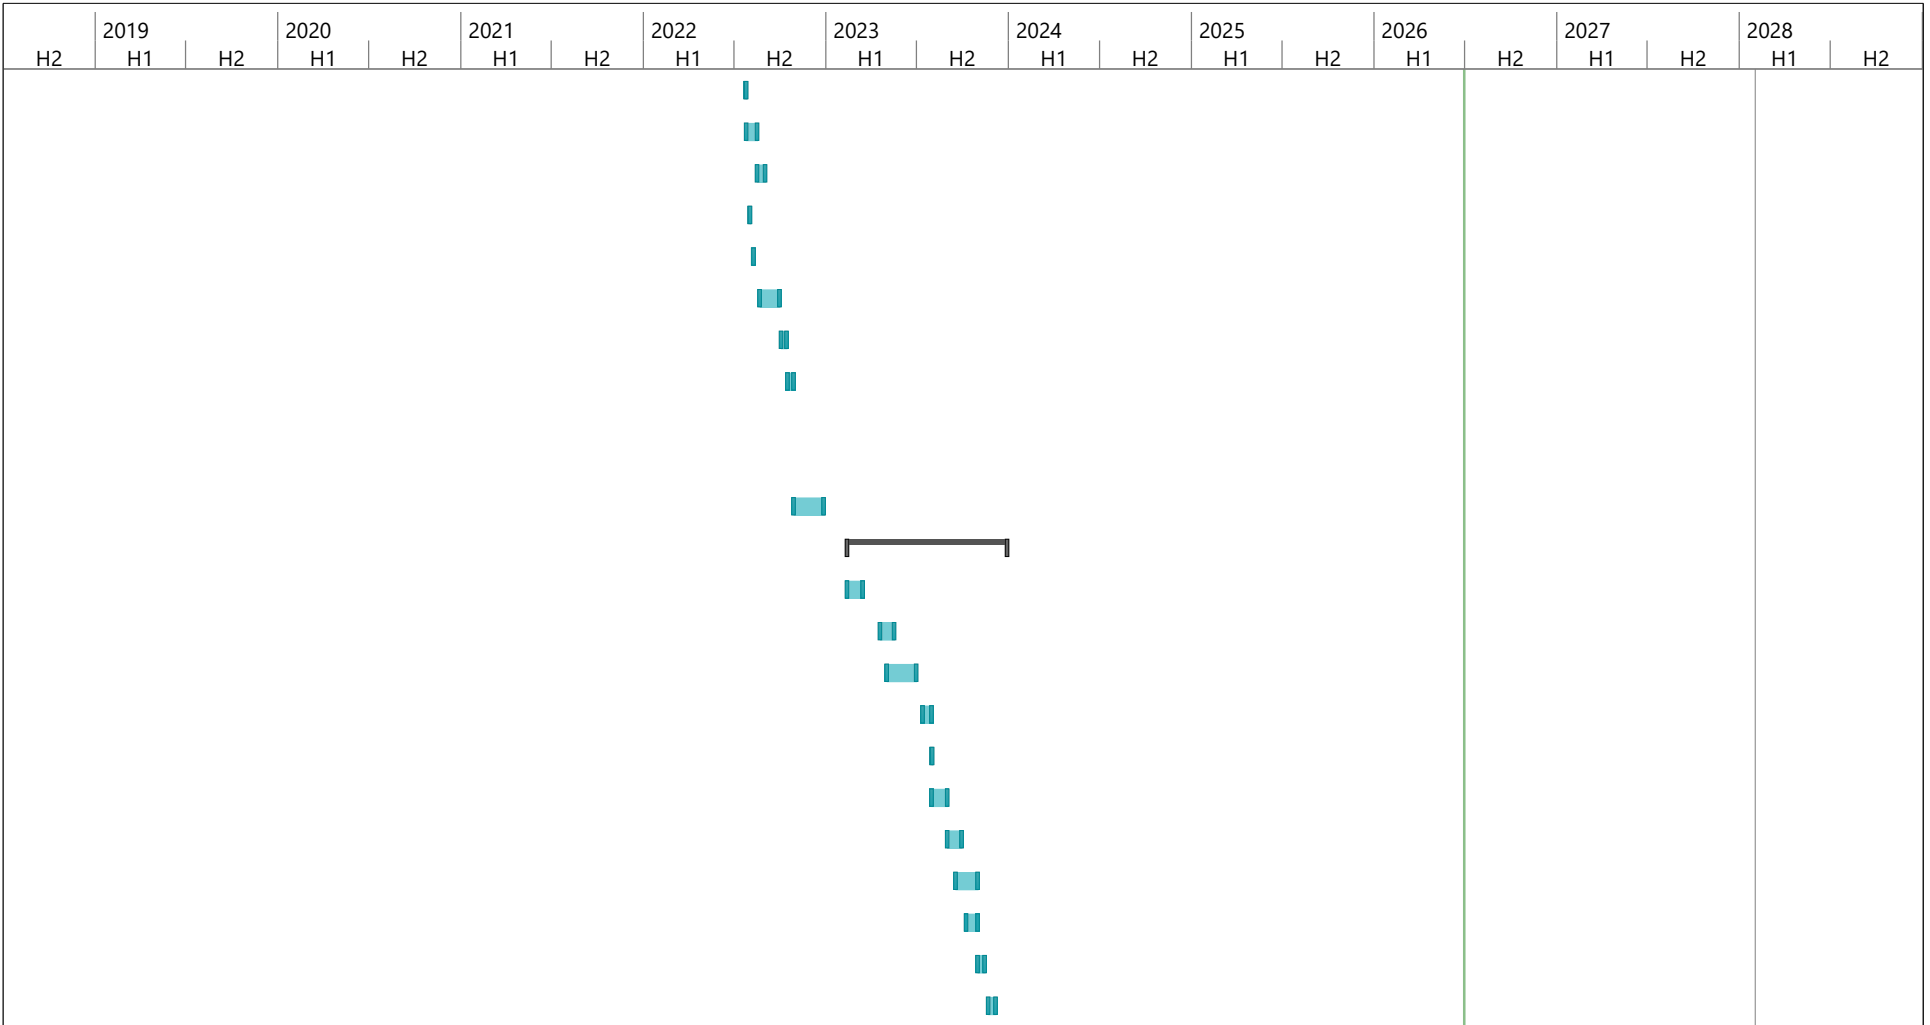


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

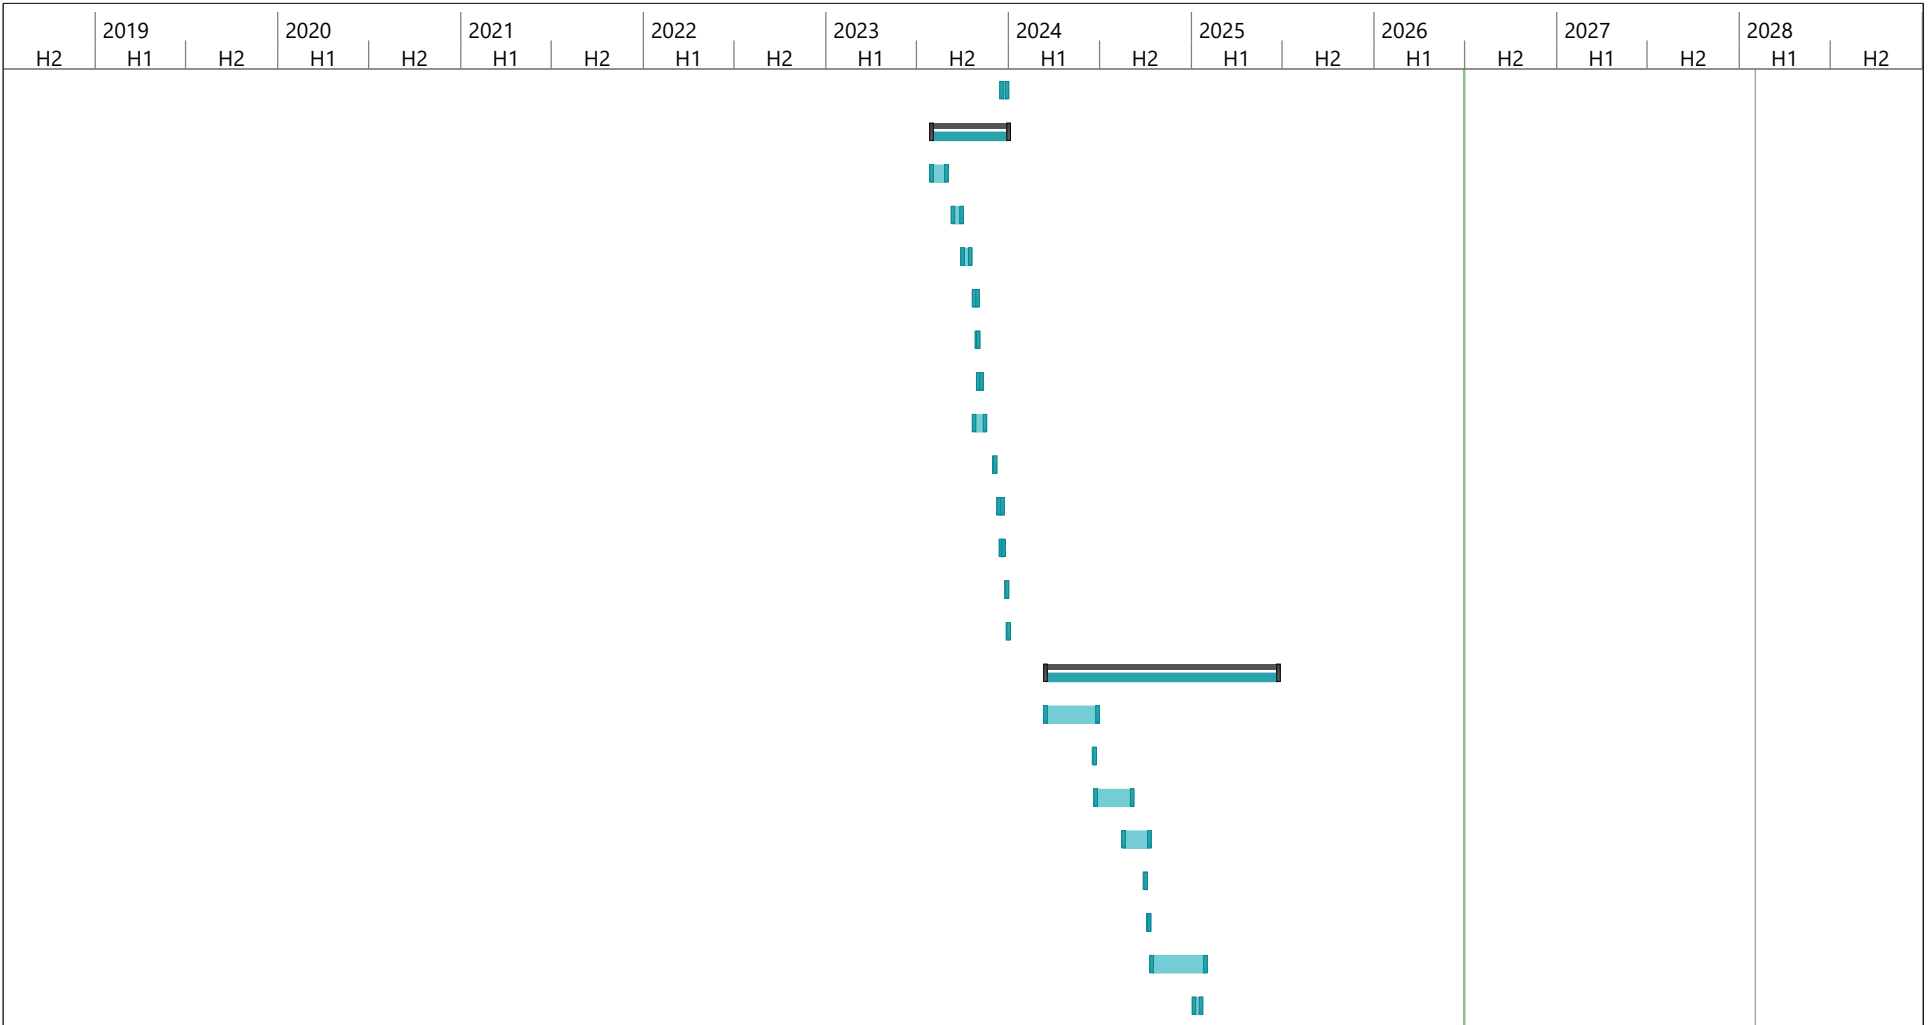


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

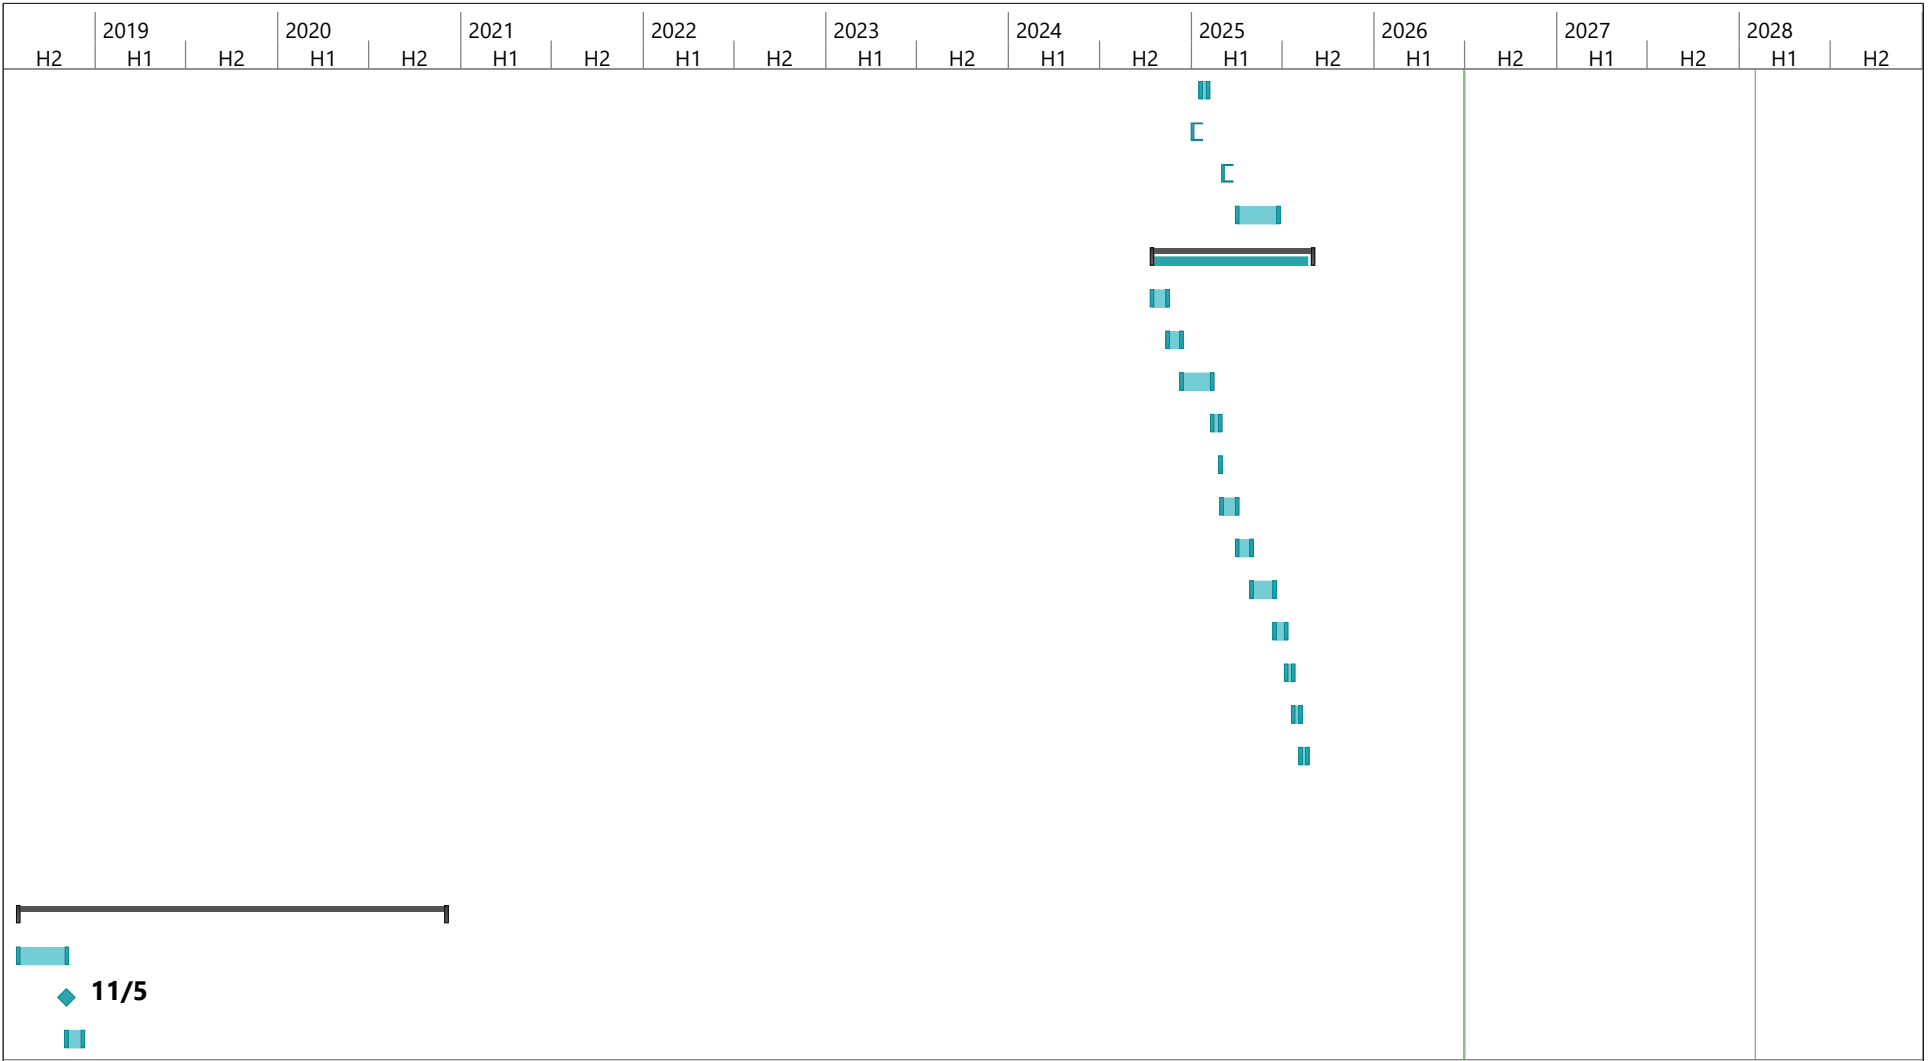


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

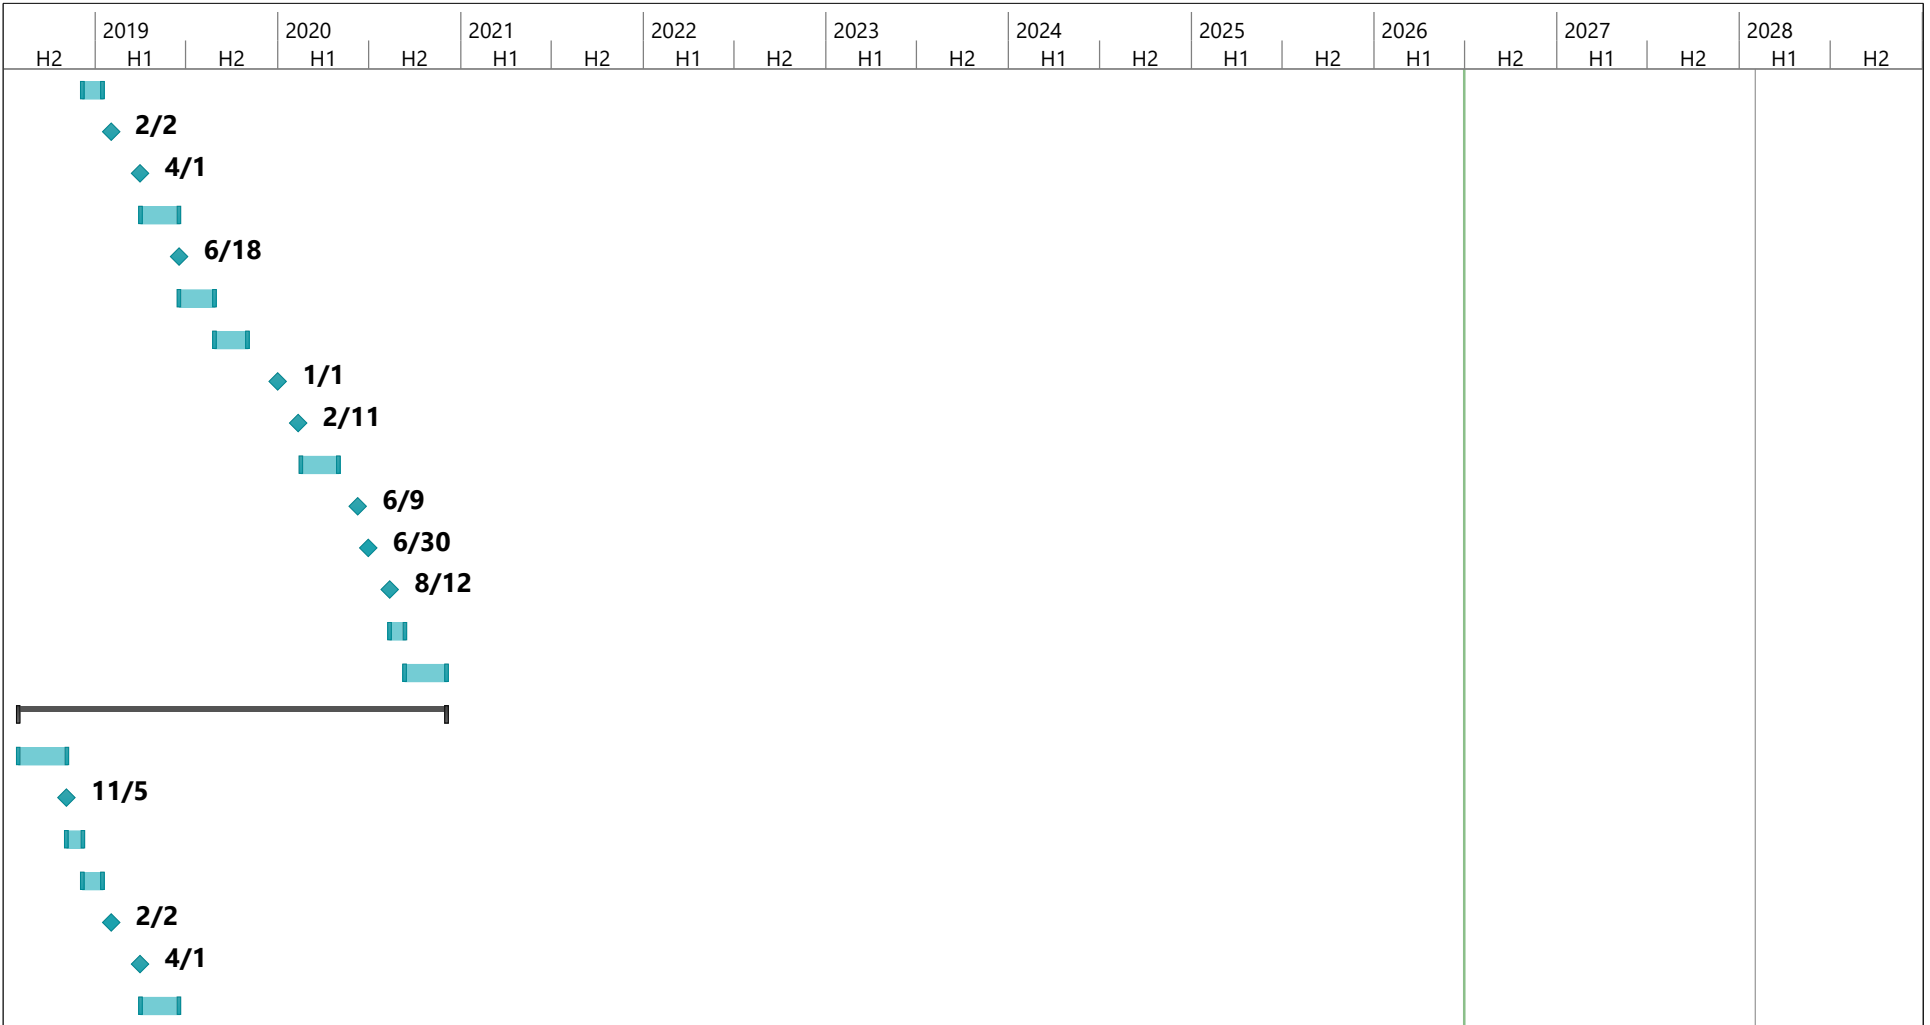


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

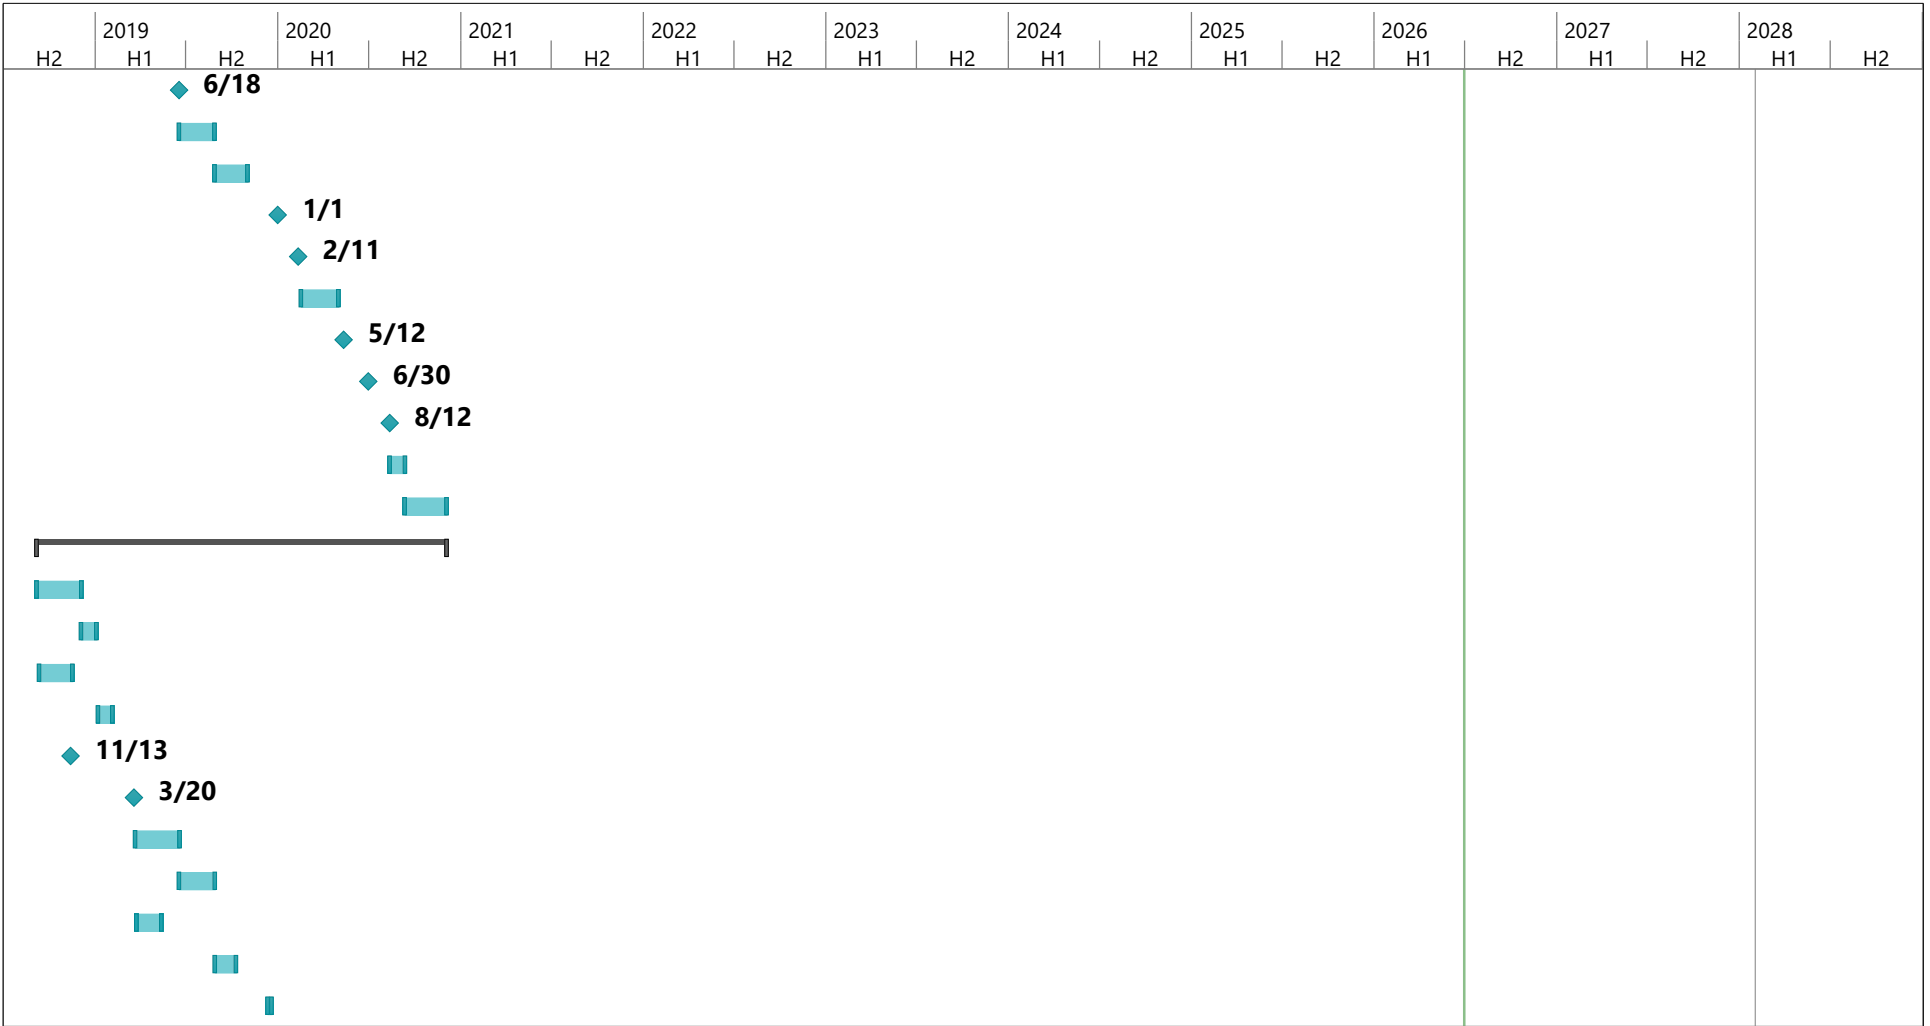


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

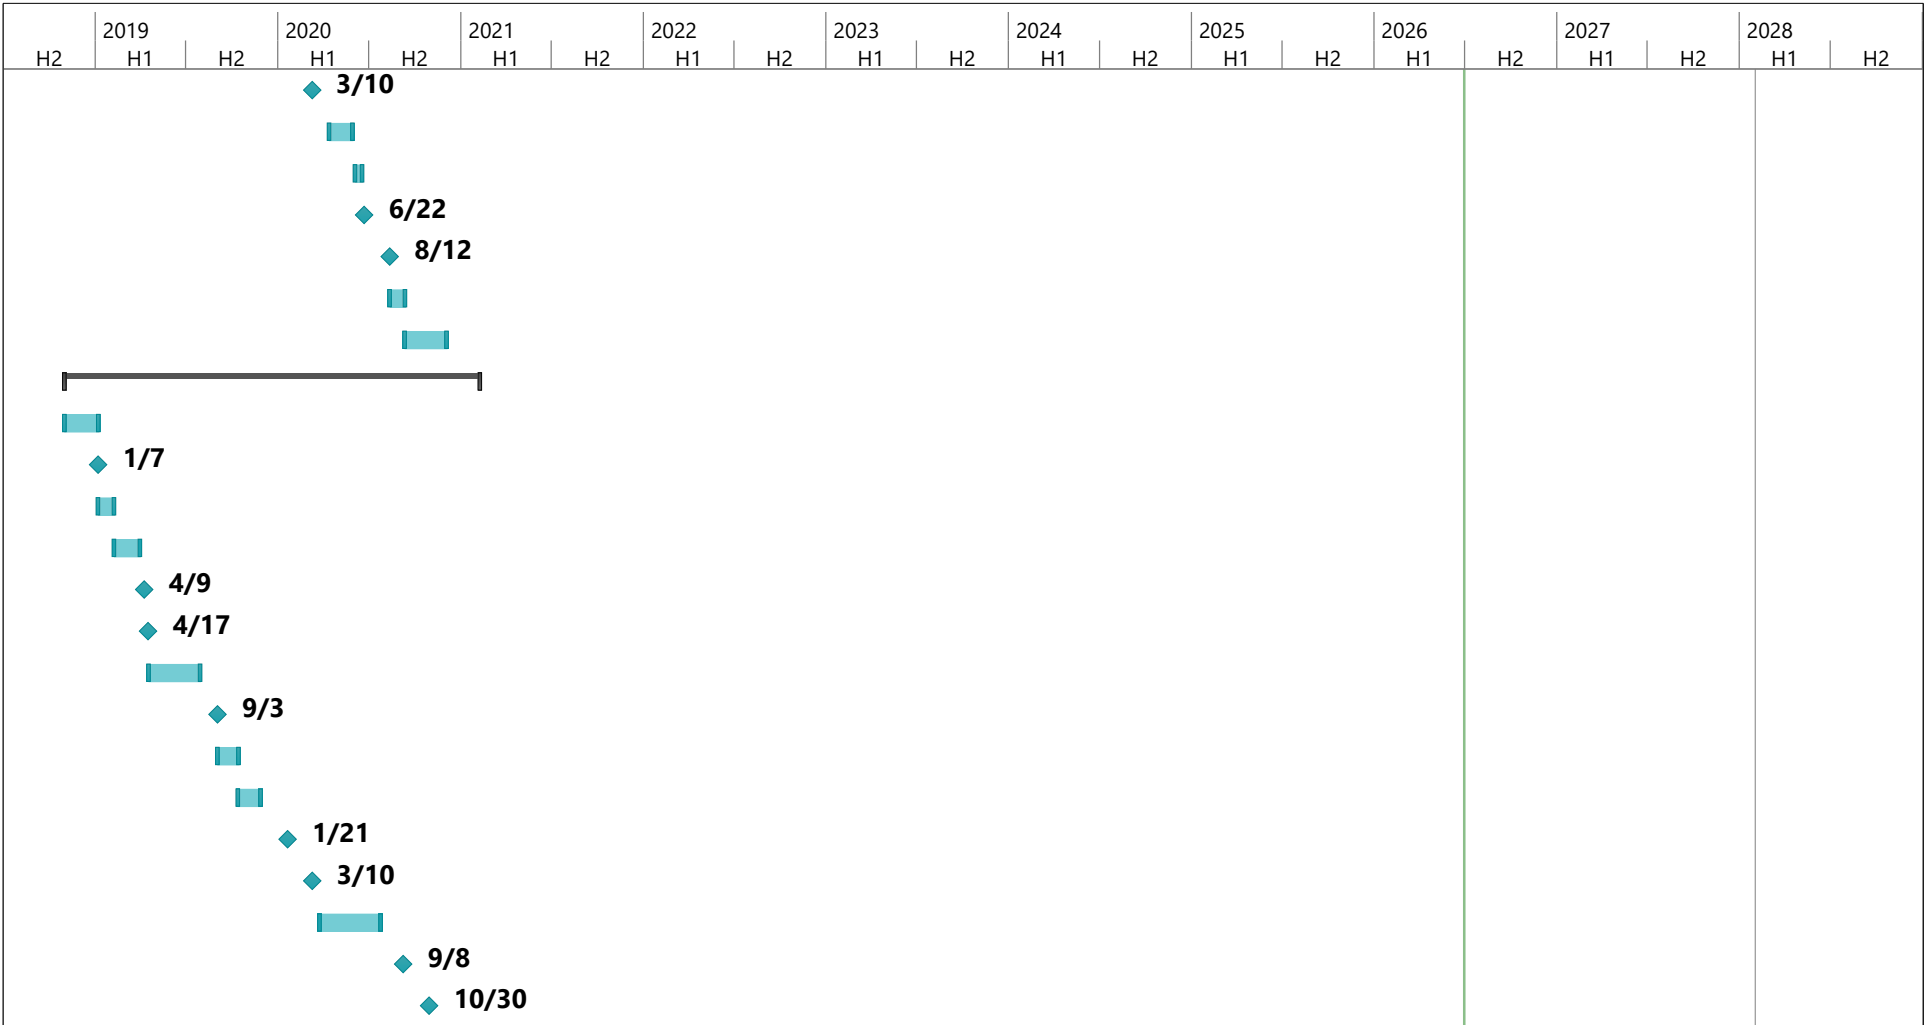


Project: IOU Master Task Timeli  
 Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

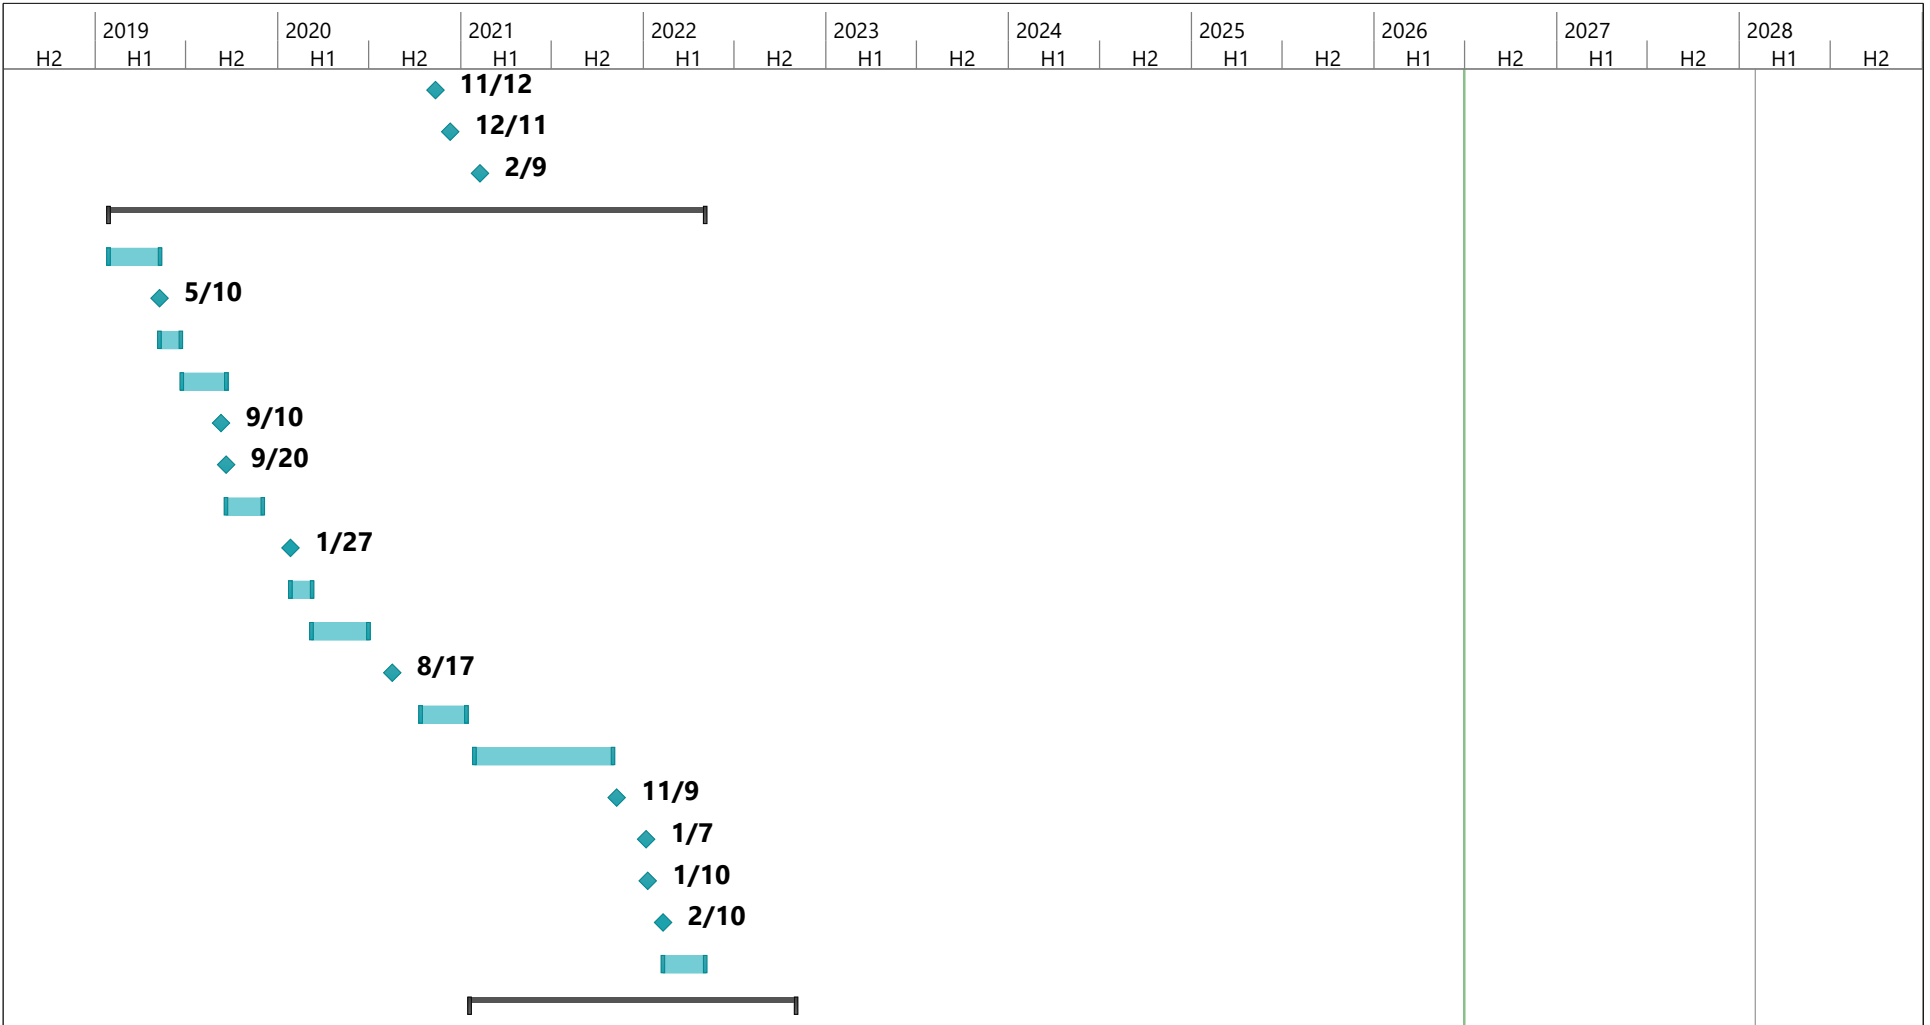


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

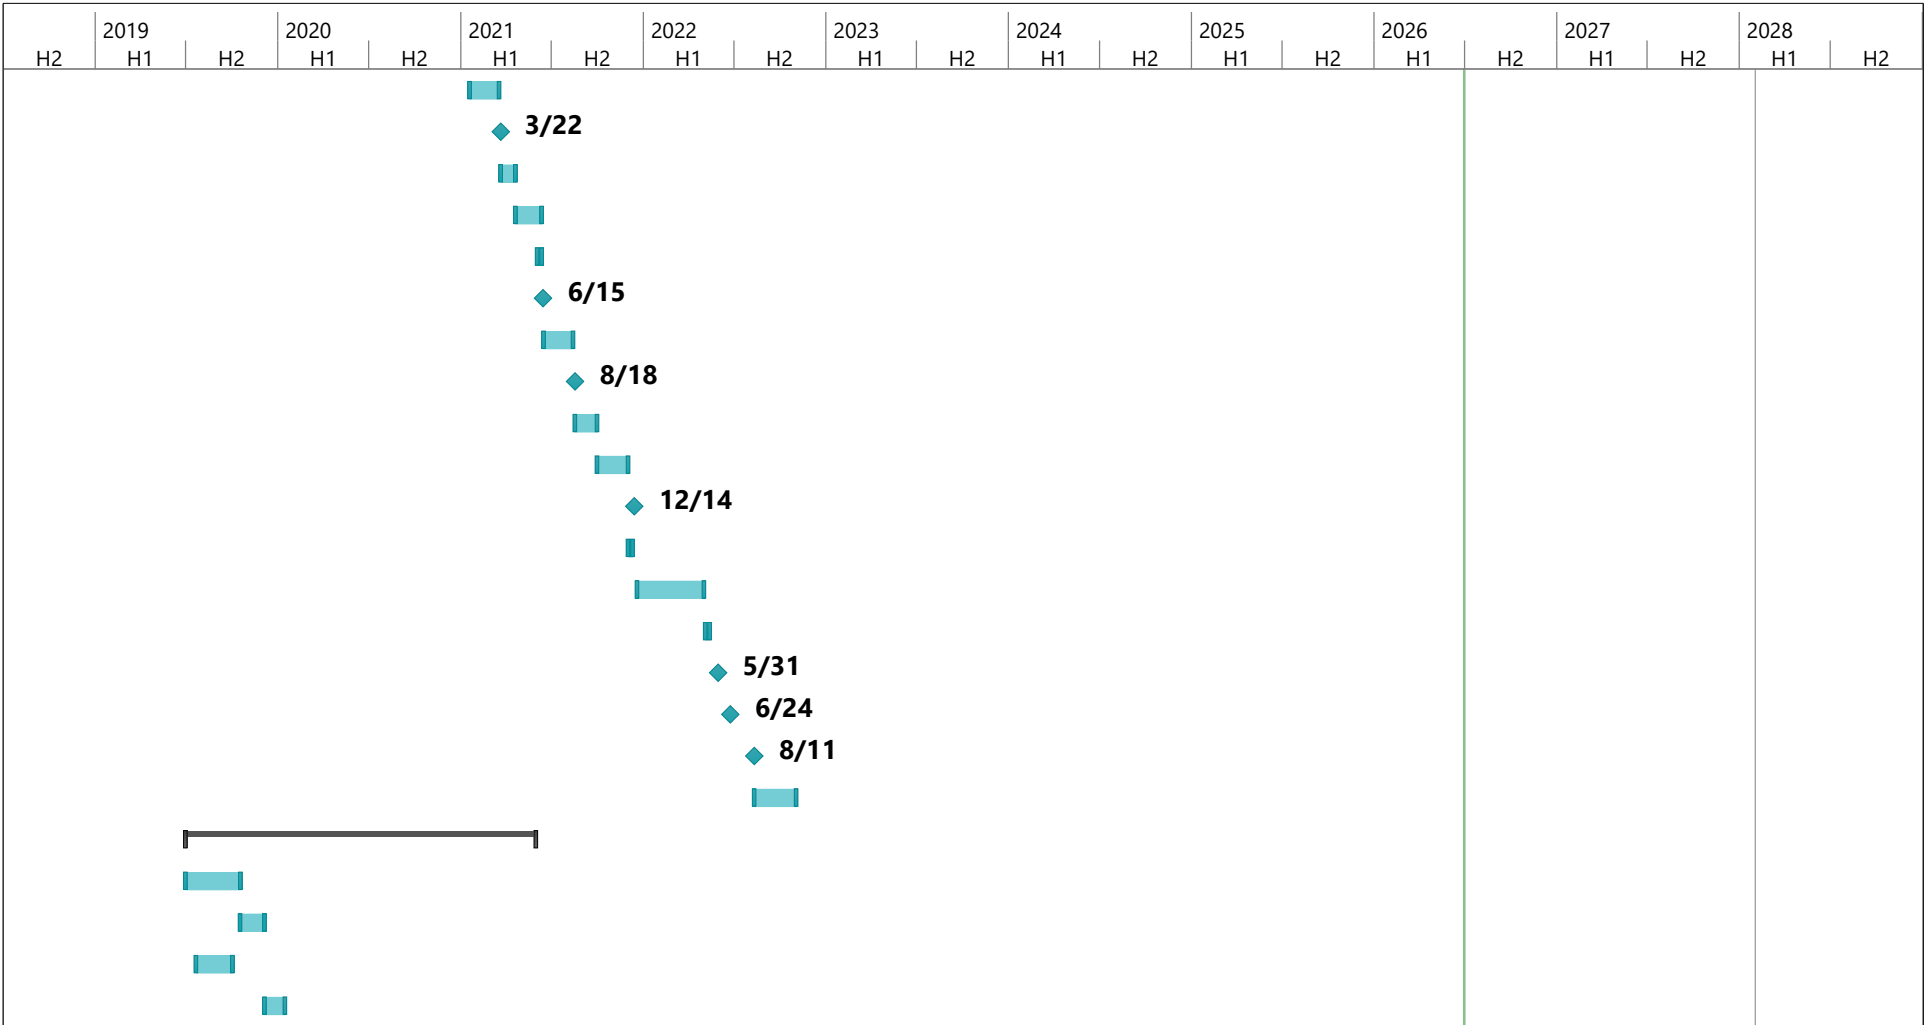


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

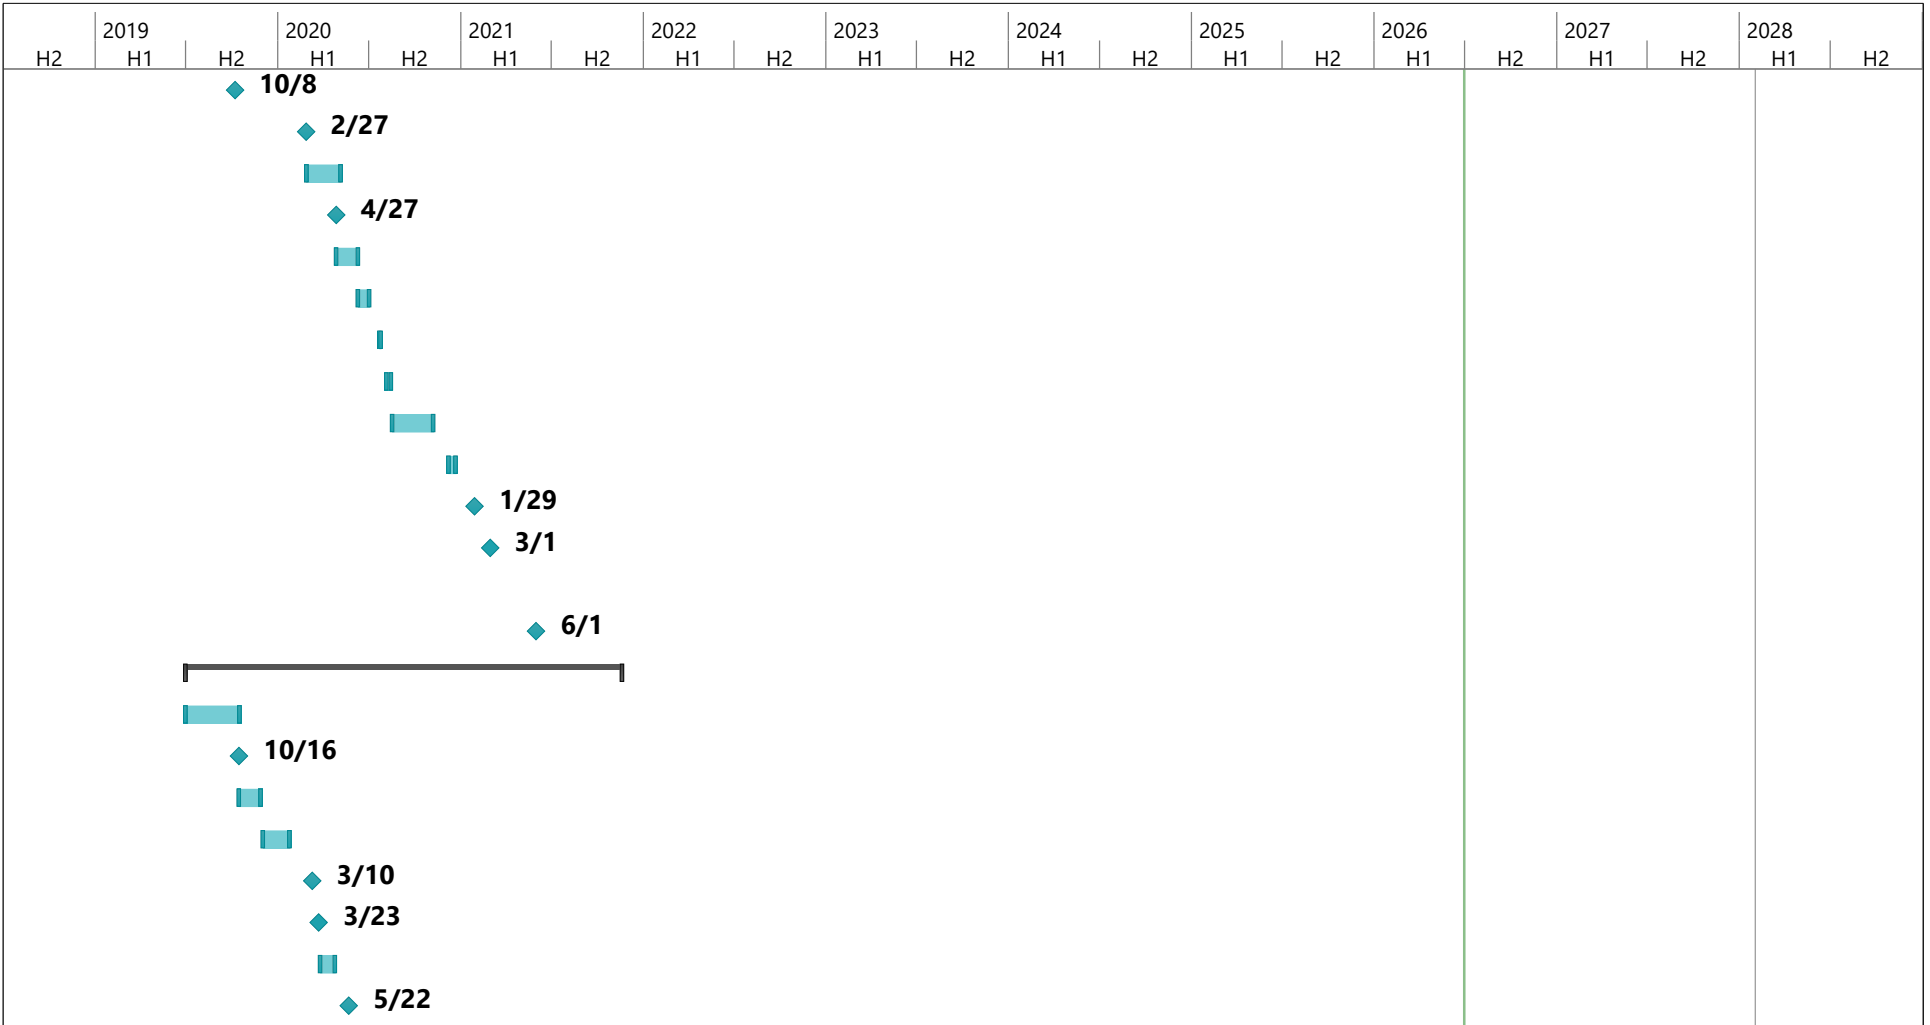


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

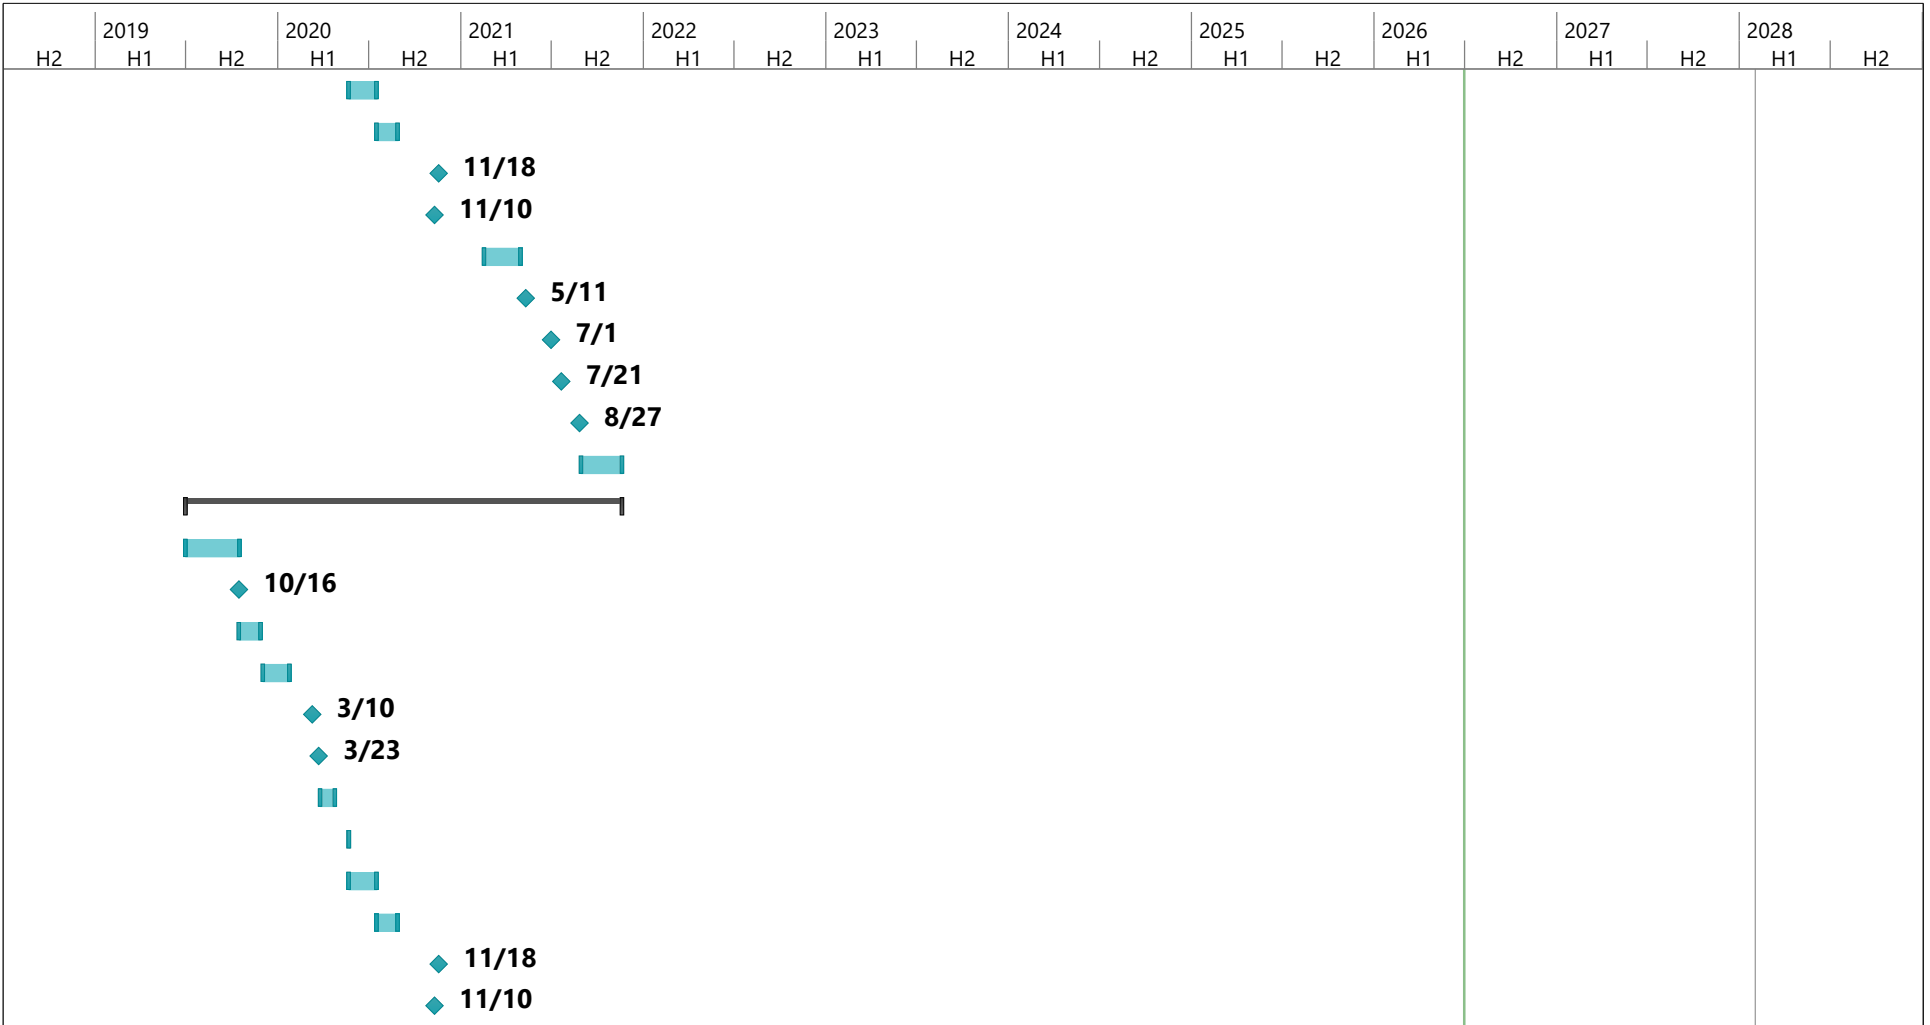


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

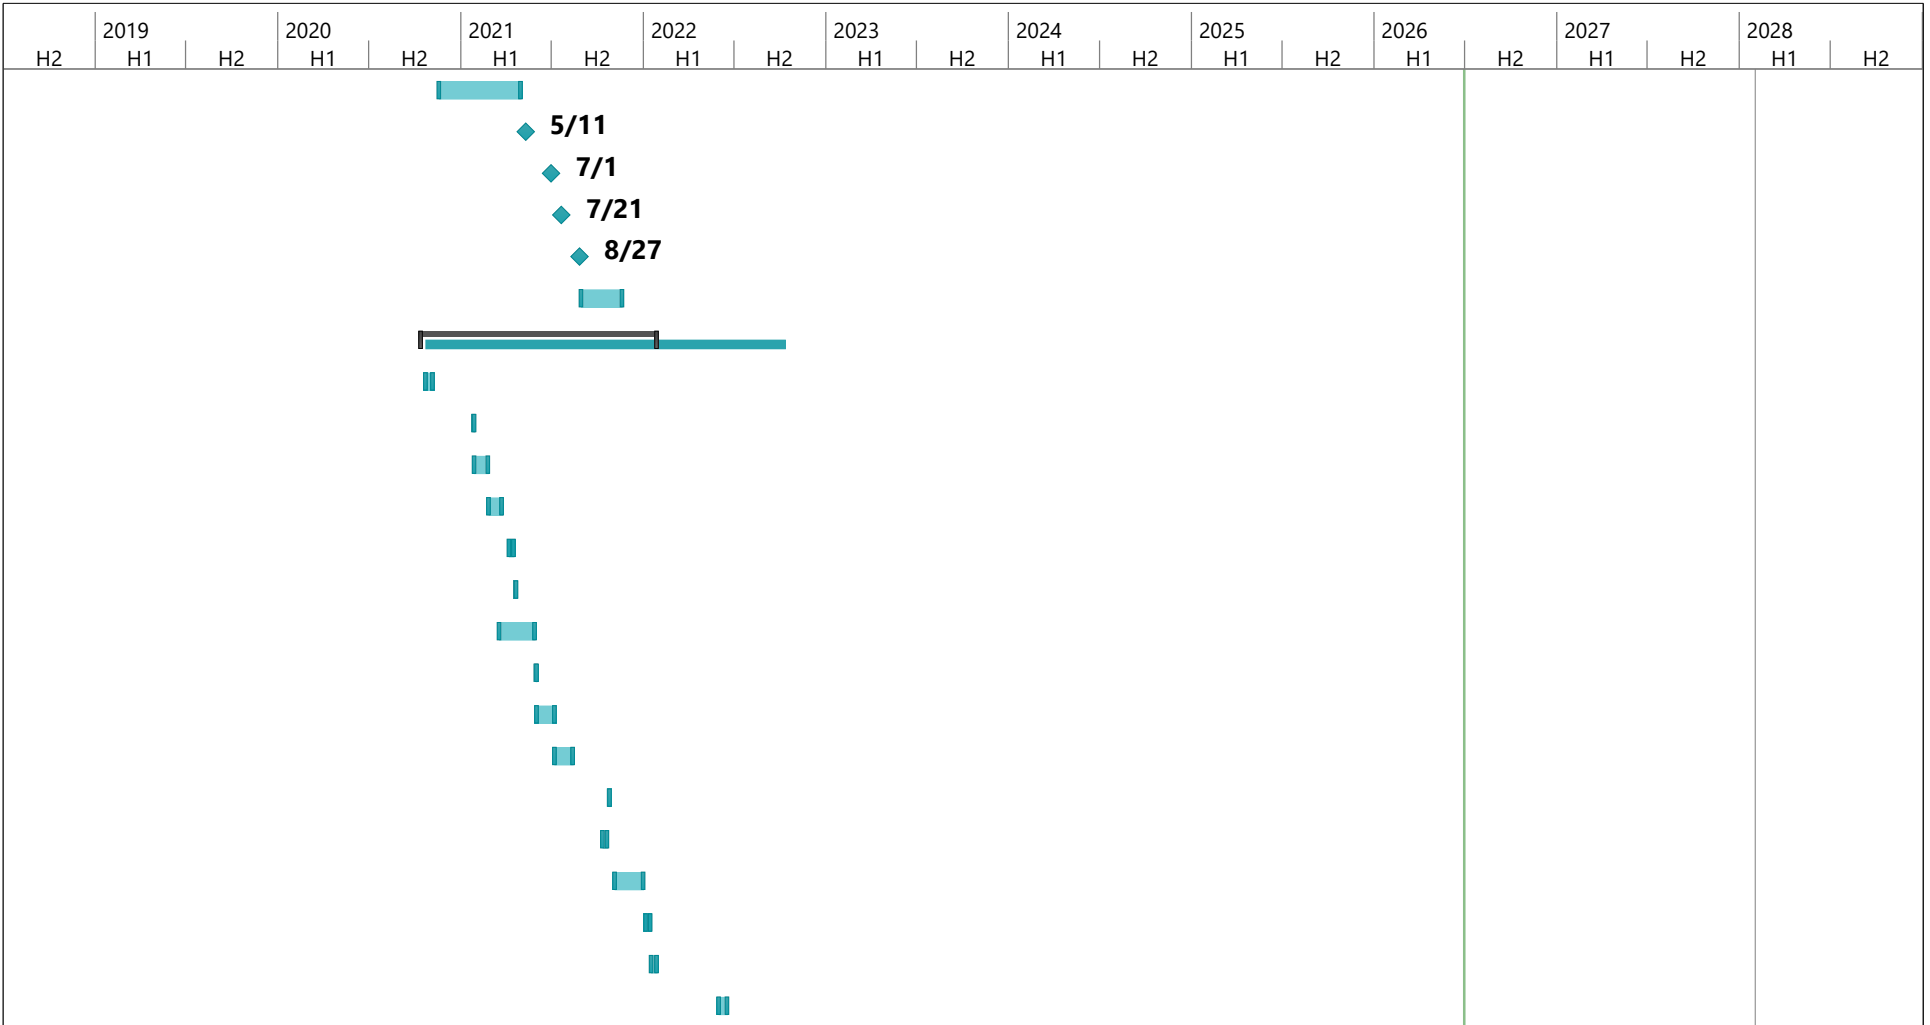


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

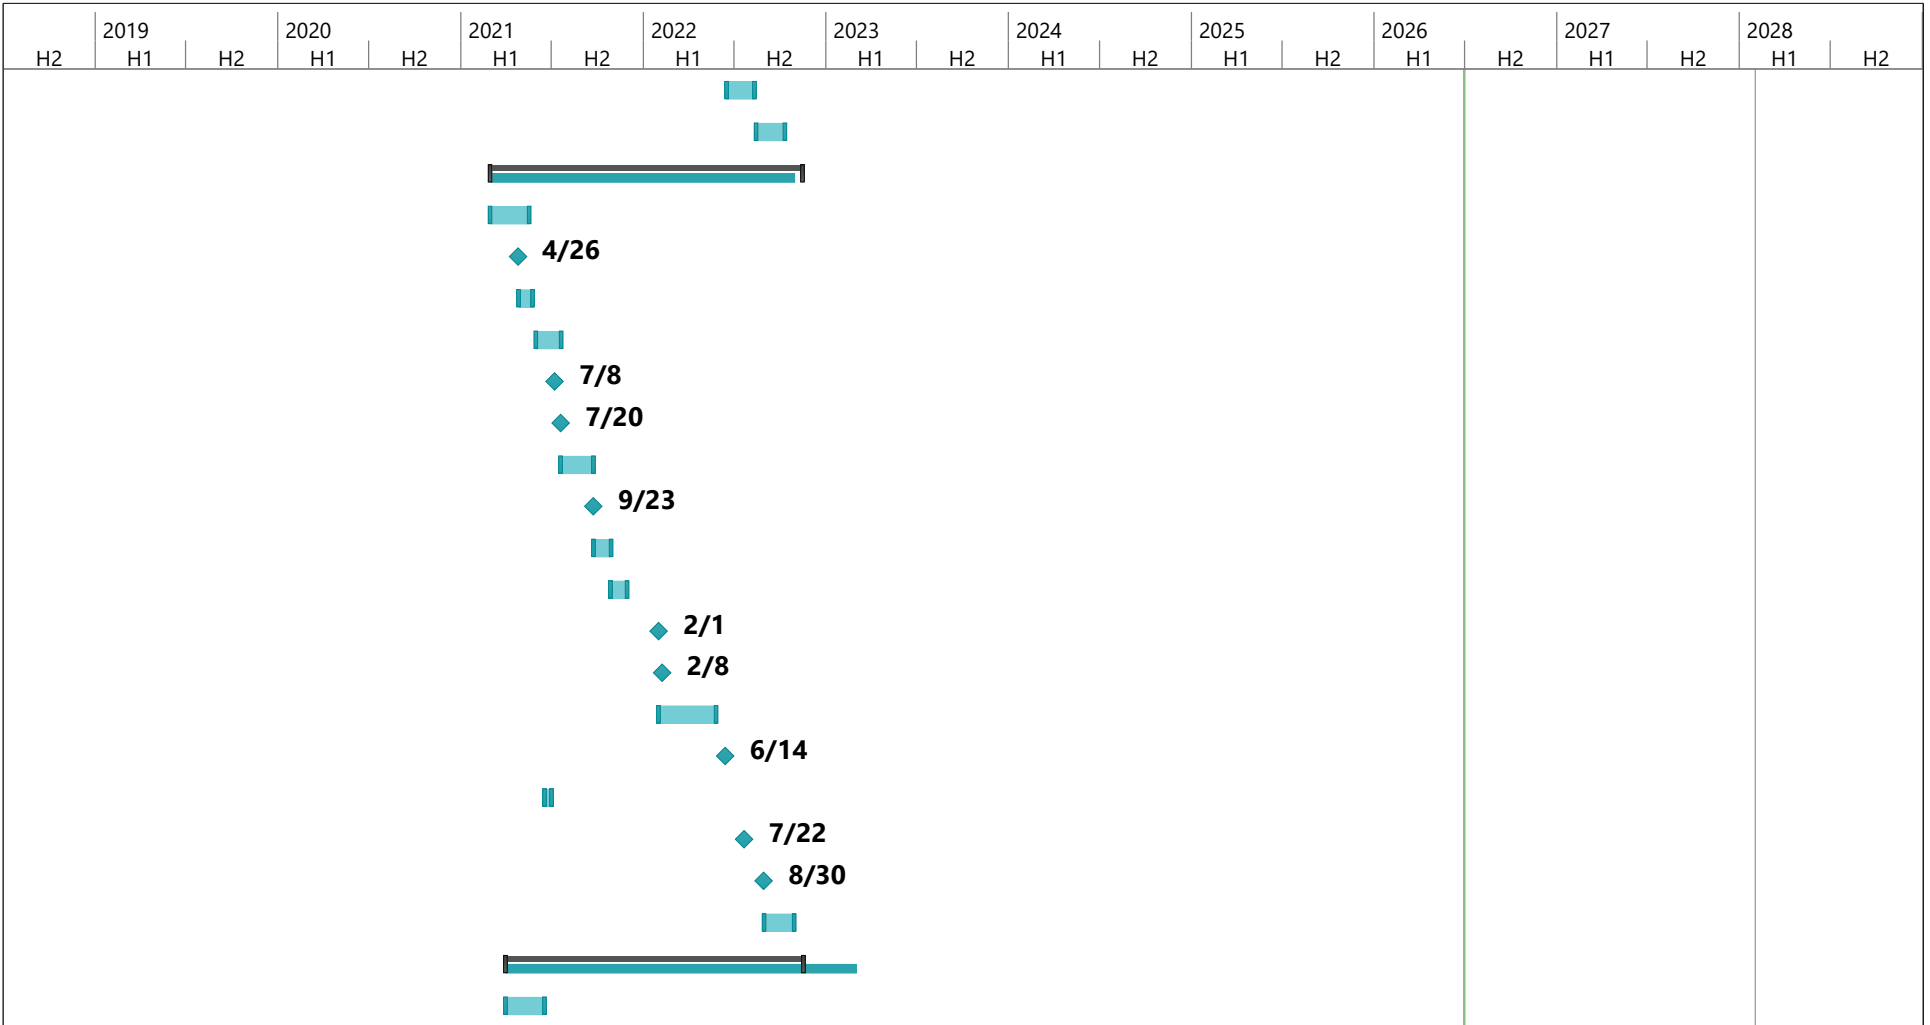


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

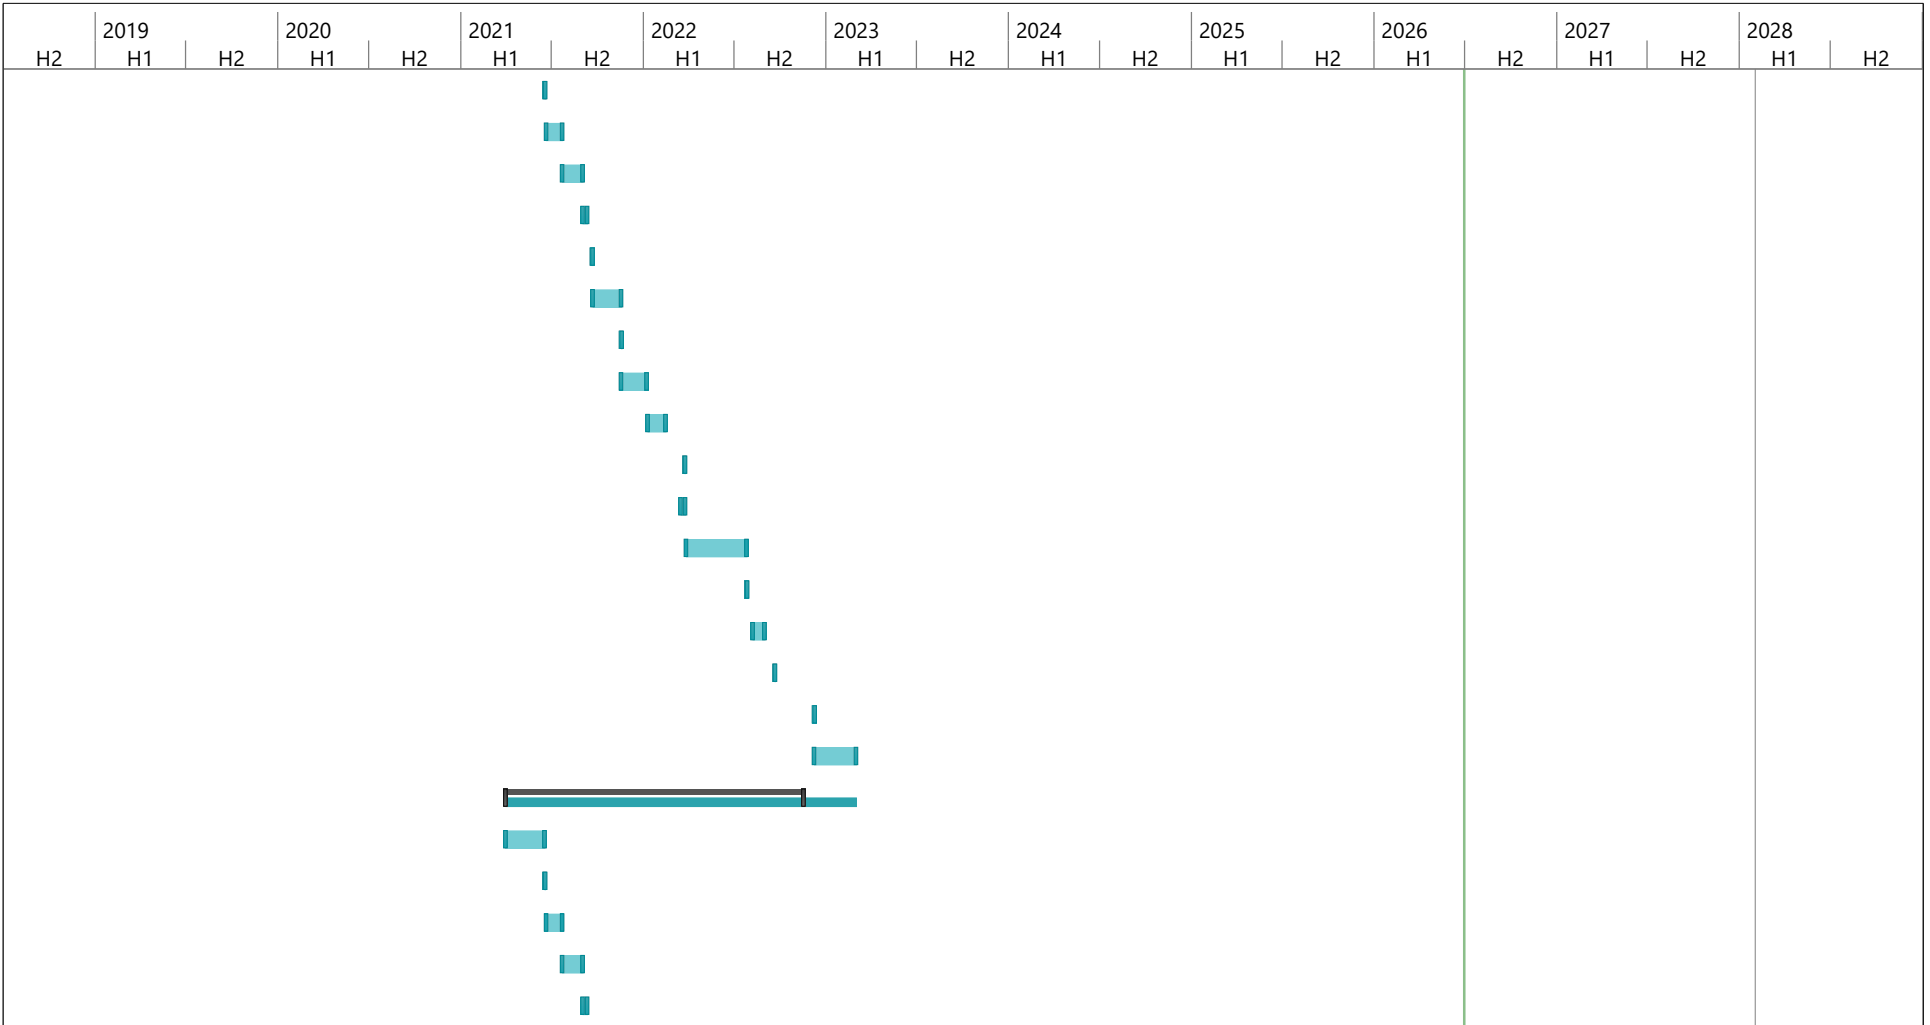


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

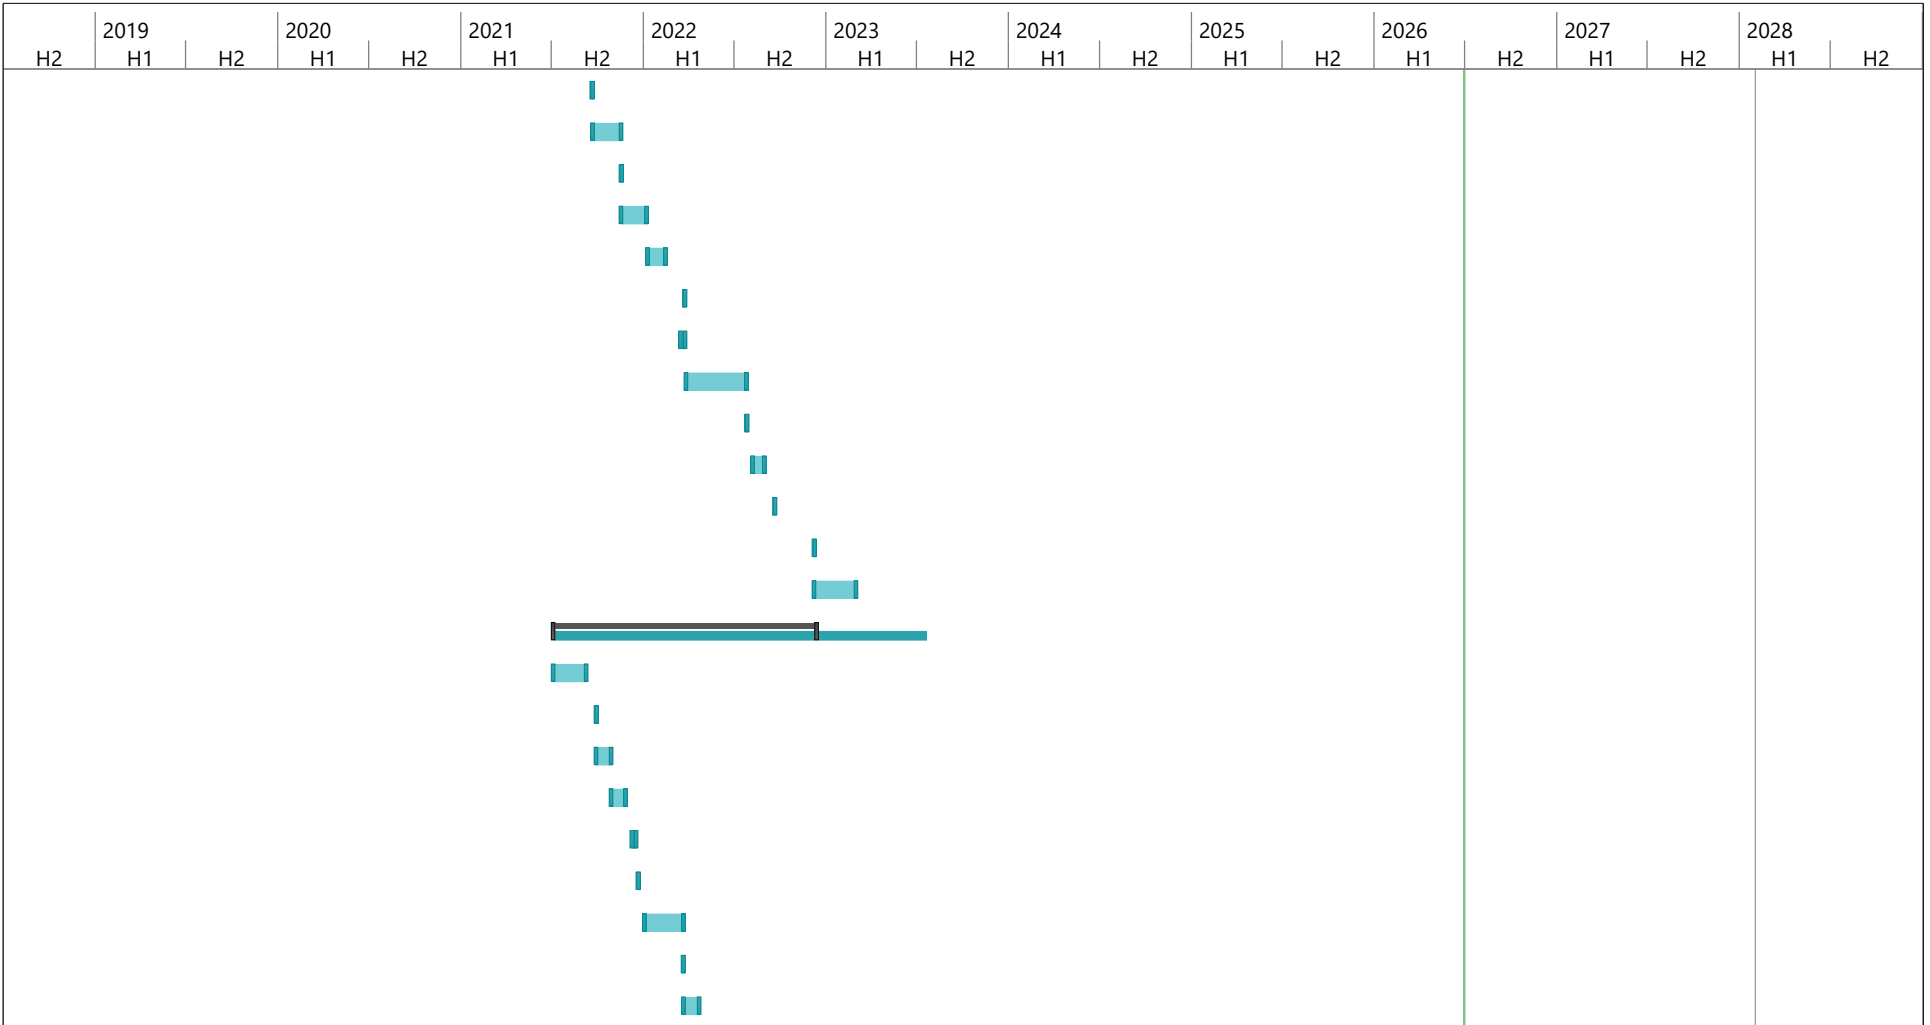


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

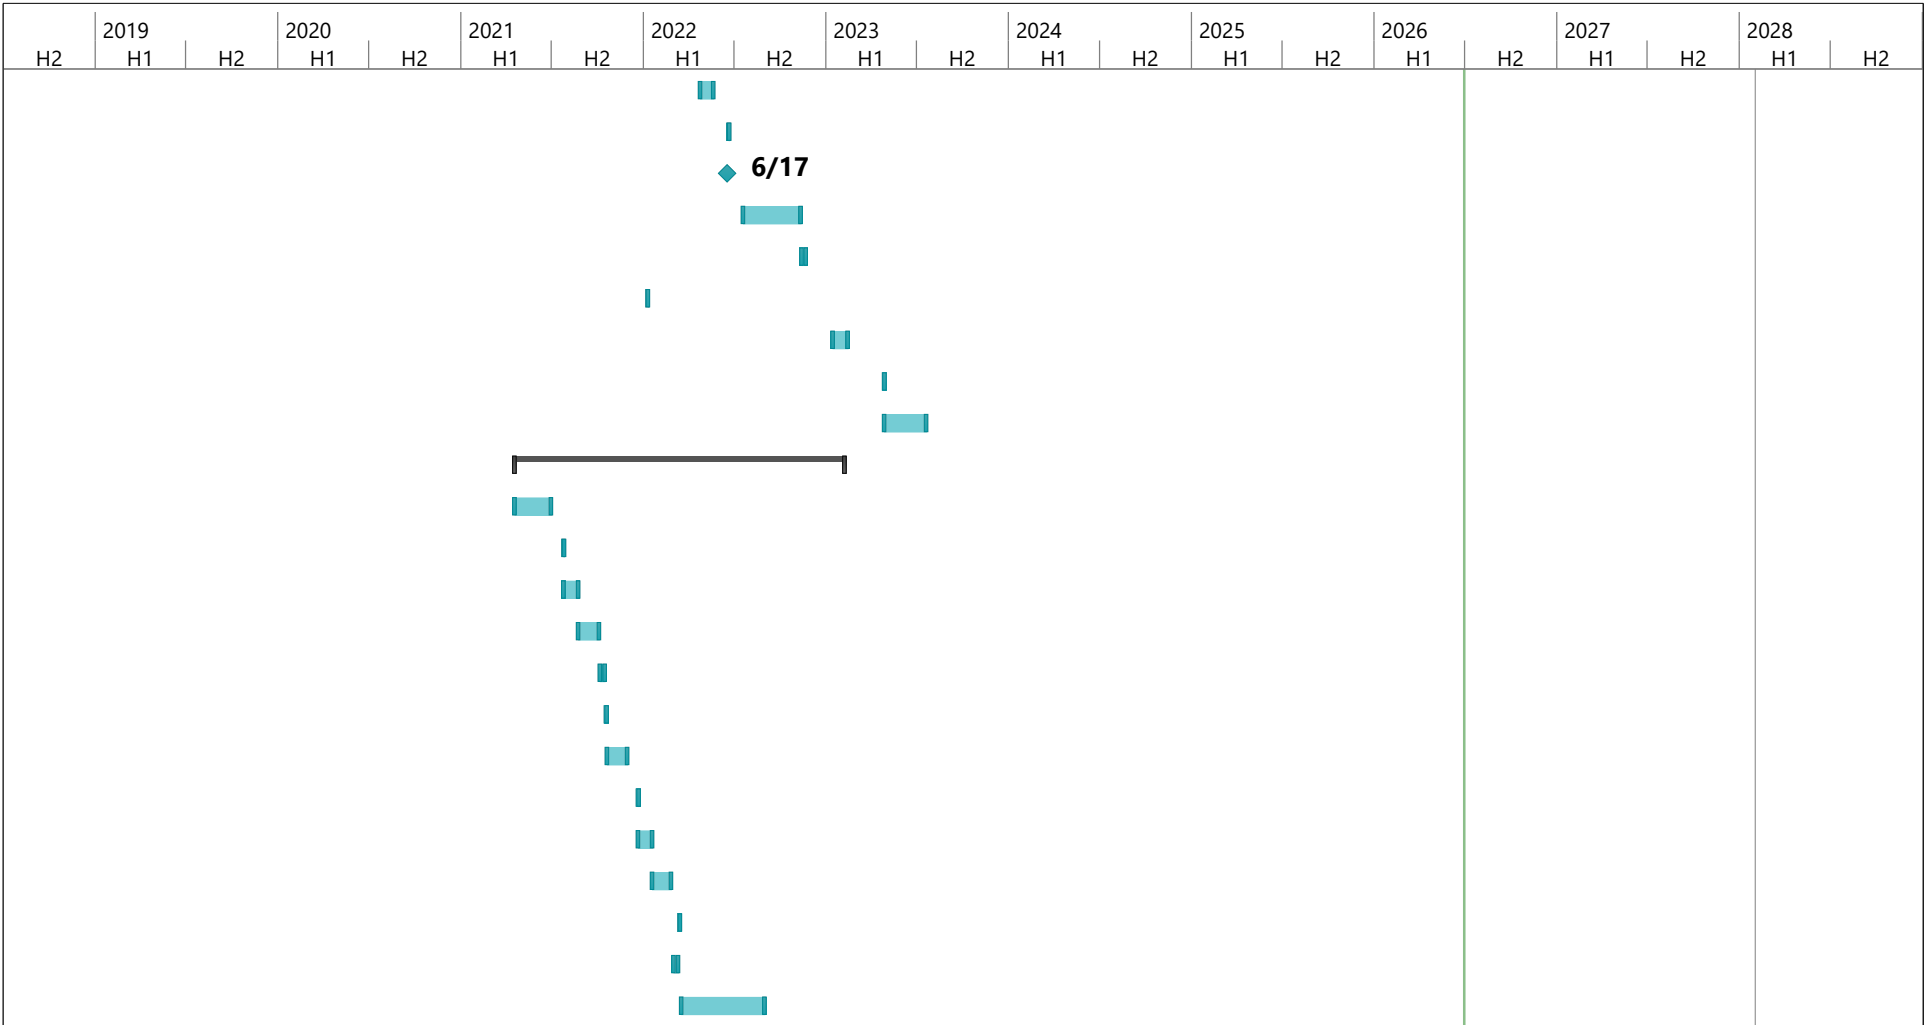


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

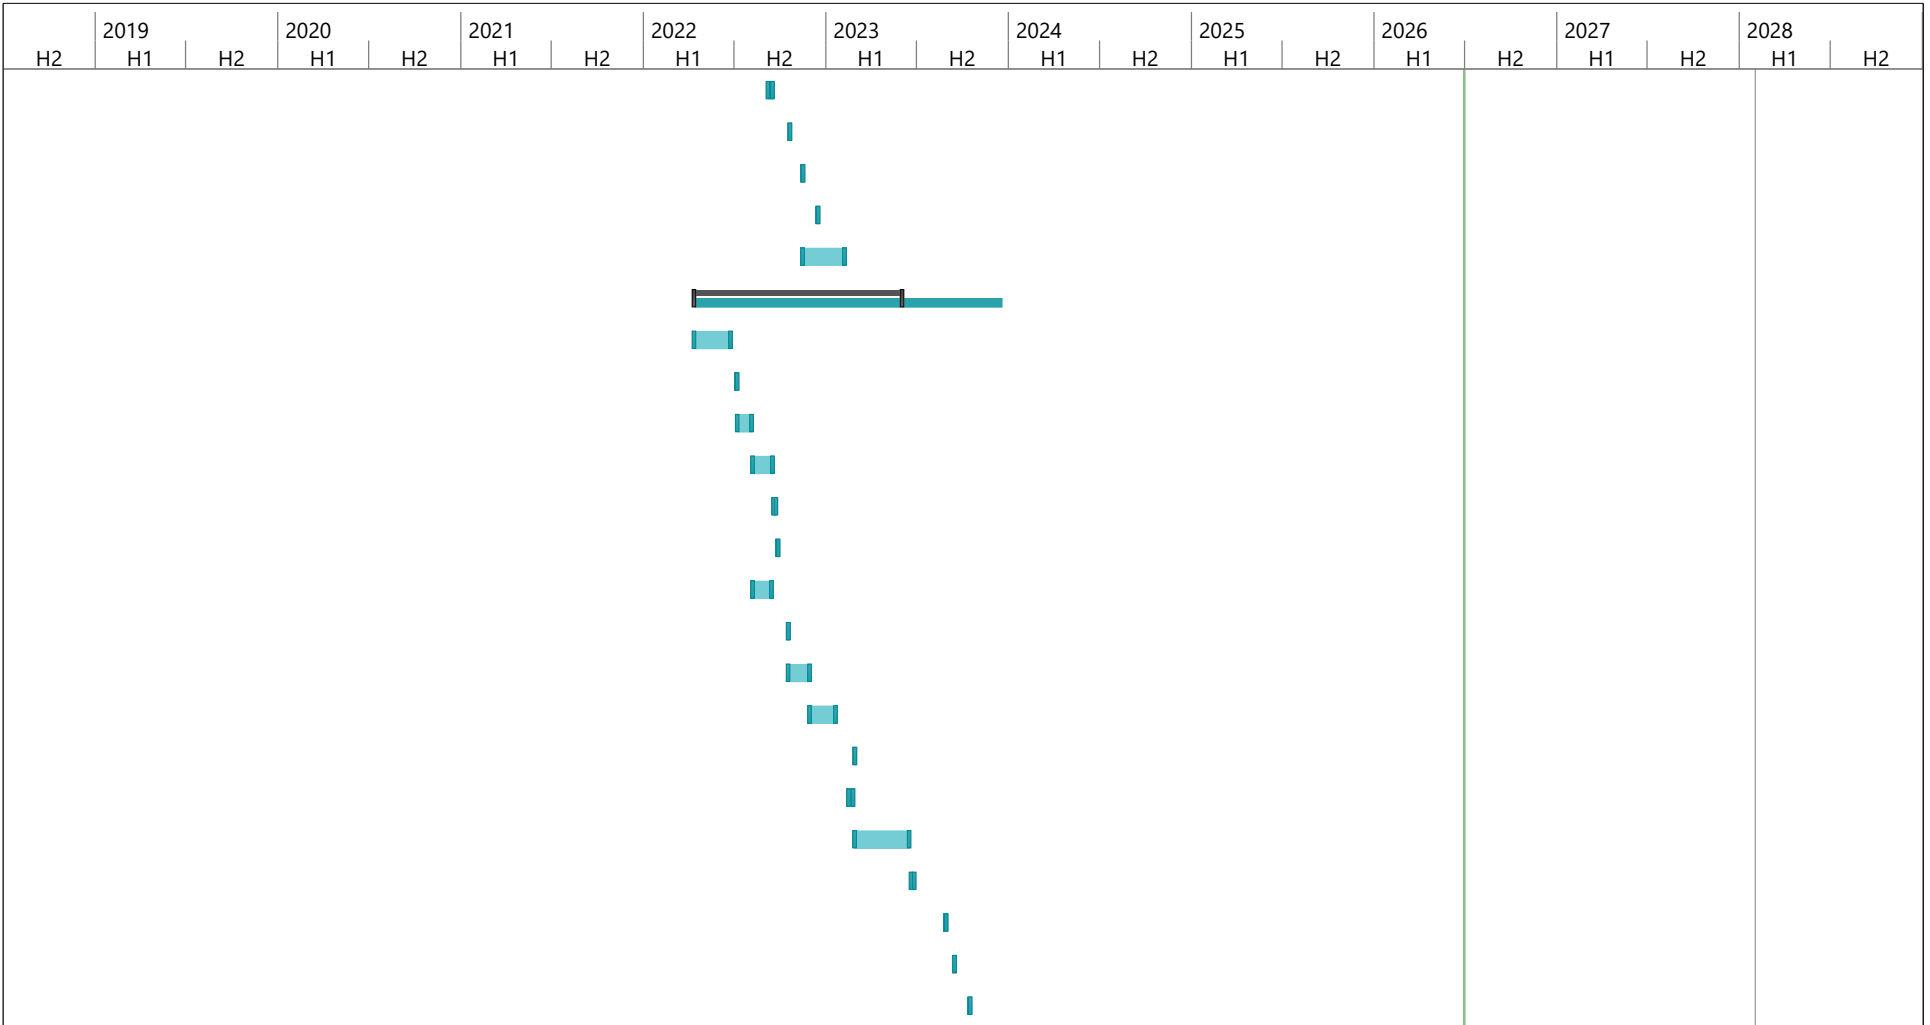


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

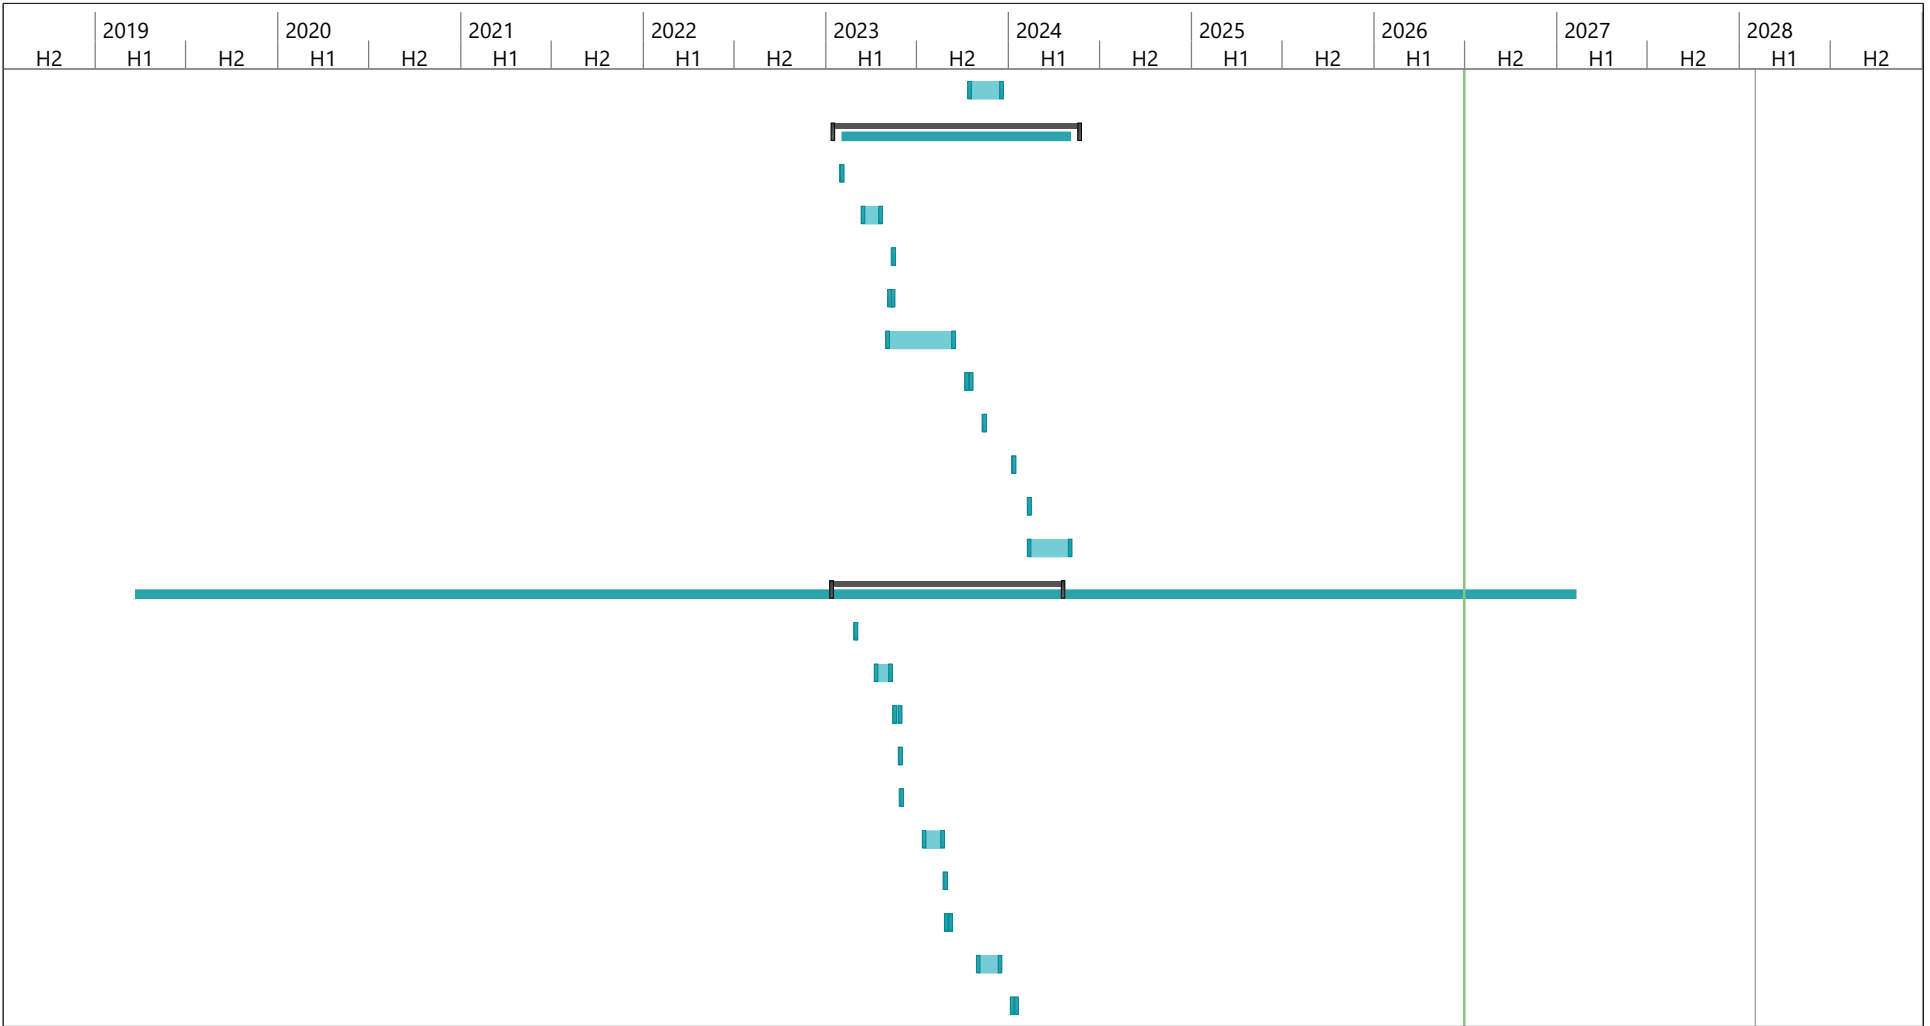


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

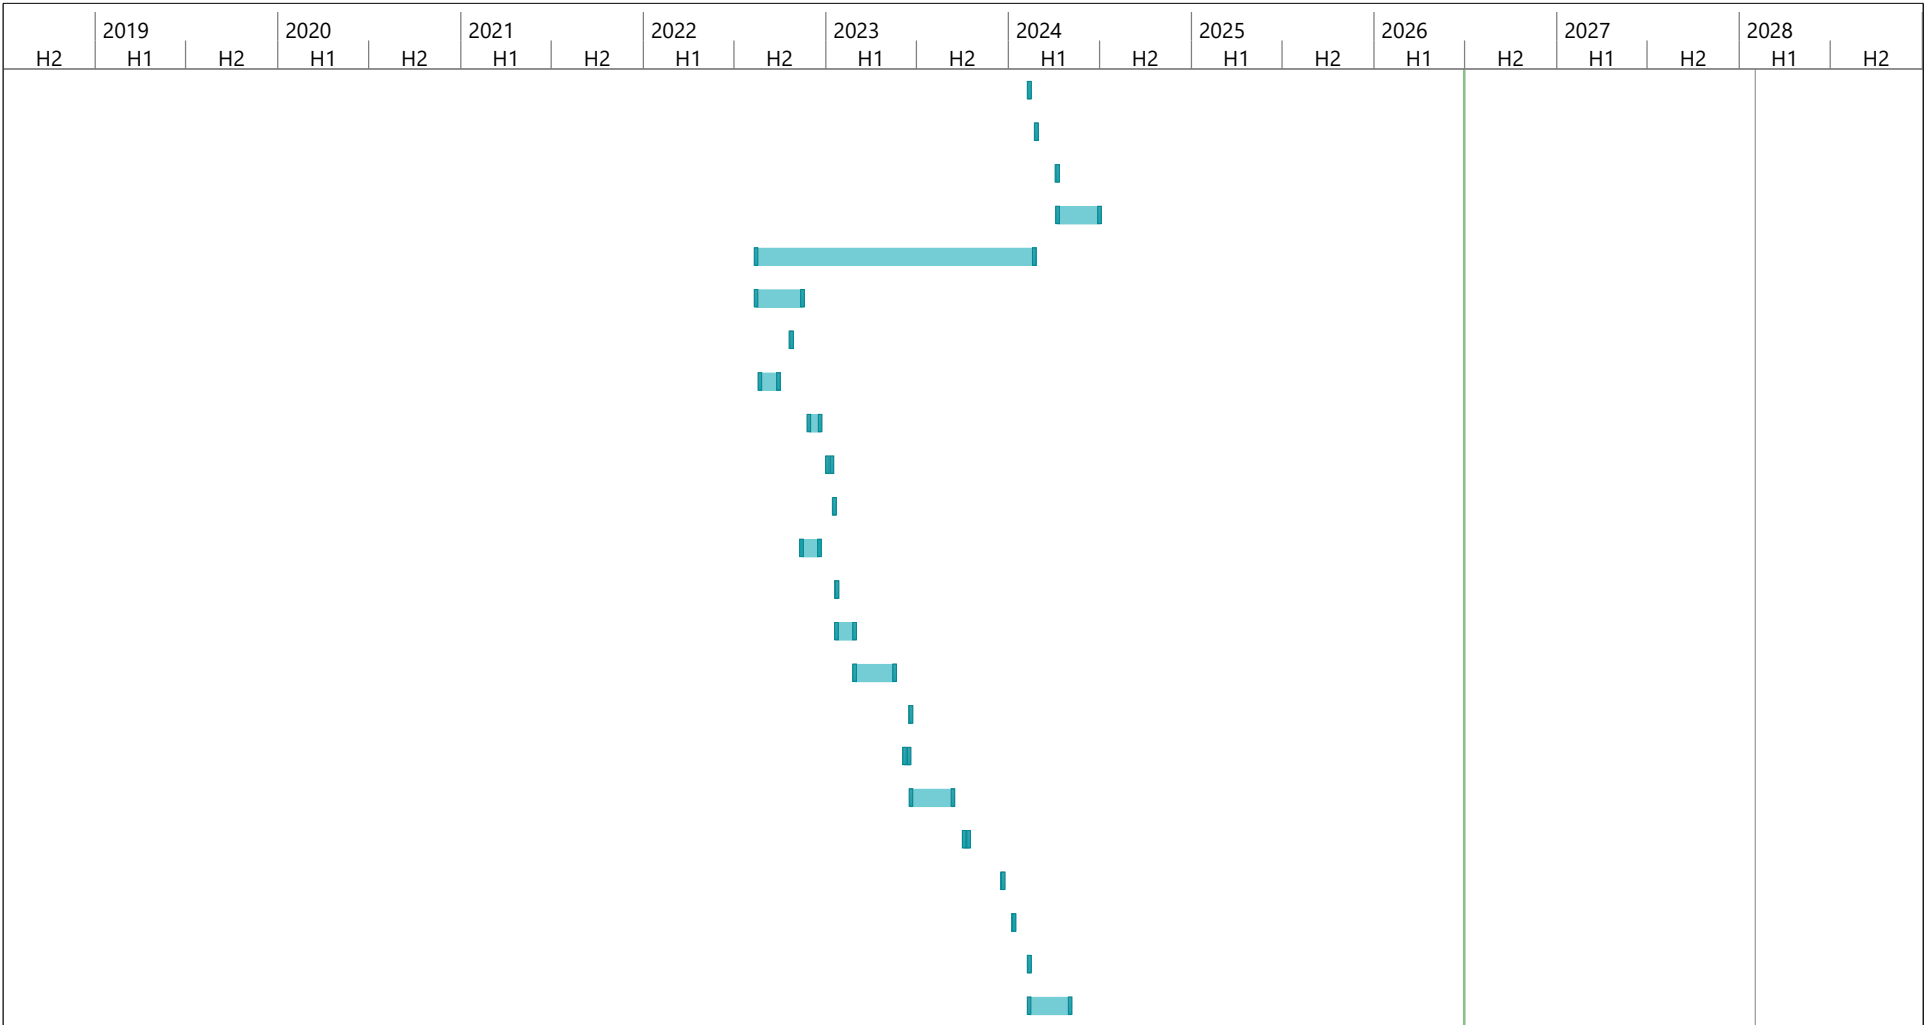


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

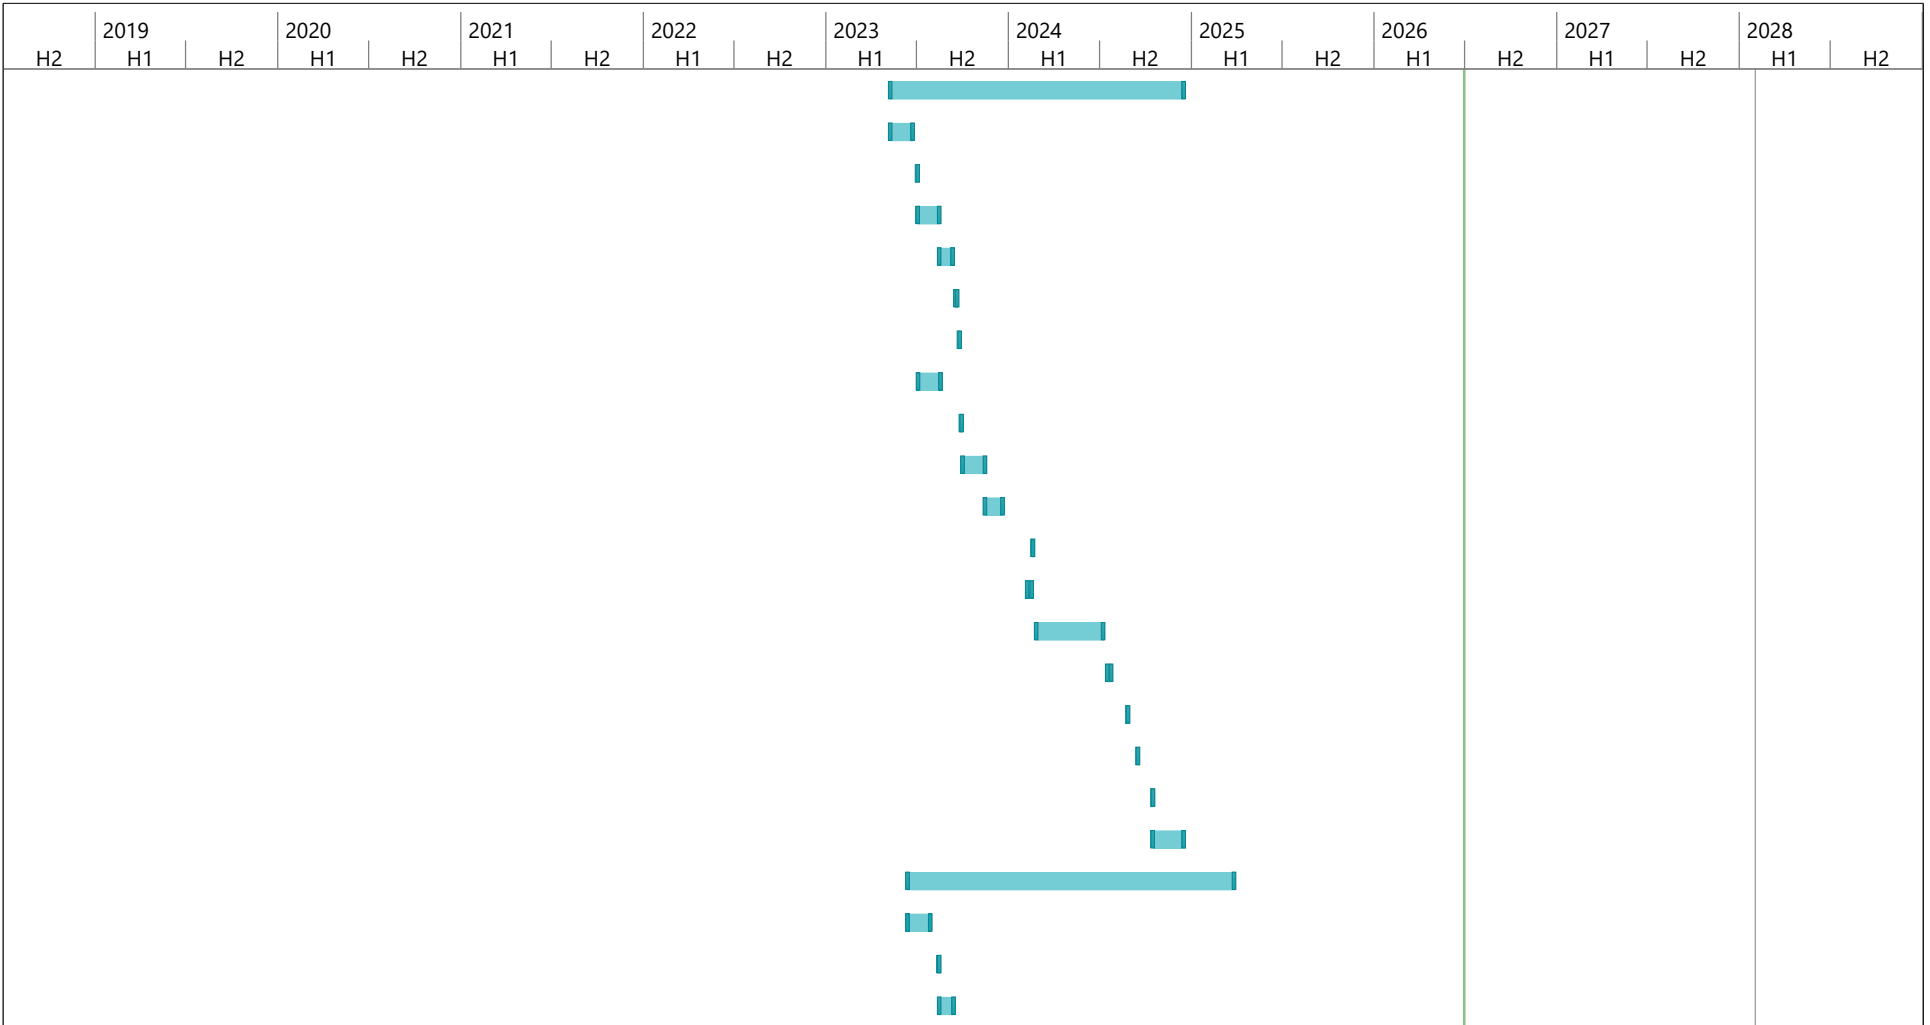


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

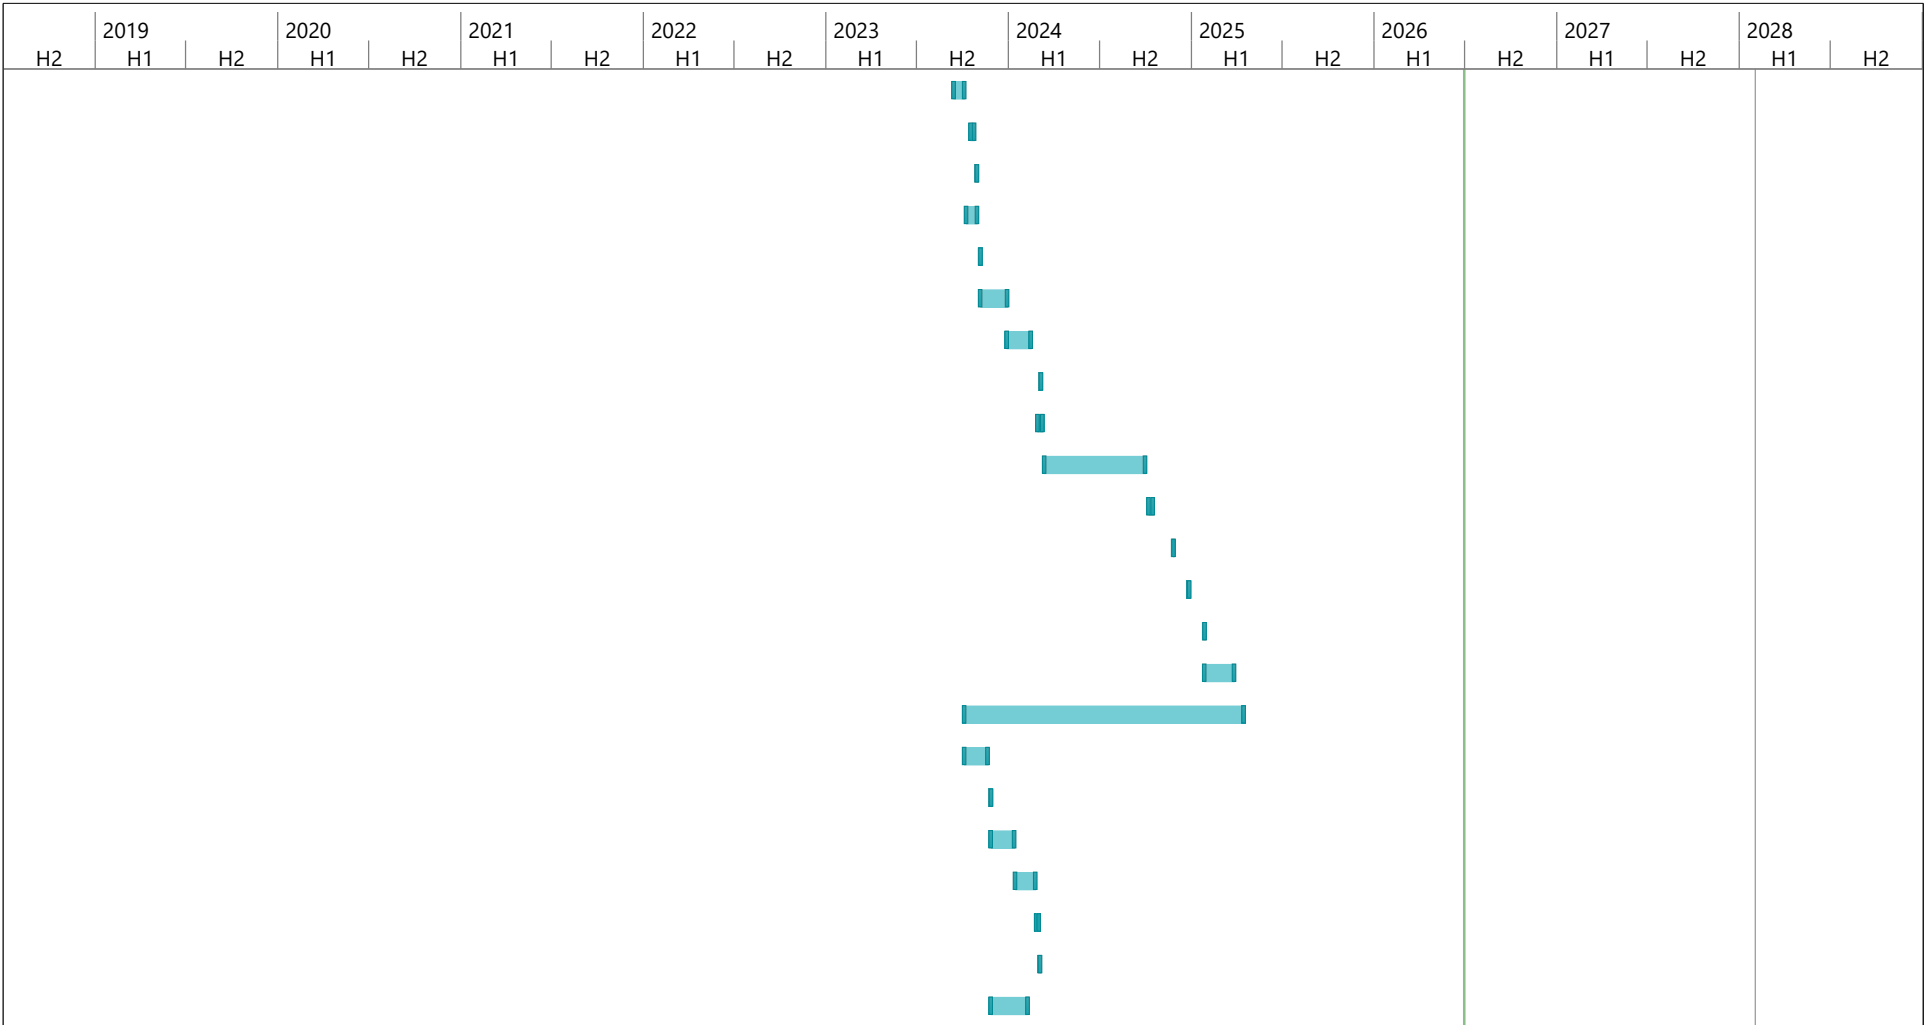


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

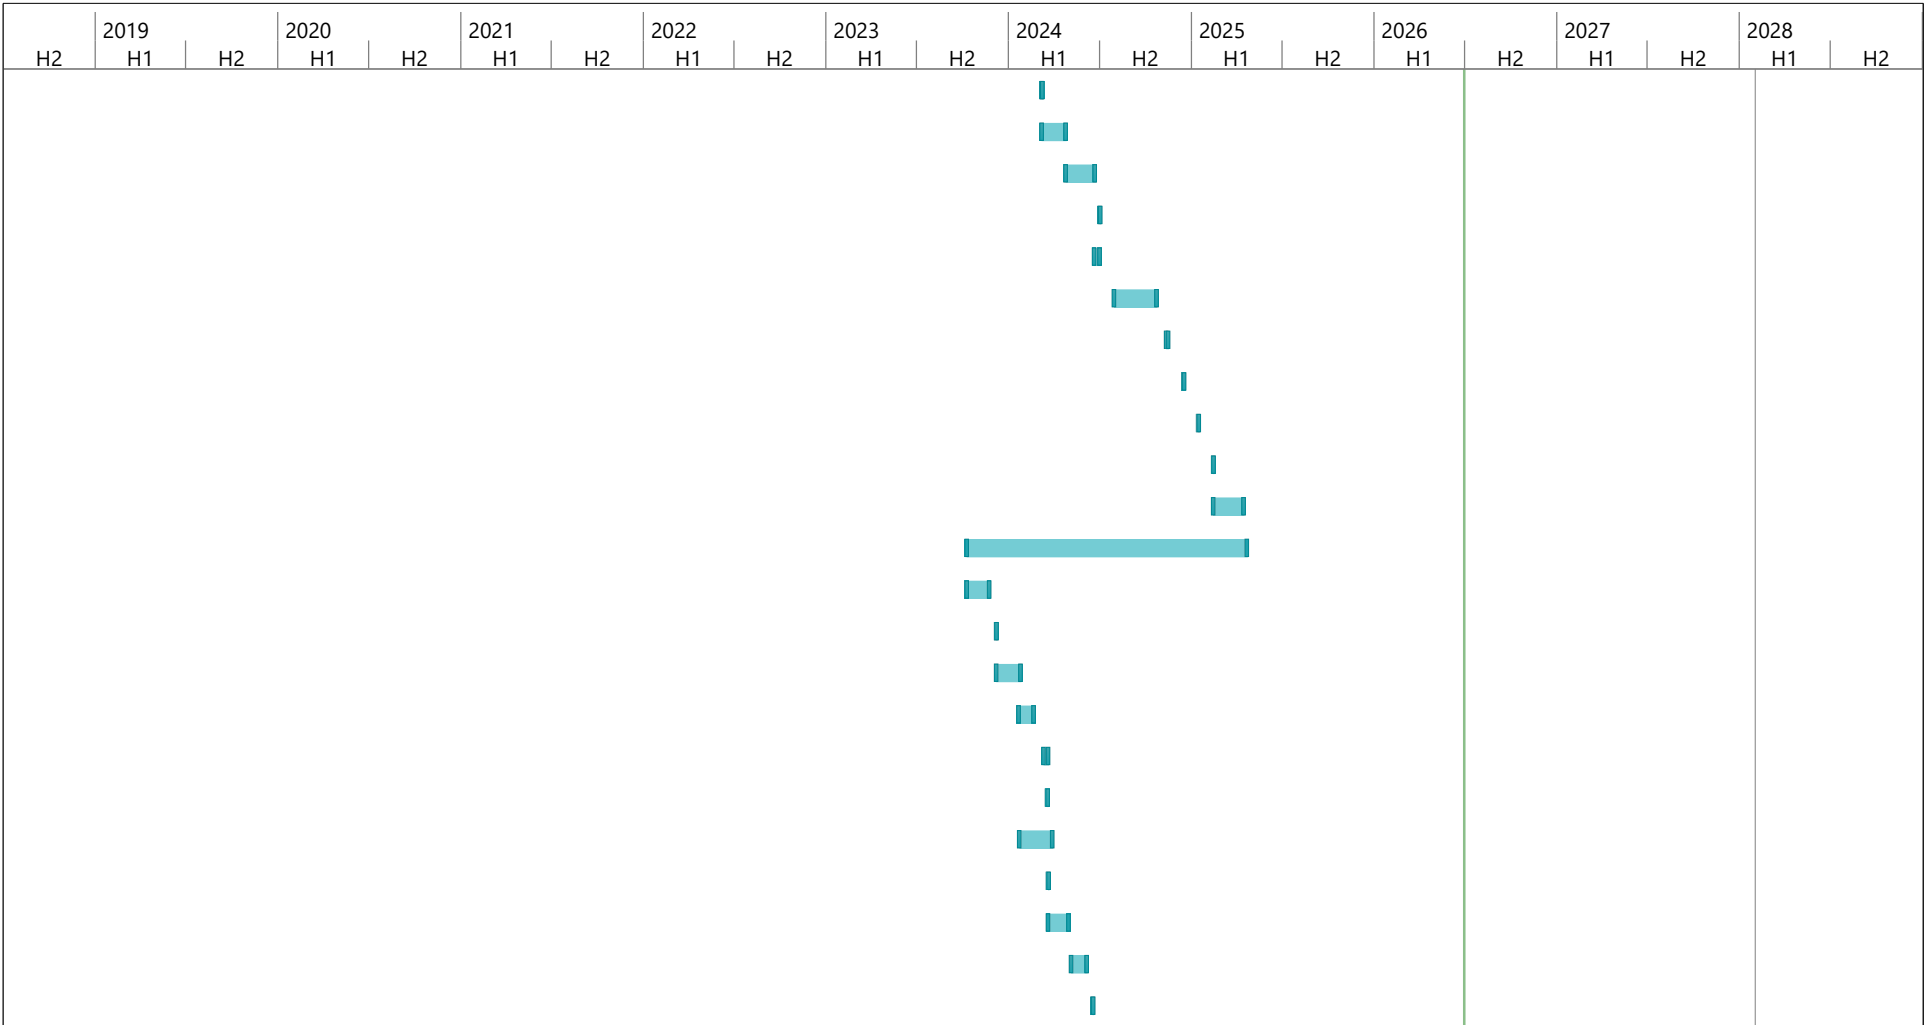


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

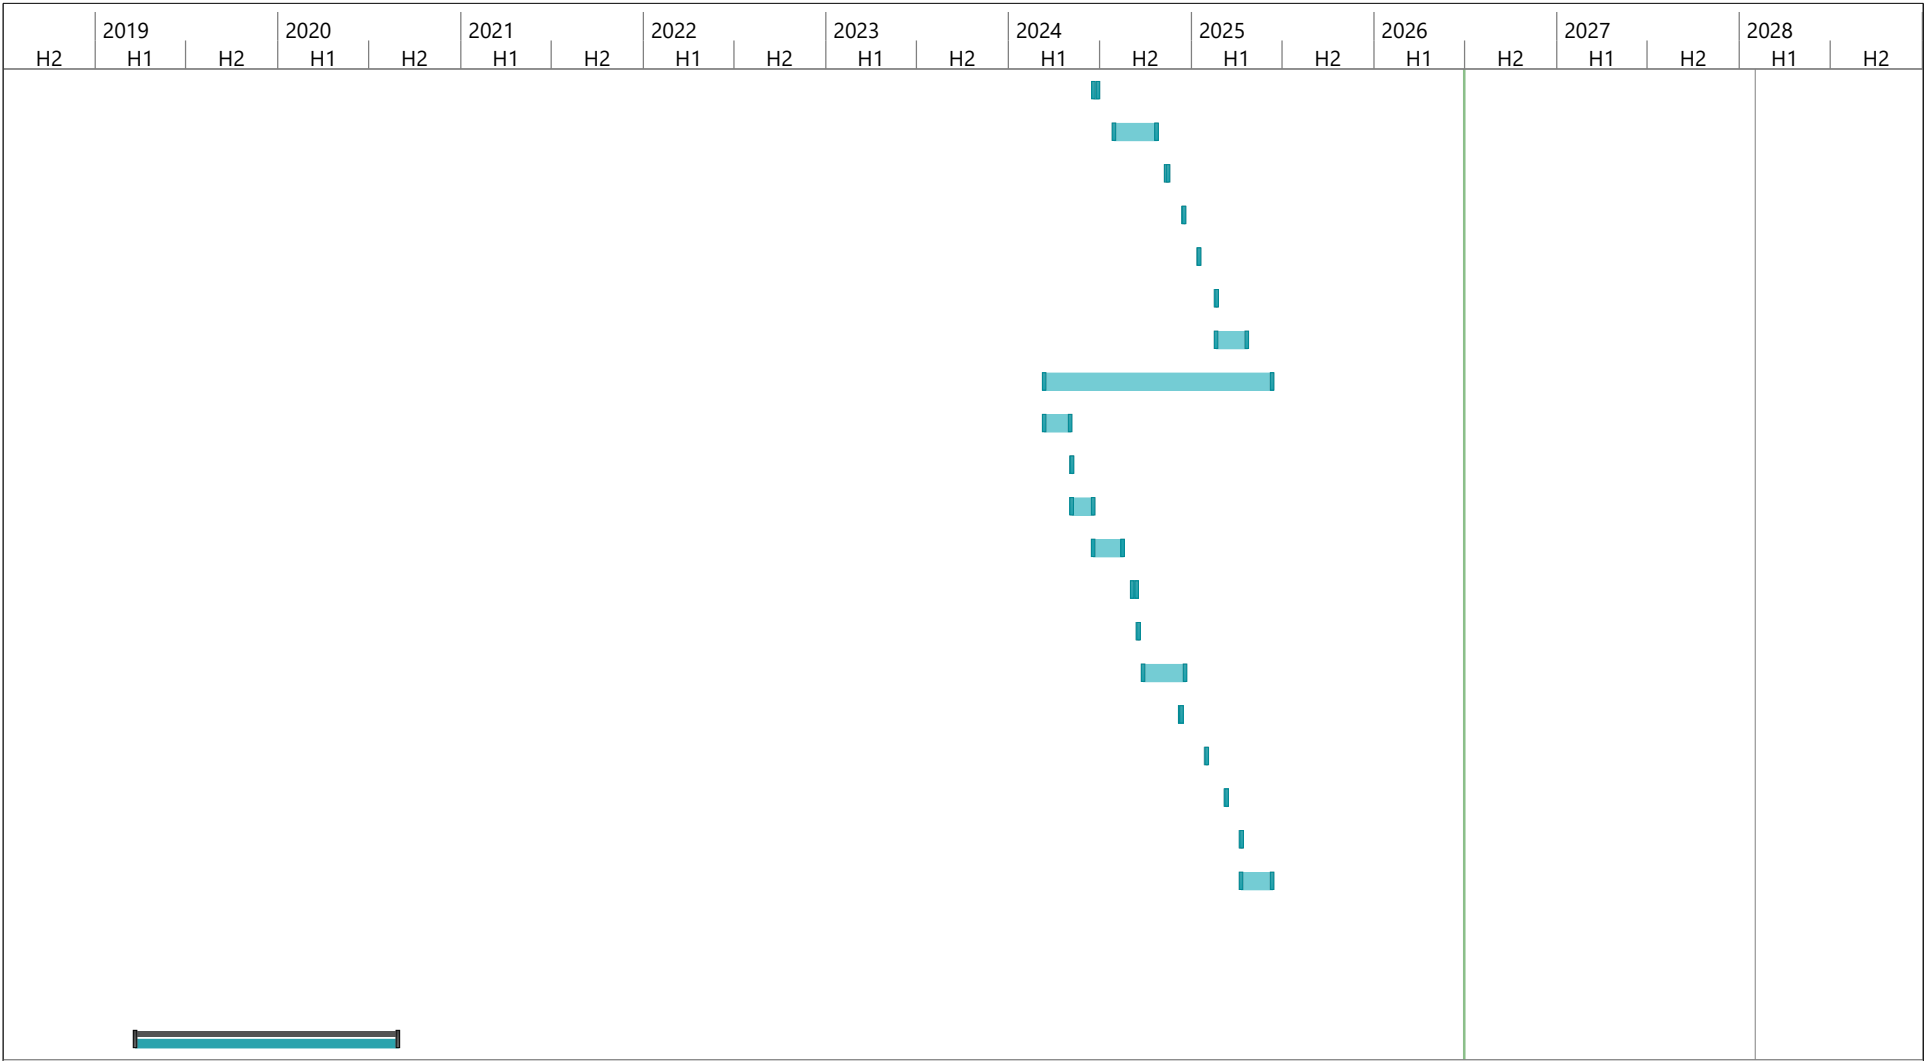


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

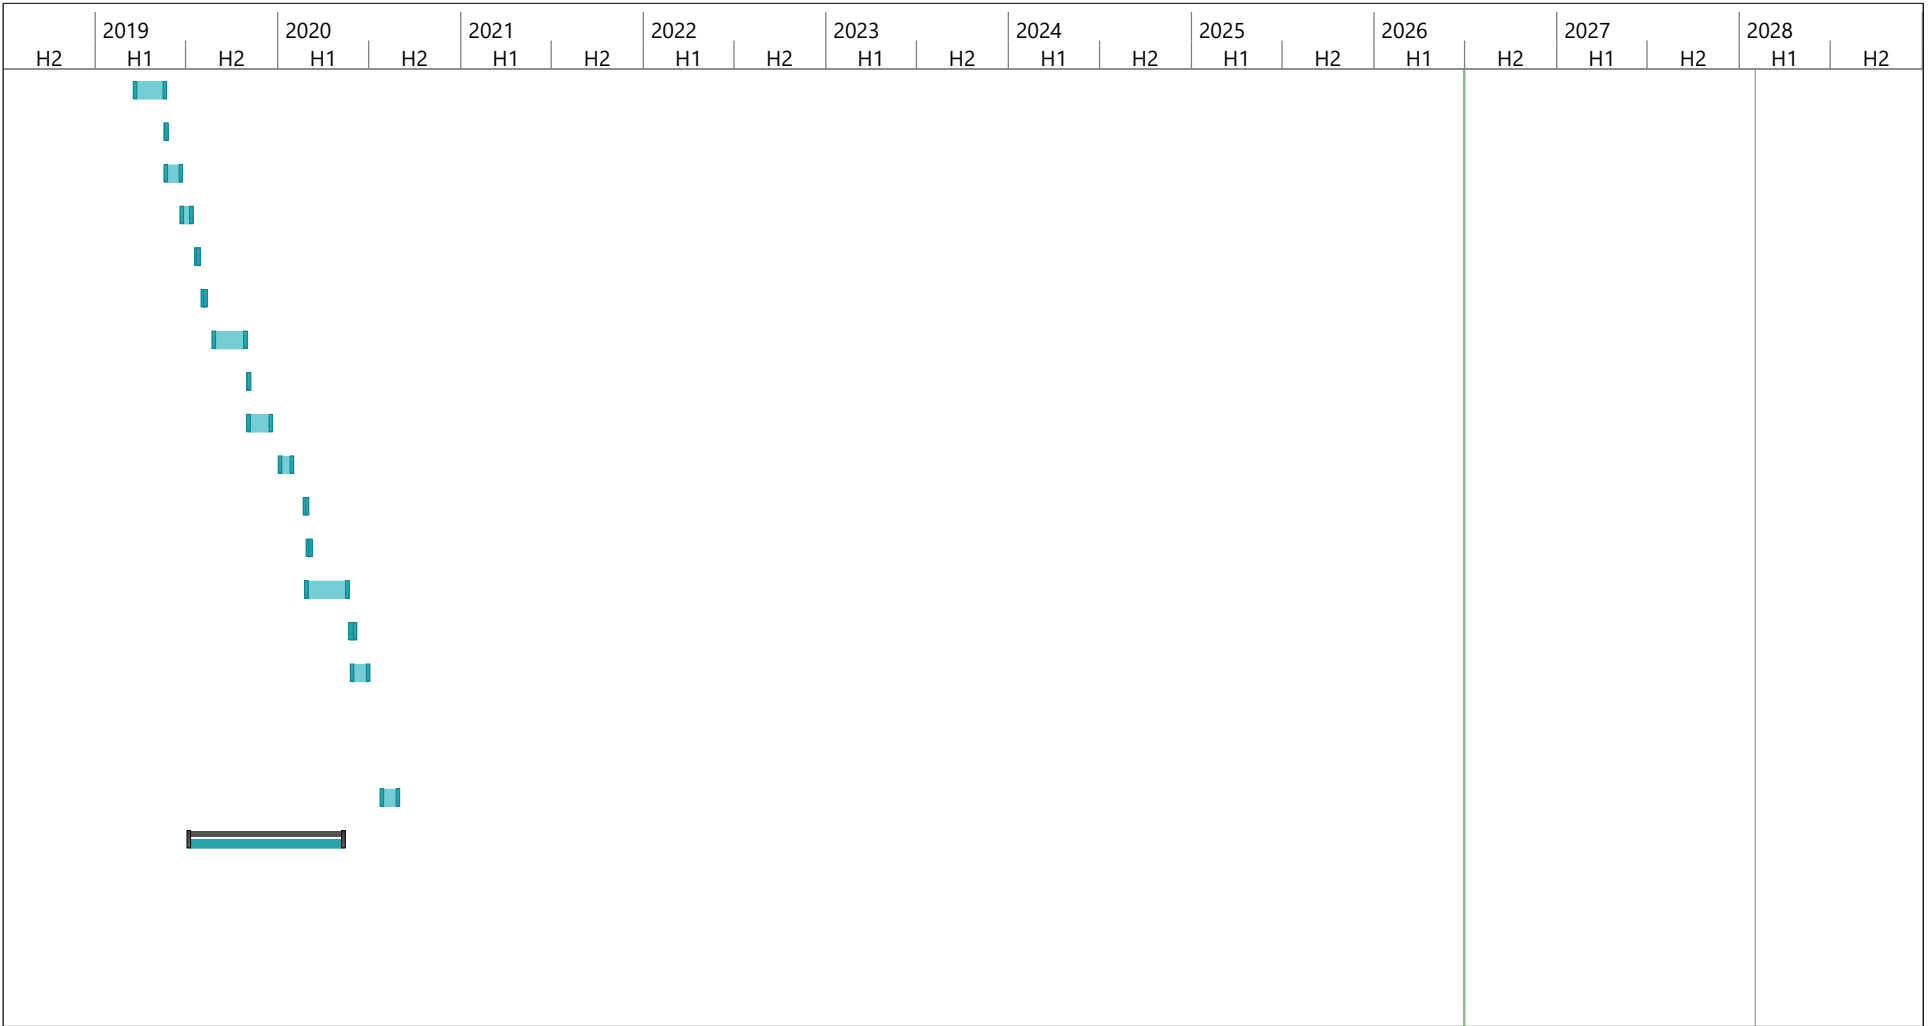


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

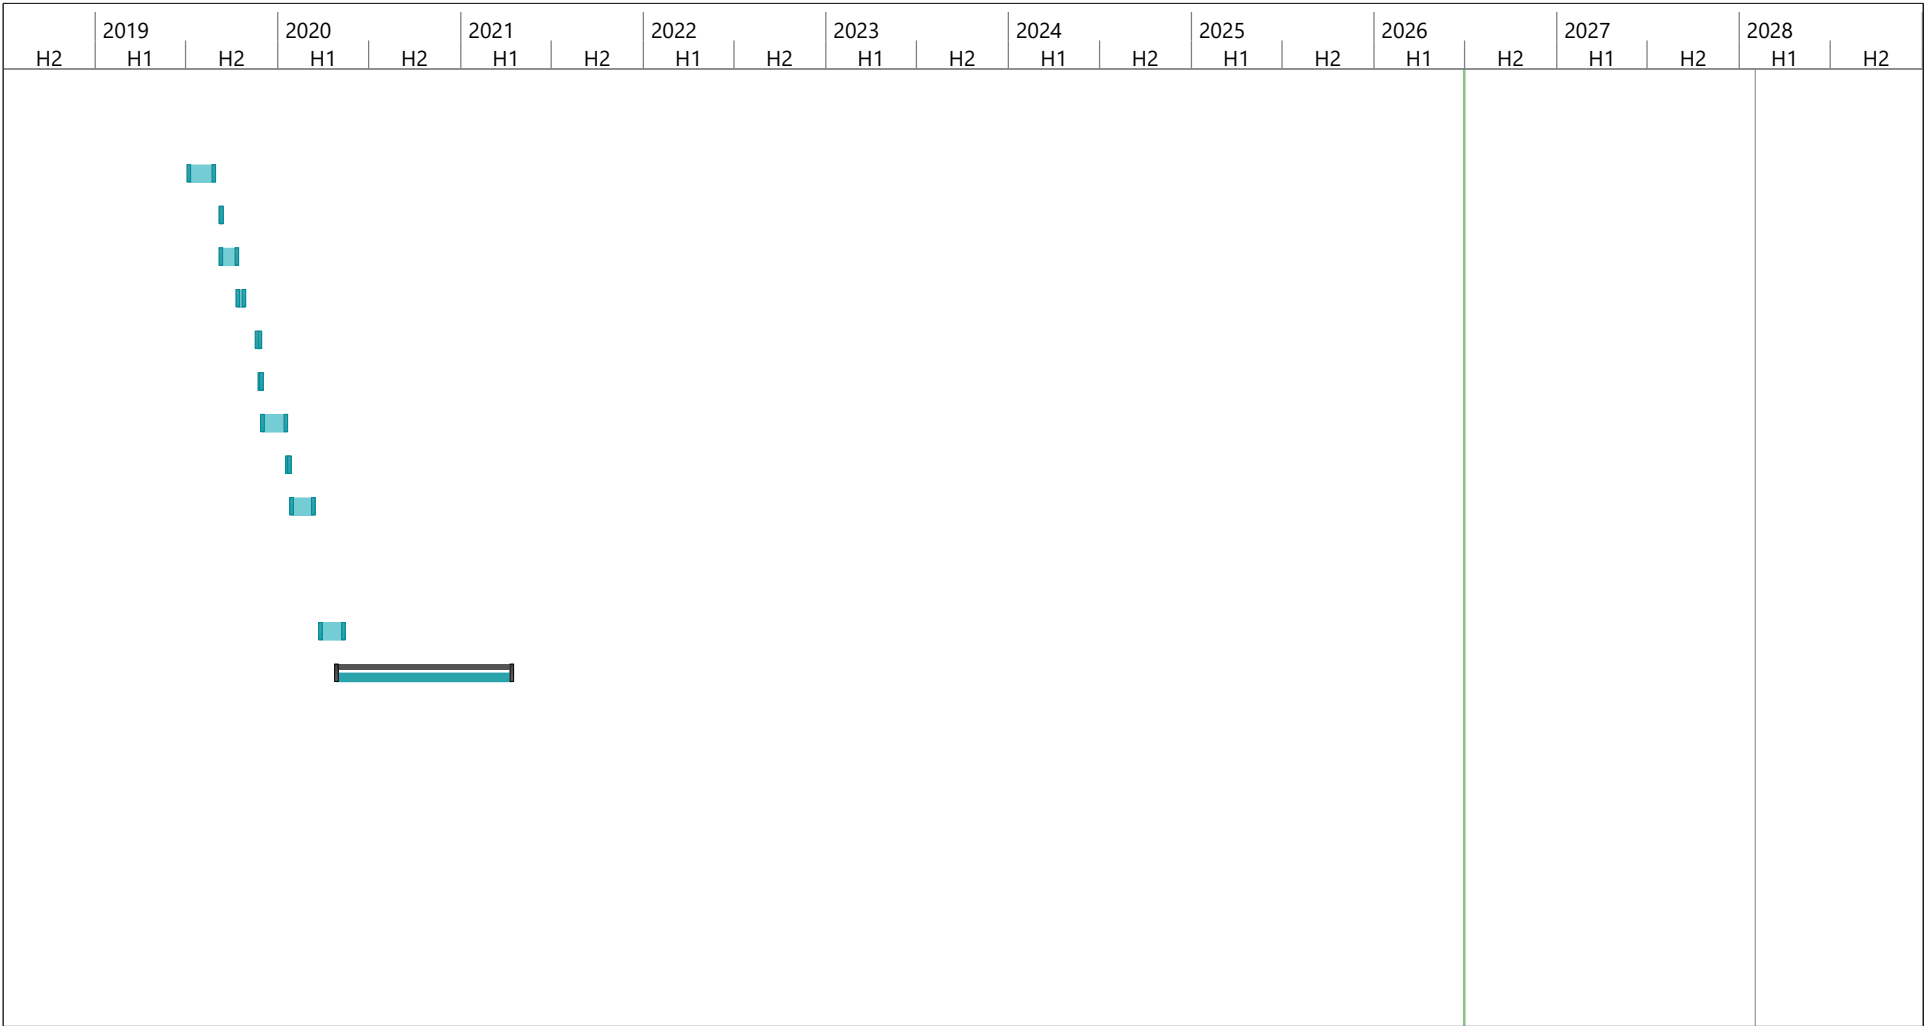


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

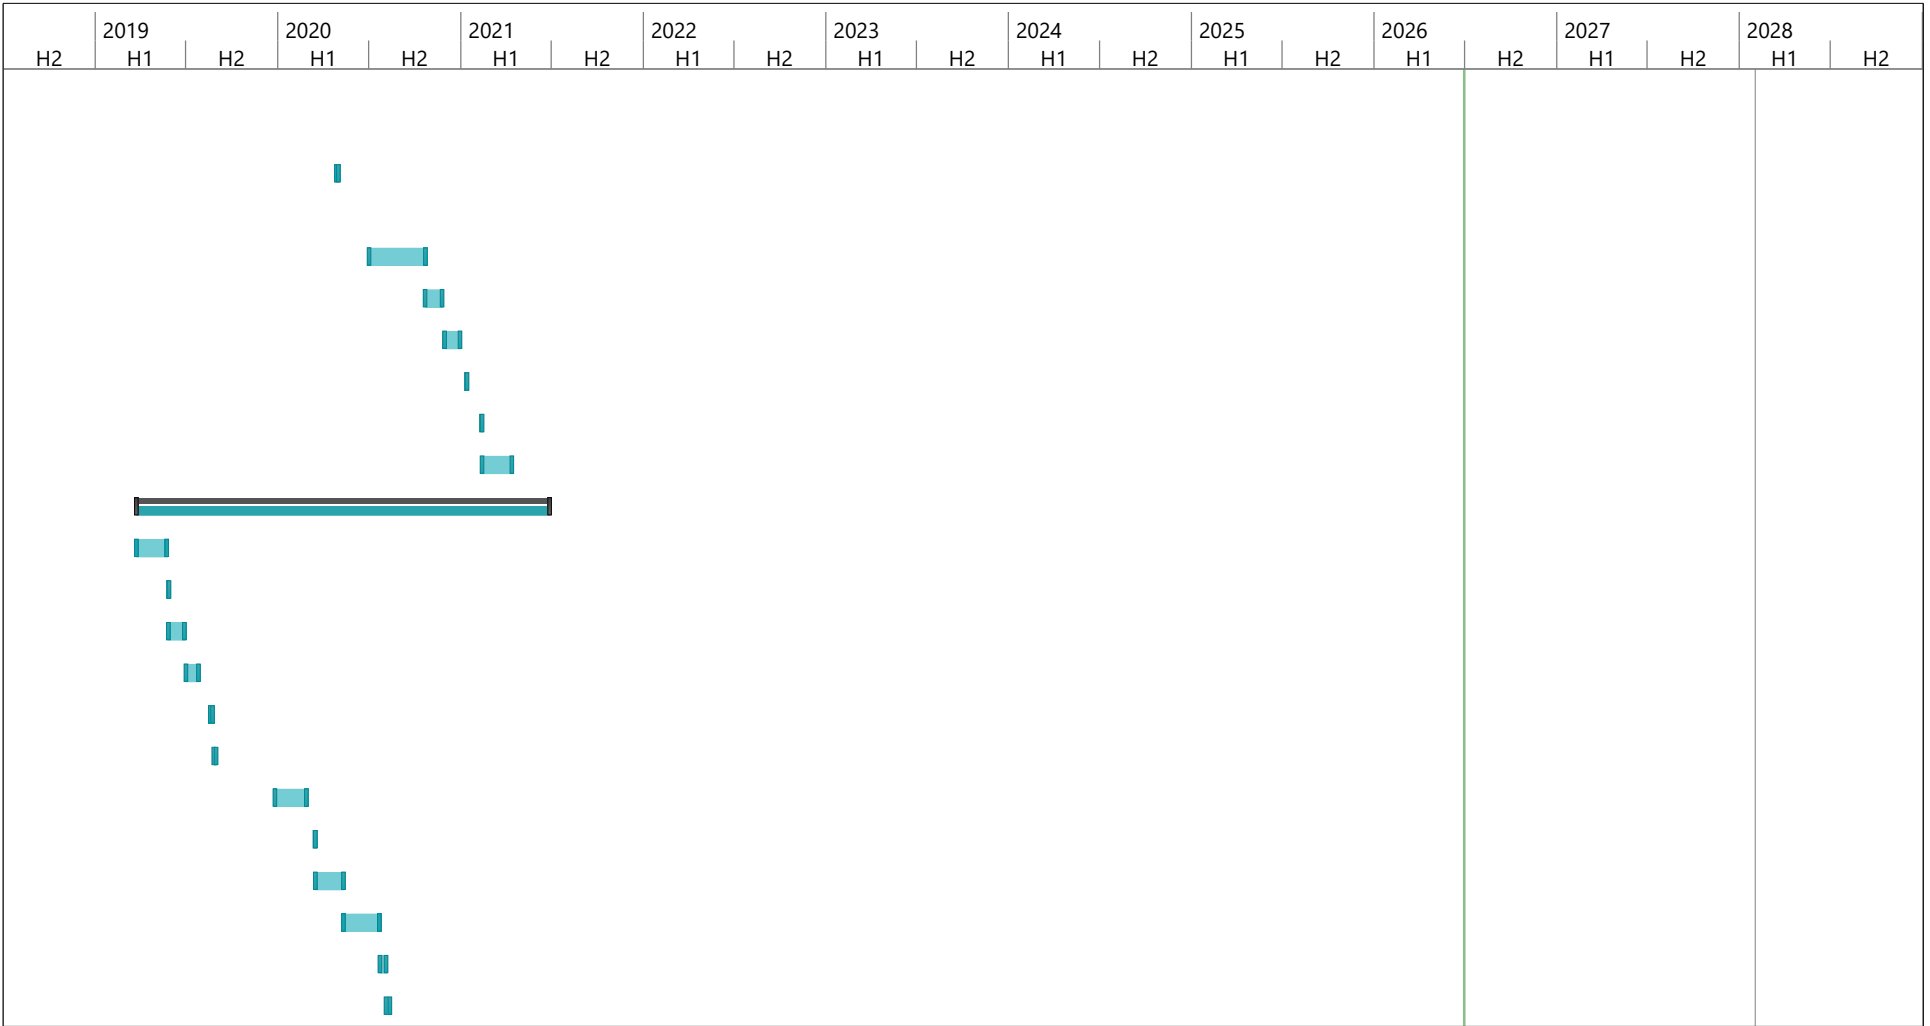


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

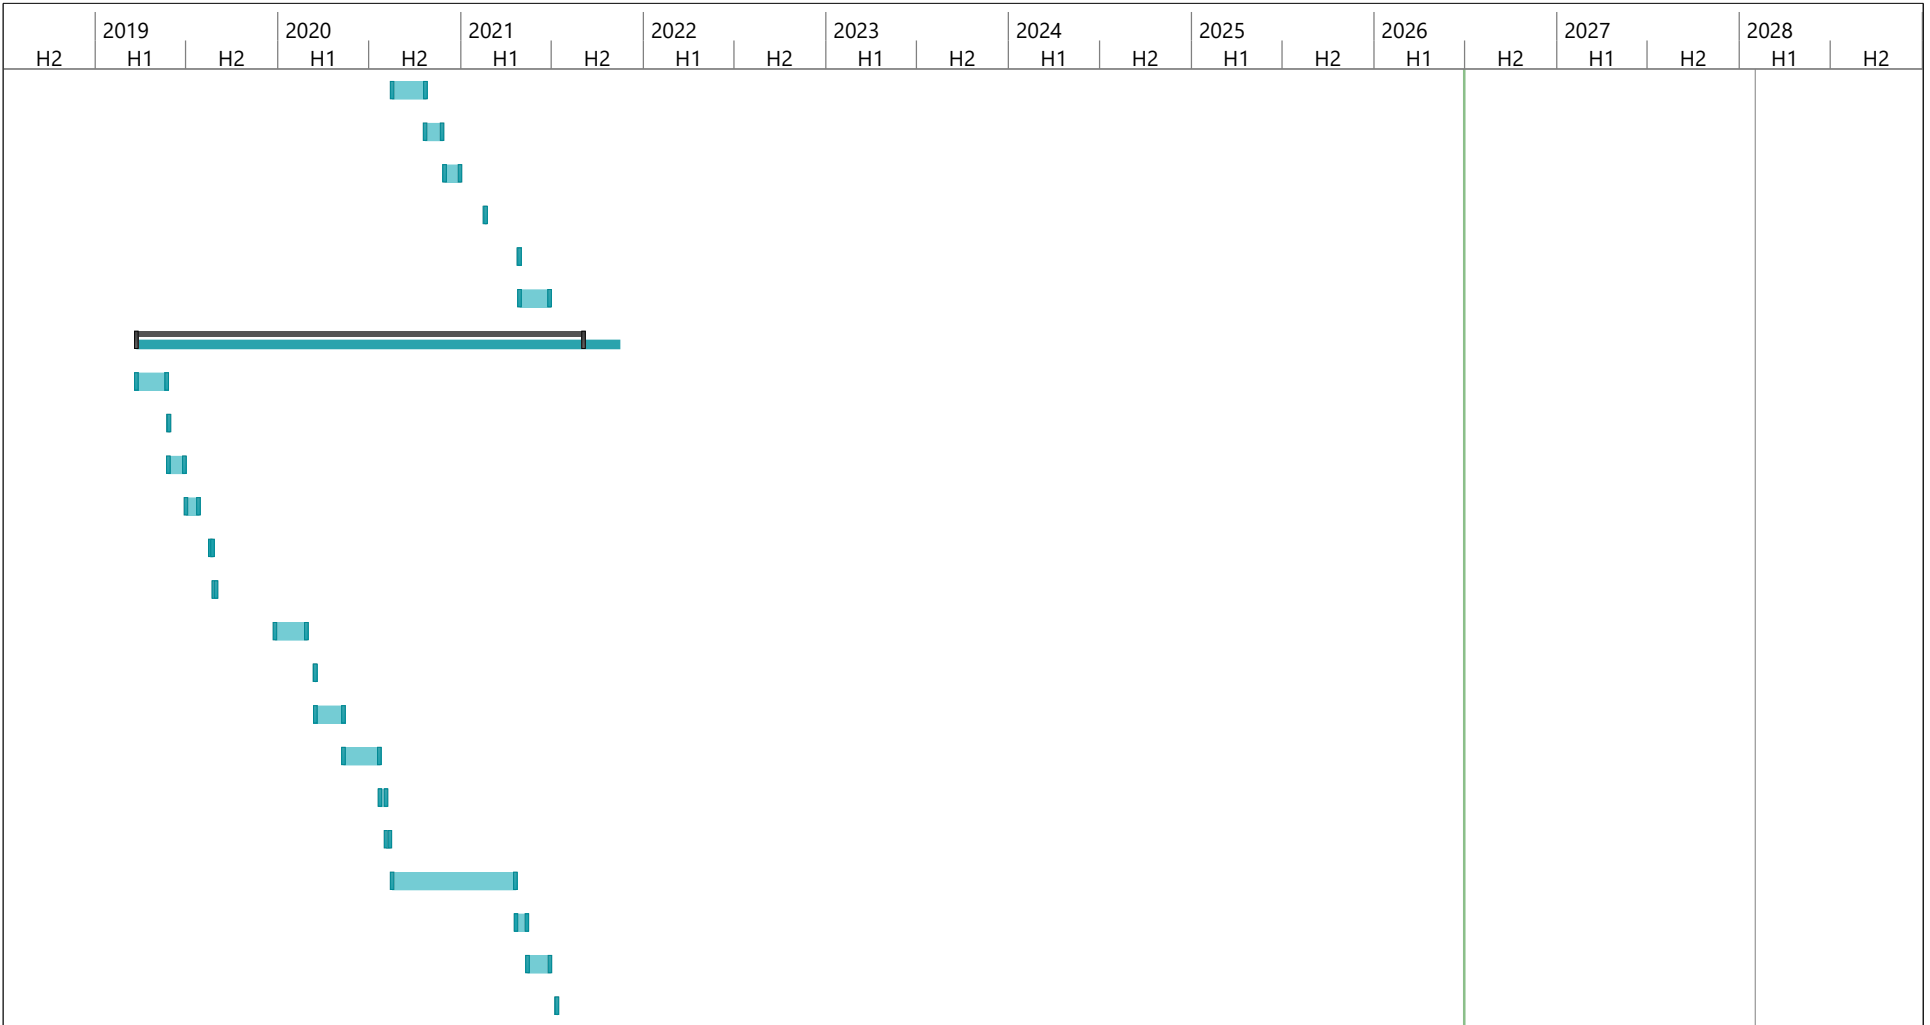


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

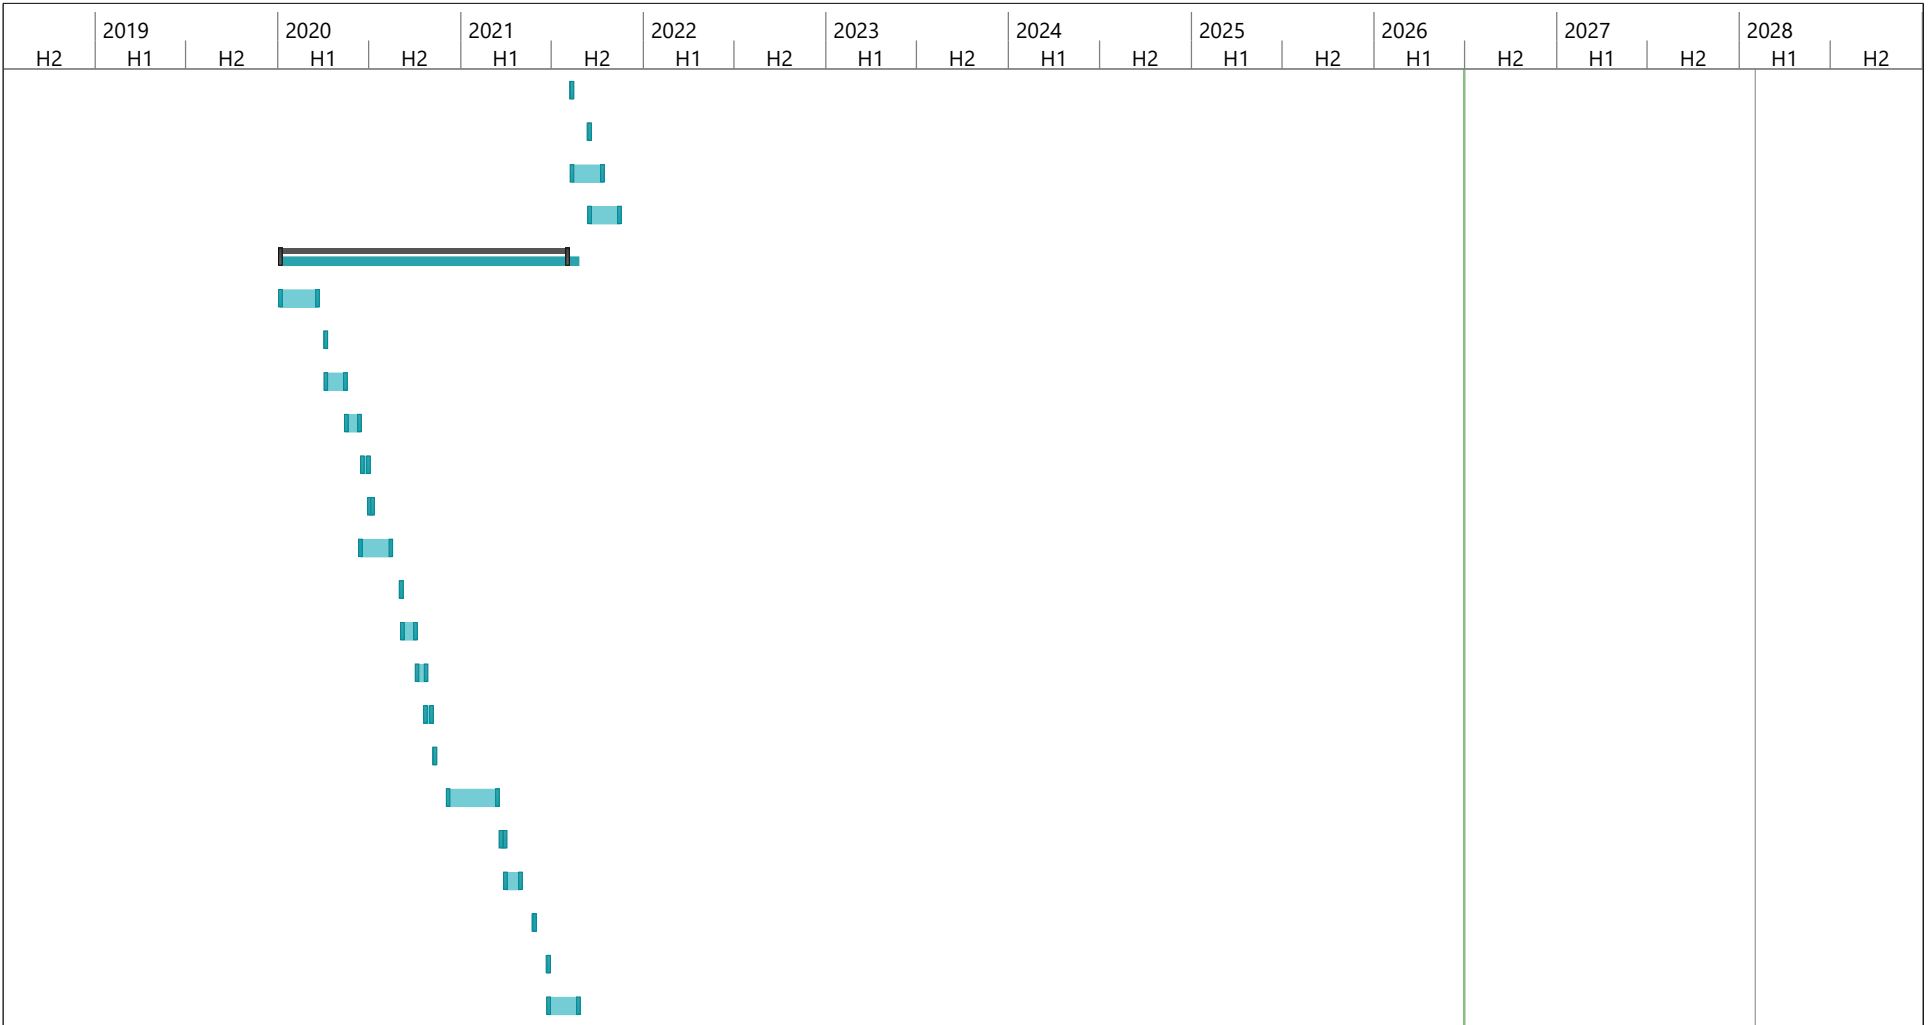


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

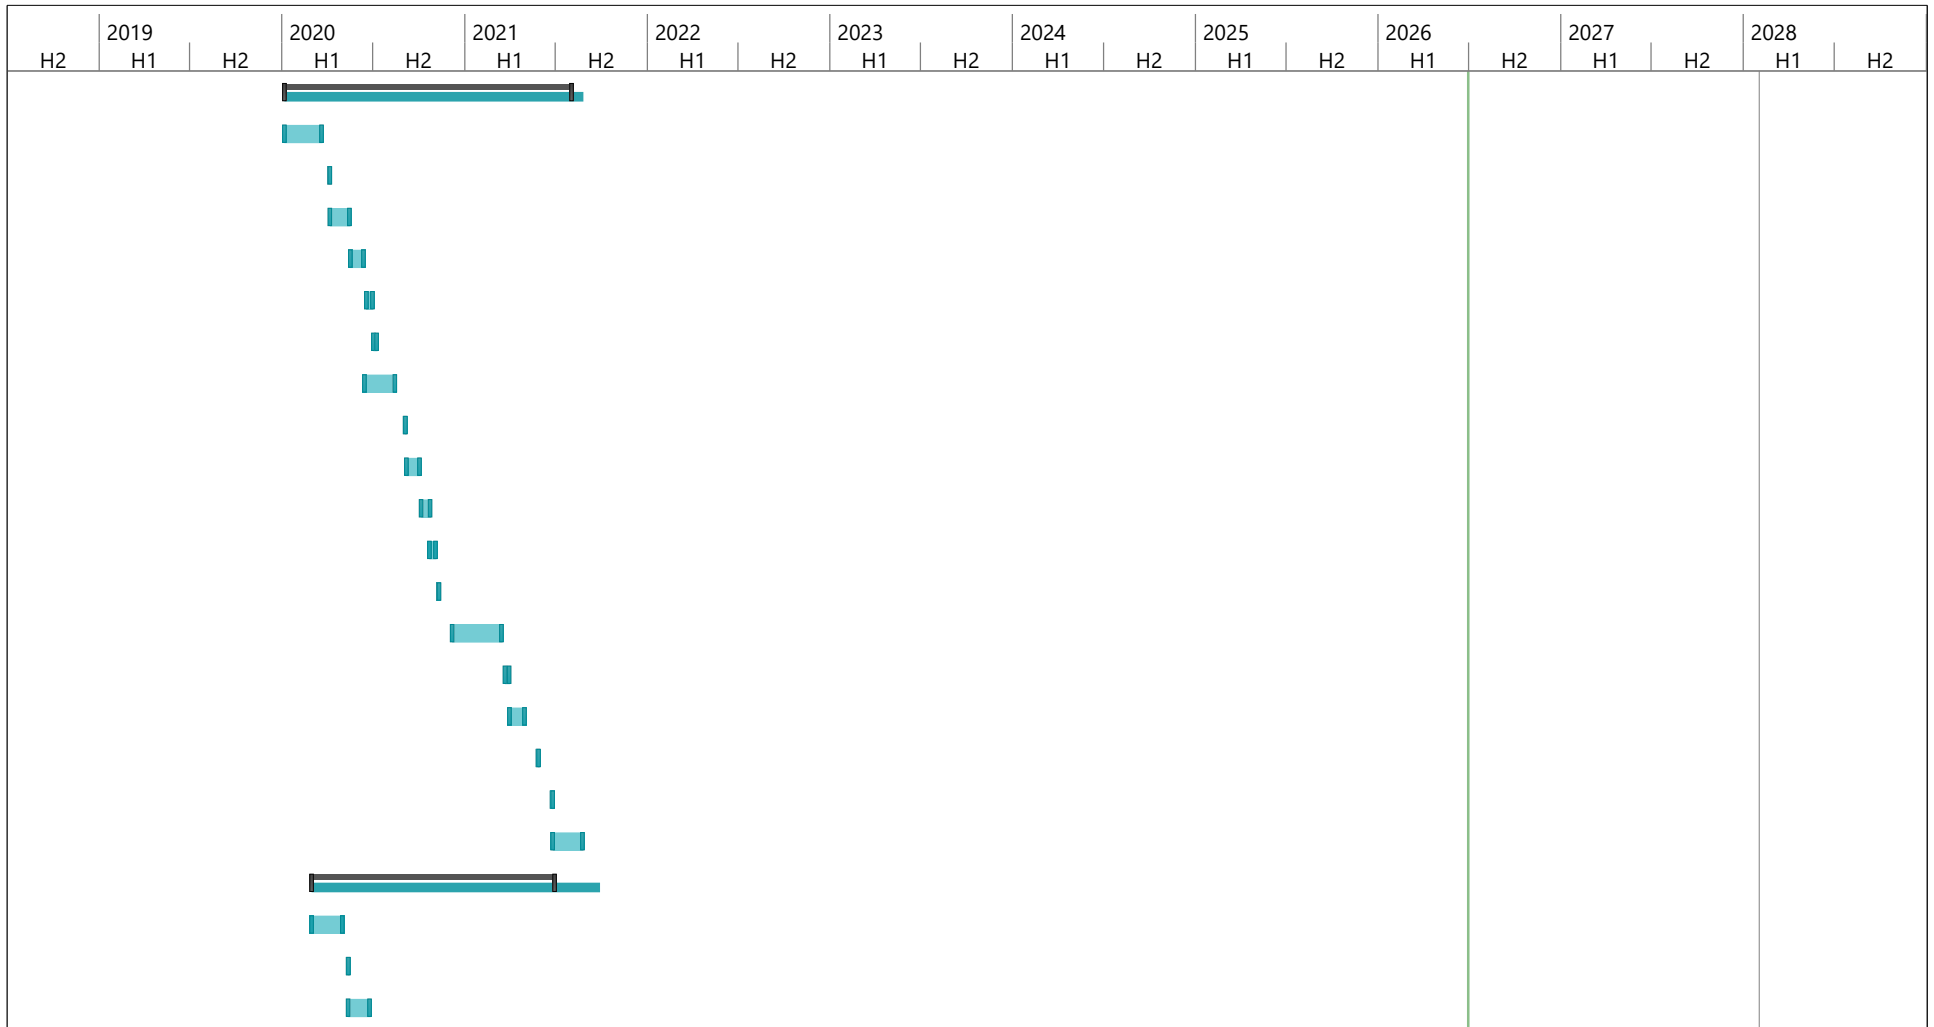


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

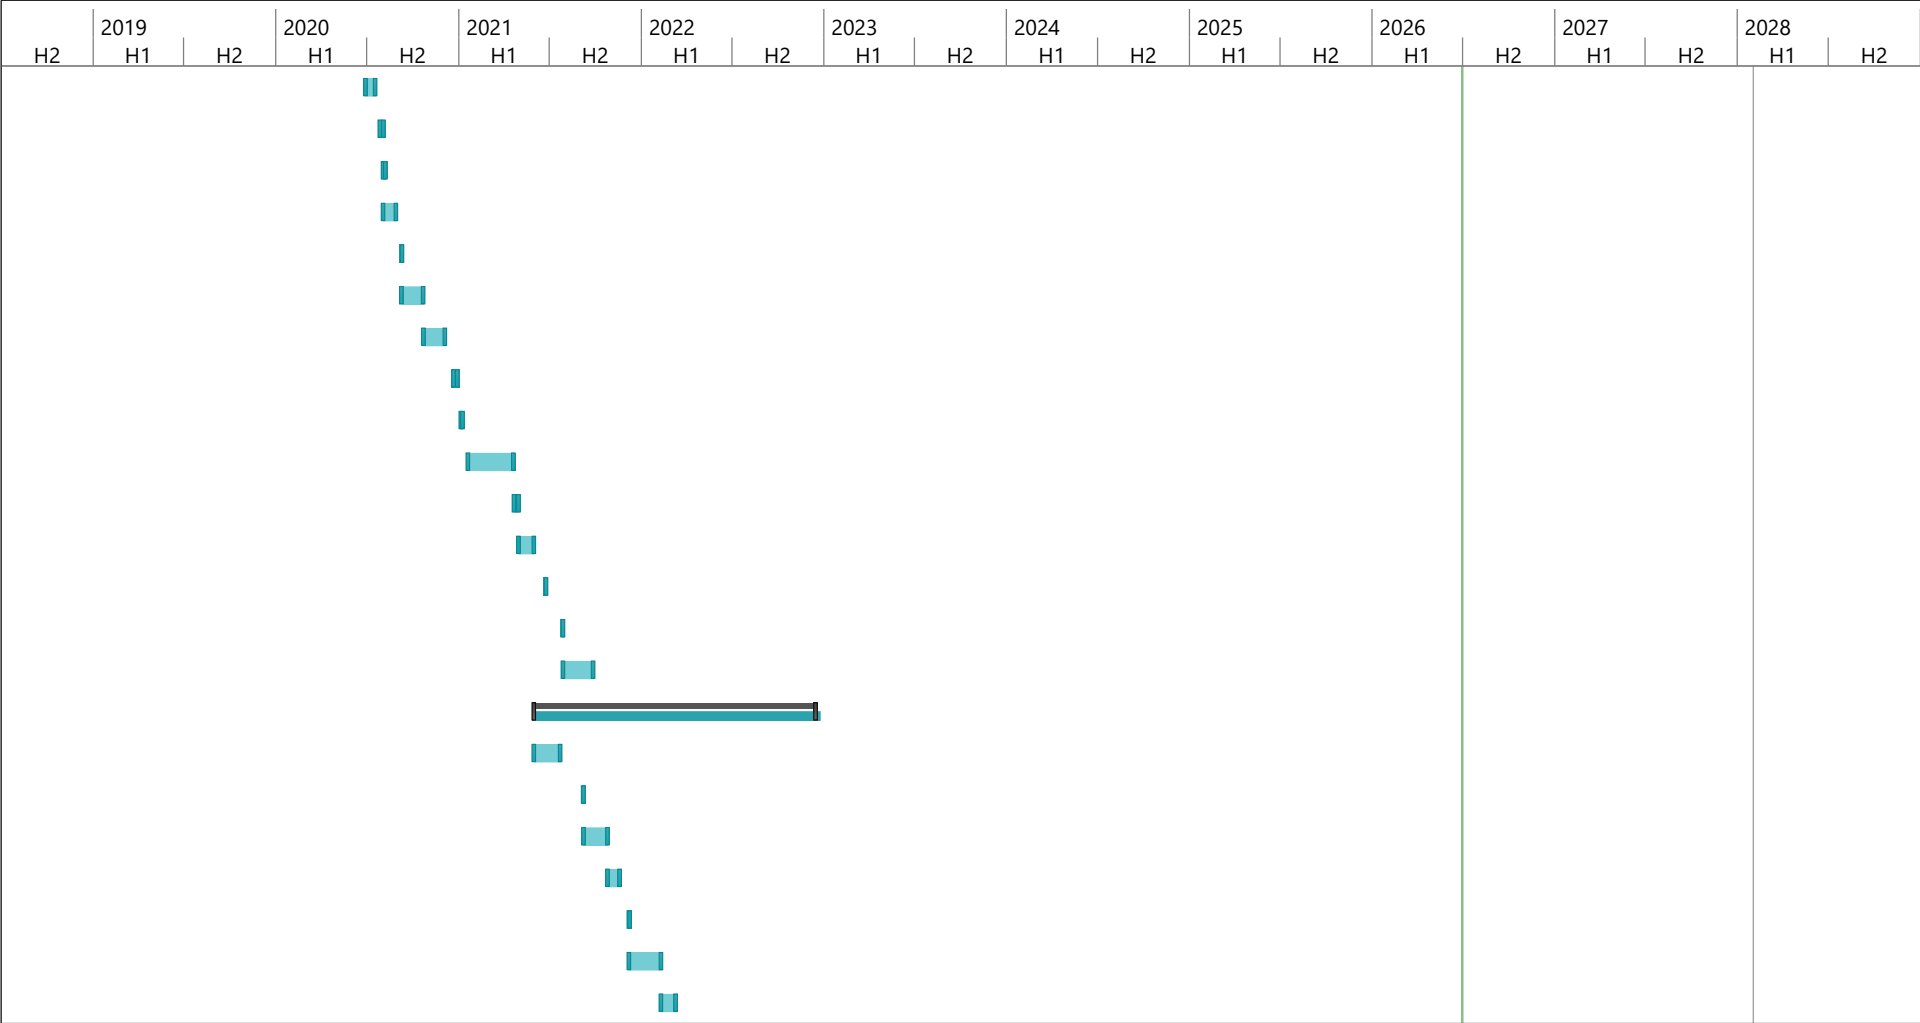


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

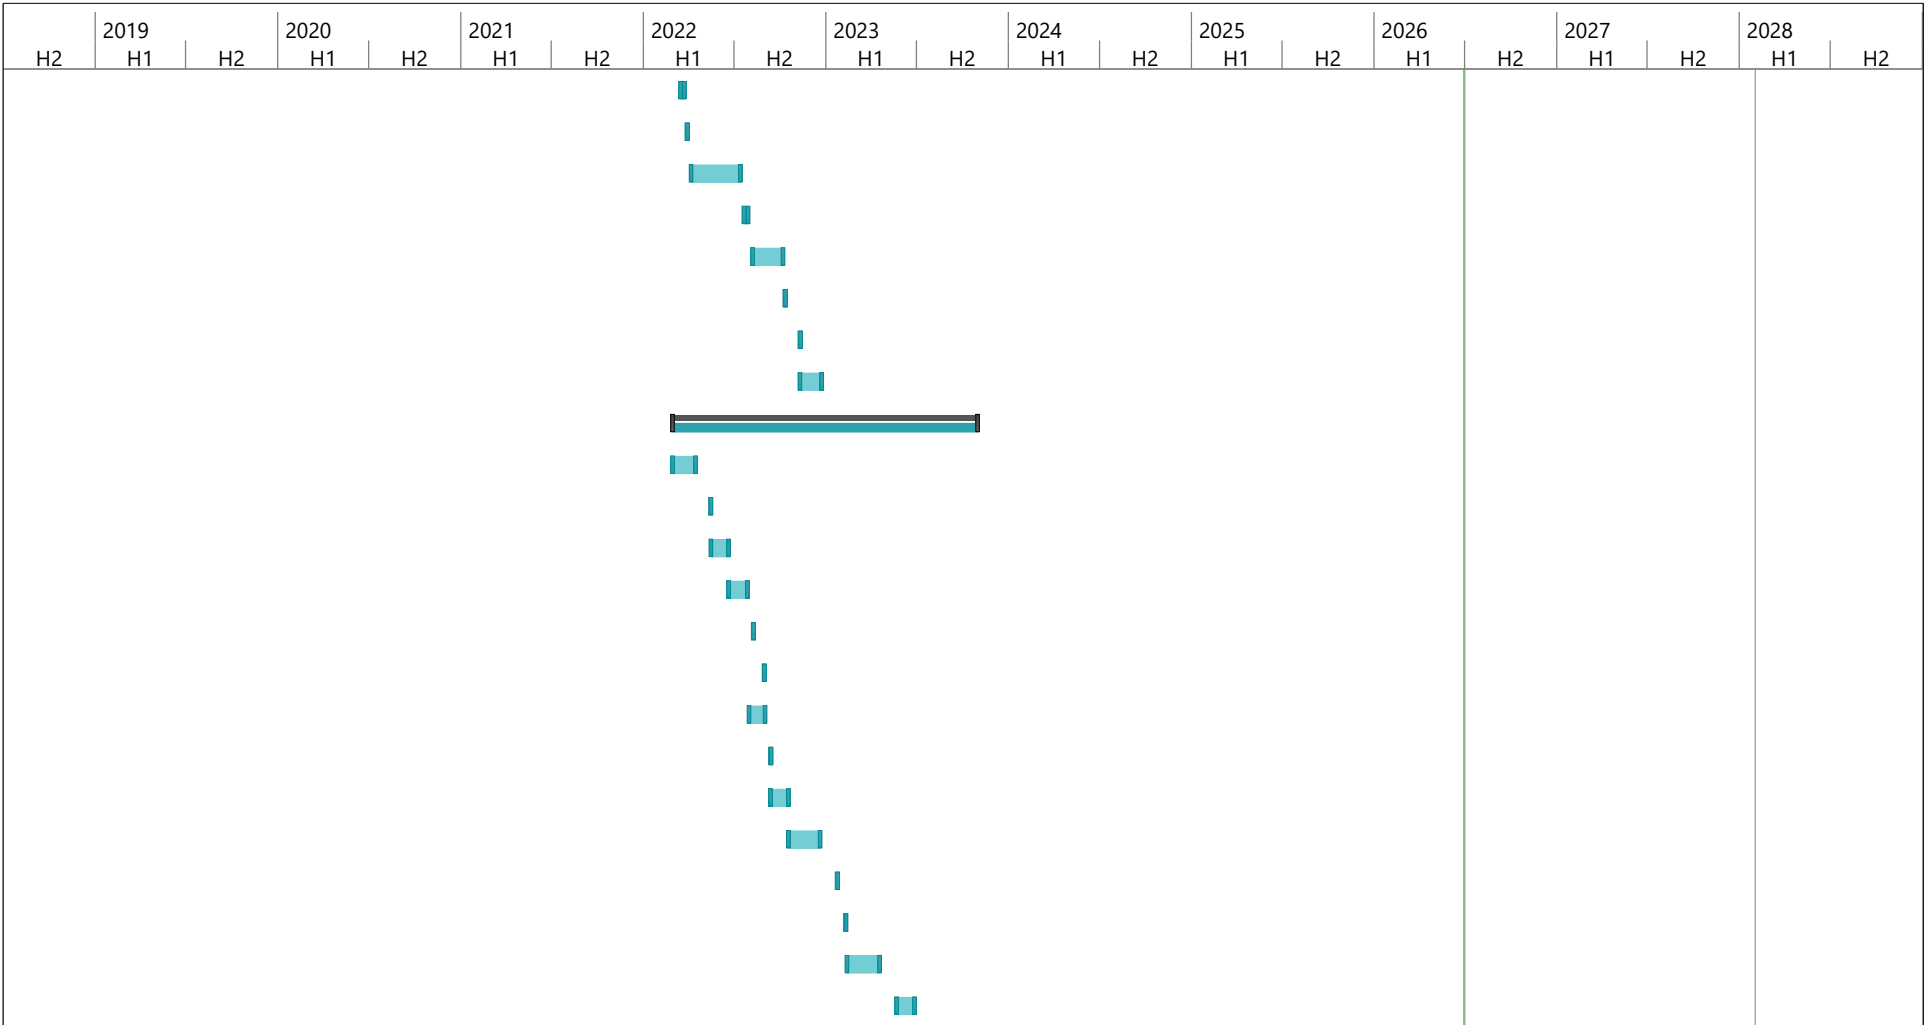


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

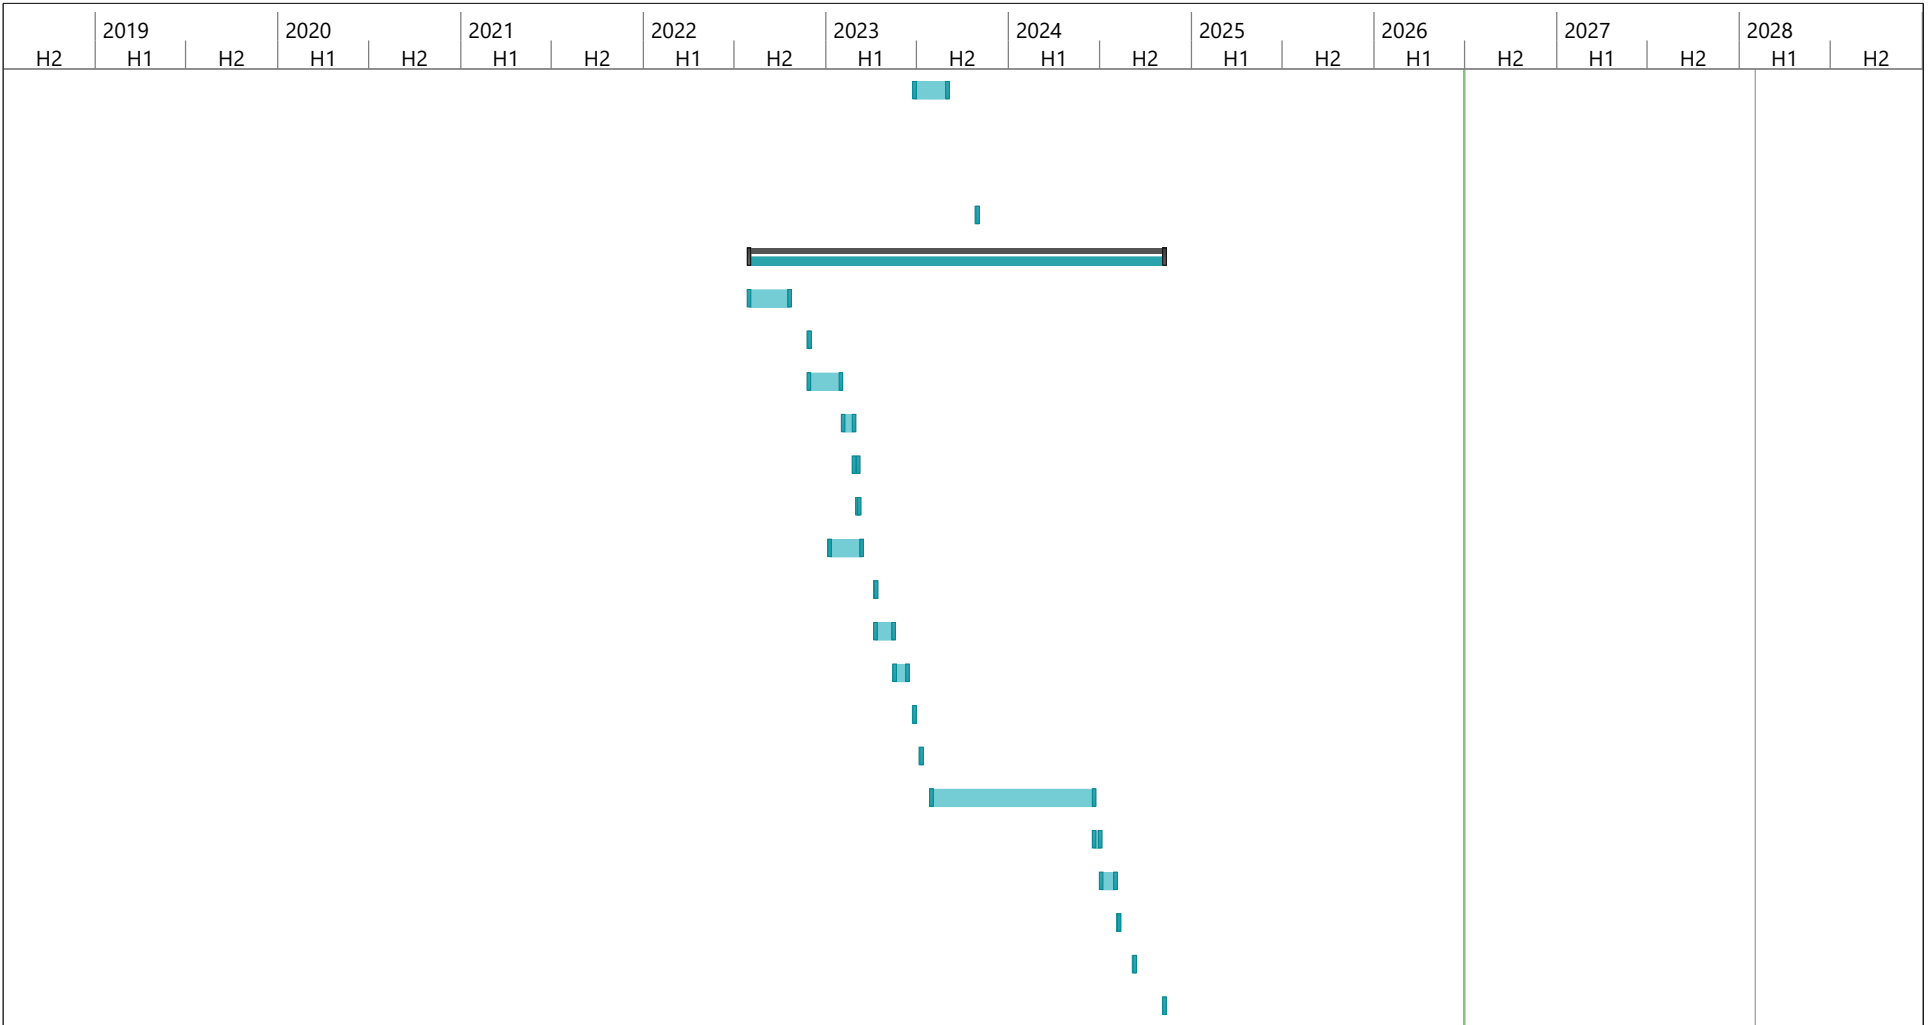


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

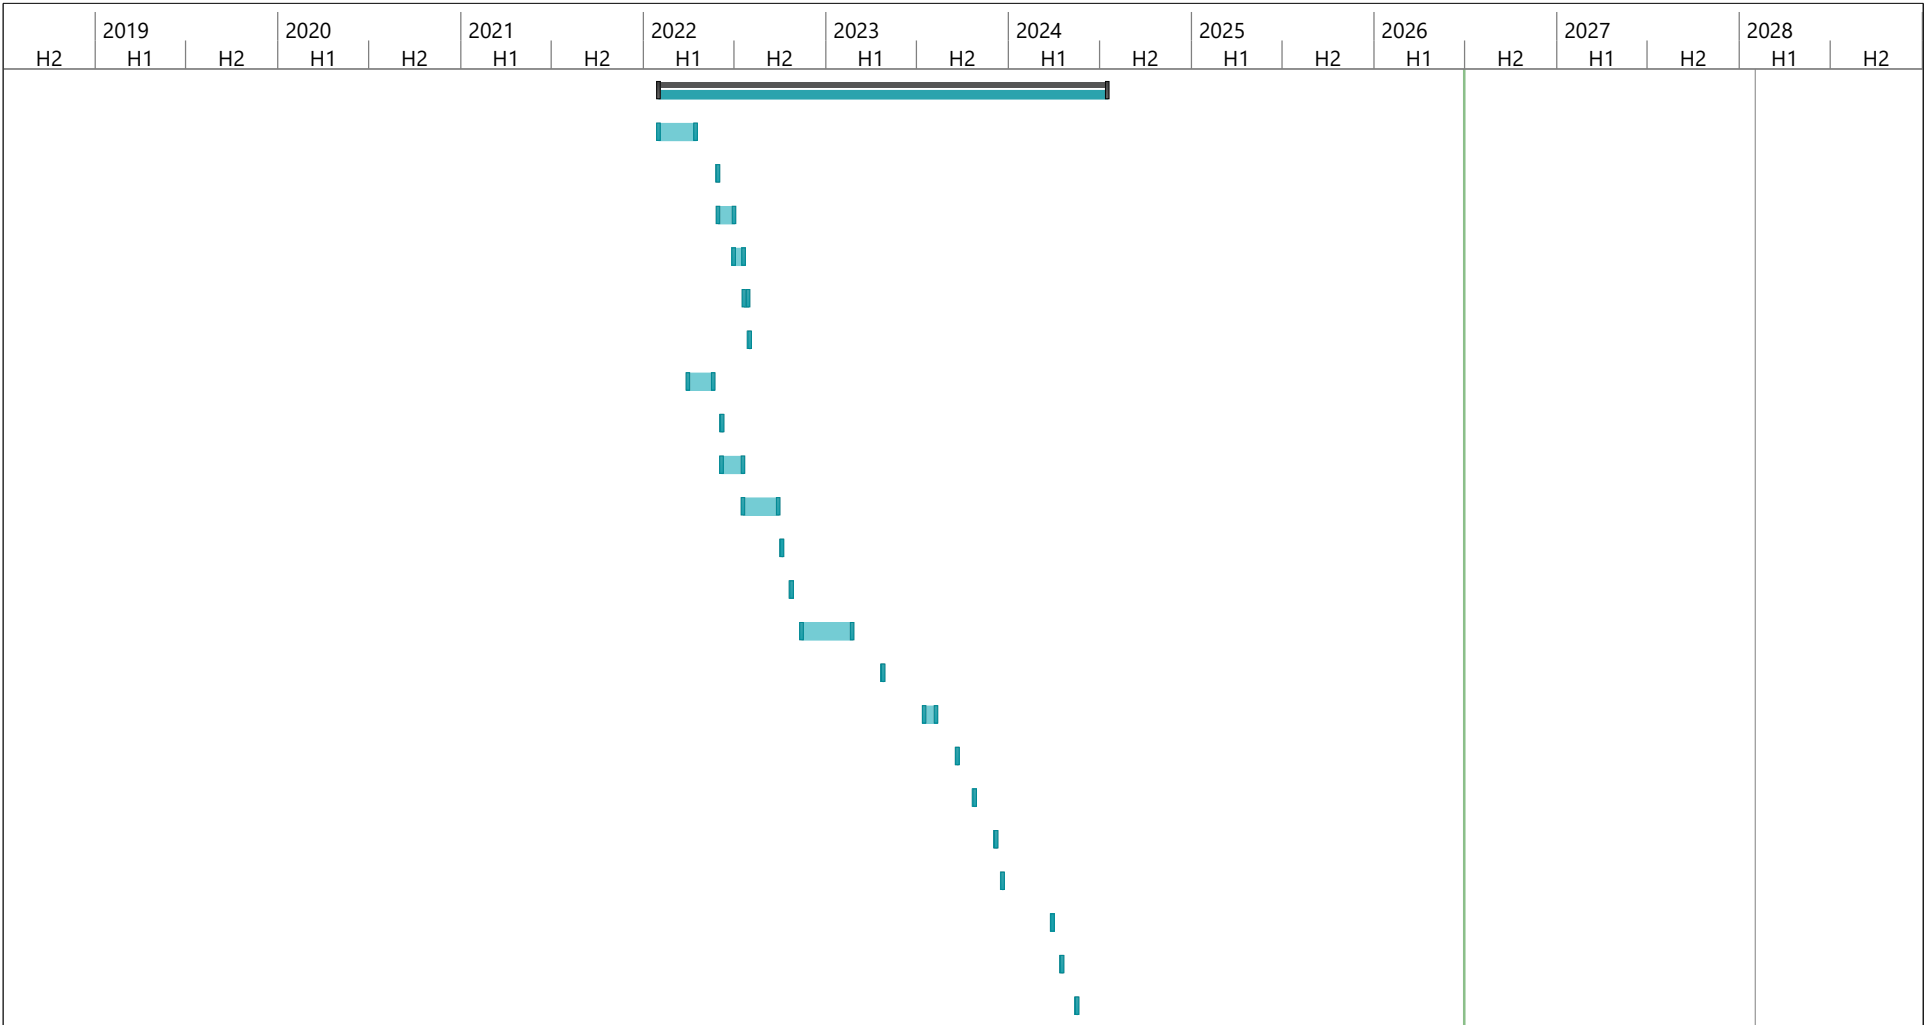


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

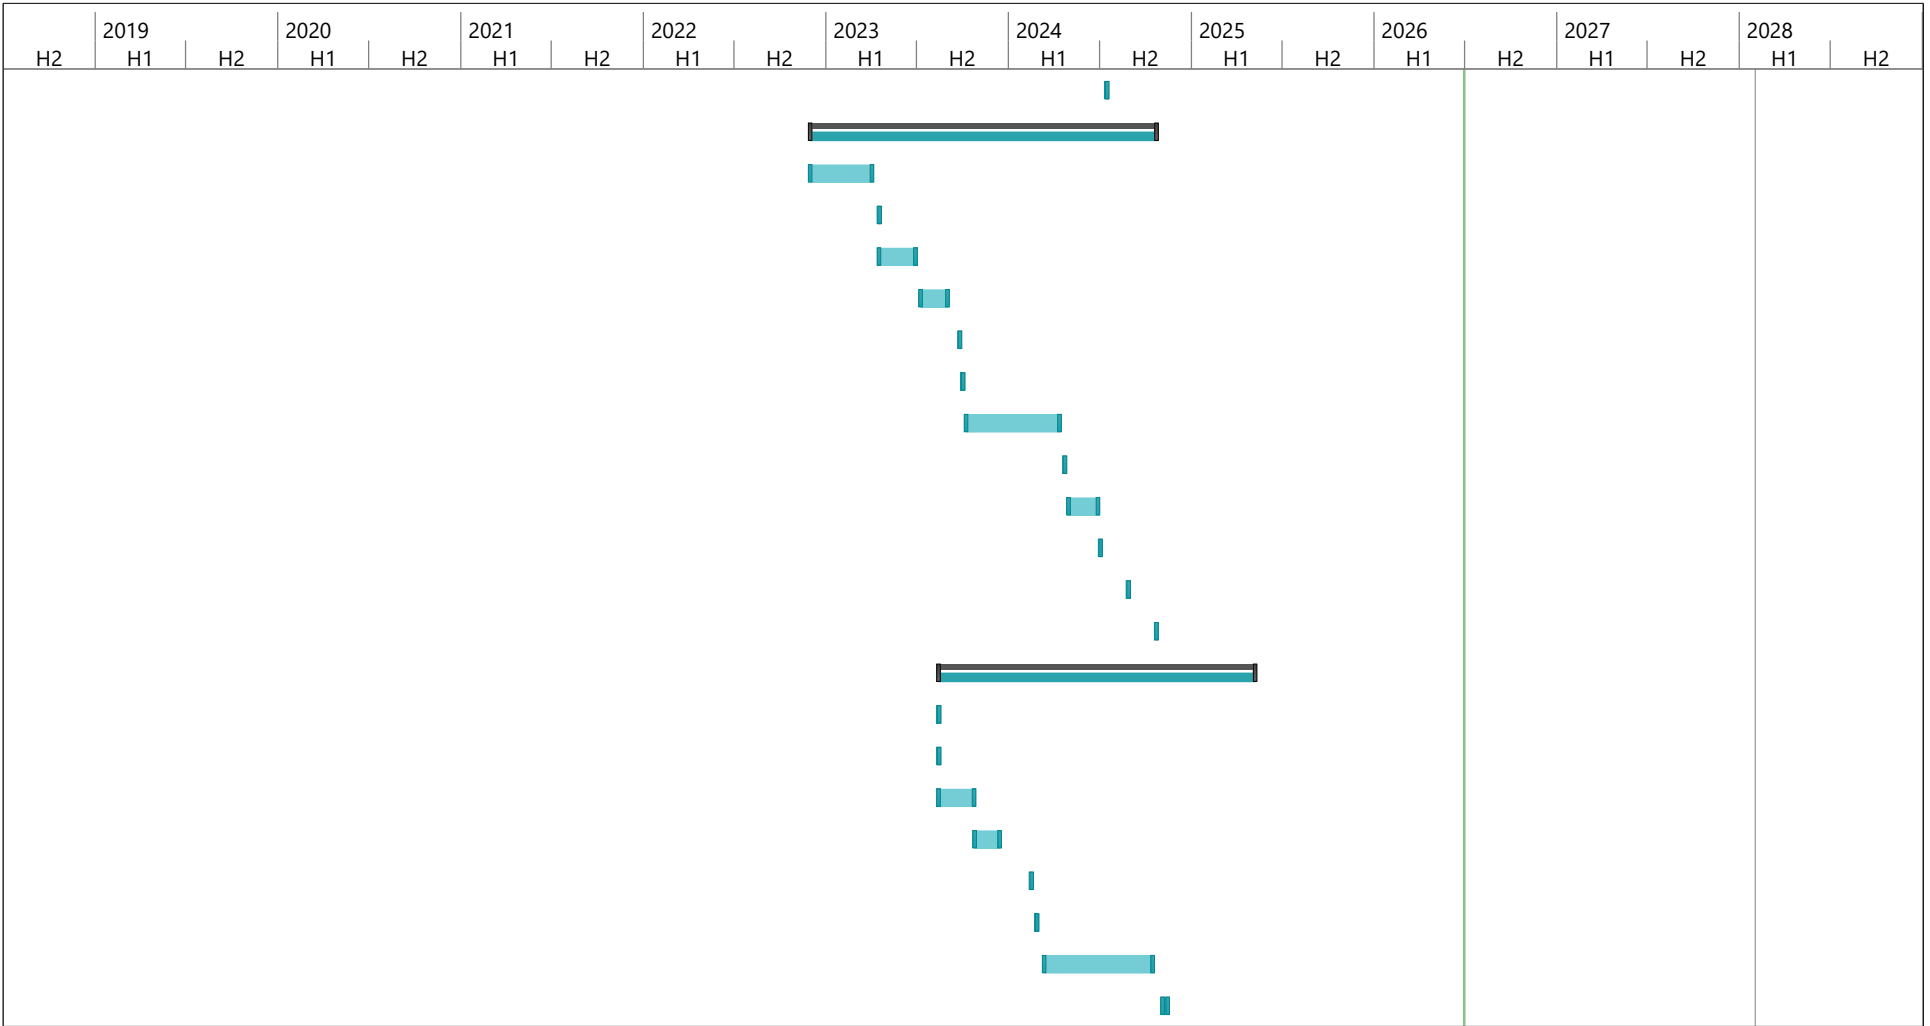


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

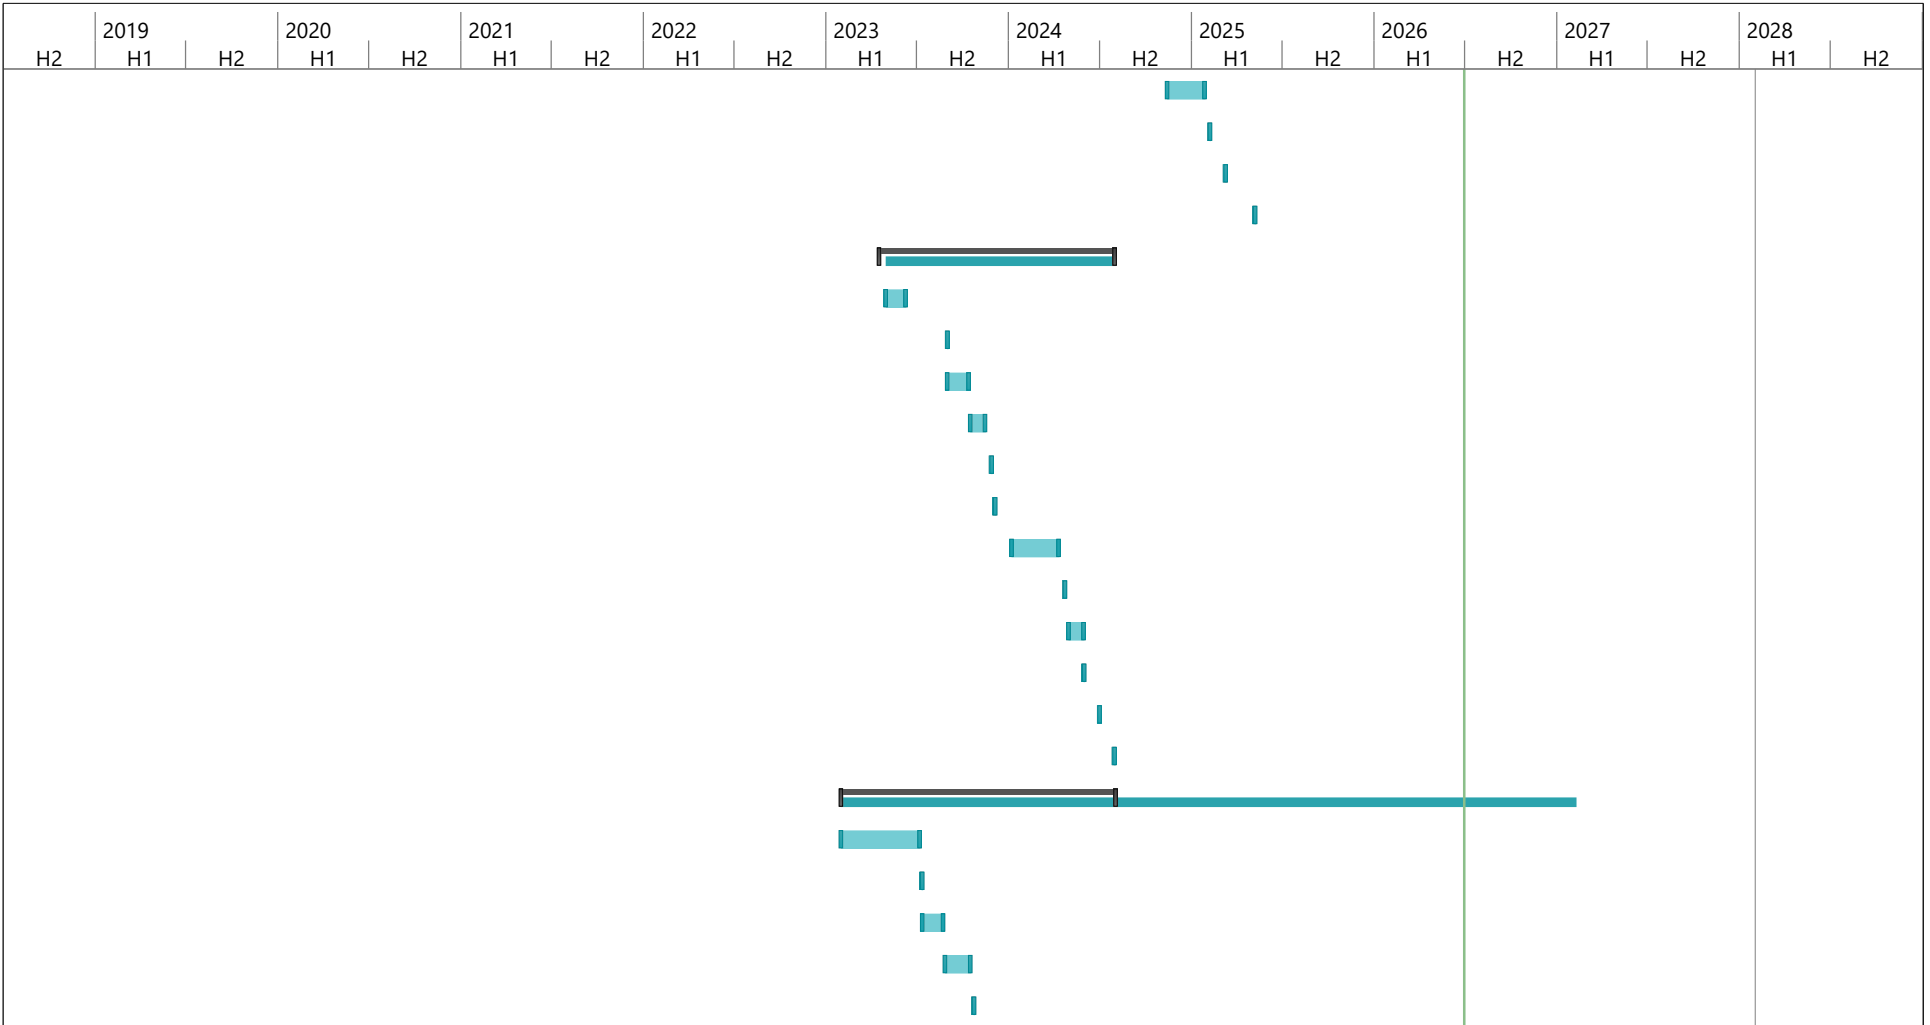


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

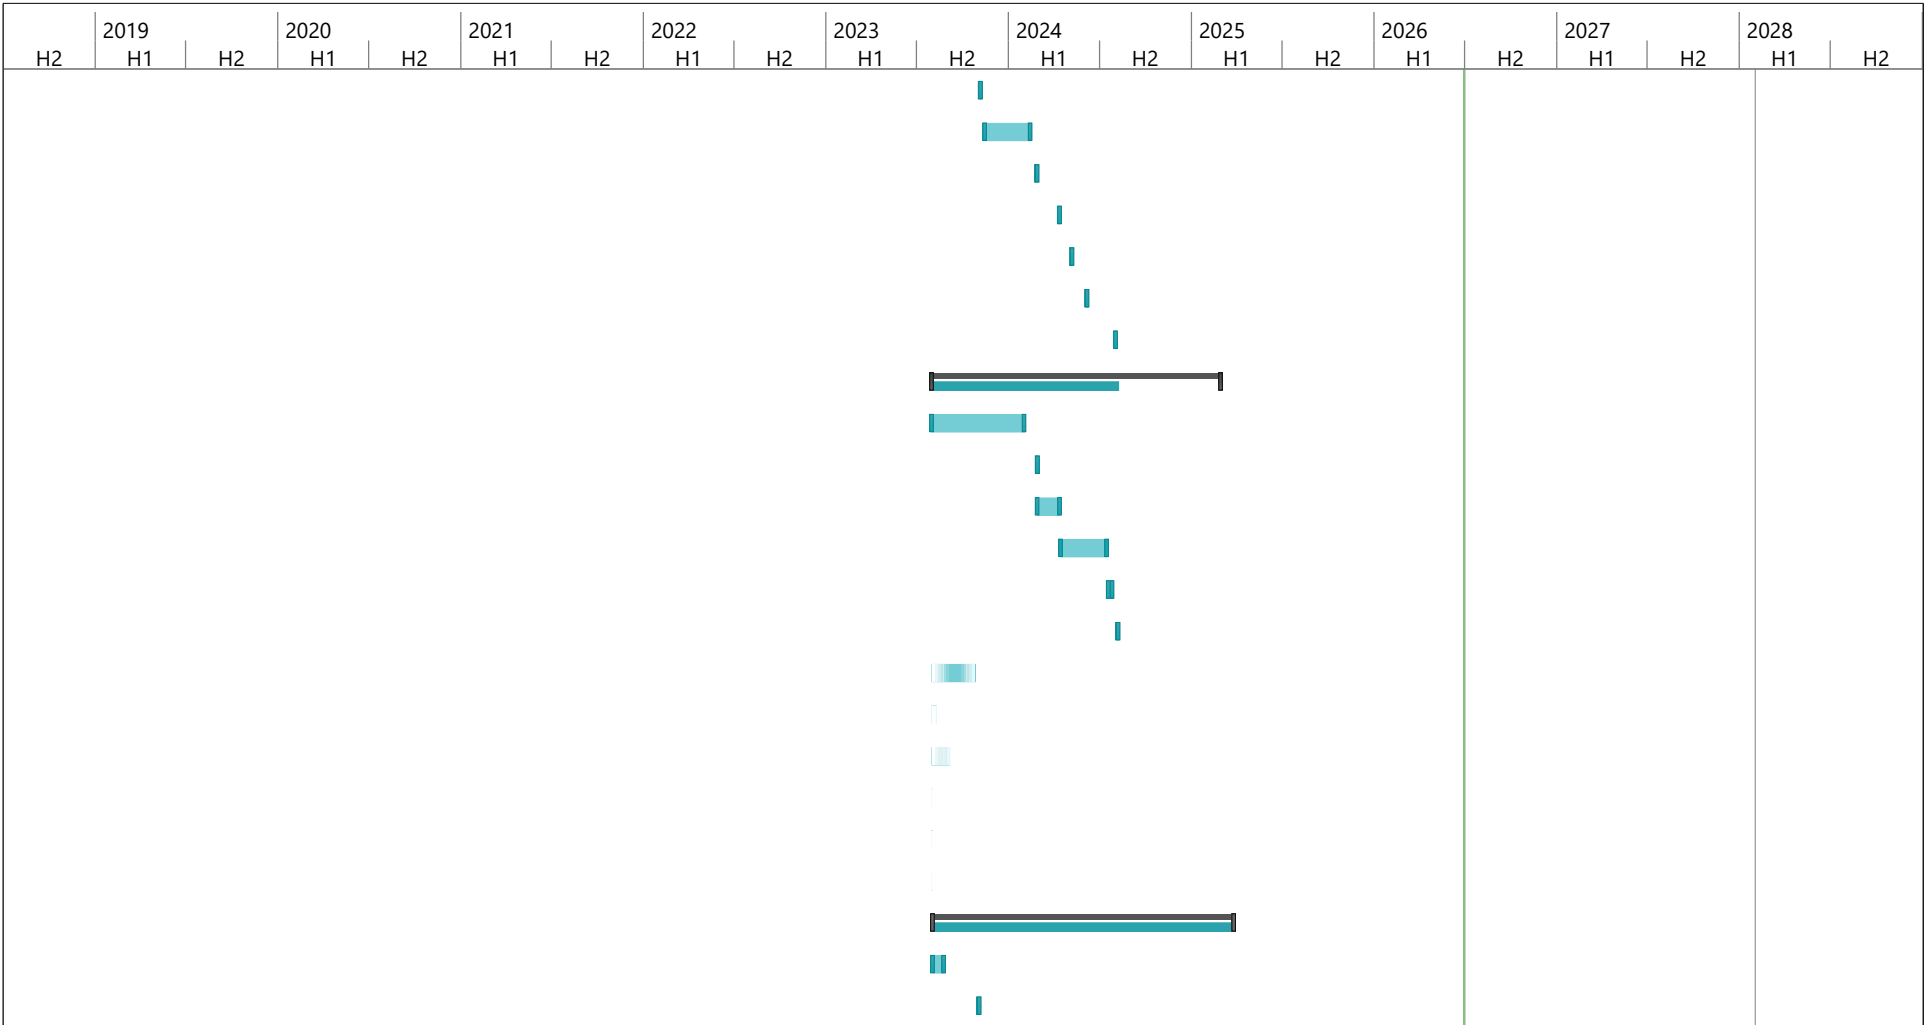


Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

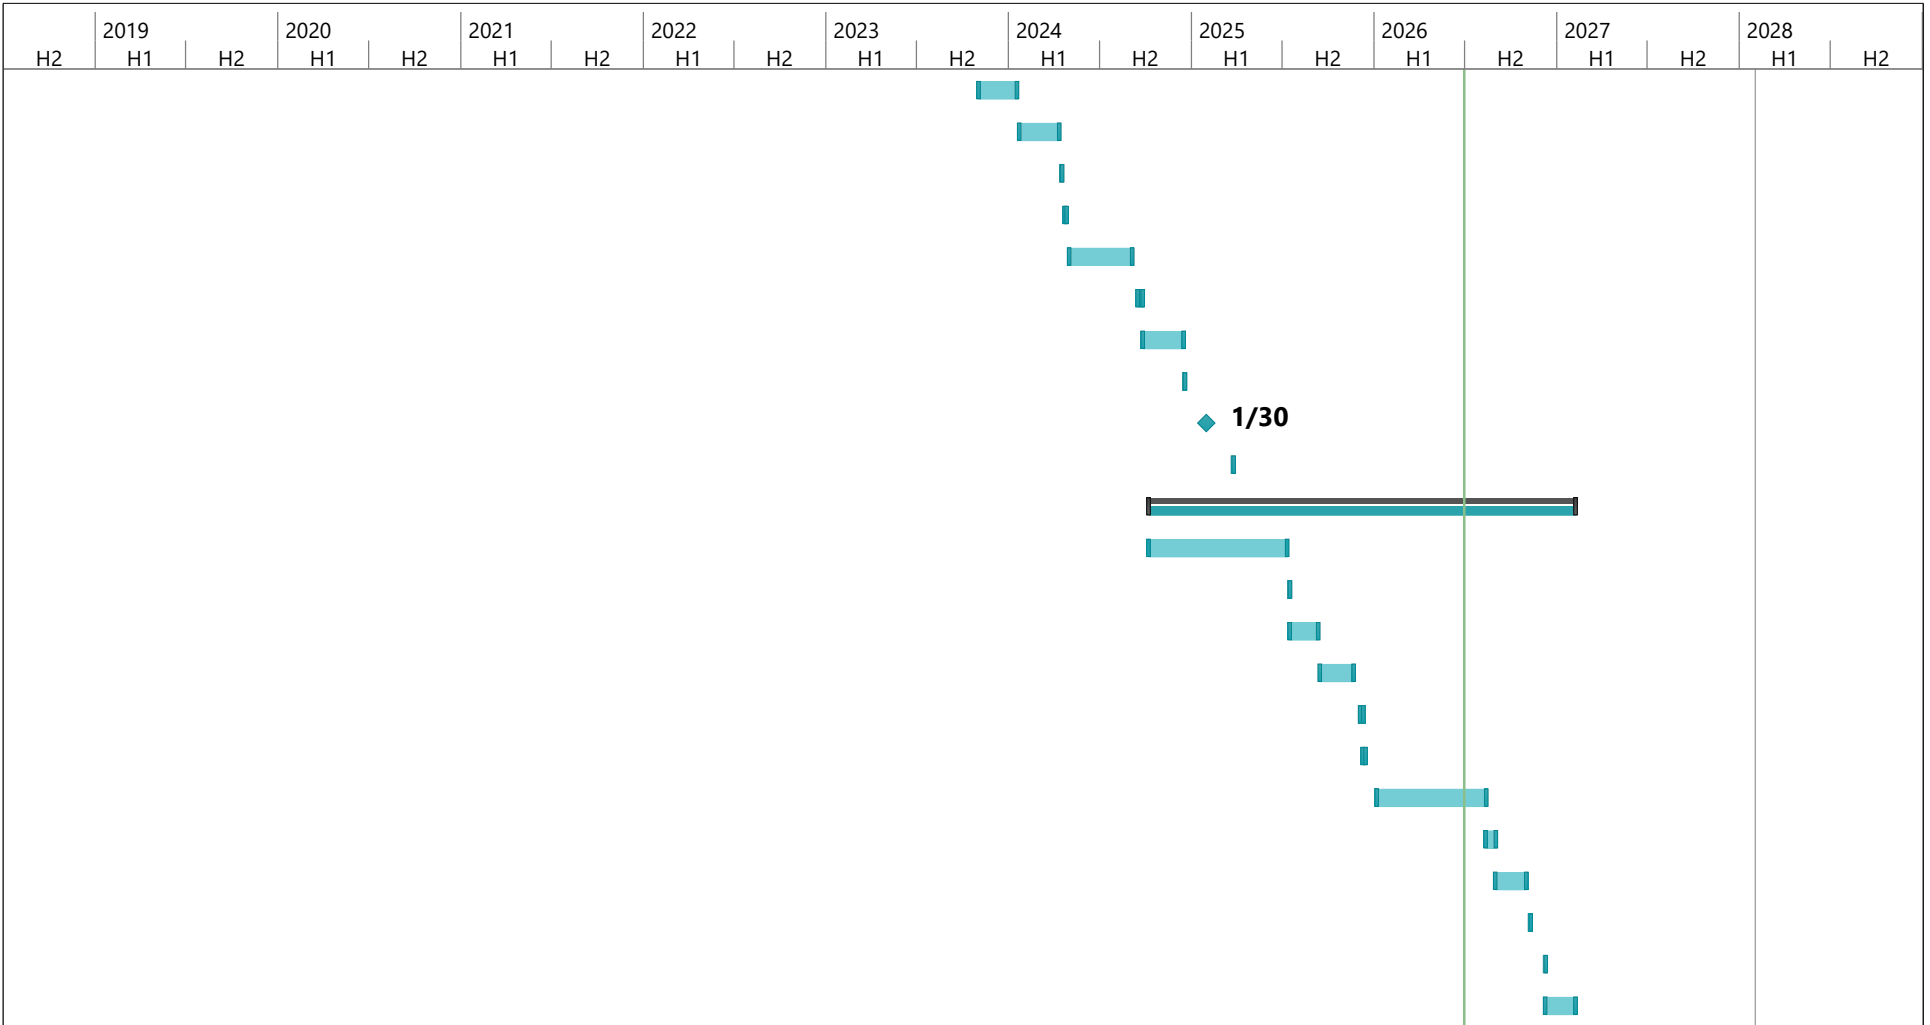

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

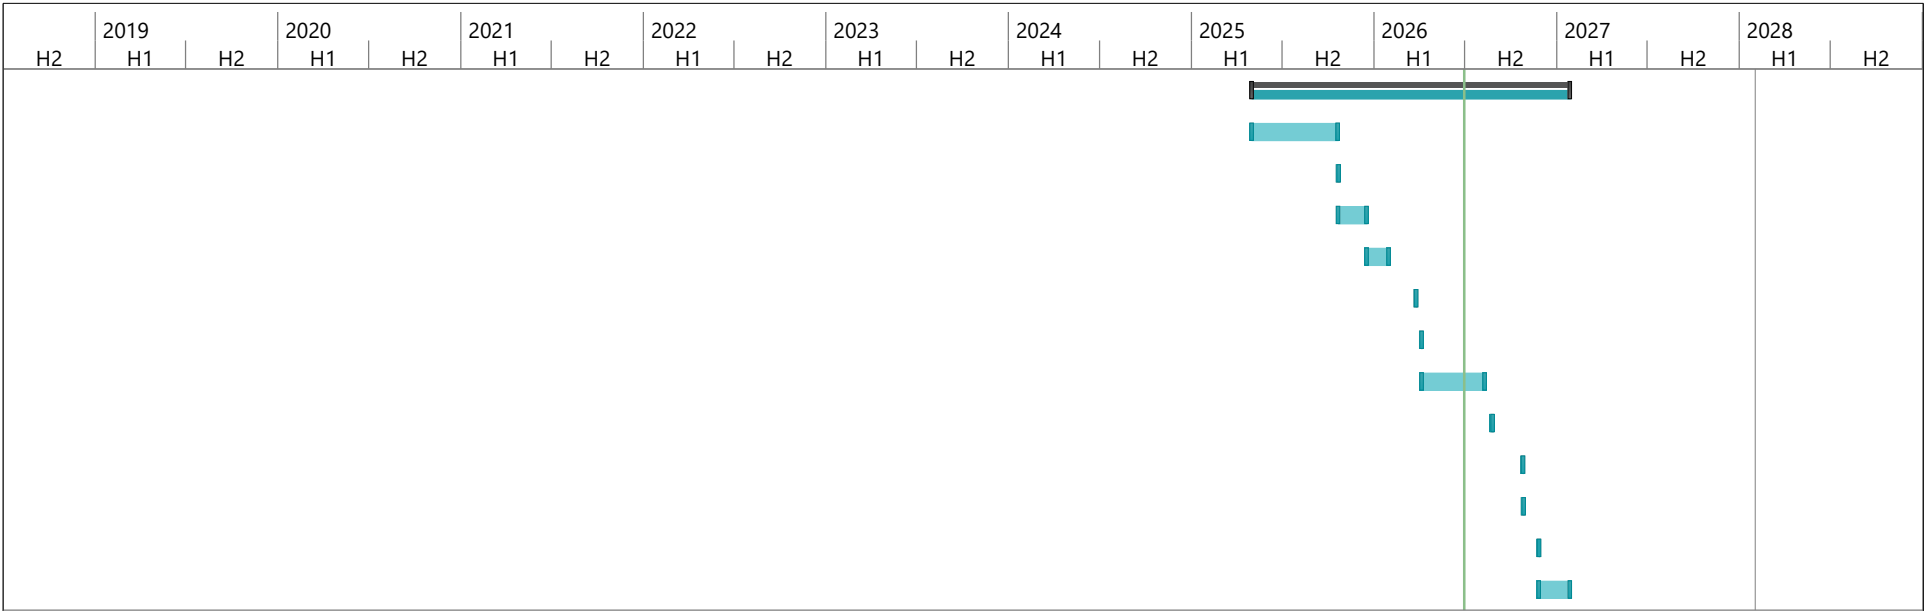

Project: IOU Master Task Timeli  
Date: Tue 6/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
