

ID		Task Name	Duration	Start	Finish	2018 H1	H2
1		UPDATED as of August 1, 2026					
2		SCE - Local RCI Solicitation	679 days	Tue 8/21/18	Fri 3/26/21		
3		SCE - RFA Preparation	40 days	Tue 8/21/18	Mon 10/15/18		
4		SCE - RFA Release	1 day	Fri 11/9/18	Fri 11/9/18		
5		SCE - RFA Abstract Creation Duration	30 days	Sat 11/10/18	Thu 12/20/18		
6		SCE - RFA Evaluation	82 days	Fri 12/21/18	Mon 4/15/19		
7		SCE - RFA Review with EE PRG	1 day	Tue 4/16/19	Tue 4/16/19		
8		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/21/19	Tue 5/21/19		
9		SCE - RFP Preparation	175 days	Wed 5/22/19	Tue 1/21/20		
10		SCE - RFP Release	1 day	Wed 1/22/20	Wed 1/22/20		
11		SCE - RFP Proposal Creation Duration	25 days	Thu 1/23/20	Wed 2/26/20		
12		SCE - RFP Evaluation	38 days	Thu 2/27/20	Mon 4/20/20		
13		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20		
14		SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20		
15		SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20		
16		SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20		
17		SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20		
18		SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20		
19		SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20		
20		SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21		
21		SCE - SW Lighting	518 days	Wed 4/3/19	Fri 3/26/21		
22		SCE - RFA Preparation	55 days	Wed 4/3/19	Tue 6/18/19		
23		SCE - RFA Release	1 day	Tue 7/2/19	Tue 7/2/19		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




ID		Task Name	Duration	Start	Finish	2018 H1	H2
24		SCE - RFA Abstract Creation Duration	20 days	Wed 7/3/19	Tue 7/30/19		
25		SCE - RFA Evaluation	34 days	Wed 7/31/19	Mon 9/16/19		
26		SCE - RFA Review with EE PRG	1 day	Tue 9/17/19	Tue 9/17/19		
27		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/24/19	Tue 9/24/19		
28		SCE - RFP Preparation	84 days	Wed 9/25/19	Mon 1/20/20		
29		SCE - RFP Release	1 day	Thu 2/6/20	Thu 2/6/20		
30		SCE - RFP Proposal Creation Duration	27 days	Fri 2/7/20	Mon 3/16/20		
31		SCE - RFP Evaluation	25 days	Tue 3/17/20	Mon 4/20/20		
32		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20		
33		SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20		
34		SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20		
35		SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20		
36		SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20		
37		SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20		
38		SCE - Advice Letter Approved	1 day	Wed 12/23/20	Wed 12/23/20		
39		SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21		
40		SCE - Local Public Sector Solicitation	573 days	Mon 8/31/20	Wed 11/9/22		
41		SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20		
42		SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20		
43		SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20		
44		SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21		
45		SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21		
46		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
47		SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21		
48		SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21		
49		SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21		
50		SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21		
51		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21		
52		SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21		
53		SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21		
54		SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21		
55		SCE - Final Award and Contract Signed	1 day	Tue 12/14/21	Tue 12/14/21		
56		SCE - Submit Advice Letter	37 days	Wed 12/15/21	Thu 2/3/22		
57		SCE - Submit Advice Letter	48 days	Wed 12/15/21	Fri 2/18/22		
58		SCE - Advice Letter Approved	1 day	Thu 8/18/22	Thu 8/18/22		
59		SCE - Implementation Plan	60 days	Thu 8/18/22	Wed 11/9/22		
60		SCE - Local Agriculture Solicitation	512 days	Mon 8/31/20	Tue 8/16/22		
61		SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20		
62		SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20		
63		SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20		
64		SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21		
65		SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21		
66		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21		
67		SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21		
68		SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21		
69		SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
70		SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21		
71		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21		
72		SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21		
73		SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21		
74		SCE - Final Award and Contract Signed	1 day	Mon 12/20/21	Mon 12/20/21		
75		SCE - Submit Advice Letter	33 days	Tue 12/21/21	Thu 2/3/22		
76		SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21		
77		SCE - Final Award and Contract Signed	1 day	Wed 12/15/21	Wed 12/15/21		
78		SCE - Submit Advice Letter	56 days	Thu 12/16/21	Thu 3/3/22		
79		SCE - Advice Letter Approved	1 day	Fri 4/22/22	Fri 4/22/22		
80		SCE - Implementation Plan	60 days	Sat 4/23/22	Thu 7/14/22		
81		SCE - SW Water/Wastewater Solicitation	522 days	Mon 11/16/20	Tue 11/15/22		
82		SCE - RFA Preparation	70 days	Mon 11/16/20	Fri 2/19/21		
83		SCE - RFA Release	1 day	Thu 3/4/21	Thu 3/4/21		
84		SCE - RFA Abstract Creation Duration	29 days	Thu 3/4/21	Tue 4/13/21		
85		SCE - RFA Evaluation	20 days	Wed 4/14/21	Tue 5/11/21		
86		SCE - RFA Review with EE PRG	1 day	Tue 5/18/21	Tue 5/18/21		
87		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/27/21	Thu 5/27/21		
88		SCE - RFP Preparation	34 days	Mon 4/19/21	Thu 6/3/21		
89		SCE - RFP Release	1 day	Thu 7/1/21	Thu 7/1/21		
90		SCE - RFP Proposal Creation Duration	25 days	Fri 7/2/21	Thu 8/5/21		
91		SCE - RFP Evaluation	41 days	Fri 8/6/21	Fri 10/1/21		
92		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/26/21	Tue 10/26/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
93		SCE - RFP Review with EE PRG	1 day	Tue 10/19/21	Tue 10/19/21		
94		SCE - Contract Negotiation and Development	94 days	Wed 10/27/21	Mon 3/7/22		
95		SCE - Contract Review with EE PRG	1 day	Tue 3/15/22	Tue 3/15/22		
96		SCE - Final Award and Contract Signed	1 day	Tue 4/19/22	Tue 4/19/22		
97		SCE - Submit Advice Letter	40 days	Wed 4/20/22	Tue 6/14/22		
98		SCE - Advice Letter Approved	26 days	Wed 6/15/22	Wed 7/20/22		
99		SCE - Implementation Plan	44 days	Thu 7/21/22	Tue 9/20/22		
100		SCE - SW ETP Solicitation	466 days	Fri 5/1/20	Fri 2/11/22		
101		SCE - RFA Preparation	57 days	Fri 5/1/20	Mon 7/20/20		
102		SCE - RFA Release	1 day	Tue 8/4/20	Tue 8/4/20		
103		SCE - RFA Abstract Creation Duration	24 days	Fri 8/7/20	Wed 9/9/20		
104		SCE - RFA Evaluation	16 days	Thu 9/10/20	Thu 10/1/20		
105		SCE - RFA Review with EE PRG	1 day	Tue 10/20/20	Tue 10/20/20		
106		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/27/20	Tue 10/27/20		
107		SCE - RFP Preparation	42 days	Tue 9/8/20	Wed 11/4/20		
108		SCE - RFP Release	1 day	Tue 1/5/21	Tue 1/5/21		
109		SCE - RFP Proposal Creation Duration	37 days	Tue 1/5/21	Wed 2/24/21		
110		SCE - RFP Evaluation	28 days	Wed 2/24/21	Fri 4/2/21		
111		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/27/21	Tue 4/27/21		
112		SCE - RFP Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21		
113		SCE - Contract Negotiation and Development	69 days	Wed 4/21/21	Mon 7/26/21		
114		SCE - Contract Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21		
115		SCE - Final Award and Contract Signed	1 day	Tue 9/14/21	Tue 9/14/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
116		SCE - Submit Advice Letter	18 days	Wed 9/15/21	Fri 10/8/21		
117		SCE - Advice Letter Approved	1 day	Tue 11/9/21	Tue 11/9/21		
118		SCE - Implementation Plan	60 days	Wed 11/10/21	Tue 2/1/22		
119		SCE - SW Higher-Education Solicitation	547 days?	Thu 10/1/20	Fri 11/4/22		
120		SCE - RFA Preparation	89 days	Thu 10/1/20	Tue 2/2/21		
121		SCE - RFA Release	1 day	Thu 2/4/21	Thu 2/4/21		
122		SCE - RFA Abstract Creation Duration	19 days	Fri 2/5/21	Wed 3/3/21		
123		SCE - RFA Evaluation	31 days	Thu 3/4/21	Thu 4/15/21		
124		SCE - RFA Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21		
125		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 4/29/21	Thu 4/29/21		
126		SCE - RFP Preparation	39 days	Mon 3/22/21	Thu 5/13/21		
127		SCE - RFP Release	1 day	Fri 5/28/21	Fri 5/28/21		
128		SCE - RFP Proposal Creation Duration	24 days	Fri 6/4/21	Wed 7/7/21		
129		SCE - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21		
130		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/30/21	Mon 8/30/21		
131		SCE - RFP Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21		
132		SCE - Contract Negotiation and Development	95 days	Fri 9/3/21	Thu 1/13/22		
133		SCE - Contract Review with EE PRG	1 day	Tue 1/18/22	Tue 1/18/22		
134		SCE - Final Award and Contract Signed	1 day	Sun 3/6/22	Sun 3/6/22		
135		SCE - Submit Advice Letter	1 day	Tue 4/19/22	Tue 4/19/22		
136		SCE - Advice Letter Approved	1 day	Mon 8/15/22	Mon 8/15/22		
137		SCE - Implementation Plan	60 days	Mon 8/15/22	Fri 11/4/22		
138		SCE - Local Equity Residential and SMB	384 days?	Tue 2/15/22	Fri 8/4/23		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
139		SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22		
140		SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22		
141		SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22		
142		SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22		
143		SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22		
144		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22		
145		SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22		
146		SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22		
147		SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22		
148		SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22		
149		SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22		
150		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22		
151		SCE - Contract Negotiation and Development	65 days	Wed 11/2/22	Tue 1/31/23		
152		SCE - Contract Review with EE PRG	1 day	Tue 2/21/23	Tue 2/21/23		
153		SCE - Final Award and Contract Signed	1 day	Thu 3/30/23	Thu 3/30/23		
154		SCE - Submit Advice Letter	22 days	Sun 4/3/22	Mon 5/2/22		
155		SCE - Advice Letter Approved	28 days	Tue 5/2/23	Thu 6/8/23		
156		SCE - Implementation Plan	45 days	Thu 6/8/23	Wed 8/9/23		
157							
158		SCE - Local Equity SMB	431 days?	Tue 2/15/22	Tue 10/10/23		
159		SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22		
160		SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22		
161		SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
162		SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22		
163		SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22		
164		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22		
165		SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22		
166		SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22		
167		SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22		
168		SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22		
169		SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22		
170		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22		
171		SCE - Contract Negotiation and Development	108 days	Wed 11/2/22	Fri 3/31/23		
172		SCE - Contract Review with EE PRG	1 day	Tue 4/18/23	Tue 4/18/23		
173		SCE - Final Award and Contract Signed	1 day	Wed 5/31/23	Wed 5/31/23		
174		SCE - Submit Advice Letter	22 days	Mon 6/6/22	Tue 7/5/22		
175		SCE - Advice Letter Approved	24 days	Thu 7/6/23	Tue 8/8/23		
176		SCE - Implementation Plan	45 days	Wed 8/9/23	Tue 10/10/23		
177		SCE - Local Strategic Energy Management Solicitation	372 days?	Thu 12/1/22	Fri 5/3/24		
178		SCE - RFP Preparation	85 days	Thu 12/1/22	Wed 3/29/23		
179		SCE - RFP Release	1 day	Fri 4/7/23	Fri 4/7/23		
180		SCE - RFP Proposal Creation Duration	35 days	Fri 4/7/23	Thu 5/25/23		
181		SCE - RFP Evaluation	22 days	Thu 6/1/23	Fri 6/30/23		
182		SCE - RFP Review with EE PRG	1 day	Tue 7/18/23	Tue 7/18/23		
183		SCE - Contract Negotiation and Development	86 days	Tue 8/1/23	Tue 11/28/23		
184		SCE - Contract Review with EE PRG	1 day	Tue 12/19/23	Tue 12/19/23		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
185		SCE - Final Award and Contract Signed	6 days	Fri 1/19/24	Fri 1/26/24		
186		SCE - Submit Advice Letter	34 days	Wed 1/31/24	Mon 3/18/24		
187		SCE - Advice Letter Approved	40 days	Tue 3/19/24	Mon 5/13/24		
188		SCE - Local Large Commercial Solicitation	488 days?	Mon 6/26/23	Wed 5/7/25		
189		SCE - RFP Preparation	35 days	Mon 6/26/23	Fri 8/11/23		
190		SCE - RFP Release	1 day	Thu 8/17/23	Thu 8/17/23		
191		SCE - RFP Proposal Creation Duration	41 days	Thu 8/17/23	Thu 10/12/23		
192		SCE - RFP Paused	1 day	Fri 10/13/23	Fri 10/13/23		
193		SCE - Residential Multifamily	326 days?	Fri 9/1/23	Fri 11/29/24		
194		SCE - RFP Preparation	47 days	Fri 9/1/23	Mon 11/6/23		
195		SCE - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23		
196		SCE - RFP Proposal Creation Duration	48 days	Mon 11/6/23	Wed 1/10/24		
197		SCE - RFP Evaluation	25 days	Thu 1/11/24	Wed 2/14/24		
198		SCE - RFP Review with EE PRG	1 day	Tue 2/20/24	Tue 2/20/24		
199		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 2/28/24	Wed 2/28/24		
200		SCE - Contract Negotiation and Development	70 days	Mon 3/4/24	Fri 6/7/24		
201		SCE - Contract Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
202		SCE - Final Award and Contract Signed	15 days	Mon 7/29/24	Fri 8/16/24		
203		SCE - Submit Advice Letter	30 days	Mon 8/19/24	Fri 9/27/24		
204		SCE - Advice Letter Approved	1 day	Mon 10/28/24	Mon 10/28/24		
205		SCE - Local Large Industrial	499 days	Fri 11/3/23	Wed 10/1/25		
206		SCE - RFP Preparation	17 days	Fri 11/3/23	Mon 11/27/23		
207		SCE - RFP Release	1 day	Mon 12/11/23	Mon 12/11/23		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
208		SCE - RFP Proposal Creation Duration	49 days	Mon 12/11/23	Thu 2/15/24		
209		SCE - RFP Evaluation	35 days	Fri 2/16/24	Thu 4/4/24		
210		SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24		
211		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/23/24	Tue 4/23/24		
212		SCE - Contract Negotiation and Development	208 days	Wed 4/24/24	Fri 2/7/25		
213		SCE - Contract Review with EE PRG	1 day	Tue 4/29/25	Tue 4/29/25		
214		SCE - Final Award and Contract Signed	42 days	Thu 5/1/25	Fri 6/27/25		
215		SCE - Submit Advice Letter	35 days	Mon 6/30/25	Fri 8/15/25		
216		SCE - Advice Letter Approved	33 days	Mon 8/18/25	Wed 10/1/25		
217		SCE - MAP - All Sectors	299 days?	Mon 11/20/23	Thu 1/9/25		
218		SCE - RFP Preparation	20 days	Mon 11/20/23	Fri 12/15/23		
219		SCE - RFP Release	1 day	Mon 1/8/24	Mon 1/8/24		
220		SCE - RFP Proposal Creation Duration	40 days	Mon 1/8/24	Fri 3/1/24		
221		SCE - RFP Evaluation	30 days	Mon 3/4/24	Fri 4/12/24		
222		SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24		
223		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/24/24	Wed 4/24/24		
224		SCE - Contract Negotiation and Development	108 days	Wed 5/1/24	Fri 9/27/24		
225		SCE - Contract Review with EE PRG	1 day	Tue 10/15/24	Tue 10/15/24		
226		SCE - Final Award and Contract Signed	12 days	Tue 10/29/24	Wed 11/13/24		
227		SCE - Submit Advice Letter	43 days	Wed 11/13/24	Fri 1/10/25		
228		SCE - Advice Letter Approved	22 days	Mon 1/13/25	Tue 2/11/25		
229		SCE - Residential	360 days?	Mon 11/20/23	Fri 4/4/25		
230		SCE - RFP Preparation	20 days	Tue 1/16/24	Mon 2/12/24		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
231		SCE - RFP Release	1 day	Thu 3/28/24	Thu 3/28/24		
232		SCE - RFP Proposal Creation Duration	41 days	Thu 3/28/24	Thu 5/23/24		
233		SCE - RFP Evaluation	35 days	Fri 5/24/24	Thu 7/11/24		
234		SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
235		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/5/24	Mon 8/5/24		
236		SCE - Contract Negotiation and Development	80 days	Mon 8/19/24	Fri 12/6/24		
237		SCE - Contract Review with EE PRG	1 day	Tue 12/17/24	Tue 12/17/24		
238		SCE - Final Award and Contract Signed	11 days	Mon 1/13/25	Mon 1/27/25		
239		SCE - Submit Advice Letter	19 days	Mon 2/3/25	Thu 2/27/25		
240		SCE - Advice Letter Approved	1 day	Tue 4/1/25	Tue 4/1/25		
241							
242		SCE - Local Comprehensive Commercial Solicitation	431 days?	Mon 11/13/23	Mon 7/7/25		
243		SCE - RFP Preparation	73 days	Mon 11/13/23	Wed 2/21/24		
244		SCE - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24		
245		SCE - RFP Proposal Creation Duration	43 days	Thu 2/29/24	Mon 4/29/24		
246		SCE - RFP Evaluation	54 days	Tue 4/30/24	Fri 7/12/24		
247		SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
248		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Phase 1	1 day	Mon 7/29/24	Mon 7/29/24		
249		SCE - Contract Negotiation and Development - Phase 1	81 days	Tue 7/30/24	Tue 11/19/24		
250		SCE - Contract Review with EE PRG - Phase 1	1 day	Tue 12/17/24	Tue 12/17/24		
251		SCE - Final Award and Contract Signed - Phase 1	1 day	Tue 1/28/25	Tue 1/28/25		
252		SCE - Submit Advice Letter - Phase 1	23 days	Tue 1/28/25	Thu 2/27/25		
253		SCE - Advice Letter Approved - Phase 1	1 day	Tue 4/1/25	Tue 4/1/25		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
254		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Pha	1 day	Mon 9/30/24	Mon 9/30/24		
255		SCE - Contract Negotiation and Development - Phase 2	80 days	Mon 12/2/24	Fri 3/21/25		
256		SCE - Contract Review with EE PRG - Phase 2	1 day	Tue 4/29/25	Tue 4/29/25		
257		SCE - Final Award and Contract Signed - Phase 2	1 day	Tue 5/20/25	Tue 5/20/25		
258		SCE - Submit Advice Letter - Phase 2	0 days	N/A	N/A		
259		SCE - Advice Letter Approved - Phase 2	0 days	N/A	N/A		
260		SCE - SW ETP Solicitation	505 days	Wed 2/25/26	Tue 2/1/28		
261		SCE - RFA Preparation	63 days	Wed 2/25/26	Fri 5/22/26		
262		SCE - RFA Release	1 day	Tue 5/26/26	Tue 5/26/26		
263		SCE - RFA Abstract Creation Duration	34 days	Tue 5/26/26	Fri 7/10/26		
264		SCE - RFA Evaluation	19 days	Tue 7/21/26	Fri 8/14/26		
265		SCE - RFA Review with EE PRG	1 day	Tue 8/18/26	Tue 8/18/26		
266		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/25/26	Tue 8/25/26		
267		SCE - RFP Preparation	42 days	Mon 7/6/26	Tue 9/1/26		
268		SCE - RFP Release	1 day	Mon 11/2/26	Mon 11/2/26		
269		SCE - RFP Proposal Creation Duration	37 days	Mon 11/2/26	Tue 12/22/26		
270		SCE - RFP Evaluation	25 days	Wed 1/6/27	Tue 2/9/27		
271		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/16/27	Tue 2/16/27		
272		SCE - RFP Review with EE PRG	1 day	Tue 2/23/27	Tue 2/23/27		
273		SCE - Contract Negotiation and Development	80 days	Tue 3/2/27	Mon 6/21/27		
274		SCE - Contract Review with EE PRG	1 day	Tue 7/20/27	Tue 7/20/27		
275		SCE - Final Award and Contract Signed	1 day	Wed 7/28/27	Wed 7/28/27		
276		SCE - Submit Advice Letter	23 days	Thu 8/5/27	Mon 9/6/27		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1	H2
277		SCE - Advice Letter Approved	46 days	Tue 9/7/27	Tue 11/9/27		
278		SCE - Implementation Plan	60 days	Wed 11/10/27	Tue 2/1/28		
279							
280		SCG - Local Single Family Solicitation	660 days	Sun 7/1/18	Thu 1/7/21		
281		SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18		
282		SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18		
283		SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19		
284		SCG - RFA Evaluation	39 days	Mon 1/7/19	Thu 2/28/19		
285		SCG - RFA Review with EE PRG	1 day	Tue 3/5/19	Tue 3/5/19		
286		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19		
287		SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19		
288		SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19		
289		SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19		
290		SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19		
291		SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19		
292		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
293		SCG - Contract Negotiation and Development	69 days	Mon 1/27/20	Thu 4/30/20		
294		SCG - Contract Review with EE PRG	14 days	Tue 5/5/20	Fri 5/22/20		
295		SCG - Final Award and Contract Signed	8 days	Mon 5/25/20	Wed 6/3/20		
296		SCG - Submit Advice Letter	96 days	Mon 6/1/20	Mon 10/12/20		
297		SCG - Advice Letter Approved	1 day	Thu 11/12/20	Thu 11/12/20		
298		SCG - Implementation Plan	41 days	Fri 11/13/20	Fri 1/8/21		
299		SCG - Local Multi-family Solicitation	735 days	Sun 7/1/18	Thu 4/22/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1	H2
300		SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18		
301		SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18		
302		SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19		
303		SCG - RFA Evaluation	59 days	Mon 1/7/19	Thu 3/28/19		
304		SCG - RFA Review with EE PRG	1 day	Tue 4/2/19	Tue 4/2/19		
305		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19		
306		SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19		
307		SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19		
308		SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19		
309		SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19		
310		SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19		
311		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
312		SCG - Contract Negotiation and Development	155 days	Mon 1/27/20	Fri 8/28/20		
313		SCG - Contract Review with EE PRG	99 days	Tue 5/5/20	Fri 9/18/20		
314		SCG - Final Award and Contract Signed	8 days	Mon 9/21/20	Wed 9/30/20		
315		SCG - Submit Advice Letter	37 days	Thu 10/1/20	Fri 11/20/20		
316		SCG - Advice Letter Approved	1 day	Sun 5/2/21	Sun 5/2/21		
317		SCG - Implementation Plan	51 days	Mon 5/3/21	Mon 7/12/21		
318		SCG - Local Small/Medium Commercial Solicitation	641 days	Tue 9/4/18	Tue 2/16/21		
319		SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19		
320		SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19		
321		SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19		
322		SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




ID		Task Name	Duration	Start	Finish	2018 H1	H2
323		SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19		
324		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19		
325		SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19		
326		SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19		
327		SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19		
328		SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19		
329		SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19		
330		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
331		SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20		
332		SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20		
333		SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20		
334		SCG - Submit Advice Letter	59 days	Tue 9/1/20	Fri 11/20/20		
335		SCG - Advice Letter Approved	1 day	Fri 12/18/20	Fri 12/18/20		
336		SCG - Implementation Plan	43 days	Sat 12/19/20	Tue 2/16/21		
337		SCG - Local Small/Medium Public Solicitation	631 days	Tue 9/4/18	Tue 2/2/21		
338		SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19		
339		SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19		
340		SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19		
341		SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19		
342		SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19		
343		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19		
344		SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19		
345		SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
346		SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19		
347		SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19		
348		SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19		
349		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
350		SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20		
351		SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20		
352		SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20		
353		SCG - Submit Advice Letter	49 days	Tue 9/1/20	Fri 11/6/20		
354		SCG - Advice Letter Approved	1 day	Fri 12/4/20	Fri 12/4/20		
355		SCG - Implementation Plan	43 days	Sat 12/5/20	Tue 2/2/21		
356		SCG - Statewide POS Food Service Solicitation	605 days	Mon 1/21/19	Fri 5/14/21		
357		SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19		
358		SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19		
359		SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19		
360		SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19		
361		SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19		
362		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20		
363		SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19		
364		SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20		
365		SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20		
366		SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20		
367		SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20		
368		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
369		SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20		
370		SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20		
371		SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20		
372		SCG - Submit Advice Letter	32 days	Mon 11/2/20	Tue 12/15/20		
373		SCG - Advice Letter Approved	1 day	Thu 1/14/21	Thu 1/14/21		
374		SCG - Implementation Plan	42 days	Fri 1/15/21	Mon 3/15/21		
375		SCG - Statewide Midstream Water Heating Solicitation	597 days	Mon 1/21/19	Tue 5/4/21		
376		SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19		
377		SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19		
378		SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19		
379		SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19		
380		SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19		
381		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20		
382		SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19		
383		SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20		
384		SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20		
385		SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20		
386		SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20		
387		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20		
388		SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20		
389		SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20		
390		SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20		
391		SCG - Submit Advice Letter	25 days	Mon 11/2/20	Fri 12/4/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
392		SCG - Advice Letter Approved	1 day	Thu 3/18/21	Thu 3/18/21		
393		SCG - Implementation Plan	22 days	Fri 3/19/21	Mon 4/19/21		
394		SCG - Statewide Gas Emerging Technology Solicitation	738 days	Wed 1/2/19	Fri 10/29/21		
395		SCG - RFA Preparation	283 days	Wed 1/2/19	Fri 1/31/20		
396		SCG - RFA Release	1 day	Wed 2/12/20	Wed 2/12/20		
397		SCG - RFA Abstract Creation Duration	30 days	Thu 2/13/20	Wed 3/25/20		
398		SCG - RFA Evaluation	26 days	Thu 3/26/20	Thu 4/30/20		
399		SCG - RFA Review with EE PRG	1 day	Tue 5/5/20	Tue 5/5/20		
400		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 5/15/20	Fri 5/15/20		
401		SCG - RFP Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
402		SCG - RFP Release	1 day	Fri 8/21/20	Fri 8/21/20		
403		SCG - RFP Proposal Creation Duration	30 days	Mon 8/24/20	Fri 10/2/20		
404		SCG - RFP Evaluation	38 days	Mon 10/5/20	Wed 11/25/20		
405		SCG - RFP Review with EE PRG	1 day	Tue 12/1/20	Tue 12/1/20		
406		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 12/7/20	Mon 12/7/20		
407		SCG - Contract Negotiation and Development	85 days	Mon 1/4/21	Fri 4/30/21		
408		SCG - Contract Review with EE PRG	9 days	Tue 5/4/21	Fri 5/14/21		
409		SCG - Final Award and Contract Signed	29 days	Mon 5/17/21	Thu 6/24/21		
410		SCG - Submit Advice Letter	23 days	Sun 6/27/21	Tue 7/27/21		
411		SCG - Advice Letter Approved	1 day	Tue 8/24/21	Tue 8/24/21		
412		SCG - Implementation Plan	44 days	Wed 8/25/21	Sat 10/23/21		
413		SCG - Local Manufactured Housing Solicitation	341 days	Fri 11/1/19	Fri 2/19/21		
414		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
415		SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20		
416		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
417		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
418		SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20		
419		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20		
420		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
421		SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20		
422		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
423		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
424		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
425		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
426		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
427		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
428		SCG - Final Award and Contract Signed	9 days	Thu 12/10/20	Tue 12/22/20		
429		SCG - Submit Advice Letter	0 days	N/A	N/A		
430		SCG - Advice Letter Approved	0 days	N/A	N/A		
431		SCG - Implementation Plan	44 days	Tue 12/22/20	Fri 2/19/21		
432		SCG - Local Large Commercial Solicitation	434 days	Fri 11/1/19	Wed 6/30/21		
433		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		
434		SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20		
435		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
436		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
437		SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
438		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20		
439		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
440		SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20		
441		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
442		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
443		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
444		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
445		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
446		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
447		SCG - Final Award and Contract Signed	10 days	Thu 12/10/20	Wed 12/23/20		
448		SCG - Submit Advice Letter	64 days	Fri 1/1/21	Wed 3/31/21		
449		SCG - Advice Letter Approved	1 day	Fri 6/4/21	Fri 6/4/21		
450		SCG - Implementation Plan	43 days	Sat 6/5/21	Tue 8/3/21		
451		SCG - Local Agricultural Solicitation	434 days	Fri 11/1/19	Wed 6/30/21		
452		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		
453		SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20		
454		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
455		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
456		SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20		
457		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20		
458		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
459		SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20		
460		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
461		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
462		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
463		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
464		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
465		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
466		SCG - Final Award and Contract Signed	2 days	Fri 12/11/20	Mon 12/14/20		
467		SCG - Submit Advice Letter	41 days	Fri 1/1/21	Fri 2/26/21		
468		SCG - Advice Letter Approved	1 day	Wed 4/7/21	Wed 4/7/21		
469		SCG - Implementation Plan	43 days	Thu 4/8/21	Mon 6/7/21		
470		SCG - Local Behavioral Solicitation - Residential	413 days?	Fri 5/1/20	Tue 11/30/21		
471		SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
472		SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20		
473		SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20		
474		SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20		
475		SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20		
476		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20		
477		SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20		
478		SCG - RFP Release	1 day	Fri 1/15/21	Fri 1/15/21		
479		SCG - RFP Proposal Creation Duration	26 days	Mon 1/18/21	Mon 2/22/21		
480		SCG - RFP Evaluation	29 days	Tue 2/23/21	Fri 4/2/21		
481		SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21		
482		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/13/21	Tue 4/13/21		
483		SCG - Contract Negotiation and Development	95 days	Mon 4/26/21	Fri 9/3/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
484		SCG - Contract Review with EE PRG	9 days	Tue 9/7/21	Fri 9/17/21		
485		SCG - Final Award and Contract Signed	30 days	Mon 9/20/21	Fri 10/29/21		
486		SCG - Submit Advice Letter	21 days	Mon 11/1/21	Mon 11/29/21		
487		SCG - Advice Letter Approved	1 day	Wed 12/22/21	Wed 12/22/21		
488		SCG - Implementation Plan	43 days	Thu 12/23/21	Sun 2/20/22		
489		SCG - Local Behavioral Solicitation - Commercial	413 days?	Fri 5/1/20	Tue 11/30/21		
490		SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
491		SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20		
492		SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20		
493		SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20		
494		SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20		
495		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20		
496		SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20		
497		SCG - RFP Release	1 day	Fri 1/22/21	Fri 1/22/21		
498		SCG - RFP Proposal Creation Duration	26 days	Mon 1/25/21	Mon 3/1/21		
499		SCG - RFP Evaluation	24 days	Tue 3/2/21	Fri 4/2/21		
500		SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21		
501		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 11/12/21	Fri 11/12/21		
502		SCG - Contract Negotiation and Development	132 days	Mon 11/29/21	Tue 5/31/22		
503		SCG - Contract Review with EE PRG	8 days	Sun 6/5/22	Tue 6/14/22		
504		SCG - Final Award and Contract Signed	109 days	Fri 7/1/22	Wed 11/30/22		
505		SCG - Submit Advice Letter	23 days	N/A	N/A		
506		SCG - Advice Letter Approved	1 day	N/A	N/A		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
507		SCG - Implementation Plan	43 days	Thu 12/1/22	Sun 1/29/23		
508		SCG - Local Industrial Solicitation	434 days?	Tue 12/1/20	Fri 7/29/22		
509		SCG - RFA Preparation	63 days?	Tue 12/1/20	Thu 2/25/21		
510		SCG - RFA Release	1 day?	Fri 3/19/21	Fri 3/19/21		
511		SCG - RFA Abstract Creation Duration	25 days?	Mon 3/22/21	Fri 4/23/21		
512		SCG - RFA Evaluation	25 days?	Mon 4/26/21	Fri 5/28/21		
513		SCG - RFA Review with EE PRG	1 day?	Tue 6/1/21	Tue 6/1/21		
514		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 6/8/21	Tue 6/8/21		
515		SCG - RFP Preparation	67 days?	Thu 4/1/21	Fri 7/2/21		
516		SCG - RFP Release	1 day?	Fri 7/16/21	Fri 7/16/21		
517		SCG - RFP Proposal Creation Duration	30 days?	Mon 7/19/21	Fri 8/27/21		
518		SCG - RFP Evaluation	25 days?	Mon 8/30/21	Fri 10/1/21		
519		SCG - RFP Review with EE PRG	1 day?	Tue 10/5/21	Tue 10/5/21		
520		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 12/14/21	Tue 12/14/21		
521		SCG - Contract Negotiation and Development	127 days?	Thu 2/3/22	Fri 7/29/22		
522		SCG - Contract Review with EE PRG	9 days?	Tue 8/2/22	Fri 8/12/22		
523		SCG - Final Award and Contract Signed	21 days?	Fri 7/29/22	Fri 8/26/22		
524		SCG - Submit Advice Letter	1 day?	Sun 10/30/22	Sun 10/30/22		
525		SCG - Advice Letter Approved	1 day?	Mon 1/30/23	Mon 1/30/23		
526		SCG - Implementation Plan	45 days?	Tue 1/31/23	Sat 4/1/23		
527		SCG - Large Public Sector Solicitation (re-Bid)	412 days	Mon 1/4/21	Tue 8/2/22		
528		SCG - RFA Preparation	65 days	Mon 1/4/21	Fri 4/2/21		
529		SCG - RFA Release	1 day	Fri 7/16/21	Fri 7/16/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1	H2
530		SCG - RFA Abstract Creation Duration	20 days	Mon 7/19/21	Fri 8/13/21		
531		SCG - RFA Evaluation	15 days	Mon 8/16/21	Fri 9/3/21		
532		SCG - RFA Review with EE PRG	1 day	Tue 9/7/21	Tue 9/7/21		
533		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/14/21	Tue 9/14/21		
534		SCG - RFP Preparation	35 days	Mon 9/13/21	Fri 10/29/21		
535		SCG - RFP Release	1 day	Mon 11/8/21	Mon 11/8/21		
536		SCG - RFP Proposal Creation Duration	29 days	Tue 11/9/21	Fri 12/17/21		
537		SCG - RFP Evaluation	30 days	Mon 12/20/21	Fri 1/28/22		
538		SCG - RFP Review with EE PRG	1 day	Tue 2/1/22	Tue 2/1/22		
539		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/8/22	Tue 3/8/22		
540		SCG - Contract Negotiation and Development	79 days	Mon 3/14/22	Thu 6/30/22		
541		SCG - Contract Review with EE PRG	9 days	Tue 7/5/22	Fri 7/15/22		
542		SCG - Final Award and Contract Signed	63 days	Mon 7/18/22	Wed 10/12/22		
543		SCG - Submit Advice Letter	23 days	N/A	N/A		
544		SCG - Advice Letter Approved	1 day	N/A	N/A		
545		SCG - Implementation Plan	44 days	Wed 10/12/22	Sat 12/10/22		
546		SCG - Outreach Solicitation	434 days	Mon 2/1/21	Thu 9/29/22		
547		SCG - RFA Preparation	65 days	Mon 2/1/21	Fri 4/30/21		
548		SCG - RFA Release	1 day	Fri 5/21/21	Fri 5/21/21		
549		SCG - RFA Abstract Creation Duration	25 days	Mon 5/24/21	Fri 6/25/21		
550		SCG - RFA Evaluation	25 days	Mon 6/28/21	Fri 7/30/21		
551		SCG - RFA Review with EE PRG	1 day	Tue 8/3/21	Tue 8/3/21		
552		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/10/21	Tue 8/10/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1	H2
553		SCG - RFP Preparation	69 days	Tue 6/1/21	Fri 9/3/21		
554		SCG - RFP Release	1 day	Fri 9/17/21	Fri 9/17/21		
555		SCG - RFP Proposal Creation Duration	30 days	Mon 9/20/21	Fri 10/29/21		
556		SCG - RFP Evaluation	25 days	Mon 11/1/21	Fri 12/3/21		
557		SCG - RFP Review with EE PRG	1 day	Tue 12/7/21	Tue 12/7/21		
558		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 12/14/21	Tue 12/14/21		
559		SCG - Contract Negotiation and Development	54 days	Mon 1/17/22	Thu 3/31/22		
560		SCG - Contract Review with EE PRG	9 days	Tue 4/5/22	Fri 4/15/22		
561		SCG - Final Award and Contract Signed	10 days	Mon 4/18/22	Fri 4/29/22		
562		SCG - Submit Advice Letter	21 days	N/A	N/A		
563		SCG - Advice Letter Approved	1 day	N/A	N/A		
564		SCG - Implementation Plan	43 days	Sat 4/30/22	Tue 6/28/22		
565		SCG - Marketplace Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
566		SCG - RFA Preparation	64 days	Sat 5/1/21	Wed 7/28/21		
567		SCG - RFA Release	1 day	Fri 8/20/21	Fri 8/20/21		
568		SCG - RFA Abstract Creation Duration	25 days	Mon 8/23/21	Fri 9/24/21		
569		SCG - RFA Evaluation	25 days	Mon 9/27/21	Fri 10/29/21		
570		SCG - RFA Review with EE PRG	1 day	Tue 11/2/21	Tue 11/2/21		
571		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/9/21	Tue 11/9/21		
572		SCG - RFP Preparation	91 days	Thu 8/26/21	Thu 12/30/21		
573		SCG - RFP Release	1 day	Fri 1/14/22	Fri 1/14/22		
574		SCG - RFP Proposal Creation Duration	30 days	Mon 1/17/22	Fri 2/25/22		
575		SCG - RFP Evaluation	25 days	Mon 2/28/22	Fri 4/1/22		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




ID		Task Name	Duration	Start	Finish	2018 H1	H2
576		SCG - RFP Review with EE PRG	1 day	Tue 5/3/22	Tue 5/3/22		
577		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 5/11/22	Wed 5/11/22		
578		SCG - Contract Negotiation and Development	117 days	Wed 6/22/22	Thu 12/1/22		
579		SCG - Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22		
580		SCG - Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22		
581		SCG - Submit Advice Letter	20 days	Tue 1/3/23	Mon 1/30/23		
582		SCG - Advice Letter Approved	1 day	Tue 5/2/23	Tue 5/2/23		
583		SCG - Implementation Plan	44 days	Wed 5/3/23	Sun 7/2/23		
584		SCG - Residential Multi-Family - Whole Building	436 days?	Mon 3/1/21	Mon 10/31/22		
585		RFA Preparation	40 days	Mon 1/10/22	Fri 3/4/22		
586		RFA Release	1 day	Fri 3/25/22	Fri 3/25/22		
587		RFA Abstract Creation Duration	25 days	Mon 3/28/22	Fri 4/29/22		
588		RFA Evaluation	25 days	Mon 5/2/22	Fri 6/3/22		
589		RFA Review with EE PRG	1 day	Tue 6/7/22	Tue 6/7/22		
590		RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/14/22	Tue 6/14/22		
591		RFP Preparation	28 days	Sun 5/1/22	Tue 6/7/22		
592		RFP Release	1 day	Fri 6/24/22	Fri 6/24/22		
593		RFP Proposal Creation Duration	52 days	Mon 6/27/22	Tue 9/6/22		
594		RFP Evaluation	11 days	Fri 9/9/22	Fri 9/23/22		
595		RFP Review with EE PRG	1 day	Thu 10/6/22	Thu 10/6/22		
596		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/11/22	Tue 10/11/22		
597		Contract Negotiation and Development	39 days	Tue 10/11/22	Fri 12/2/22		
598		Contract Review with EE PRG	1 day	Tue 12/6/22	Tue 12/6/22		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
599		Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22		
600		Submit Advice Letter	22 days	Mon 1/2/23	Tue 1/31/23		
601		Advice Letter Approved	1 day	Fri 3/31/23	Fri 3/31/23		
602		Implementation Plan	43 days	Sat 4/1/23	Tue 5/30/23		
603		SCG – Youth Education Outreach Solicitation	331 days	Tue 3/1/22	Tue 6/6/23		
604		SCG - HERS Rater Training Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
605		RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22		
606		RFP Release	1 day	Fri 5/13/22	Fri 5/13/22		
607		RFP Proposal Creation Duration	20 days	Mon 5/16/22	Fri 6/10/22		
608		RFP Evaluation	59 days	Mon 6/13/22	Thu 9/1/22		
609		RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22		
610		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 8/31/22	Wed 8/31/22		
611		Contract Negotiation and Development	53 days	Fri 9/16/22	Tue 11/29/22		
612		Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22		
613		Final Award and Contract Signed	9 days	Mon 12/19/22	Thu 12/29/22		
614		Submit Advice Letter	N/A	N/A	N/A		
615		Advice Letter Approved	N/A	N/A	N/A		
616		Implementation Plan	42 days	Fri 12/30/22	Mon 2/27/23		
617		SCG - Retail Partnering Solicitation	29 days?	Tue 9/27/22	Fri 11/4/22		
618		RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22		
619		RFP Release	1 day	Fri 6/17/22	Fri 6/17/22		
620		RFP Proposal Creation Duration	30 days	Mon 6/20/22	Fri 7/29/22		
621		RFP Evaluation	24 days	Mon 8/1/22	Thu 9/1/22		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
622		RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22		
623		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/13/22	Tue 9/13/22		
624		Contract Negotiation and Development	29 days	Mon 9/19/22	Thu 10/27/22		
625		Contract Review with EE PRG	9 days	Tue 11/1/22	Fri 11/11/22		
626		Final Award and Contract Signed	13 days	Mon 11/14/22	Wed 11/30/22		
627		Submit Advice Letter	N/A	N/A	N/A		
628		Advice Letter Approved	N/A	N/A	N/A		
629		Implementation Plan	43 days	Sat 10/1/22	Tue 11/29/22		
630		SCG - Non-Residential EE Advisor Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
631		RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22		
632		RFP Release	1 day	Fri 8/26/22	Fri 8/26/22		
633		RFP Proposal Creation Duration	20 days	Mon 8/29/22	Fri 9/23/22		
634		RFP Evaluation	16 days	Sat 9/24/22	Fri 10/14/22		
635		RFP Review with EE PRG	5 days	Mon 10/17/22	Fri 10/21/22		
636		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/25/22	Tue 10/25/22		
637		Contract Negotiation and Development	32 days	Sun 10/30/22	Mon 12/12/22		
638		Contract Review with EE PRG	9 days	Tue 12/13/22	Fri 12/23/22		
639		Final Award and Contract Signed	4 days	Tue 12/27/22	Fri 12/30/22		
640		Submit Advice Letter	N/A	N/A	N/A		
641		Advice Letter Approved	N/A	N/A	N/A		
642		Implementation Plan	44 days	Sun 1/1/23	Wed 3/1/23		
643		SCG - Residential EE Kits Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
644		RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
645		RFP Release	1 day	Mon 7/25/22	Mon 7/25/22		
646		RFP Proposal Creation Duration	16 days	Tue 7/26/22	Tue 8/16/22		
647		RFP Evaluation	12 days	Wed 8/17/22	Thu 9/1/22		
648		RFP Review with EE PRG	1 day	Tue 8/2/22	Tue 8/2/22		
649		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/9/22	Tue 8/9/22		
650		Contract Negotiation and Development	30 days	Mon 8/22/22	Fri 9/30/22		
651		Contract Review with EE PRG	9 days	Tue 10/4/22	Fri 10/14/22		
652		Final Award and Contract Signed	10 days	Mon 10/17/22	Fri 10/28/22		
653		Submit Advice Letter	N/A	N/A	N/A		
654		Advice Letter Approved	N/A	N/A	N/A		
655		Implementation Plan	43 days	Sat 10/29/22	Tue 12/27/22		
656		SCG - IDEEA 365	230 days	Mon 2/13/23	Fri 12/29/23		
657		RFP Preparation	23 days	Mon 2/13/23	Wed 3/15/23		
658		RFP Release	20 days	Thu 4/20/23	Wed 5/17/23		
659		RFP Proposal Creation Duration	43 days	Wed 5/3/23	Fri 6/30/23		
660		RFP Evaluation	12 days	Fri 7/14/23	Mon 7/31/23		
661		RFP Review with EE PRG	1 day	Tue 8/1/23	Tue 8/1/23		
662		RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Tue 8/1/23	Thu 8/31/23		
663		Contract Negotiation and Development	21 days	Fri 9/1/23	Fri 9/29/23		
664		Contract Review with EE PRG	32 days	Mon 9/18/23	Tue 10/31/23		
665		Final Award and Contract Signed	17 days	Mon 10/9/23	Tue 10/31/23		
666		Submit Advice Letter	10 days	Wed 11/1/23	Tue 11/14/23		
667		Advice Letter Approved	11 days	Wed 11/22/23	Wed 12/6/23		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
668		Implementation Plan	9 days	Tue 12/19/23	Fri 12/29/23		
669		SCG - Commercial SEM	110 days?	Tue 8/1/23	Mon 1/1/24		
670		RFP Preparation	22 days	Tue 8/1/23	Wed 8/30/23		
671		RFP Release	13 days	Wed 9/13/23	Fri 9/29/23		
672		RFP Proposal Creation Duration	11 days	Mon 10/2/23	Mon 10/16/23		
673		RFP Evaluation	5 days	Wed 10/25/23	Tue 10/31/23		
674		RFP Review with EE PRG	2 days	Tue 10/31/23	Wed 11/1/23		
675		RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Thu 11/2/23	Wed 11/8/23		
676		Contract Negotiation and Development	16 days	Wed 10/25/23	Wed 11/15/23		
677		Contract Review with EE PRG	1 day	Tue 12/5/23	Tue 12/5/23		
678		Final Award and Contract Signed	6 days	Wed 12/13/23	Wed 12/20/23		
679		Submit Advice Letter	5 days	Mon 12/18/23	Fri 12/22/23		
680		Advice Letter Approved	1 day	Fri 12/29/23	Fri 12/29/23		
681		Implementation Plan	1 day	Mon 1/1/24	Mon 1/1/24		
682		SCG - Market Access Program	333 days?	Sat 3/16/24	Tue 6/24/25		
683		RFP Preparation	75 days	Sat 3/16/24	Thu 6/27/24		
684		RFP Release	1 day	Fri 6/21/24	Fri 6/21/24		
685		RFP Proposal Creation Duration	53 days	Mon 6/24/24	Wed 9/4/24		
686		RFP Evaluation	38 days	Mon 8/19/24	Wed 10/9/24		
687		RFP Review with EE PRG	1 day	Tue 10/1/24	Tue 10/1/24		
688		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/8/24	Tue 10/8/24		
689		Contract Negotiation and Development	78 days	Mon 10/14/24	Wed 1/29/25		
690		Contract Review with EE PRG	10 days	Tue 1/7/25	Mon 1/20/25		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
691		Final Award and Contract Signed	11 days	Mon 1/20/25	Mon 2/3/25		
692		Submit Advice Letter	N/A	Wed 1/1/25			
693		Advice Letter Approved	N/A	Mon 3/3/25			
694		Implementation Plan	59 days	Thu 4/3/25	Tue 6/24/25		
695		SCG - IDEEA 365 (Round 3)	230 days?	Tue 10/15/24	Mon 9/1/25		
696		RFP Preparation	23 days	Tue 10/15/24	Thu 11/14/24		
697		RFP Release	20 days	Fri 11/15/24	Thu 12/12/24		
698		RFP Proposal Creation Duration	43 days	Fri 12/13/24	Tue 2/11/25		
699		RFP Evaluation	12 days	Wed 2/12/25	Thu 2/27/25		
700		RFP Review with EE PRG	1 day	Fri 2/28/25	Fri 2/28/25		
701		RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Mon 3/3/25	Wed 4/2/25		
702		Contract Negotiation and Development	21 days	Thu 4/3/25	Thu 5/1/25		
703		Contract Review with EE PRG	32 days	Fri 5/2/25	Mon 6/16/25		
704		Final Award and Contract Signed	17 days	Tue 6/17/25	Wed 7/9/25		
705		Submit Advice Letter	10 days	Thu 7/10/25	Wed 7/23/25		
706		Advice Letter Approved	11 days	Thu 7/24/25	Thu 8/7/25		
707		Implementation Plan	9 days	Fri 8/8/25	Wed 8/20/25		
708							
709		<i>Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change</i>					
710		SDG&E - Small Commercial (<20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20		
711		SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18		
712		SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18		
713		SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
714		SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19		
715		SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19		
716		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19		
717		SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19		
718		SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19		
719		SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19		
720		SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19		
721		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20		
722		SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20		
723		SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20		
724		SDG&E - Contract Review with EE PRG	0 days	Tue 6/9/20	Tue 6/9/20		
725		SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20		
726		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
727		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
728		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
729		SDG&E - Large Commercial (>20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20		
730		SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18		
731		SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18		
732		SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18		
733		SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19		
734		SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19		
735		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19		
736		SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
737		SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19		
738		SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19		
739		SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19		
740		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20		
741		SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20		
742		SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20		
743		SDG&E - Contract Review with EE PRG	0 days	Tue 5/12/20	Tue 5/12/20		
744		SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20		
745		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
746		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
747		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
748		SDG&E - Residential Multi-Family Solicitation	586 days	Thu 9/6/18	Thu 12/3/20		
749		SDG&E - RFA Preparation	64 days	Thu 9/6/18	Tue 12/4/18		
750		SDG&E - RFA Release	23 days	Tue 12/4/18	Thu 1/3/19		
751		SDG&E - RFA Abstract Creation Duration	49 days	Tue 9/11/18	Fri 11/16/18		
752		SDG&E - RFA Evaluation	21 days	Mon 1/7/19	Mon 2/4/19		
753		SDG&E - RFA Review with EE PRG	0 days	Tue 11/13/18	Tue 11/13/18		
754		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 3/20/19	Wed 3/20/19		
755		SDG&E - RFP Preparation	63 days	Fri 3/22/19	Tue 6/18/19		
756		SDG&E - RFP Release	52 days	Tue 6/18/19	Wed 8/28/19		
757		SDG&E - RFP Proposal Creation Duration	36 days	Mon 3/25/19	Mon 5/13/19		
758		SDG&E - RFP Evaluation	30 days	Thu 8/29/19	Wed 10/9/19		
759		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Thu 12/12/19	Thu 12/19/19		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
760		SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
761		SDG&E - Contract Negotiation and Development	35 days	Mon 4/13/20	Fri 5/29/20		
762		SDG&E - Contract Review with EE PRG	10 days	Thu 6/4/20	Wed 6/17/20		
763		SDG&E - Final Award and Contract Signed	0 days	Mon 6/22/20	Mon 6/22/20		
764		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
765		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
766		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
767		SDG&E - SW HVAC Solicitation	593 days	Thu 11/1/18	Tue 2/9/21		
768		SDG&E - RFA Preparation	48 days	Thu 11/1/18	Mon 1/7/19		
769		SDG&E - RFA Release	0 days	Mon 1/7/19	Mon 1/7/19		
770		SDG&E - RFA Abstract Creation Duration	24 days	Mon 1/7/19	Thu 2/7/19		
771		SDG&E - RFA Evaluation	37 days	Fri 2/8/19	Sun 3/31/19		
772		SDG&E - RFA Review with EE PRG	0 days	Tue 4/9/19	Tue 4/9/19		
773		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 4/17/19	Wed 4/17/19		
774		SDG&E - RFP Preparation	73 days	Thu 4/18/19	Mon 7/29/19		
775		SDG&E - RFP Release	0 days	Tue 9/3/19	Tue 9/3/19		
776		SDG&E - RFP Proposal Creation Duration	30 days	Tue 9/3/19	Mon 10/14/19		
777		SDG&E - RFP Evaluation	33 days	Mon 10/14/19	Wed 11/27/19		
778		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20		
779		SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
780		SDG&E - Contract Negotiation and Development	88 days	Wed 3/25/20	Fri 7/24/20		
781		SDG&E - Contract Review with EE PRG	0 days	Tue 9/8/20	Tue 9/8/20		
782		SDG&E - Final Award and Contract Signed	0 days	Fri 10/30/20	Fri 10/30/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
783		SDG&E - Submit Advice Letter	0 days	Thu 11/12/20	Thu 11/12/20		
784		SDG&E - Advice Letter Approved	0 days	Fri 12/11/20	Fri 12/11/20		
785		SDG&E - Implementation Plan	0 days	Tue 2/9/21	Tue 2/9/21		
786		SDG&E - SW PLA Solicitation	853 days	Mon 1/28/19	Wed 5/4/22		
787		SDG&E - RFA Preparation	75 days	Mon 1/28/19	Fri 5/10/19		
788		SDG&E - RFA Release	0 days	Fri 5/10/19	Fri 5/10/19		
789		SDG&E - RFA Abstract Creation Duration	31 days	Fri 5/10/19	Fri 6/21/19		
790		SDG&E - RFA Evaluation	65 days	Mon 6/24/19	Fri 9/20/19		
791		SDG&E - RFA Review with EE PRG	0 days	Tue 9/10/19	Tue 9/10/19		
792		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 9/20/19	Fri 9/20/19		
793		SDG&E - RFP Preparation	52 days	Fri 9/20/19	Mon 12/2/19		
794		SDG&E - RFP Release	0 days	Mon 1/27/20	Mon 1/27/20		
795		SDG&E - RFP Proposal Creation Duration	31 days	Mon 1/27/20	Mon 3/9/20		
796		SDG&E - RFP Evaluation	82 days	Mon 3/9/20	Tue 6/30/20		
797		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/17/20	Mon 8/17/20		
798		SDG&E - Selection Review with EE PRG	66 days	Tue 10/13/20	Tue 1/12/21		
799		SDG&E - Contract Negotiation and Development	197 days	Fri 1/29/21	Mon 11/1/21		
800		SDG&E - Contract Review with EE PRG	0 days	Tue 11/9/21	Tue 11/9/21		
801		SDG&E - Final Award and Contract Signed	0 days	Fri 1/7/22	Fri 1/7/22		
802		SDG&E - Submit Advice Letter	0 days	Mon 1/10/22	Mon 1/10/22		
803		SDG&E - Advice Letter Approved	0 days	Thu 2/10/22	Thu 2/10/22		
804		SDG&E - Implementation Plan	60 days	Thu 2/10/22	Wed 5/4/22		
805		SDG&E - Residential Single-Family 2.0 Solicitation	467 days	Tue 1/19/21	Wed 11/2/22		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
806		SDG&E - RFA Preparation	43 days	Tue 1/19/21	Thu 3/18/21		
807		SDG&E - RFA Release	0 days	Mon 3/22/21	Mon 3/22/21		
808		SDG&E - RFA Abstract Creation Duration	22 days	Mon 3/22/21	Tue 4/20/21		
809		SDG&E - RFA Evaluation	38 days	Wed 4/21/21	Fri 6/11/21		
810		SDG&E - RFA Review with EE PRG	7 days	Thu 6/3/21	Fri 6/11/21		
811		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 6/15/21	Tue 6/15/21		
812		SDG&E - RFP Preparation	43 days	Wed 6/16/21	Fri 8/13/21		
813		SDG&E - RFP Release	0 days	Wed 8/18/21	Wed 8/18/21		
814		SDG&E - RFP Proposal Creation Duration	32 days	Wed 8/18/21	Thu 9/30/21		
815		SDG&E - RFP Evaluation	44 days	Fri 10/1/21	Wed 12/1/21		
816		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 12/14/21	Tue 12/14/21		
817		SDG&E - Selection Review with EE PRG	7 days	Thu 12/2/21	Fri 12/10/21		
818		SDG&E - Contract Negotiation and Development	96 days	Mon 12/20/21	Mon 5/2/22		
819		SDG&E - Contract Review with EE PRG	7 days	Thu 5/5/22	Fri 5/13/22		
820		SDG&E - Final Award and Contract Signed	0 days	Tue 5/31/22	Tue 5/31/22		
821		SDG&E - Submit Advice Letter	0 days	Fri 6/24/22	Fri 6/24/22		
822		SDG&E - Advice Letter Approved	0 days	Thu 8/11/22	Thu 8/11/22		
823		SDG&E - Implementation Plan	60 days	Thu 8/11/22	Wed 11/2/22		
824		SDG&E - Residential Single-Family Solicitation	501 days	Mon 7/1/19	Tue 6/1/21		
825		SDG&E - RFA Preparation	80 days	Mon 7/1/19	Fri 10/18/19		
826		SDG&E - RFA Release	35 days	Fri 10/18/19	Thu 12/5/19		
827		SDG&E - RFA Abstract Creation Duration	53 days	Mon 7/22/19	Wed 10/2/19		
828		SDG&E - RFA Evaluation	29 days	Fri 12/6/19	Wed 1/15/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
829		SDG&E - RFA Review with EE PRG	0 days	Tue 10/8/19	Tue 10/8/19		
830		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 2/27/20	Thu 2/27/20		
831		SDG&E - RFP Preparation	48 days	Fri 2/28/20	Tue 5/5/20		
832		SDG&E - RFP Release	0 days	Mon 4/27/20	Mon 4/27/20		
833		SDG&E - RFP Proposal Creation Duration	32 days	Mon 4/27/20	Tue 6/9/20		
834		SDG&E - RFP Evaluation	16 days	Wed 6/10/20	Wed 7/1/20		
835		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 7/23/20	Fri 7/24/20		
836		SDG&E - Selection Review with EE PRG	7 days	Thu 8/6/20	Fri 8/14/20		
837		SDG&E - Contract Negotiation and Development	60 days	Mon 8/17/20	Fri 11/6/20		
838		SDG&E - Contract Review with EE PRG	10 days	Tue 12/8/20	Mon 12/21/20		
839		SDG&E - Final Award and Contract Signed	0 days	Fri 1/29/21	Fri 1/29/21		
840		SDG&E - Submit Advice Letter	0 days	Mon 3/1/21	Mon 3/1/21		
841		SDG&E - Advice Letter Approved					
842		SDG&E - Implementation Plan	0 days	Tue 6/1/21	Tue 6/1/21		
843		SDG&E - Public Sector: Federal Solicitation	625 days	Mon 7/1/19	Fri 11/19/21		
844		SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19		
845		SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19		
846		SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19		
847		SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20		
848		SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
849		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20		
850		SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20		
851		SDG&E - RFP Release	0 days	Fri 5/22/20	Fri 5/22/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
852		SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20		
853		SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20		
854		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20		
855		SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20		
856		SDG&E - Contract Negotiation and Development	53 days	Wed 2/17/21	Fri 4/30/21		
857		SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21		
858		SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21		
859		SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21		
860		SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21		
861		SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21		
862		SDG&E - Public Sector: K-12 Solicitation	625 days	Mon 7/1/19	Fri 11/19/21		
863		SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19		
864		SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19		
865		SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19		
866		SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20		
867		SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
868		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20		
869		SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20		
870		SDG&E - RFP Release	1 day	Fri 5/22/20	Fri 5/22/20		
871		SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20		
872		SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20		
873		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20		
874		SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
875		SDG&E - Contract Negotiation and Development	117 days	Thu 11/19/20	Fri 4/30/21		
876		SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21		
877		SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21		
878		SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21		
879		SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21		
880		SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21		
881		SDG&E - Public Sector: Local Government Solicitation	338 days	Tue 10/13/20	Thu 1/27/22		
882		SDG&E - RFA Preparation	10 days	Fri 10/23/20	Thu 11/5/20		
883		SDG&E - RFA Release	1 day	Wed 1/27/21	Wed 1/27/21		
884		SDG&E - RFA Abstract Creation Duration	20 days	Thu 1/28/21	Wed 2/24/21		
885		SDG&E - RFA Evaluation	18 days	Fri 2/26/21	Tue 3/23/21		
886		SDG&E - RFA Review with EE PRG	7 days	Thu 4/8/21	Fri 4/16/21		
887		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/21/21	Wed 4/21/21		
888		SDG&E - RFP Preparation	51 days	Fri 3/19/21	Fri 5/28/21		
889		SDG&E - RFP Release	1 day	Tue 6/1/21	Tue 6/1/21		
890		SDG&E - RFP Proposal Creation Duration	26 days	Wed 6/2/21	Wed 7/7/21		
891		SDG&E - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21		
892		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/25/21	Mon 10/25/21		
893		SDG&E - Selection Review with EE PRG	7 days	Tue 10/12/21	Wed 10/20/21		
894		SDG&E - Contract Negotiation and Development	41 days	Fri 11/5/21	Fri 12/31/21		
895		SDG&E - Contract Review with EE PRG	7 days	Thu 1/6/22	Fri 1/14/22		
896		SDG&E - Final Award and Contract Signed	9 days	Mon 1/17/22	Thu 1/27/22		
897		SDG&E - Submit Advice Letter	13 days	Wed 6/1/22	Fri 6/17/22		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
898		SDG&E - Advice Letter Approved	40 days	Fri 6/17/22	Thu 8/11/22		
899		SDG&E - Implementation Plan	42 days	Mon 8/15/22	Tue 10/11/22		
900		SDG&E - Agricultural Sector: Local Agriculture Solicitation	447 days	Mon 3/1/21	Tue 11/15/22		
901		SDG&E - RFA Preparation	56 days	Mon 3/1/21	Mon 5/17/21		
902		SDG&E - RFA Release	0 days	Mon 4/26/21	Mon 4/26/21		
903		SDG&E - RFA Abstract Creation Duration	20 days	Tue 4/27/21	Mon 5/24/21		
904		SDG&E - RFA Evaluation	36 days	Tue 6/1/21	Tue 7/20/21		
905		SDG&E - RFA Review with EE PRG	0 days	Thu 7/8/21	Thu 7/8/21		
906		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 7/20/21	Tue 7/20/21		
907		SDG&E - RFP Preparation	48 days	Tue 7/20/21	Thu 9/23/21		
908		SDG&E - RFP Release	0 days	Thu 9/23/21	Thu 9/23/21		
909		SDG&E - RFP Proposal Creation Duration	25 days	Fri 9/24/21	Thu 10/28/21		
910		SDG&E - RFP Evaluation	23 days	Thu 10/28/21	Mon 11/29/21		
911		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 2/1/22	Tue 2/1/22		
912		SDG&E - Selection Review with EE PRG	0 days	Tue 2/8/22	Tue 2/8/22		
913		SDG&E - Contract Negotiation and Development	83 days	Tue 2/1/22	Thu 5/26/22		
914		SDG&E - Contract Review with EE PRG	0 days	Tue 6/14/22	Tue 6/14/22		
915		SDG&E - Final Award and Contract Signed	10 days	Fri 6/18/21	Thu 7/1/21		
916		SDG&E - Submit Advice Letter	0 days	Fri 7/22/22	Fri 7/22/22		
917		SDG&E - Advice Letter Approved	0 days	Tue 8/30/22	Tue 8/30/22		
918		SDG&E - Implementation Plan	44 days	Wed 8/31/22	Sat 10/29/22		
919		*SDG&E - Industrial Solicitation	426 days	Thu 4/1/21	Thu 11/17/22		
920		SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
921		SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21		
922		SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21		
923		SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21		
924		SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21		
925		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21		
926		SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21		
927		SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21		
928		SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22		
929		SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22		
930		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22		
931		SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22		
932		SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22		
933		SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22		
934		SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22		
935		SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22		
936		SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22		
937		SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23		
938		*SDG&E - Industrial-Port Tenants Solicitation	426 days	Thu 4/1/21	Thu 11/17/22		
939		SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21		
940		SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21		
941		SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21		
942		SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21		
943		SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
944		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21		
945		SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21		
946		SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21		
947		SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22		
948		SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22		
949		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22		
950		SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22		
951		SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22		
952		SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22		
953		SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22		
954		SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22		
955		SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22		
956		SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23		
957		*SDG&E - SW Residential HVAC QI/QM Solicitation	377 days	Mon 7/5/21	Tue 12/13/22		
958		SDG&E - RFA Preparation	48 days	Mon 7/5/21	Wed 9/8/21		
959		SDG&E - RFA Release	1 day	Wed 9/29/21	Wed 9/29/21		
960		SDG&E - RFA Abstract Creation Duration	22 days	Wed 9/29/21	Thu 10/28/21		
961		SDG&E - RFA Evaluation	21 days	Fri 10/29/21	Fri 11/26/21		
962		SDG&E - RFA Review with EE PRG	6 days	Fri 12/10/21	Fri 12/17/21		
963		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 12/22/21	Wed 12/22/21		
964		SDG&E - RFP Preparation	56 days	Tue 1/4/22	Tue 3/22/22		
965		SDG&E - RFP Release	1 day	Tue 3/22/22	Tue 3/22/22		
966		SDG&E - RFP Proposal Creation Duration	23 days	Wed 3/23/22	Fri 4/22/22		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
967		SDG&E - RFP Evaluation	20 days	Mon 4/25/22	Fri 5/20/22		
968		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/21/22	Tue 6/21/22		
969		SDG&E - Selection Review with EE PRG	0 days	Fri 6/17/22	Fri 6/17/22		
970		SDG&E - Contract Negotiation and Development	83 days	Wed 7/20/22	Fri 11/11/22		
971		SDG&E - Contract Review with EE PRG	6 days	Mon 11/14/22	Mon 11/21/22		
972		SDG&E - Final Award and Contract Signed	1 day	Mon 1/10/22	Mon 1/10/22		
973		SDG&E - Submit Advice Letter	22 days	Sun 1/15/23	Mon 2/13/23		
974		SDG&E - Advice Letter Approved	1 day	Fri 4/28/23	Fri 4/28/23		
975		SDG&E - Implementation Plan	60 days	Fri 4/28/23	Thu 7/20/23		
976		*SDG&E - Local/Residential Behavioral Solicitation	472 days	Mon 4/19/21	Tue 2/7/23		
977		SDG&E - RFA Preparation	53 days	Mon 4/19/21	Wed 6/30/21		
978		SDG&E - RFA Release	1 day	Mon 7/26/21	Mon 7/26/21		
979		SDG&E - RFA Abstract Creation Duration	21 days	Mon 7/26/21	Mon 8/23/21		
980		SDG&E - RFA Evaluation	30 days	Tue 8/24/21	Mon 10/4/21		
981		SDG&E - RFA Review with EE PRG	7 days	Thu 10/7/21	Fri 10/15/21		
982		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/19/21	Tue 10/19/21		
983		SDG&E - RFP Preparation	28 days	Thu 10/21/21	Mon 11/29/21		
984		SDG&E - RFP Release	1 day	Wed 12/22/21	Wed 12/22/21		
985		SDG&E - RFP Proposal Creation Duration	20 days	Wed 12/22/21	Tue 1/18/22		
986		SDG&E - RFP Evaluation	28 days	Wed 1/19/22	Fri 2/25/22		
987		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/15/22	Tue 3/15/22		
988		SDG&E - Selection Review with EE PRG	7 days	Thu 3/3/22	Fri 3/11/22		
989		SDG&E - Contract Negotiation and Development	119 days	Fri 3/18/22	Wed 8/31/22		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
990		SDG&E - Contract Review with EE PRG	7 days	Thu 9/8/22	Fri 9/16/22		
991		SDG&E - Final Award and Contract Signed	1 day	Fri 10/21/22	Fri 10/21/22		
992		SDG&E - Submit Advice Letter	1 day	Wed 11/16/22	Wed 11/16/22		
993		SDG&E - Advice Letter Approved	1 day	Fri 12/16/22	Fri 12/16/22		
994		SDG&E - Implementation Plan	60 days	Wed 11/16/22	Tue 2/7/23		
995		*SDG&E - Small Business Outreach Solicitation	298 days?	Wed 4/13/22	Fri 6/2/23		
996		SDG&E - RFA Preparation	53 days	Wed 4/13/22	Fri 6/24/22		
997		SDG&E - RFA Release	1 day	Thu 7/7/22	Thu 7/7/22		
998		SDG&E - RFA Abstract Creation Duration	21 days	Fri 7/8/22	Fri 8/5/22		
999		SDG&E - RFA Evaluation	30 days	Mon 8/8/22	Fri 9/16/22		
1000		SDG&E - RFA Review with EE PRG	5 days	Mon 9/19/22	Fri 9/23/22		
1001		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/27/22	Tue 9/27/22		
1002		SDG&E - RFP Preparation	28 days	Mon 8/8/22	Wed 9/14/22		
1003		SDG&E - RFP Release	1 day	Tue 10/18/22	Tue 10/18/22		
1004		SDG&E - RFP Proposal Creation Duration	31 days	Tue 10/18/22	Tue 11/29/22		
1005		SDG&E - RFP Evaluation	38 days	Wed 11/30/22	Fri 1/20/23		
1006		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/28/23	Tue 2/28/23		
1007		SDG&E - Selection Review with EE PRG	7 days	Thu 2/16/23	Fri 2/24/23		
1008		SDG&E - Contract Negotiation and Development	79 days	Tue 2/28/23	Fri 6/16/23		
1009		SDG&E - Contract Review with EE PRG	4 days	Wed 6/21/23	Mon 6/26/23		
1010		SDG&E - Final Award and Contract Signed	1 day	Tue 8/29/23	Tue 8/29/23		
1011		SDG&E - Submit Advice Letter	1 day	Fri 9/15/23	Fri 9/15/23		
1012		SDG&E - Advice Letter Approved	1 day	Mon 10/16/23	Mon 10/16/23		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1013		SDG&E - Implementation Plan	46 days	Mon 10/16/23	Mon 12/18/23		
1014		*SDG&E - Workforce Education & Training /Integrated Energy Education Solicitatio	353 days?	Mon 1/16/23	Wed 5/22/24		
1015		SDG&E - RFP Release	1 day?	Thu 2/2/23	Thu 2/2/23		
1016		SDG&E - RFP Evaluation	25 days	Fri 3/17/23	Thu 4/20/23		
1017		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/16/23	Tue 5/16/23		
1018		SDG&E - Selection Review with EE PRG	5 days	Tue 5/9/23	Mon 5/15/23		
1019		SDG&E - Contract Negotiation and Development	94 days	Fri 5/5/23	Wed 9/13/23		
1020		SDG&E - Contract Review with EE PRG	7 days	Tue 10/10/23	Wed 10/18/23		
1021		SDG&E - Final Award and Contract Signed	1 day	Tue 11/14/23	Tue 11/14/23		
1022		SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24		
1023		SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24		
1024		SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24		
1025		*SDG&E - Residential Equity Education & Outreach Solicitation	331 days?	Fri 1/13/23	Fri 4/19/24		
1026		SDG&E - RFA Release	1 day	Thu 3/2/23	Thu 3/2/23		
1027		SDG&E - RFA Evaluation	21 days	Wed 4/12/23	Wed 5/10/23		
1028		SDG&E - RFA Review with EE PRG	7 days	Fri 5/19/23	Mon 5/29/23		
1029		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/30/23	Tue 5/30/23		
1030		SDG&E - RFP Release	1 day	Thu 6/1/23	Thu 6/1/23		
1031		SDG&E - RFP Evaluation	27 days	Mon 7/17/23	Tue 8/22/23		
1032		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/28/23	Mon 8/28/23		
1033		SDG&E - Selection Review with EE PRG	7 days	Wed 8/30/23	Thu 9/7/23		
1034		SDG&E - Contract Negotiation and Development	32 days	Thu 11/2/23	Fri 12/15/23		
1035		SDG&E - Contract Review with EE PRG	7 days	Tue 1/9/24	Wed 1/17/24		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1036		SDG&E - Final Award and Contract Signed	1 day	Mon 2/12/24	Mon 2/12/24		
1037		SDG&E - Submit Advice Letter	1 day	Mon 2/26/24	Mon 2/26/24		
1038		SDG&E - Advice Letter Approved	1 day	Mon 4/8/24	Mon 4/8/24		
1039		SDG&E - Implementation Plan	60 days	Tue 4/9/24	Mon 7/1/24		
1040		*SDG&E - Non-Residential Behavioral Solicitation	398 days	Mon 8/15/22	Wed 2/21/24		
1041		SDG&E - RFA Preparation	67 days	Mon 8/15/22	Tue 11/15/22		
1042		SDG&E - RFA Release	1 day	Mon 10/24/22	Mon 10/24/22		
1043		SDG&E - RFA Abstract Creation Duration	27 days	Tue 8/23/22	Wed 9/28/22		
1044		SDG&E - RFA Evaluation	16 days	Tue 11/29/22	Tue 12/20/22		
1045		SDG&E - RFA Review with EE PRG	7 days	Thu 1/5/23	Fri 1/13/23		
1046		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 1/18/23	Wed 1/18/23		
1047		SDG&E - RFP Preparation	26 days	Mon 11/14/22	Mon 12/19/22		
1048		SDG&E - RFP Release	1 day	Mon 1/23/23	Mon 1/23/23		
1049		SDG&E - RFP Proposal Creation Duration	26 days	Mon 1/23/23	Mon 2/27/23		
1050		SDG&E - RFP Evaluation	58 days	Tue 2/28/23	Thu 5/18/23		
1051		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/20/23	Tue 6/20/23		
1052		SDG&E - Selection Review with EE PRG	7 days	Thu 6/8/23	Fri 6/16/23		
1053		SDG&E - Contract Negotiation and Development	60 days	Wed 6/21/23	Tue 9/12/23		
1054		SDG&E - Contract Review with EE PRG	7 days	Thu 10/5/23	Fri 10/13/23		
1055		SDG&E - Final Award and Contract Signed	1 day	Thu 12/21/23	Thu 12/21/23		
1056		SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24		
1057		SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24		
1058		SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1059		*SDG&E - Retail Offices and Wholesale Solicitation	419 days	Wed 5/10/23	Mon 12/16/24		
1060		SDG&E - RFA Preparation	33 days	Wed 5/10/23	Fri 6/23/23		
1061		SDG&E - RFA Release	1 day	Mon 7/3/23	Mon 7/3/23		
1062		SDG&E - RFA Abstract Creation Duration	31 days	Tue 7/4/23	Tue 8/15/23		
1063		SDG&E - RFA Evaluation	19 days	Wed 8/16/23	Mon 9/11/23		
1064		SDG&E - RFA Review with EE PRG	3 days	Mon 9/18/23	Wed 9/20/23		
1065		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 9/25/23	Mon 9/25/23		
1066		SDG&E - RFP Preparation	33 days	Wed 7/5/23	Fri 8/18/23		
1067		SDG&E - RFP Release	1 day	Fri 9/29/23	Fri 9/29/23		
1068		SDG&E - RFP Proposal Creation Duration	33 days	Mon 10/2/23	Wed 11/15/23		
1069		SDG&E - RFP Evaluation	25 days	Thu 11/16/23	Wed 12/20/23		
1070		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 2/19/24	Mon 2/19/24		
1071		SDG&E - Selection Review with EE PRG	7 days	Thu 2/8/24	Fri 2/16/24		
1072		SDG&E - Contract Negotiation and Development	96 days	Mon 2/26/24	Mon 7/8/24		
1073		SDG&E - Contract Review with EE PRG	6 days	Wed 7/17/24	Wed 7/24/24		
1074		SDG&E - Final Award and Contract Signed	1 day	Tue 8/27/24	Tue 8/27/24		
1075		SDG&E - Submit Advice Letter	1 day	Mon 9/16/24	Mon 9/16/24		
1076		SDG&E - Advice Letter Approved	1 day	Wed 10/16/24	Wed 10/16/24		
1077		SDG&E - Implementation Plan	44 days	Wed 10/16/24	Mon 12/16/24		
1078		*SDG&E - Groceries, Restaurants and Food Storage Solicitation	467 days	Wed 6/14/23	Thu 3/27/25		
1079		SDG&E - RFA Preparation	33 days	Wed 6/14/23	Fri 7/28/23		
1080		SDG&E - RFA Release	1 day	Tue 8/15/23	Tue 8/15/23		
1081		SDG&E - RFA Abstract Creation Duration	21 days	Wed 8/16/23	Wed 9/13/23		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1082		SDG&E - RFA Evaluation	15 days	Thu 9/14/23	Wed 10/4/23		
1083		SDG&E - RFA Review with EE PRG	5 days	Wed 10/18/23	Tue 10/24/23		
1084		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/30/23	Mon 10/30/23		
1085		SDG&E - RFP Preparation	16 days	Mon 10/9/23	Mon 10/30/23		
1086		SDG&E - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23		
1087		SDG&E - RFP Proposal Creation Duration	40 days	Mon 11/6/23	Fri 12/29/23		
1088		SDG&E - RFP Evaluation	34 days	Fri 12/29/23	Wed 2/14/24		
1089		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 3/6/24	Wed 3/6/24		
1090		SDG&E - Selection Review with EE PRG	7 days	Thu 2/29/24	Fri 3/8/24		
1091		SDG&E - Contract Negotiation and Development	144 days	Wed 3/13/24	Mon 9/30/24		
1092		SDG&E - Contract Review with EE PRG	6 days	Tue 10/8/24	Tue 10/15/24		
1093		SDG&E - Final Award and Contract Signed	1 day	Tue 11/26/24	Tue 11/26/24		
1094		SDG&E - Submit Advice Letter	1 day	Fri 12/27/24	Fri 12/27/24		
1095		SDG&E - Advice Letter Approved	1 day	Mon 1/27/25	Mon 1/27/25		
1096		SDG&E - Implementation Plan	44 days	Mon 1/27/25	Thu 3/27/25		
1097		*SDG&E - Private Institutions and Healthcare Solicitation	399 days	Thu 10/5/23	Tue 4/15/25		
1098		SDG&E - RFA Preparation	33 days	Thu 10/5/23	Mon 11/20/23		
1099		SDG&E - RFA Release	1 day	Mon 11/27/23	Mon 11/27/23		
1100		SDG&E - RFA Abstract Creation Duration	35 days	Mon 11/27/23	Fri 1/12/24		
1101		SDG&E - RFA Evaluation	30 days	Mon 1/15/24	Fri 2/23/24		
1102		SDG&E - RFA Review with EE PRG	5 days	Mon 2/26/24	Fri 3/1/24		
1103		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 3/4/24	Mon 3/4/24		
1104		SDG&E - RFP Preparation	54 days	Mon 11/27/23	Thu 2/8/24		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1105		SDG&E - RFP Release	1 day	Fri 3/8/24	Fri 3/8/24		
1106		SDG&E - RFP Proposal Creation Duration	34 days	Fri 3/8/24	Wed 4/24/24		
1107		SDG&E - RFP Evaluation	42 days	Thu 4/25/24	Fri 6/21/24		
1108		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 7/2/24	Tue 7/2/24		
1109		SDG&E - Selection Review with EE PRG	7 days	Fri 6/21/24	Mon 7/1/24		
1110		SDG&E - Contract Negotiation and Development	61 days	Wed 7/31/24	Wed 10/23/24		
1111		SDG&E - Contract Review with EE PRG	4 days	Tue 11/12/24	Fri 11/15/24		
1112		SDG&E - Final Award and Contract Signed	1 day	Tue 12/17/24	Tue 12/17/24		
1113		SDG&E - Submit Advice Letter	1 day	Wed 1/15/25	Wed 1/15/25		
1114		SDG&E - Advice Letter Approved	1 day	Fri 2/14/25	Fri 2/14/25		
1115		SDG&E - Implementation Plan	43 days	Fri 2/14/25	Tue 4/15/25		
1116		*SDG&E - Lodging: Hotels/Motels Solicitation	400 days	Tue 10/10/23	Mon 4/21/25		
1117		SDG&E - RFA Preparation	33 days	Tue 10/10/23	Thu 11/23/23		
1118		SDG&E - RFA Release	1 day	Fri 12/8/23	Fri 12/8/23		
1119		SDG&E - RFA Abstract Creation Duration	35 days	Fri 12/8/23	Thu 1/25/24		
1120		SDG&E - RFA Evaluation	22 days	Mon 1/22/24	Tue 2/20/24		
1121		SDG&E - RFA Review with EE PRG	7 days	Tue 3/12/24	Wed 3/20/24		
1122		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/19/24	Tue 3/19/24		
1123		SDG&E - RFP Preparation	48 days	Tue 1/23/24	Thu 3/28/24		
1124		SDG&E - RFP Release	1 day	Thu 3/21/24	Thu 3/21/24		
1125		SDG&E - RFP Proposal Creation Duration	29 days	Thu 3/21/24	Tue 4/30/24		
1126		SDG&E - RFP Evaluation	23 days	Mon 5/6/24	Wed 6/5/24		
1127		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/18/24	Tue 6/18/24		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1128		SDG&E - Selection Review with EE PRG	7 days	Thu 6/20/24	Fri 6/28/24		
1129		SDG&E - Contract Negotiation and Development	61 days	Wed 7/31/24	Wed 10/23/24		
1130		SDG&E - Contract Review with EE PRG	4 days	Tue 11/12/24	Fri 11/15/24		
1131		SDG&E - Final Award and Contract Signed	1 day	Tue 12/17/24	Tue 12/17/24		
1132		SDG&E - Submit Advice Letter	1 day	Thu 1/16/25	Thu 1/16/25		
1133		SDG&E - Advice Letter Approved	1 day	Thu 2/20/25	Thu 2/20/25		
1134		SDG&E - Implementation Plan	43 days	Thu 2/20/25	Mon 4/21/25		
1135		*SDG&E - Market Access Program (MAP)	326 days	Wed 3/13/24	Wed 6/11/25		
1136		SDG&E - RFP Preparation	38 days	Wed 3/13/24	Fri 5/3/24		
1137		SDG&E - RFP Release	1 day	Tue 5/7/24	Tue 5/7/24		
1138		SDG&E - RFP Proposal Creation Duration	31 days	Tue 5/7/24	Tue 6/18/24		
1139		SDG&E - RFP Evaluation	43 days	Wed 6/19/24	Fri 8/16/24		
1140		SDG&E - Selection Review with EE PRG	7 days	Thu 9/5/24	Fri 9/13/24		
1141		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/17/24	Tue 9/17/24		
1142		SDG&E - Contract Negotiation and Development	60 days	Fri 9/27/24	Thu 12/19/24		
1143		SDG&E - Contract Review with EE PRG	3 days	Tue 12/10/24	Thu 12/12/24		
1144		SDG&E - Final Award and Contract Signed	1 day	Fri 1/31/25	Fri 1/31/25		
1145		SDG&E - Submit Advice Letter	1 day	Wed 3/12/25	Wed 3/12/25		
1146		SDG&E - Advice Letter Approved	1 day	Fri 4/11/25	Fri 4/11/25		
1147		SDG&E - Implementation Plan	44 days	Fri 4/11/25	Wed 6/11/25		
1148		Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change					
1149							
1150		PG&E - Local Government Partnerships (non-resource programs) Solicitation	376 days?	Fri 3/22/19	Fri 8/28/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1151		PG&E - RFA Preparation	42 days	Fri 3/22/19	Mon 5/20/19		
1152		PG&E - RFA Release	1 day	Thu 5/23/19	Thu 5/23/19		
1153		PG&E - RFA Abstract Creation Duration	22 days	Thu 5/23/19	Fri 6/21/19		
1154		PG&E - RFA Evaluation	15 days	Mon 6/24/19	Fri 7/12/19		
1155		PG&E - RFA Review with EE PRG	4 days	Tue 7/23/19	Fri 7/26/19		
1156		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/5/19	Fri 8/9/19		
1157		PG&E - RFP Preparation	45 days	Tue 8/27/19	Mon 10/28/19		
1158		PG&E - RFP Release	1 day	Mon 11/4/19	Mon 11/4/19		
1159		PG&E - RFP Proposal Creation Duration	33 days	Mon 11/4/19	Wed 12/18/19		
1160		PG&E - RFP Evaluation	18 days	Mon 1/6/20	Wed 1/29/20		
1161		PG&E - RFP Review with EE PRG	4 days	Tue 2/25/20	Fri 2/28/20		
1162		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/2/20	Fri 3/6/20		
1163		PG&E - Contract Negotiation and Development	58 days	Fri 2/28/20	Tue 5/19/20		
1164		PG&E - Contract Review with EE PRG	7 days	Tue 5/26/20	Wed 6/3/20		
1165		PG&E - Final Award and Contract Signed	22 days	Fri 5/29/20	Mon 6/29/20		
1166		PG&E - Submit Advice Letter		N/A	N/A		
1167		PG&E - Advice Letter Approved					
1168		PG&E - Implementation Plan	24 days	Tue 7/28/20	Fri 8/28/20		
1169		PG&E - Statewide Codes & Standards (RFP only) Solicitation	221 days?	Mon 7/8/19	Mon 5/11/20		
1170		PG&E - RFA Preparation		N/A	N/A		
1171		PG&E - RFA Release		N/A	N/A		
1172		PG&E - RFA Abstract Creation Duration		N/A	N/A		
1173		PG&E - RFA Evaluation		N/A	N/A		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1174		PG&E - RFA Review with EE PRG		N/A	N/A		
1175		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A		
1176		PG&E - RFP Preparation	36 days	Mon 7/8/19	Mon 8/26/19		
1177		PG&E - RFP Release	1 day	Tue 9/10/19	Tue 9/10/19		
1178		PG&E - RFP Proposal Creation Duration	24 days	Tue 9/10/19	Fri 10/11/19		
1179		PG&E - RFP Evaluation	10 days	Mon 10/14/19	Fri 10/25/19		
1180		PG&E - RFP Review with EE PRG	4 days	Thu 11/21/19	Tue 11/26/19		
1181		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 11/27/19	Fri 11/29/19		
1182		PG&E - Contract Negotiation and Development	35 days	Mon 12/2/19	Fri 1/17/20		
1183		PG&E - Contract Review with EE PRG	4 days	Tue 1/21/20	Fri 1/24/20		
1184		PG&E - Final Award and Contract Signed	32 days	Wed 1/29/20	Thu 3/12/20		
1185		PG&E - Submit Advice Letter		N/A	N/A		
1186		PG&E - Advice Letter Approved					
1187		PG&E - Implementation Plan	32 days	Fri 3/27/20	Mon 5/11/20		
1188		PG&E - Local Multi-Sector (40% outsource) Solicitation	251 days?	Tue 4/28/20	Tue 4/13/21		
1189		PG&E - RFA Preparation		N/A	N/A		
1190		PG&E - RFA Release		N/A	N/A		
1191		PG&E - RFA Abstract Creation Duration		N/A	N/A		
1192		PG&E - RFA Evaluation		N/A	N/A		
1193		PG&E - RFA Review with EE PRG		N/A	N/A		
1194		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A		
1195		PG&E - RFP Preparation		N/A	N/A		
1196		PG&E - RFP Release		N/A	N/A		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1197		PG&E - RFP Proposal Creation Duration		N/A	N/A		
1198		PG&E - RFP Evaluation		N/A	N/A		
1199		PG&E - RFP Review with EE PRG	4 days	Tue 4/28/20	Fri 5/1/20		
1200		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder					
1201		PG&E - Contract Negotiation and Development	81 days	Thu 7/2/20	Thu 10/22/20		
1202		PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20		
1203		PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20		
1204		PG&E - Submit Advice Letter	1 day	Wed 1/13/21	Wed 1/13/21		
1205		PG&E - Advice Letter Approved	1 day?	Fri 2/12/21	Fri 2/12/21		
1206		PG&E - Implementation Plan	43 days	Sat 2/13/21	Tue 4/13/21		
1207		PG&E - Statewide New Constructions (Non-Residential) Solicitation	591 days	Mon 3/25/19	Sun 6/27/21		
1208		PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19		
1209		PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19		
1210		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19		
1211		PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19		
1212		PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19		
1213		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19		
1214		PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20		
1215		PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20		
1216		PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20		
1217		PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20		
1218		PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20		
1219		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1220		PG&E - Contract Negotiation and Development	49 days	Mon 8/17/20	Thu 10/22/20		
1221		PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20		
1222		PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20		
1223		PG&E - Submit Advice Letter	1 day	Fri 2/19/21	Fri 2/19/21		
1224		PG&E - Advice Letter Approved	1 day	Wed 4/28/21	Wed 4/28/21		
1225		PG&E - Implementation Plan	43 days	Thu 4/29/21	Sun 6/27/21		
1226		PG&E - Statewide New Construction (Residential) Solicitation	640 days?	Mon 3/25/19	Fri 9/3/21		
1227		PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19		
1228		PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19		
1229		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19		
1230		PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19		
1231		PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19		
1232		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19		
1233		PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20		
1234		PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20		
1235		PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20		
1236		PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20		
1237		PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20		
1238		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20		
1239		PG&E - Contract Negotiation and Development	177 days	Mon 8/17/20	Tue 4/20/21		
1240		PG&E - Contract Review with EE PRG	16 days	Thu 4/22/21	Thu 5/13/21		
1241		PG&E - Final Award and Contract Signed	32 days	Sat 5/15/21	Mon 6/28/21		
1242		PG&E - Submit Advice Letter	1 day	Mon 7/12/21	Mon 7/12/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1243		PG&E - Advice Letter Approved (all electric)	1 day	Wed 8/11/21	Wed 8/11/21		
1244		PG&E - Advice Letter Approved (mixed fuel)	1 day	Wed 9/15/21	Wed 9/15/21		
1245		PG&E - Implementation Plan (all electric)	43 days	Thu 8/12/21	Mon 10/11/21		
1246		PG&E - Implementation Plan (mixed fuel)	43 days	Thu 9/16/21	Sun 11/14/21		
1247		PG&E - Statewide WE&T Career Connections Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21		
1248		PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20		
1249		PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20		
1250		PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20		
1251		PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20		
1252		PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20		
1253		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20		
1254		PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20		
1255		PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20		
1256		PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20		
1257		PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20		
1258		PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20		
1259		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20		
1260		PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21		
1261		PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21		
1262		PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21		
1263		PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21		
1264		PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21		
1265		PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1266		PG&E - Statewide WE&T Career and Workforce Readiness Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21		
1267		PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20		
1268		PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20		
1269		PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20		
1270		PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20		
1271		PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20		
1272		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20		
1273		PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20		
1274		PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20		
1275		PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20		
1276		PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20		
1277		PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20		
1278		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20		
1279		PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21		
1280		PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21		
1281		PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21		
1282		PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21		
1283		PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21		
1284		PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21		
1285		PG&E - Statewide State of CA (Dept. of Corrections) Solicitation	348 days?	Sun 3/1/20	Tue 6/29/21		
1286		PG&E - RFA Preparation	46 days	Sun 3/1/20	Fri 5/1/20		
1287		PG&E - RFA Release	1 day	Wed 5/13/20	Wed 5/13/20		
1288		PG&E - RFA Abstract Creation Duration	31 days	Wed 5/13/20	Wed 6/24/20		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1289		PG&E - RFA Evaluation	15 days	Mon 6/29/20	Fri 7/17/20		
1290		PG&E - RFA Review with EE PRG	5 days	Tue 7/28/20	Mon 8/3/20		
1291		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/3/20	Fri 8/7/20		
1292		PG&E - RFP Preparation	20 days	Mon 8/3/20	Fri 8/28/20		
1293		PG&E - RFP Release	1 day	Wed 9/9/20	Wed 9/9/20		
1294		PG&E - RFP Proposal Creation Duration	31 days	Wed 9/9/20	Wed 10/21/20		
1295		PG&E - RFP Evaluation	31 days	Fri 10/23/20	Fri 12/4/20		
1296		PG&E - RFP Review with EE PRG	6 days	Tue 12/22/20	Tue 12/29/20		
1297		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 1/6/21	Fri 1/8/21		
1298		PG&E - Contract Negotiation and Development	65 days	Wed 1/20/21	Tue 4/20/21		
1299		PG&E - Contract Review with EE PRG	7 days	Thu 4/22/21	Fri 4/30/21		
1300		PG&E - Final Award and Contract Signed	22 days	Sat 5/1/21	Mon 5/31/21		
1301		PG&E - Submit Advice Letter	1 day	Thu 6/24/21	Thu 6/24/21		
1302		PG&E - Advice Letter Approved	1 day	Wed 7/28/21	Wed 7/28/21		
1303		PG&E - Implementation Plan	43 days	Thu 7/29/21	Sun 9/26/21		
1304		PG&E - Local (Micro and Small Business Equity Program) Solicitation	403 days?	Tue 6/1/21	Thu 12/15/22		
1305		PG&E - RFA Preparation	38 days	Tue 6/1/21	Thu 7/22/21		
1306		PG&E - RFA Release	1 day	Tue 9/7/21	Tue 9/7/21		
1307		PG&E - RFA Abstract Creation Duration	34 days	Wed 9/8/21	Mon 10/25/21		
1308		PG&E - RFA Evaluation	18 days	Tue 10/26/21	Thu 11/18/21		
1309		PG&E - RFP Release	1 day	Wed 12/8/21	Wed 12/8/21		
1310		PG&E - RFP Proposal Creation Duration	46 days	Wed 12/8/21	Wed 2/9/22		
1311		PG&E - RFP Evaluation	21 days	Thu 2/10/22	Thu 3/10/22		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1312		PG&E - RFP Review with EE PRG	6 days	Thu 3/17/22	Thu 3/24/22		
1313		PG&E - RFP Estimated Bidder Notification	1 day	Wed 3/30/22	Wed 3/30/22		
1314		PG&E - Contract Negotiation and Development	71 days	Thu 4/7/22	Thu 7/14/22		
1315		PG&E - Contract Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22		
1316		PG&E - Final Award and Contract Signed	45 days	Mon 8/8/22	Fri 10/7/22		
1317		PG&E - Submit Advice Letter	1 day	Wed 10/12/22	Wed 10/12/22		
1318		PG&E - Advice Letter Approved	1 day	Fri 11/11/22	Fri 11/11/22		
1319		PG&E - Implementation Plan	31 days	Fri 11/11/22	Fri 12/23/22		
1320		PG&E - Local (C&S Compliance Improvement) Solicitation	436 days	Tue 3/1/22	Tue 10/31/23		
1321		PG&E - RFA Preparation	34 days	Tue 3/1/22	Fri 4/15/22		
1322		PG&E - RFA Release	1 day	Mon 5/16/22	Mon 5/16/22		
1323		PG&E - RFA Abstract Creation Duration	25 days	Tue 5/17/22	Mon 6/20/22		
1324		PG&E - RFA Evaluation	28 days	Tue 6/21/22	Thu 7/28/22		
1325		PG&E - RFA Review with EE PRG	1 day	Tue 8/9/22	Tue 8/9/22		
1326		PG&E - RFA Estimated Bidder Notification	1 day	Wed 8/31/22	Wed 8/31/22		
1327		PG&E - RFP Preparation	24 days	Mon 8/1/22	Thu 9/1/22		
1328		PG&E - RFP Release	1 day	Tue 9/13/22	Tue 9/13/22		
1329		PG&E - RFP Proposal Creation Duration	26 days	Tue 9/13/22	Tue 10/18/22		
1330		PG&E - RFP Evaluation	45 days	Wed 10/19/22	Tue 12/20/22		
1331		PG&E - RFP Review with EE PRG	1 day	Tue 1/24/23	Tue 1/24/23		
1332		PG&E - RFP Estimated Bidder Notification	1 day	Fri 2/10/23	Fri 2/10/23		
1333		PG&E - Contract Negotiation and Development	47 days	Mon 2/13/23	Tue 4/18/23		
1334		PG&E - Contract Review with EE PRG	26 days	Tue 5/23/23	Tue 6/27/23		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1335		PG&E - Final Award and Contract Signed	48 days	Wed 6/28/23	Fri 9/1/23		
1336		PG&E - Submit Advice Letter		N/A			
1337		PG&E - Advice Letter Approved		N/A			
1338		PG&E - Implementation Plan	1 day	Tue 10/31/23	Tue 10/31/23		
1339		PG&E - Residential Electrification Equity Program Solicitation	595 days	Mon 8/1/22	Fri 11/8/24		
1340		PG&E - RFA Preparation	59 days	Mon 8/1/22	Thu 10/20/22		
1341		PG&E - RFA Release	1 day	Tue 11/29/22	Tue 11/29/22		
1342		PG&E - RFA Abstract Creation Duration	46 days	Tue 11/29/22	Tue 1/31/23		
1343		PG&E - RFA Evaluation	17 days	Sun 2/5/23	Sun 2/26/23		
1344		PG&E - RFA Review with EE PRG	6 days	Mon 2/27/23	Mon 3/6/23		
1345		PG&E - RFA Estimated Bidder Notification	3 days	Mon 3/6/23	Wed 3/8/23		
1346		PG&E - RFP Preparation	46 days	Mon 1/9/23	Mon 3/13/23		
1347		PG&E - RFP Release	1 day	Tue 4/11/23	Tue 4/11/23		
1348		PG&E - RFP Proposal Creation Duration	26 days	Tue 4/11/23	Tue 5/16/23		
1349		PG&E - RFP Evaluation	18 days	Fri 5/19/23	Tue 6/13/23		
1350		PG&E - RFP Review with EE PRG	1 day	Tue 6/27/23	Tue 6/27/23		
1351		PG&E - RFP Estimated Bidder Notification	1 day	Tue 7/11/23	Tue 7/11/23		
1352		PG&E - Contract Negotiation and Development	233 days	Tue 8/1/23	Thu 6/20/24		
1353		PG&E - Contract Review with EE PRG	8 days	Fri 6/21/24	Tue 7/2/24		
1354		PG&E - Final Award and Contract Signed	21 days	Fri 7/5/24	Fri 8/2/24		
1355		PG&E - Submit Advice Letter	1 day	Fri 8/9/24	Fri 8/9/24		
1356		PG&E - Advice Letter Approved	1 day	Mon 9/9/24	Mon 9/9/24		
1357		PG&E - Implementation Plan	1 day	Fri 11/8/24	Fri 11/8/24		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1358		PG&E - Statewide C&S Advocacy Solicitation	641 days	Tue 2/1/22	Tue 7/16/24		
1359		PG&E - RFA Preparation	54 days	Tue 2/1/22	Fri 4/15/22		
1360		PG&E - RFA Release	1 day	Mon 5/30/22	Mon 5/30/22		
1361		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/31/22	Fri 7/1/22		
1362		PG&E - RFA Evaluation	14 days	Fri 7/1/22	Wed 7/20/22		
1363		PG&E - RFA Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22		
1364		PG&E - RFA Estimated Bidder Notification	1 day	Mon 8/1/22	Mon 8/1/22		
1365		PG&E - RFP Preparation	36 days	Fri 4/1/22	Fri 5/20/22		
1366		PG&E - RFP Release	1 day	Tue 6/7/22	Tue 6/7/22		
1367		PG&E - RFP Proposal Creation Duration	31 days	Tue 6/7/22	Tue 7/19/22		
1368		PG&E - RFP Evaluation	50 days	Wed 7/20/22	Tue 9/27/22		
1369		PG&E - RFP Review with EE PRG	1 day	Wed 10/5/22	Wed 10/5/22		
1370		PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/24/22	Mon 10/24/22		
1371		PG&E - Contract Negotiation and Development	73 days	Mon 11/14/22	Wed 2/22/23		
1372		PG&E - Contract Review with EE PRG - Wave 1	1 day	Tue 4/25/23	Tue 4/25/23		
1373		PG&E - Final Award and Contract Signed	18 days	Mon 7/17/23	Wed 8/9/23		
1374		PG&E - Submit Advice Letter (wave 1)	1 day	Thu 9/21/23	Thu 9/21/23		
1375		PG&E - Advice Letter Approved	1 day	Wed 10/25/23	Wed 10/25/23		
1376		PG&E - Implementation Plan	1 day	Thu 12/7/23	Thu 12/7/23		
1377		PG&E - Contract Review with EE PRG - Wave 2	1 day	Wed 12/20/23	Wed 12/20/23		
1378		PG&E - Final Award and Contract Signed	1 day	Fri 3/29/24	Fri 3/29/24		
1379		PG&E - Submit Advice Letter	1 day	Wed 4/17/24	Wed 4/17/24		
1380		PG&E - Advice Letter Approved	1 day	Fri 5/17/24	Fri 5/17/24		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1381		PG&E - Implementation Plan	1 day	Tue 7/16/24	Tue 7/16/24		
1382		PG&E - Zonal Electrification Solicitation	495 days	Thu 12/1/22	Wed 10/23/24		
1383		PG&E - RFP Preparation	88 days	Thu 12/1/22	Mon 4/3/23		
1384		PG&E - RFP Release	1 day	Tue 4/18/23	Tue 4/18/23		
1385		PG&E - RFP Proposal Creation Duration	53 days	Tue 4/18/23	Thu 6/29/23		
1386		PG&E - RFP Evaluation (including interviews)	40 days	Mon 7/10/23	Fri 9/1/23		
1387		PG&E - RFP Review with EE PRG	1 day	Tue 9/26/23	Tue 9/26/23		
1388		PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/2/23	Mon 10/2/23		
1389		PG&E - Contract Negotiation and Development	135 days	Mon 10/9/23	Fri 4/12/24		
1390		PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24		
1391		PG&E - Final Award and Contract Signed	43 days	Wed 5/1/24	Fri 6/28/24		
1392		PG&E - Submit Advice Letter	1 day	Wed 7/3/24	Wed 7/3/24		
1393		PG&E - Advice Letter Approved	1 day	Wed 8/28/24	Wed 8/28/24		
1394		PG&E - Implementation Plan	1 day	Wed 10/23/24	Wed 10/23/24		
1395		PG&E - Residential Whole Home Load Management RFP	453 days	Tue 8/15/23	Thu 5/8/25		
1396		PG&E - RFP Preparation	1 day	Tue 8/15/23	Tue 8/15/23		
1397		PG&E - RFP Release	1 day	Tue 8/15/23	Tue 8/15/23		
1398		PG&E - RFP Proposal Creation Duration	51 days	Tue 8/15/23	Tue 10/24/23		
1399		PG&E - RFP Evaluation	36 days	Thu 10/26/23	Thu 12/14/23		
1400		PG&E - RFP Review with EE PRG	1 day	Fri 2/16/24	Fri 2/16/24		
1401		PG&E - RFP Estimated Bidder Notification	1 day	Tue 2/27/24	Tue 2/27/24		
1402		PG&E - Contract Negotiation and Development	155 days	Wed 3/13/24	Tue 10/15/24		
1403		PG&E - Contract Review with EE PRG	8 days	Tue 11/5/24	Thu 11/14/24		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1404		PG&E - Final Award and Contract Signed	53 days	Thu 11/14/24	Mon 1/27/25		
1405		PG&E - Submit Advice Letter	1 day	Fri 2/7/25	Fri 2/7/25		
1406		PG&E - Advice Letter Approved	1 day	Mon 3/10/25	Mon 3/10/25		
1407		PG&E - Implementation Plan	1 day	Thu 5/8/25	Thu 5/8/25		
1408		PG&E - 2024 Summer Reliability Platform Administrator RFP	337 days?	Tue 4/18/23	Wed 7/31/24		
1409		PG&E - RFP Preparation	30 days	Mon 5/1/23	Fri 6/9/23		
1410		PG&E - RFP Release	1 day	Fri 9/1/23	Fri 9/1/23		
1411		PG&E - RFP Proposal Creation Duration	31 days	Fri 9/1/23	Fri 10/13/23		
1412		PG&E - RFP Evaluation	22 days	Tue 10/17/23	Wed 11/15/23		
1413		PG&E - RFP Review with EE PRG	1 day	Tue 11/28/23	Tue 11/28/23		
1414		PG&E - RFP Estimated Bidder Notification	1 day	Tue 12/5/23	Tue 12/5/23		
1415		PG&E - Contract Negotiation and Development	68 days	Mon 1/8/24	Wed 4/10/24		
1416		PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24		
1417		PG&E - Final Award and Contract Signed	22 days	Wed 5/1/24	Thu 5/30/24		
1418		PG&E - Submit Advice Letter	1 day	Fri 5/31/24	Fri 5/31/24		
1419		PG&E - Advice Letter Approved	1 day	Mon 7/1/24	Mon 7/1/24		
1420		PG&E - Implementation Plan	1 day	Wed 7/31/24	Wed 7/31/24		
1421		PG&E - C&S Code Readiness RFP	393 days?	Wed 2/1/23	Fri 8/2/24		
1422		PG&E - RFP Preparation	113 days	Wed 2/1/23	Fri 7/7/23		
1423		PG&E - RFP Release	1 day	Wed 7/12/23	Wed 7/12/23		
1424		PG&E - RFP Proposal Creation Duration	30 days	Thu 7/13/23	Wed 8/23/23		
1425		PG&E - RFP Evaluation	36 days	Mon 8/28/23	Mon 10/16/23		
1426		PG&E - RFP Review with EE PRG	1 day	Tue 10/24/23	Tue 10/24/23		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1427		PG&E - RFP Estimated Bidder Notification	1 day	Mon 11/6/23	Mon 11/6/23		
1428		PG&E - Contract Negotiation and Development	65 days	Wed 11/15/23	Tue 2/13/24		
1429		PG&E - Contract Review with EE PRG	1 day	Tue 2/27/24	Tue 2/27/24		
1430		PG&E - Final Award and Contract Signed	1 day	Fri 4/12/24	Fri 4/12/24		
1431		PG&E - Submit Advice Letter	1 day	Tue 5/7/24	Tue 5/7/24		
1432		PG&E - Advice Letter Approved	1 day	Thu 6/6/24	Thu 6/6/24		
1433		PG&E - Implementation Plan	1 day	Fri 8/2/24	Fri 8/2/24		
1434		PG&E - Residential Electrification - Single Point of Contact	414 days	Tue 8/1/23	Fri 2/28/25		
1435		PG&E - RFP Preparation	133 days	Tue 8/1/23	Thu 2/1/24		
1436		PG&E - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24		
1437		PG&E - RFP Proposal Creation Duration	33 days	Wed 2/28/24	Fri 4/12/24		
1438		PG&E - RFP Evaluation	66 days	Mon 4/15/24	Mon 7/15/24		
1439		PG&E - RFP Review with EE PRG	6 days	Fri 7/19/24	Fri 7/26/24		
1440		PG&E - RFP Estimated Bidder Notification	1 day	Wed 8/7/24	Wed 8/7/24		
1441		PG&E - Contract Negotiation and Development	62 days				
1442		PG&E - Contract Review with EE PRG	6 days				
1443		PG&E - Final Award and Contract Signed	25 days				
1444		PG&E - Submit Advice Letter	1 day				
1445		PG&E - Advice Letter Approved	1 day				
1446		PG&E - Implementation Plan	1 day				
1447		PG&E - Commercial SEM FP	430 days	Thu 8/3/23	Wed 3/26/25		
1448		PG&E - RFP Preparation	16 days	Thu 8/3/23	Thu 8/24/23		
1449		PG&E - RFP Release	1 day	Fri 11/3/23	Fri 11/3/23		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1	H2
1450		PG&E - RFP Proposal Creation Duration	55 days	Fri 11/3/23	Thu 1/18/24		
1451		PG&E - RFP Evaluation	58 days	Tue 1/23/24	Thu 4/11/24		
1452		PG&E - RFP Review with EE PRG	1 day	Wed 4/17/24	Wed 4/17/24		
1453		PG&E - RFP Estimated Bidder Notification	4 days	Tue 4/23/24	Fri 4/26/24		
1454		PG&E - Contract Negotiation and Development	90 days	Thu 5/2/24	Wed 9/4/24		
1455		PG&E - Contract Review with EE PRG	8 days	Mon 9/16/24	Wed 9/25/24		
1456		PG&E - Final Award and Contract Signed	58 days	Thu 9/26/24	Mon 12/16/24		
1457		PG&E - Submit Advice Letter	1 day	Thu 12/19/24	Thu 12/19/24		
1458		PG&E - Advice Letter Approved	0 days	Thu 1/30/25	Thu 1/30/25		
1459		PG&E - Implementation Plan	1 day	Wed 3/26/25	Wed 3/26/25		
1460		PG&E - SW WE&T Career & Workforce Readiness	610 days	Tue 10/8/24	Mon 2/8/27		
1461		PG&E - RFP Preparation	199 days	Tue 10/8/24	Fri 7/11/25		
1462		PG&E - RFP Release	1 day	Thu 7/17/25	Thu 7/17/25		
1463		PG&E - RFP Proposal Creation Duration	41 days	Thu 7/17/25	Thu 9/11/25		
1464		PG&E - RFP Evaluation	50 days	Mon 9/15/25	Fri 11/21/25		
1465		PG&E - RFP Review with EE PRG	4 days	Fri 12/5/25	Wed 12/10/25		
1466		PG&E - RFP Estimated Bidder Notification	4 days	Wed 12/10/25	Mon 12/15/25		
1467		PG&E - Contract Negotiation and Development	157 days	Wed 1/7/26	Thu 8/13/26		
1468		PG&E - Contract Review with EE PRG	14 days	Thu 8/13/26	Tue 9/1/26		
1469		PG&E - Final Award and Contract Signed	45 days	Tue 9/1/26	Sun 11/1/26		
1470		PG&E - Submit Advice Letter	1 day	Tue 11/10/26	Tue 11/10/26		
1471		PG&E - Advice Letter Approved	1 day	Thu 12/10/26	Thu 12/10/26		
1472		PG&E - Implementation Plan	43 days	Thu 12/10/26	Mon 2/8/27		

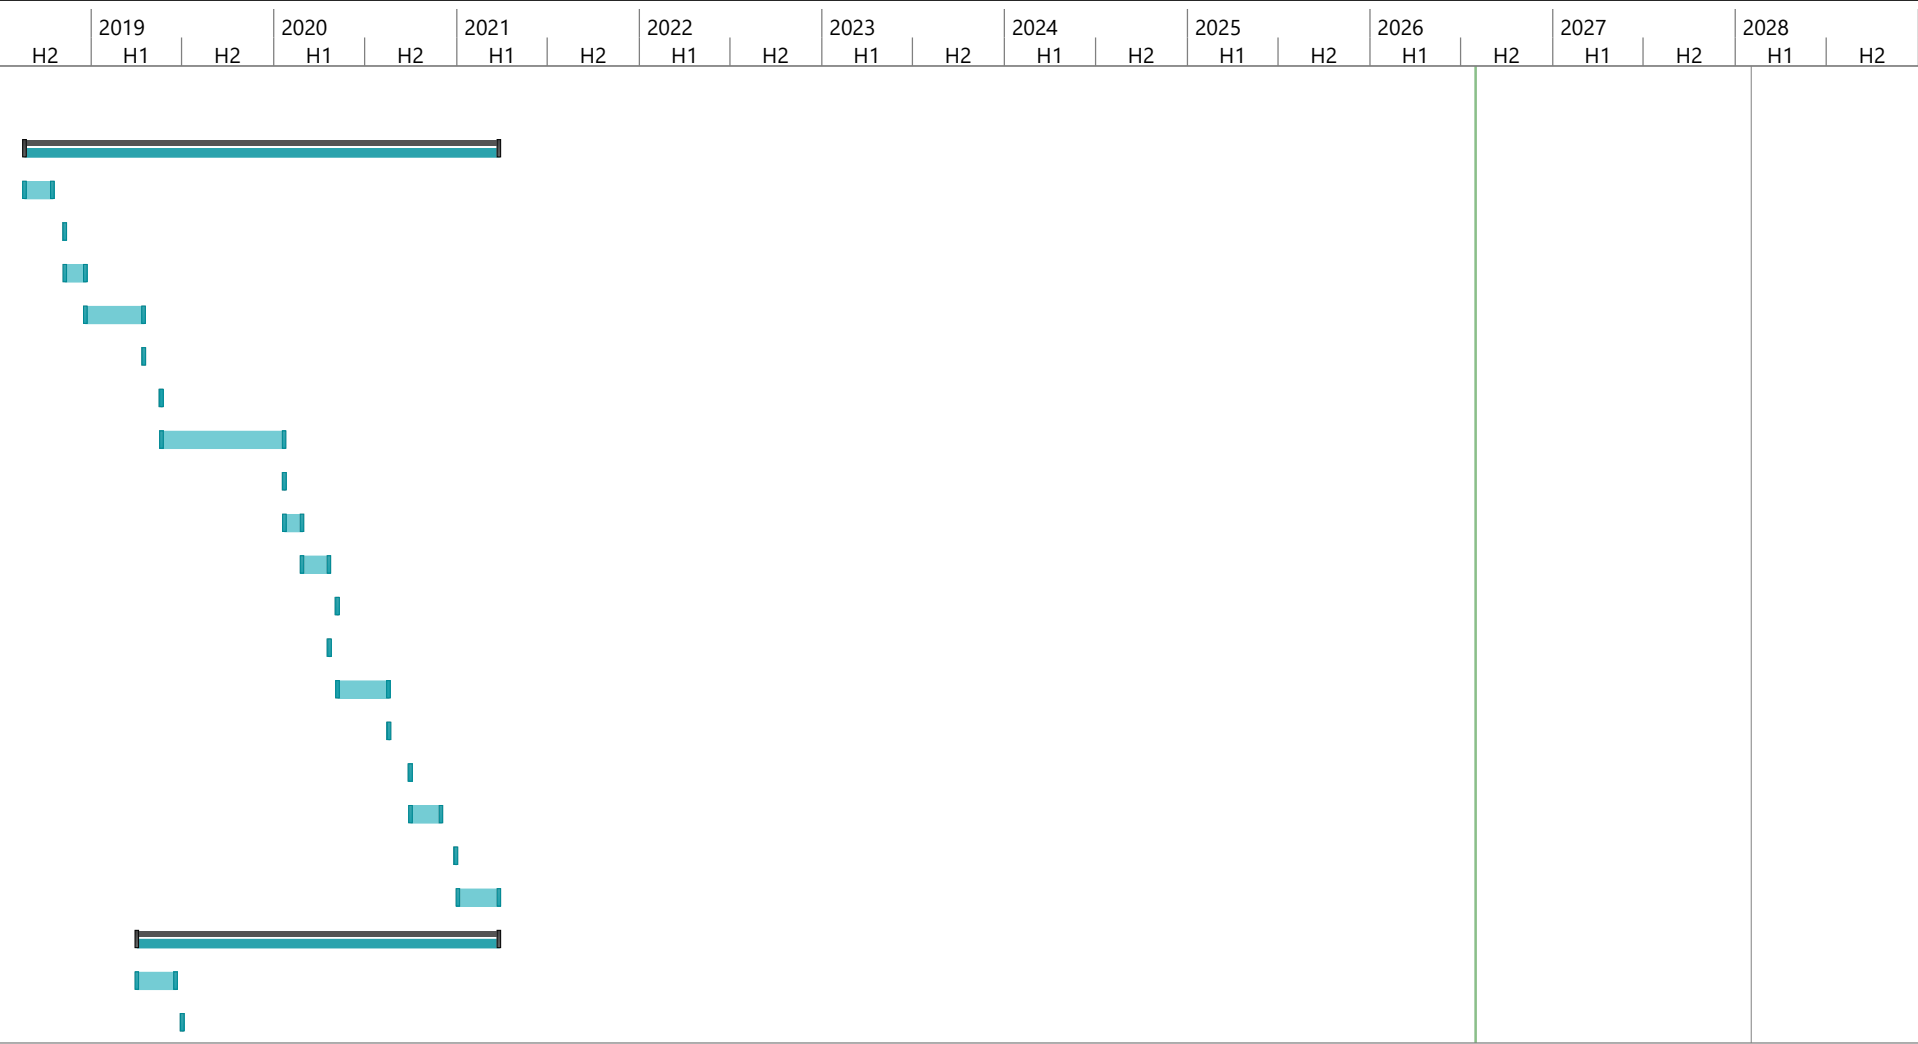
Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

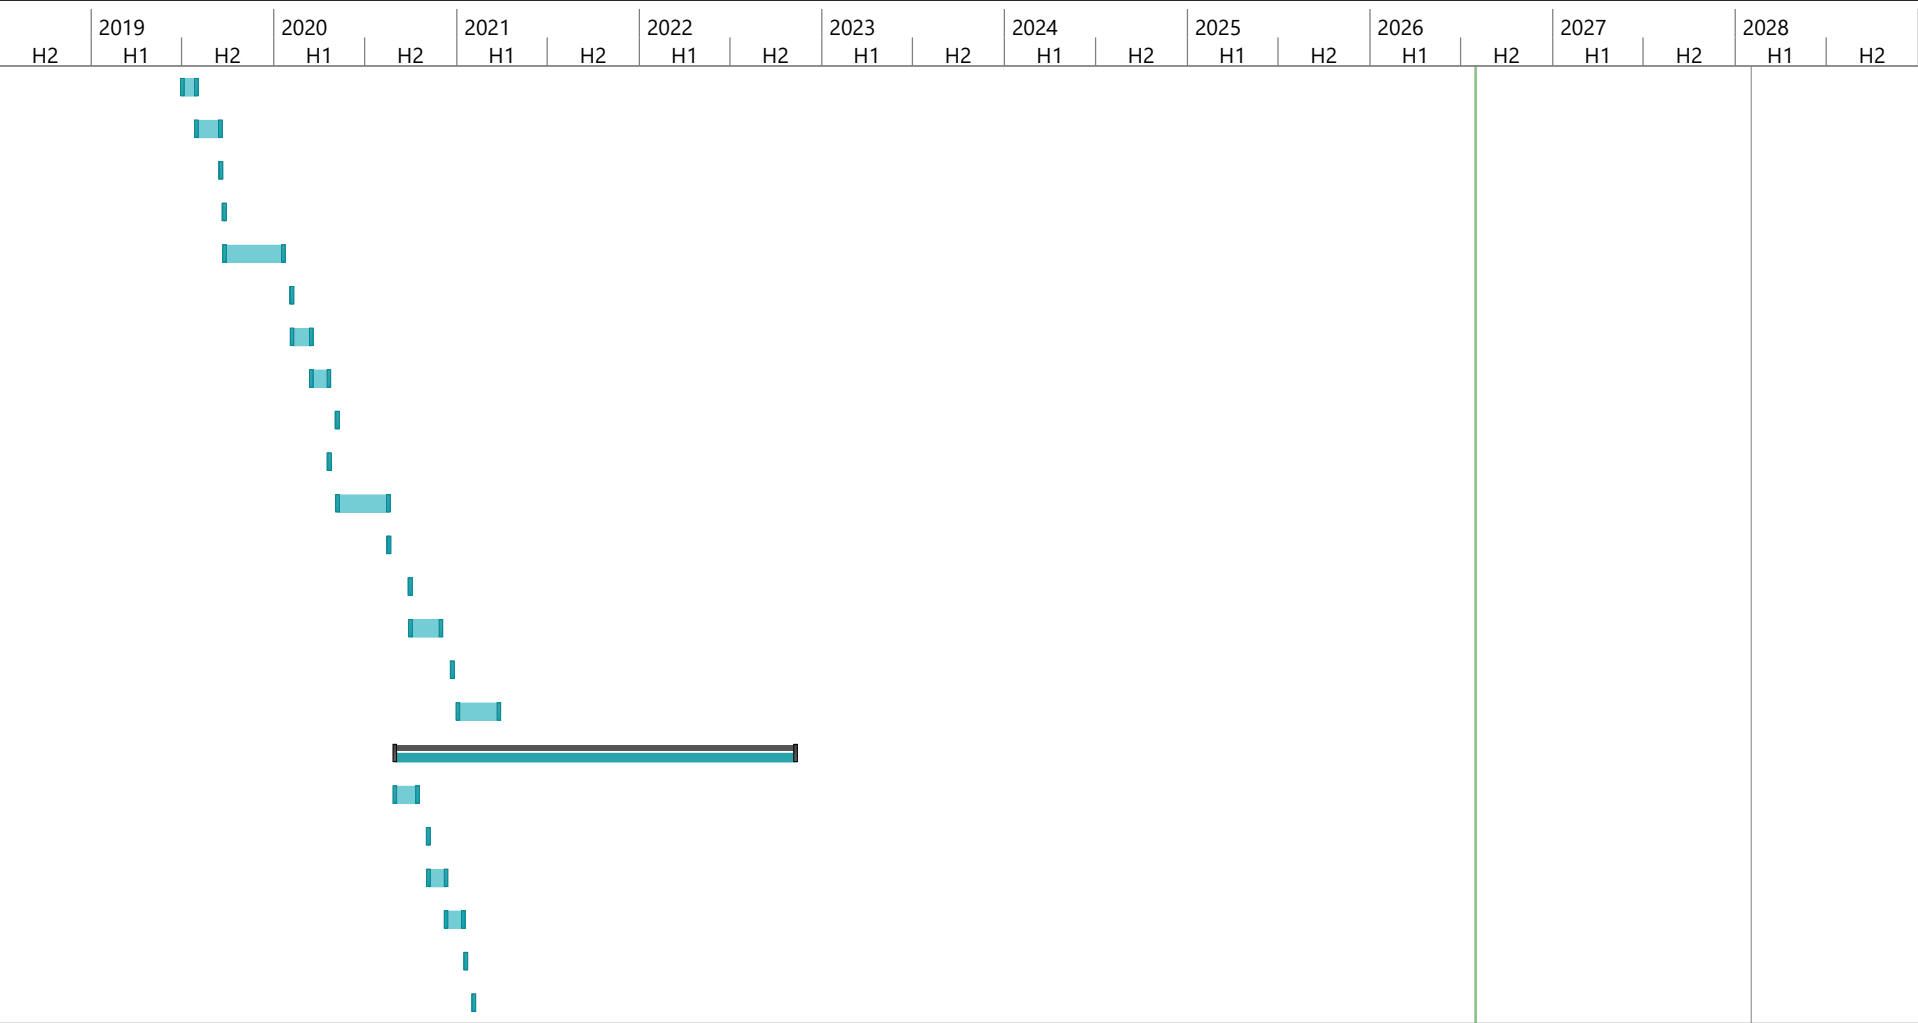
ID		Task Name	Duration	Start	Finish	2018 H1	H2
1473		PG&E - Statewide HVAC	532 days	Fri 5/2/25	Sat 5/15/27		
1474		PG&E - RFP Preparation	122 days	Fri 5/2/25	Mon 10/20/25		
1475		PG&E - RFP Release	1 day	Wed 10/22/25	Wed 10/22/25		
1476		PG&E - RFP Proposal Creation Duration	41 days	Wed 10/22/25	Wed 12/17/25		
1477		PG&E - RFP Evaluation	32 days	Thu 12/18/25	Fri 1/30/26		
1478		PG&E - RFP Review with EE PRG	1 day	Thu 3/26/26	Thu 3/26/26		
1479		PG&E - RFP Estimated Bidder Notification	1 day	Mon 4/6/26	Mon 4/6/26		
1480		PG&E - Contract Negotiation and Development	130 days	Tue 4/7/26	Mon 10/5/26		
1481		PG&E - Contract Review with EE PRG	9 days	Tue 10/20/26	Fri 10/30/26		
1482		PG&E - Final Award and Contract Signed	1 day	Fri 2/5/27	Fri 2/5/27		
1483		PG&E - Submit Advice Letter	1 day	Mon 2/15/27	Mon 2/15/27		
1484		PG&E - Advice Letter Approved	1 day	Mon 3/15/27	Mon 3/15/27		
1485		PG&E - Implementation Plan	1 day	Sat 5/15/27	Sat 5/15/27		

Project: IOU Master Task Timeli
Date: Fri 7/31/26

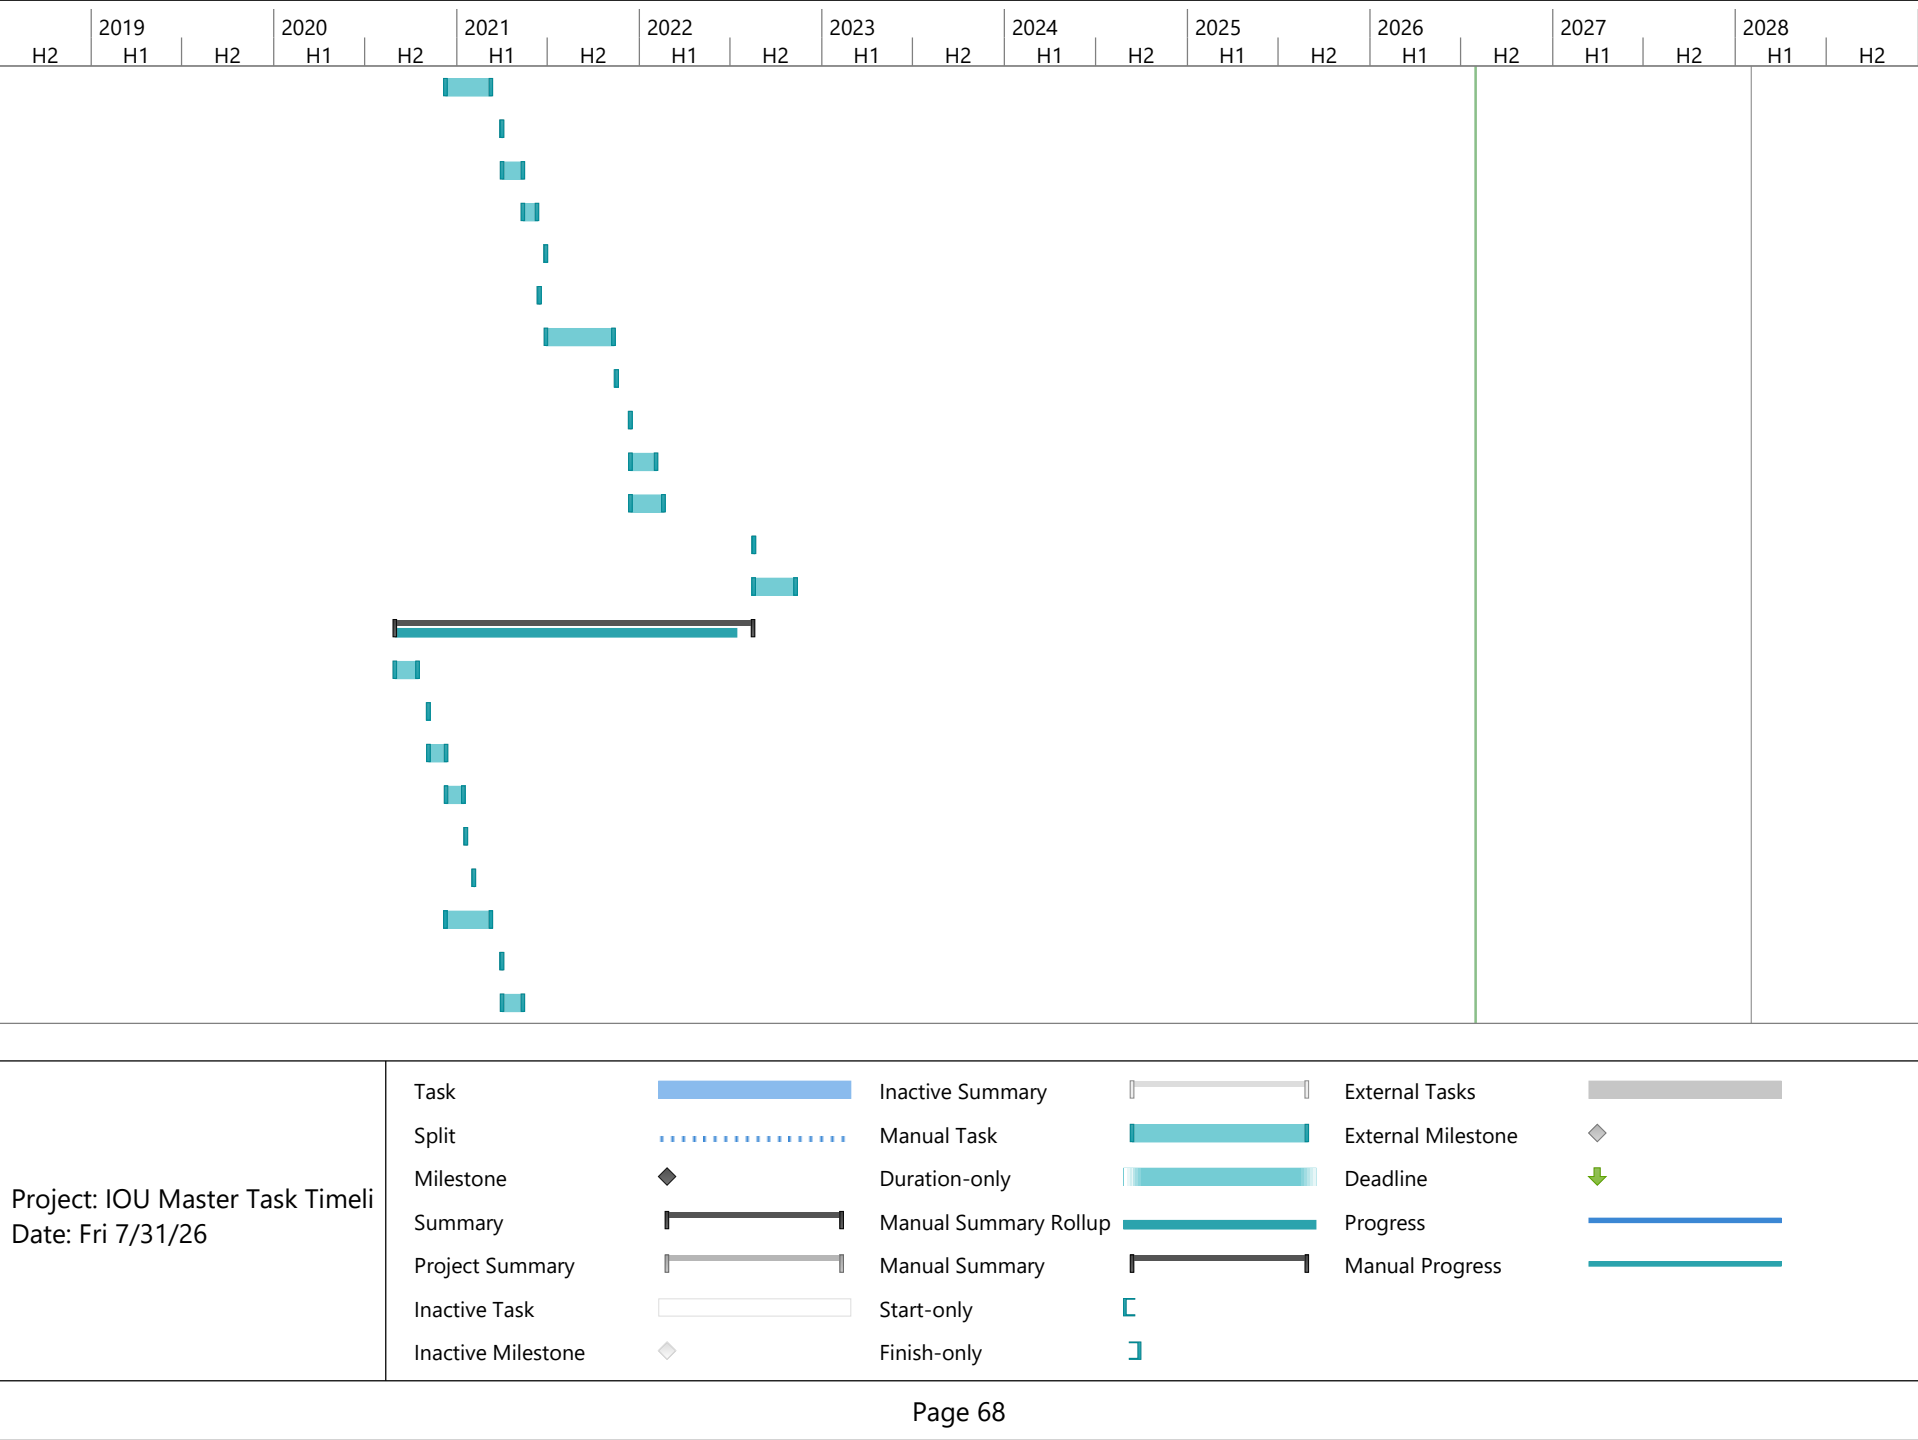
Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

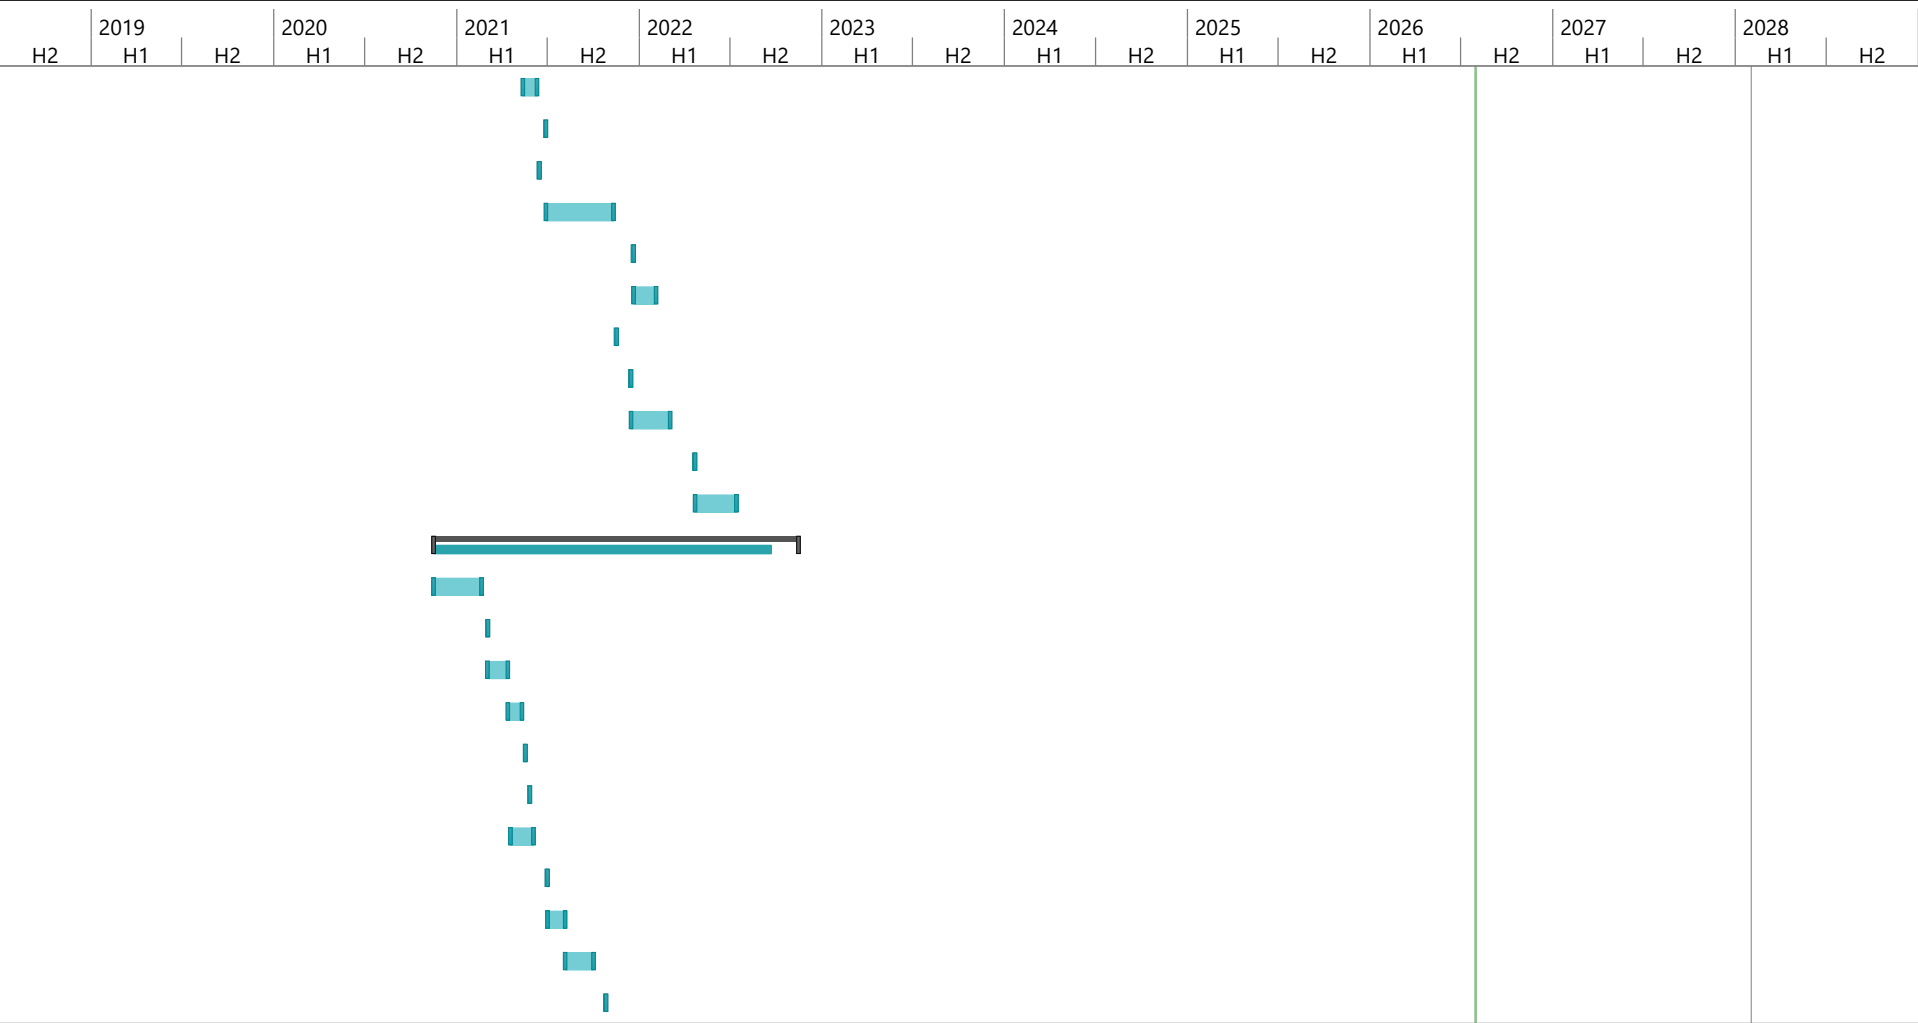


Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

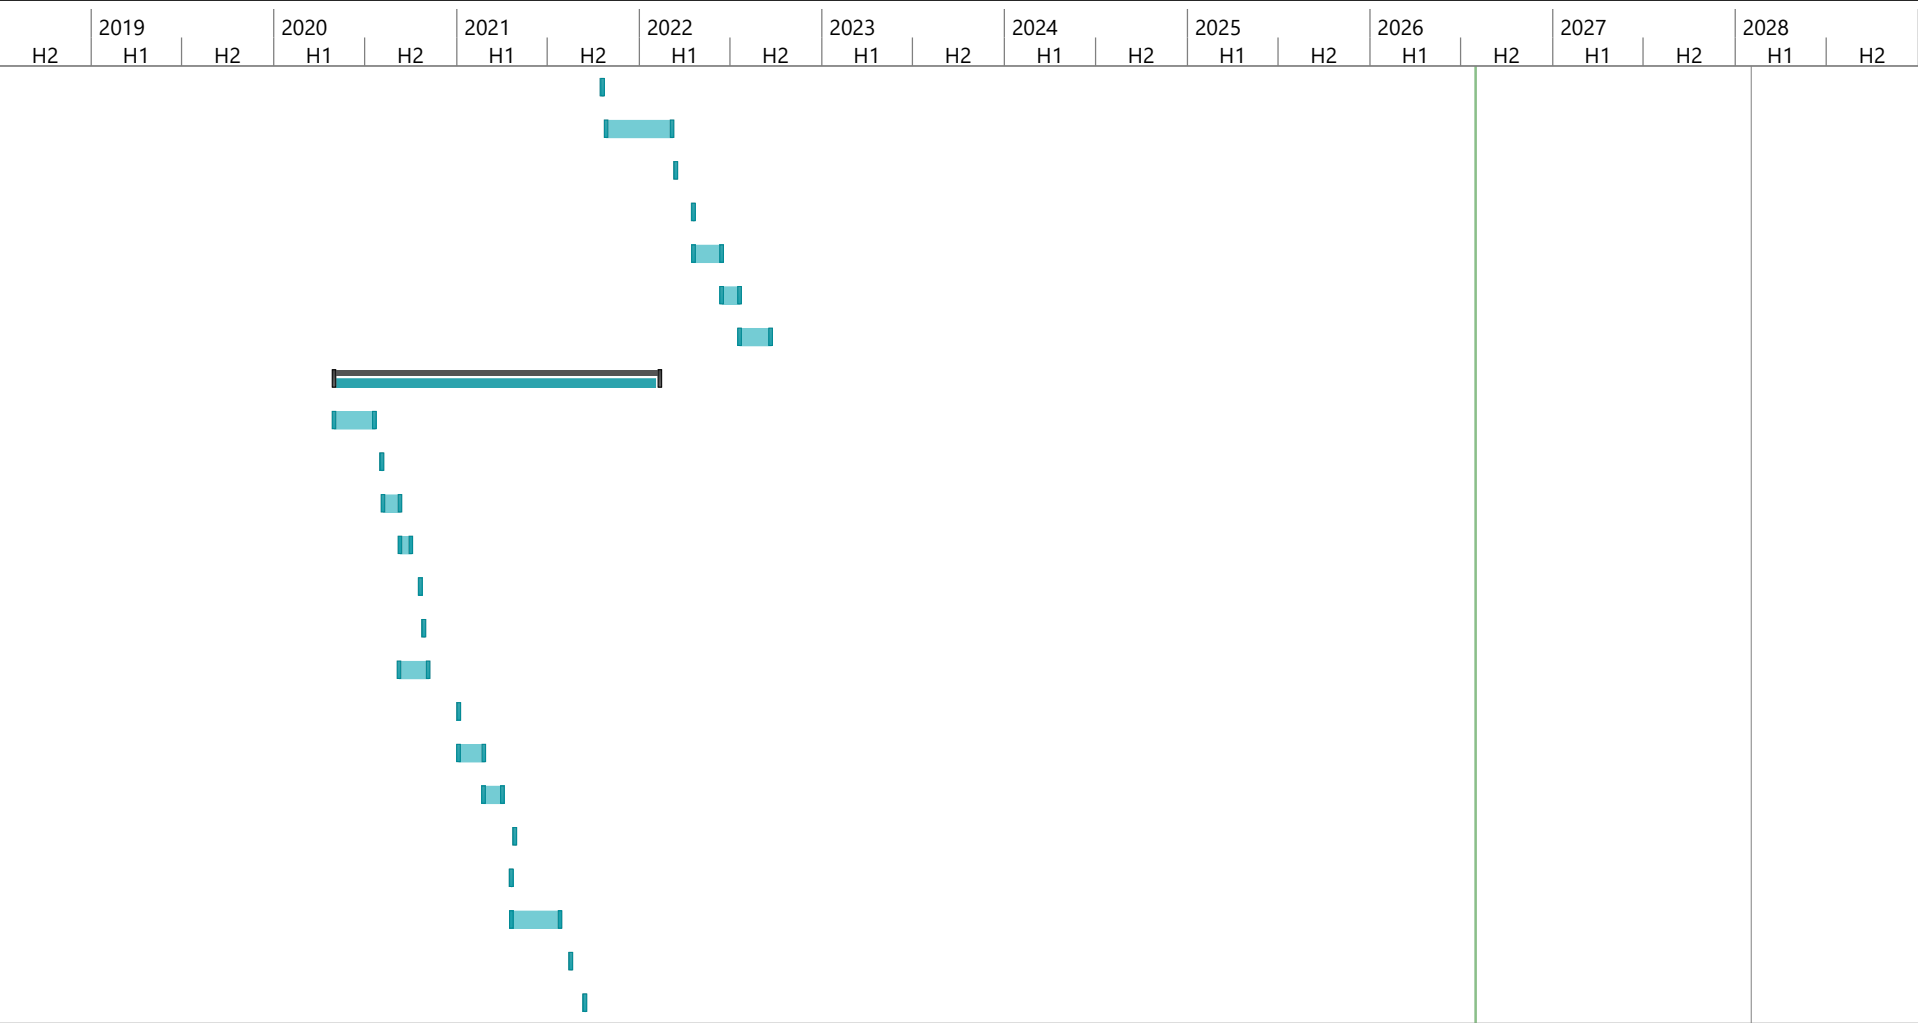



Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

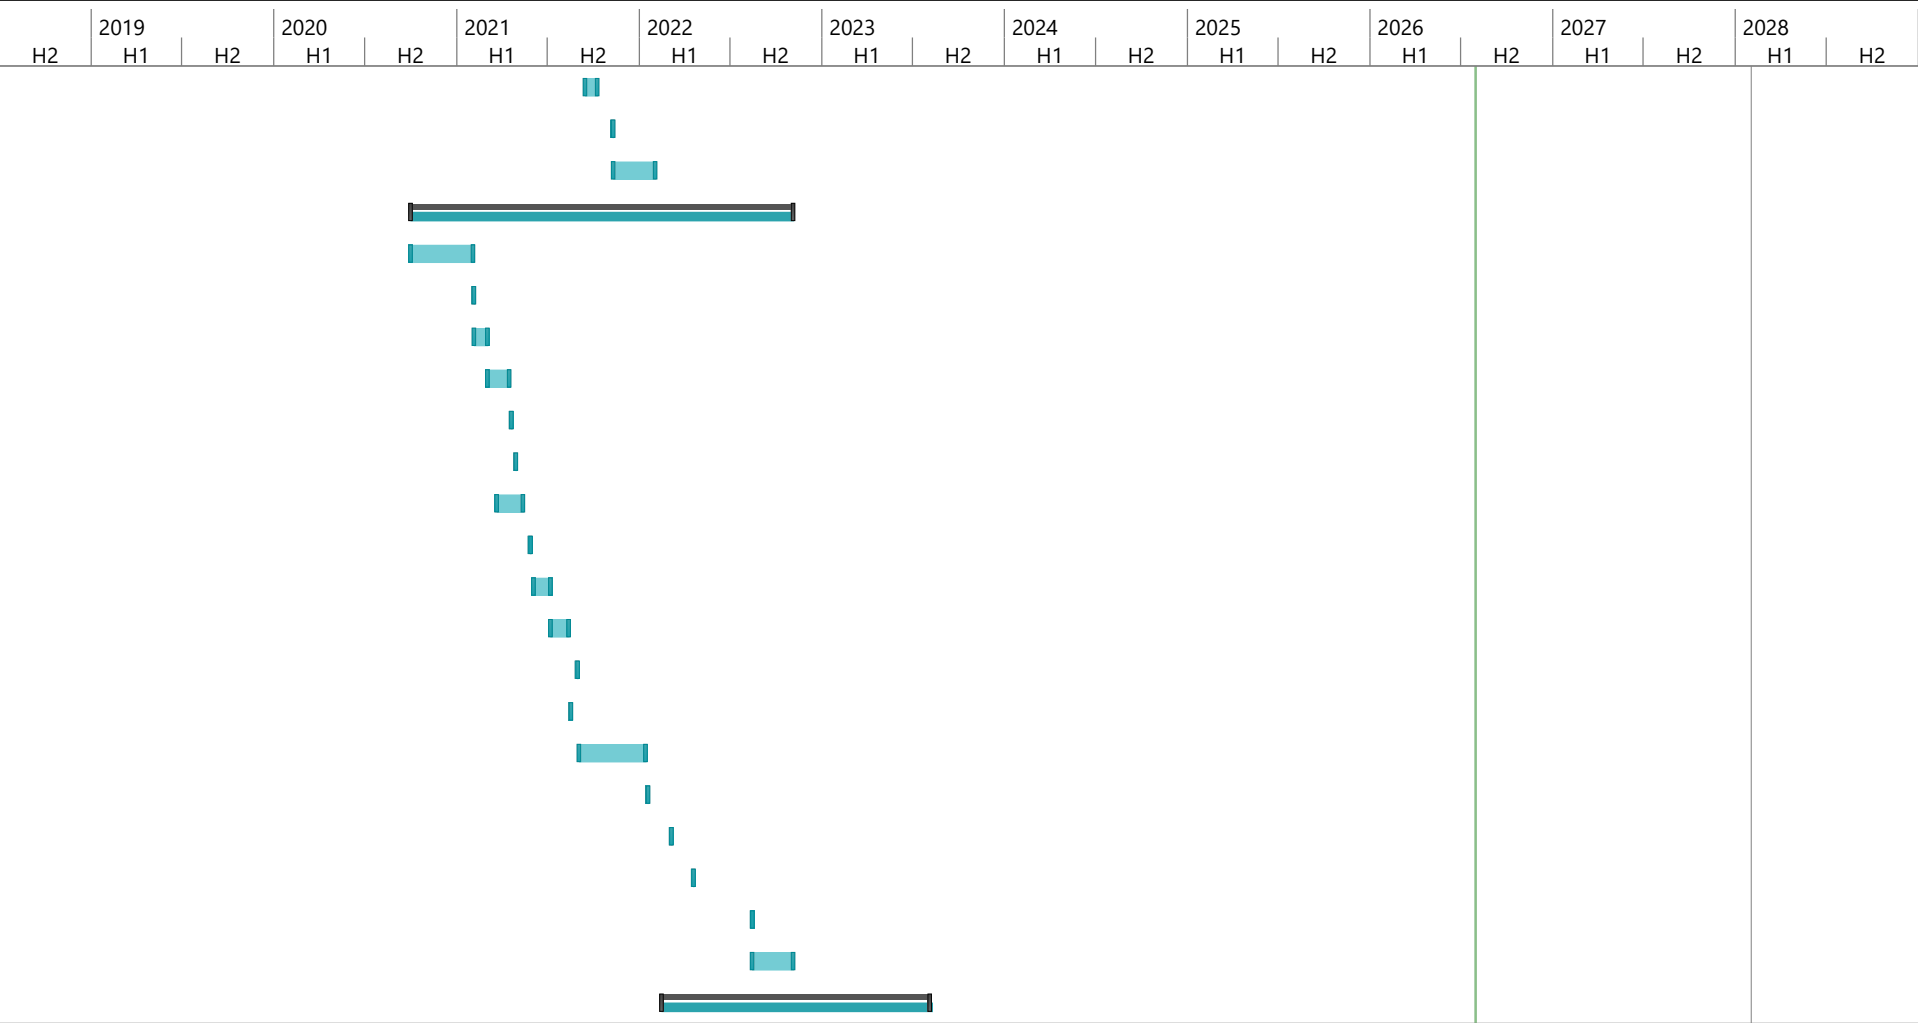




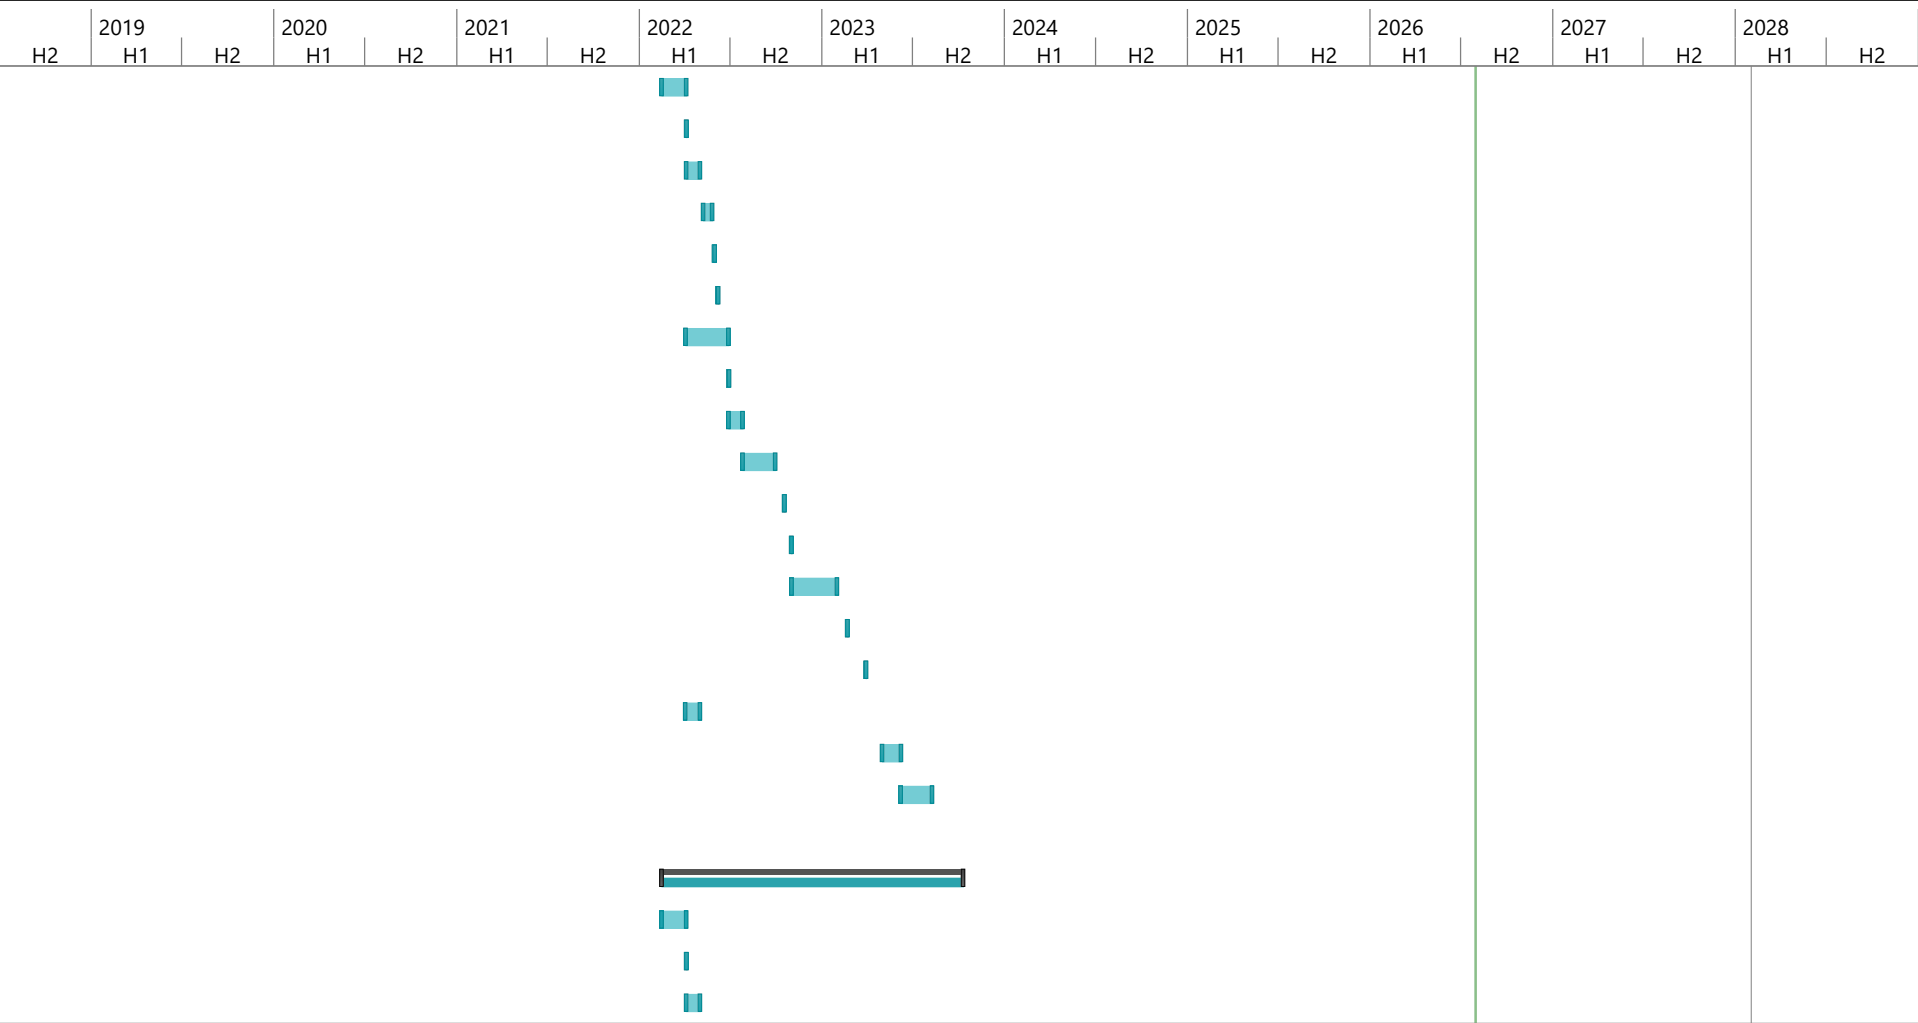
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



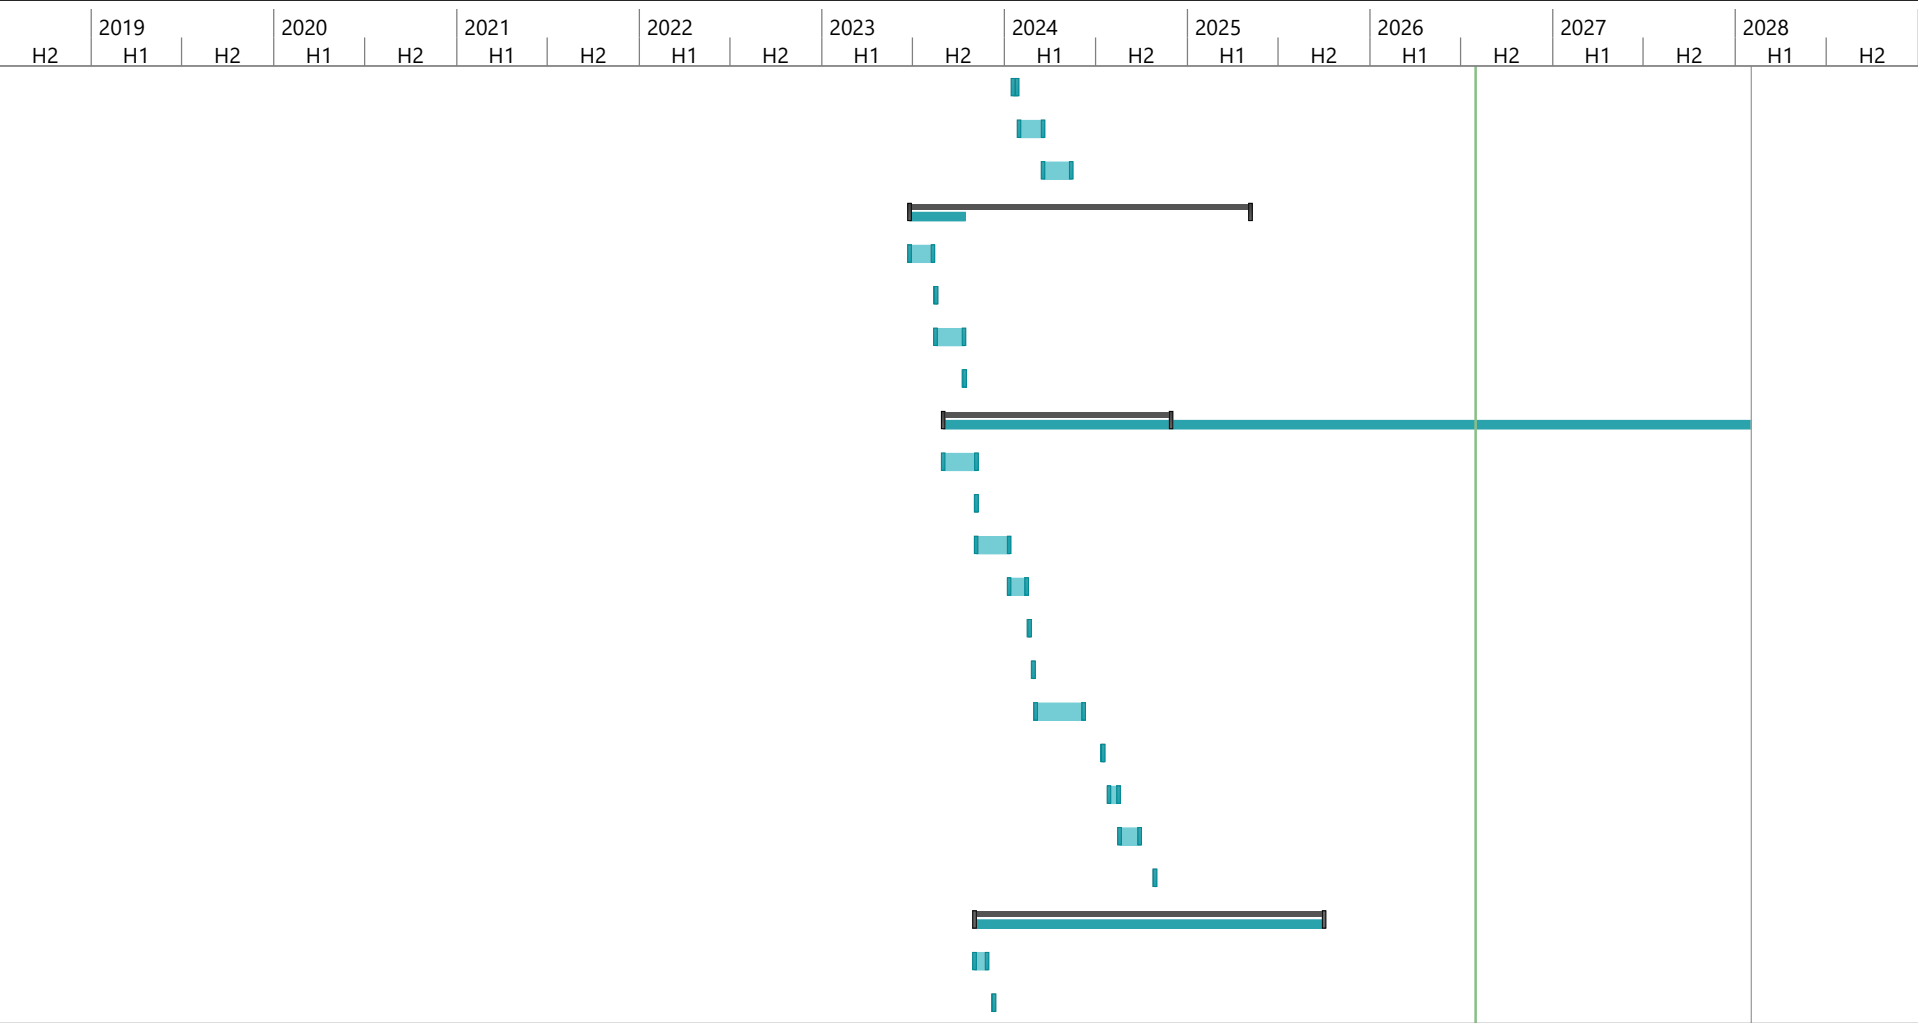
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



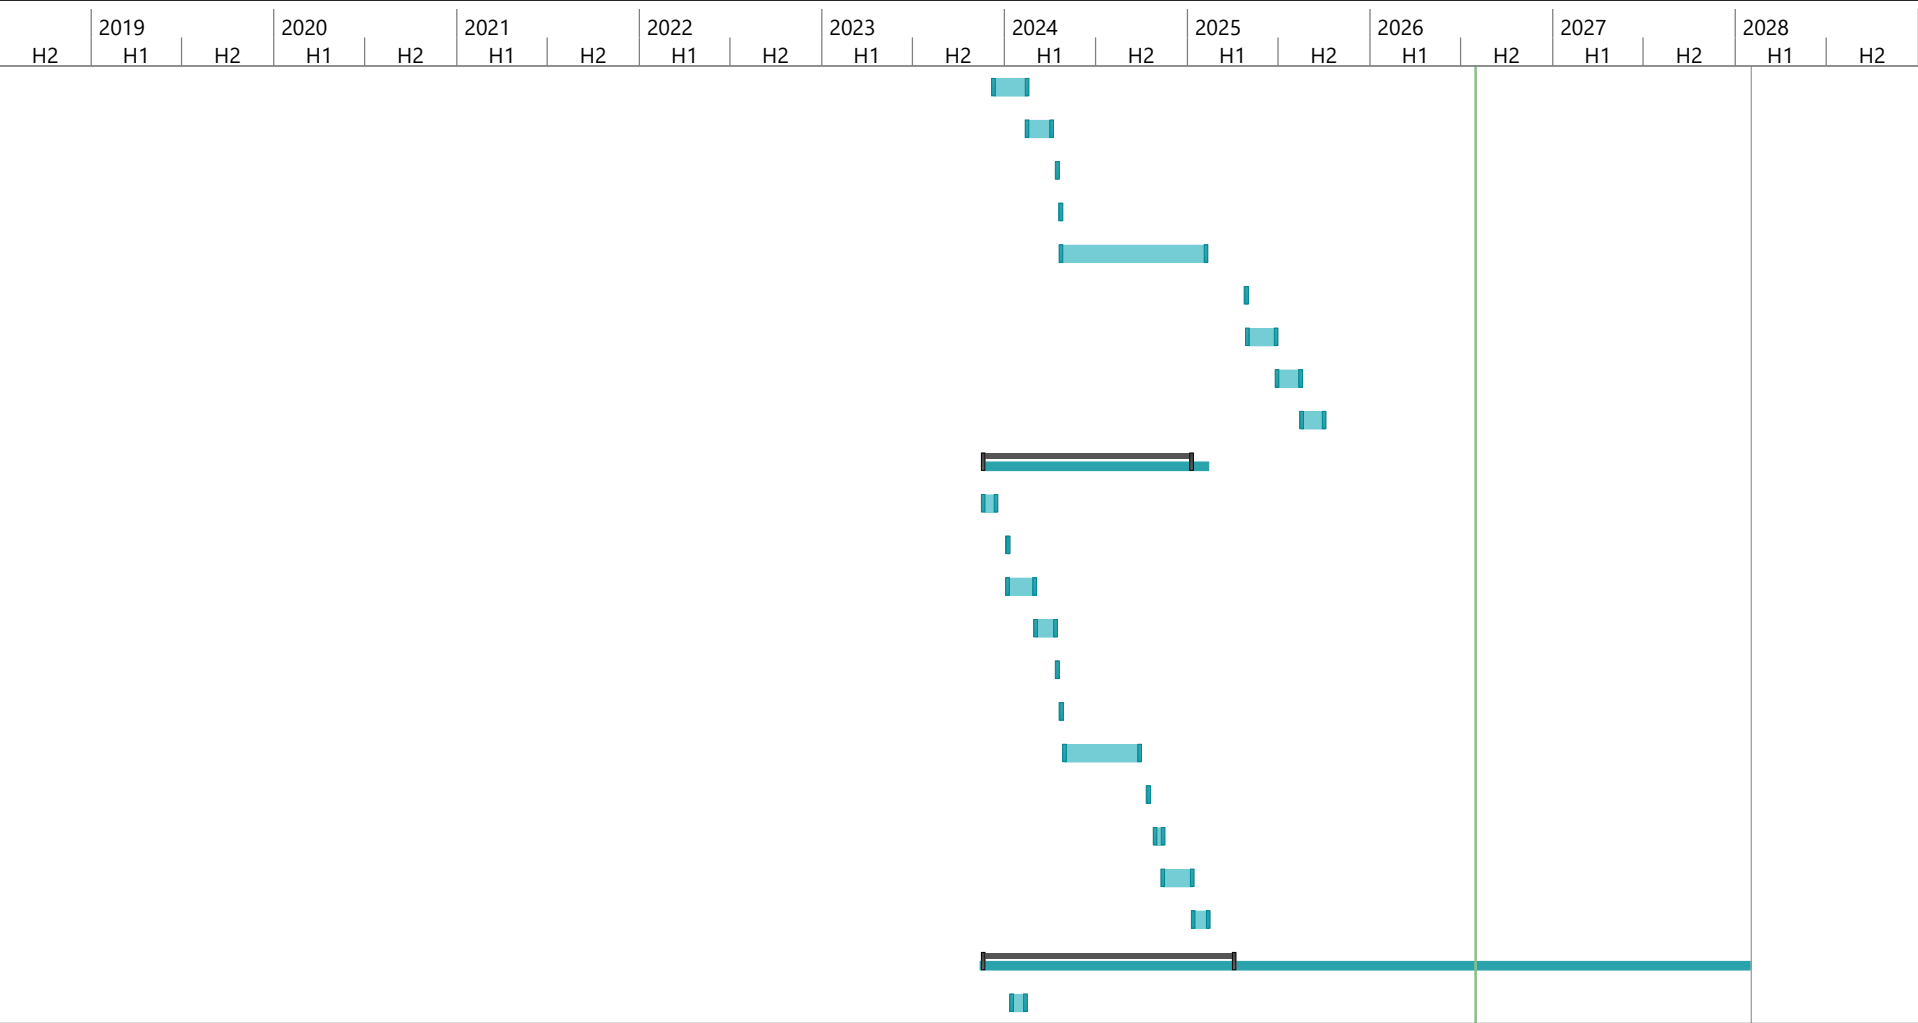
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



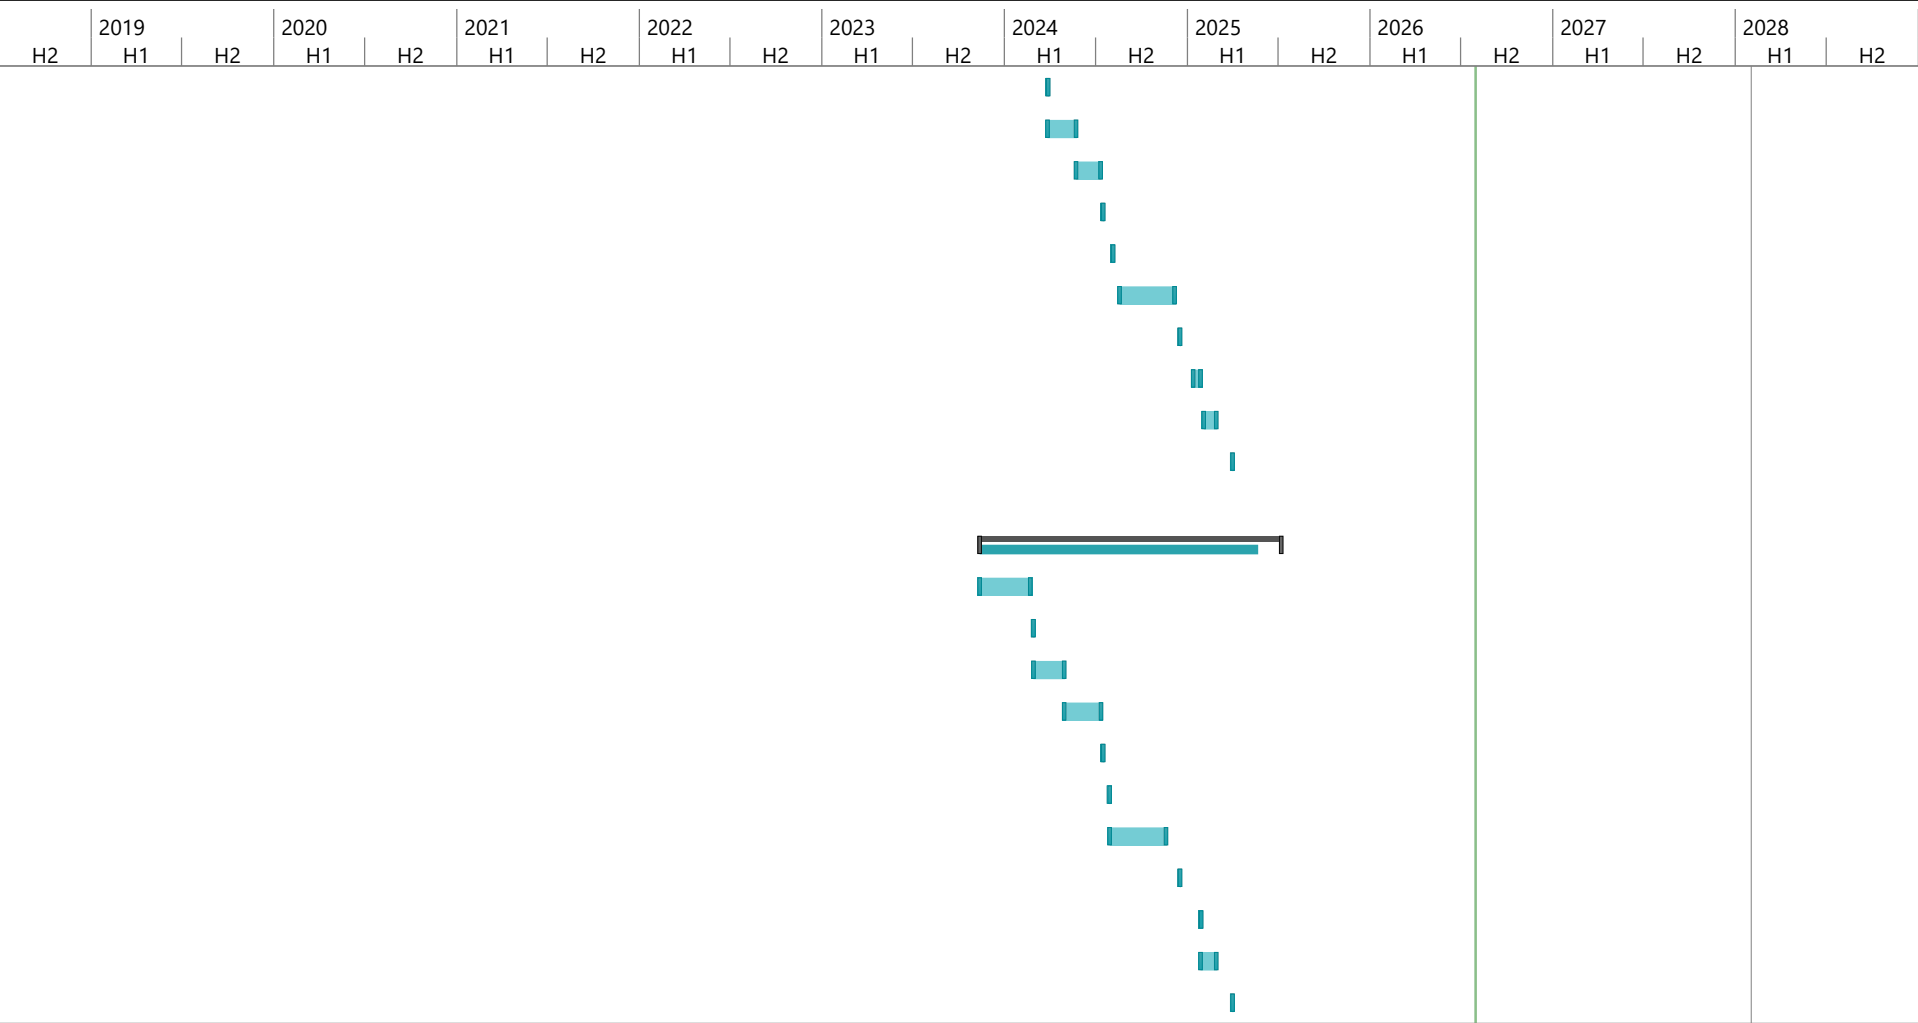
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



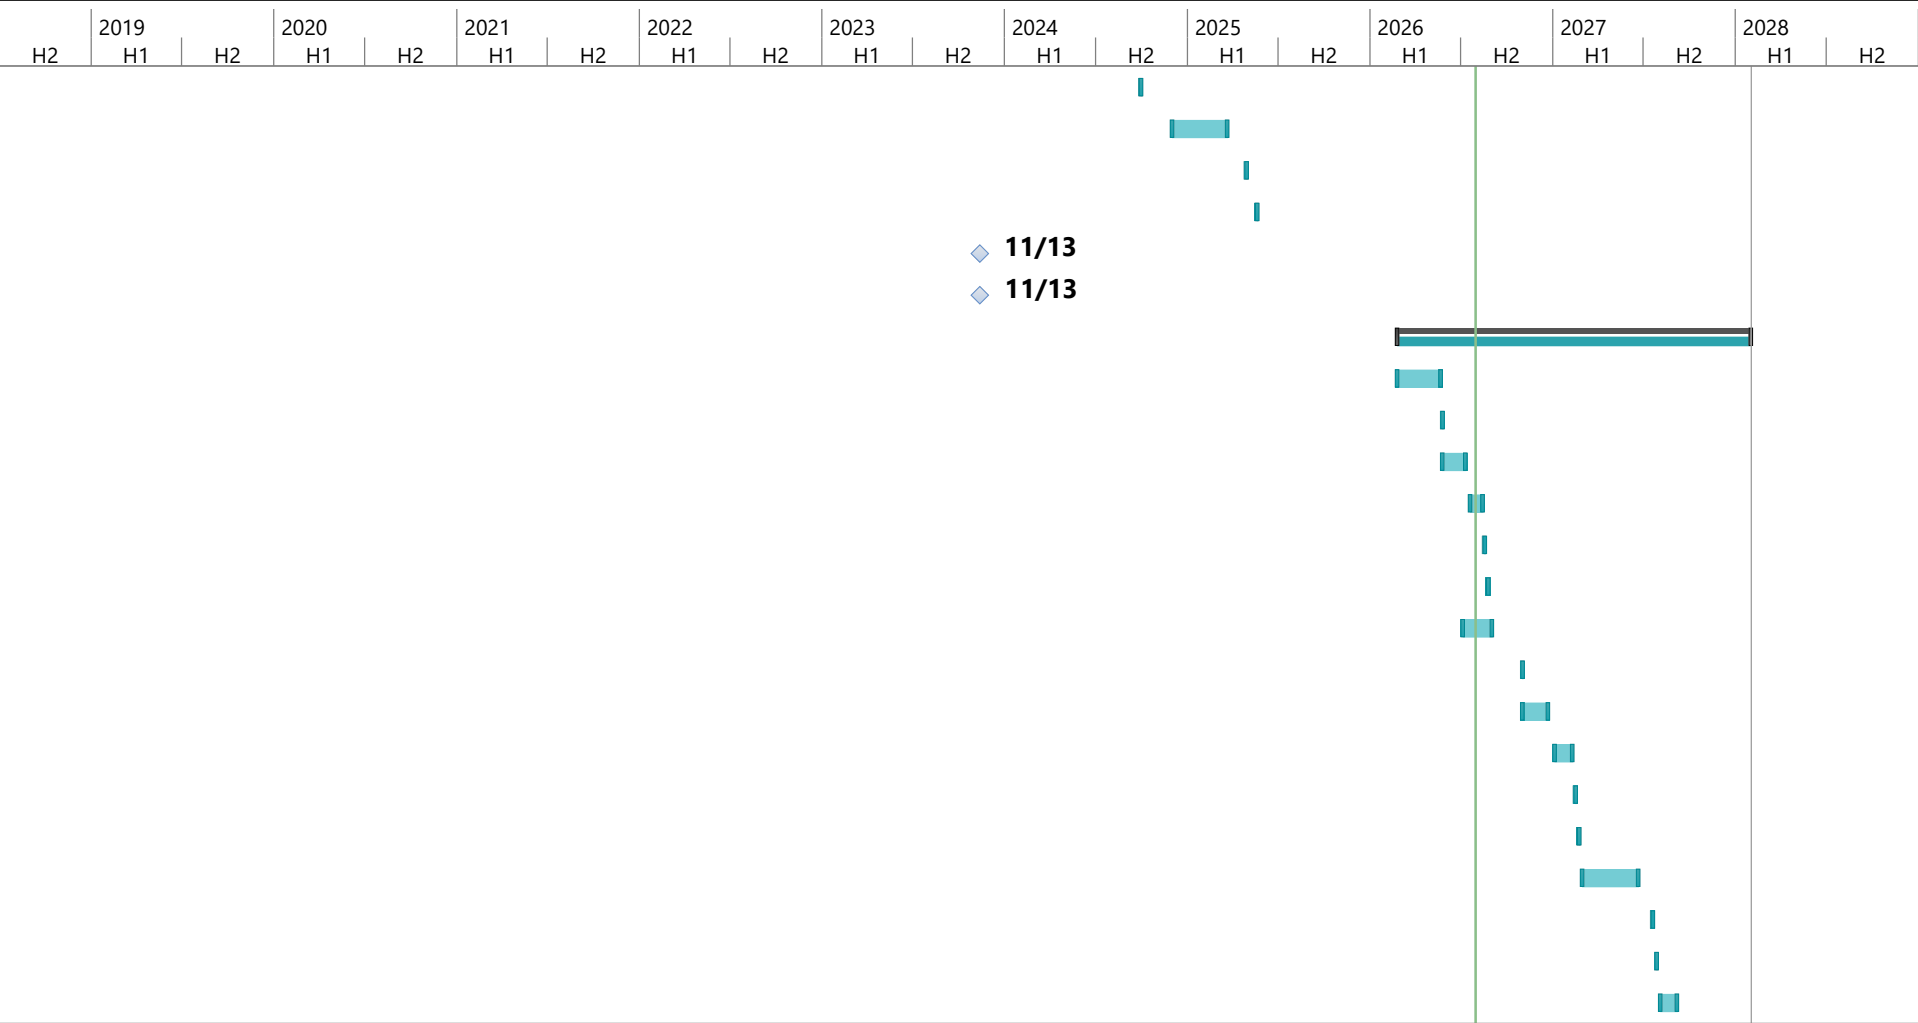
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



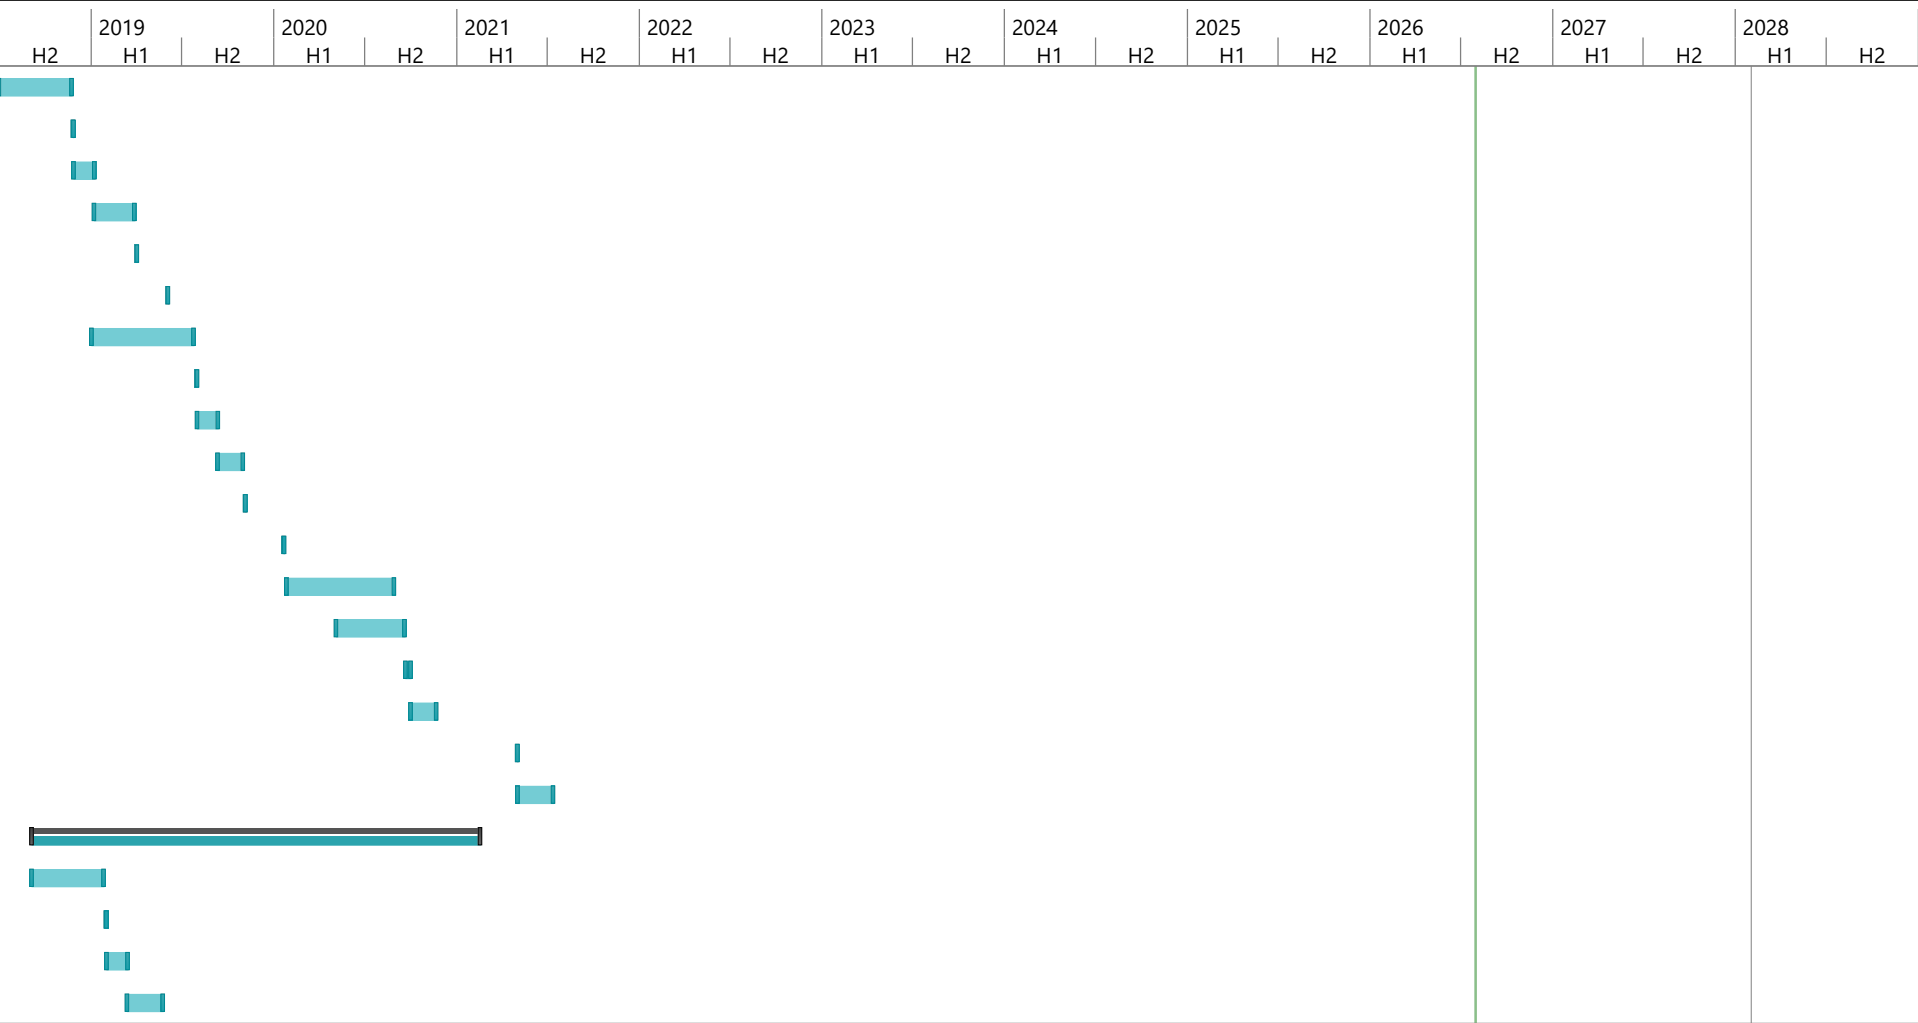
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



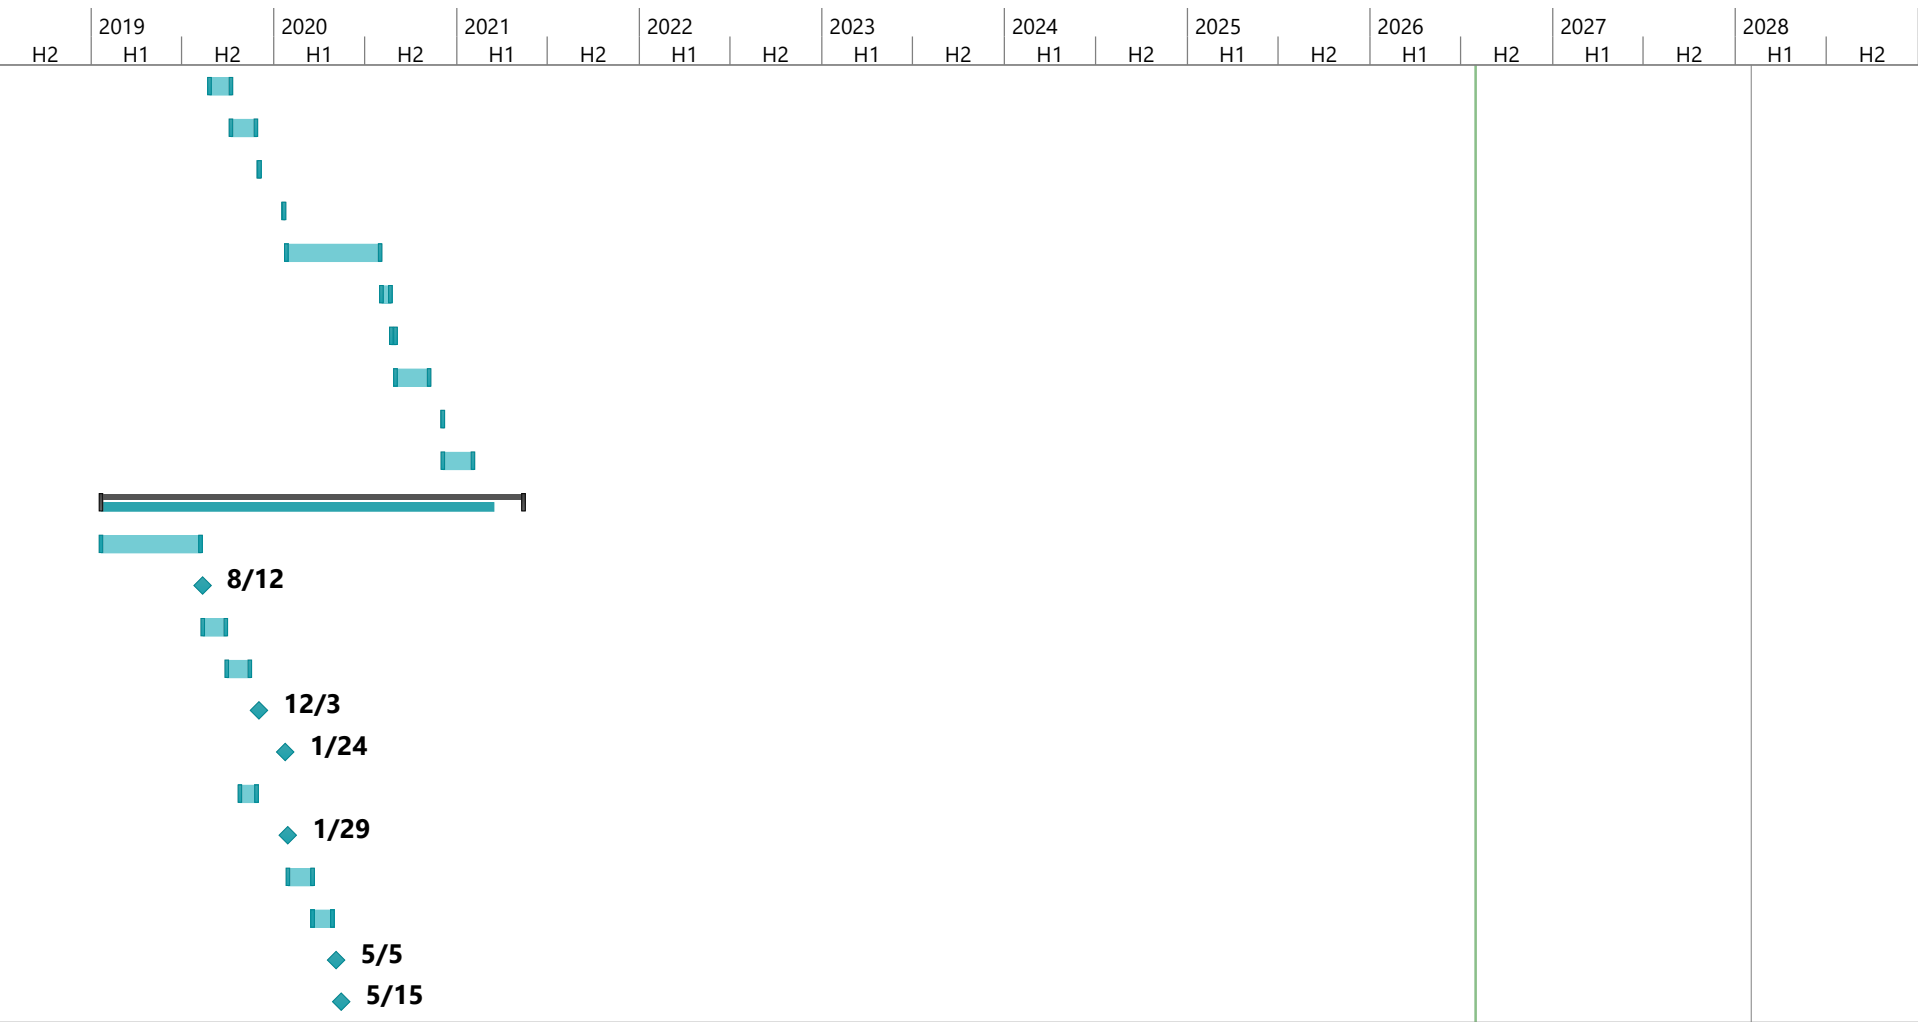
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



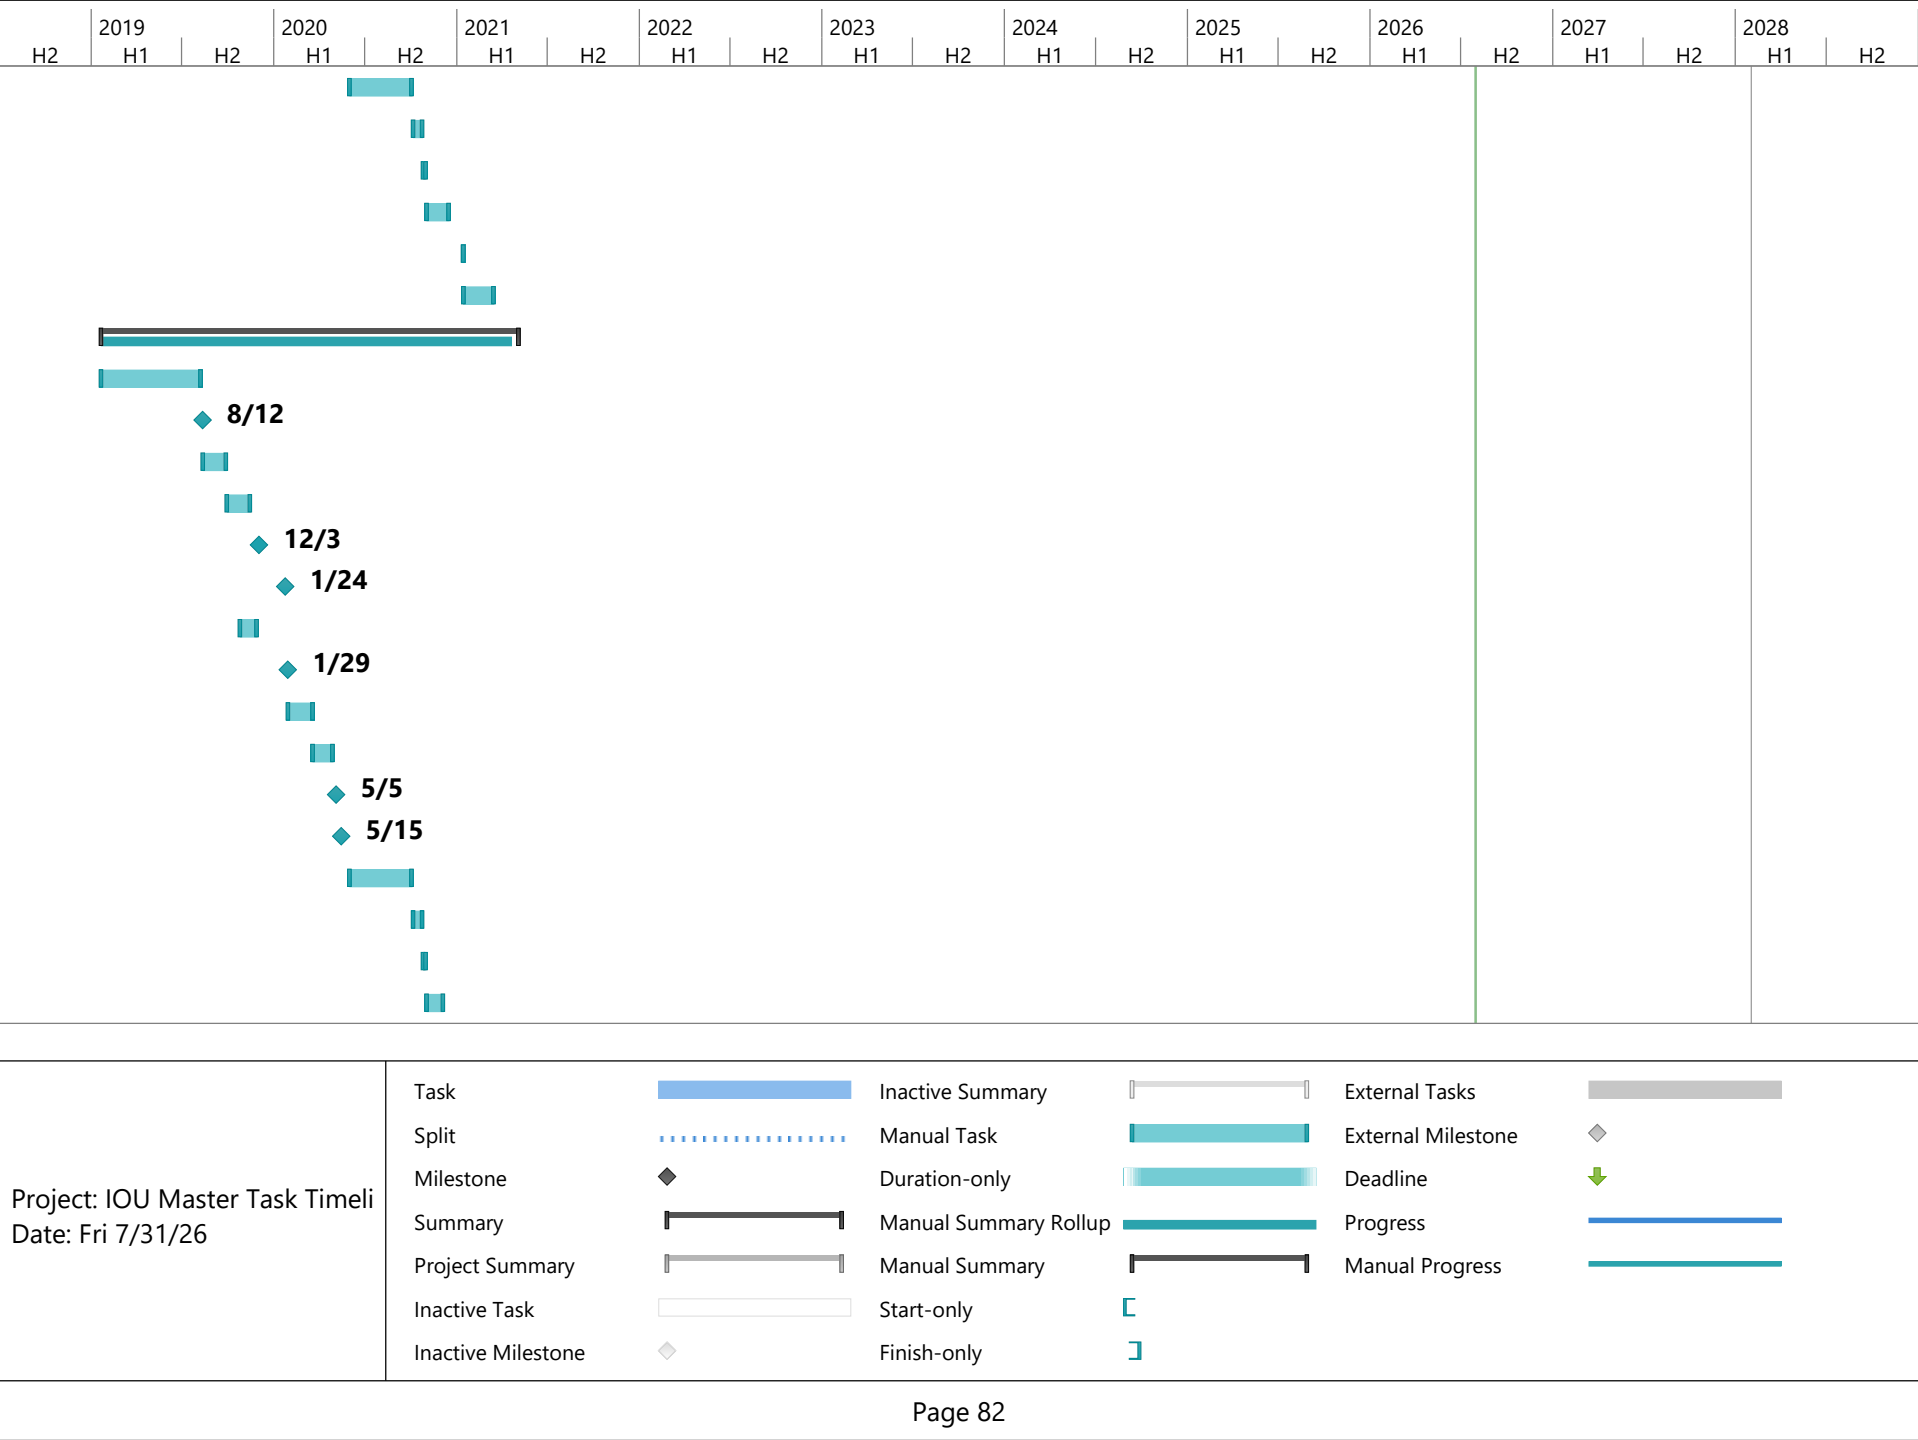
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

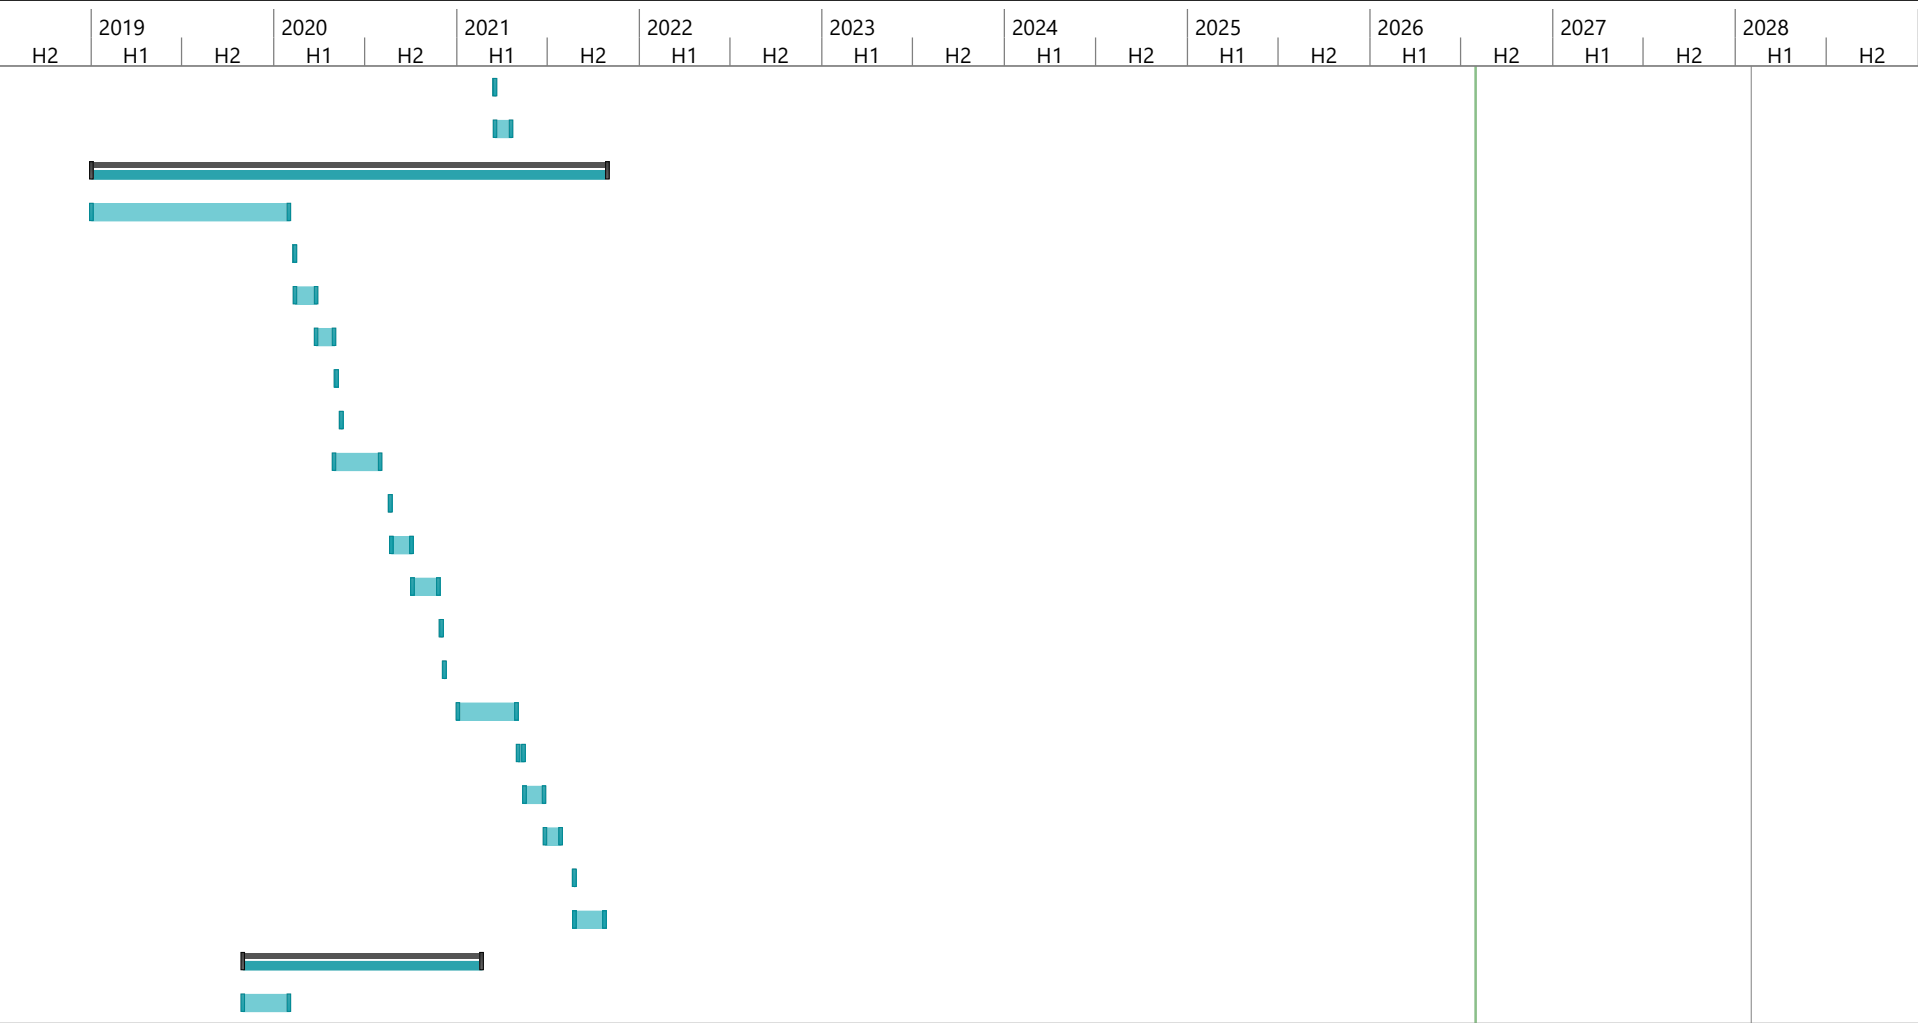


Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

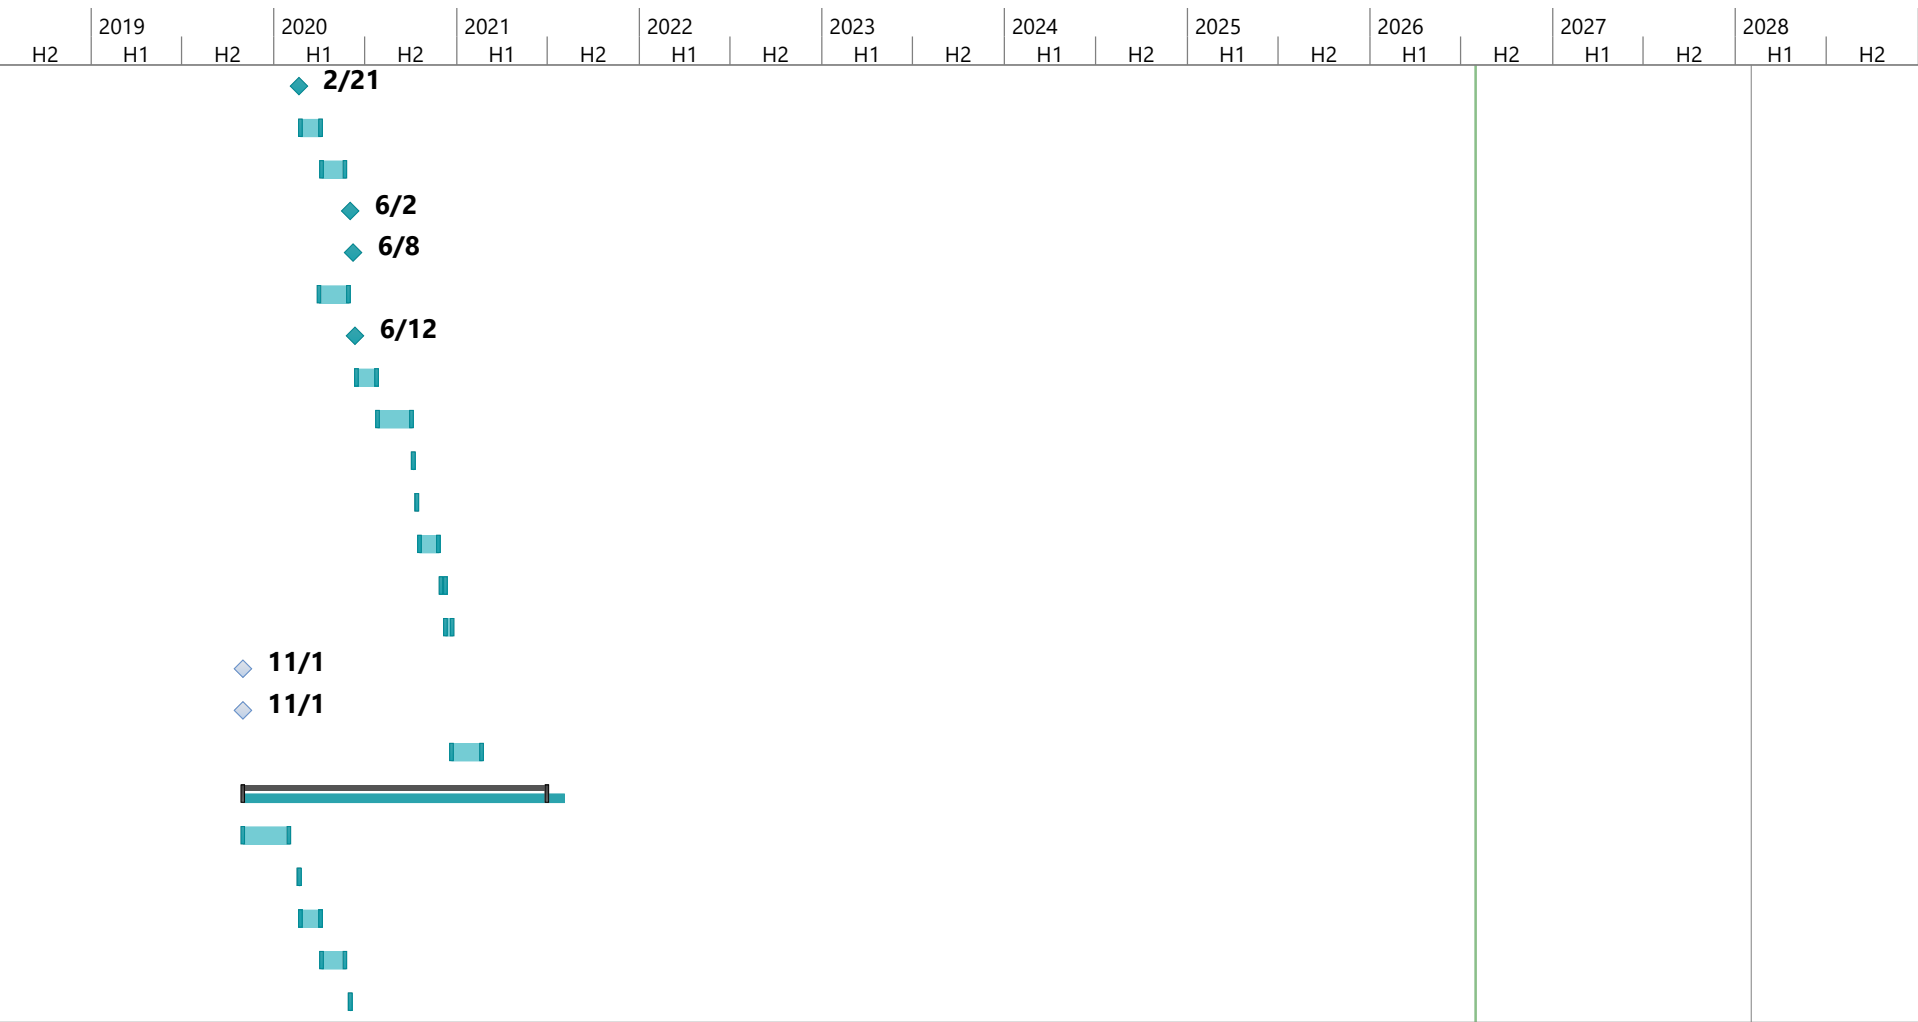


Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

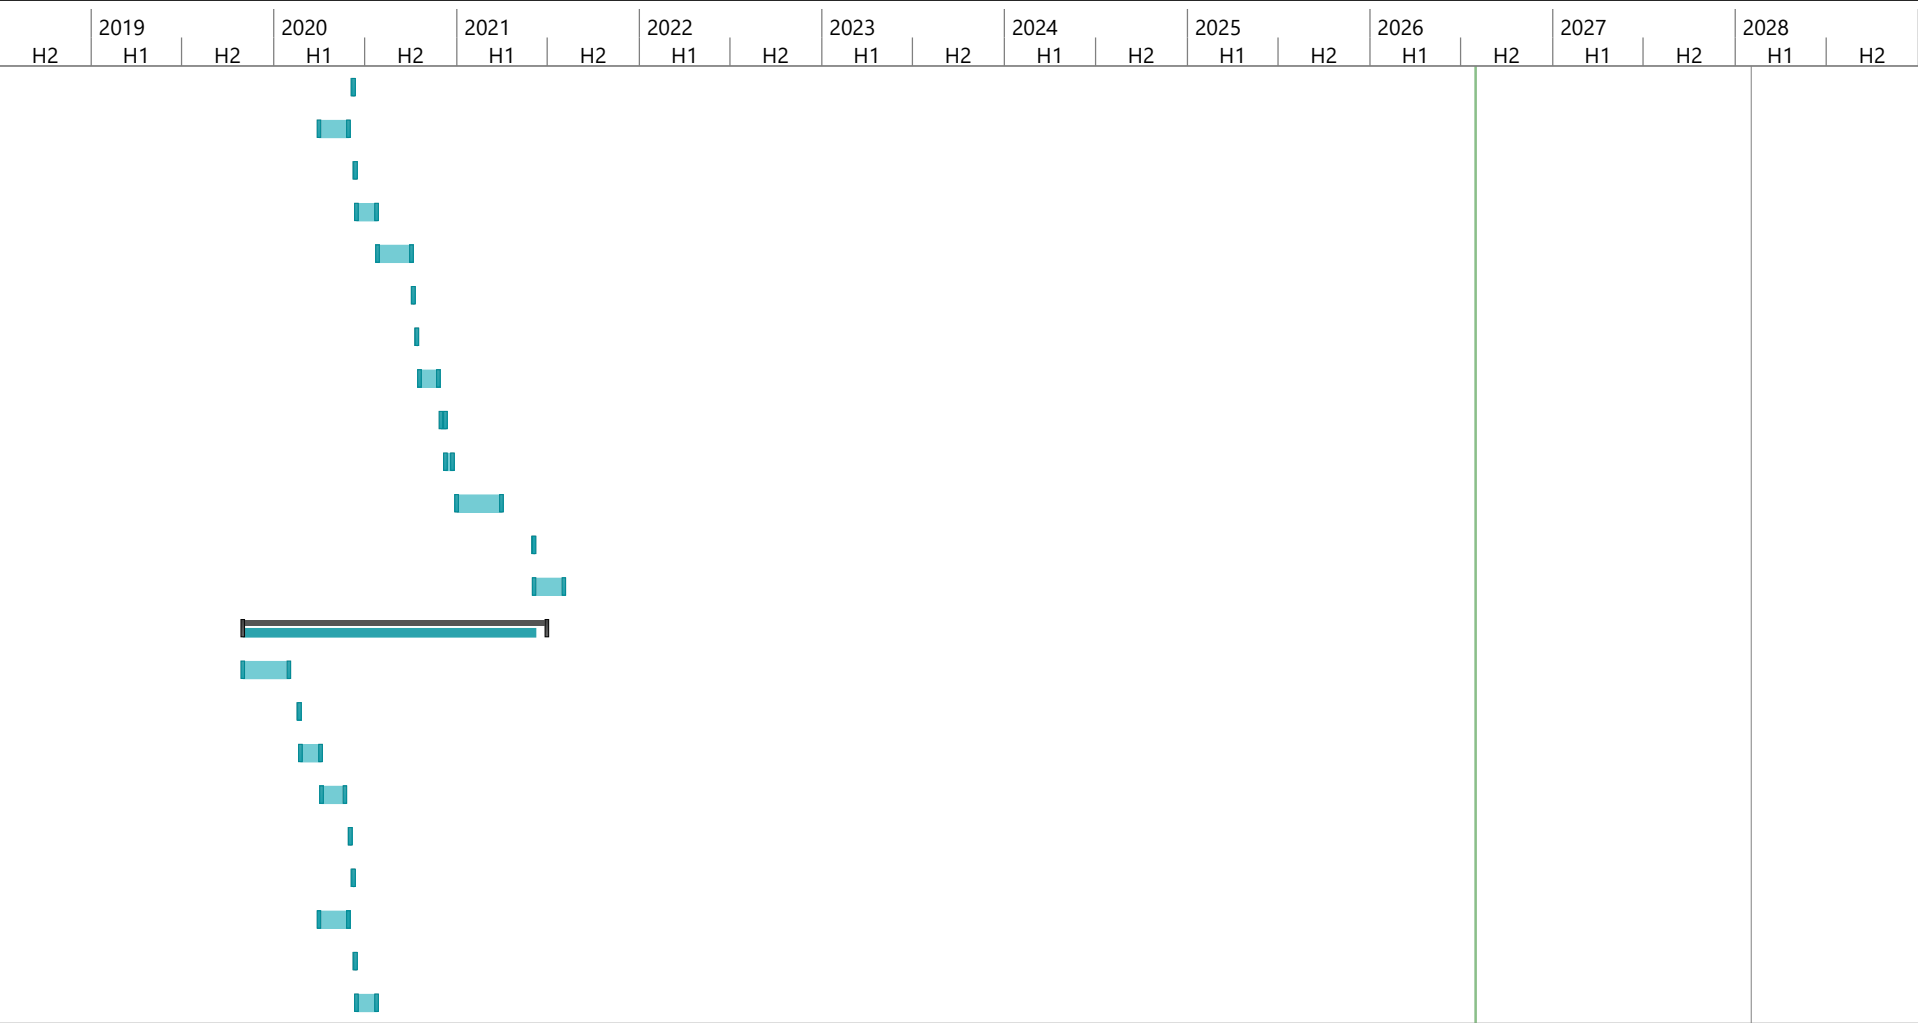




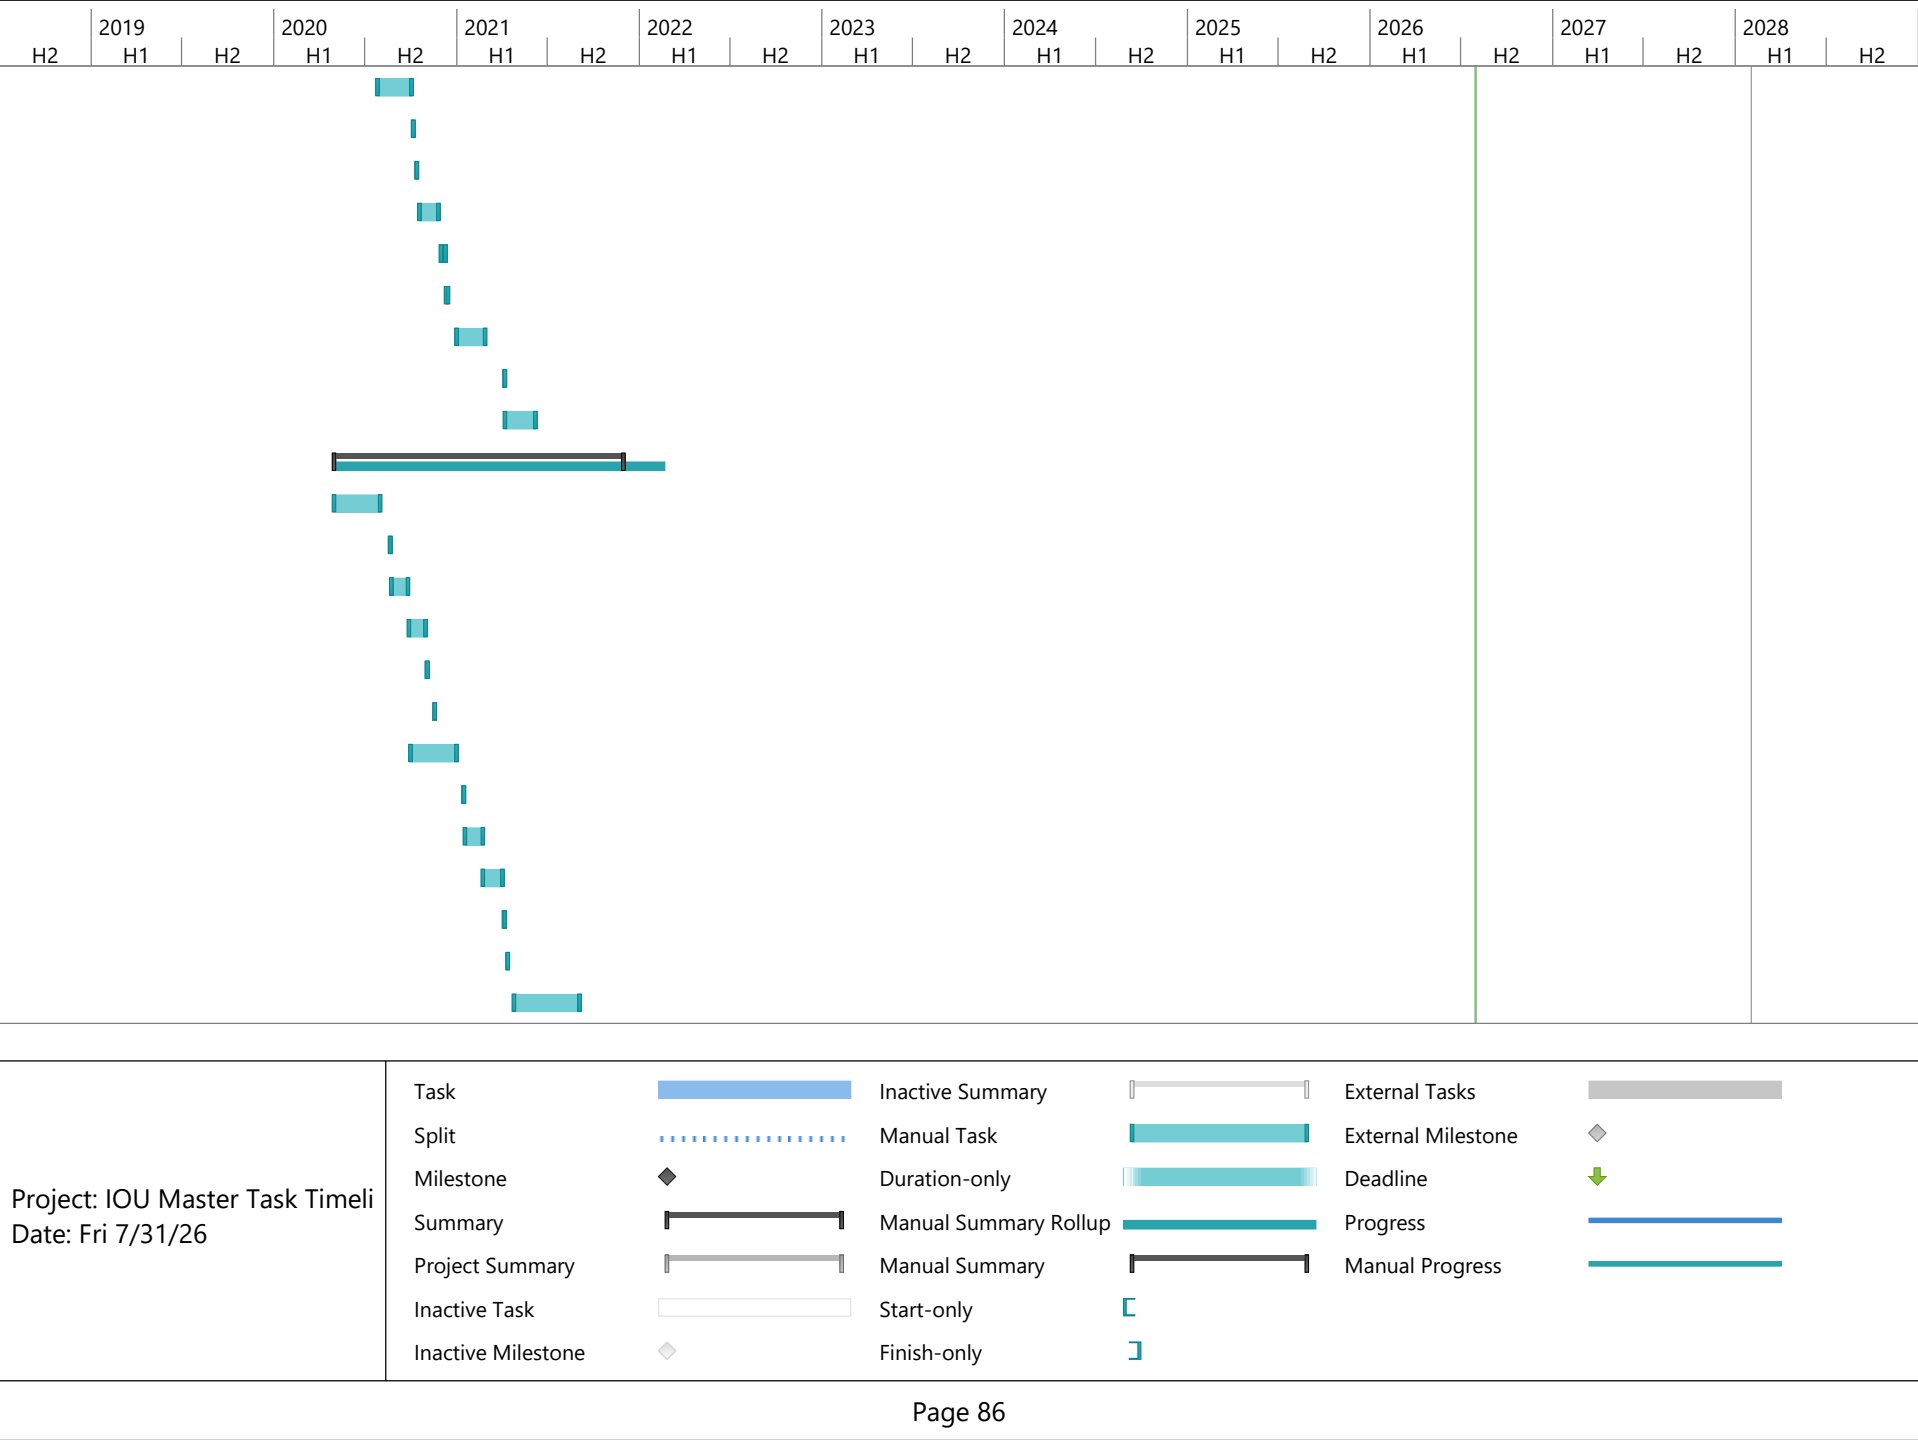
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

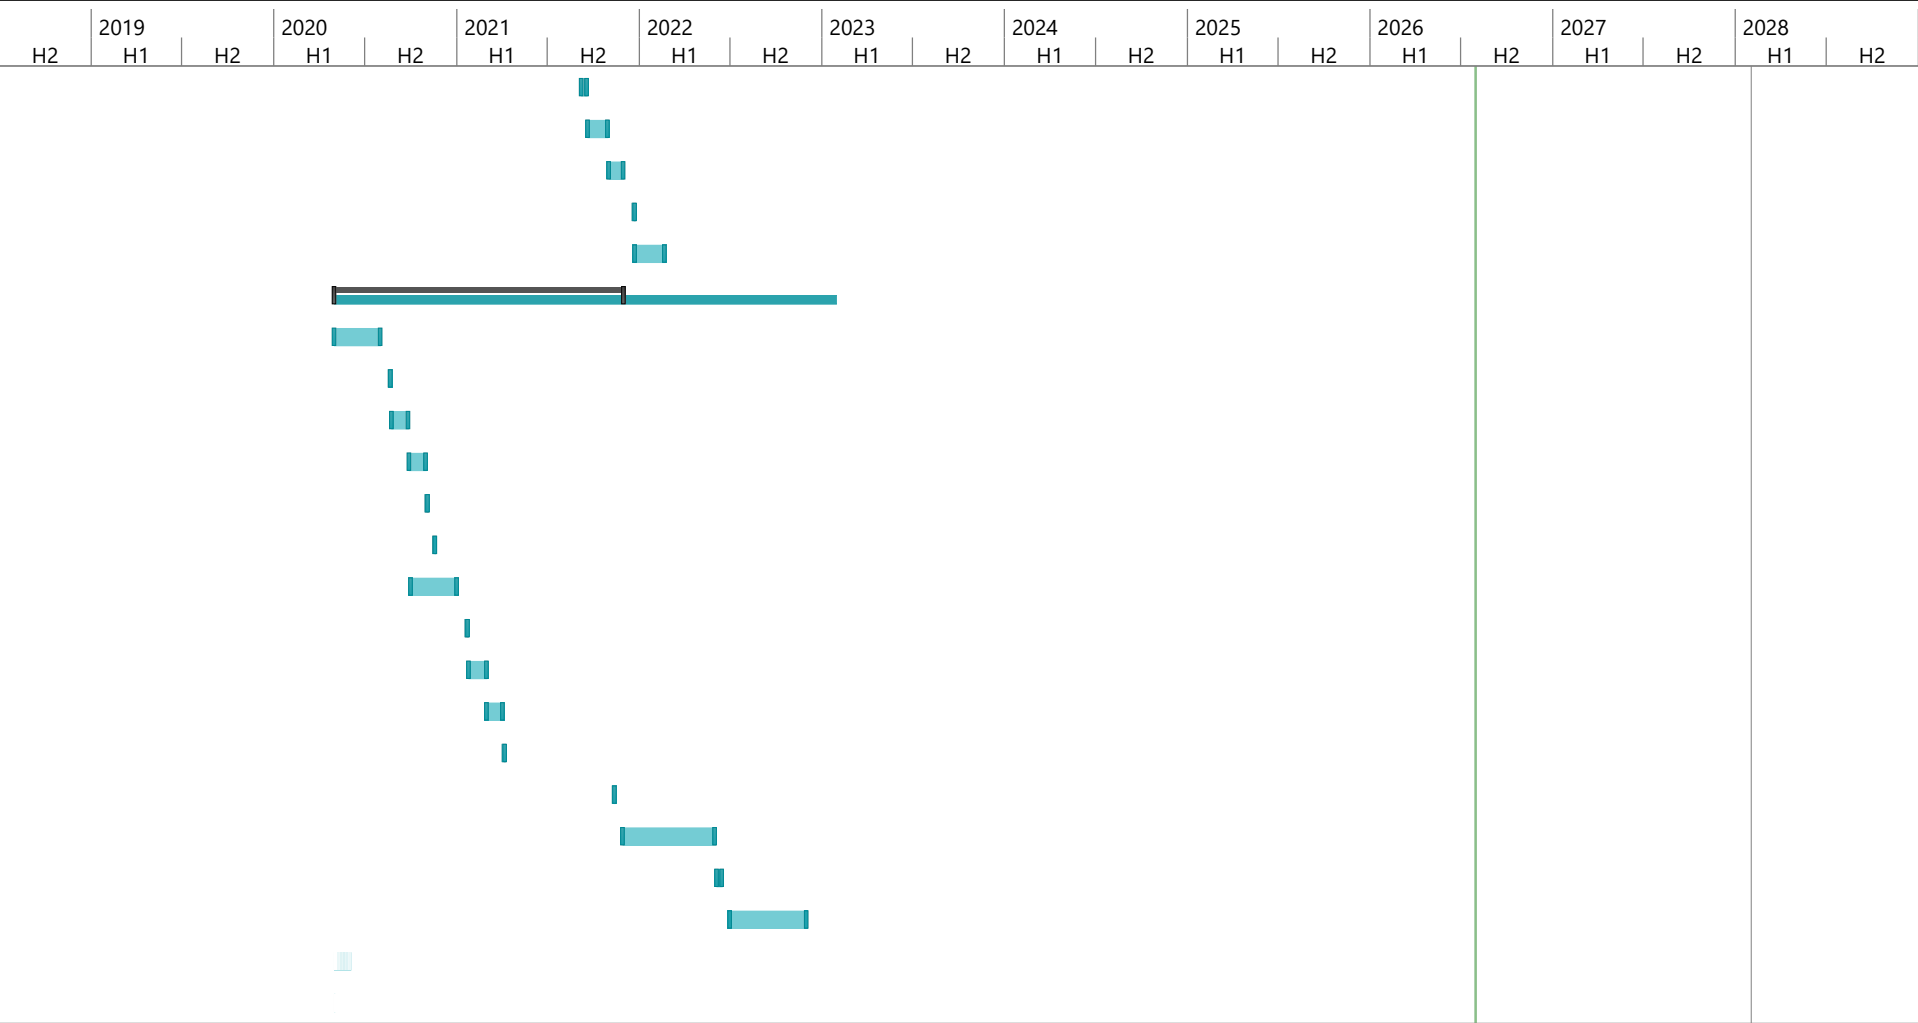


Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

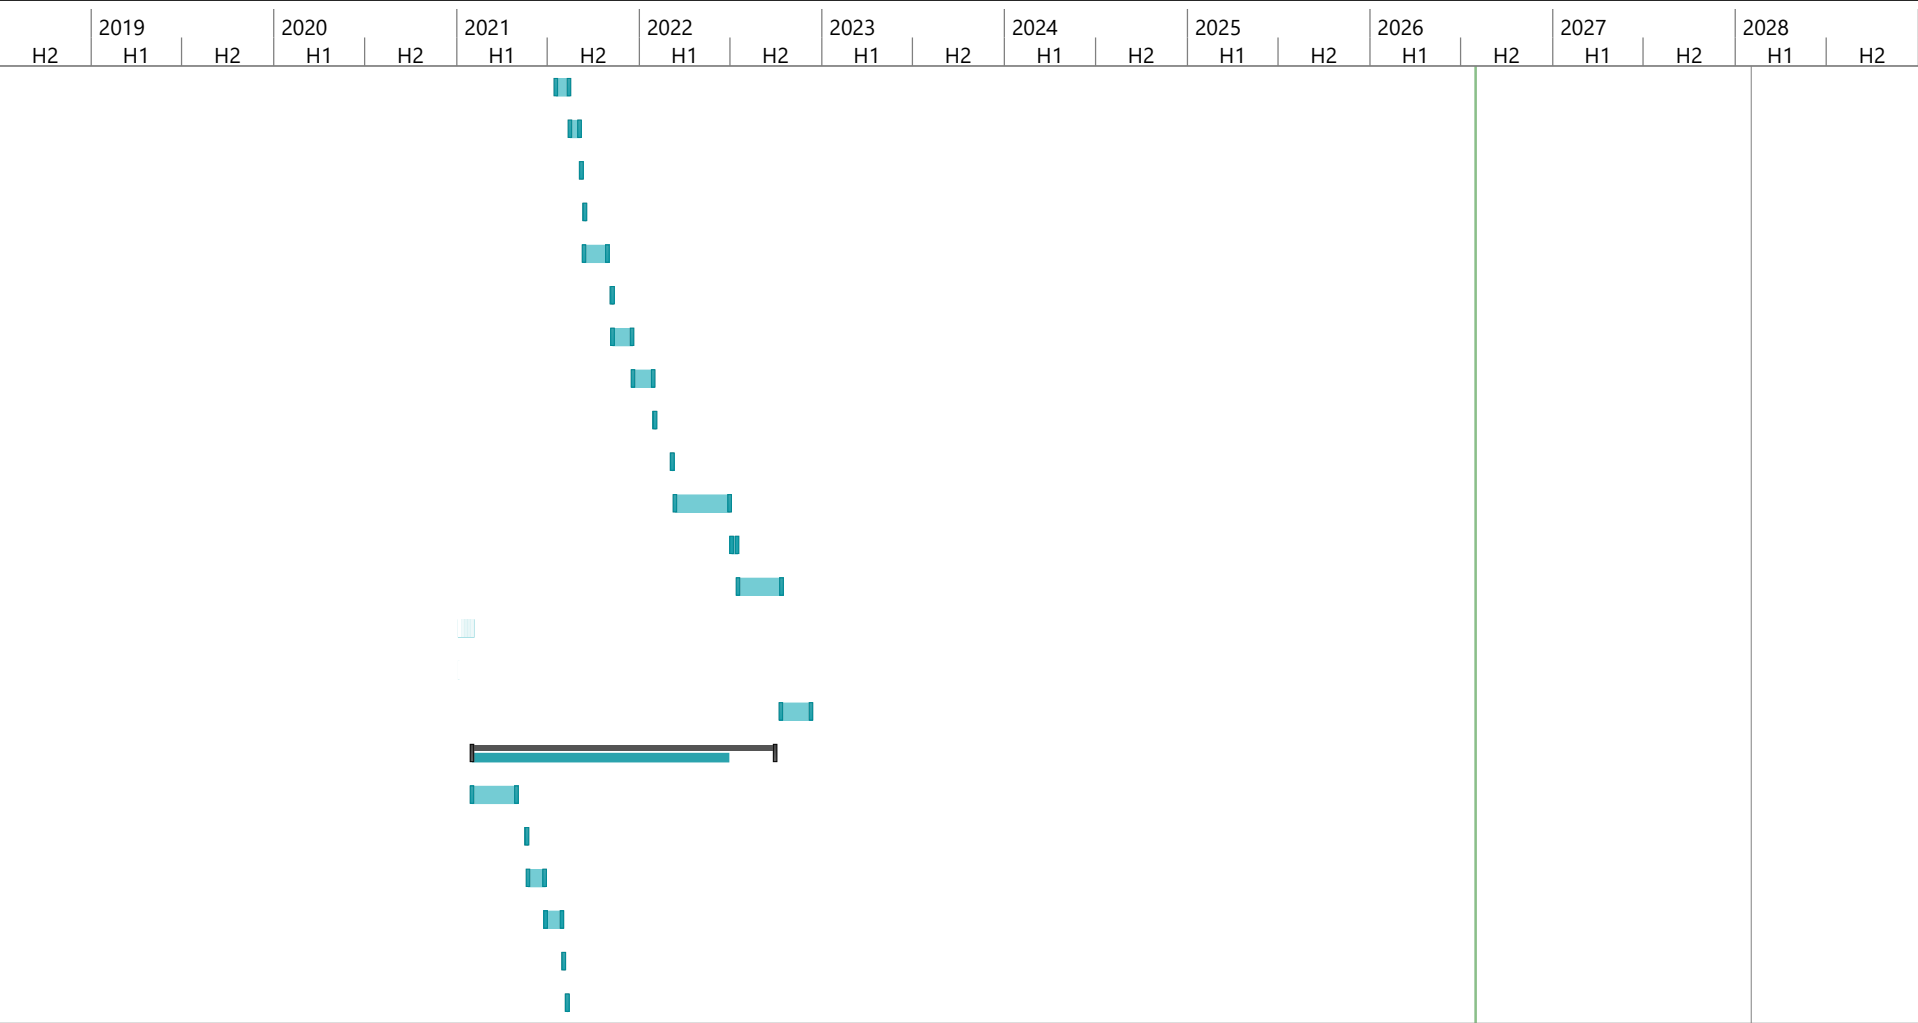


Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			





Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

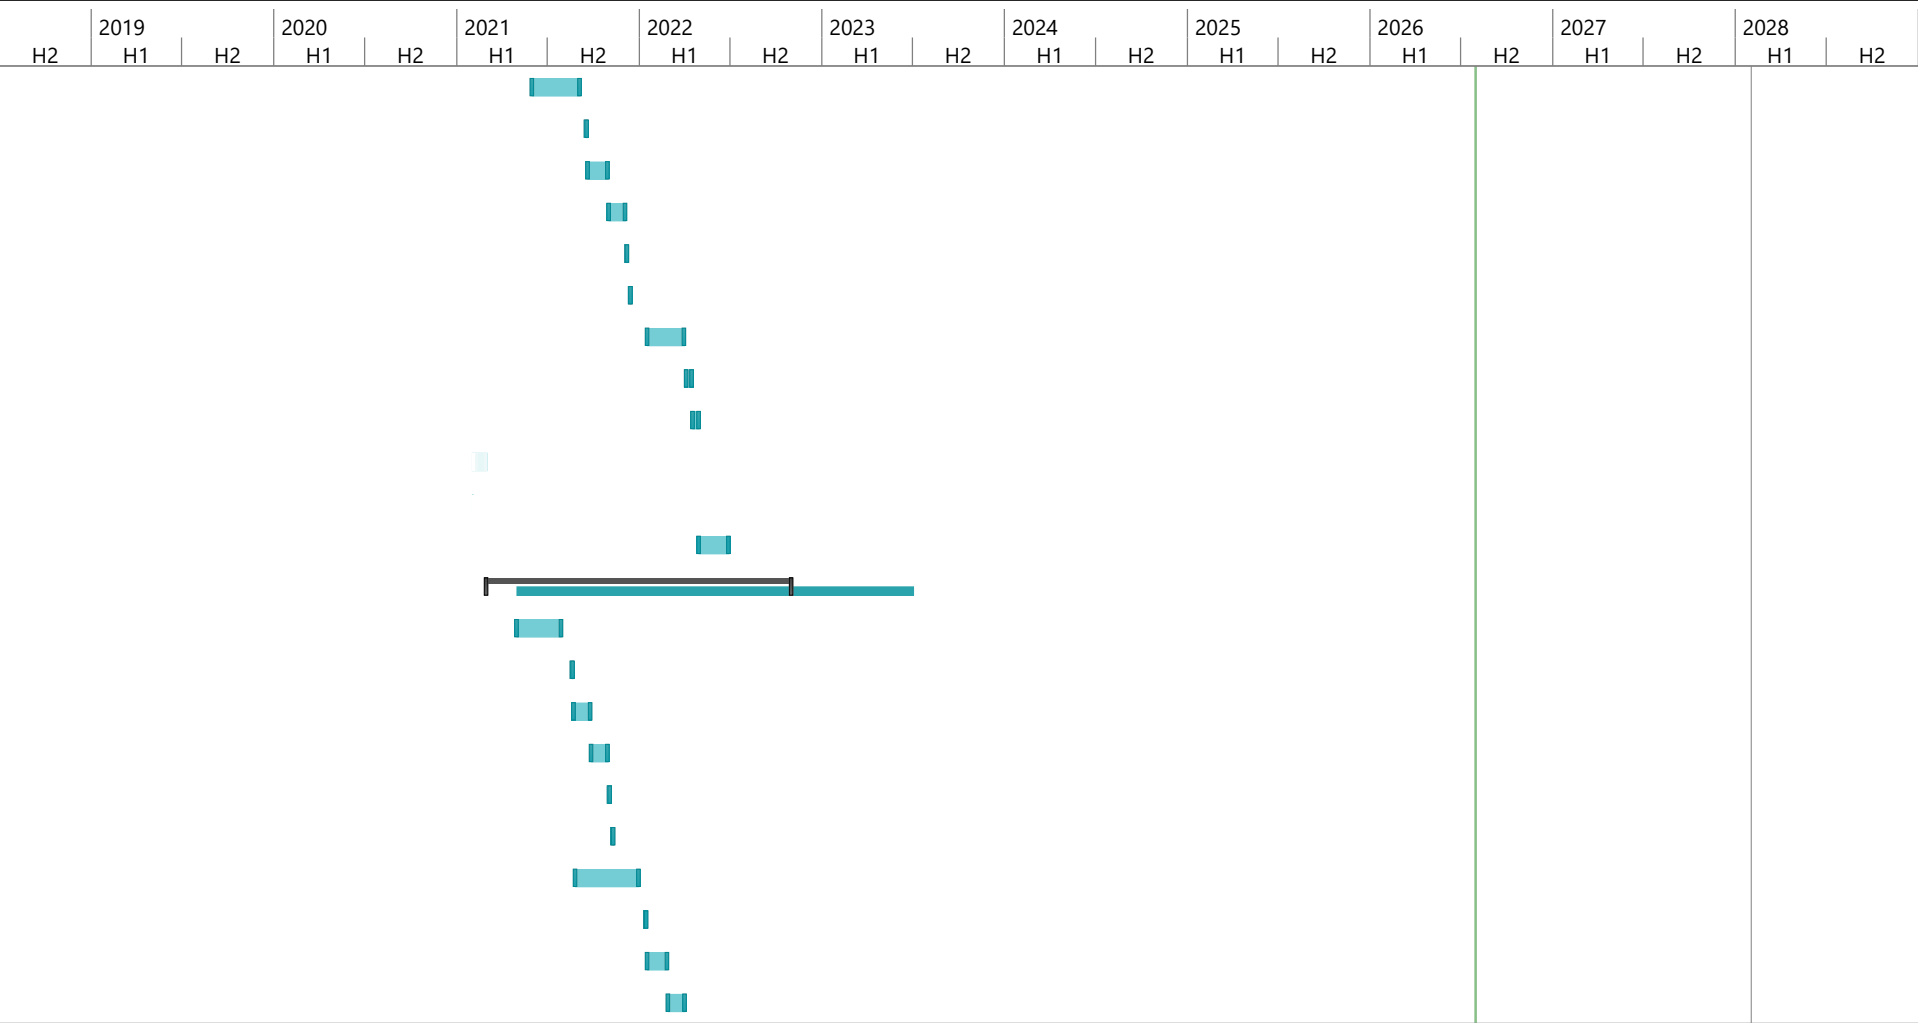
External Milestone

Deadline

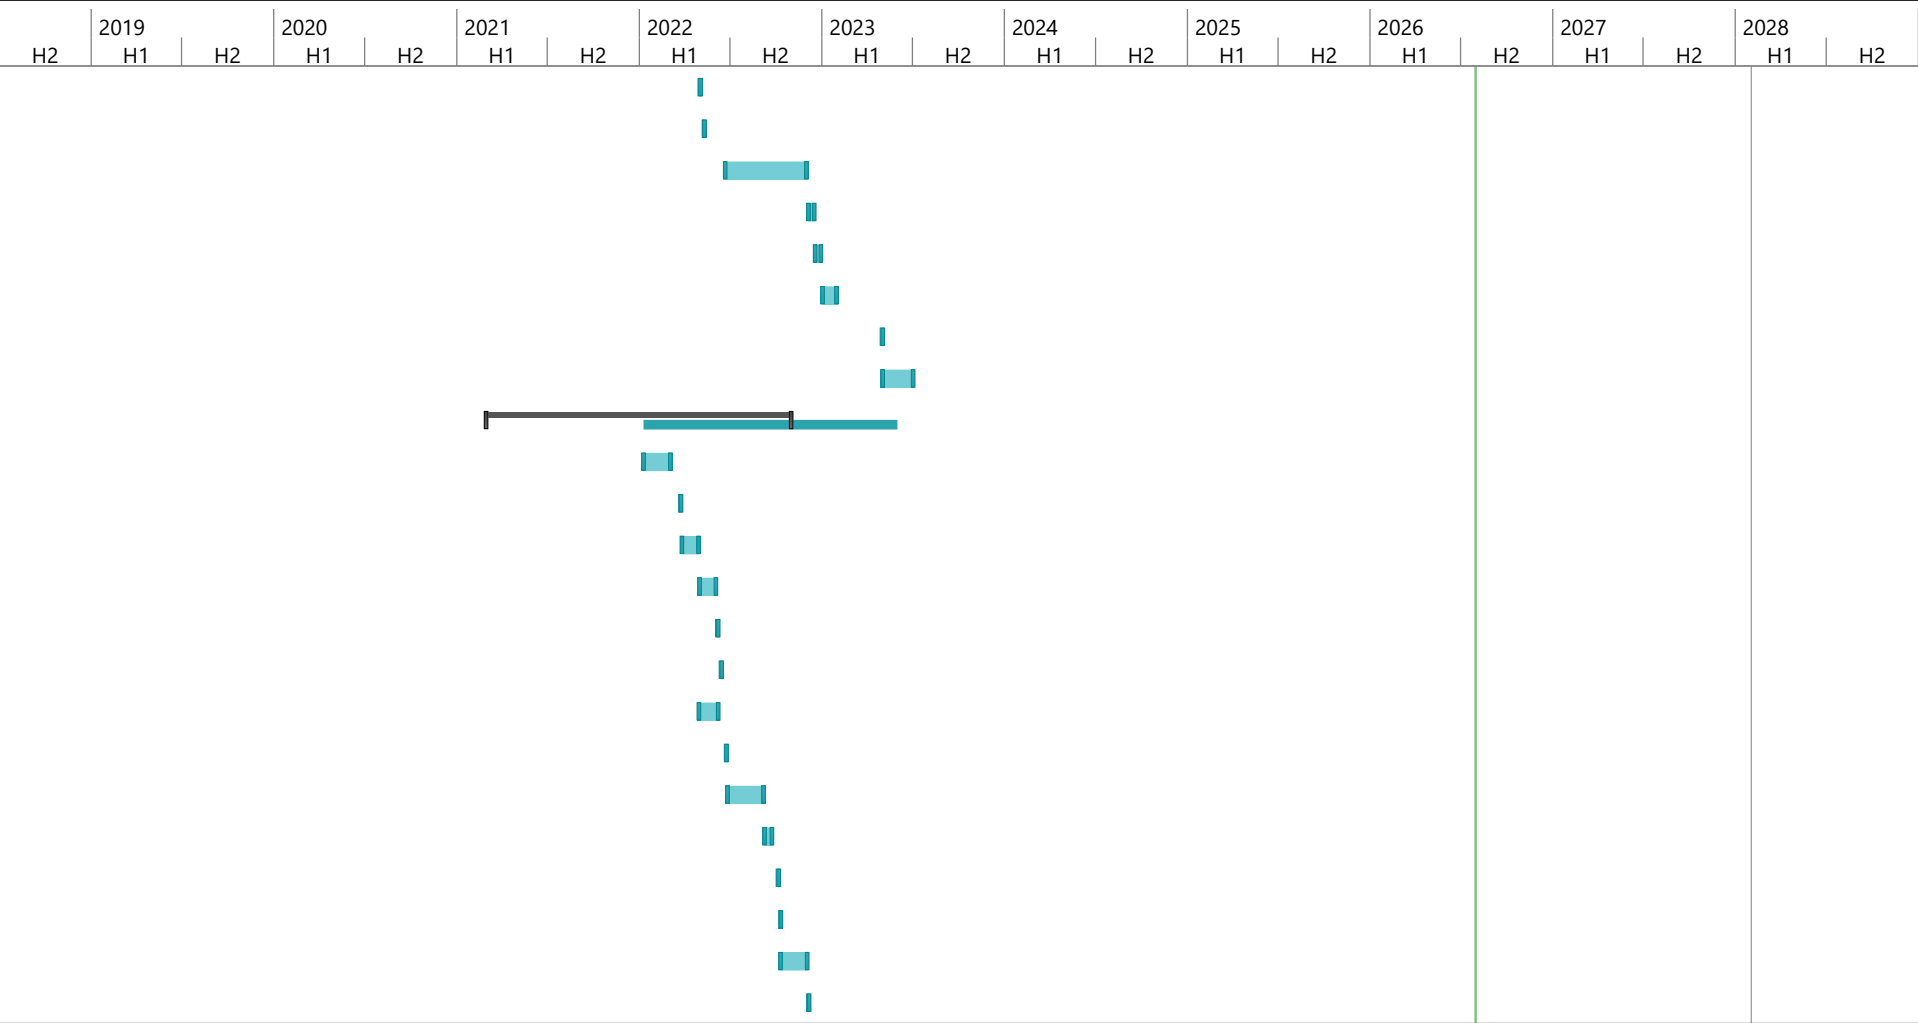
Progress

Manual Progress

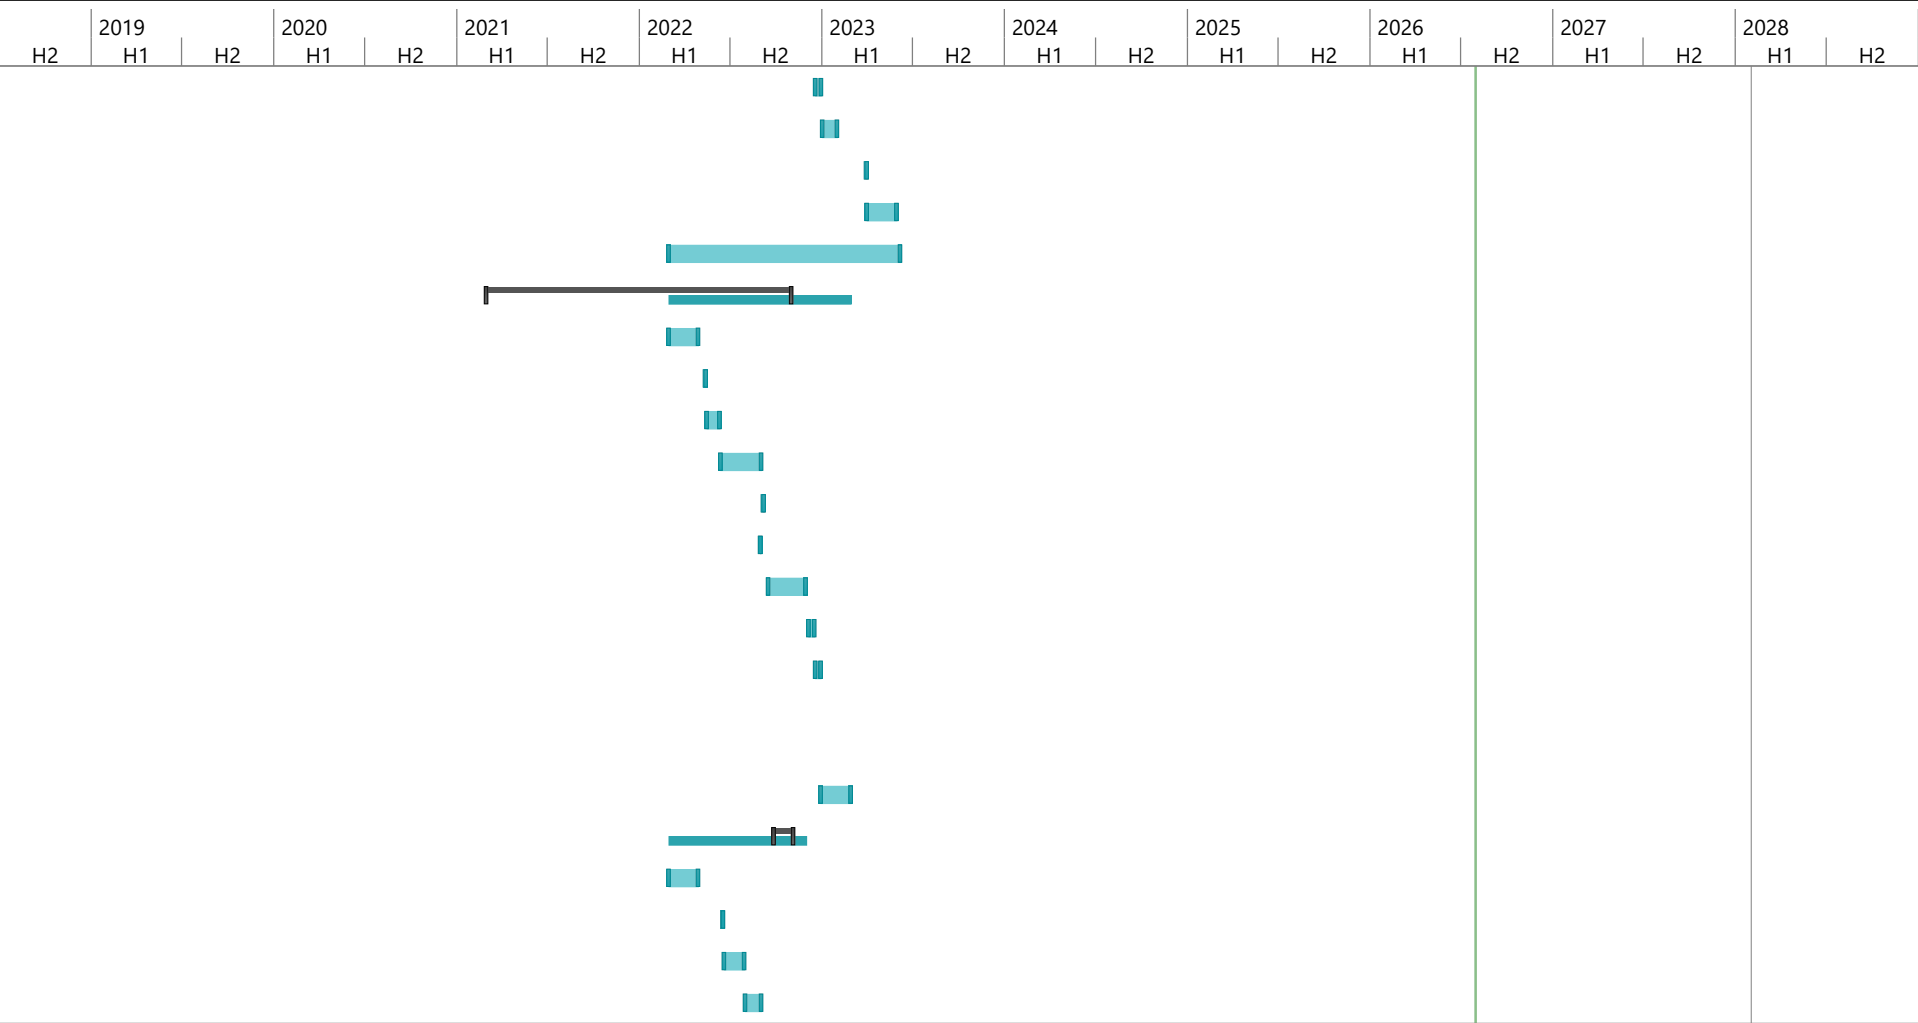
Page 89



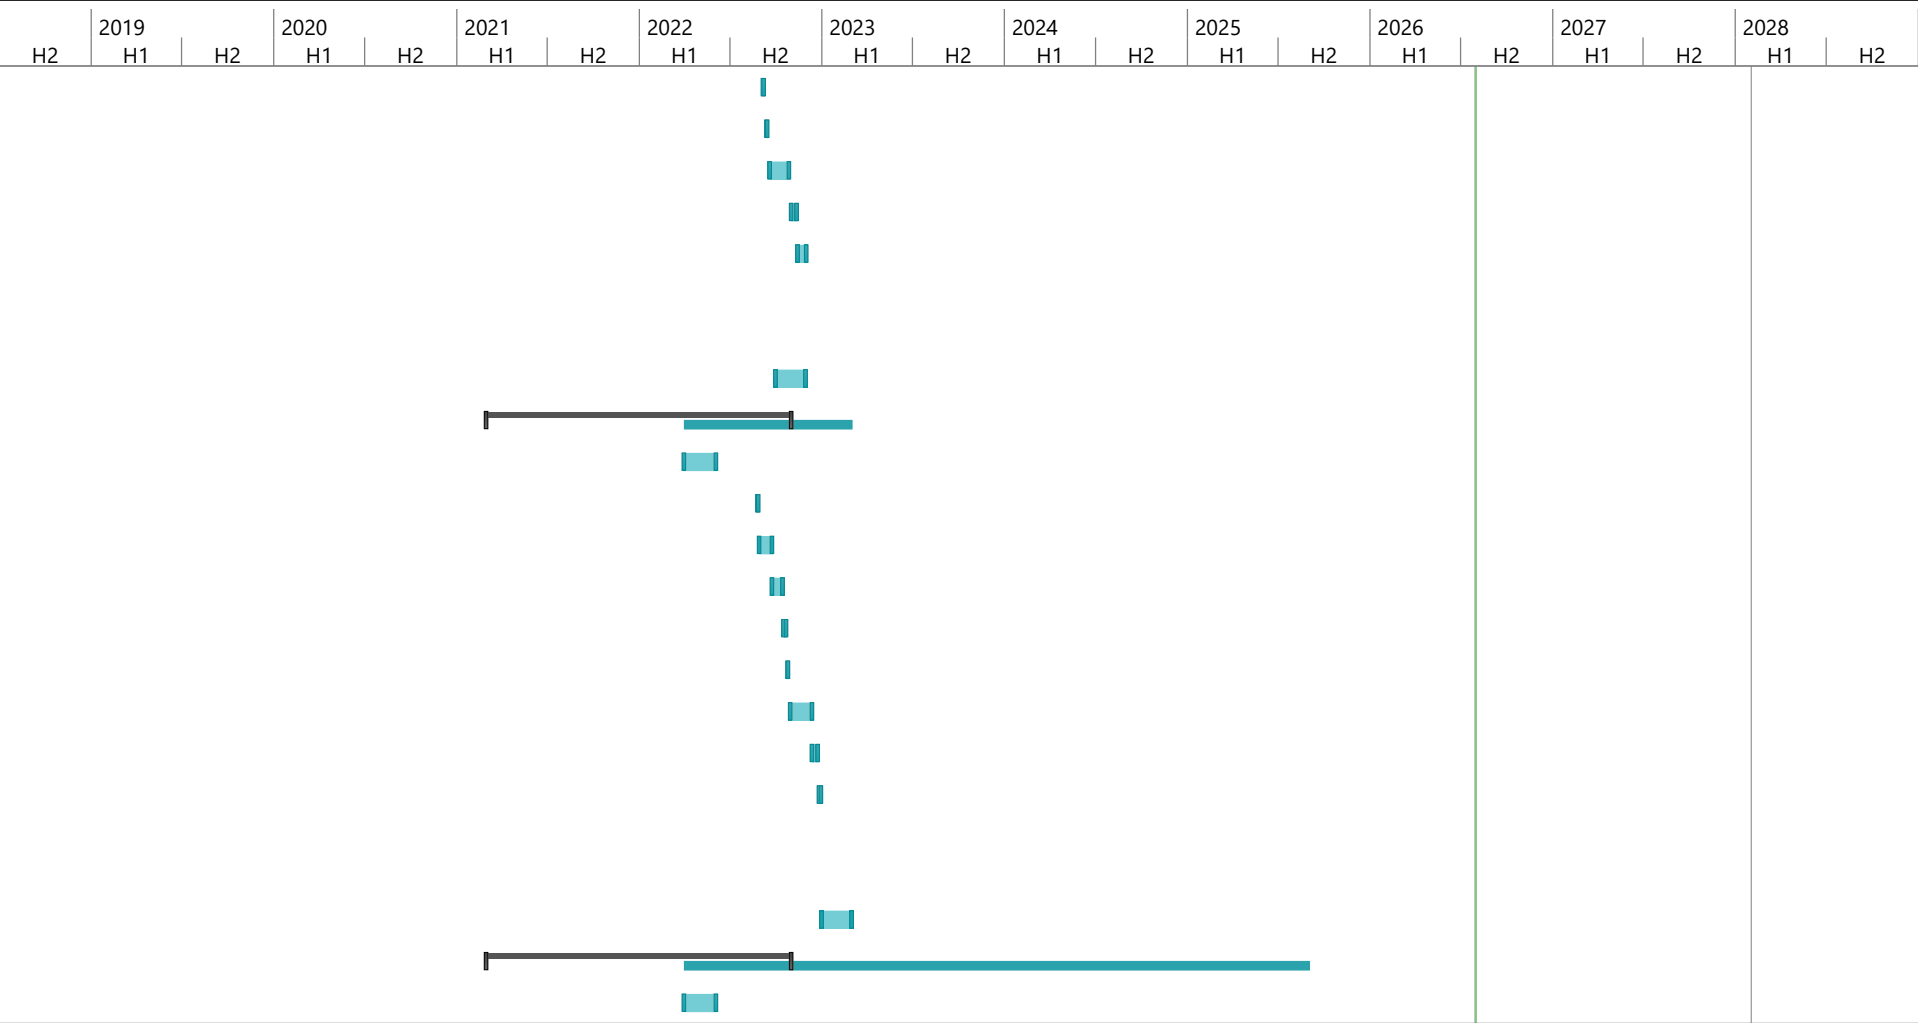
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



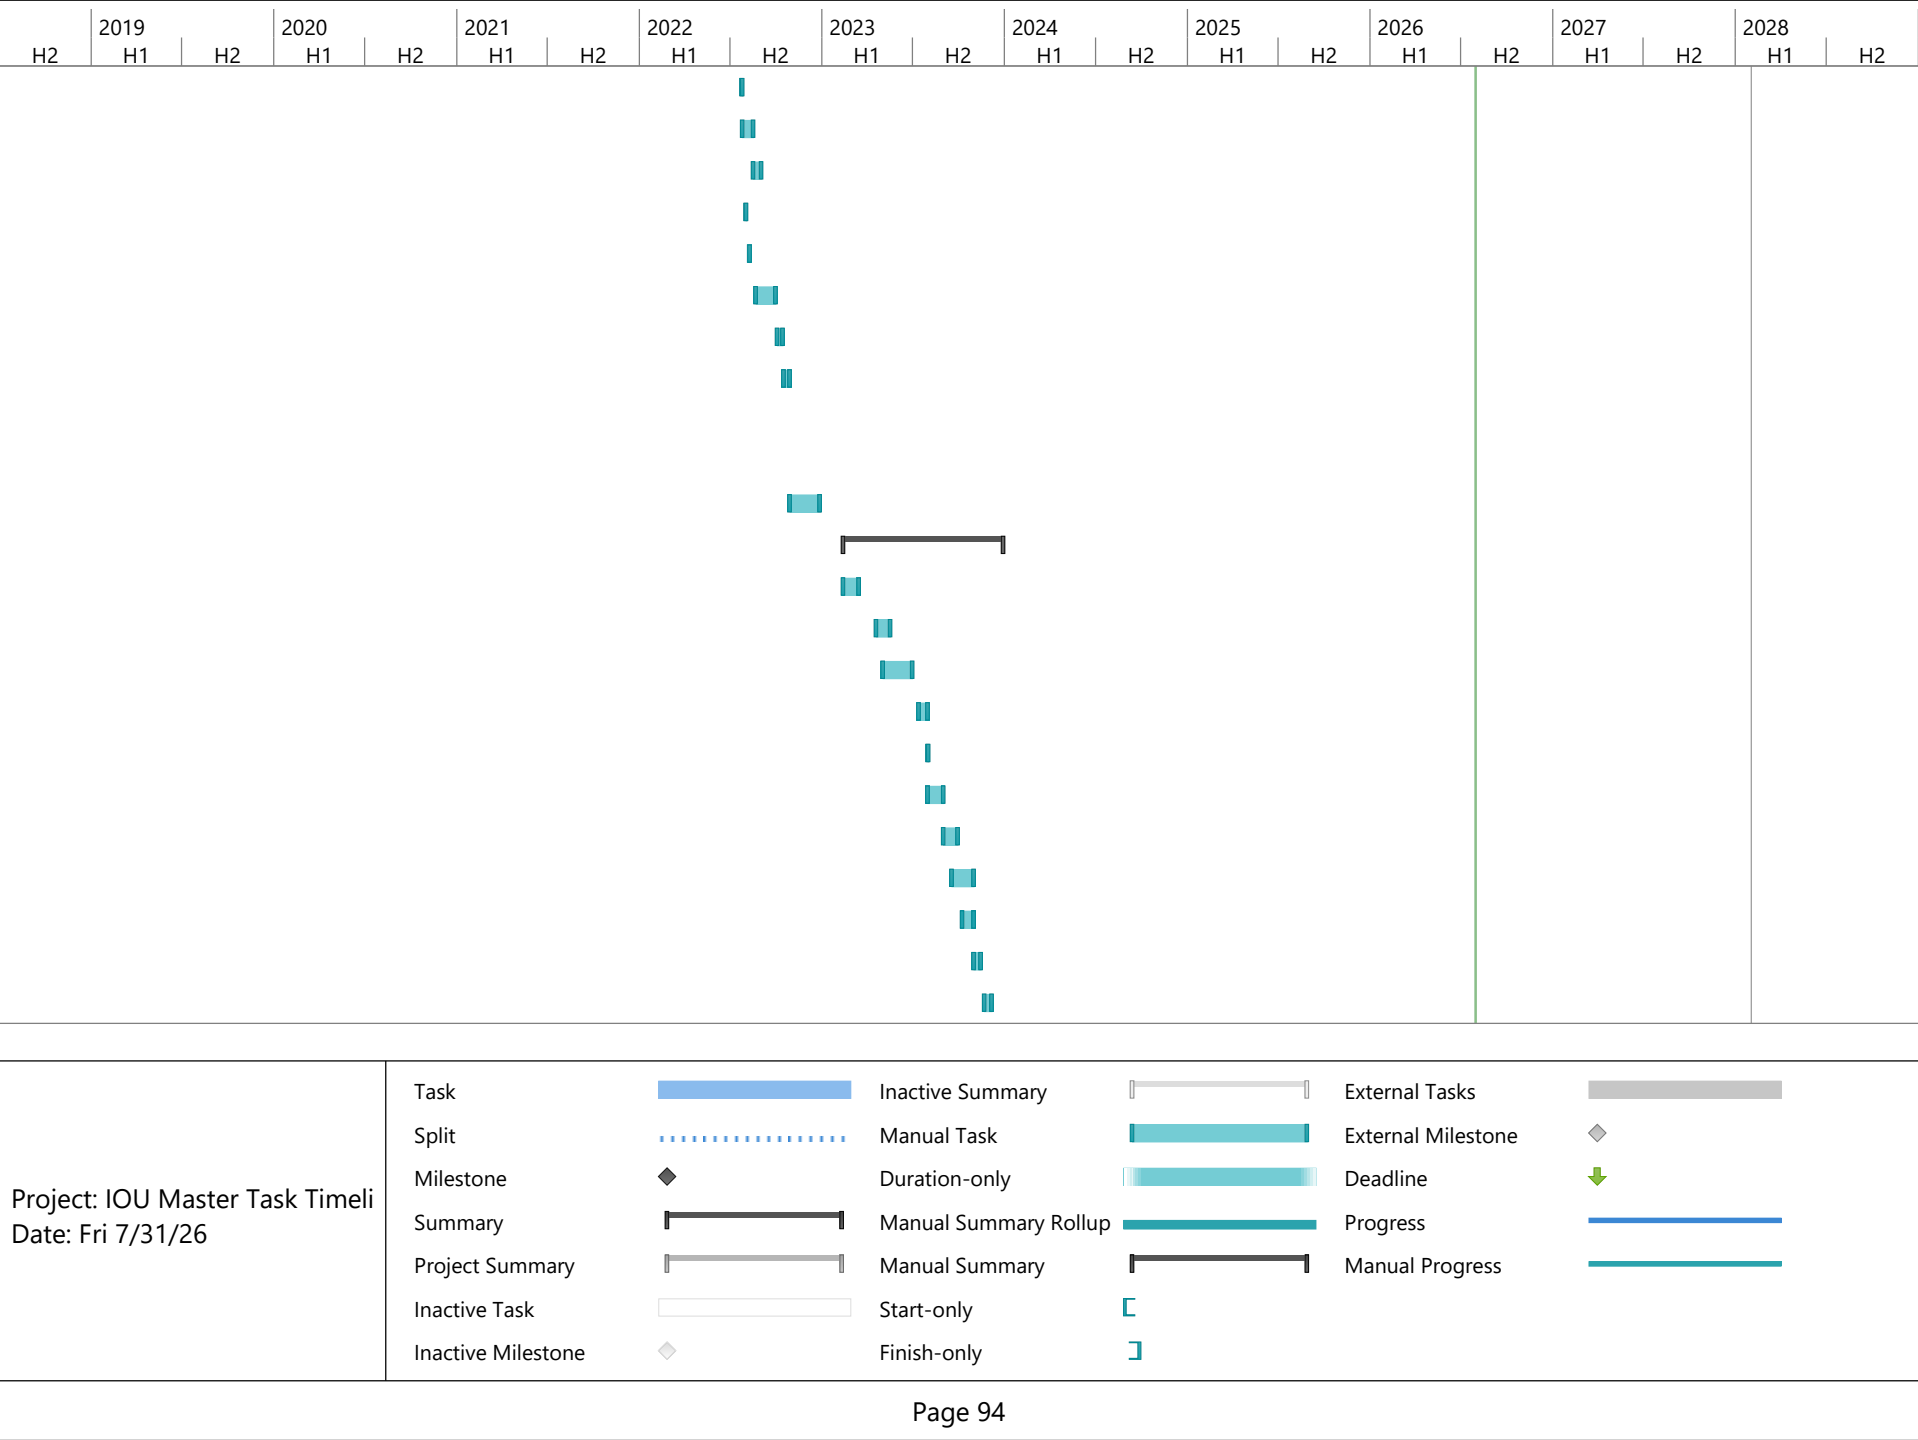
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

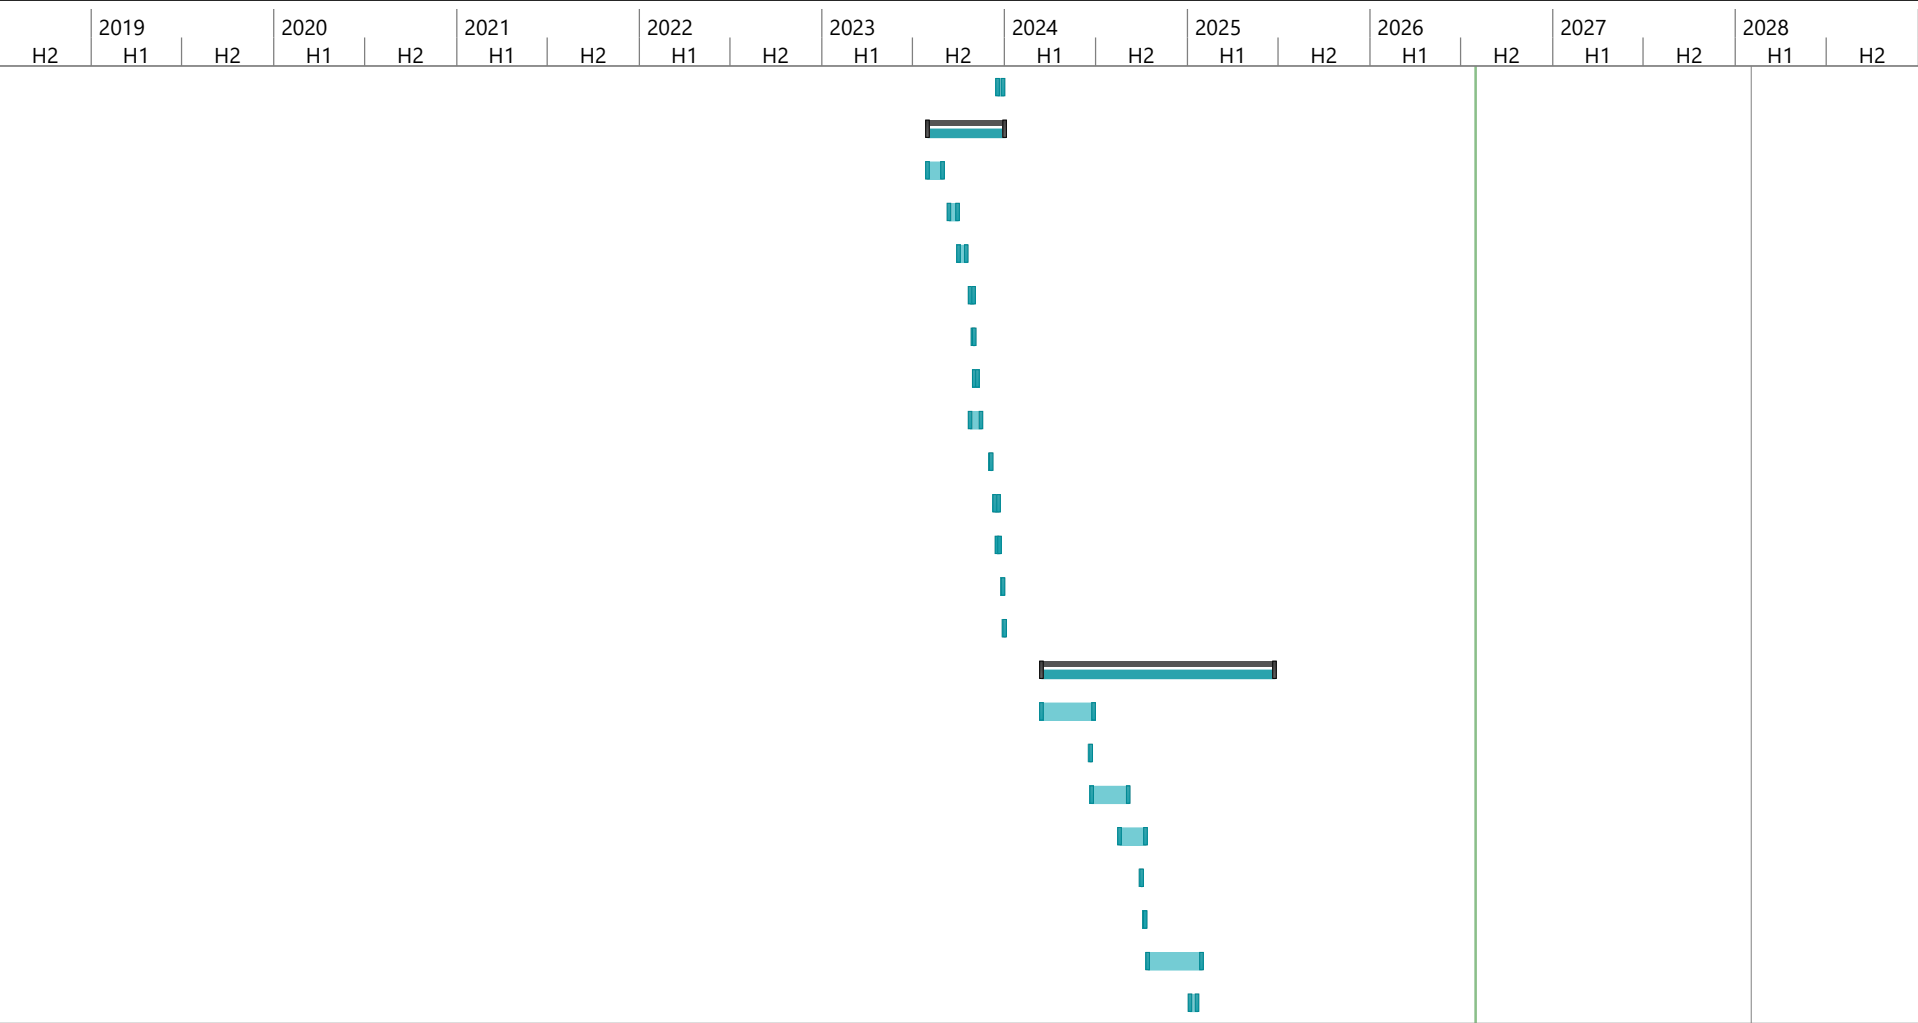


Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

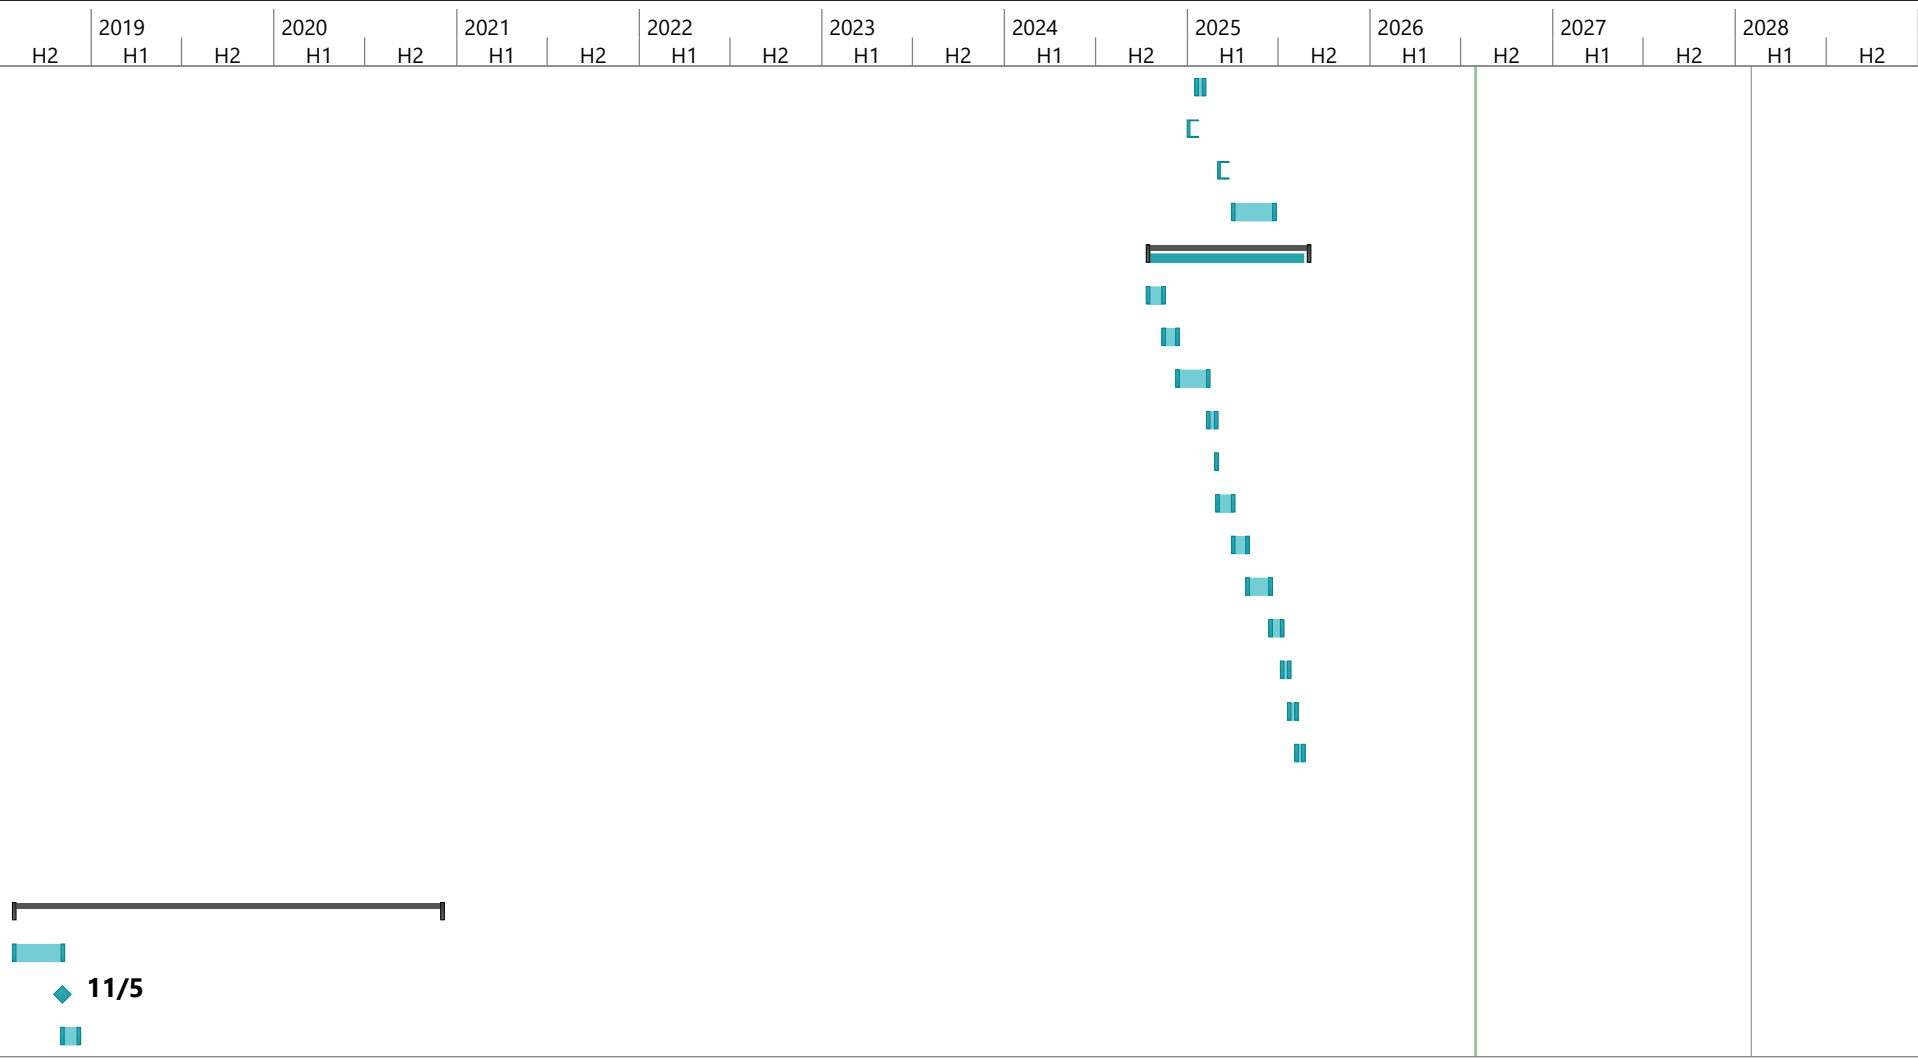


Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

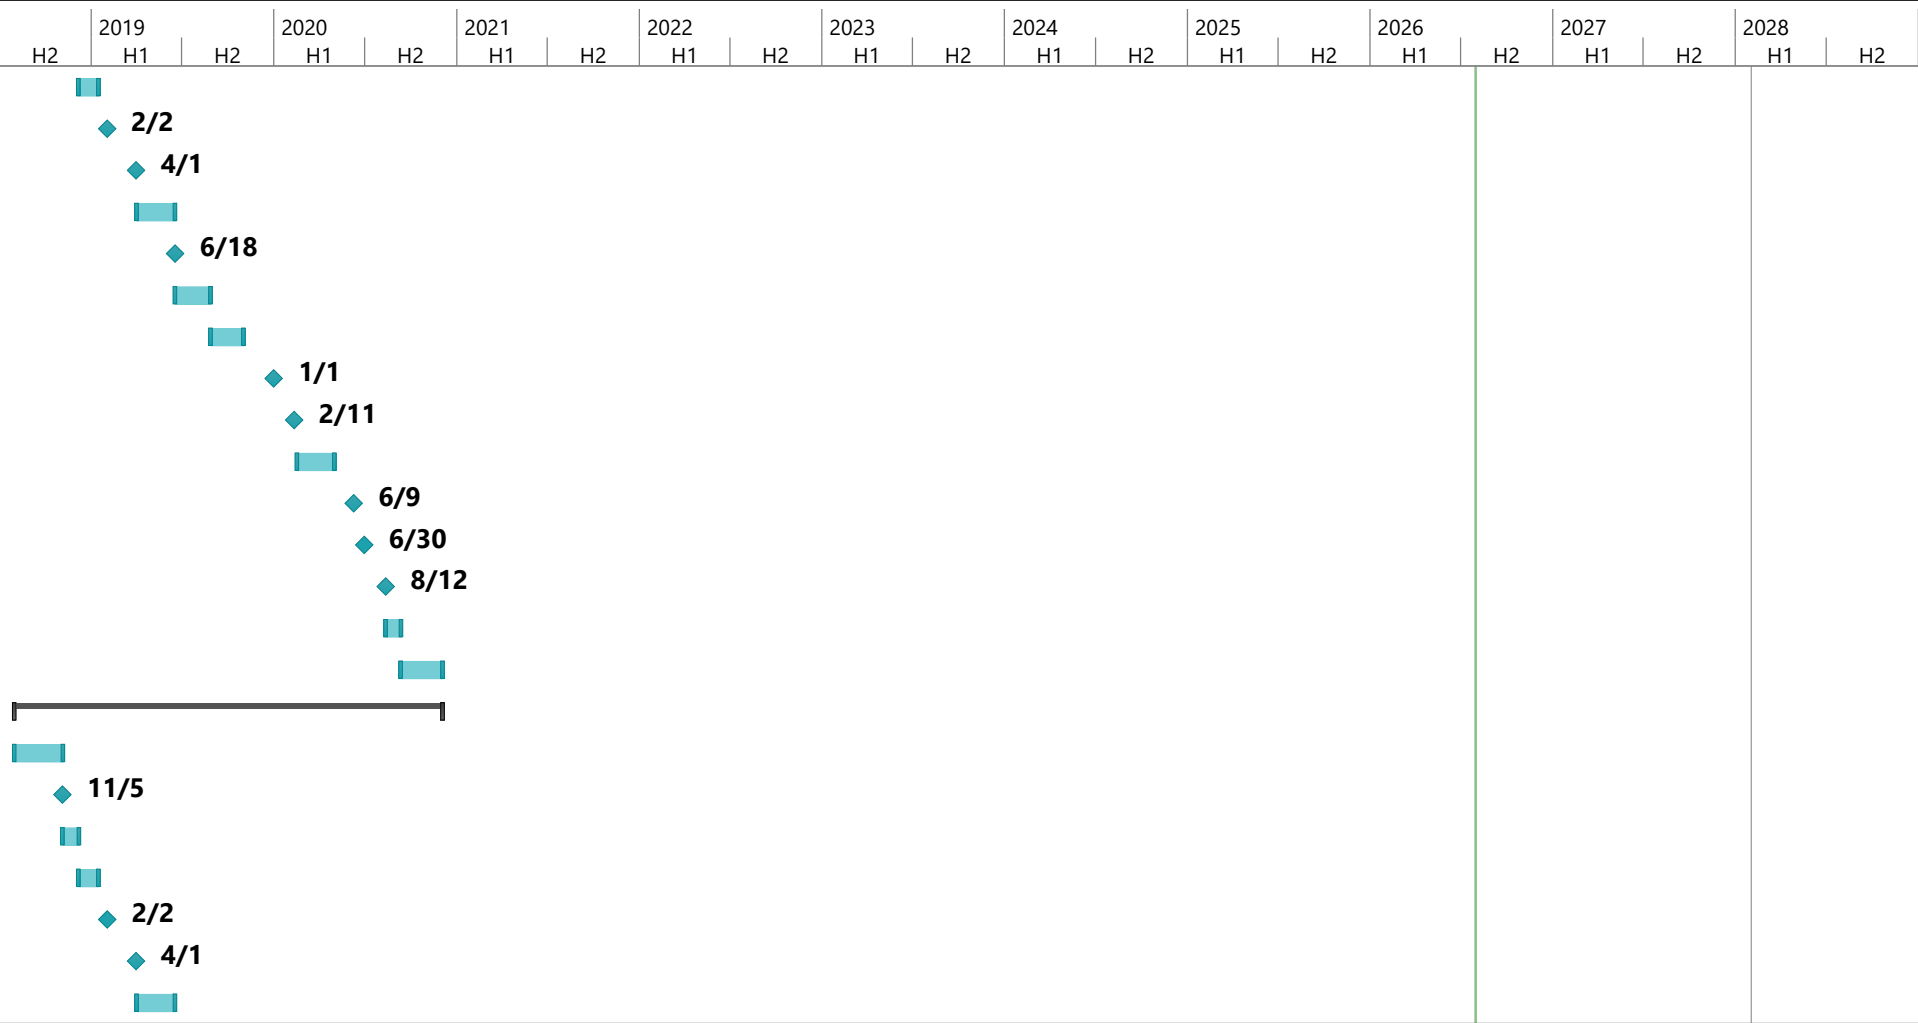




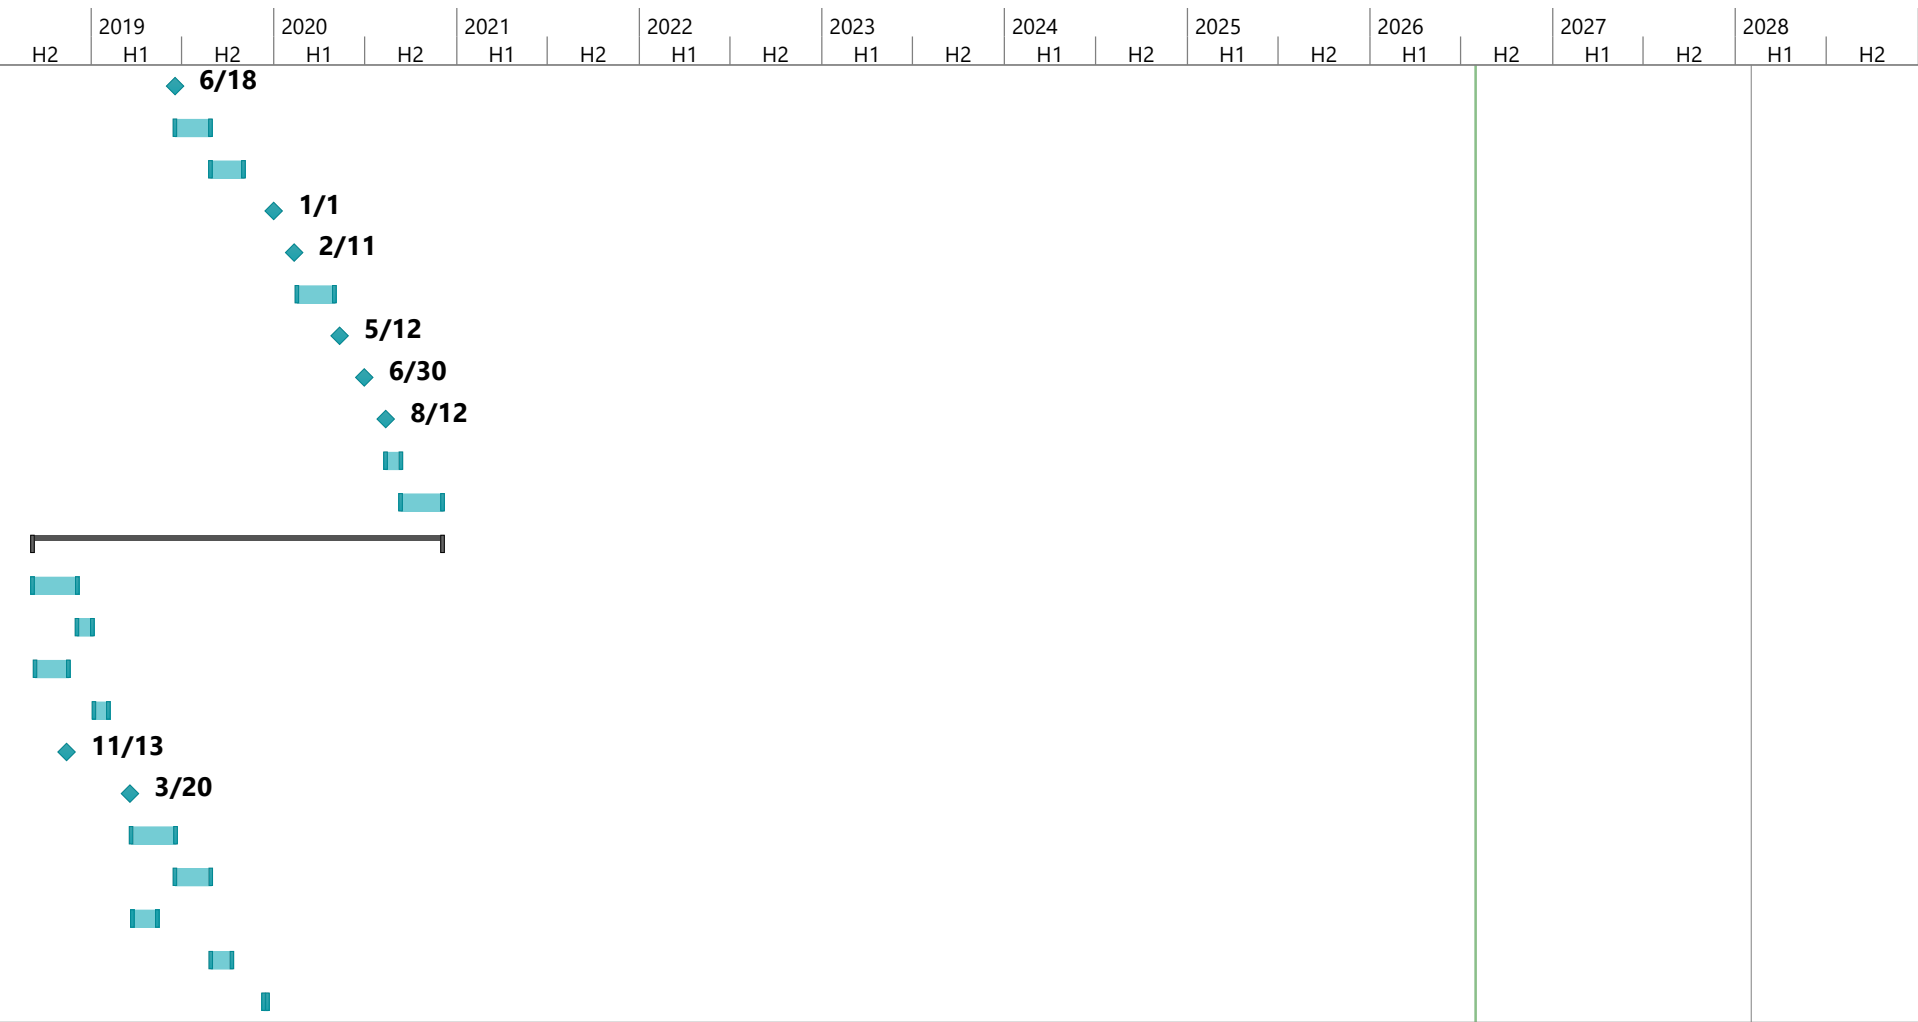
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



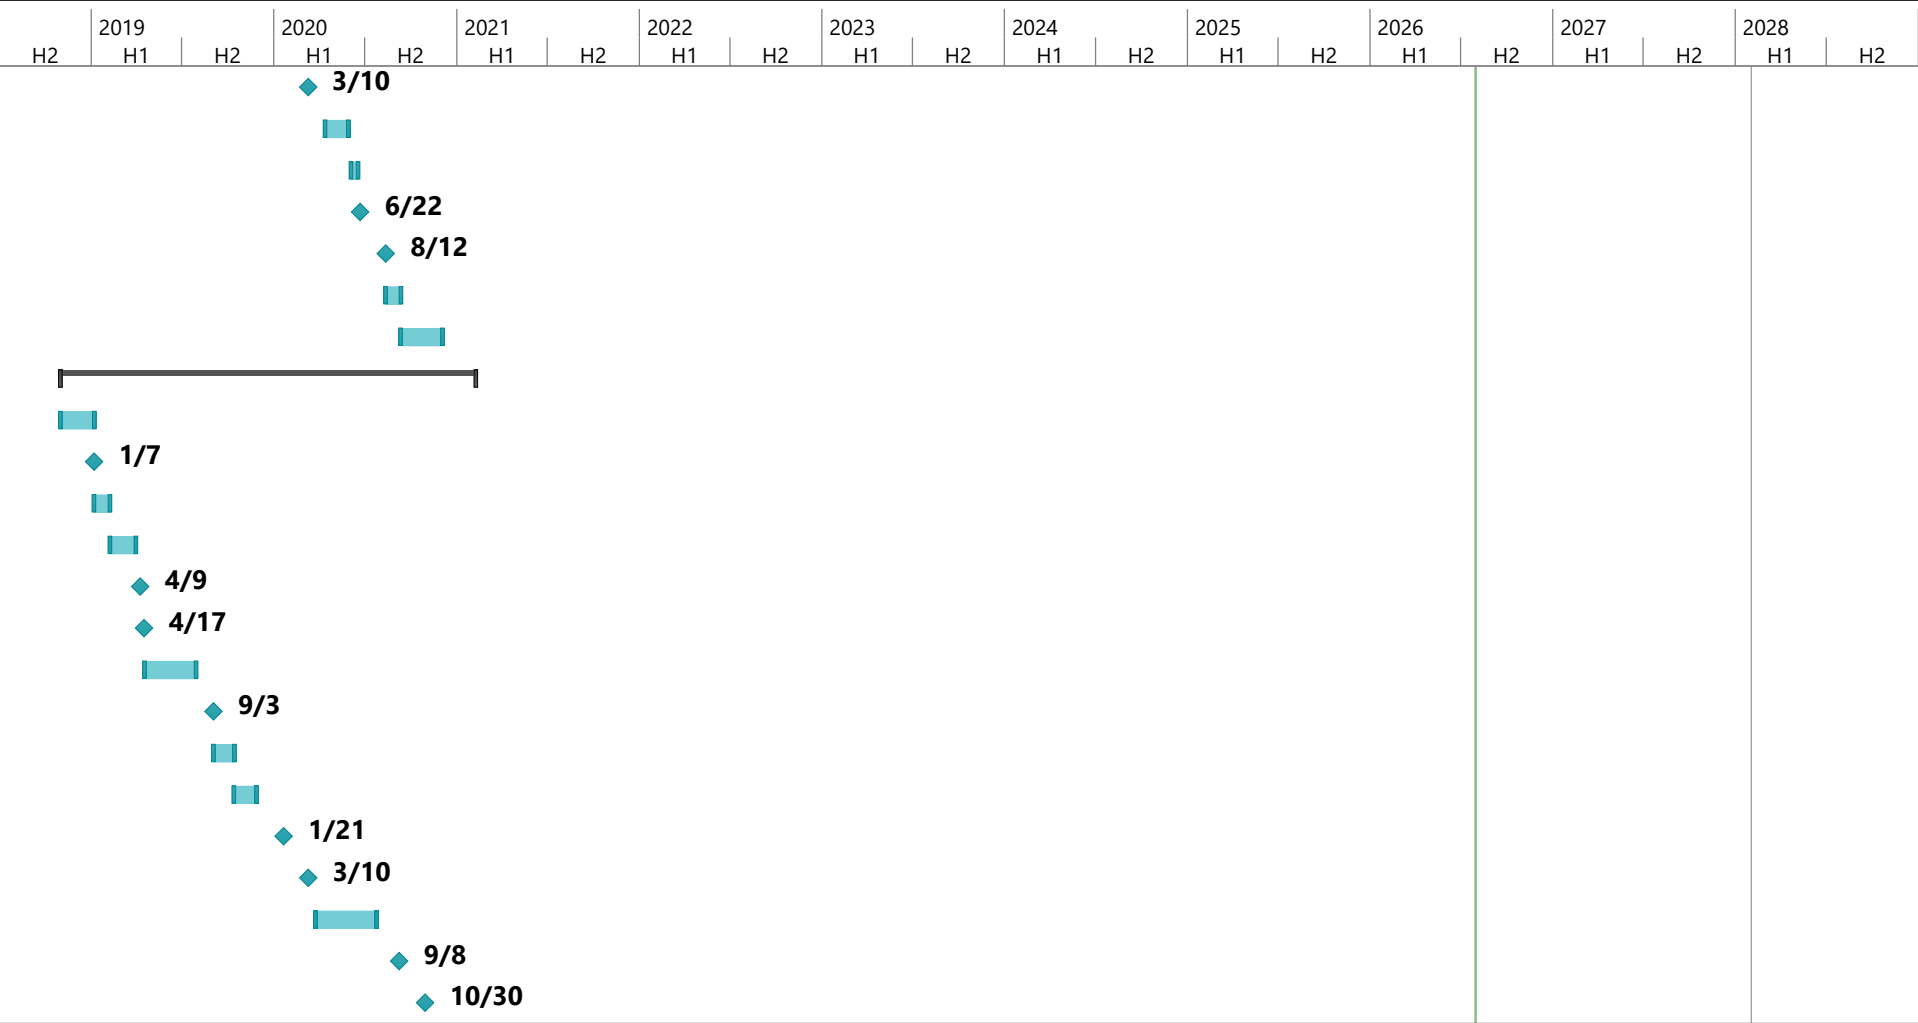
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



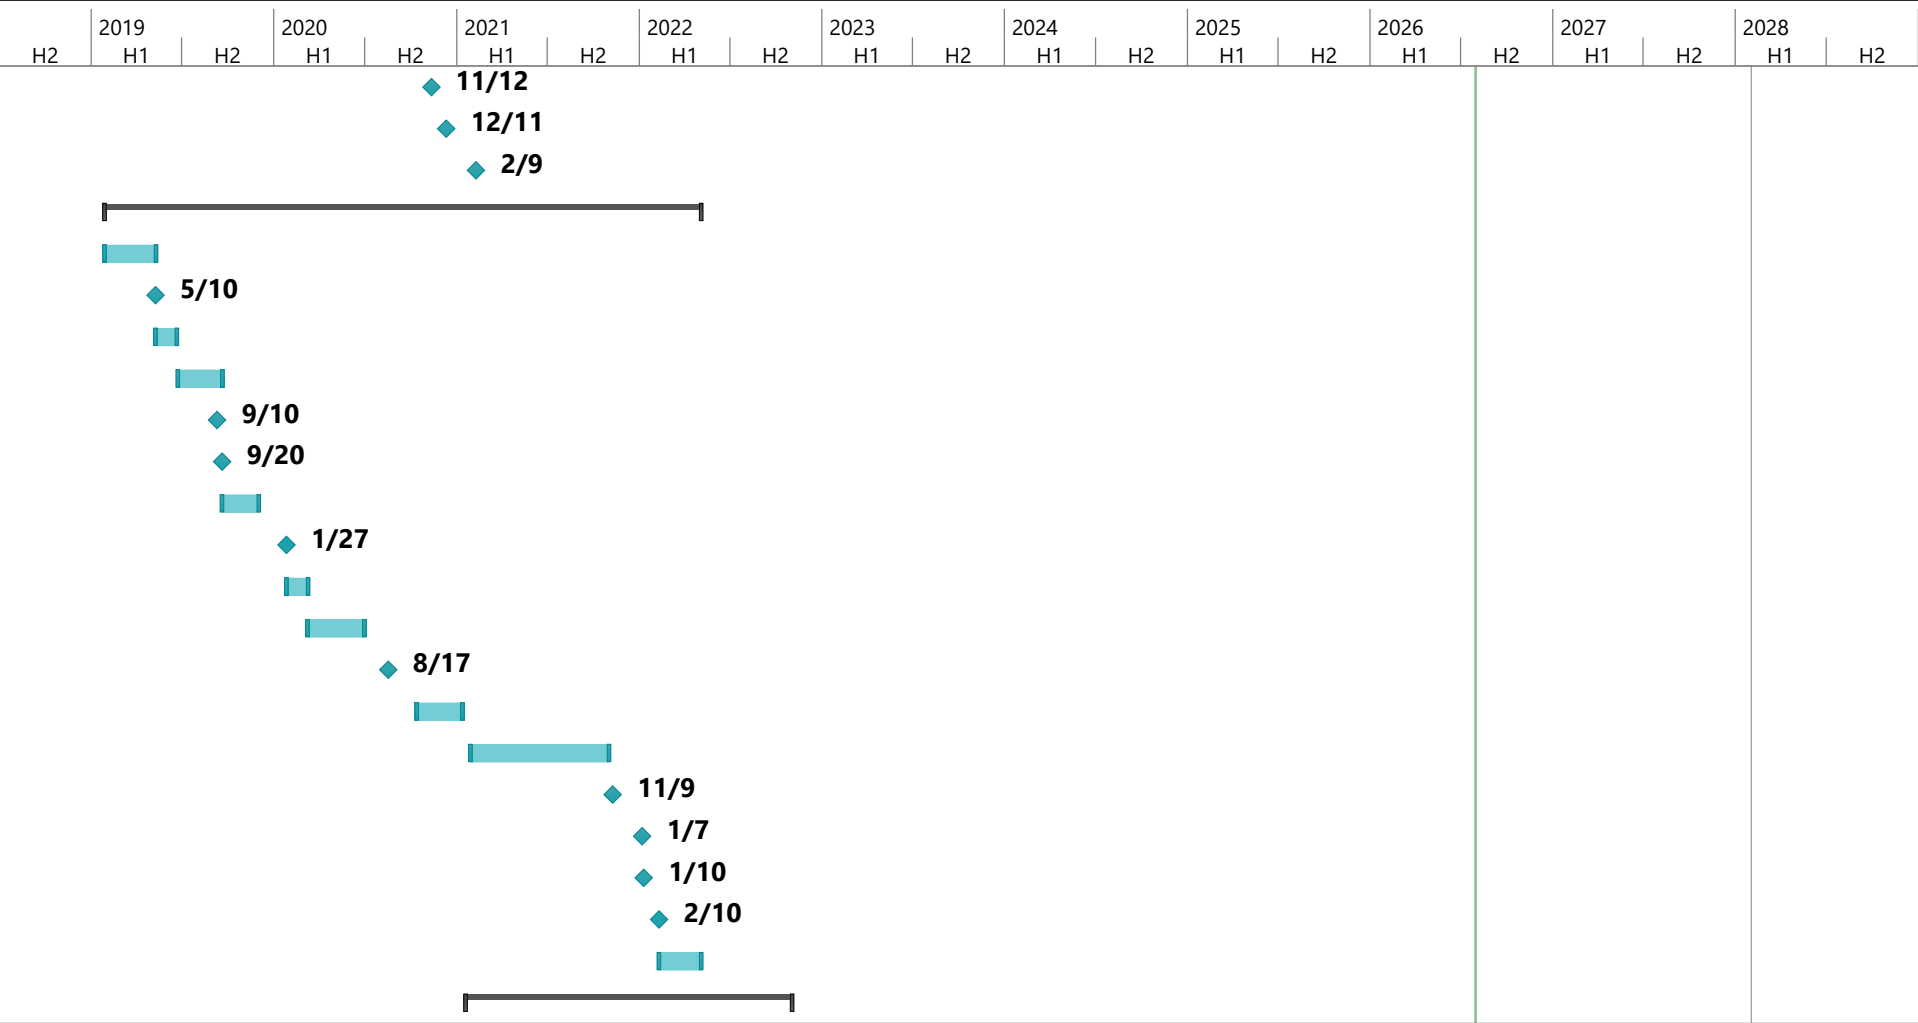
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



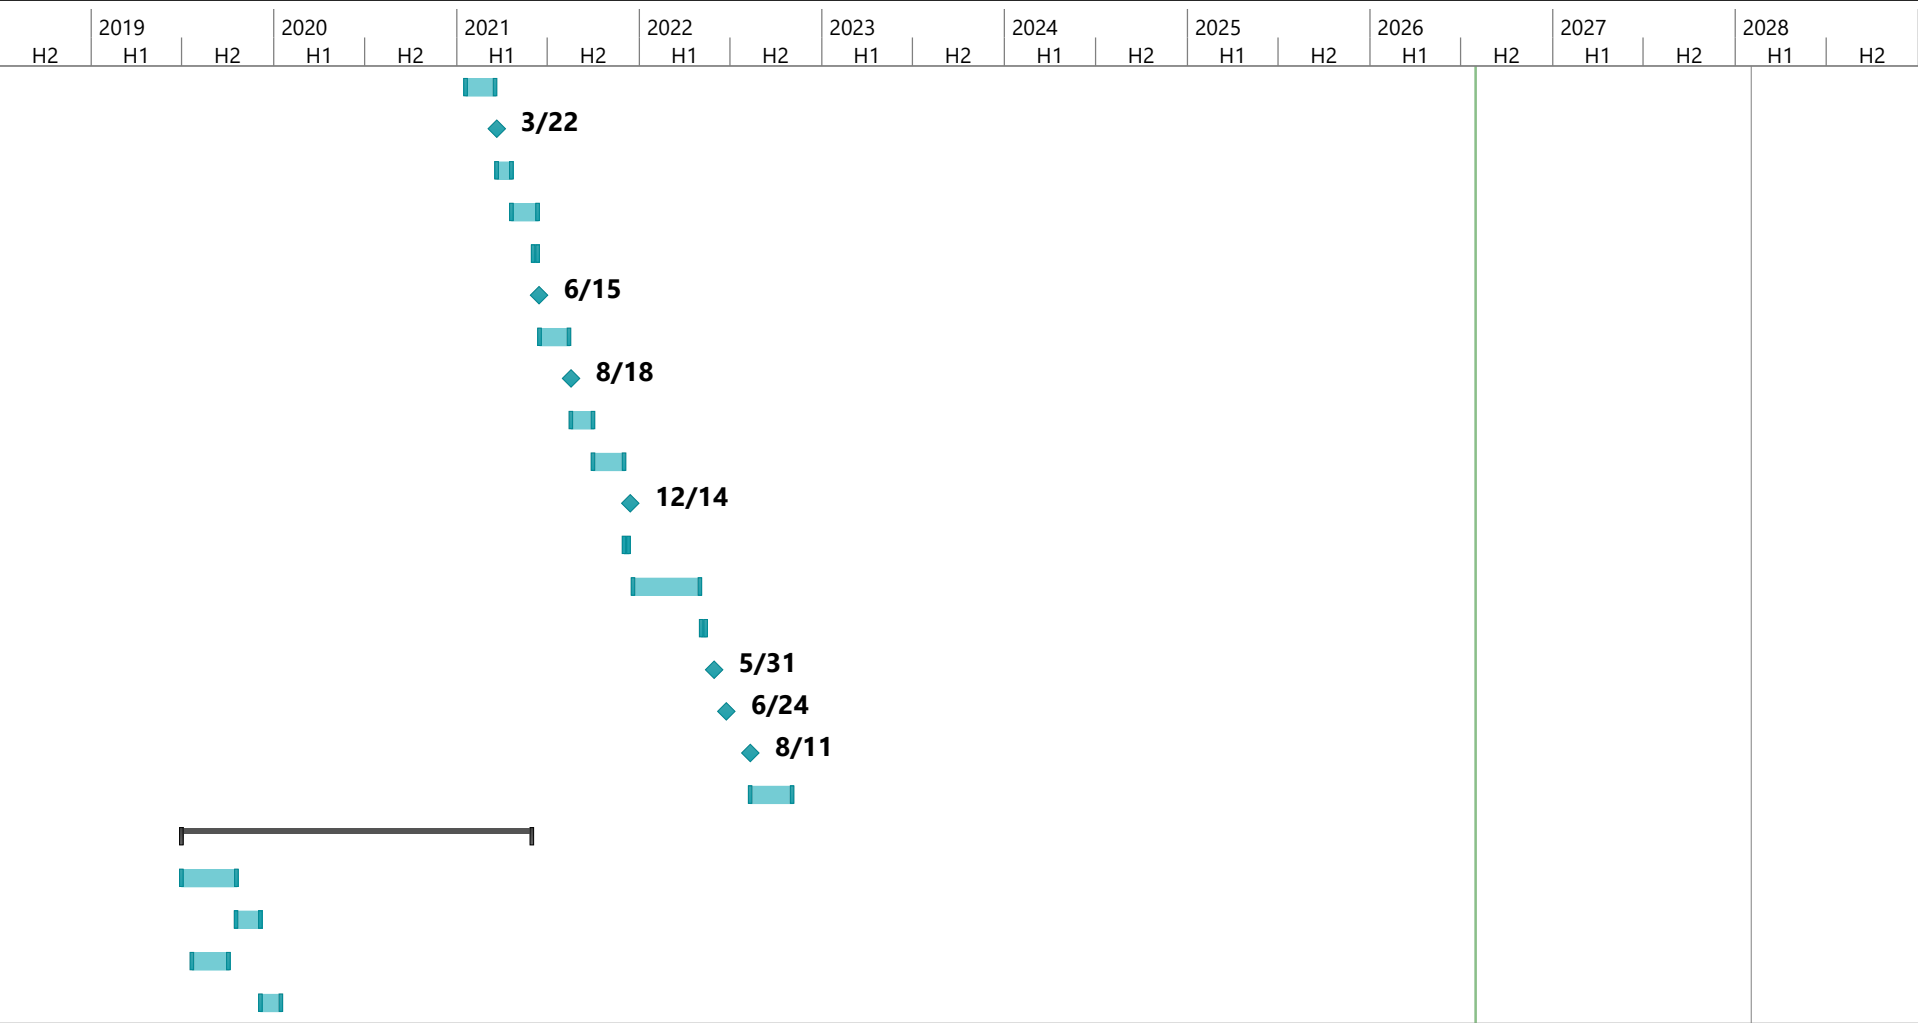
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



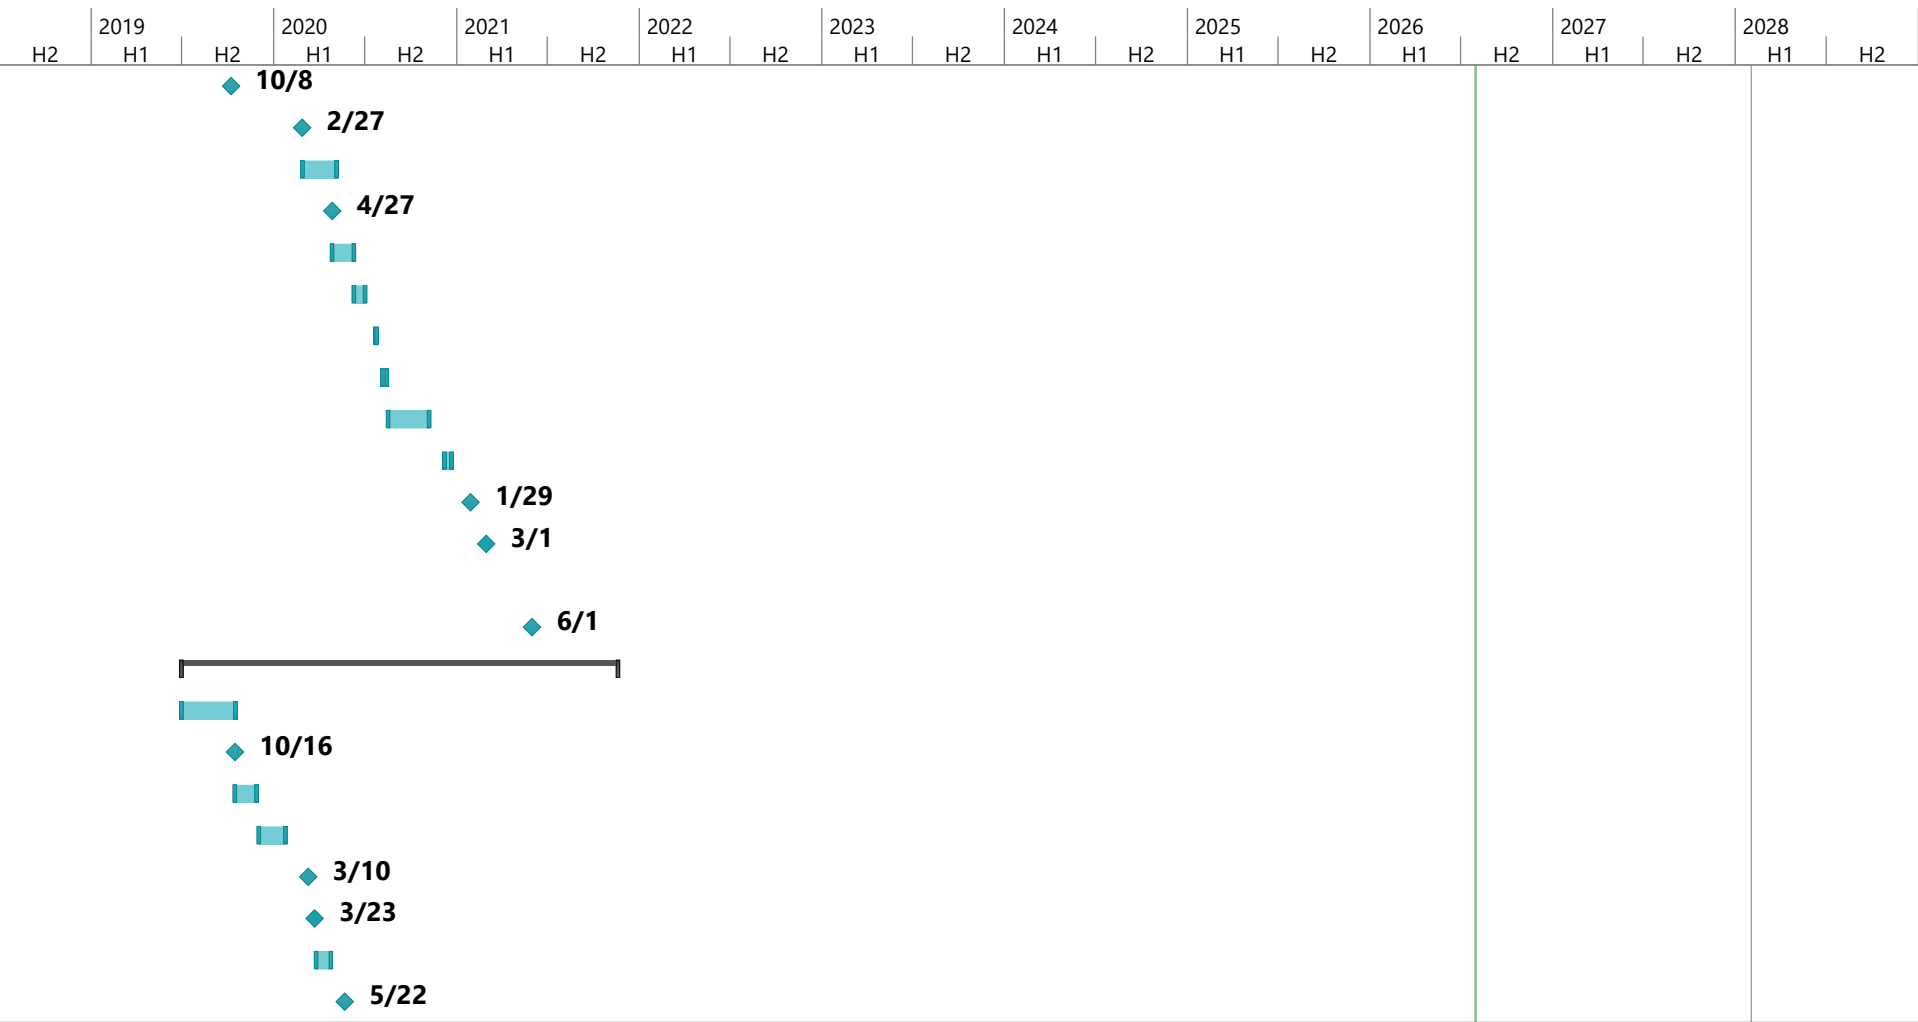
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



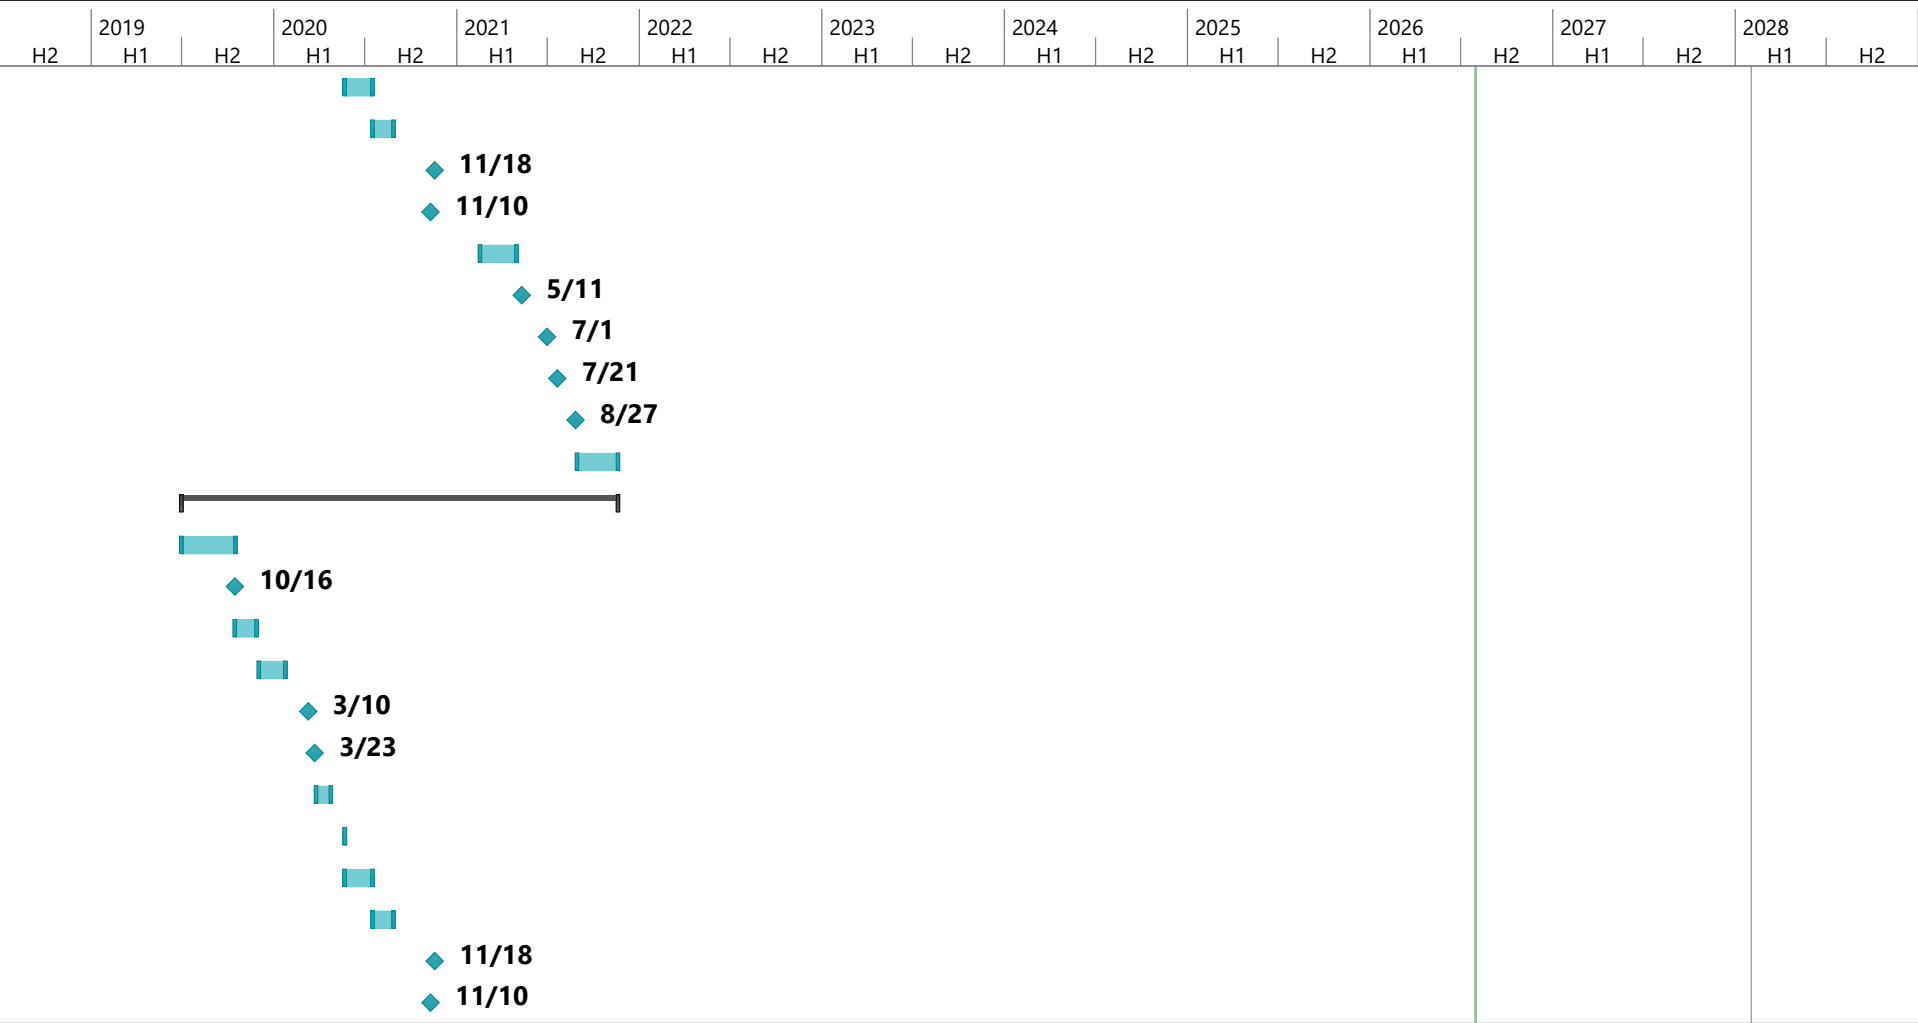
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



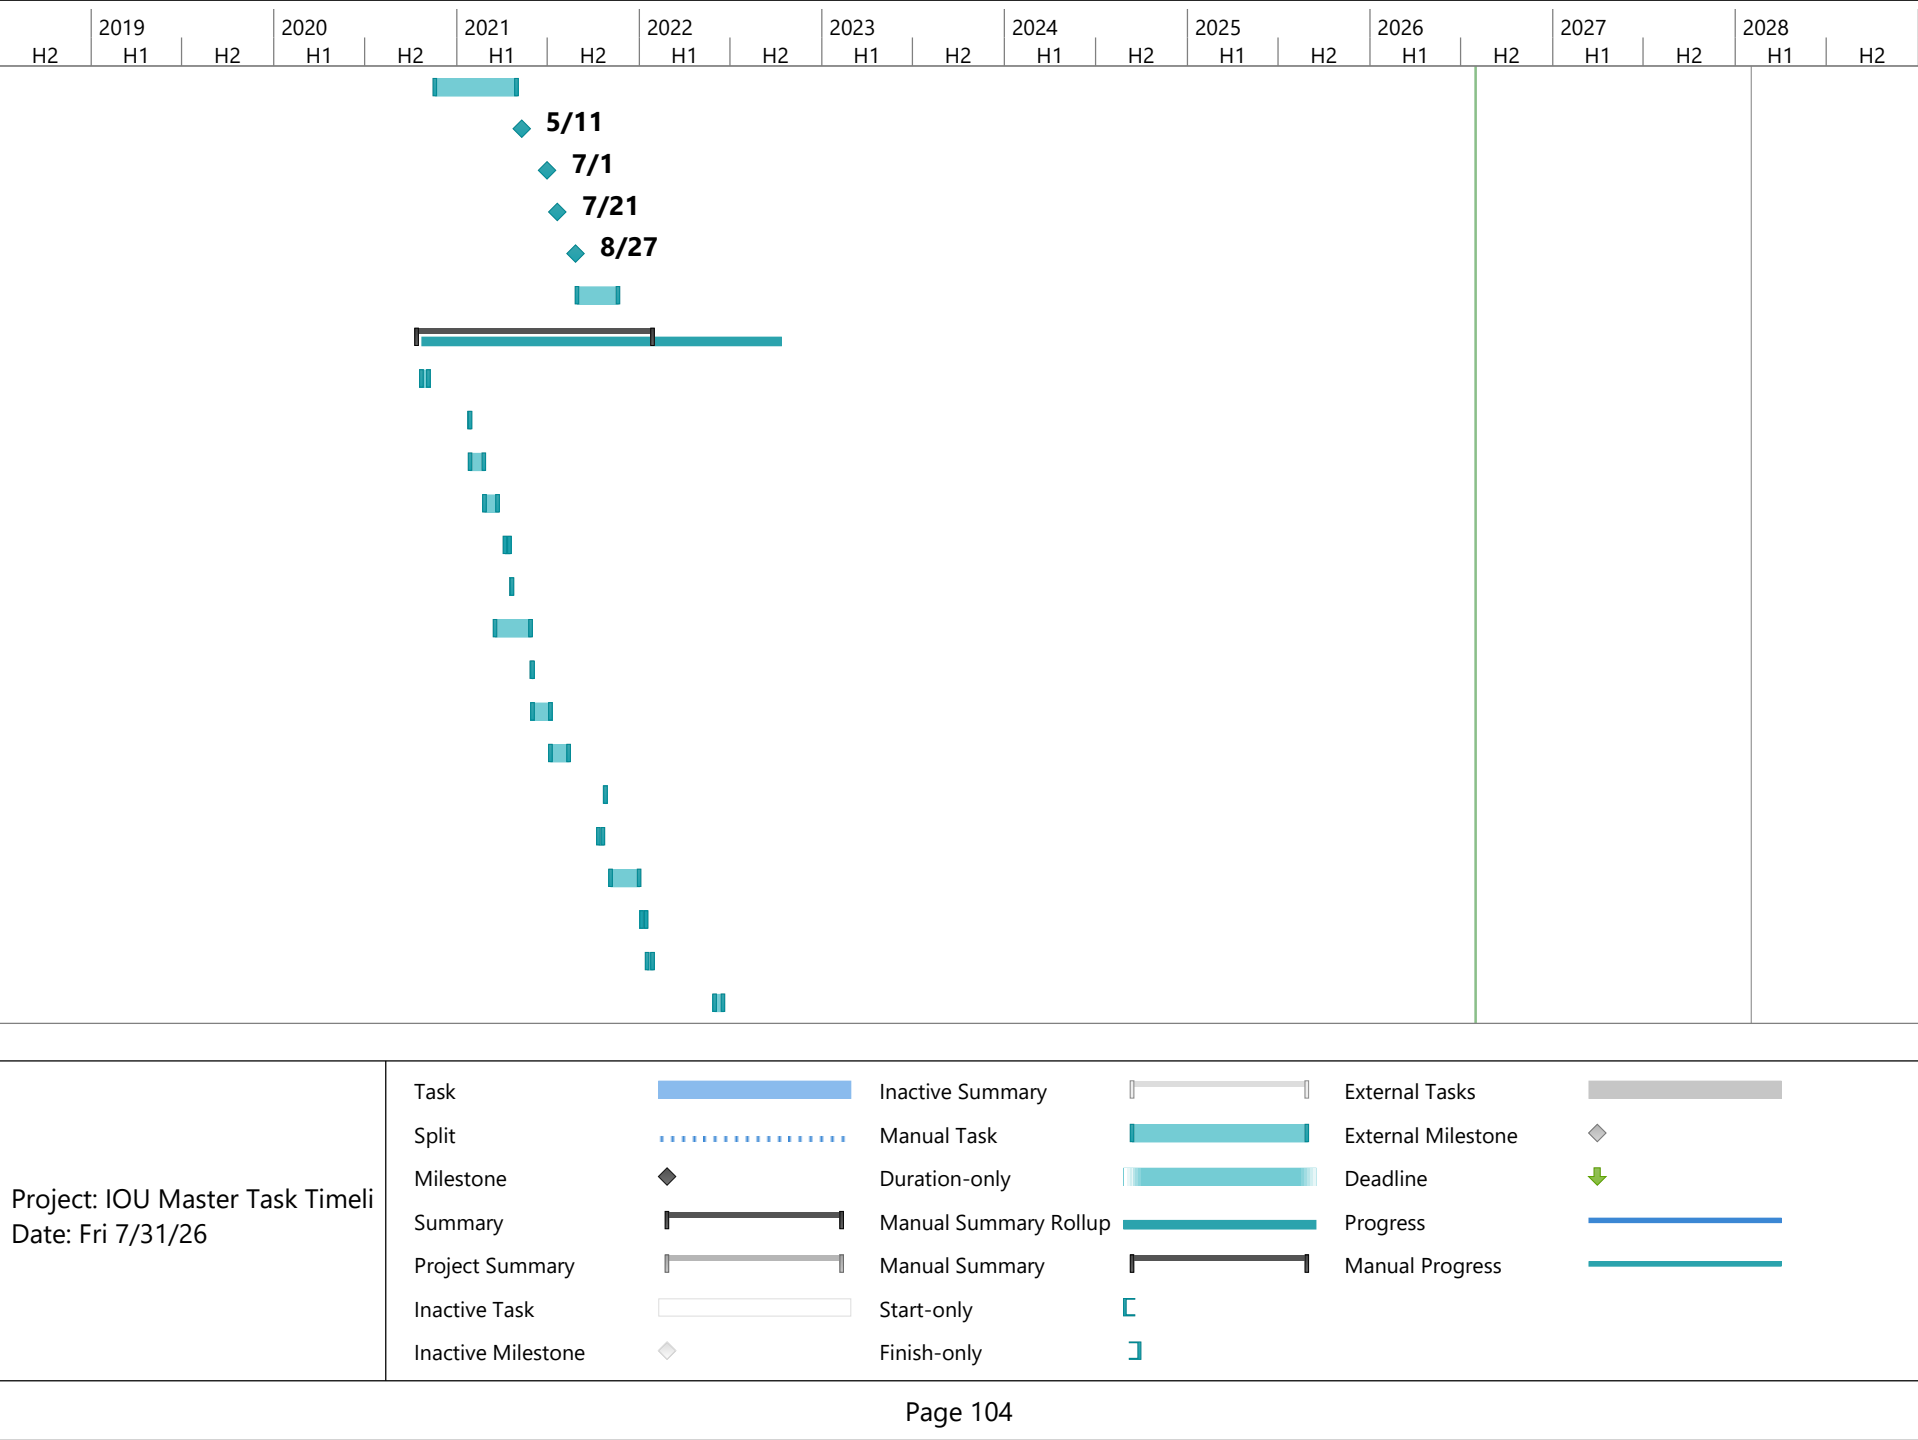
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

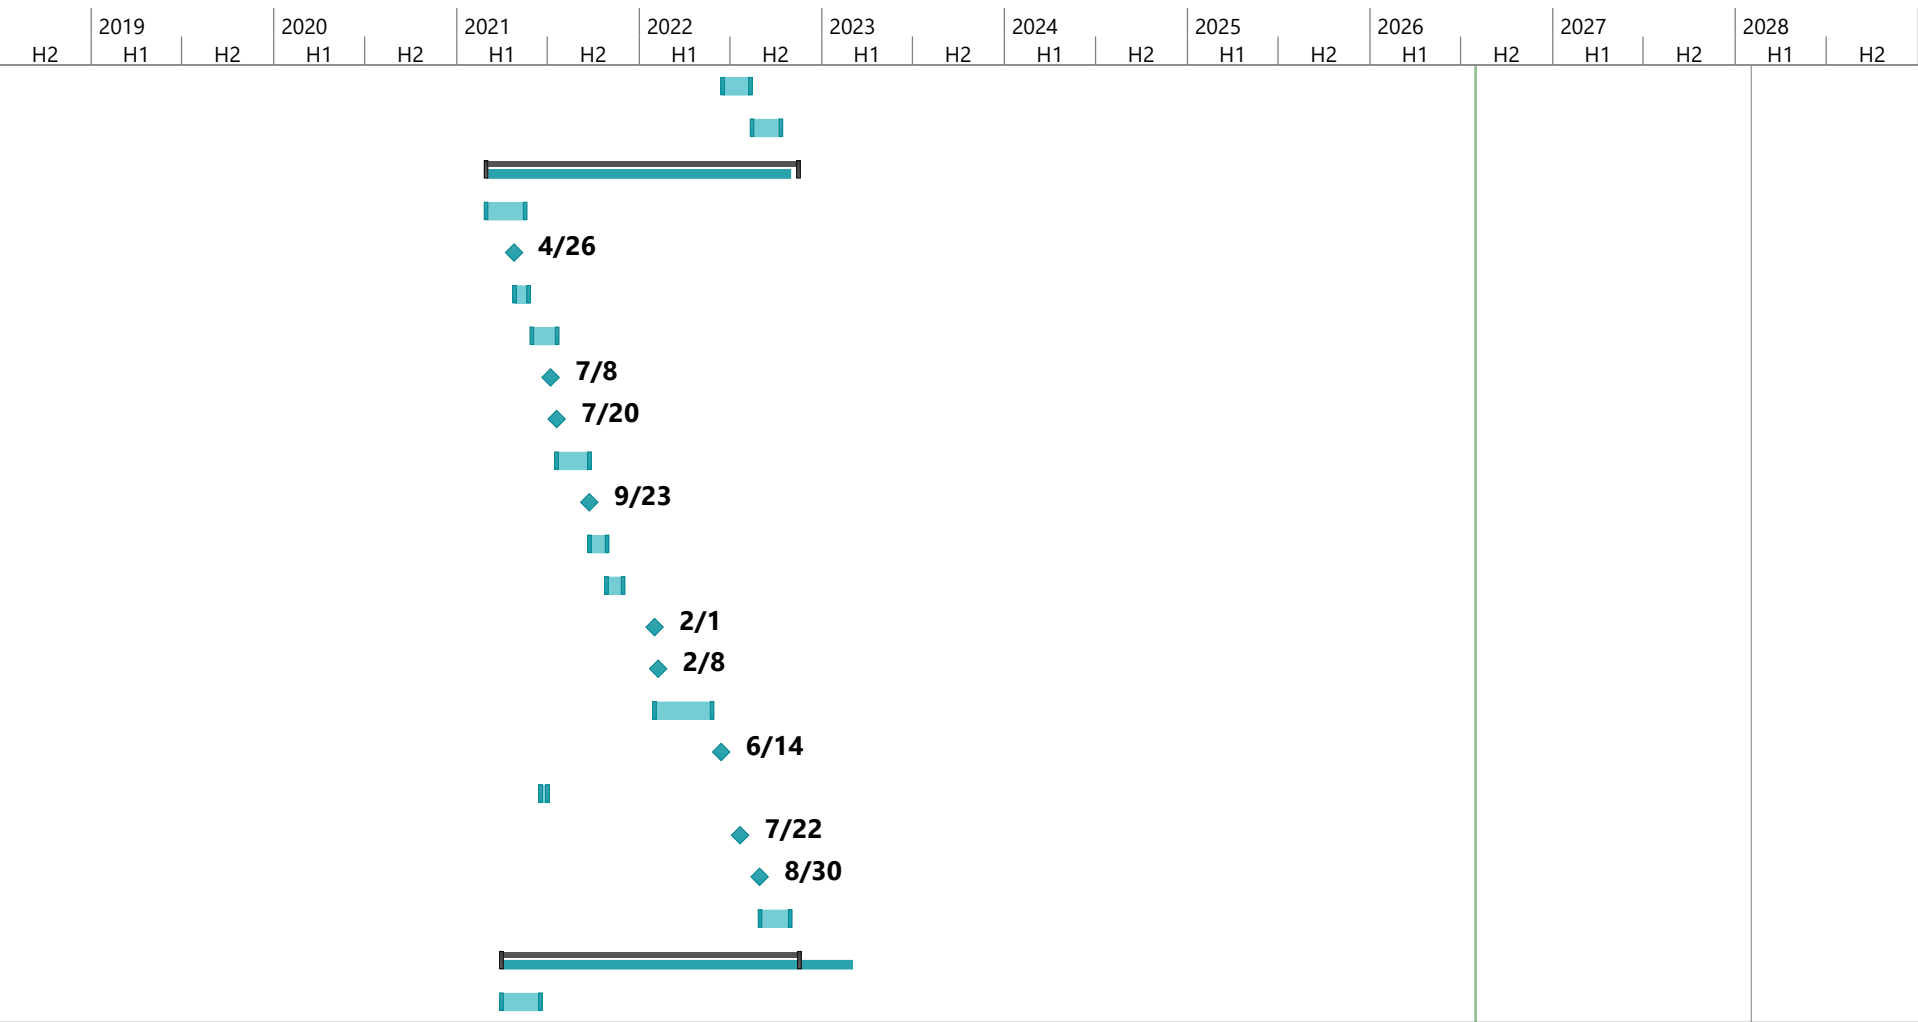


Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

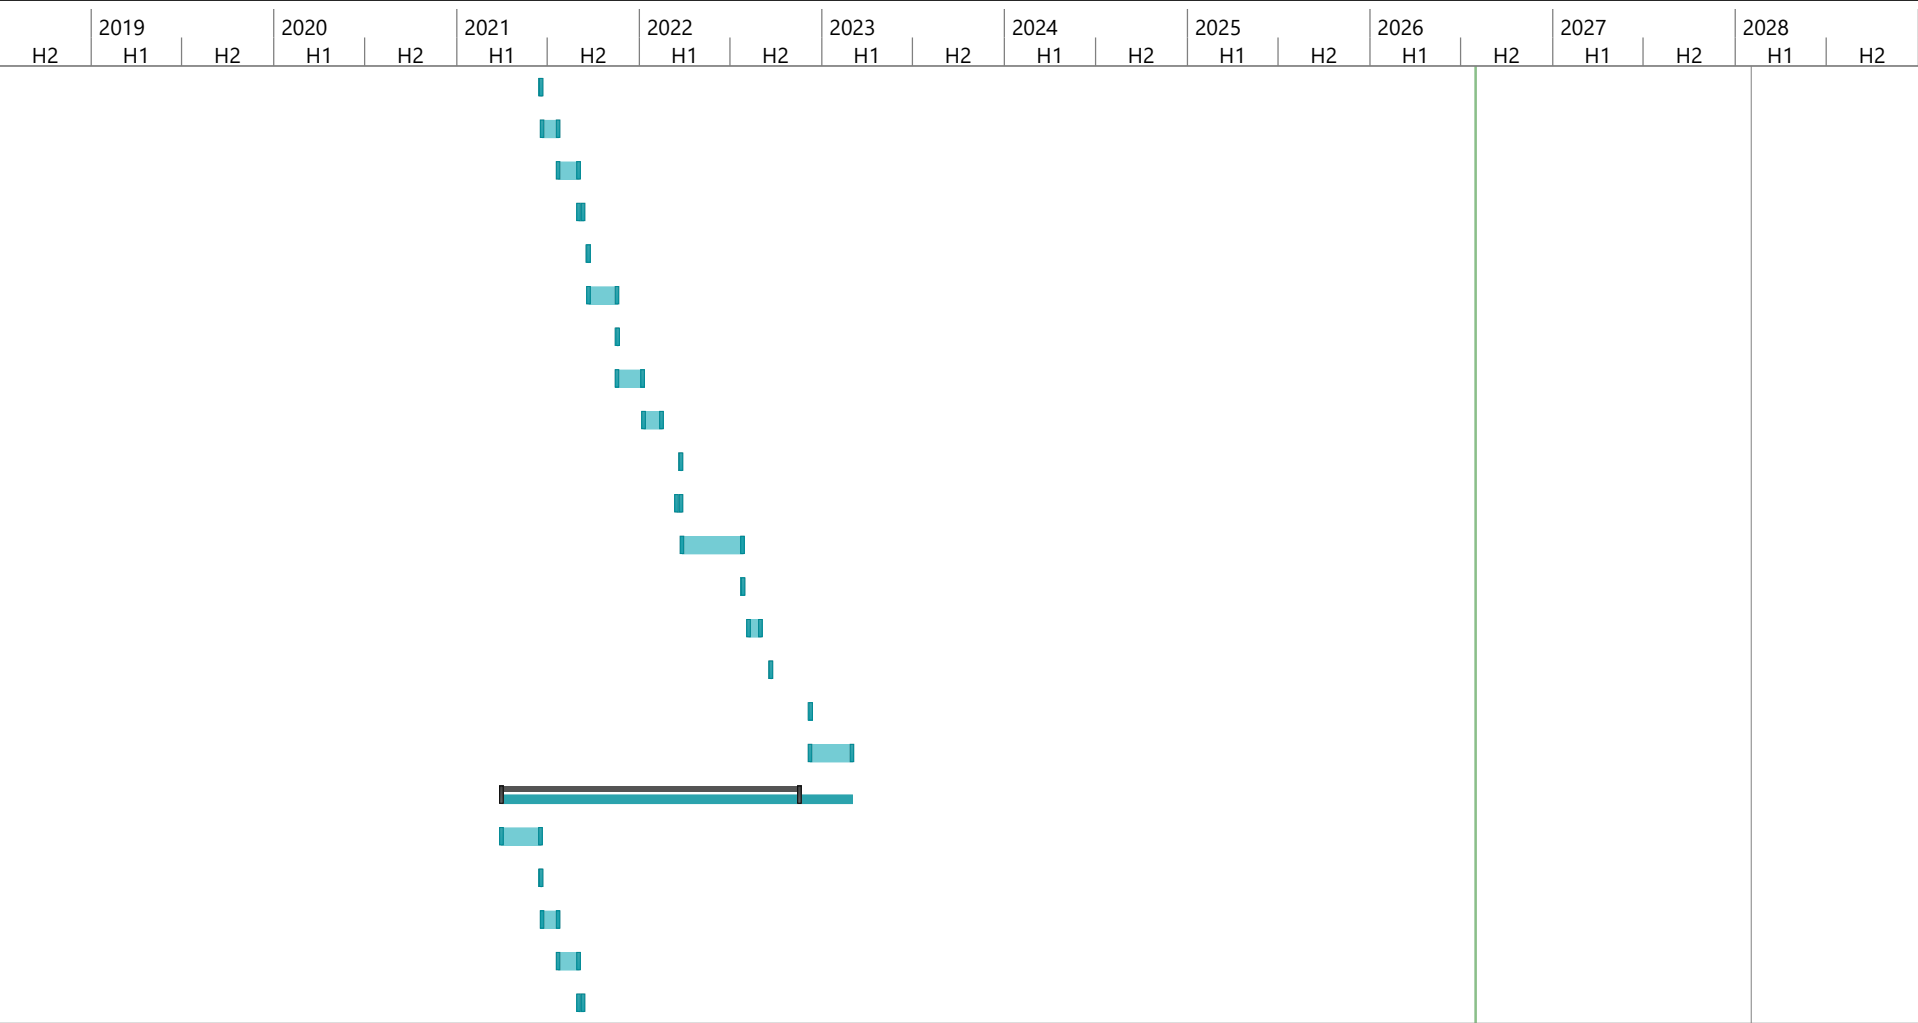


Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			





Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 7/31/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

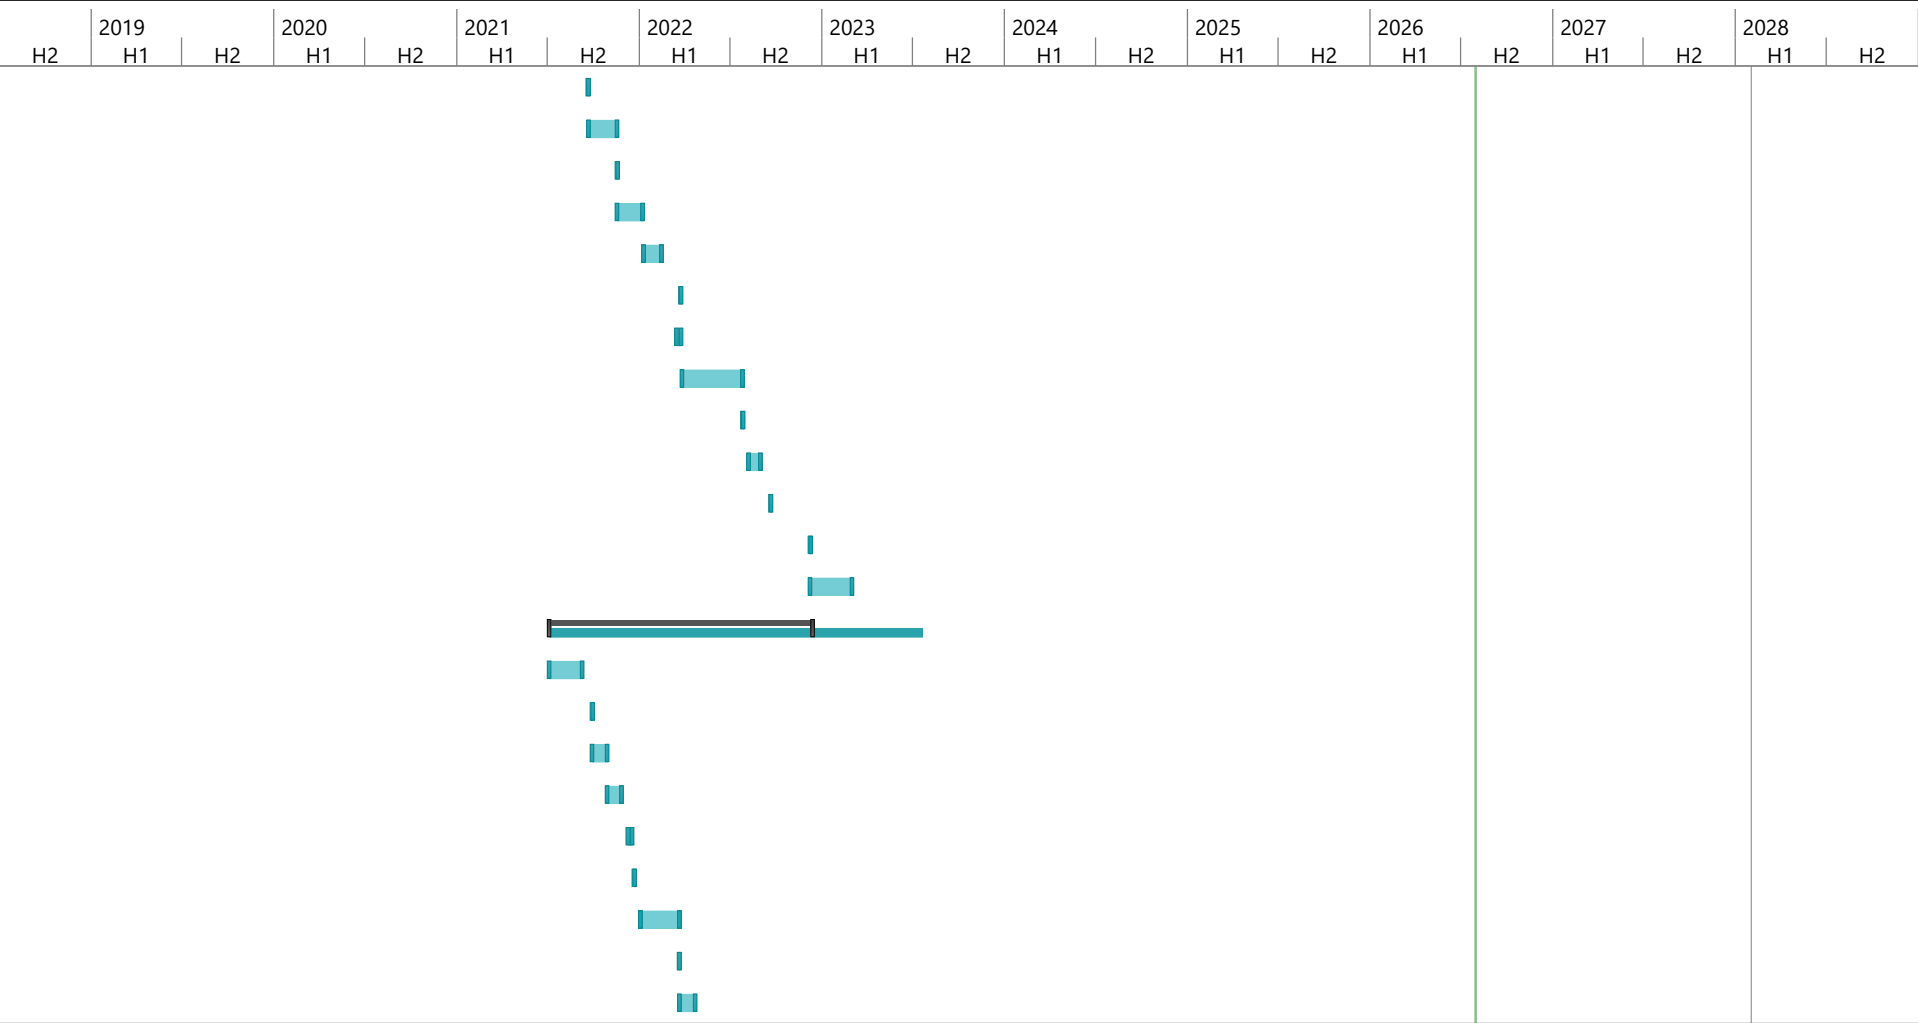
External Milestone

Deadline

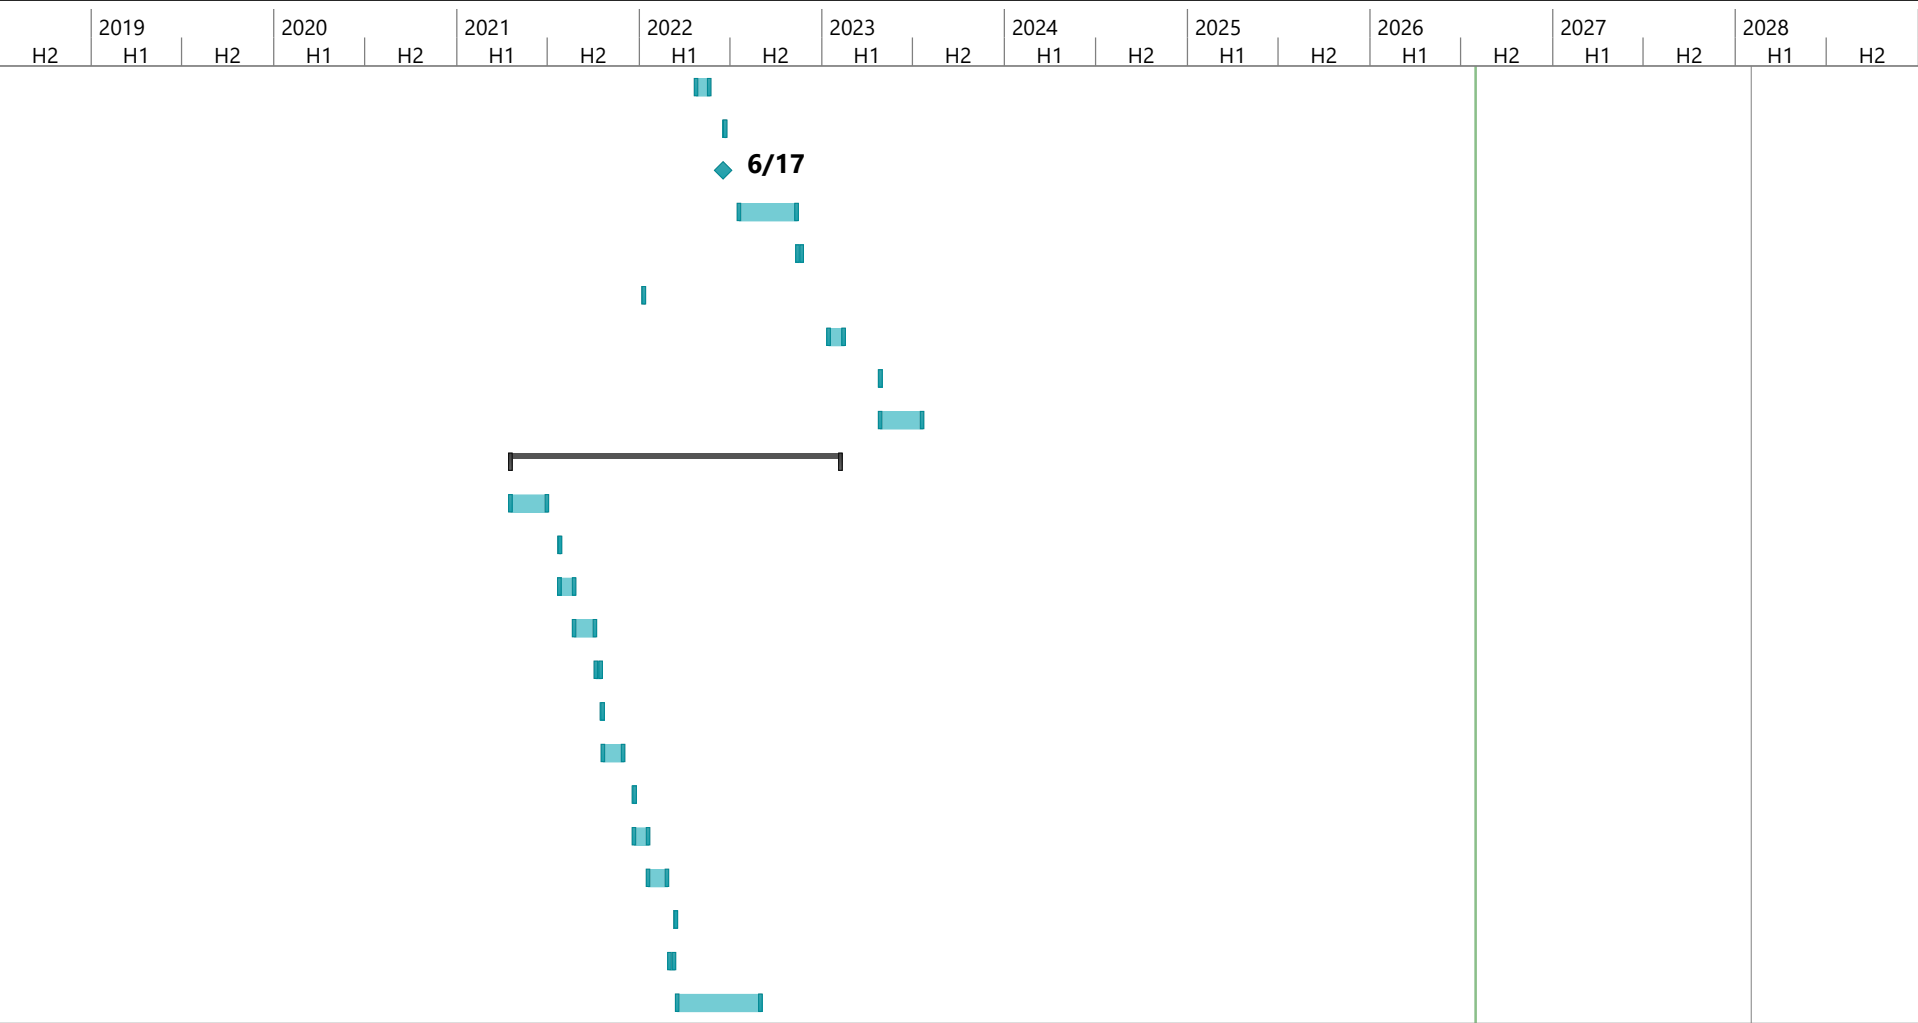
Progress

Manual Progress

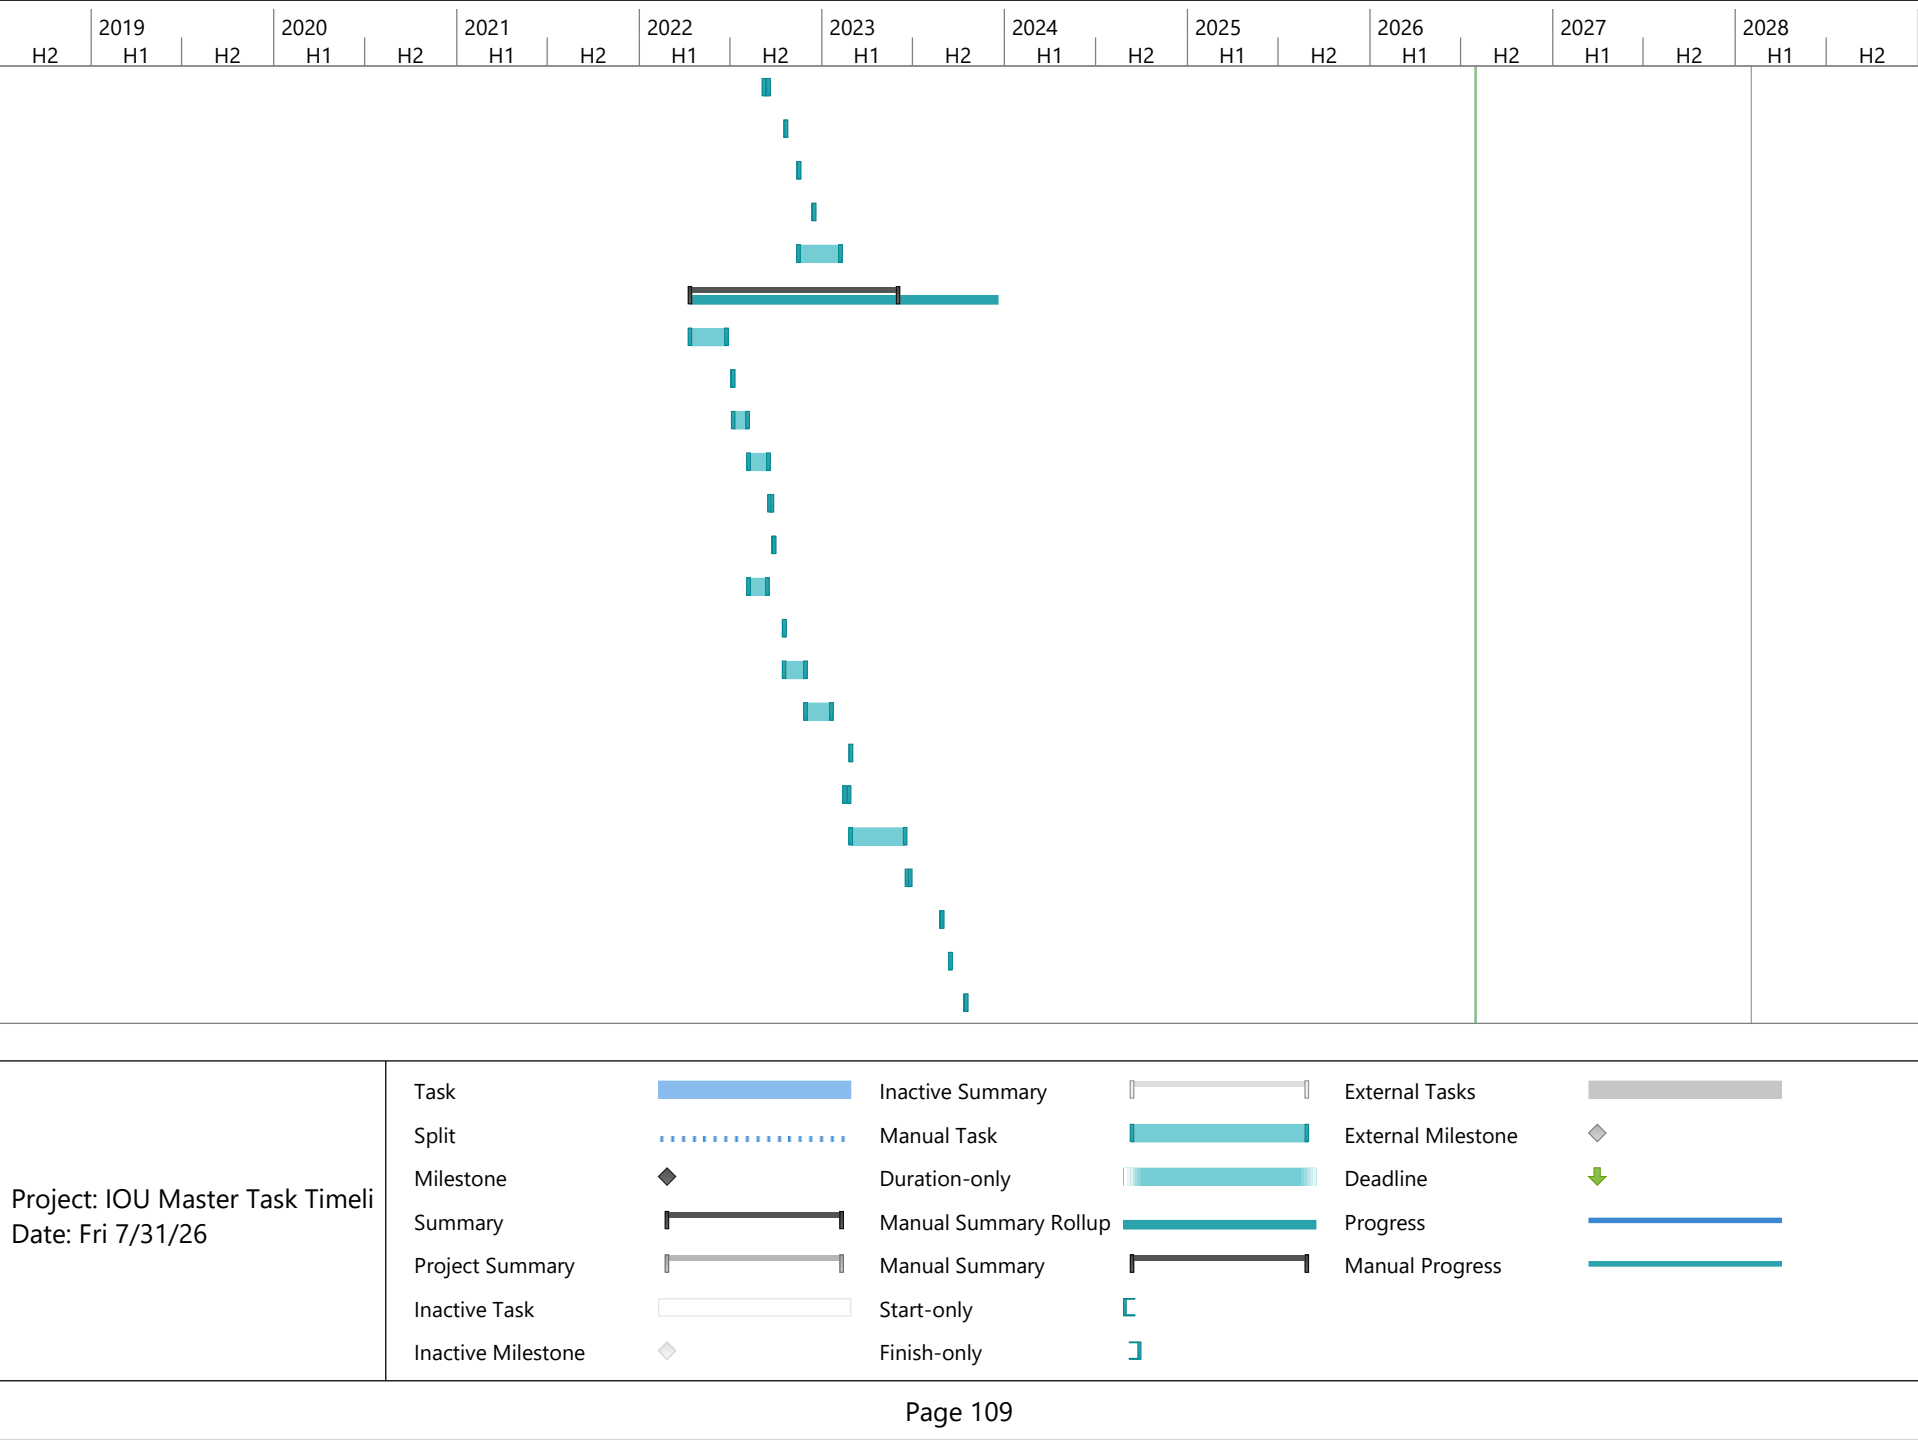
Page 106

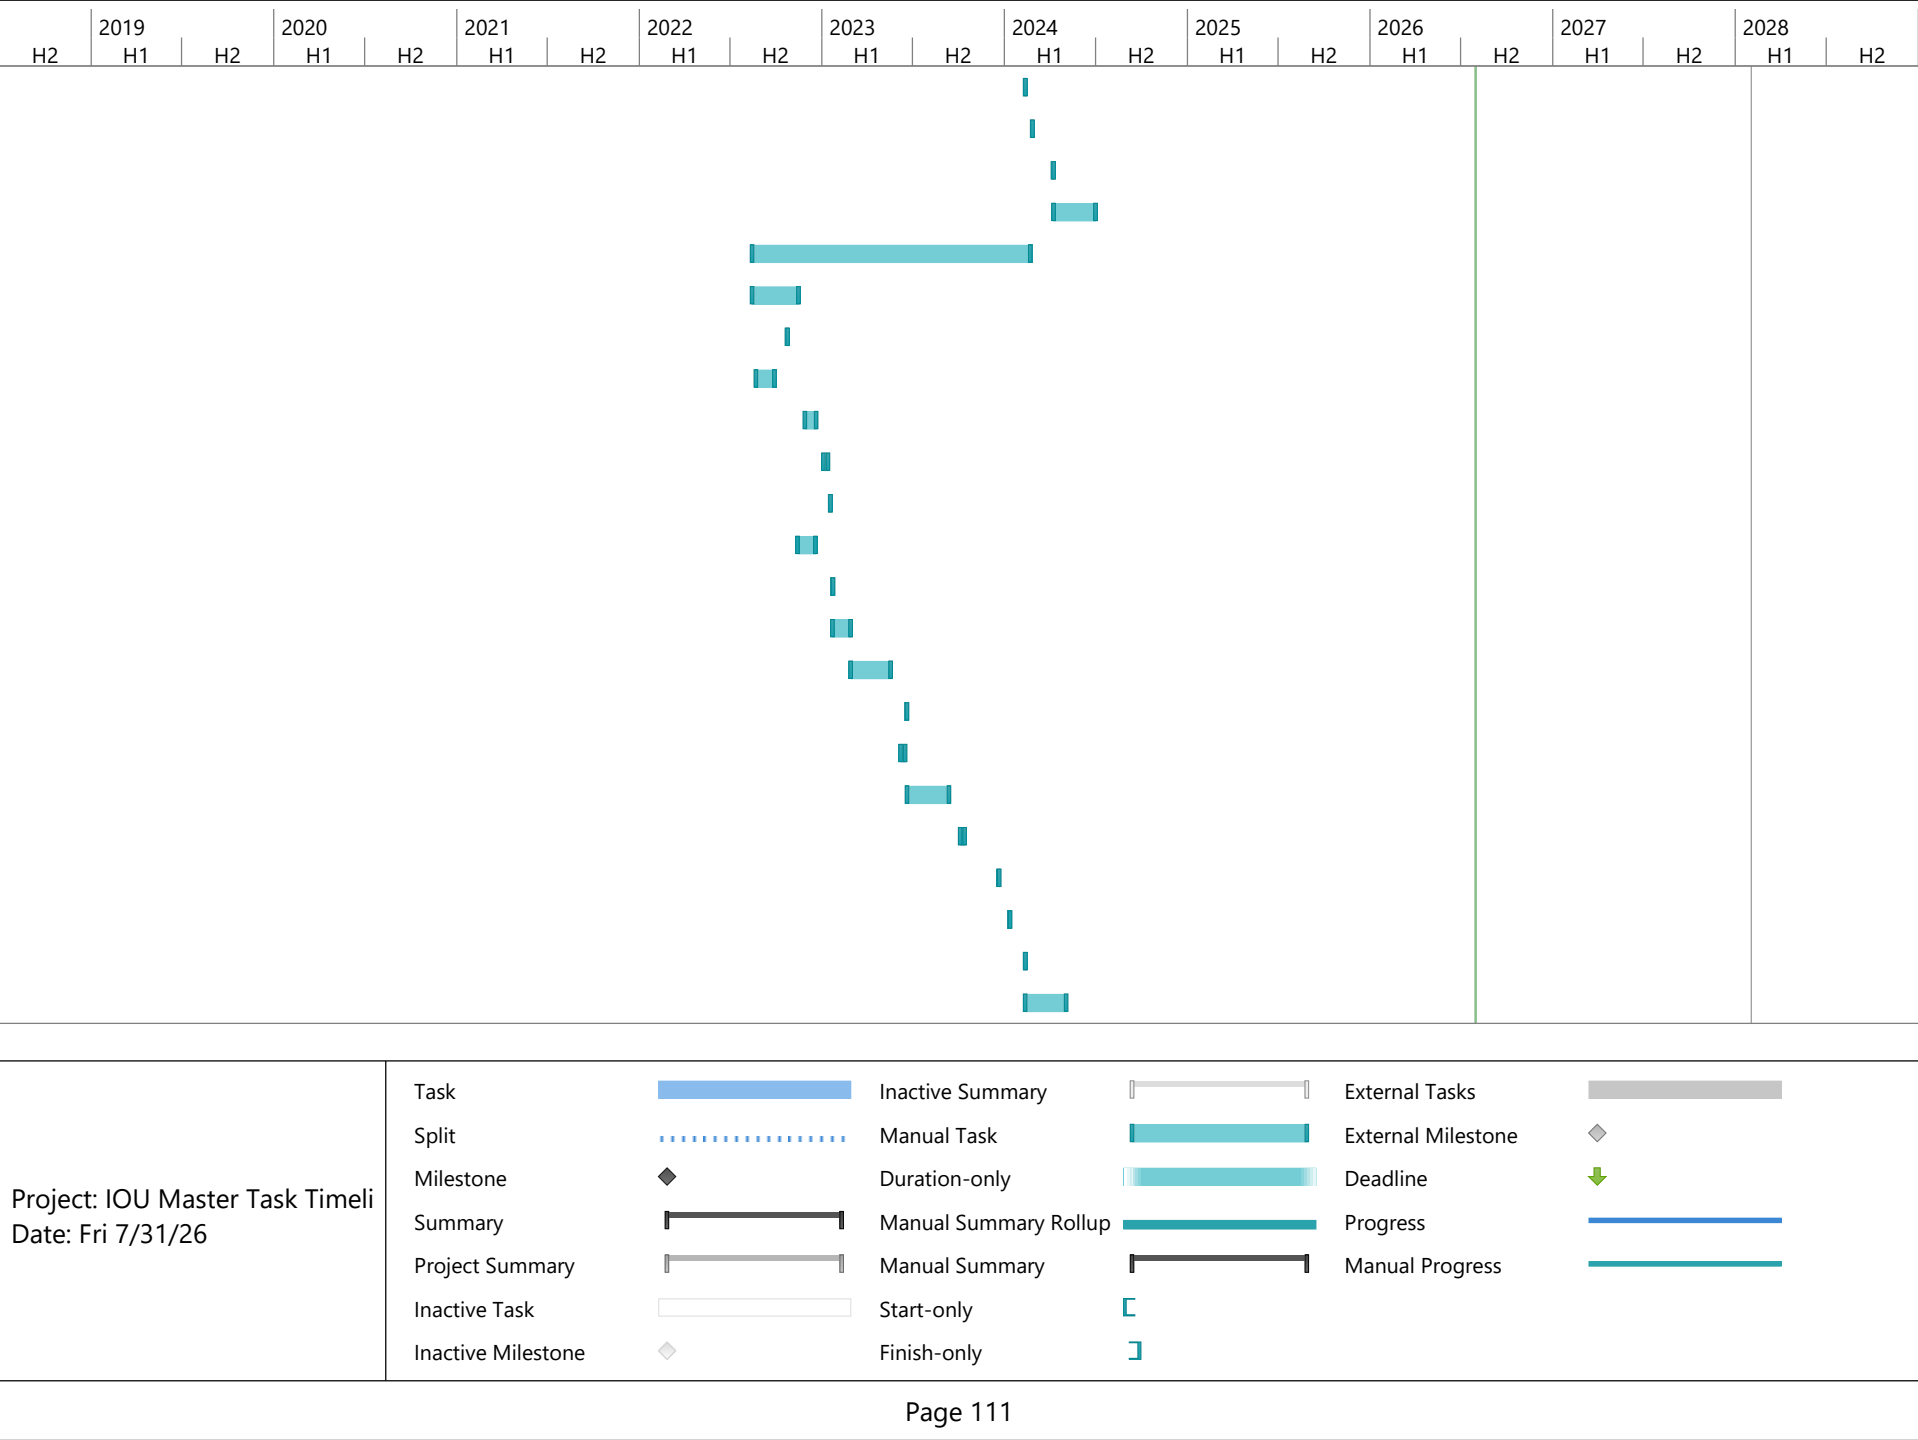


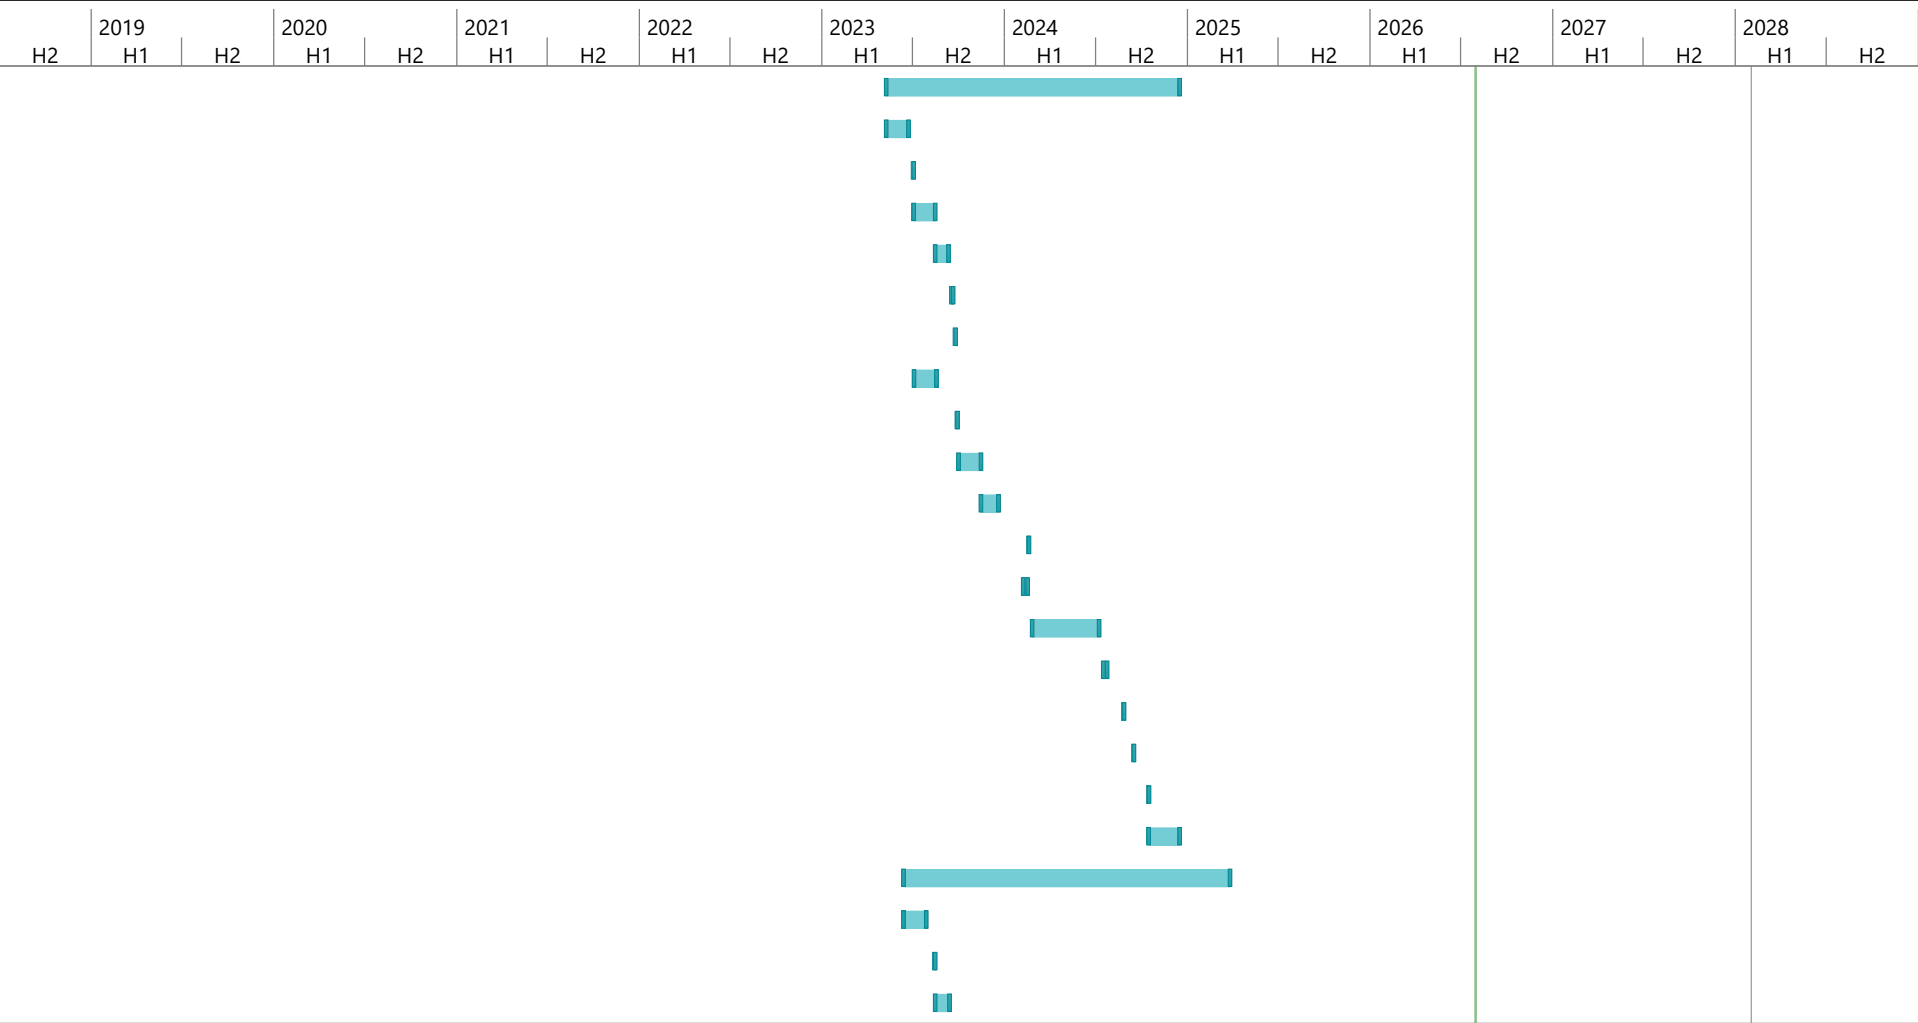
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

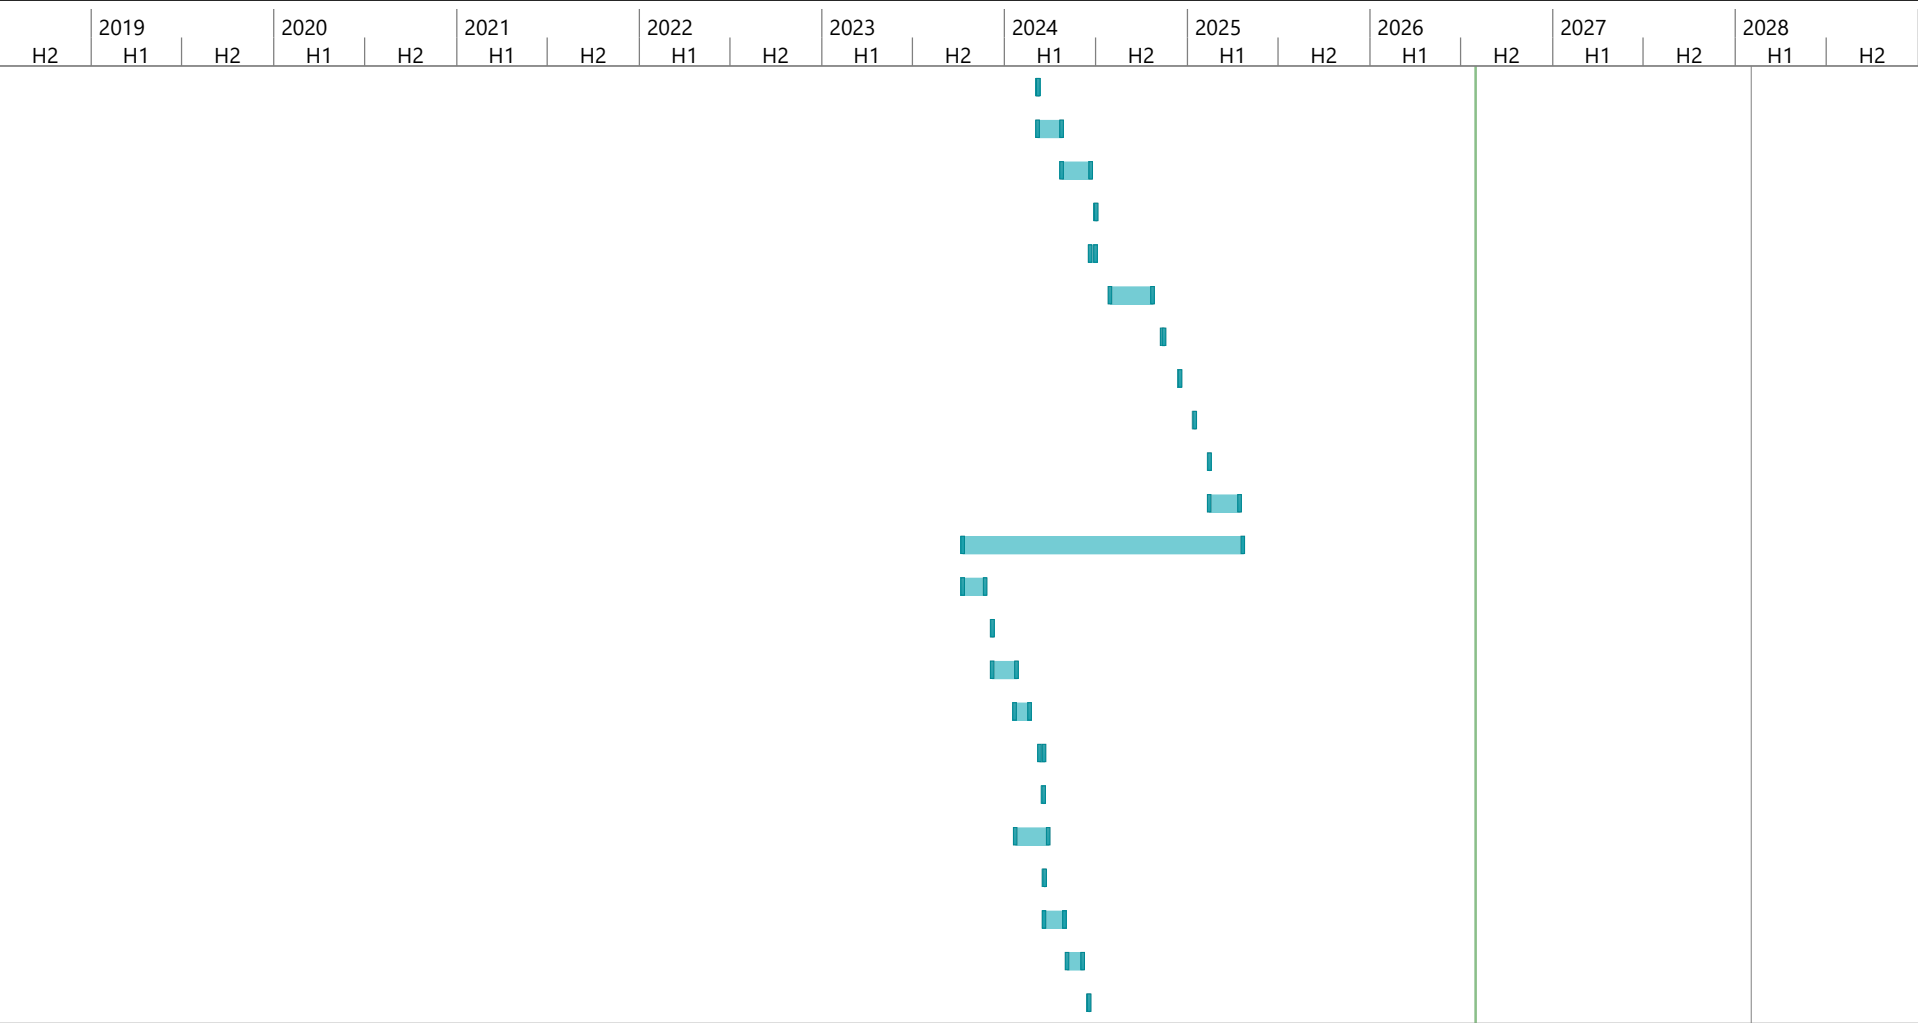





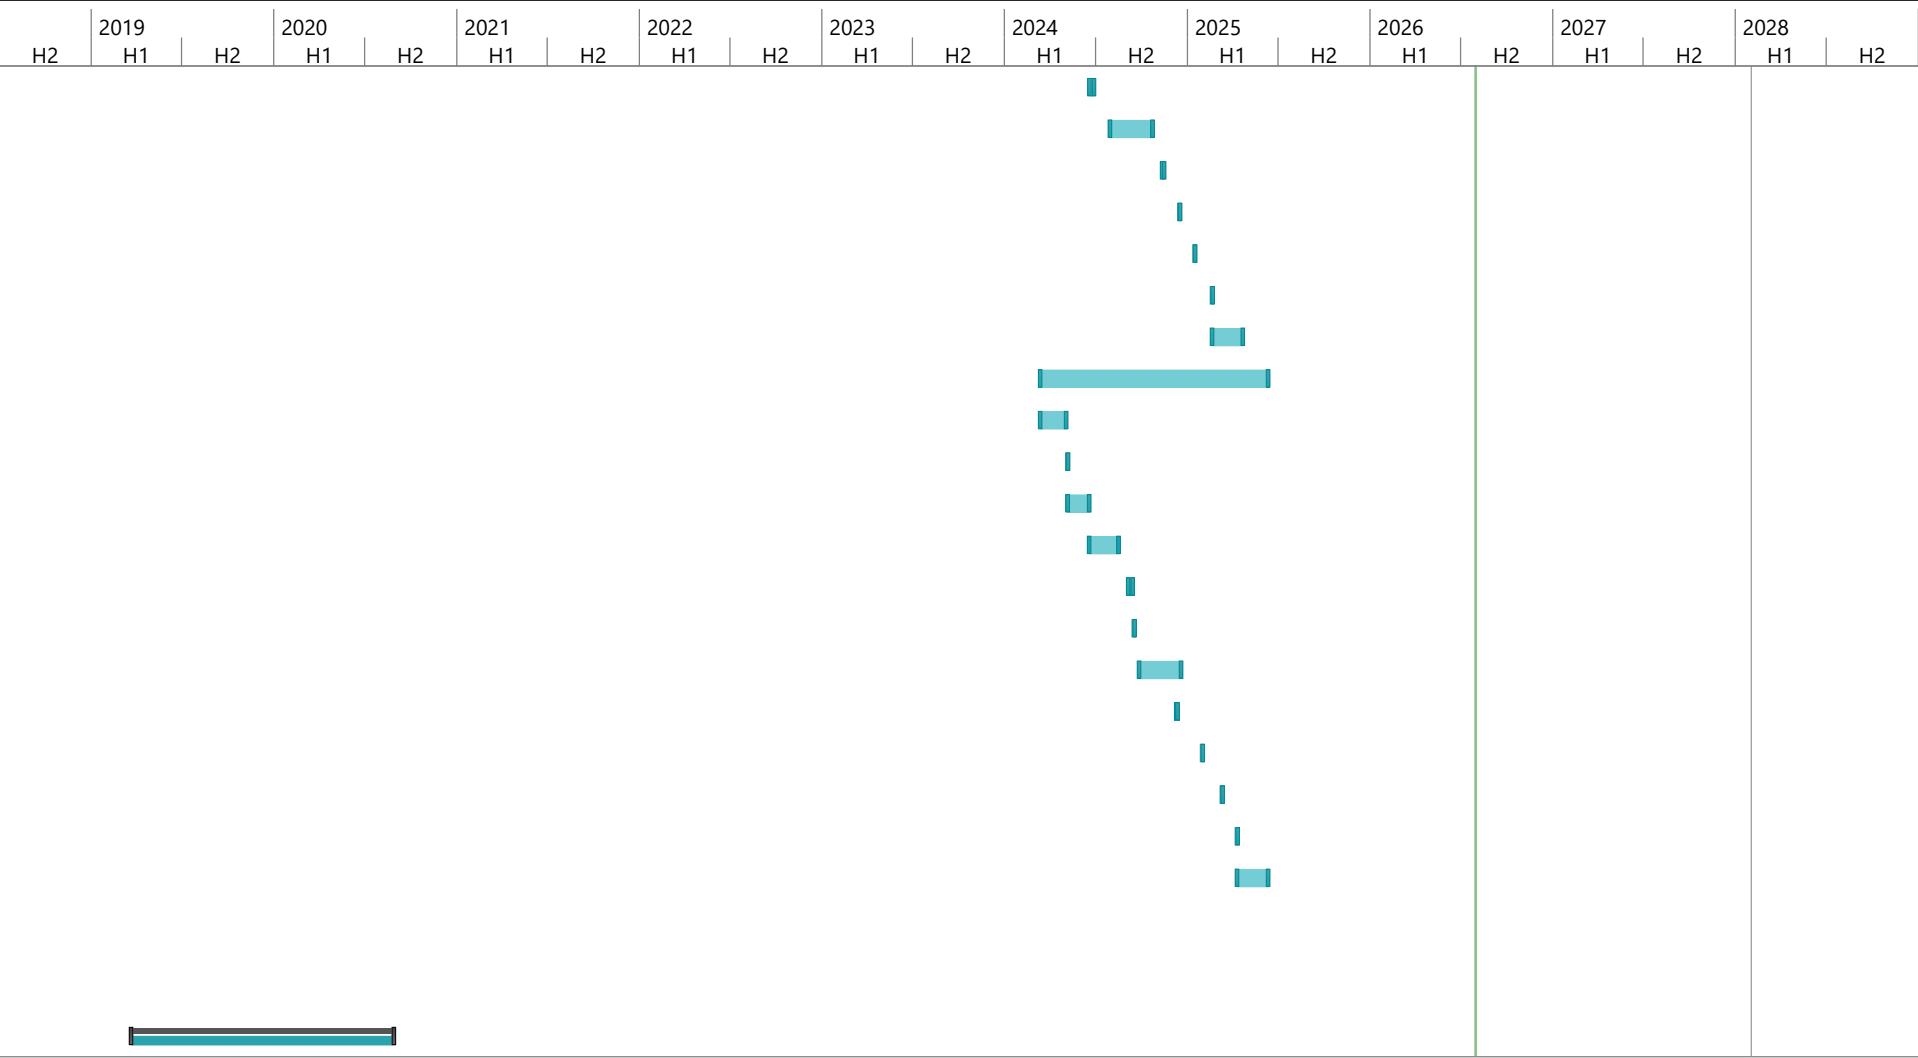


Project: IOU Master Task Timeli
Date: Fri 7/31/26

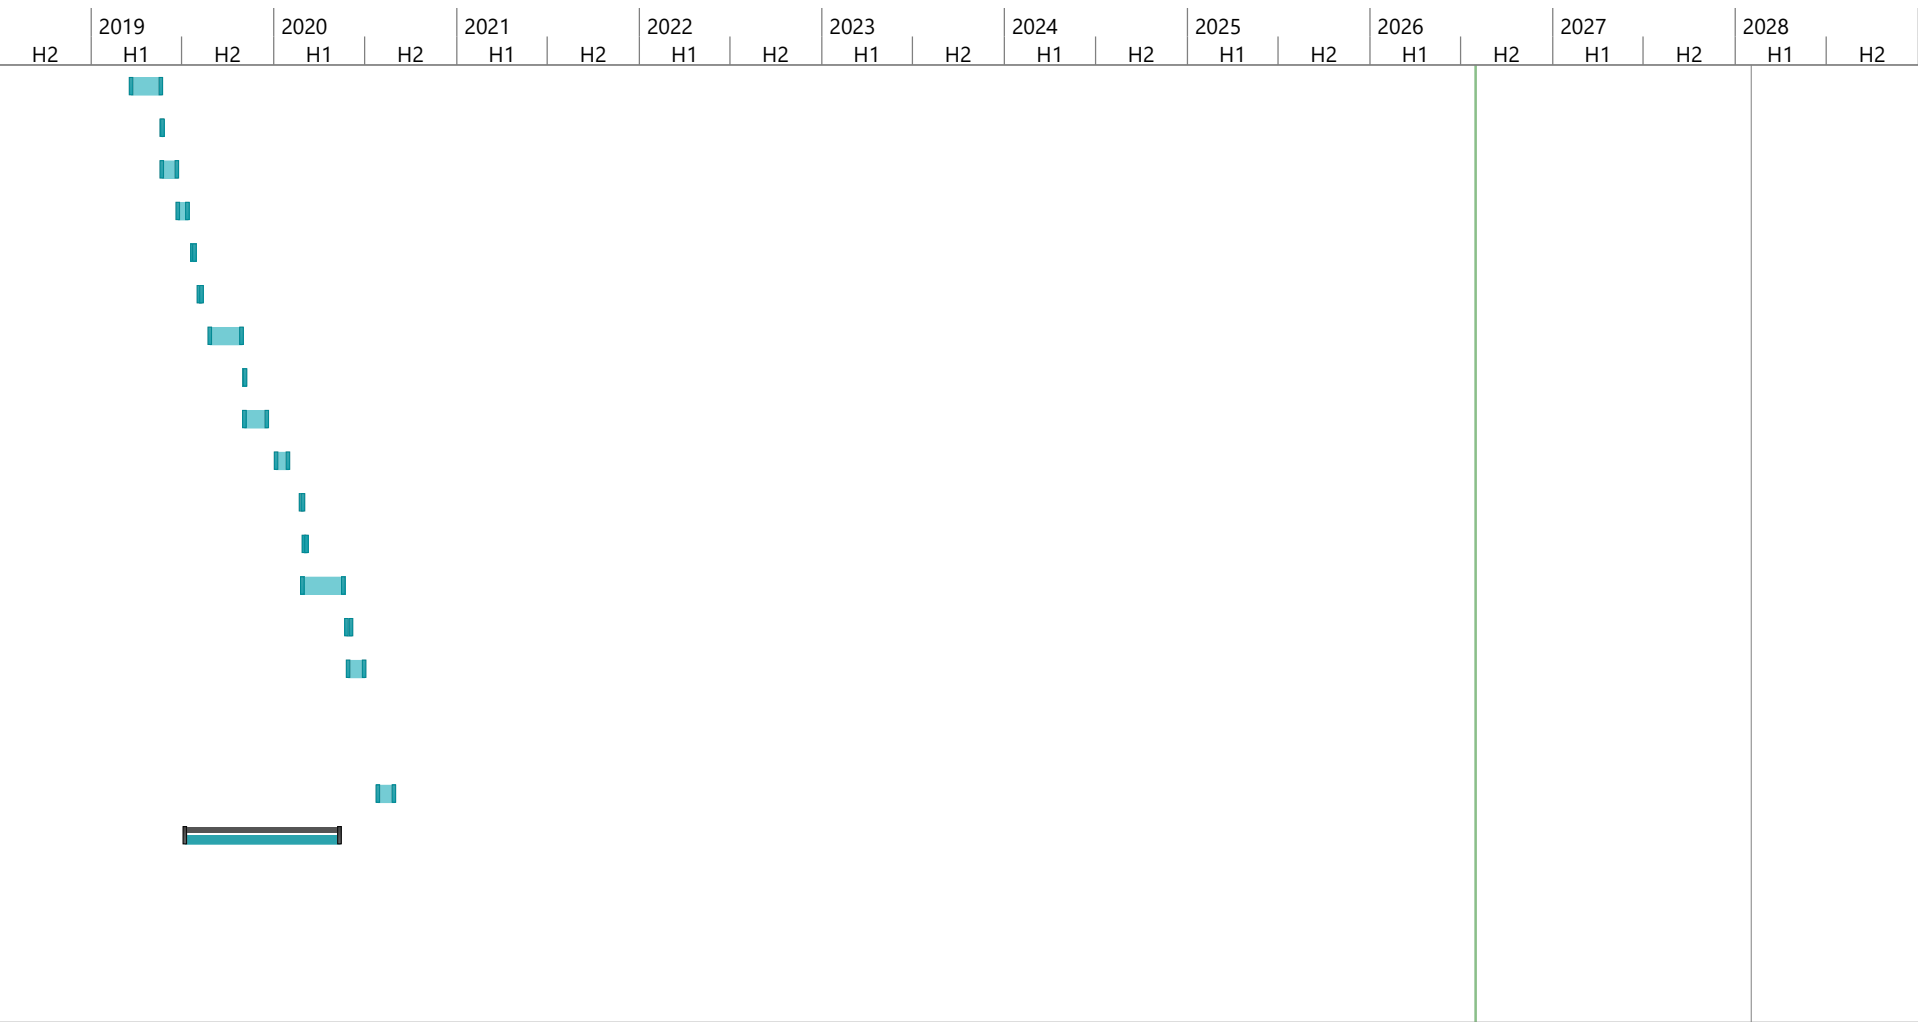
Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



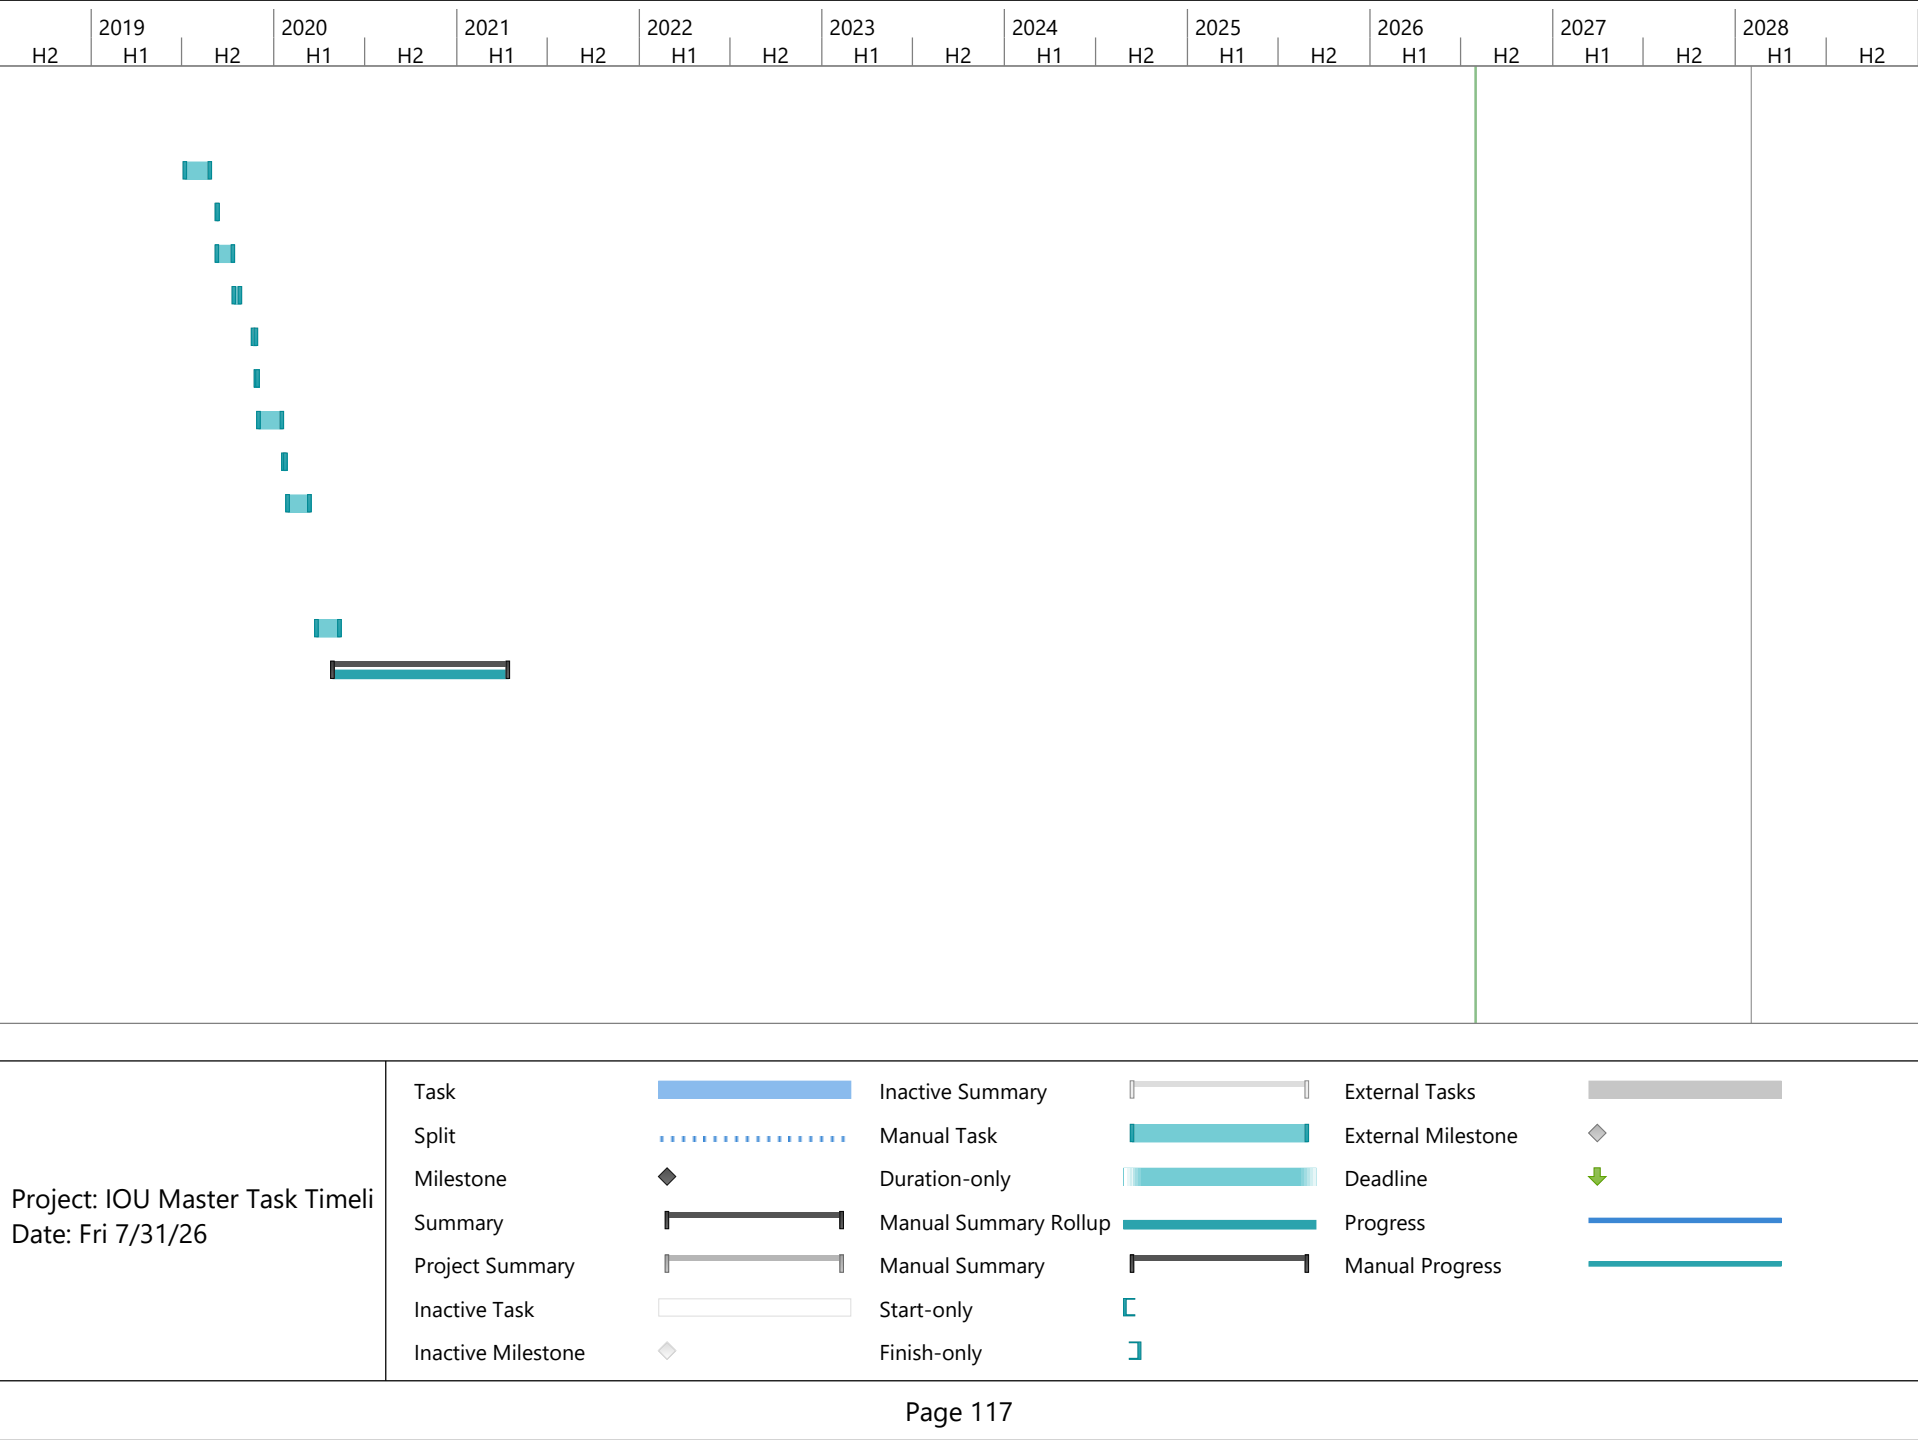
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

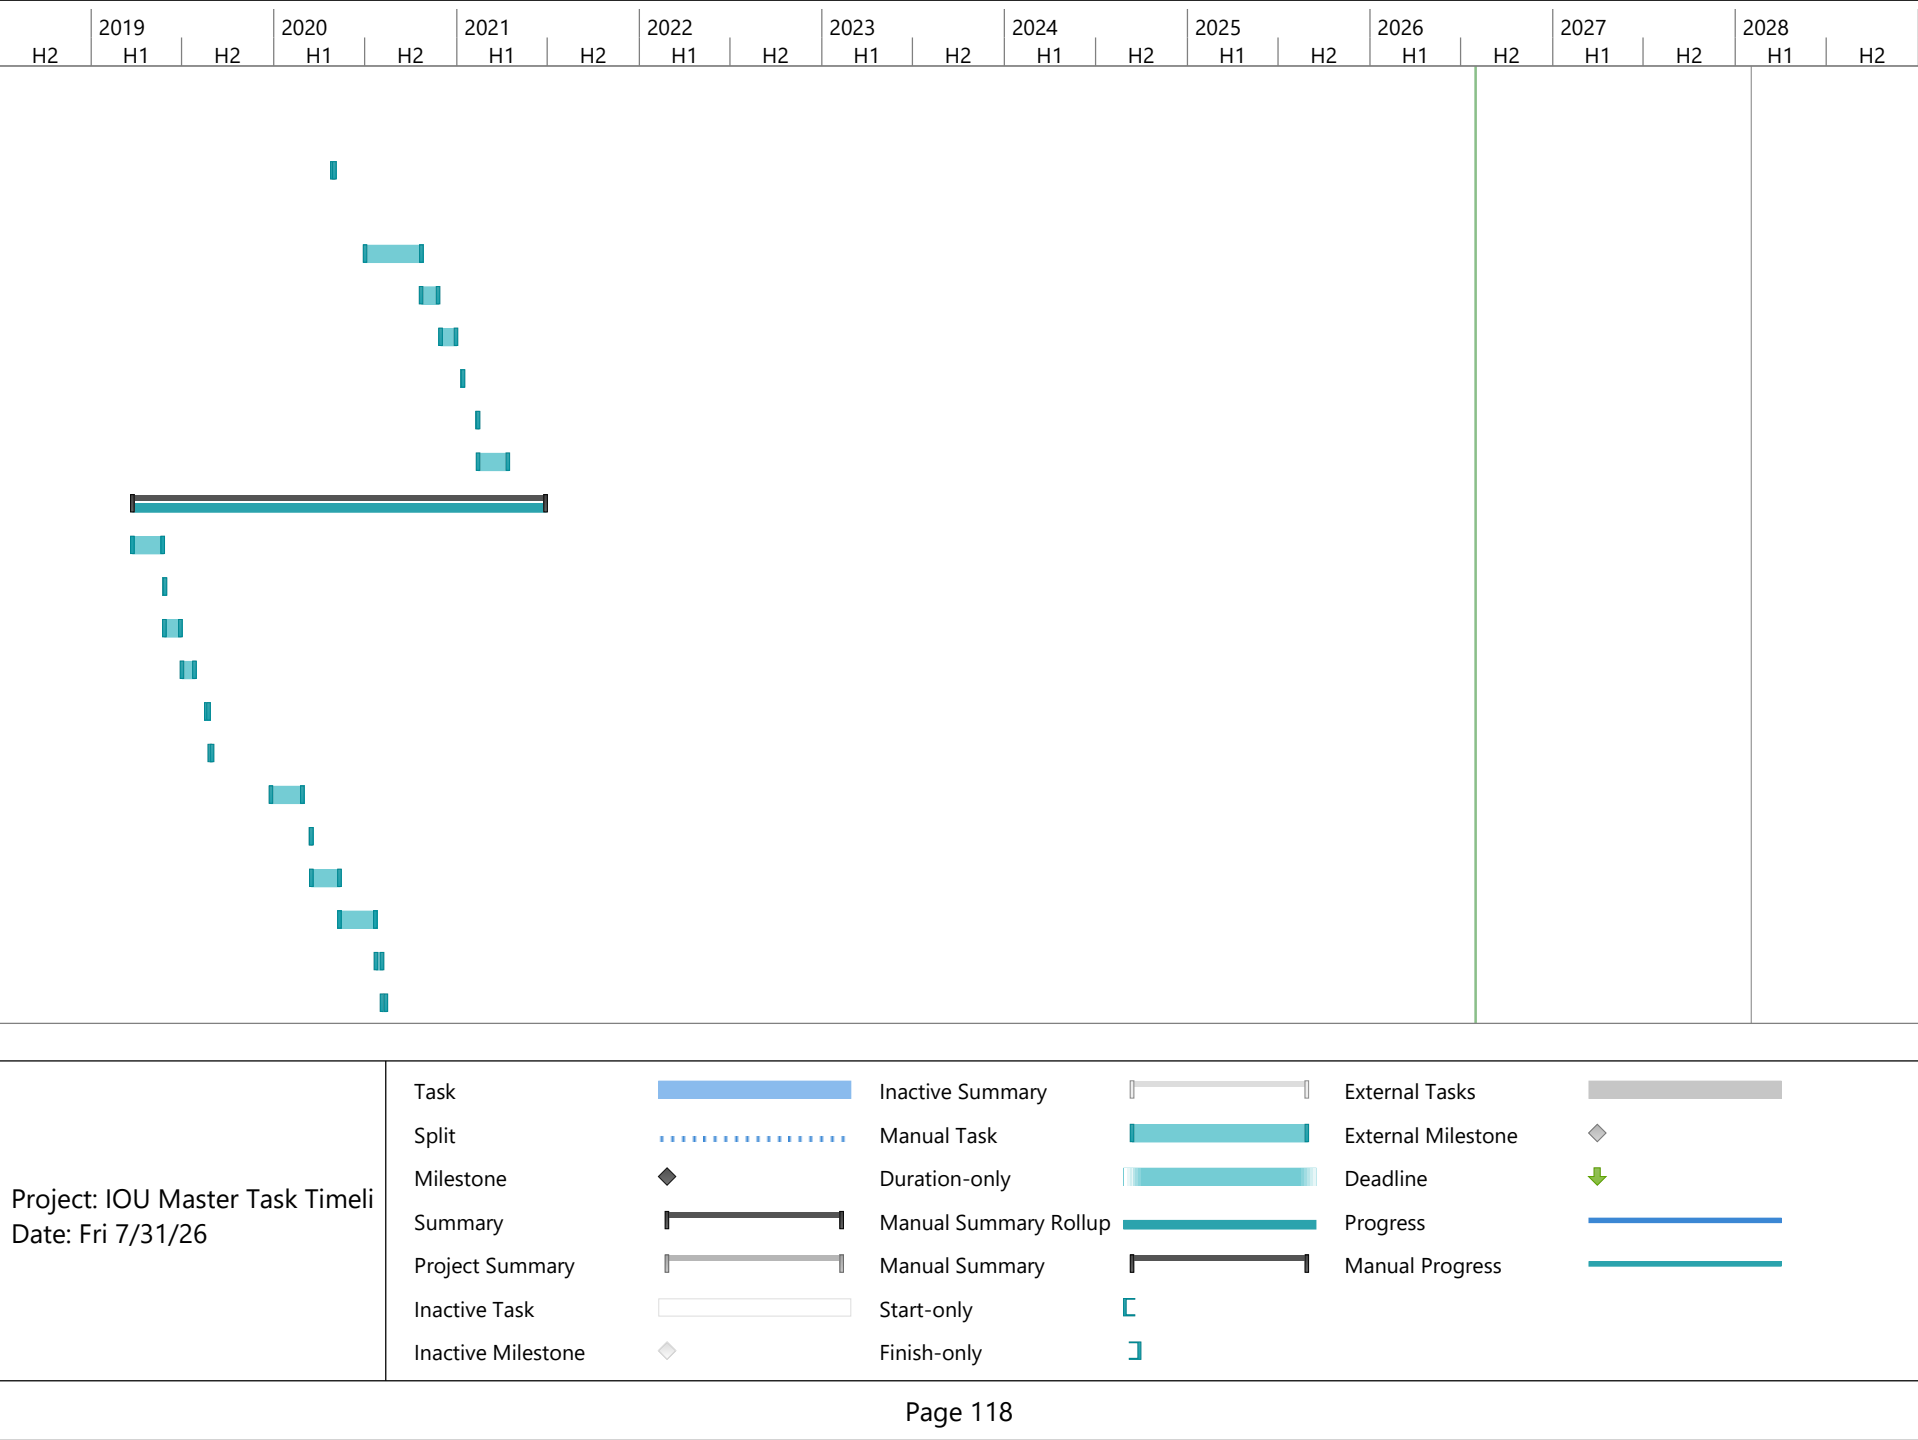


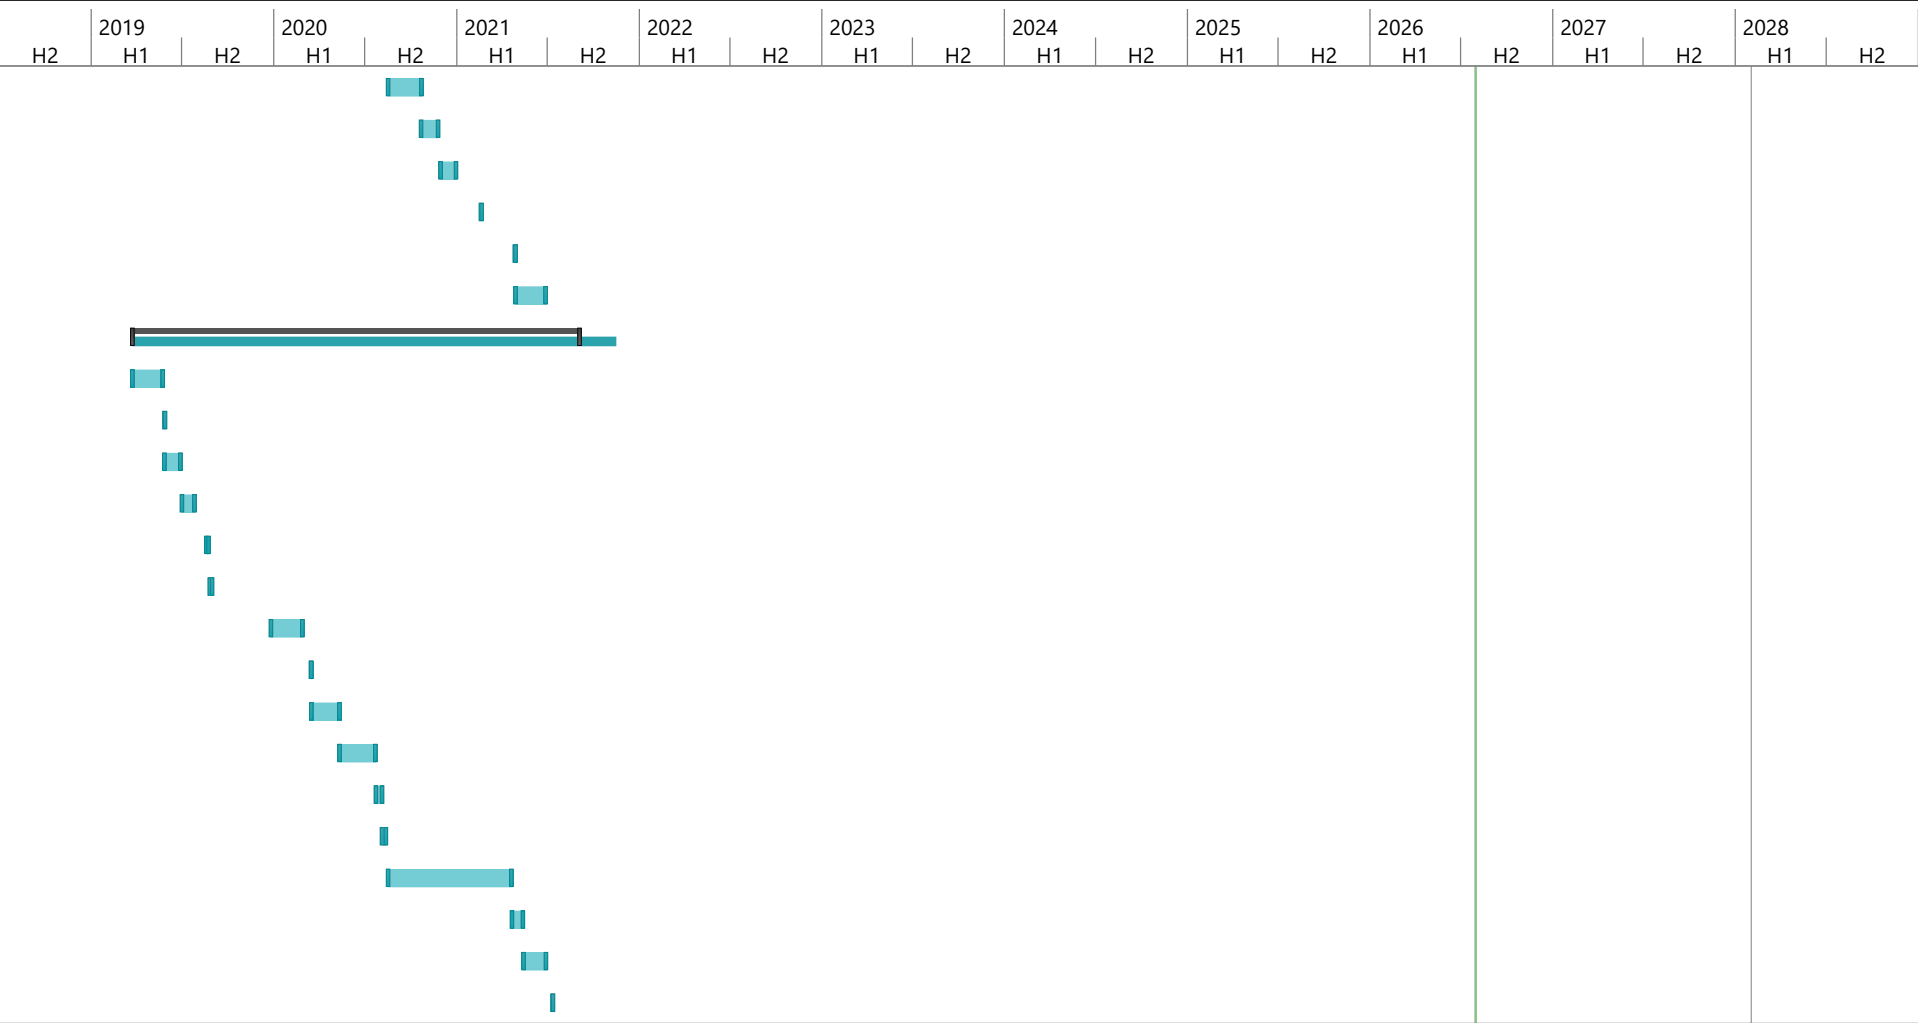
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



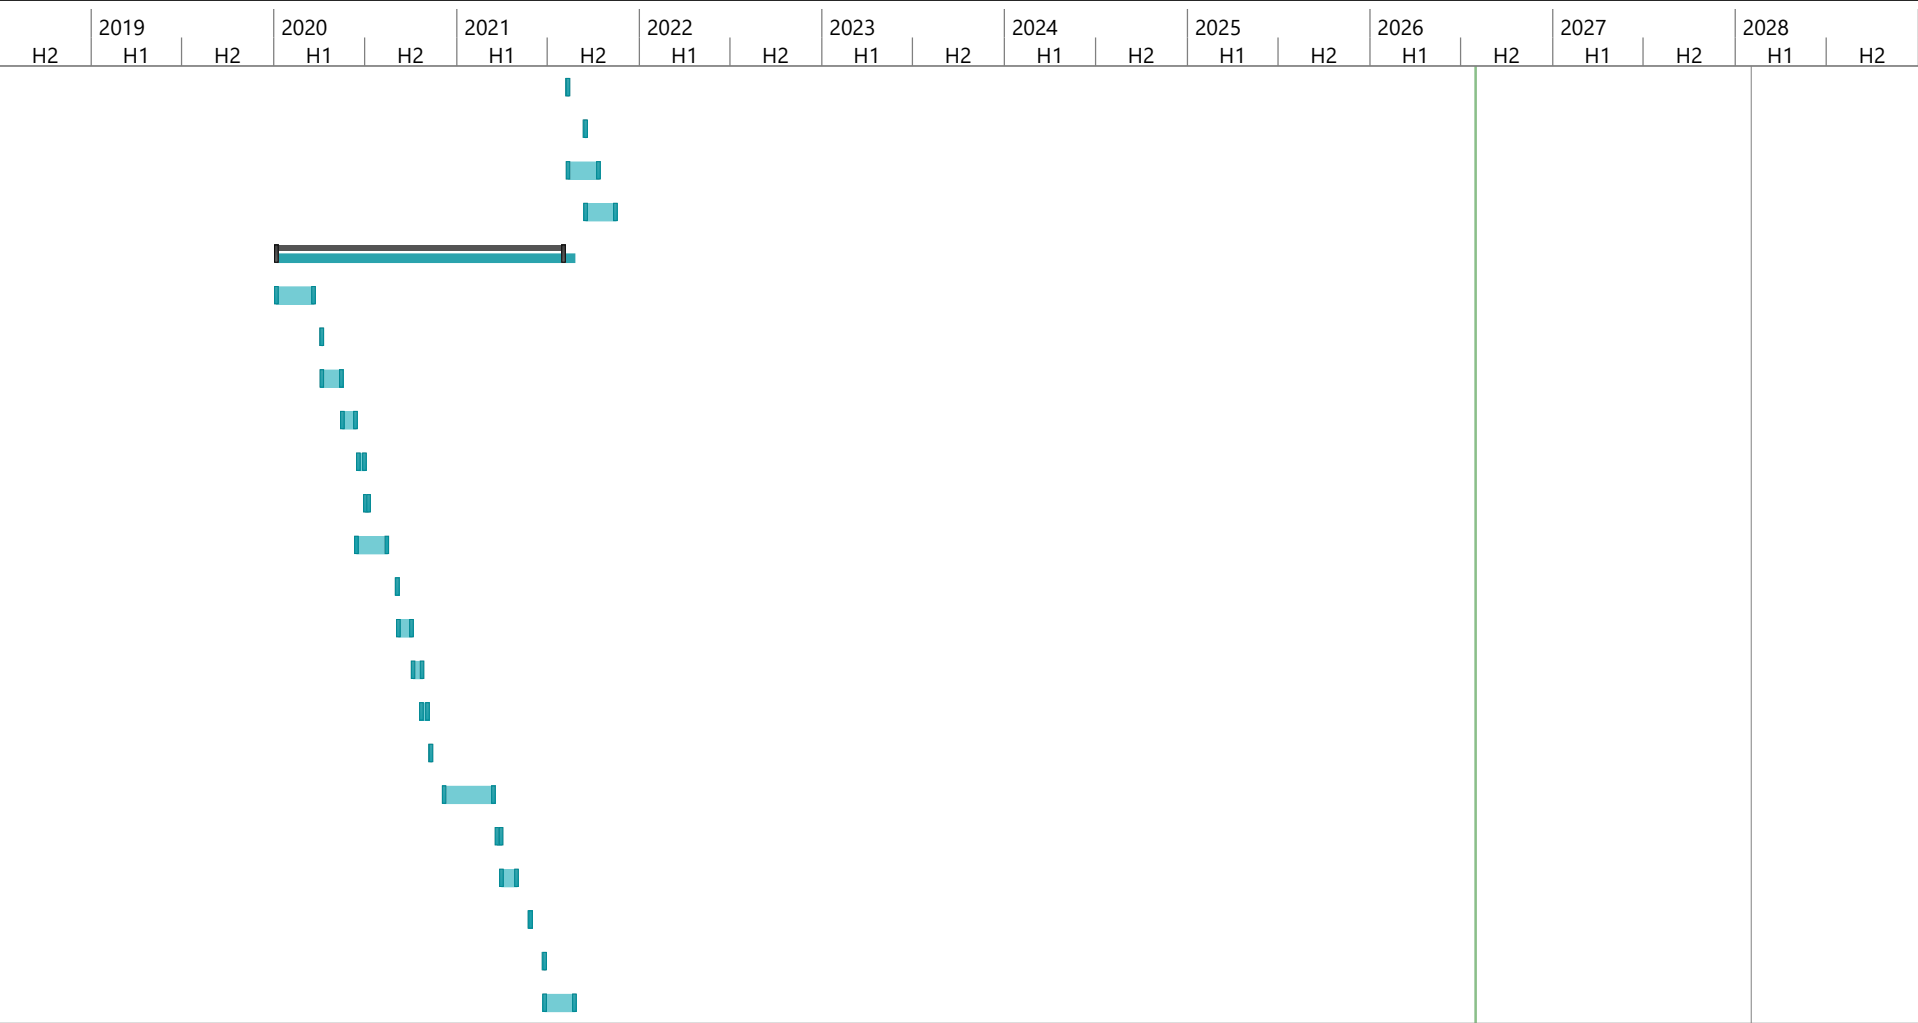
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



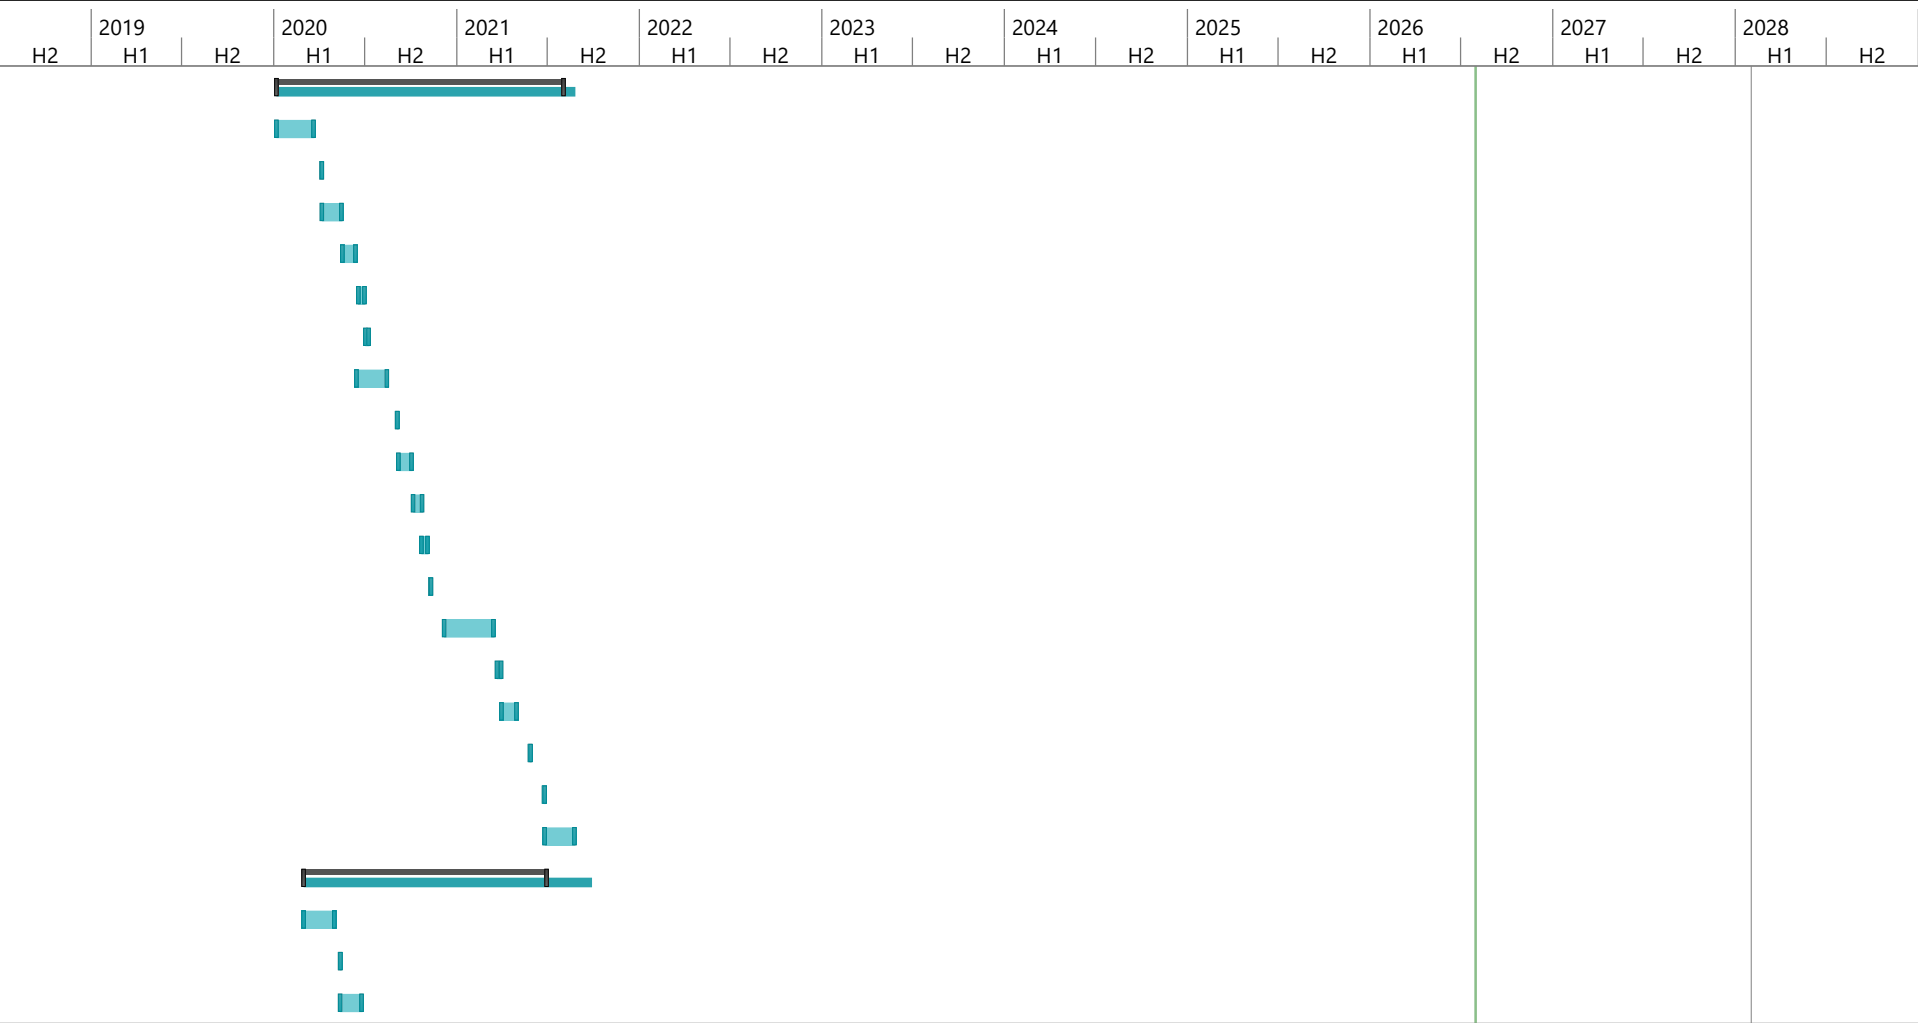




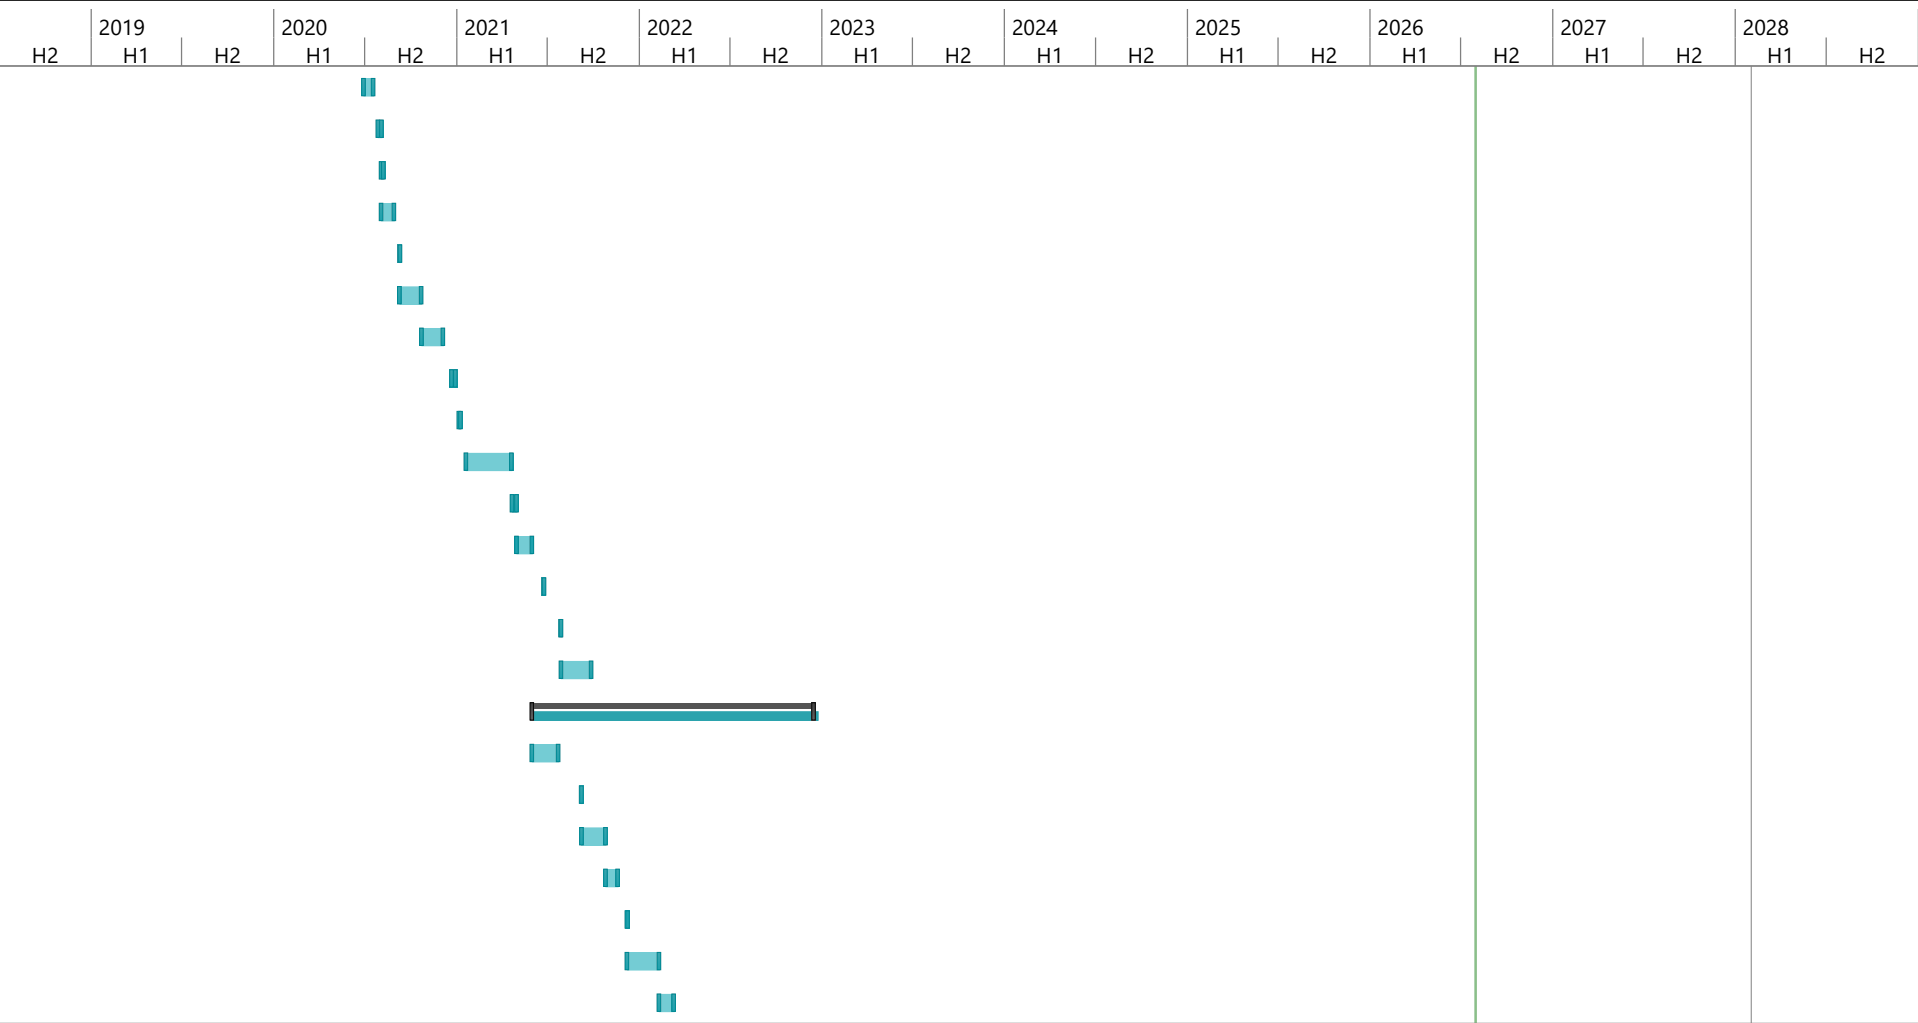
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



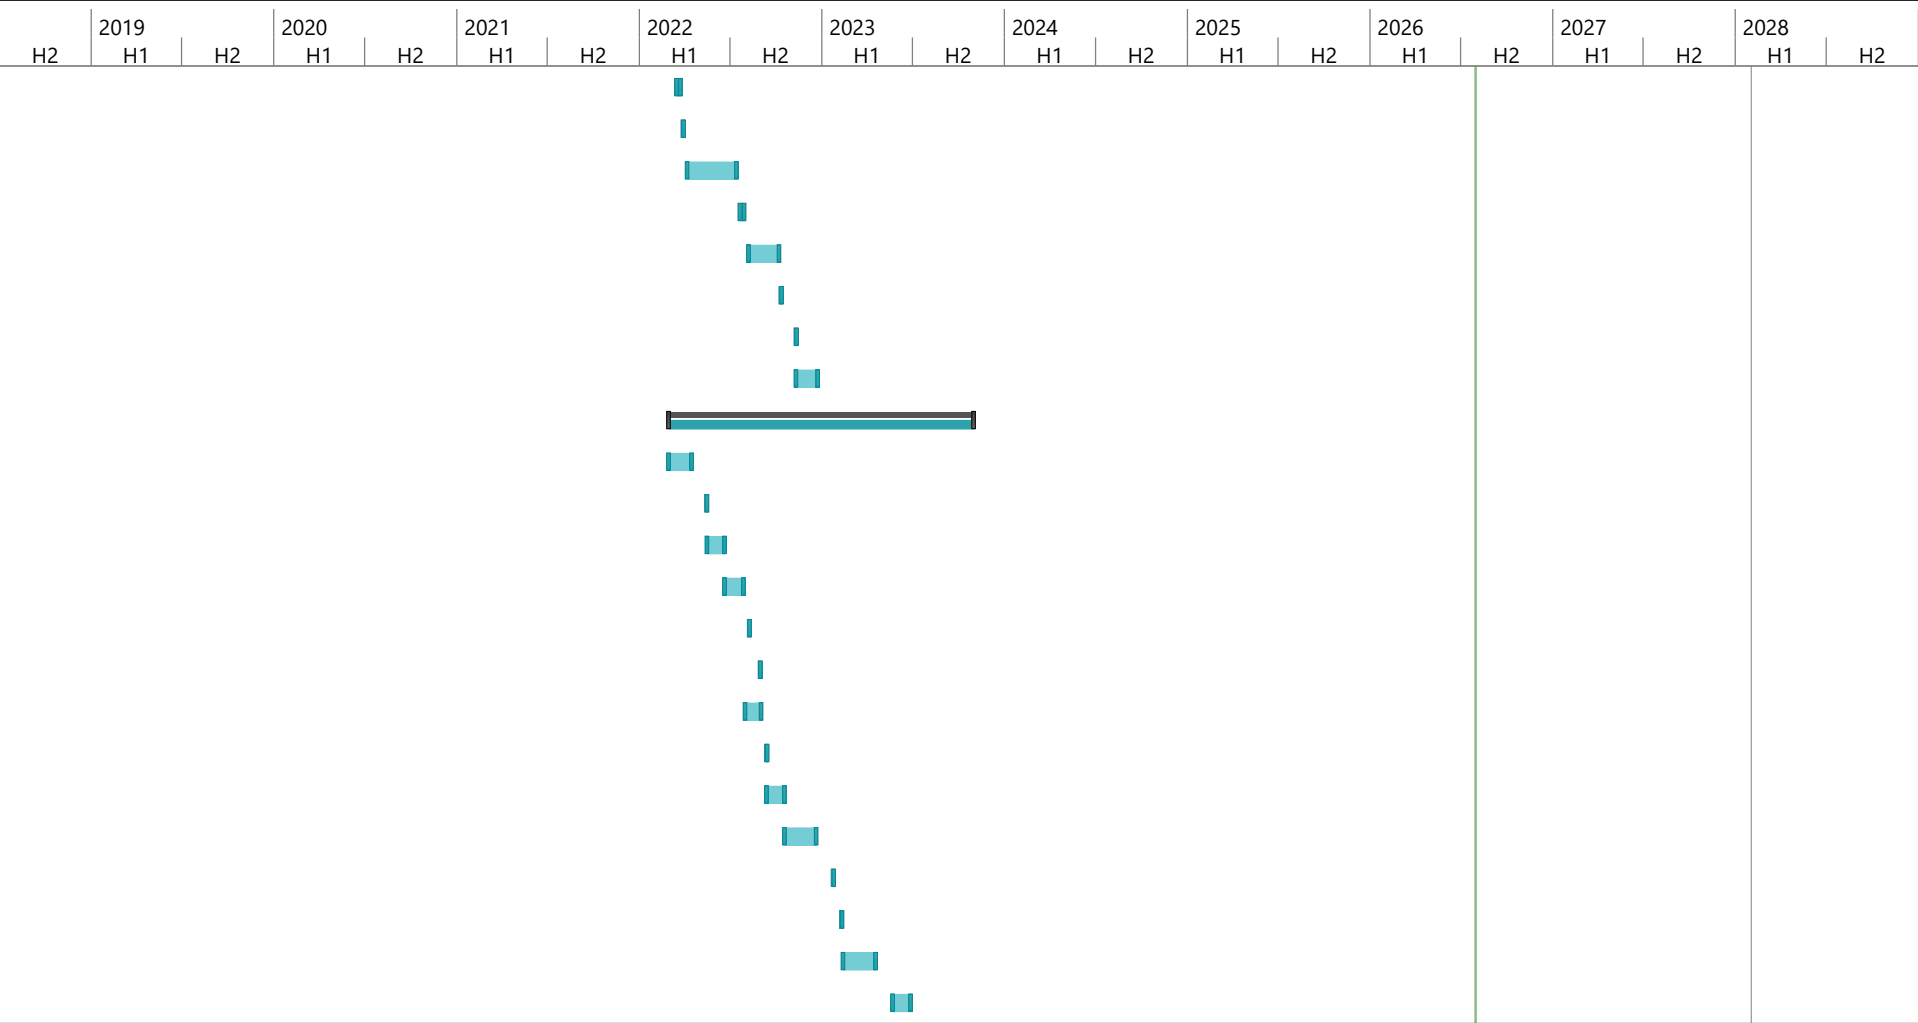
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



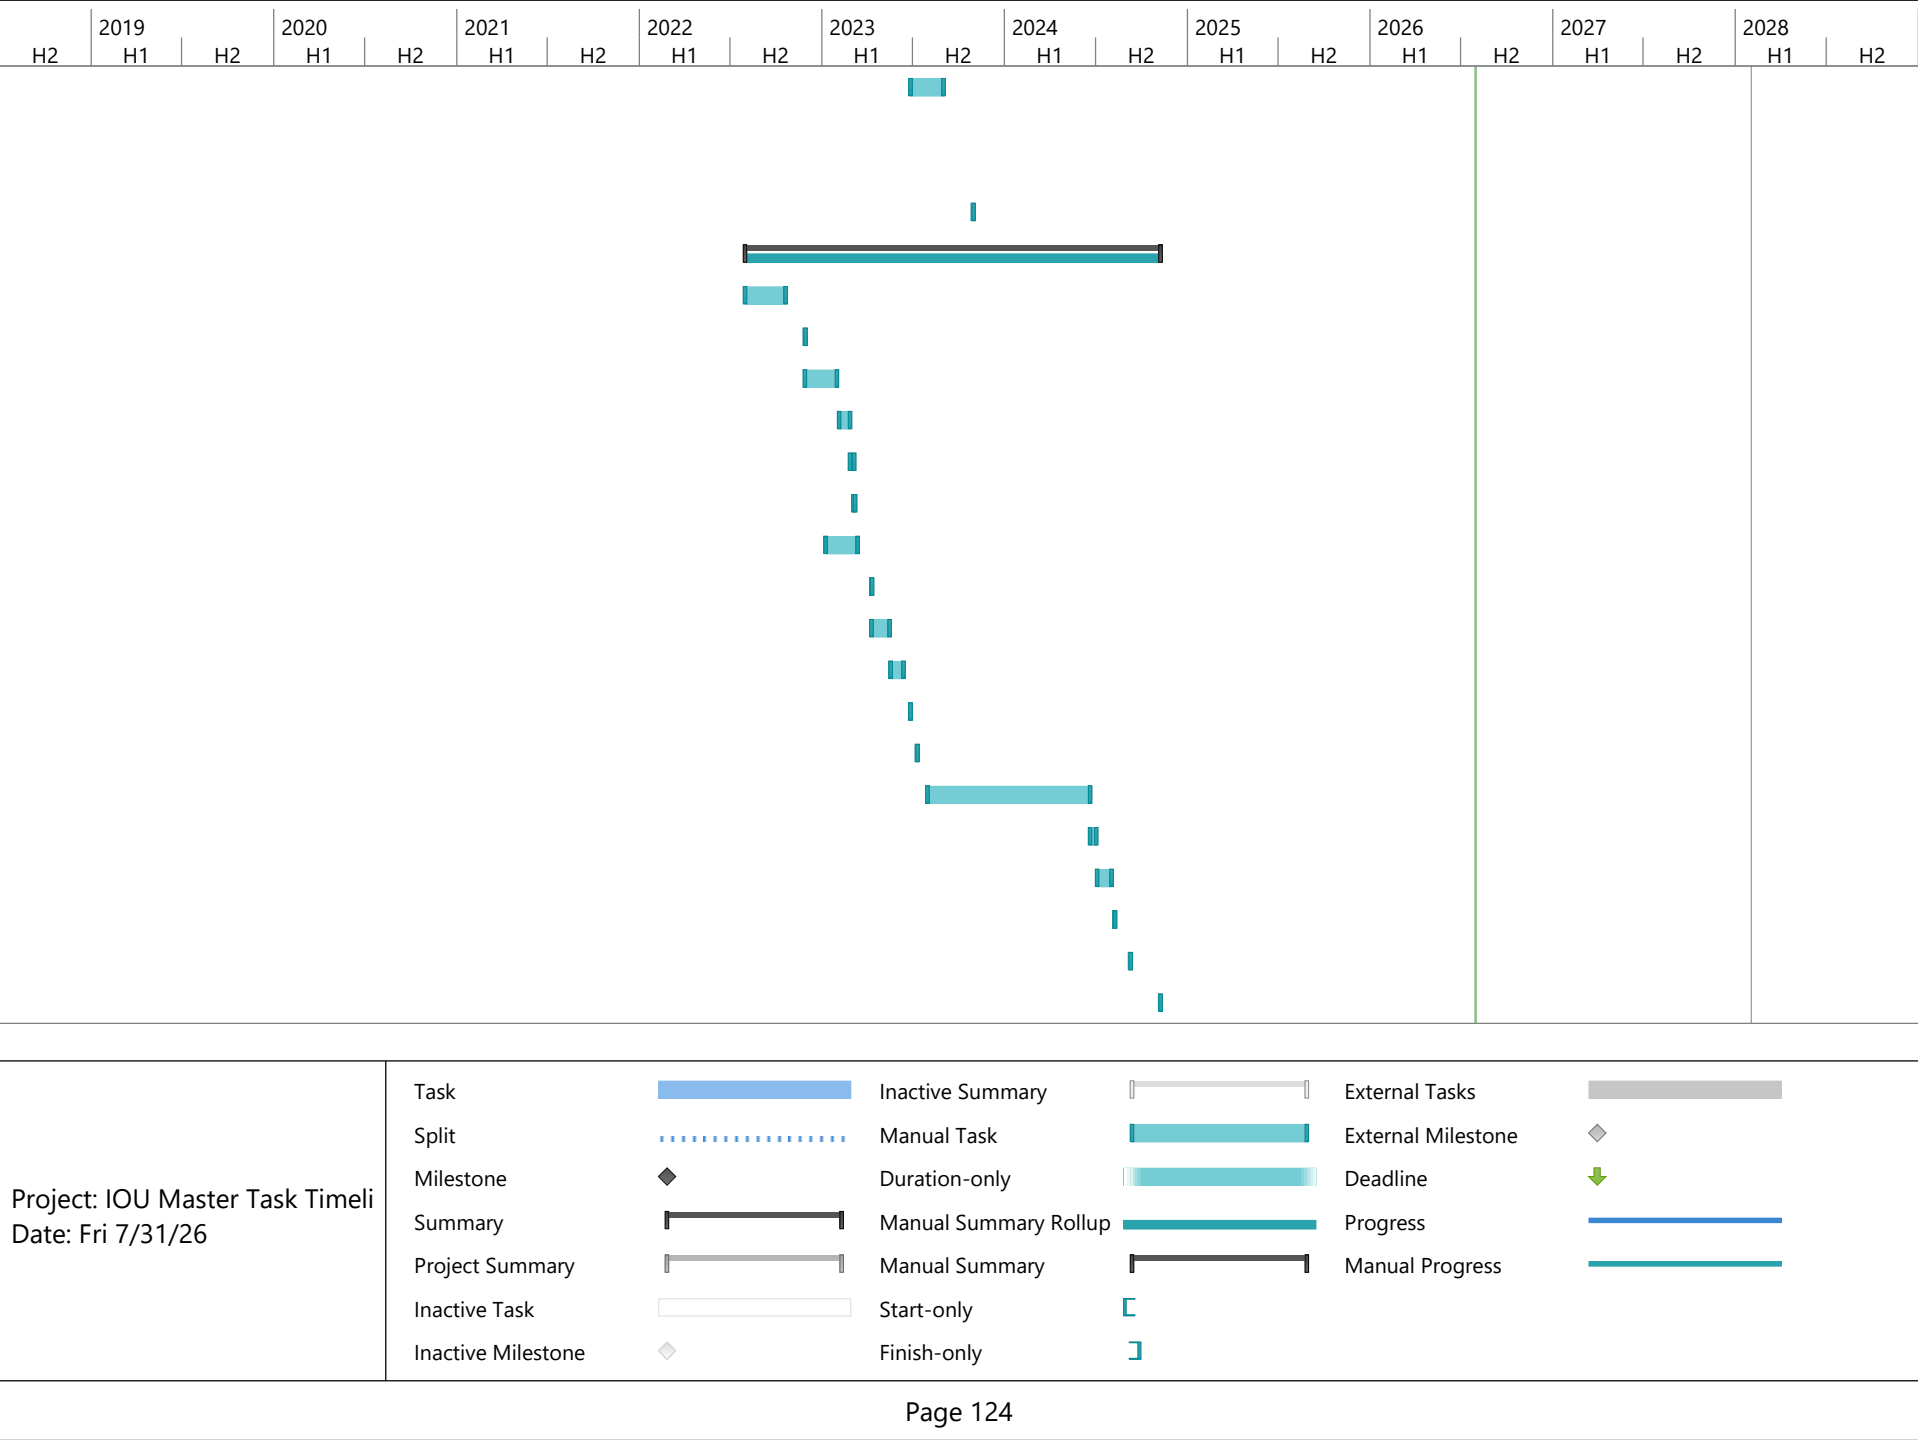
Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

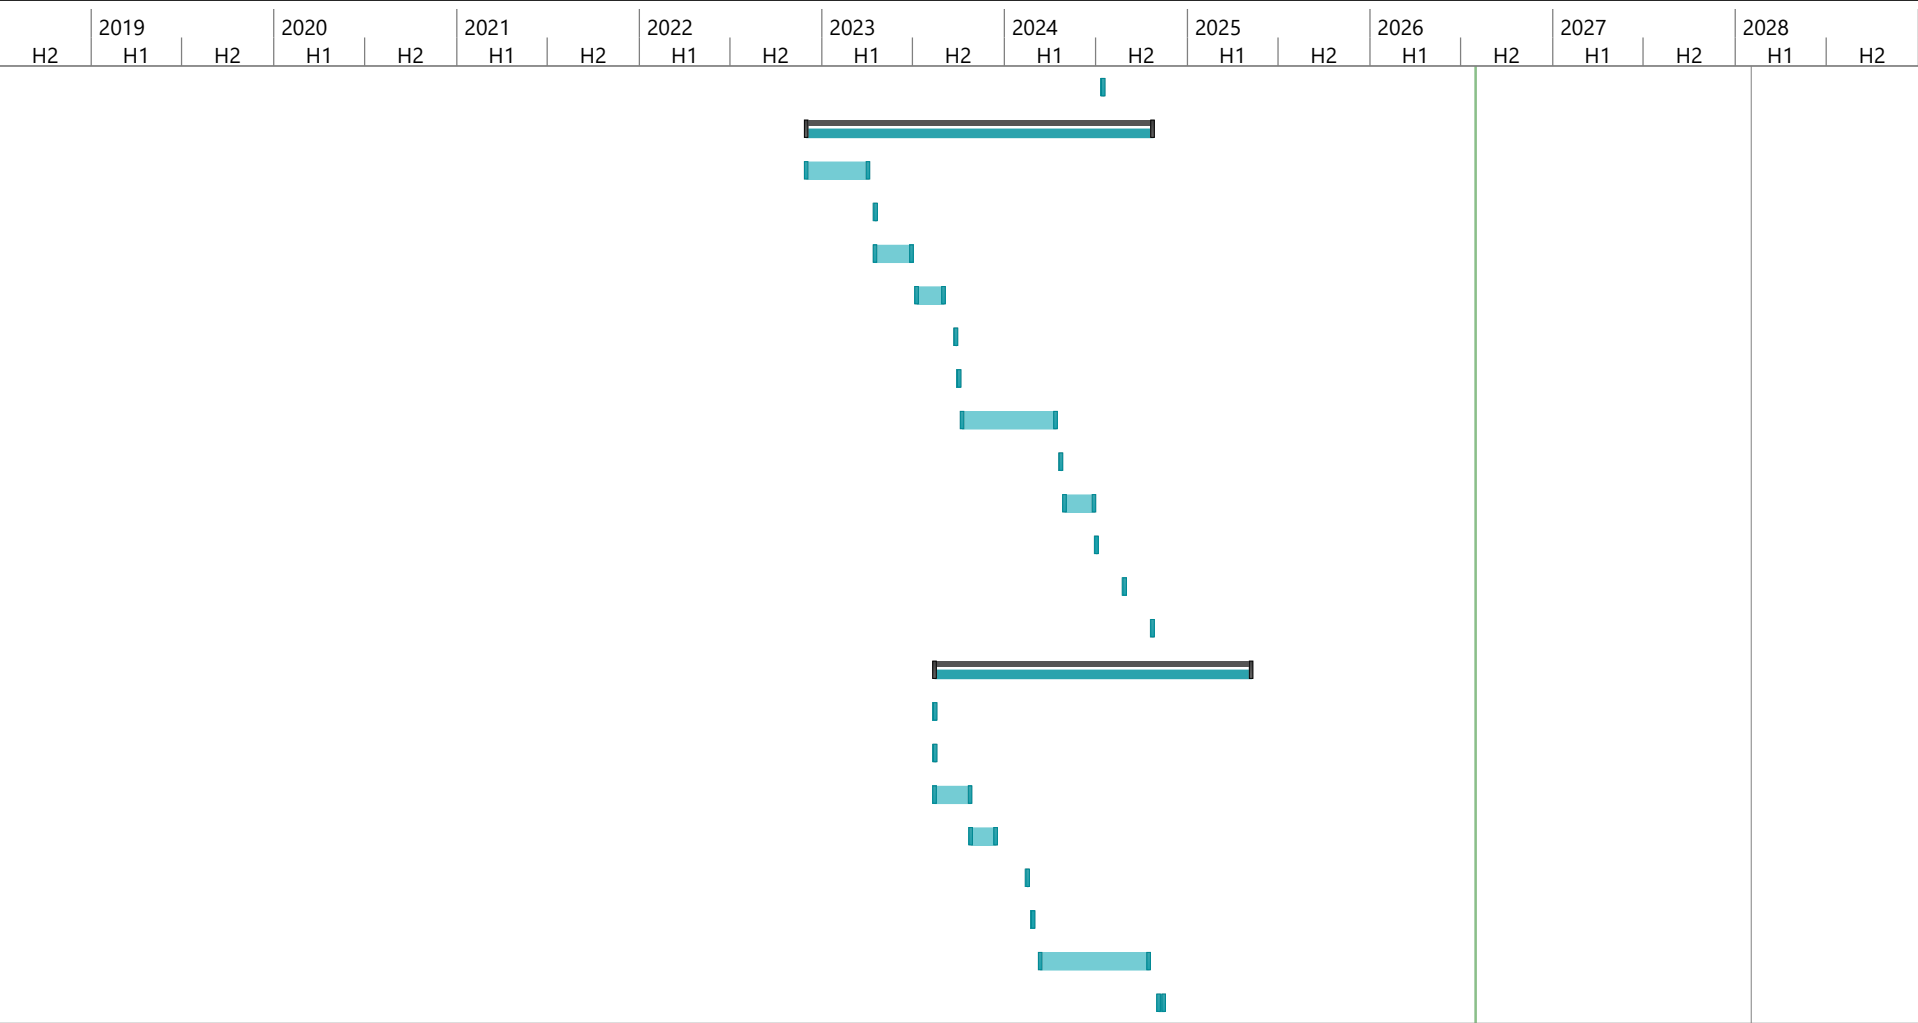


Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

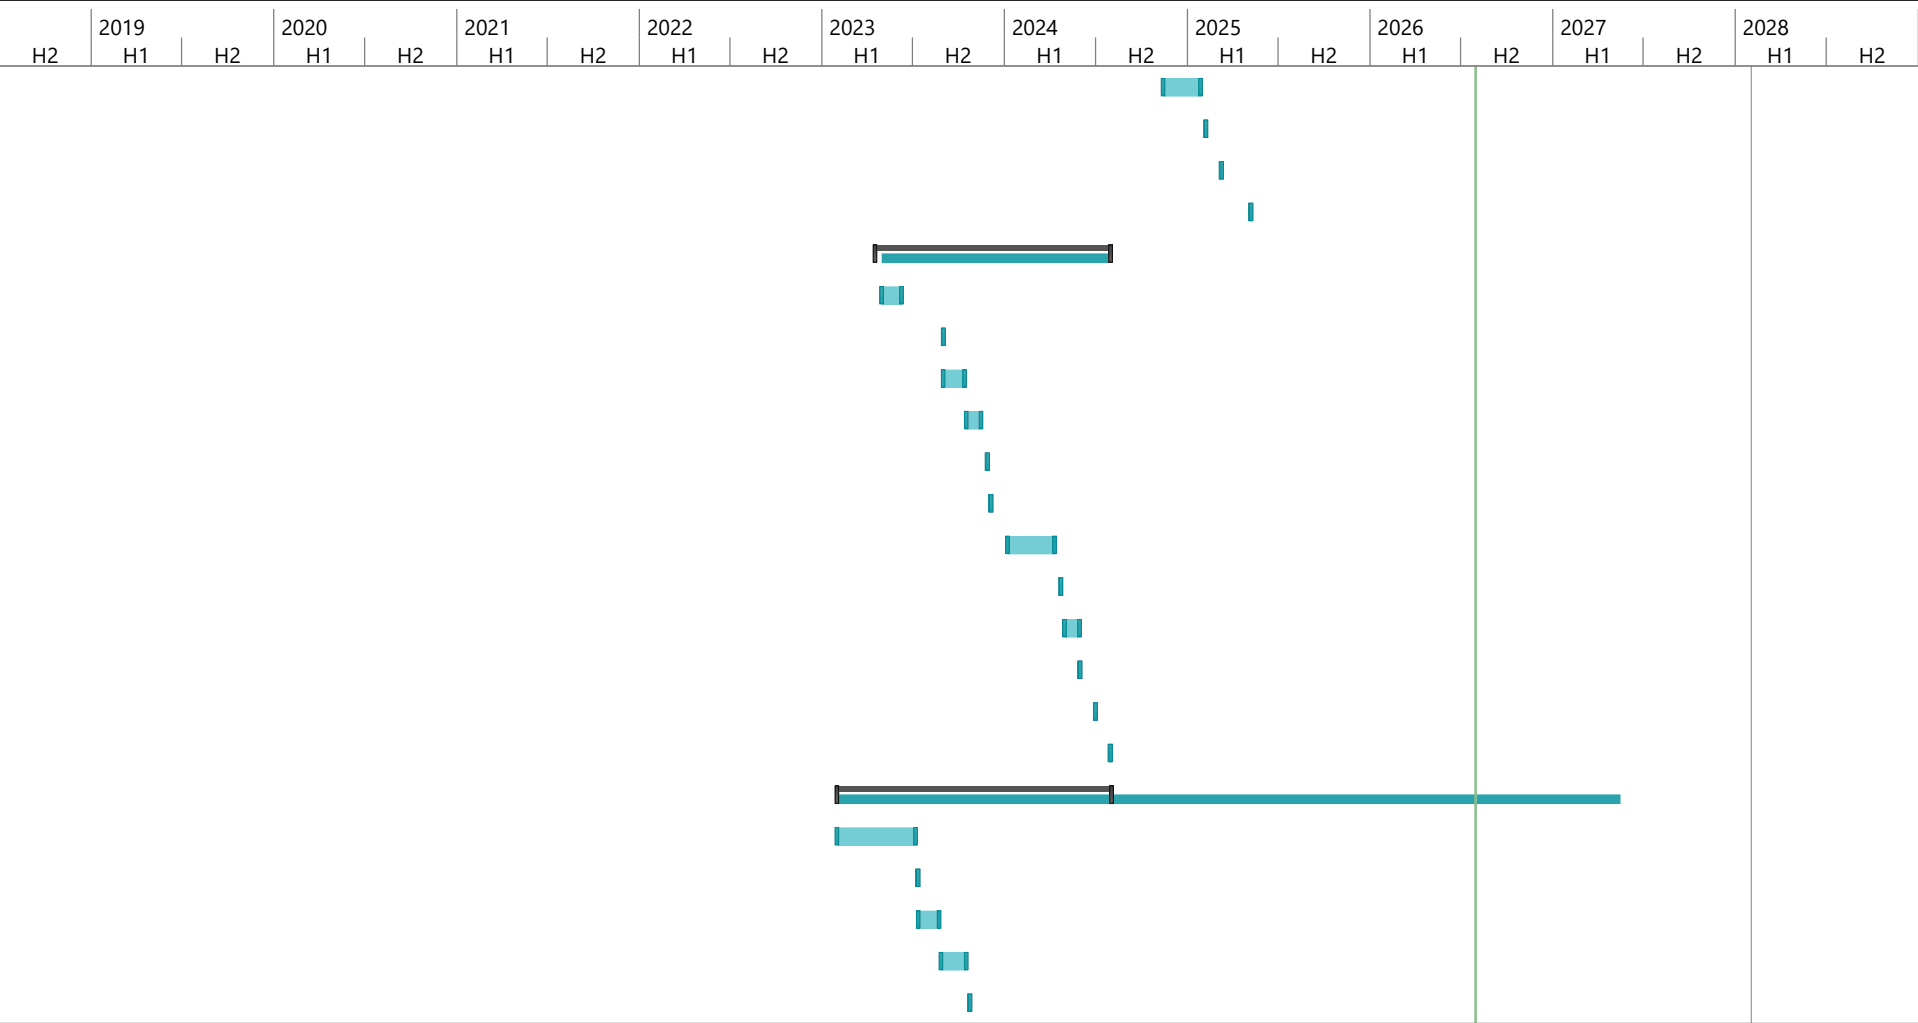


Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

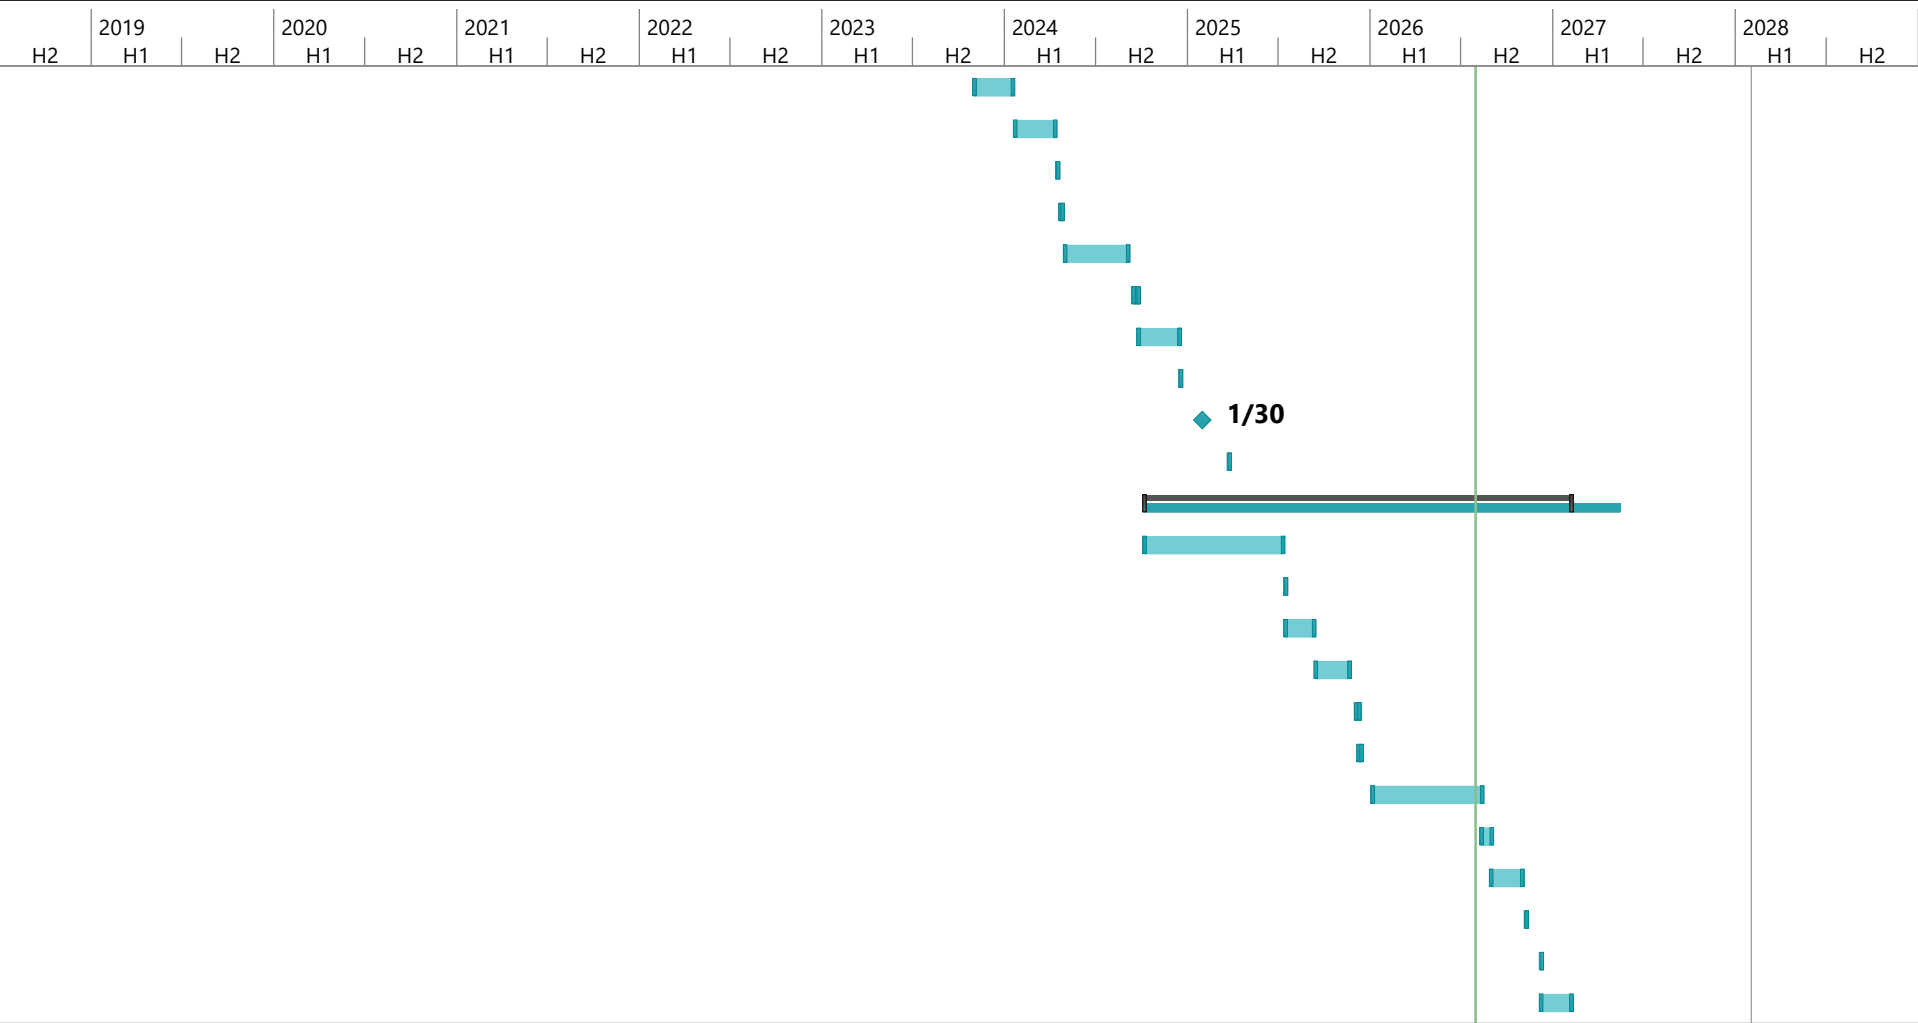




Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 7/31/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

