


ID		Task Name	Duration	Start	Finish	2018 H1
1		UPDATED as of October 1, 2025				
2		SCE - Local RCI Solicitation	679 days	Tue 8/21/18	Fri 3/26/21	
3		SCE - RFA Preparation	40 days	Tue 8/21/18	Mon 10/15/18	
4		SCE - RFA Release	1 day	Fri 11/9/18	Fri 11/9/18	
5		SCE - RFA Abstract Creation Duration	30 days	Sat 11/10/18	Thu 12/20/18	
6		SCE - RFA Evaluation	82 days	Fri 12/21/18	Mon 4/15/19	
7		SCE - RFA Review with EE PRG	1 day	Tue 4/16/19	Tue 4/16/19	
8		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/21/19	Tue 5/21/19	
9		SCE - RFP Preparation	175 days	Wed 5/22/19	Tue 1/21/20	
10		SCE - RFP Release	1 day	Wed 1/22/20	Wed 1/22/20	
11		SCE - RFP Proposal Creation Duration	25 days	Thu 1/23/20	Wed 2/26/20	
12		SCE - RFP Evaluation	38 days	Thu 2/27/20	Mon 4/20/20	
13		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20	
14		SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20	
15		SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20	
16		SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20	
17		SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20	
18		SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20	
19		SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20	
20		SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21	
21		SCE - SW Lighting	518 days	Wed 4/3/19	Fri 3/26/21	
22		SCE - RFA Preparation	55 days	Wed 4/3/19	Tue 6/18/19	
23		SCE - RFA Release	1 day	Tue 7/2/19	Tue 7/2/19	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
24		SCE - RFA Abstract Creation Duration	20 days	Wed 7/3/19	Tue 7/30/19	
25		SCE - RFA Evaluation	34 days	Wed 7/31/19	Mon 9/16/19	
26		SCE - RFA Review with EE PRG	1 day	Tue 9/17/19	Tue 9/17/19	
27		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/24/19	Tue 9/24/19	
28		SCE - RFP Preparation	84 days	Wed 9/25/19	Mon 1/20/20	
29		SCE - RFP Release	1 day	Thu 2/6/20	Thu 2/6/20	
30		SCE - RFP Proposal Creation Duration	27 days	Fri 2/7/20	Mon 3/16/20	
31		SCE - RFP Evaluation	25 days	Tue 3/17/20	Mon 4/20/20	
32		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20	
33		SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20	
34		SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20	
35		SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20	
36		SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20	
37		SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20	
38		SCE - Advice Letter Approved	1 day	Wed 12/23/20	Wed 12/23/20	
39		SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21	
40		SCE - Local Public Sector Solicitation	573 days	Mon 8/31/20	Wed 11/9/22	
41		SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20	
42		SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20	
43		SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20	
44		SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21	
45		SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21	
46		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only



ID		Task Name	Duration	Start	Finish	2018 H1
47		SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21	
48		SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21	
49		SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21	
50		SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21	
51		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21	
52		SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21	
53		SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21	
54		SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21	
55		SCE - Final Award and Contract Signed	1 day	Tue 12/14/21	Tue 12/14/21	
56		SCE - Submit Advice Letter	37 days	Wed 12/15/21	Thu 2/3/22	
57		SCE - Submit Advice Letter	48 days	Wed 12/15/21	Fri 2/18/22	
58		SCE - Advice Letter Approved	1 day	Thu 8/18/22	Thu 8/18/22	
59		SCE - Implementation Plan	60 days	Thu 8/18/22	Wed 11/9/22	
60		SCE - Local Agriculture Solicitation	512 days	Mon 8/31/20	Tue 8/16/22	
61		SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20	
62		SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20	
63		SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20	
64		SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21	
65		SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21	
66		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21	
67		SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21	
68		SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21	
69		SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
70		SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21	
71		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21	
72		SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21	
73		SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21	
74		SCE - Final Award and Contract Signed	1 day	Mon 12/20/21	Mon 12/20/21	
75		SCE - Submit Advice Letter	33 days	Tue 12/21/21	Thu 2/3/22	
76		SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21	
77		SCE - Final Award and Contract Signed	1 day	Wed 12/15/21	Wed 12/15/21	
78		SCE - Submit Advice Letter	56 days	Thu 12/16/21	Thu 3/3/22	
79		SCE - Advice Letter Approved	1 day	Fri 4/22/22	Fri 4/22/22	
80		SCE - Implementation Plan	60 days	Sat 4/23/22	Thu 7/14/22	
81		SCE - SW Water/Wastewater Solicitation	522 days	Mon 11/16/20	Tue 11/15/22	
82		SCE - RFA Preparation	70 days	Mon 11/16/20	Fri 2/19/21	
83		SCE - RFA Release	1 day	Thu 3/4/21	Thu 3/4/21	
84		SCE - RFA Abstract Creation Duration	29 days	Thu 3/4/21	Tue 4/13/21	
85		SCE - RFA Evaluation	20 days	Wed 4/14/21	Tue 5/11/21	
86		SCE - RFA Review with EE PRG	1 day	Tue 5/18/21	Tue 5/18/21	
87		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/27/21	Thu 5/27/21	
88		SCE - RFP Preparation	34 days	Mon 4/19/21	Thu 6/3/21	
89		SCE - RFP Release	1 day	Thu 7/1/21	Thu 7/1/21	
90		SCE - RFP Proposal Creation Duration	25 days	Fri 7/2/21	Thu 8/5/21	
91		SCE - RFP Evaluation	41 days	Fri 8/6/21	Fri 10/1/21	
92		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/26/21	Tue 10/26/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




ID		Task Name	Duration	Start	Finish	2018 H1
93		SCE - RFP Review with EE PRG	1 day	Tue 10/19/21	Tue 10/19/21	
94		SCE - Contract Negotiation and Development	94 days	Wed 10/27/21	Mon 3/7/22	
95		SCE - Contract Review with EE PRG	1 day	Tue 3/15/22	Tue 3/15/22	
96		SCE - Final Award and Contract Signed	1 day	Tue 4/19/22	Tue 4/19/22	
97		SCE - Submit Advice Letter	40 days	Wed 4/20/22	Tue 6/14/22	
98		SCE - Advice Letter Approved	26 days	Wed 6/15/22	Wed 7/20/22	
99		SCE - Implementation Plan	44 days	Thu 7/21/22	Tue 9/20/22	
100		SCE - SW ETP Solicitation	466 days	Fri 5/1/20	Fri 2/11/22	
101		SCE - RFA Preparation	57 days	Fri 5/1/20	Mon 7/20/20	
102		SCE - RFA Release	1 day	Tue 8/4/20	Tue 8/4/20	
103		SCE - RFA Abstract Creation Duration	24 days	Fri 8/7/20	Wed 9/9/20	
104		SCE - RFA Evaluation	16 days	Thu 9/10/20	Thu 10/1/20	
105		SCE - RFA Review with EE PRG	1 day	Tue 10/20/20	Tue 10/20/20	
106		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/27/20	Tue 10/27/20	
107		SCE - RFP Preparation	42 days	Tue 9/8/20	Wed 11/4/20	
108		SCE - RFP Release	1 day	Tue 1/5/21	Tue 1/5/21	
109		SCE - RFP Proposal Creation Duration	37 days	Tue 1/5/21	Wed 2/24/21	
110		SCE - RFP Evaluation	28 days	Wed 2/24/21	Fri 4/2/21	
111		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/27/21	Tue 4/27/21	
112		SCE - RFP Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21	
113		SCE - Contract Negotiation and Development	69 days	Wed 4/21/21	Mon 7/26/21	
114		SCE - Contract Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21	
115		SCE - Final Award and Contract Signed	1 day	Tue 9/14/21	Tue 9/14/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
116		SCE - Submit Advice Letter	18 days	Wed 9/15/21	Fri 10/8/21	
117		SCE - Advice Letter Approved	1 day	Tue 11/9/21	Tue 11/9/21	
118		SCE - Implementation Plan	60 days	Wed 11/10/21	Tue 2/1/22	
119		SCE - SW Higher-Education Solicitation	547 days?	Thu 10/1/20	Fri 11/4/22	
120		SCE - RFA Preparation	89 days	Thu 10/1/20	Tue 2/2/21	
121		SCE - RFA Release	1 day	Thu 2/4/21	Thu 2/4/21	
122		SCE - RFA Abstract Creation Duration	19 days	Fri 2/5/21	Wed 3/3/21	
123		SCE - RFA Evaluation	31 days	Thu 3/4/21	Thu 4/15/21	
124		SCE - RFA Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21	
125		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 4/29/21	Thu 4/29/21	
126		SCE - RFP Preparation	39 days	Mon 3/22/21	Thu 5/13/21	
127		SCE - RFP Release	1 day	Fri 5/28/21	Fri 5/28/21	
128		SCE - RFP Proposal Creation Duration	24 days	Fri 6/4/21	Wed 7/7/21	
129		SCE - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21	
130		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/30/21	Mon 8/30/21	
131		SCE - RFP Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21	
132		SCE - Contract Negotiation and Development	95 days	Fri 9/3/21	Thu 1/13/22	
133		SCE - Contract Review with EE PRG	1 day	Tue 1/18/22	Tue 1/18/22	
134		SCE - Final Award and Contract Signed	1 day	Sun 3/6/22	Sun 3/6/22	
135		SCE - Submit Advice Letter	1 day	Tue 4/19/22	Tue 4/19/22	
136		SCE - Advice Letter Approved	1 day	Mon 8/15/22	Mon 8/15/22	
137		SCE - Implementation Plan	60 days	Mon 8/15/22	Fri 11/4/22	
138		SCE - Local Equity Residential and SMB	384 days?	Tue 2/15/22	Fri 8/4/23	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
139		SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22	
140		SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22	
141		SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22	
142		SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22	
143		SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22	
144		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22	
145		SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22	
146		SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22	
147		SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22	
148		SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22	
149		SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22	
150		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22	
151		SCE - Contract Negotiation and Development	65 days	Wed 11/2/22	Tue 1/31/23	
152		SCE - Contract Review with EE PRG	1 day	Tue 2/21/23	Tue 2/21/23	
153		SCE - Final Award and Contract Signed	1 day	Thu 3/30/23	Thu 3/30/23	
154		SCE - Submit Advice Letter	22 days	Sun 4/3/22	Mon 5/2/22	
155		SCE - Advice Letter Approved	28 days	Tue 5/2/23	Thu 6/8/23	
156		SCE - Implementation Plan	45 days	Thu 6/8/23	Wed 8/9/23	
157						
158		SCE - Local Equity SMB	431 days?	Tue 2/15/22	Tue 10/10/23	
159		SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22	
160		SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22	
161		SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
162		SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22	
163		SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22	
164		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22	
165		SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22	
166		SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22	
167		SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22	
168		SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22	
169		SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22	
170		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22	
171		SCE - Contract Negotiation and Development	108 days	Wed 11/2/22	Fri 3/31/23	
172		SCE - Contract Review with EE PRG	1 day	Tue 4/18/23	Tue 4/18/23	
173		SCE - Final Award and Contract Signed	1 day	Wed 5/31/23	Wed 5/31/23	
174		SCE - Submit Advice Letter	22 days	Mon 6/6/22	Tue 7/5/22	
175		SCE - Advice Letter Approved	24 days	Thu 7/6/23	Tue 8/8/23	
176		SCE - Implementation Plan	45 days	Wed 8/9/23	Tue 10/10/23	
177		SCE - Local Strategic Energy Management Solicitation	372 days?	Thu 12/1/22	Fri 5/3/24	
178		SCE - RFP Preparation	85 days	Thu 12/1/22	Wed 3/29/23	
179		SCE - RFP Release	1 day	Fri 4/7/23	Fri 4/7/23	
180		SCE - RFP Proposal Creation Duration	35 days	Fri 4/7/23	Thu 5/25/23	
181		SCE - RFP Evaluation	22 days	Thu 6/1/23	Fri 6/30/23	
182		SCE - RFP Review with EE PRG	1 day	Tue 7/18/23	Tue 7/18/23	
183		SCE - Contract Negotiation and Development	86 days	Tue 8/1/23	Tue 11/28/23	
184		SCE - Contract Review with EE PRG	1 day	Tue 12/19/23	Tue 12/19/23	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
185		SCE - Final Award and Contract Signed	6 days	Fri 1/19/24	Fri 1/26/24	
186		SCE - Submit Advice Letter	34 days	Wed 1/31/24	Mon 3/18/24	
187		SCE - Advice Letter Approved	40 days	Tue 3/19/24	Mon 5/13/24	
188		SCE - Local Large Commercial Solicitation	488 days?	Mon 6/26/23	Wed 5/7/25	
189		SCE - RFP Preparation	35 days	Mon 6/26/23	Fri 8/11/23	
190		SCE - RFP Release	1 day	Thu 8/17/23	Thu 8/17/23	
191		SCE - RFP Proposal Creation Duration	41 days	Thu 8/17/23	Thu 10/12/23	
192		SCE - RFP Paused	1 day	Fri 10/13/23	Fri 10/13/23	
193		SCE - Residential Multifamily	326 days?	Fri 9/1/23	Fri 11/29/24	
194		SCE - RFP Preparation	47 days	Fri 9/1/23	Mon 11/6/23	
195		SCE - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23	
196		SCE - RFP Proposal Creation Duration	48 days	Mon 11/6/23	Wed 1/10/24	
197		SCE - RFP Evaluation	25 days	Thu 1/11/24	Wed 2/14/24	
198		SCE - RFP Review with EE PRG	1 day	Tue 2/20/24	Tue 2/20/24	
199		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 2/28/24	Wed 2/28/24	
200		SCE - Contract Negotiation and Development	70 days	Mon 3/4/24	Fri 6/7/24	
201		SCE - Contract Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24	
202		SCE - Final Award and Contract Signed	15 days	Mon 7/29/24	Fri 8/16/24	
203		SCE - Submit Advice Letter	30 days	Mon 8/19/24	Fri 9/27/24	
204		SCE - Advice Letter Approved	1 day	Mon 10/28/24	Mon 10/28/24	
205		SCE - Local Large Industrial	489 days	Fri 11/3/23	Wed 9/17/25	
206		SCE - RFP Preparation	17 days	Fri 11/3/23	Mon 11/27/23	
207		SCE - RFP Release	1 day	Mon 12/11/23	Mon 12/11/23	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
208		SCE - RFP Proposal Creation Duration	49 days	Mon 12/11/23	Thu 2/15/24	
209		SCE - RFP Evaluation	35 days	Fri 2/16/24	Thu 4/4/24	
210		SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24	
211		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/23/24	Tue 4/23/24	
212		SCE - Contract Negotiation and Development	208 days	Wed 4/24/24	Fri 2/7/25	
213		SCE - Contract Review with EE PRG	1 day	Tue 4/29/25	Tue 4/29/25	
214		SCE - Final Award and Contract Signed	42 days	Thu 5/1/25	Fri 6/27/25	
215		SCE - Submit Advice Letter	35 days	Mon 6/30/25	Fri 8/15/25	
216		SCE - Advice Letter Approved	23 days	Mon 8/18/25	Wed 9/17/25	
217		SCE - MAP - All Sectors	299 days?	Mon 11/20/23	Thu 1/9/25	
218		SCE - RFP Preparation	20 days	Mon 11/20/23	Fri 12/15/23	
219		SCE - RFP Release	1 day	Mon 1/8/24	Mon 1/8/24	
220		SCE - RFP Proposal Creation Duration	40 days	Mon 1/8/24	Fri 3/1/24	
221		SCE - RFP Evaluation	30 days	Mon 3/4/24	Fri 4/12/24	
222		SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24	
223		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/24/24	Wed 4/24/24	
224		SCE - Contract Negotiation and Development	108 days	Wed 5/1/24	Fri 9/27/24	
225		SCE - Contract Review with EE PRG	1 day	Tue 10/15/24	Tue 10/15/24	
226		SCE - Final Award and Contract Signed	12 days	Tue 10/29/24	Wed 11/13/24	
227		SCE - Submit Advice Letter	43 days	Wed 11/13/24	Fri 1/10/25	
228		SCE - Advice Letter Approved	22 days	Mon 1/13/25	Tue 2/11/25	
229		SCE - Residential	360 days?	Mon 11/20/23	Fri 4/4/25	
230		SCE - RFP Preparation	20 days	Tue 1/16/24	Mon 2/12/24	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
231		SCE - RFP Release	1 day	Thu 3/28/24	Thu 3/28/24	
232		SCE - RFP Proposal Creation Duration	41 days	Thu 3/28/24	Thu 5/23/24	
233		SCE - RFP Evaluation	35 days	Fri 5/24/24	Thu 7/11/24	
234		SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24	
235		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/5/24	Mon 8/5/24	
236		SCE - Contract Negotiation and Development	80 days	Mon 8/19/24	Fri 12/6/24	
237		SCE - Contract Review with EE PRG	1 day	Tue 12/17/24	Tue 12/17/24	
238		SCE - Final Award and Contract Signed	11 days	Mon 1/13/25	Mon 1/27/25	
239		SCE - Submit Advice Letter	19 days	Mon 2/3/25	Thu 2/27/25	
240		SCE - Advice Letter Approved	1 day	Tue 4/1/25	Tue 4/1/25	
241						
242		SCE - Local Comprehensive Commercial Solicitation	431 days?	Mon 11/13/23	Mon 7/7/25	
243		SCE - RFP Preparation	73 days	Mon 11/13/23	Wed 2/21/24	
244		SCE - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24	
245		SCE - RFP Proposal Creation Duration	43 days	Thu 2/29/24	Mon 4/29/24	
246		SCE - RFP Evaluation	54 days	Tue 4/30/24	Fri 7/12/24	
247		SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24	
248		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Phase 1	1 day	Mon 7/29/24	Mon 7/29/24	
249		SCE - Contract Negotiation and Development - Phase 1	81 days	Tue 7/30/24	Tue 11/19/24	
250		SCE - Contract Review with EE PRG - Phase 1	1 day	Tue 12/17/24	Tue 12/17/24	
251		SCE - Final Award and Contract Signed - Phase 1	1 day	Tue 1/28/25	Tue 1/28/25	
252		SCE - Submit Advice Letter - Phase 1	23 days	Tue 1/28/25	Thu 2/27/25	
253		SCE - Advice Letter Approved - Phase 1	1 day	Tue 4/1/25	Tue 4/1/25	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
254		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Pha	1 day	Mon 9/30/24	Mon 9/30/24	
255		SCE - Contract Negotiation and Development - Phase 2	80 days	Mon 12/2/24	Fri 3/21/25	
256		SCE - Contract Review with EE PRG - Phase 2	1 day	Tue 4/29/25	Tue 4/29/25	
257		SCE - Final Award and Contract Signed - Phase 2	1 day	Tue 5/20/25	Tue 5/20/25	
258		SCE - Submit Advice Letter - Phase 2	0 days	N/A	N/A	
259		SCE - Advice Letter Approved - Phase 2	0 days	N/A	N/A	
260						
261		SCE - Statewide Plug Load and Appliances	481 days	Wed 9/18/24	Wed 7/22/26	
262		SCE - RFP Preparation	127 days	Tue 1/28/25	Wed 7/23/25	
263		SCE - RFI Preparation	15 days	Tue 1/28/25	Mon 2/17/25	
264		SCE - RFI Review with EE PRG	1 day	Tue 2/18/25	Tue 2/18/25	
265		SCE - RFI Release	1 day	Tue 2/25/25	Tue 2/25/25	
266		SCE - RFI Creation Duration	16 days	Wed 2/26/25	Wed 3/19/25	
267		SCE - RFI Review with EE PRG	1 day	Tue 4/29/25	Tue 4/29/25	
268		SCE - RFP Release	1 day	Wed 7/23/25	Wed 7/23/25	
269		SCE - RFP Proposal Creation Duration	35 days	Wed 7/23/25	Tue 9/9/25	
270		SCE - RFP Evaluation	39 days	Tue 9/9/25	Fri 10/31/25	
271		SCE - RFP Review with EE PRG	1 day	Tue 11/18/25	Tue 11/18/25	
272		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/26/25	Wed 11/26/25	
273		SCE - Contract Negotiation and Development	0 days	Thu 2/27/25	Thu 2/27/25	
274		SCE - Contract Review with EE PRG	1 day	Tue 3/17/26	Tue 3/17/26	
275		SCE - Final Award and Contract Signed	0 days	Mon 5/19/25	Mon 5/19/25	
276		SCE - Submit Advice Letter	46 days	Wed 5/20/26	Wed 7/22/26	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
277		SCE - Advice Letter Approved	1 day	Wed 7/22/26	Wed 7/22/26	
278						
279		SCG - Local Single Family Solicitation	660 days	Sun 7/1/18	Thu 1/7/21	
280		SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18	
281		SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18	
282		SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19	
283		SCG - RFA Evaluation	39 days	Mon 1/7/19	Thu 2/28/19	
284		SCG - RFA Review with EE PRG	1 day	Tue 3/5/19	Tue 3/5/19	
285		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19	
286		SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19	
287		SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19	
288		SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19	
289		SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19	
290		SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19	
291		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20	
292		SCG - Contract Negotiation and Development	69 days	Mon 1/27/20	Thu 4/30/20	
293		SCG - Contract Review with EE PRG	14 days	Tue 5/5/20	Fri 5/22/20	
294		SCG - Final Award and Contract Signed	8 days	Mon 5/25/20	Wed 6/3/20	
295		SCG - Submit Advice Letter	96 days	Mon 6/1/20	Mon 10/12/20	
296		SCG - Advice Letter Approved	1 day	Thu 11/12/20	Thu 11/12/20	
297		SCG - Implementation Plan	41 days	Fri 11/13/20	Fri 1/8/21	
298		SCG - Local Multi-family Solicitation	735 days	Sun 7/1/18	Thu 4/22/21	
299		SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
300		SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18	
301		SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19	
302		SCG - RFA Evaluation	59 days	Mon 1/7/19	Thu 3/28/19	
303		SCG - RFA Review with EE PRG	1 day	Tue 4/2/19	Tue 4/2/19	
304		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19	
305		SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19	
306		SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19	
307		SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19	
308		SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19	
309		SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19	
310		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20	
311		SCG - Contract Negotiation and Development	155 days	Mon 1/27/20	Fri 8/28/20	
312		SCG - Contract Review with EE PRG	99 days	Tue 5/5/20	Fri 9/18/20	
313		SCG - Final Award and Contract Signed	8 days	Mon 9/21/20	Wed 9/30/20	
314		SCG - Submit Advice Letter	37 days	Thu 10/1/20	Fri 11/20/20	
315		SCG - Advice Letter Approved	1 day	Sun 5/2/21	Sun 5/2/21	
316		SCG - Implementation Plan	51 days	Mon 5/3/21	Mon 7/12/21	
317		SCG - Local Small/Medium Commercial Solicitation	641 days	Tue 9/4/18	Tue 2/16/21	
318		SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19	
319		SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19	
320		SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19	
321		SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19	
322		SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
323		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19	
324		SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19	
325		SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19	
326		SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19	
327		SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19	
328		SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19	
329		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20	
330		SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20	
331		SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20	
332		SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20	
333		SCG - Submit Advice Letter	59 days	Tue 9/1/20	Fri 11/20/20	
334		SCG - Advice Letter Approved	1 day	Fri 12/18/20	Fri 12/18/20	
335		SCG - Implementation Plan	43 days	Sat 12/19/20	Tue 2/16/21	
336		SCG - Local Small/Medium Public Solicitation	631 days	Tue 9/4/18	Tue 2/2/21	
337		SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19	
338		SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19	
339		SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19	
340		SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19	
341		SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19	
342		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19	
343		SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19	
344		SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19	
345		SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
346		SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19	
347		SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19	
348		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20	
349		SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20	
350		SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20	
351		SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20	
352		SCG - Submit Advice Letter	49 days	Tue 9/1/20	Fri 11/6/20	
353		SCG - Advice Letter Approved	1 day	Fri 12/4/20	Fri 12/4/20	
354		SCG - Implementation Plan	43 days	Sat 12/5/20	Tue 2/2/21	
355		SCG - Statewide POS Food Service Solicitation	605 days	Mon 1/21/19	Fri 5/14/21	
356		SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19	
357		SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19	
358		SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19	
359		SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19	
360		SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19	
361		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20	
362		SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19	
363		SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20	
364		SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20	
365		SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20	
366		SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20	
367		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20	
368		SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
369		SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20	
370		SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20	
371		SCG - Submit Advice Letter	32 days	Mon 11/2/20	Tue 12/15/20	
372		SCG - Advice Letter Approved	1 day	Thu 1/14/21	Thu 1/14/21	
373		SCG - Implementation Plan	42 days	Fri 1/15/21	Mon 3/15/21	
374		SCG - Statewide Midstream Water Heating Solicitation	597 days	Mon 1/21/19	Tue 5/4/21	
375		SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19	
376		SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19	
377		SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19	
378		SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19	
379		SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19	
380		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20	
381		SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19	
382		SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20	
383		SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20	
384		SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20	
385		SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20	
386		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20	
387		SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20	
388		SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20	
389		SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20	
390		SCG - Submit Advice Letter	25 days	Mon 11/2/20	Fri 12/4/20	
391		SCG - Advice Letter Approved	1 day	Thu 3/18/21	Thu 3/18/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




ID		Task Name	Duration	Start	Finish	2018 H1
392		SCG - Implementation Plan	22 days	Fri 3/19/21	Mon 4/19/21	
393		SCG - Statewide Gas Emerging Technology Solicitation	738 days	Wed 1/2/19	Fri 10/29/21	
394		SCG - RFA Preparation	283 days	Wed 1/2/19	Fri 1/31/20	
395		SCG - RFA Release	1 day	Wed 2/12/20	Wed 2/12/20	
396		SCG - RFA Abstract Creation Duration	30 days	Thu 2/13/20	Wed 3/25/20	
397		SCG - RFA Evaluation	26 days	Thu 3/26/20	Thu 4/30/20	
398		SCG - RFA Review with EE PRG	1 day	Tue 5/5/20	Tue 5/5/20	
399		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 5/15/20	Fri 5/15/20	
400		SCG - RFP Preparation	66 days	Fri 5/1/20	Fri 7/31/20	
401		SCG - RFP Release	1 day	Fri 8/21/20	Fri 8/21/20	
402		SCG - RFP Proposal Creation Duration	30 days	Mon 8/24/20	Fri 10/2/20	
403		SCG - RFP Evaluation	38 days	Mon 10/5/20	Wed 11/25/20	
404		SCG - RFP Review with EE PRG	1 day	Tue 12/1/20	Tue 12/1/20	
405		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 12/7/20	Mon 12/7/20	
406		SCG - Contract Negotiation and Development	85 days	Mon 1/4/21	Fri 4/30/21	
407		SCG - Contract Review with EE PRG	9 days	Tue 5/4/21	Fri 5/14/21	
408		SCG - Final Award and Contract Signed	29 days	Mon 5/17/21	Thu 6/24/21	
409		SCG - Submit Advice Letter	23 days	Sun 6/27/21	Tue 7/27/21	
410		SCG - Advice Letter Approved	1 day	Tue 8/24/21	Tue 8/24/21	
411		SCG - Implementation Plan	44 days	Wed 8/25/21	Sat 10/23/21	
412		SCG - Local Manufactured Housing Solicitation	341 days	Fri 11/1/19	Fri 2/19/21	
413		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20	
414		SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
415		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20	
416		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20	
417		SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20	
418		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20	
419		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20	
420		SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20	
421		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20	
422		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20	
423		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20	
424		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20	
425		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20	
426		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20	
427		SCG - Final Award and Contract Signed	9 days	Thu 12/10/20	Tue 12/22/20	
428		SCG - Submit Advice Letter	0 days	N/A	N/A	
429		SCG - Advice Letter Approved	0 days	N/A	N/A	
430		SCG - Implementation Plan	44 days	Tue 12/22/20	Fri 2/19/21	
431		SCG - Local Large Commercial Solicitation	434 days	Fri 11/1/19	Wed 6/30/21	
432		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20	
433		SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20	
434		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20	
435		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20	
436		SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20	
437		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
438		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20	
439		SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20	
440		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20	
441		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20	
442		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20	
443		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20	
444		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20	
445		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20	
446		SCG - Final Award and Contract Signed	10 days	Thu 12/10/20	Wed 12/23/20	
447		SCG - Submit Advice Letter	64 days	Fri 1/1/21	Wed 3/31/21	
448		SCG - Advice Letter Approved	1 day	Fri 6/4/21	Fri 6/4/21	
449		SCG - Implementation Plan	43 days	Sat 6/5/21	Tue 8/3/21	
450		SCG - Local Agricultural Solicitation	434 days	Fri 11/1/19	Wed 6/30/21	
451		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20	
452		SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20	
453		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20	
454		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20	
455		SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20	
456		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20	
457		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20	
458		SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20	
459		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20	
460		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
461		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20	
462		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20	
463		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20	
464		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20	
465		SCG - Final Award and Contract Signed	2 days	Fri 12/11/20	Mon 12/14/20	
466		SCG - Submit Advice Letter	41 days	Fri 1/1/21	Fri 2/26/21	
467		SCG - Advice Letter Approved	1 day	Wed 4/7/21	Wed 4/7/21	
468		SCG - Implementation Plan	43 days	Thu 4/8/21	Mon 6/7/21	
469		SCG - Local Behavioral Solicitation - Residential	413 days?	Fri 5/1/20	Tue 11/30/21	
470		SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20	
471		SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20	
472		SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20	
473		SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20	
474		SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20	
475		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20	
476		SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20	
477		SCG - RFP Release	1 day	Fri 1/15/21	Fri 1/15/21	
478		SCG - RFP Proposal Creation Duration	26 days	Mon 1/18/21	Mon 2/22/21	
479		SCG - RFP Evaluation	29 days	Tue 2/23/21	Fri 4/2/21	
480		SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21	
481		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/13/21	Tue 4/13/21	
482		SCG - Contract Negotiation and Development	95 days	Mon 4/26/21	Fri 9/3/21	
483		SCG - Contract Review with EE PRG	9 days	Tue 9/7/21	Fri 9/17/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
484		SCG - Final Award and Contract Signed	30 days	Mon 9/20/21	Fri 10/29/21	
485		SCG - Submit Advice Letter	21 days	Mon 11/1/21	Mon 11/29/21	
486		SCG - Advice Letter Approved	1 day	Wed 12/22/21	Wed 12/22/21	
487		SCG - Implementation Plan	43 days	Thu 12/23/21	Sun 2/20/22	
488		SCG - Local Behavioral Solicitation - Commercial	413 days?	Fri 5/1/20	Tue 11/30/21	
489		SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20	
490		SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20	
491		SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20	
492		SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20	
493		SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20	
494		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20	
495		SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20	
496		SCG - RFP Release	1 day	Fri 1/22/21	Fri 1/22/21	
497		SCG - RFP Proposal Creation Duration	26 days	Mon 1/25/21	Mon 3/1/21	
498		SCG - RFP Evaluation	24 days	Tue 3/2/21	Fri 4/2/21	
499		SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21	
500		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 11/12/21	Fri 11/12/21	
501		SCG - Contract Negotiation and Development	132 days	Mon 11/29/21	Tue 5/31/22	
502		SCG - Contract Review with EE PRG	8 days	Sun 6/5/22	Tue 6/14/22	
503		SCG - Final Award and Contract Signed	109 days	Fri 7/1/22	Wed 11/30/22	
504		SCG - Submit Advice Letter	23 days	N/A	N/A	
505		SCG - Advice Letter Approved	1 day	N/A	N/A	
506		SCG - Implementation Plan	43 days	Thu 12/1/22	Sun 1/29/23	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
507		SCG - Local Industrial Solicitation	434 days?	Tue 12/1/20	Fri 7/29/22	
508		SCG - RFA Preparation	63 days?	Tue 12/1/20	Thu 2/25/21	
509		SCG - RFA Release	1 day?	Fri 3/19/21	Fri 3/19/21	
510		SCG - RFA Abstract Creation Duration	25 days?	Mon 3/22/21	Fri 4/23/21	
511		SCG - RFA Evaluation	25 days?	Mon 4/26/21	Fri 5/28/21	
512		SCG - RFA Review with EE PRG	1 day?	Tue 6/1/21	Tue 6/1/21	
513		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 6/8/21	Tue 6/8/21	
514		SCG - RFP Preparation	67 days?	Thu 4/1/21	Fri 7/2/21	
515		SCG - RFP Release	1 day?	Fri 7/16/21	Fri 7/16/21	
516		SCG - RFP Proposal Creation Duration	30 days?	Mon 7/19/21	Fri 8/27/21	
517		SCG - RFP Evaluation	25 days?	Mon 8/30/21	Fri 10/1/21	
518		SCG - RFP Review with EE PRG	1 day?	Tue 10/5/21	Tue 10/5/21	
519		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 12/14/21	Tue 12/14/21	
520		SCG - Contract Negotiation and Development	127 days?	Thu 2/3/22	Fri 7/29/22	
521		SCG - Contract Review with EE PRG	9 days?	Tue 8/2/22	Fri 8/12/22	
522		SCG - Final Award and Contract Signed	21 days?	Fri 7/29/22	Fri 8/26/22	
523		SCG - Submit Advice Letter	1 day?	Sun 10/30/22	Sun 10/30/22	
524		SCG - Advice Letter Approved	1 day?	Mon 1/30/23	Mon 1/30/23	
525		SCG - Implementation Plan	45 days?	Tue 1/31/23	Sat 4/1/23	
526		SCG - Large Public Sector Solicitation (re-Bid)	412 days	Mon 1/4/21	Tue 8/2/22	
527		SCG - RFA Preparation	65 days	Mon 1/4/21	Fri 4/2/21	
528		SCG - RFA Release	1 day	Fri 7/16/21	Fri 7/16/21	
529		SCG - RFA Abstract Creation Duration	20 days	Mon 7/19/21	Fri 8/13/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
530		SCG - RFA Evaluation	15 days	Mon 8/16/21	Fri 9/3/21	
531		SCG - RFA Review with EE PRG	1 day	Tue 9/7/21	Tue 9/7/21	
532		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/14/21	Tue 9/14/21	
533		SCG - RFP Preparation	35 days	Mon 9/13/21	Fri 10/29/21	
534		SCG - RFP Release	1 day	Mon 11/8/21	Mon 11/8/21	
535		SCG - RFP Proposal Creation Duration	29 days	Tue 11/9/21	Fri 12/17/21	
536		SCG - RFP Evaluation	30 days	Mon 12/20/21	Fri 1/28/22	
537		SCG - RFP Review with EE PRG	1 day	Tue 2/1/22	Tue 2/1/22	
538		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/8/22	Tue 3/8/22	
539		SCG - Contract Negotiation and Development	79 days	Mon 3/14/22	Thu 6/30/22	
540		SCG - Contract Review with EE PRG	9 days	Tue 7/5/22	Fri 7/15/22	
541		SCG - Final Award and Contract Signed	63 days	Mon 7/18/22	Wed 10/12/22	
542		SCG - Submit Advice Letter	23 days	N/A	N/A	
543		SCG - Advice Letter Approved	1 day	N/A	N/A	
544		SCG - Implementation Plan	44 days	Wed 10/12/22	Sat 12/10/22	
545		SCG - Outreach Solicitation	434 days	Mon 2/1/21	Thu 9/29/22	
546		SCG - RFA Preparation	65 days	Mon 2/1/21	Fri 4/30/21	
547		SCG - RFA Release	1 day	Fri 5/21/21	Fri 5/21/21	
548		SCG - RFA Abstract Creation Duration	25 days	Mon 5/24/21	Fri 6/25/21	
549		SCG - RFA Evaluation	25 days	Mon 6/28/21	Fri 7/30/21	
550		SCG - RFA Review with EE PRG	1 day	Tue 8/3/21	Tue 8/3/21	
551		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/10/21	Tue 8/10/21	
552		SCG - RFP Preparation	69 days	Tue 6/1/21	Fri 9/3/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
553		SCG - RFP Release	1 day	Fri 9/17/21	Fri 9/17/21	
554		SCG - RFP Proposal Creation Duration	30 days	Mon 9/20/21	Fri 10/29/21	
555		SCG - RFP Evaluation	25 days	Mon 11/1/21	Fri 12/3/21	
556		SCG - RFP Review with EE PRG	1 day	Tue 12/7/21	Tue 12/7/21	
557		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 12/14/21	Tue 12/14/21	
558		SCG - Contract Negotiation and Development	54 days	Mon 1/17/22	Thu 3/31/22	
559		SCG - Contract Review with EE PRG	9 days	Tue 4/5/22	Fri 4/15/22	
560		SCG - Final Award and Contract Signed	10 days	Mon 4/18/22	Fri 4/29/22	
561		SCG - Submit Advice Letter	21 days	N/A	N/A	
562		SCG - Advice Letter Approved	1 day	N/A	N/A	
563		SCG - Implementation Plan	43 days	Sat 4/30/22	Tue 6/28/22	
564		SCG - Marketplace Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22	
565		SCG - RFA Preparation	64 days	Sat 5/1/21	Wed 7/28/21	
566		SCG - RFA Release	1 day	Fri 8/20/21	Fri 8/20/21	
567		SCG - RFA Abstract Creation Duration	25 days	Mon 8/23/21	Fri 9/24/21	
568		SCG - RFA Evaluation	25 days	Mon 9/27/21	Fri 10/29/21	
569		SCG - RFA Review with EE PRG	1 day	Tue 11/2/21	Tue 11/2/21	
570		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/9/21	Tue 11/9/21	
571		SCG - RFP Preparation	91 days	Thu 8/26/21	Thu 12/30/21	
572		SCG - RFP Release	1 day	Fri 1/14/22	Fri 1/14/22	
573		SCG - RFP Proposal Creation Duration	30 days	Mon 1/17/22	Fri 2/25/22	
574		SCG - RFP Evaluation	25 days	Mon 2/28/22	Fri 4/1/22	
575		SCG - RFP Review with EE PRG	1 day	Tue 5/3/22	Tue 5/3/22	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only



ID		Task Name	Duration	Start	Finish	2018 H1
576		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 5/11/22	Wed 5/11/22	
577		SCG - Contract Negotiation and Development	117 days	Wed 6/22/22	Thu 12/1/22	
578		SCG - Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22	
579		SCG - Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22	
580		SCG - Submit Advice Letter	20 days	Tue 1/3/23	Mon 1/30/23	
581		SCG - Advice Letter Approved	1 day	Tue 5/2/23	Tue 5/2/23	
582		SCG - Implementation Plan	44 days	Wed 5/3/23	Sun 7/2/23	
583		SCG - Residential Multi-Family - Whole Building	436 days?	Mon 3/1/21	Mon 10/31/22	
584		RFA Preparation	40 days	Mon 1/10/22	Fri 3/4/22	
585		RFA Release	1 day	Fri 3/25/22	Fri 3/25/22	
586		RFA Abstract Creation Duration	25 days	Mon 3/28/22	Fri 4/29/22	
587		RFA Evaluation	25 days	Mon 5/2/22	Fri 6/3/22	
588		RFA Review with EE PRG	1 day	Tue 6/7/22	Tue 6/7/22	
589		RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/14/22	Tue 6/14/22	
590		RFP Preparation	28 days	Sun 5/1/22	Tue 6/7/22	
591		RFP Release	1 day	Fri 6/24/22	Fri 6/24/22	
592		RFP Proposal Creation Duration	52 days	Mon 6/27/22	Tue 9/6/22	
593		RFP Evaluation	11 days	Fri 9/9/22	Fri 9/23/22	
594		RFP Review with EE PRG	1 day	Thu 10/6/22	Thu 10/6/22	
595		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/11/22	Tue 10/11/22	
596		Contract Negotiation and Development	39 days	Tue 10/11/22	Fri 12/2/22	
597		Contract Review with EE PRG	1 day	Tue 12/6/22	Tue 12/6/22	
598		Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
599		Submit Advice Letter	22 days	Mon 1/2/23	Tue 1/31/23	
600		Advice Letter Approved	1 day	Fri 3/31/23	Fri 3/31/23	
601		Implementation Plan	43 days	Sat 4/1/23	Tue 5/30/23	
602		SCG - Youth Education Outreach Solicitation	331 days	Tue 3/1/22	Tue 6/6/23	
603		SCG - HERS Rater Training Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22	
604		RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22	
605		RFP Release	1 day	Fri 5/13/22	Fri 5/13/22	
606		RFP Proposal Creation Duration	20 days	Mon 5/16/22	Fri 6/10/22	
607		RFP Evaluation	59 days	Mon 6/13/22	Thu 9/1/22	
608		RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22	
609		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 8/31/22	Wed 8/31/22	
610		Contract Negotiation and Development	53 days	Fri 9/16/22	Tue 11/29/22	
611		Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22	
612		Final Award and Contract Signed	9 days	Mon 12/19/22	Thu 12/29/22	
613		Submit Advice Letter	N/A	N/A	N/A	
614		Advice Letter Approved	N/A	N/A	N/A	
615		Implementation Plan	42 days	Fri 12/30/22	Mon 2/27/23	
616		SCG - Retail Partnering Solicitation	29 days?	Tue 9/27/22	Fri 11/4/22	
617		RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22	
618		RFP Release	1 day	Fri 6/17/22	Fri 6/17/22	
619		RFP Proposal Creation Duration	30 days	Mon 6/20/22	Fri 7/29/22	
620		RFP Evaluation	24 days	Mon 8/1/22	Thu 9/1/22	
621		RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




ID		Task Name	Duration	Start	Finish	2018 H1
622		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/13/22	Tue 9/13/22	
623		Contract Negotiation and Development	29 days	Mon 9/19/22	Thu 10/27/22	
624		Contract Review with EE PRG	9 days	Tue 11/1/22	Fri 11/11/22	
625		Final Award and Contract Signed	13 days	Mon 11/14/22	Wed 11/30/22	
626		Submit Advice Letter	N/A	N/A	N/A	
627		Advice Letter Approved	N/A	N/A	N/A	
628		Implementation Plan	43 days	Sat 10/1/22	Tue 11/29/22	
629		SCG - Non-Residential EE Advisor Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22	
630		RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22	
631		RFP Release	1 day	Fri 8/26/22	Fri 8/26/22	
632		RFP Proposal Creation Duration	20 days	Mon 8/29/22	Fri 9/23/22	
633		RFP Evaluation	16 days	Sat 9/24/22	Fri 10/14/22	
634		RFP Review with EE PRG	5 days	Mon 10/17/22	Fri 10/21/22	
635		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/25/22	Tue 10/25/22	
636		Contract Negotiation and Development	32 days	Sun 10/30/22	Mon 12/12/22	
637		Contract Review with EE PRG	9 days	Tue 12/13/22	Fri 12/23/22	
638		Final Award and Contract Signed	4 days	Tue 12/27/22	Fri 12/30/22	
639		Submit Advice Letter	N/A	N/A	N/A	
640		Advice Letter Approved	N/A	N/A	N/A	
641		Implementation Plan	44 days	Sun 1/1/23	Wed 3/1/23	
642		SCG - Residential EE Kits Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22	
643		RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22	
644		RFP Release	1 day	Mon 7/25/22	Mon 7/25/22	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
645		RFP Proposal Creation Duration	16 days	Tue 7/26/22	Tue 8/16/22	
646		RFP Evaluation	12 days	Wed 8/17/22	Thu 9/1/22	
647		RFP Review with EE PRG	1 day	Tue 8/2/22	Tue 8/2/22	
648		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/9/22	Tue 8/9/22	
649		Contract Negotiation and Development	30 days	Mon 8/22/22	Fri 9/30/22	
650		Contract Review with EE PRG	9 days	Tue 10/4/22	Fri 10/14/22	
651		Final Award and Contract Signed	10 days	Mon 10/17/22	Fri 10/28/22	
652		Submit Advice Letter	N/A	N/A	N/A	
653		Advice Letter Approved	N/A	N/A	N/A	
654		Implementation Plan	43 days	Sat 10/29/22	Tue 12/27/22	
655		SCG - IDEEA 365	230 days	Mon 2/13/23	Fri 12/29/23	
656		RFP Preparation	23 days	Mon 2/13/23	Wed 3/15/23	
657		RFP Release	20 days	Thu 4/20/23	Wed 5/17/23	
658		RFP Proposal Creation Duration	43 days	Wed 5/3/23	Fri 6/30/23	
659		RFP Evaluation	12 days	Fri 7/14/23	Mon 7/31/23	
660		RFP Review with EE PRG	1 day	Tue 8/1/23	Tue 8/1/23	
661		RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Tue 8/1/23	Thu 8/31/23	
662		Contract Negotiation and Development	21 days	Fri 9/1/23	Fri 9/29/23	
663		Contract Review with EE PRG	32 days	Mon 9/18/23	Tue 10/31/23	
664		Final Award and Contract Signed	17 days	Mon 10/9/23	Tue 10/31/23	
665		Submit Advice Letter	10 days	Wed 11/1/23	Tue 11/14/23	
666		Advice Letter Approved	11 days	Wed 11/22/23	Wed 12/6/23	
667		Implementation Plan	9 days	Tue 12/19/23	Fri 12/29/23	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
668		SCG - Commercial SEM	110 days?	Tue 8/1/23	Mon 1/1/24	
669		RFP Preparation	22 days	Tue 8/1/23	Wed 8/30/23	
670		RFP Release	13 days	Wed 9/13/23	Fri 9/29/23	
671		RFP Proposal Creation Duration	11 days	Mon 10/2/23	Mon 10/16/23	
672		RFP Evaluation	5 days	Wed 10/25/23	Tue 10/31/23	
673		RFP Review with EE PRG	2 days	Tue 10/31/23	Wed 11/1/23	
674		RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Thu 11/2/23	Wed 11/8/23	
675		Contract Negotiation and Development	16 days	Wed 10/25/23	Wed 11/15/23	
676		Contract Review with EE PRG	1 day	Tue 12/5/23	Tue 12/5/23	
677		Final Award and Contract Signed	6 days	Wed 12/13/23	Wed 12/20/23	
678		Submit Advice Letter	5 days	Mon 12/18/23	Fri 12/22/23	
679		Advice Letter Approved	1 day	Fri 12/29/23	Fri 12/29/23	
680		Implementation Plan	1 day	Mon 1/1/24	Mon 1/1/24	
681		SCG - Market Access Program	333 days?	Sat 3/16/24	Tue 6/24/25	
682		RFP Preparation	75 days	Sat 3/16/24	Thu 6/27/24	
683		RFP Release	1 day	Fri 6/21/24	Fri 6/21/24	
684		RFP Proposal Creation Duration	53 days	Mon 6/24/24	Wed 9/4/24	
685		RFP Evaluation	38 days	Mon 8/19/24	Wed 10/9/24	
686		RFP Review with EE PRG	1 day	Tue 10/1/24	Tue 10/1/24	
687		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/8/24	Tue 10/8/24	
688		Contract Negotiation and Development	78 days	Mon 10/14/24	Wed 1/29/25	
689		Contract Review with EE PRG	10 days	Tue 1/7/25	Mon 1/20/25	
690		Final Award and Contract Signed	11 days	Mon 1/20/25	Mon 2/3/25	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
691		Submit Advice Letter	N/A	Wed 1/1/25		
692		Advice Letter Approved	N/A	Mon 3/3/25		
693		Implementation Plan	59 days	Thu 4/3/25	Tue 6/24/25	
694		SCG - IDEEA 365 (Round 3)	230 days?	Tue 10/15/24	Mon 9/1/25	
695		RFP Preparation	23 days	Tue 10/15/24	Thu 11/14/24	
696		RFP Release	20 days	Fri 11/15/24	Thu 12/12/24	
697		RFP Proposal Creation Duration	43 days	Fri 12/13/24	Tue 2/11/25	
698		RFP Evaluation	12 days	Wed 2/12/25	Thu 2/27/25	
699		RFP Review with EE PRG	1 day	Fri 2/28/25	Fri 2/28/25	
700		RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Mon 3/3/25	Wed 4/2/25	
701		Contract Negotiation and Development	21 days	Thu 4/3/25	Thu 5/1/25	
702		Contract Review with EE PRG	32 days	Fri 5/2/25	Mon 6/16/25	
703		Final Award and Contract Signed	17 days	Tue 6/17/25	Wed 7/9/25	
704		Submit Advice Letter	10 days	Thu 7/10/25	Wed 7/23/25	
705		Advice Letter Approved	11 days	Thu 7/24/25	Thu 8/7/25	
706		Implementation Plan	9 days	Fri 8/8/25	Wed 8/20/25	
707						
708		<i>Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change</i>				
709		SDG&E - Small Commercial (<20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20	
710		SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18	
711		SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18	
712		SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18	
713		SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
714		SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19	
715		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19	
716		SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19	
717		SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19	
718		SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19	
719		SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19	
720		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20	
721		SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20	
722		SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20	
723		SDG&E - Contract Review with EE PRG	0 days	Tue 6/9/20	Tue 6/9/20	
724		SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20	
725		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20	
726		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20	
727		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20	
728		SDG&E - Large Commercial (>20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20	
729		SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18	
730		SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18	
731		SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18	
732		SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19	
733		SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19	
734		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19	
735		SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19	
736		SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
737		SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19	
738		SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19	
739		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20	
740		SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20	
741		SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20	
742		SDG&E - Contract Review with EE PRG	0 days	Tue 5/12/20	Tue 5/12/20	
743		SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20	
744		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20	
745		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20	
746		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20	
747		SDG&E - Residential Multi-Family Solicitation	586 days	Thu 9/6/18	Thu 12/3/20	
748		SDG&E - RFA Preparation	64 days	Thu 9/6/18	Tue 12/4/18	
749		SDG&E - RFA Release	23 days	Tue 12/4/18	Thu 1/3/19	
750		SDG&E - RFA Abstract Creation Duration	49 days	Tue 9/11/18	Fri 11/16/18	
751		SDG&E - RFA Evaluation	21 days	Mon 1/7/19	Mon 2/4/19	
752		SDG&E - RFA Review with EE PRG	0 days	Tue 11/13/18	Tue 11/13/18	
753		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 3/20/19	Wed 3/20/19	
754		SDG&E - RFP Preparation	63 days	Fri 3/22/19	Tue 6/18/19	
755		SDG&E - RFP Release	52 days	Tue 6/18/19	Wed 8/28/19	
756		SDG&E - RFP Proposal Creation Duration	36 days	Mon 3/25/19	Mon 5/13/19	
757		SDG&E - RFP Evaluation	30 days	Thu 8/29/19	Wed 10/9/19	
758		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Thu 12/12/19	Thu 12/19/19	
759		SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
760		SDG&E - Contract Negotiation and Development	35 days	Mon 4/13/20	Fri 5/29/20	
761		SDG&E - Contract Review with EE PRG	10 days	Thu 6/4/20	Wed 6/17/20	
762		SDG&E - Final Award and Contract Signed	0 days	Mon 6/22/20	Mon 6/22/20	
763		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20	
764		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20	
765		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20	
766		SDG&E - SW HVAC Solicitation	593 days	Thu 11/1/18	Tue 2/9/21	
767		SDG&E - RFA Preparation	48 days	Thu 11/1/18	Mon 1/7/19	
768		SDG&E - RFA Release	0 days	Mon 1/7/19	Mon 1/7/19	
769		SDG&E - RFA Abstract Creation Duration	24 days	Mon 1/7/19	Thu 2/7/19	
770		SDG&E - RFA Evaluation	37 days	Fri 2/8/19	Sun 3/31/19	
771		SDG&E - RFA Review with EE PRG	0 days	Tue 4/9/19	Tue 4/9/19	
772		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 4/17/19	Wed 4/17/19	
773		SDG&E - RFP Preparation	73 days	Thu 4/18/19	Mon 7/29/19	
774		SDG&E - RFP Release	0 days	Tue 9/3/19	Tue 9/3/19	
775		SDG&E - RFP Proposal Creation Duration	30 days	Tue 9/3/19	Mon 10/14/19	
776		SDG&E - RFP Evaluation	33 days	Mon 10/14/19	Wed 11/27/19	
777		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20	
778		SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20	
779		SDG&E - Contract Negotiation and Development	88 days	Wed 3/25/20	Fri 7/24/20	
780		SDG&E - Contract Review with EE PRG	0 days	Tue 9/8/20	Tue 9/8/20	
781		SDG&E - Final Award and Contract Signed	0 days	Fri 10/30/20	Fri 10/30/20	
782		SDG&E - Submit Advice Letter	0 days	Thu 11/12/20	Thu 11/12/20	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
783		SDG&E - Advice Letter Approved	0 days	Fri 12/11/20	Fri 12/11/20	
784		SDG&E - Implementation Plan	0 days	Tue 2/9/21	Tue 2/9/21	
785		SDG&E - SW PLA Solicitation	853 days	Mon 1/28/19	Wed 5/4/22	
786		SDG&E - RFA Preparation	75 days	Mon 1/28/19	Fri 5/10/19	
787		SDG&E - RFA Release	0 days	Fri 5/10/19	Fri 5/10/19	
788		SDG&E - RFA Abstract Creation Duration	31 days	Fri 5/10/19	Fri 6/21/19	
789		SDG&E - RFA Evaluation	65 days	Mon 6/24/19	Fri 9/20/19	
790		SDG&E - RFA Review with EE PRG	0 days	Tue 9/10/19	Tue 9/10/19	
791		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 9/20/19	Fri 9/20/19	
792		SDG&E - RFP Preparation	52 days	Fri 9/20/19	Mon 12/2/19	
793		SDG&E - RFP Release	0 days	Mon 1/27/20	Mon 1/27/20	
794		SDG&E - RFP Proposal Creation Duration	31 days	Mon 1/27/20	Mon 3/9/20	
795		SDG&E - RFP Evaluation	82 days	Mon 3/9/20	Tue 6/30/20	
796		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/17/20	Mon 8/17/20	
797		SDG&E - Selection Review with EE PRG	66 days	Tue 10/13/20	Tue 1/12/21	
798		SDG&E - Contract Negotiation and Development	197 days	Fri 1/29/21	Mon 11/1/21	
799		SDG&E - Contract Review with EE PRG	0 days	Tue 11/9/21	Tue 11/9/21	
800		SDG&E - Final Award and Contract Signed	0 days	Fri 1/7/22	Fri 1/7/22	
801		SDG&E - Submit Advice Letter	0 days	Mon 1/10/22	Mon 1/10/22	
802		SDG&E - Advice Letter Approved	0 days	Thu 2/10/22	Thu 2/10/22	
803		SDG&E - Implementation Plan	60 days	Thu 2/10/22	Wed 5/4/22	
804		SDG&E - Residential Single-Family 2.0 Solicitation	467 days	Tue 1/19/21	Wed 11/2/22	
805		SDG&E - RFA Preparation	43 days	Tue 1/19/21	Thu 3/18/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
806		SDG&E - RFA Release	0 days	Mon 3/22/21	Mon 3/22/21	
807		SDG&E - RFA Abstract Creation Duration	22 days	Mon 3/22/21	Tue 4/20/21	
808		SDG&E - RFA Evaluation	38 days	Wed 4/21/21	Fri 6/11/21	
809		SDG&E - RFA Review with EE PRG	7 days	Thu 6/3/21	Fri 6/11/21	
810		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 6/15/21	Tue 6/15/21	
811		SDG&E - RFP Preparation	43 days	Wed 6/16/21	Fri 8/13/21	
812		SDG&E - RFP Release	0 days	Wed 8/18/21	Wed 8/18/21	
813		SDG&E - RFP Proposal Creation Duration	32 days	Wed 8/18/21	Thu 9/30/21	
814		SDG&E - RFP Evaluation	44 days	Fri 10/1/21	Wed 12/1/21	
815		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 12/14/21	Tue 12/14/21	
816		SDG&E - Selection Review with EE PRG	7 days	Thu 12/2/21	Fri 12/10/21	
817		SDG&E - Contract Negotiation and Development	96 days	Mon 12/20/21	Mon 5/2/22	
818		SDG&E - Contract Review with EE PRG	7 days	Thu 5/5/22	Fri 5/13/22	
819		SDG&E - Final Award and Contract Signed	0 days	Tue 5/31/22	Tue 5/31/22	
820		SDG&E - Submit Advice Letter	0 days	Fri 6/24/22	Fri 6/24/22	
821		SDG&E - Advice Letter Approved	0 days	Thu 8/11/22	Thu 8/11/22	
822		SDG&E - Implementation Plan	60 days	Thu 8/11/22	Wed 11/2/22	
823		SDG&E - Residential Single-Family Solicitation	501 days	Mon 7/1/19	Tue 6/1/21	
824		SDG&E - RFA Preparation	80 days	Mon 7/1/19	Fri 10/18/19	
825		SDG&E - RFA Release	35 days	Fri 10/18/19	Thu 12/5/19	
826		SDG&E - RFA Abstract Creation Duration	53 days	Mon 7/22/19	Wed 10/2/19	
827		SDG&E - RFA Evaluation	29 days	Fri 12/6/19	Wed 1/15/20	
828		SDG&E - RFA Review with EE PRG	0 days	Tue 10/8/19	Tue 10/8/19	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
829		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 2/27/20	Thu 2/27/20	
830		SDG&E - RFP Preparation	48 days	Fri 2/28/20	Tue 5/5/20	
831		SDG&E - RFP Release	0 days	Mon 4/27/20	Mon 4/27/20	
832		SDG&E - RFP Proposal Creation Duration	32 days	Mon 4/27/20	Tue 6/9/20	
833		SDG&E - RFP Evaluation	16 days	Wed 6/10/20	Wed 7/1/20	
834		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 7/23/20	Fri 7/24/20	
835		SDG&E - Selection Review with EE PRG	7 days	Thu 8/6/20	Fri 8/14/20	
836		SDG&E - Contract Negotiation and Development	60 days	Mon 8/17/20	Fri 11/6/20	
837		SDG&E - Contract Review with EE PRG	10 days	Tue 12/8/20	Mon 12/21/20	
838		SDG&E - Final Award and Contract Signed	0 days	Fri 1/29/21	Fri 1/29/21	
839		SDG&E - Submit Advice Letter	0 days	Mon 3/1/21	Mon 3/1/21	
840		SDG&E - Advice Letter Approved				
841		SDG&E - Implementation Plan	0 days	Tue 6/1/21	Tue 6/1/21	
842		SDG&E - Public Sector: Federal Solicitation	625 days	Mon 7/1/19	Fri 11/19/21	
843		SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19	
844		SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19	
845		SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19	
846		SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20	
847		SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20	
848		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20	
849		SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20	
850		SDG&E - RFP Release	0 days	Fri 5/22/20	Fri 5/22/20	
851		SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
852		SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20	
853		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20	
854		SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20	
855		SDG&E - Contract Negotiation and Development	53 days	Wed 2/17/21	Fri 4/30/21	
856		SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21	
857		SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21	
858		SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21	
859		SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21	
860		SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21	
861		SDG&E - Public Sector: K-12 Solicitation	625 days	Mon 7/1/19	Fri 11/19/21	
862		SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19	
863		SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19	
864		SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19	
865		SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20	
866		SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20	
867		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20	
868		SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20	
869		SDG&E - RFP Release	1 day	Fri 5/22/20	Fri 5/22/20	
870		SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20	
871		SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20	
872		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20	
873		SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20	
874		SDG&E - Contract Negotiation and Development	117 days	Thu 11/19/20	Fri 4/30/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
875		SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21	
876		SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21	
877		SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21	
878		SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21	
879		SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21	
880		SDG&E - Public Sector: Local Government Solicitation	338 days	Tue 10/13/20	Thu 1/27/22	
881		SDG&E - RFA Preparation	10 days	Fri 10/23/20	Thu 11/5/20	
882		SDG&E - RFA Release	1 day	Wed 1/27/21	Wed 1/27/21	
883		SDG&E - RFA Abstract Creation Duration	20 days	Thu 1/28/21	Wed 2/24/21	
884		SDG&E - RFA Evaluation	18 days	Fri 2/26/21	Tue 3/23/21	
885		SDG&E - RFA Review with EE PRG	7 days	Thu 4/8/21	Fri 4/16/21	
886		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/21/21	Wed 4/21/21	
887		SDG&E - RFP Preparation	51 days	Fri 3/19/21	Fri 5/28/21	
888		SDG&E - RFP Release	1 day	Tue 6/1/21	Tue 6/1/21	
889		SDG&E - RFP Proposal Creation Duration	26 days	Wed 6/2/21	Wed 7/7/21	
890		SDG&E - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21	
891		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/25/21	Mon 10/25/21	
892		SDG&E - Selection Review with EE PRG	7 days	Tue 10/12/21	Wed 10/20/21	
893		SDG&E - Contract Negotiation and Development	41 days	Fri 11/5/21	Fri 12/31/21	
894		SDG&E - Contract Review with EE PRG	7 days	Thu 1/6/22	Fri 1/14/22	
895		SDG&E - Final Award and Contract Signed	9 days	Mon 1/17/22	Thu 1/27/22	
896		SDG&E - Submit Advice Letter	13 days	Wed 6/1/22	Fri 6/17/22	
897		SDG&E - Advice Letter Approved	40 days	Fri 6/17/22	Thu 8/11/22	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
898		SDG&E - Implementation Plan	42 days	Mon 8/15/22	Tue 10/11/22	
899		SDG&E - Agricultural Sector: Local Agriculture Solicitation	447 days	Mon 3/1/21	Tue 11/15/22	
900		SDG&E - RFA Preparation	56 days	Mon 3/1/21	Mon 5/17/21	
901		SDG&E - RFA Release	0 days	Mon 4/26/21	Mon 4/26/21	
902		SDG&E - RFA Abstract Creation Duration	20 days	Tue 4/27/21	Mon 5/24/21	
903		SDG&E - RFA Evaluation	36 days	Tue 6/1/21	Tue 7/20/21	
904		SDG&E - RFA Review with EE PRG	0 days	Thu 7/8/21	Thu 7/8/21	
905		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 7/20/21	Tue 7/20/21	
906		SDG&E - RFP Preparation	48 days	Tue 7/20/21	Thu 9/23/21	
907		SDG&E - RFP Release	0 days	Thu 9/23/21	Thu 9/23/21	
908		SDG&E - RFP Proposal Creation Duration	25 days	Fri 9/24/21	Thu 10/28/21	
909		SDG&E - RFP Evaluation	23 days	Thu 10/28/21	Mon 11/29/21	
910		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 2/1/22	Tue 2/1/22	
911		SDG&E - Selection Review with EE PRG	0 days	Tue 2/8/22	Tue 2/8/22	
912		SDG&E - Contract Negotiation and Development	83 days	Tue 2/1/22	Thu 5/26/22	
913		SDG&E - Contract Review with EE PRG	0 days	Tue 6/14/22	Tue 6/14/22	
914		SDG&E - Final Award and Contract Signed	10 days	Fri 6/18/21	Thu 7/1/21	
915		SDG&E - Submit Advice Letter	0 days	Fri 7/22/22	Fri 7/22/22	
916		SDG&E - Advice Letter Approved	0 days	Tue 8/30/22	Tue 8/30/22	
917		SDG&E - Implementation Plan	44 days	Wed 8/31/22	Sat 10/29/22	
918		*SDG&E - Industrial Solicitation	426 days	Thu 4/1/21	Thu 11/17/22	
919		SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21	
920		SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
921		SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21	
922		SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21	
923		SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21	
924		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21	
925		SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21	
926		SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21	
927		SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22	
928		SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22	
929		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22	
930		SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22	
931		SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22	
932		SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22	
933		SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22	
934		SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22	
935		SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22	
936		SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23	
937		*SDG&E - Industrial-Port Tenants Solicitation	426 days	Thu 4/1/21	Thu 11/17/22	
938		SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21	
939		SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21	
940		SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21	
941		SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21	
942		SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21	
943		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
944		SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21	
945		SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21	
946		SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22	
947		SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22	
948		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22	
949		SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22	
950		SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22	
951		SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22	
952		SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22	
953		SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22	
954		SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22	
955		SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23	
956		*SDG&E - SW Residential HVAC QI/QM Solicitation	377 days	Mon 7/5/21	Tue 12/13/22	
957		SDG&E - RFA Preparation	48 days	Mon 7/5/21	Wed 9/8/21	
958		SDG&E - RFA Release	1 day	Wed 9/29/21	Wed 9/29/21	
959		SDG&E - RFA Abstract Creation Duration	22 days	Wed 9/29/21	Thu 10/28/21	
960		SDG&E - RFA Evaluation	21 days	Fri 10/29/21	Fri 11/26/21	
961		SDG&E - RFA Review with EE PRG	6 days	Fri 12/10/21	Fri 12/17/21	
962		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 12/22/21	Wed 12/22/21	
963		SDG&E - RFP Preparation	56 days	Tue 1/4/22	Tue 3/22/22	
964		SDG&E - RFP Release	1 day	Tue 3/22/22	Tue 3/22/22	
965		SDG&E - RFP Proposal Creation Duration	23 days	Wed 3/23/22	Fri 4/22/22	
966		SDG&E - RFP Evaluation	20 days	Mon 4/25/22	Fri 5/20/22	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
967		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/21/22	Tue 6/21/22	
968		SDG&E - Selection Review with EE PRG	0 days	Fri 6/17/22	Fri 6/17/22	
969		SDG&E - Contract Negotiation and Development	83 days	Wed 7/20/22	Fri 11/11/22	
970		SDG&E - Contract Review with EE PRG	6 days	Mon 11/14/22	Mon 11/21/22	
971		SDG&E - Final Award and Contract Signed	1 day	Mon 1/10/22	Mon 1/10/22	
972		SDG&E - Submit Advice Letter	22 days	Sun 1/15/23	Mon 2/13/23	
973		SDG&E - Advice Letter Approved	1 day	Fri 4/28/23	Fri 4/28/23	
974		SDG&E - Implementation Plan	60 days	Fri 4/28/23	Thu 7/20/23	
975		*SDG&E - Local/Residential Behavioral Solicitation	472 days	Mon 4/19/21	Tue 2/7/23	
976		SDG&E - RFA Preparation	53 days	Mon 4/19/21	Wed 6/30/21	
977		SDG&E - RFA Release	1 day	Mon 7/26/21	Mon 7/26/21	
978		SDG&E - RFA Abstract Creation Duration	21 days	Mon 7/26/21	Mon 8/23/21	
979		SDG&E - RFA Evaluation	30 days	Tue 8/24/21	Mon 10/4/21	
980		SDG&E - RFA Review with EE PRG	7 days	Thu 10/7/21	Fri 10/15/21	
981		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/19/21	Tue 10/19/21	
982		SDG&E - RFP Preparation	28 days	Thu 10/21/21	Mon 11/29/21	
983		SDG&E - RFP Release	1 day	Wed 12/22/21	Wed 12/22/21	
984		SDG&E - RFP Proposal Creation Duration	20 days	Wed 12/22/21	Tue 1/18/22	
985		SDG&E - RFP Evaluation	28 days	Wed 1/19/22	Fri 2/25/22	
986		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/15/22	Tue 3/15/22	
987		SDG&E - Selection Review with EE PRG	7 days	Thu 3/3/22	Fri 3/11/22	
988		SDG&E - Contract Negotiation and Development	119 days	Fri 3/18/22	Wed 8/31/22	
989		SDG&E - Contract Review with EE PRG	7 days	Thu 9/8/22	Fri 9/16/22	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
990		SDG&E - Final Award and Contract Signed	1 day	Fri 10/21/22	Fri 10/21/22	
991		SDG&E - Submit Advice Letter	1 day	Wed 11/16/22	Wed 11/16/22	
992		SDG&E - Advice Letter Approved	1 day	Fri 12/16/22	Fri 12/16/22	
993		SDG&E - Implementation Plan	60 days	Wed 11/16/22	Tue 2/7/23	
994		*SDG&E - Small Business Outreach Solicitation	298 days?	Wed 4/13/22	Fri 6/2/23	
995		SDG&E - RFA Preparation	53 days	Wed 4/13/22	Fri 6/24/22	
996		SDG&E - RFA Release	1 day	Thu 7/7/22	Thu 7/7/22	
997		SDG&E - RFA Abstract Creation Duration	21 days	Fri 7/8/22	Fri 8/5/22	
998		SDG&E - RFA Evaluation	30 days	Mon 8/8/22	Fri 9/16/22	
999		SDG&E - RFA Review with EE PRG	5 days	Mon 9/19/22	Fri 9/23/22	
1000		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/27/22	Tue 9/27/22	
1001		SDG&E - RFP Preparation	28 days	Mon 8/8/22	Wed 9/14/22	
1002		SDG&E - RFP Release	1 day	Tue 10/18/22	Tue 10/18/22	
1003		SDG&E - RFP Proposal Creation Duration	31 days	Tue 10/18/22	Tue 11/29/22	
1004		SDG&E - RFP Evaluation	38 days	Wed 11/30/22	Fri 1/20/23	
1005		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/28/23	Tue 2/28/23	
1006		SDG&E - Selection Review with EE PRG	7 days	Thu 2/16/23	Fri 2/24/23	
1007		SDG&E - Contract Negotiation and Development	79 days	Tue 2/28/23	Fri 6/16/23	
1008		SDG&E - Contract Review with EE PRG	4 days	Wed 6/21/23	Mon 6/26/23	
1009		SDG&E - Final Award and Contract Signed	1 day	Tue 8/29/23	Tue 8/29/23	
1010		SDG&E - Submit Advice Letter	1 day	Fri 9/15/23	Fri 9/15/23	
1011		SDG&E - Advice Letter Approved	1 day	Mon 10/16/23	Mon 10/16/23	
1012		SDG&E - Implementation Plan	46 days	Mon 10/16/23	Mon 12/18/23	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only



ID		Task Name	Duration	Start	Finish	2018 H1
1013		*SDG&E - Workforce Education & Training /Integrated Energy Education Solicitatio	353 days?	Mon 1/16/23	Wed 5/22/24	
1014		SDG&E - RFP Release	1 day?	Thu 2/2/23	Thu 2/2/23	
1015		SDG&E - RFP Evaluation	25 days	Fri 3/17/23	Thu 4/20/23	
1016		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/16/23	Tue 5/16/23	
1017		SDG&E - Selection Review with EE PRG	5 days	Tue 5/9/23	Mon 5/15/23	
1018		SDG&E - Contract Negotiation and Development	94 days	Fri 5/5/23	Wed 9/13/23	
1019		SDG&E - Contract Review with EE PRG	7 days	Tue 10/10/23	Wed 10/18/23	
1020		SDG&E - Final Award and Contract Signed	1 day	Tue 11/14/23	Tue 11/14/23	
1021		SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24	
1022		SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24	
1023		SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24	
1024		*SDG&E - Residential Equity Education & Outreach Solicitation	331 days?	Fri 1/13/23	Fri 4/19/24	
1025		SDG&E - RFA Release	1 day	Thu 3/2/23	Thu 3/2/23	
1026		SDG&E - RFA Evaluation	21 days	Wed 4/12/23	Wed 5/10/23	
1027		SDG&E - RFA Review with EE PRG	7 days	Fri 5/19/23	Mon 5/29/23	
1028		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/30/23	Tue 5/30/23	
1029		SDG&E - RFP Release	1 day	Thu 6/1/23	Thu 6/1/23	
1030		SDG&E - RFP Evaluation	27 days	Mon 7/17/23	Tue 8/22/23	
1031		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/28/23	Mon 8/28/23	
1032		SDG&E - Selection Review with EE PRG	7 days	Wed 8/30/23	Thu 9/7/23	
1033		SDG&E - Contract Negotiation and Development	32 days	Thu 11/2/23	Fri 12/15/23	
1034		SDG&E - Contract Review with EE PRG	7 days	Tue 1/9/24	Wed 1/17/24	
1035		SDG&E - Final Award and Contract Signed	1 day	Mon 2/12/24	Mon 2/12/24	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
1036		SDG&E - Submit Advice Letter	1 day	Mon 2/26/24	Mon 2/26/24	
1037		SDG&E - Advice Letter Approved	1 day	Mon 4/8/24	Mon 4/8/24	
1038		SDG&E - Implementation Plan	60 days	Tue 4/9/24	Mon 7/1/24	
1039		*SDG&E - Non-Residential Behavioral Solicitation	398 days	Mon 8/15/22	Wed 2/21/24	
1040		SDG&E - RFA Preparation	67 days	Mon 8/15/22	Tue 11/15/22	
1041		SDG&E - RFA Release	1 day	Mon 10/24/22	Mon 10/24/22	
1042		SDG&E - RFA Abstract Creation Duration	27 days	Tue 8/23/22	Wed 9/28/22	
1043		SDG&E - RFA Evaluation	16 days	Tue 11/29/22	Tue 12/20/22	
1044		SDG&E - RFA Review with EE PRG	7 days	Thu 1/5/23	Fri 1/13/23	
1045		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 1/18/23	Wed 1/18/23	
1046		SDG&E - RFP Preparation	26 days	Mon 11/14/22	Mon 12/19/22	
1047		SDG&E - RFP Release	1 day	Mon 1/23/23	Mon 1/23/23	
1048		SDG&E - RFP Proposal Creation Duration	26 days	Mon 1/23/23	Mon 2/27/23	
1049		SDG&E - RFP Evaluation	58 days	Tue 2/28/23	Thu 5/18/23	
1050		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/20/23	Tue 6/20/23	
1051		SDG&E - Selection Review with EE PRG	7 days	Thu 6/8/23	Fri 6/16/23	
1052		SDG&E - Contract Negotiation and Development	60 days	Wed 6/21/23	Tue 9/12/23	
1053		SDG&E - Contract Review with EE PRG	7 days	Thu 10/5/23	Fri 10/13/23	
1054		SDG&E - Final Award and Contract Signed	1 day	Thu 12/21/23	Thu 12/21/23	
1055		SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24	
1056		SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24	
1057		SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24	
1058		*SDG&E - Retail Offices and Wholesale Solicitation	419 days	Wed 5/10/23	Mon 12/16/24	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone



Finish-only



ID		Task Name	Duration	Start	Finish	2018 H1
1059		SDG&E - RFA Preparation	33 days	Wed 5/10/23	Fri 6/23/23	
1060		SDG&E - RFA Release	1 day	Mon 7/3/23	Mon 7/3/23	
1061		SDG&E - RFA Abstract Creation Duration	31 days	Tue 7/4/23	Tue 8/15/23	
1062		SDG&E - RFA Evaluation	19 days	Wed 8/16/23	Mon 9/11/23	
1063		SDG&E - RFA Review with EE PRG	3 days	Mon 9/18/23	Wed 9/20/23	
1064		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 9/25/23	Mon 9/25/23	
1065		SDG&E - RFP Preparation	33 days	Wed 7/5/23	Fri 8/18/23	
1066		SDG&E - RFP Release	1 day	Fri 9/29/23	Fri 9/29/23	
1067		SDG&E - RFP Proposal Creation Duration	33 days	Mon 10/2/23	Wed 11/15/23	
1068		SDG&E - RFP Evaluation	25 days	Thu 11/16/23	Wed 12/20/23	
1069		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 2/19/24	Mon 2/19/24	
1070		SDG&E - Selection Review with EE PRG	7 days	Thu 2/8/24	Fri 2/16/24	
1071		SDG&E - Contract Negotiation and Development	96 days	Mon 2/26/24	Mon 7/8/24	
1072		SDG&E - Contract Review with EE PRG	6 days	Wed 7/17/24	Wed 7/24/24	
1073		SDG&E - Final Award and Contract Signed	1 day	Tue 8/27/24	Tue 8/27/24	
1074		SDG&E - Submit Advice Letter	1 day	Mon 9/16/24	Mon 9/16/24	
1075		SDG&E - Advice Letter Approved	1 day	Wed 10/16/24	Wed 10/16/24	
1076		SDG&E - Implementation Plan	44 days	Wed 10/16/24	Mon 12/16/24	
1077		*SDG&E - Groceries, Restaurants and Food Storage Solicitation	467 days	Wed 6/14/23	Thu 3/27/25	
1078		SDG&E - RFA Preparation	33 days	Wed 6/14/23	Fri 7/28/23	
1079		SDG&E - RFA Release	1 day	Tue 8/15/23	Tue 8/15/23	
1080		SDG&E - RFA Abstract Creation Duration	21 days	Wed 8/16/23	Wed 9/13/23	
1081		SDG&E - RFA Evaluation	15 days	Thu 9/14/23	Wed 10/4/23	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




ID		Task Name	Duration	Start	Finish	2018 H1
1082		SDG&E - RFA Review with EE PRG	5 days	Wed 10/18/23	Tue 10/24/23	
1083		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/30/23	Mon 10/30/23	
1084		SDG&E - RFP Preparation	16 days	Mon 10/9/23	Mon 10/30/23	
1085		SDG&E - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23	
1086		SDG&E - RFP Proposal Creation Duration	40 days	Mon 11/6/23	Fri 12/29/23	
1087		SDG&E - RFP Evaluation	34 days	Fri 12/29/23	Wed 2/14/24	
1088		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 3/6/24	Wed 3/6/24	
1089		SDG&E - Selection Review with EE PRG	7 days	Thu 2/29/24	Fri 3/8/24	
1090		SDG&E - Contract Negotiation and Development	144 days	Wed 3/13/24	Mon 9/30/24	
1091		SDG&E - Contract Review with EE PRG	6 days	Tue 10/8/24	Tue 10/15/24	
1092		SDG&E - Final Award and Contract Signed	1 day	Tue 11/26/24	Tue 11/26/24	
1093		SDG&E - Submit Advice Letter	1 day	Fri 12/27/24	Fri 12/27/24	
1094		SDG&E - Advice Letter Approved	1 day	Mon 1/27/25	Mon 1/27/25	
1095		SDG&E - Implementation Plan	44 days	Mon 1/27/25	Thu 3/27/25	
1096		*SDG&E - Private Institutions and Healthcare Solicitation	399 days	Thu 10/5/23	Tue 4/15/25	
1097		SDG&E - RFA Preparation	33 days	Thu 10/5/23	Mon 11/20/23	
1098		SDG&E - RFA Release	1 day	Mon 11/27/23	Mon 11/27/23	
1099		SDG&E - RFA Abstract Creation Duration	35 days	Mon 11/27/23	Fri 1/12/24	
1100		SDG&E - RFA Evaluation	30 days	Mon 1/15/24	Fri 2/23/24	
1101		SDG&E - RFA Review with EE PRG	5 days	Mon 2/26/24	Fri 3/1/24	
1102		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 3/4/24	Mon 3/4/24	
1103		SDG&E - RFP Preparation	54 days	Mon 11/27/23	Thu 2/8/24	
1104		SDG&E - RFP Release	1 day	Fri 3/8/24	Fri 3/8/24	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
1105		SDG&E - RFP Proposal Creation Duration	34 days	Fri 3/8/24	Wed 4/24/24	
1106		SDG&E - RFP Evaluation	42 days	Thu 4/25/24	Fri 6/21/24	
1107		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 7/2/24	Tue 7/2/24	
1108		SDG&E - Selection Review with EE PRG	7 days	Fri 6/21/24	Mon 7/1/24	
1109		SDG&E - Contract Negotiation and Development	61 days	Wed 7/31/24	Wed 10/23/24	
1110		SDG&E - Contract Review with EE PRG	4 days	Tue 11/12/24	Fri 11/15/24	
1111		SDG&E - Final Award and Contract Signed	1 day	Tue 12/17/24	Tue 12/17/24	
1112		SDG&E - Submit Advice Letter	1 day	Wed 1/15/25	Wed 1/15/25	
1113		SDG&E - Advice Letter Approved	1 day	Fri 2/14/25	Fri 2/14/25	
1114		SDG&E - Implementation Plan	43 days	Fri 2/14/25	Tue 4/15/25	
1115		*SDG&E - Lodging: Hotels/Motels Solicitation	400 days	Tue 10/10/23	Mon 4/21/25	
1116		SDG&E - RFA Preparation	33 days	Tue 10/10/23	Thu 11/23/23	
1117		SDG&E - RFA Release	1 day	Fri 12/8/23	Fri 12/8/23	
1118		SDG&E - RFA Abstract Creation Duration	35 days	Fri 12/8/23	Thu 1/25/24	
1119		SDG&E - RFA Evaluation	22 days	Mon 1/22/24	Tue 2/20/24	
1120		SDG&E - RFA Review with EE PRG	7 days	Tue 3/12/24	Wed 3/20/24	
1121		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/19/24	Tue 3/19/24	
1122		SDG&E - RFP Preparation	48 days	Tue 1/23/24	Thu 3/28/24	
1123		SDG&E - RFP Release	1 day	Thu 3/21/24	Thu 3/21/24	
1124		SDG&E - RFP Proposal Creation Duration	29 days	Thu 3/21/24	Tue 4/30/24	
1125		SDG&E - RFP Evaluation	23 days	Mon 5/6/24	Wed 6/5/24	
1126		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/18/24	Tue 6/18/24	
1127		SDG&E - Selection Review with EE PRG	7 days	Thu 6/20/24	Fri 6/28/24	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
1128		SDG&E - Contract Negotiation and Development	61 days	Wed 7/31/24	Wed 10/23/24	
1129		SDG&E - Contract Review with EE PRG	4 days	Tue 11/12/24	Fri 11/15/24	
1130		SDG&E - Final Award and Contract Signed	1 day	Tue 12/17/24	Tue 12/17/24	
1131		SDG&E - Submit Advice Letter	1 day	Thu 1/16/25	Thu 1/16/25	
1132		SDG&E - Advice Letter Approved	1 day	Thu 2/20/25	Thu 2/20/25	
1133		SDG&E - Implementation Plan	43 days	Thu 2/20/25	Mon 4/21/25	
1134		*SDG&E - Market Access Program (MAP)	326 days	Wed 3/13/24	Wed 6/11/25	
1135		SDG&E - RFP Preparation	38 days	Wed 3/13/24	Fri 5/3/24	
1136		SDG&E - RFP Release	1 day	Tue 5/7/24	Tue 5/7/24	
1137		SDG&E - RFP Proposal Creation Duration	31 days	Tue 5/7/24	Tue 6/18/24	
1138		SDG&E - RFP Evaluation	43 days	Wed 6/19/24	Fri 8/16/24	
1139		SDG&E - Selection Review with EE PRG	7 days	Thu 9/5/24	Fri 9/13/24	
1140		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/17/24	Tue 9/17/24	
1141		SDG&E - Contract Negotiation and Development	60 days	Fri 9/27/24	Thu 12/19/24	
1142		SDG&E - Contract Review with EE PRG	3 days	Tue 12/10/24	Thu 12/12/24	
1143		SDG&E - Final Award and Contract Signed	1 day	Fri 1/31/25	Fri 1/31/25	
1144		SDG&E - Submit Advice Letter	1 day	Wed 3/12/25	Wed 3/12/25	
1145		SDG&E - Advice Letter Approved	1 day	Fri 4/11/25	Fri 4/11/25	
1146		SDG&E - Implementation Plan	44 days	Fri 4/11/25	Wed 6/11/25	
1147		Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change				
1148						
1149		PG&E - Local Government Partnerships (non-resource programs) Solicitation	376 days?	Fri 3/22/19	Fri 8/28/20	
1150		PG&E - RFA Preparation	42 days	Fri 3/22/19	Mon 5/20/19	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone



Finish-only



ID		Task Name	Duration	Start	Finish	2018 H1
1151		PG&E - RFA Release	1 day	Thu 5/23/19	Thu 5/23/19	
1152		PG&E - RFA Abstract Creation Duration	22 days	Thu 5/23/19	Fri 6/21/19	
1153		PG&E - RFA Evaluation	15 days	Mon 6/24/19	Fri 7/12/19	
1154		PG&E - RFA Review with EE PRG	4 days	Tue 7/23/19	Fri 7/26/19	
1155		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/5/19	Fri 8/9/19	
1156		PG&E - RFP Preparation	45 days	Tue 8/27/19	Mon 10/28/19	
1157		PG&E - RFP Release	1 day	Mon 11/4/19	Mon 11/4/19	
1158		PG&E - RFP Proposal Creation Duration	33 days	Mon 11/4/19	Wed 12/18/19	
1159		PG&E - RFP Evaluation	18 days	Mon 1/6/20	Wed 1/29/20	
1160		PG&E - RFP Review with EE PRG	4 days	Tue 2/25/20	Fri 2/28/20	
1161		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/2/20	Fri 3/6/20	
1162		PG&E - Contract Negotiation and Development	58 days	Fri 2/28/20	Tue 5/19/20	
1163		PG&E - Contract Review with EE PRG	7 days	Tue 5/26/20	Wed 6/3/20	
1164		PG&E - Final Award and Contract Signed	22 days	Fri 5/29/20	Mon 6/29/20	
1165		PG&E - Submit Advice Letter		N/A	N/A	
1166		PG&E - Advice Letter Approved				
1167		PG&E - Implementation Plan	24 days	Tue 7/28/20	Fri 8/28/20	
1168		PG&E - Statewide Codes & Standards (RFP only) Solicitation	221 days?	Mon 7/8/19	Mon 5/11/20	
1169		PG&E - RFA Preparation		N/A	N/A	
1170		PG&E - RFA Release		N/A	N/A	
1171		PG&E - RFA Abstract Creation Duration		N/A	N/A	
1172		PG&E - RFA Evaluation		N/A	N/A	
1173		PG&E - RFA Review with EE PRG		N/A	N/A	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




ID		Task Name	Duration	Start	Finish	2018 H1
1174		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A	
1175		PG&E - RFP Preparation	36 days	Mon 7/8/19	Mon 8/26/19	
1176		PG&E - RFP Release	1 day	Tue 9/10/19	Tue 9/10/19	
1177		PG&E - RFP Proposal Creation Duration	24 days	Tue 9/10/19	Fri 10/11/19	
1178		PG&E - RFP Evaluation	10 days	Mon 10/14/19	Fri 10/25/19	
1179		PG&E - RFP Review with EE PRG	4 days	Thu 11/21/19	Tue 11/26/19	
1180		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 11/27/19	Fri 11/29/19	
1181		PG&E - Contract Negotiation and Development	35 days	Mon 12/2/19	Fri 1/17/20	
1182		PG&E - Contract Review with EE PRG	4 days	Tue 1/21/20	Fri 1/24/20	
1183		PG&E - Final Award and Contract Signed	32 days	Wed 1/29/20	Thu 3/12/20	
1184		PG&E - Submit Advice Letter		N/A	N/A	
1185		PG&E - Advice Letter Approved				
1186		PG&E - Implementation Plan	32 days	Fri 3/27/20	Mon 5/11/20	
1187		PG&E - Local Multi-Sector (40% outsource) Solicitation	251 days?	Tue 4/28/20	Tue 4/13/21	
1188		PG&E - RFA Preparation		N/A	N/A	
1189		PG&E - RFA Release		N/A	N/A	
1190		PG&E - RFA Abstract Creation Duration		N/A	N/A	
1191		PG&E - RFA Evaluation		N/A	N/A	
1192		PG&E - RFA Review with EE PRG		N/A	N/A	
1193		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A	
1194		PG&E - RFP Preparation		N/A	N/A	
1195		PG&E - RFP Release		N/A	N/A	
1196		PG&E - RFP Proposal Creation Duration		N/A	N/A	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
1197		PG&E - RFP Evaluation		N/A	N/A	
1198		PG&E - RFP Review with EE PRG	4 days	Tue 4/28/20	Fri 5/1/20	
1199		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder				
1200		PG&E - Contract Negotiation and Development	81 days	Thu 7/2/20	Thu 10/22/20	
1201		PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20	
1202		PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20	
1203		PG&E - Submit Advice Letter	1 day	Wed 1/13/21	Wed 1/13/21	
1204		PG&E - Advice Letter Approved	1 day?	Fri 2/12/21	Fri 2/12/21	
1205		PG&E - Implementation Plan	43 days	Sat 2/13/21	Tue 4/13/21	
1206		PG&E - Statewide New Constructions (Non-Residential) Solicitation	591 days	Mon 3/25/19	Sun 6/27/21	
1207		PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19	
1208		PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19	
1209		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19	
1210		PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19	
1211		PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19	
1212		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19	
1213		PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20	
1214		PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20	
1215		PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20	
1216		PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20	
1217		PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20	
1218		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20	
1219		PG&E - Contract Negotiation and Development	49 days	Mon 8/17/20	Thu 10/22/20	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
1220		PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20	
1221		PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20	
1222		PG&E - Submit Advice Letter	1 day	Fri 2/19/21	Fri 2/19/21	
1223		PG&E - Advice Letter Approved	1 day	Wed 4/28/21	Wed 4/28/21	
1224		PG&E - Implementation Plan	43 days	Thu 4/29/21	Sun 6/27/21	
1225		PG&E - Statewide New Construction (Residential) Solicitation	640 days?	Mon 3/25/19	Fri 9/3/21	
1226		PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19	
1227		PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19	
1228		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19	
1229		PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19	
1230		PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19	
1231		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19	
1232		PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20	
1233		PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20	
1234		PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20	
1235		PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20	
1236		PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20	
1237		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20	
1238		PG&E - Contract Negotiation and Development	177 days	Mon 8/17/20	Tue 4/20/21	
1239		PG&E - Contract Review with EE PRG	16 days	Thu 4/22/21	Thu 5/13/21	
1240		PG&E - Final Award and Contract Signed	32 days	Sat 5/15/21	Mon 6/28/21	
1241		PG&E - Submit Advice Letter	1 day	Mon 7/12/21	Mon 7/12/21	
1242		PG&E - Advice Letter Approved (all electric)	1 day	Wed 8/11/21	Wed 8/11/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
1243		PG&E - Advice Letter Approved (mixed fuel)	1 day	Wed 9/15/21	Wed 9/15/21	
1244		PG&E - Implementation Plan (all electric)	43 days	Thu 8/12/21	Mon 10/11/21	
1245		PG&E - Implementation Plan (mixed fuel)	43 days	Thu 9/16/21	Sun 11/14/21	
1246		PG&E - Statewide WE&T Career Connections Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21	
1247		PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20	
1248		PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20	
1249		PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20	
1250		PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20	
1251		PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20	
1252		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20	
1253		PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20	
1254		PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20	
1255		PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20	
1256		PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20	
1257		PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20	
1258		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20	
1259		PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21	
1260		PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21	
1261		PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21	
1262		PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21	
1263		PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21	
1264		PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21	
1265		PG&E - Statewide WE&T Career and Workforce Readiness Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
1266		PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20	
1267		PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20	
1268		PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20	
1269		PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20	
1270		PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20	
1271		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20	
1272		PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20	
1273		PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20	
1274		PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20	
1275		PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20	
1276		PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20	
1277		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20	
1278		PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21	
1279		PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21	
1280		PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21	
1281		PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21	
1282		PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21	
1283		PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21	
1284		PG&E - Statewide State of CA (Dept. of Corrections) Solicitation	348 days?	Sun 3/1/20	Tue 6/29/21	
1285		PG&E - RFA Preparation	46 days	Sun 3/1/20	Fri 5/1/20	
1286		PG&E - RFA Release	1 day	Wed 5/13/20	Wed 5/13/20	
1287		PG&E - RFA Abstract Creation Duration	31 days	Wed 5/13/20	Wed 6/24/20	
1288		PG&E - RFA Evaluation	15 days	Mon 6/29/20	Fri 7/17/20	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
1289		PG&E - RFA Review with EE PRG	5 days	Tue 7/28/20	Mon 8/3/20	
1290		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/3/20	Fri 8/7/20	
1291		PG&E - RFP Preparation	20 days	Mon 8/3/20	Fri 8/28/20	
1292		PG&E - RFP Release	1 day	Wed 9/9/20	Wed 9/9/20	
1293		PG&E - RFP Proposal Creation Duration	31 days	Wed 9/9/20	Wed 10/21/20	
1294		PG&E - RFP Evaluation	31 days	Fri 10/23/20	Fri 12/4/20	
1295		PG&E - RFP Review with EE PRG	6 days	Tue 12/22/20	Tue 12/29/20	
1296		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 1/6/21	Fri 1/8/21	
1297		PG&E - Contract Negotiation and Development	65 days	Wed 1/20/21	Tue 4/20/21	
1298		PG&E - Contract Review with EE PRG	7 days	Thu 4/22/21	Fri 4/30/21	
1299		PG&E - Final Award and Contract Signed	22 days	Sat 5/1/21	Mon 5/31/21	
1300		PG&E - Submit Advice Letter	1 day	Thu 6/24/21	Thu 6/24/21	
1301		PG&E - Advice Letter Approved	1 day	Wed 7/28/21	Wed 7/28/21	
1302		PG&E - Implementation Plan	43 days	Thu 7/29/21	Sun 9/26/21	
1303		PG&E - Local (Micro and Small Business Equity Program) Solicitation	403 days?	Tue 6/1/21	Thu 12/15/22	
1304		PG&E - RFA Preparation	38 days	Tue 6/1/21	Thu 7/22/21	
1305		PG&E - RFA Release	1 day	Tue 9/7/21	Tue 9/7/21	
1306		PG&E - RFA Abstract Creation Duration	34 days	Wed 9/8/21	Mon 10/25/21	
1307		PG&E - RFA Evaluation	18 days	Tue 10/26/21	Thu 11/18/21	
1308		PG&E - RFP Release	1 day	Wed 12/8/21	Wed 12/8/21	
1309		PG&E - RFP Proposal Creation Duration	46 days	Wed 12/8/21	Wed 2/9/22	
1310		PG&E - RFP Evaluation	21 days	Thu 2/10/22	Thu 3/10/22	
1311		PG&E - RFP Review with EE PRG	6 days	Thu 3/17/22	Thu 3/24/22	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
1312		PG&E - RFP Estimated Bidder Notification	1 day	Wed 3/30/22	Wed 3/30/22	
1313		PG&E - Contract Negotiation and Development	71 days	Thu 4/7/22	Thu 7/14/22	
1314		PG&E - Contract Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22	
1315		PG&E - Final Award and Contract Signed	45 days	Mon 8/8/22	Fri 10/7/22	
1316		PG&E - Submit Advice Letter	1 day	Wed 10/12/22	Wed 10/12/22	
1317		PG&E - Advice Letter Approved	1 day	Fri 11/11/22	Fri 11/11/22	
1318		PG&E - Implementation Plan	31 days	Fri 11/11/22	Fri 12/23/22	
1319		PG&E - Local (C&S Compliance Improvement) Solicitation	436 days	Tue 3/1/22	Tue 10/31/23	
1320		PG&E - RFA Preparation	34 days	Tue 3/1/22	Fri 4/15/22	
1321		PG&E - RFA Release	1 day	Mon 5/16/22	Mon 5/16/22	
1322		PG&E - RFA Abstract Creation Duration	25 days	Tue 5/17/22	Mon 6/20/22	
1323		PG&E - RFA Evaluation	28 days	Tue 6/21/22	Thu 7/28/22	
1324		PG&E - RFA Review with EE PRG	1 day	Tue 8/9/22	Tue 8/9/22	
1325		PG&E - RFA Estimated Bidder Notification	1 day	Wed 8/31/22	Wed 8/31/22	
1326		PG&E - RFP Preparation	24 days	Mon 8/1/22	Thu 9/1/22	
1327		PG&E - RFP Release	1 day	Tue 9/13/22	Tue 9/13/22	
1328		PG&E - RFP Proposal Creation Duration	26 days	Tue 9/13/22	Tue 10/18/22	
1329		PG&E - RFP Evaluation	45 days	Wed 10/19/22	Tue 12/20/22	
1330		PG&E - RFP Review with EE PRG	1 day	Tue 1/24/23	Tue 1/24/23	
1331		PG&E - RFP Estimated Bidder Notification	1 day	Fri 2/10/23	Fri 2/10/23	
1332		PG&E - Contract Negotiation and Development	47 days	Mon 2/13/23	Tue 4/18/23	
1333		PG&E - Contract Review with EE PRG	26 days	Tue 5/23/23	Tue 6/27/23	
1334		PG&E - Final Award and Contract Signed	48 days	Wed 6/28/23	Fri 9/1/23	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
1335		PG&E - Submit Advice Letter		N/A		
1336		PG&E - Advice Letter Approved		N/A		
1337		PG&E - Implementation Plan	1 day	Tue 10/31/23	Tue 10/31/23	
1338		PG&E - Residential Electrification Equity Program Solicitation	595 days	Mon 8/1/22	Fri 11/8/24	
1339		PG&E - RFA Preparation	59 days	Mon 8/1/22	Thu 10/20/22	
1340		PG&E - RFA Release	1 day	Tue 11/29/22	Tue 11/29/22	
1341		PG&E - RFA Abstract Creation Duration	46 days	Tue 11/29/22	Tue 1/31/23	
1342		PG&E - RFA Evaluation	17 days	Sun 2/5/23	Sun 2/26/23	
1343		PG&E - RFA Review with EE PRG	6 days	Mon 2/27/23	Mon 3/6/23	
1344		PG&E - RFA Estimated Bidder Notification	3 days	Mon 3/6/23	Wed 3/8/23	
1345		PG&E - RFP Preparation	46 days	Mon 1/9/23	Mon 3/13/23	
1346		PG&E - RFP Release	1 day	Tue 4/11/23	Tue 4/11/23	
1347		PG&E - RFP Proposal Creation Duration	26 days	Tue 4/11/23	Tue 5/16/23	
1348		PG&E - RFP Evaluation	18 days	Fri 5/19/23	Tue 6/13/23	
1349		PG&E - RFP Review with EE PRG	1 day	Tue 6/27/23	Tue 6/27/23	
1350		PG&E - RFP Estimated Bidder Notification	1 day	Tue 7/11/23	Tue 7/11/23	
1351		PG&E - Contract Negotiation and Development	233 days	Tue 8/1/23	Thu 6/20/24	
1352		PG&E - Contract Review with EE PRG	8 days	Fri 6/21/24	Tue 7/2/24	
1353		PG&E - Final Award and Contract Signed	21 days	Fri 7/5/24	Fri 8/2/24	
1354		PG&E - Submit Advice Letter	1 day	Fri 8/9/24	Fri 8/9/24	
1355		PG&E - Advice Letter Approved	1 day	Mon 9/9/24	Mon 9/9/24	
1356		PG&E - Implementation Plan	1 day	Fri 11/8/24	Fri 11/8/24	
1357		PG&E - Statewide C&S Advocacy Solicitation	641 days	Tue 2/1/22	Tue 7/16/24	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
1358		PG&E - RFA Preparation	54 days	Tue 2/1/22	Fri 4/15/22	
1359		PG&E - RFA Release	1 day	Mon 5/30/22	Mon 5/30/22	
1360		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/31/22	Fri 7/1/22	
1361		PG&E - RFA Evaluation	14 days	Fri 7/1/22	Wed 7/20/22	
1362		PG&E - RFA Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22	
1363		PG&E - RFA Estimated Bidder Notification	1 day	Mon 8/1/22	Mon 8/1/22	
1364		PG&E - RFP Preparation	36 days	Fri 4/1/22	Fri 5/20/22	
1365		PG&E - RFP Release	1 day	Tue 6/7/22	Tue 6/7/22	
1366		PG&E - RFP Proposal Creation Duration	31 days	Tue 6/7/22	Tue 7/19/22	
1367		PG&E - RFP Evaluation	50 days	Wed 7/20/22	Tue 9/27/22	
1368		PG&E - RFP Review with EE PRG	1 day	Wed 10/5/22	Wed 10/5/22	
1369		PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/24/22	Mon 10/24/22	
1370		PG&E - Contract Negotiation and Development	73 days	Mon 11/14/22	Wed 2/22/23	
1371		PG&E - Contract Review with EE PRG - Wave 1	1 day	Tue 4/25/23	Tue 4/25/23	
1372		PG&E - Final Award and Contract Signed	18 days	Mon 7/17/23	Wed 8/9/23	
1373		PG&E - Submit Advice Letter (wave 1)	1 day	Thu 9/21/23	Thu 9/21/23	
1374		PG&E - Advice Letter Approved	1 day	Wed 10/25/23	Wed 10/25/23	
1375		PG&E - Implementation Plan	1 day	Thu 12/7/23	Thu 12/7/23	
1376		PG&E - Contract Review with EE PRG - Wave 2	1 day	Wed 12/20/23	Wed 12/20/23	
1377		PG&E - Final Award and Contract Signed	1 day	Fri 3/29/24	Fri 3/29/24	
1378		PG&E - Submit Advice Letter	1 day	Wed 4/17/24	Wed 4/17/24	
1379		PG&E - Advice Letter Approved	1 day	Fri 5/17/24	Fri 5/17/24	
1380		PG&E - Implementation Plan	1 day	Tue 7/16/24	Tue 7/16/24	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




ID		Task Name	Duration	Start	Finish	2018 H1
1381		PG&E - Zonal Electrification Solicitation	495 days	Thu 12/1/22	Wed 10/23/24	
1382		PG&E - RFP Preparation	88 days	Thu 12/1/22	Mon 4/3/23	
1383		PG&E - RFP Release	1 day	Tue 4/18/23	Tue 4/18/23	
1384		PG&E - RFP Proposal Creation Duration	53 days	Tue 4/18/23	Thu 6/29/23	
1385		PG&E - RFP Evaluation (including interviews)	40 days	Mon 7/10/23	Fri 9/1/23	
1386		PG&E - RFP Review with EE PRG	1 day	Tue 9/26/23	Tue 9/26/23	
1387		PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/2/23	Mon 10/2/23	
1388		PG&E - Contract Negotiation and Development	135 days	Mon 10/9/23	Fri 4/12/24	
1389		PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24	
1390		PG&E - Final Award and Contract Signed	43 days	Wed 5/1/24	Fri 6/28/24	
1391		PG&E - Submit Advice Letter	1 day	Wed 7/3/24	Wed 7/3/24	
1392		PG&E - Advice Letter Approved	1 day	Wed 8/28/24	Wed 8/28/24	
1393		PG&E - Implementation Plan	1 day	Wed 10/23/24	Wed 10/23/24	
1394		PG&E - Residential Whole Home Load Management RFP	453 days	Tue 8/15/23	Thu 5/8/25	
1395		PG&E - RFP Preparation	1 day	Tue 8/15/23	Tue 8/15/23	
1396		PG&E - RFP Release	1 day	Tue 8/15/23	Tue 8/15/23	
1397		PG&E - RFP Proposal Creation Duration	51 days	Tue 8/15/23	Tue 10/24/23	
1398		PG&E - RFP Evaluation	36 days	Thu 10/26/23	Thu 12/14/23	
1399		PG&E - RFP Review with EE PRG	1 day	Fri 2/16/24	Fri 2/16/24	
1400		PG&E - RFP Estimated Bidder Notification	1 day	Tue 2/27/24	Tue 2/27/24	
1401		PG&E - Contract Negotiation and Development	155 days	Wed 3/13/24	Tue 10/15/24	
1402		PG&E - Contract Review with EE PRG	8 days	Tue 11/5/24	Thu 11/14/24	
1403		PG&E - Final Award and Contract Signed	53 days	Thu 11/14/24	Mon 1/27/25	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
1404		PG&E - Submit Advice Letter	1 day	Fri 2/7/25	Fri 2/7/25	
1405		PG&E - Advice Letter Approved	1 day	Mon 3/10/25	Mon 3/10/25	
1406		PG&E - Implementation Plan	1 day	Thu 5/8/25	Thu 5/8/25	
1407		PG&E - 2024 Summer Reliability Platform Administrator RFP	337 days?	Tue 4/18/23	Wed 7/31/24	
1408		PG&E - RFP Preparation	30 days	Mon 5/1/23	Fri 6/9/23	
1409		PG&E - RFP Release	1 day	Fri 9/1/23	Fri 9/1/23	
1410		PG&E - RFP Proposal Creation Duration	31 days	Fri 9/1/23	Fri 10/13/23	
1411		PG&E - RFP Evaluation	22 days	Tue 10/17/23	Wed 11/15/23	
1412		PG&E - RFP Review with EE PRG	1 day	Tue 11/28/23	Tue 11/28/23	
1413		PG&E - RFP Estimated Bidder Notification	1 day	Tue 12/5/23	Tue 12/5/23	
1414		PG&E - Contract Negotiation and Development	68 days	Mon 1/8/24	Wed 4/10/24	
1415		PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24	
1416		PG&E - Final Award and Contract Signed	22 days	Wed 5/1/24	Thu 5/30/24	
1417		PG&E - Submit Advice Letter	1 day	Fri 5/31/24	Fri 5/31/24	
1418		PG&E - Advice Letter Approved	1 day	Mon 7/1/24	Mon 7/1/24	
1419		PG&E - Implementation Plan	1 day	Wed 7/31/24	Wed 7/31/24	
1420		PG&E - C&S Code Readiness RFP	393 days?	Wed 2/1/23	Fri 8/2/24	
1421		PG&E - RFP Preparation	113 days	Wed 2/1/23	Fri 7/7/23	
1422		PG&E - RFP Release	1 day	Wed 7/12/23	Wed 7/12/23	
1423		PG&E - RFP Proposal Creation Duration	30 days	Thu 7/13/23	Wed 8/23/23	
1424		PG&E - RFP Evaluation	36 days	Mon 8/28/23	Mon 10/16/23	
1425		PG&E - RFP Review with EE PRG	1 day	Tue 10/24/23	Tue 10/24/23	
1426		PG&E - RFP Estimated Bidder Notification	1 day	Mon 11/6/23	Mon 11/6/23	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
1427		PG&E - Contract Negotiation and Development	65 days	Wed 11/15/23	Tue 2/13/24	
1428		PG&E - Contract Review with EE PRG	1 day	Tue 2/27/24	Tue 2/27/24	
1429		PG&E - Final Award and Contract Signed	1 day	Fri 4/12/24	Fri 4/12/24	
1430		PG&E - Submit Advice Letter	1 day	Tue 5/7/24	Tue 5/7/24	
1431		PG&E - Advice Letter Approved	1 day	Thu 6/6/24	Thu 6/6/24	
1432		PG&E - Implementation Plan	1 day	Fri 8/2/24	Fri 8/2/24	
1433		PG&E - Residential Electrification - Single Point of Contact	414 days	Tue 8/1/23	Fri 2/28/25	
1434		PG&E - RFP Preparation	133 days	Tue 8/1/23	Thu 2/1/24	
1435		PG&E - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24	
1436		PG&E - RFP Proposal Creation Duration	33 days	Wed 2/28/24	Fri 4/12/24	
1437		PG&E - RFP Evaluation	66 days	Mon 4/15/24	Mon 7/15/24	
1438		PG&E - RFP Review with EE PRG	6 days	Fri 7/19/24	Fri 7/26/24	
1439		PG&E - RFP Estimated Bidder Notification	1 day	Wed 8/7/24	Wed 8/7/24	
1440		PG&E - Contract Negotiation and Development	62 days			
1441		PG&E - Contract Review with EE PRG	6 days			
1442		PG&E - Final Award and Contract Signed	25 days			
1443		PG&E - Submit Advice Letter	1 day			
1444		PG&E - Advice Letter Approved	1 day			
1445		PG&E - Implementation Plan	1 day			
1446		PG&E - Commercial SEM FP	430 days	Thu 8/3/23	Wed 3/26/25	
1447		PG&E - RFP Preparation	16 days	Thu 8/3/23	Thu 8/24/23	
1448		PG&E - RFP Release	1 day	Fri 11/3/23	Fri 11/3/23	
1449		PG&E - RFP Proposal Creation Duration	55 days	Fri 11/3/23	Thu 1/18/24	

Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	2018 H1
1450		PG&E - RFP Evaluation	58 days	Tue 1/23/24	Thu 4/11/24	
1451		PG&E - RFP Review with EE PRG	1 day	Wed 4/17/24	Wed 4/17/24	
1452		PG&E - RFP Estimated Bidder Notification	4 days	Tue 4/23/24	Fri 4/26/24	
1453		PG&E - Contract Negotiation and Development	90 days	Thu 5/2/24	Wed 9/4/24	
1454		PG&E - Contract Review with EE PRG	8 days	Mon 9/16/24	Wed 9/25/24	
1455		PG&E - Final Award and Contract Signed	58 days	Thu 9/26/24	Mon 12/16/24	
1456		PG&E - Submit Advice Letter	1 day	Thu 12/19/24	Thu 12/19/24	
1457		PG&E - Advice Letter Approved	0 days	Thu 1/30/25	Thu 1/30/25	
1458		PG&E - Implementation Plan	1 day	Wed 3/26/25	Wed 3/26/25	
1459		PG&E - SW WE&T Career & Workforce Readiness	479 days	Tue 10/8/24	Fri 8/7/26	
1460		PG&E - RFP Preparation	199 days	Tue 10/8/24	Fri 7/11/25	
1461		PG&E - RFP Release	1 day	Thu 7/17/25	Thu 7/17/25	
1462		PG&E - RFP Proposal Creation Duration	41 days	Thu 7/17/25	Thu 9/11/25	
1463		PG&E - RFP Evaluation	39 days	Mon 9/15/25	Thu 11/6/25	
1464		PG&E - RFP Review with EE PRG	8 days	Thu 11/6/25	Mon 11/17/25	
1465		PG&E - RFP Estimated Bidder Notification	11 days	Tue 11/18/25	Tue 12/2/25	
1466		PG&E - Contract Negotiation and Development	52 days	Fri 12/12/25	Mon 2/23/26	
1467		PG&E - Contract Review with EE PRG	7 days	Tue 3/3/26	Wed 3/11/26	
1468		PG&E - Final Award and Contract Signed	39 days	Wed 3/11/26	Mon 5/4/26	
1469		PG&E - Submit Advice Letter	1 day	Mon 5/11/26	Mon 5/11/26	
1470		PG&E - Advice Letter Approved	1 day	Wed 6/10/26	Wed 6/10/26	
1471		PG&E - Implementation Plan	43 days	Wed 6/10/26	Fri 8/7/26	
1472		PG&E - Statewide HVAC	423 days	Fri 5/2/25	Tue 12/15/26	

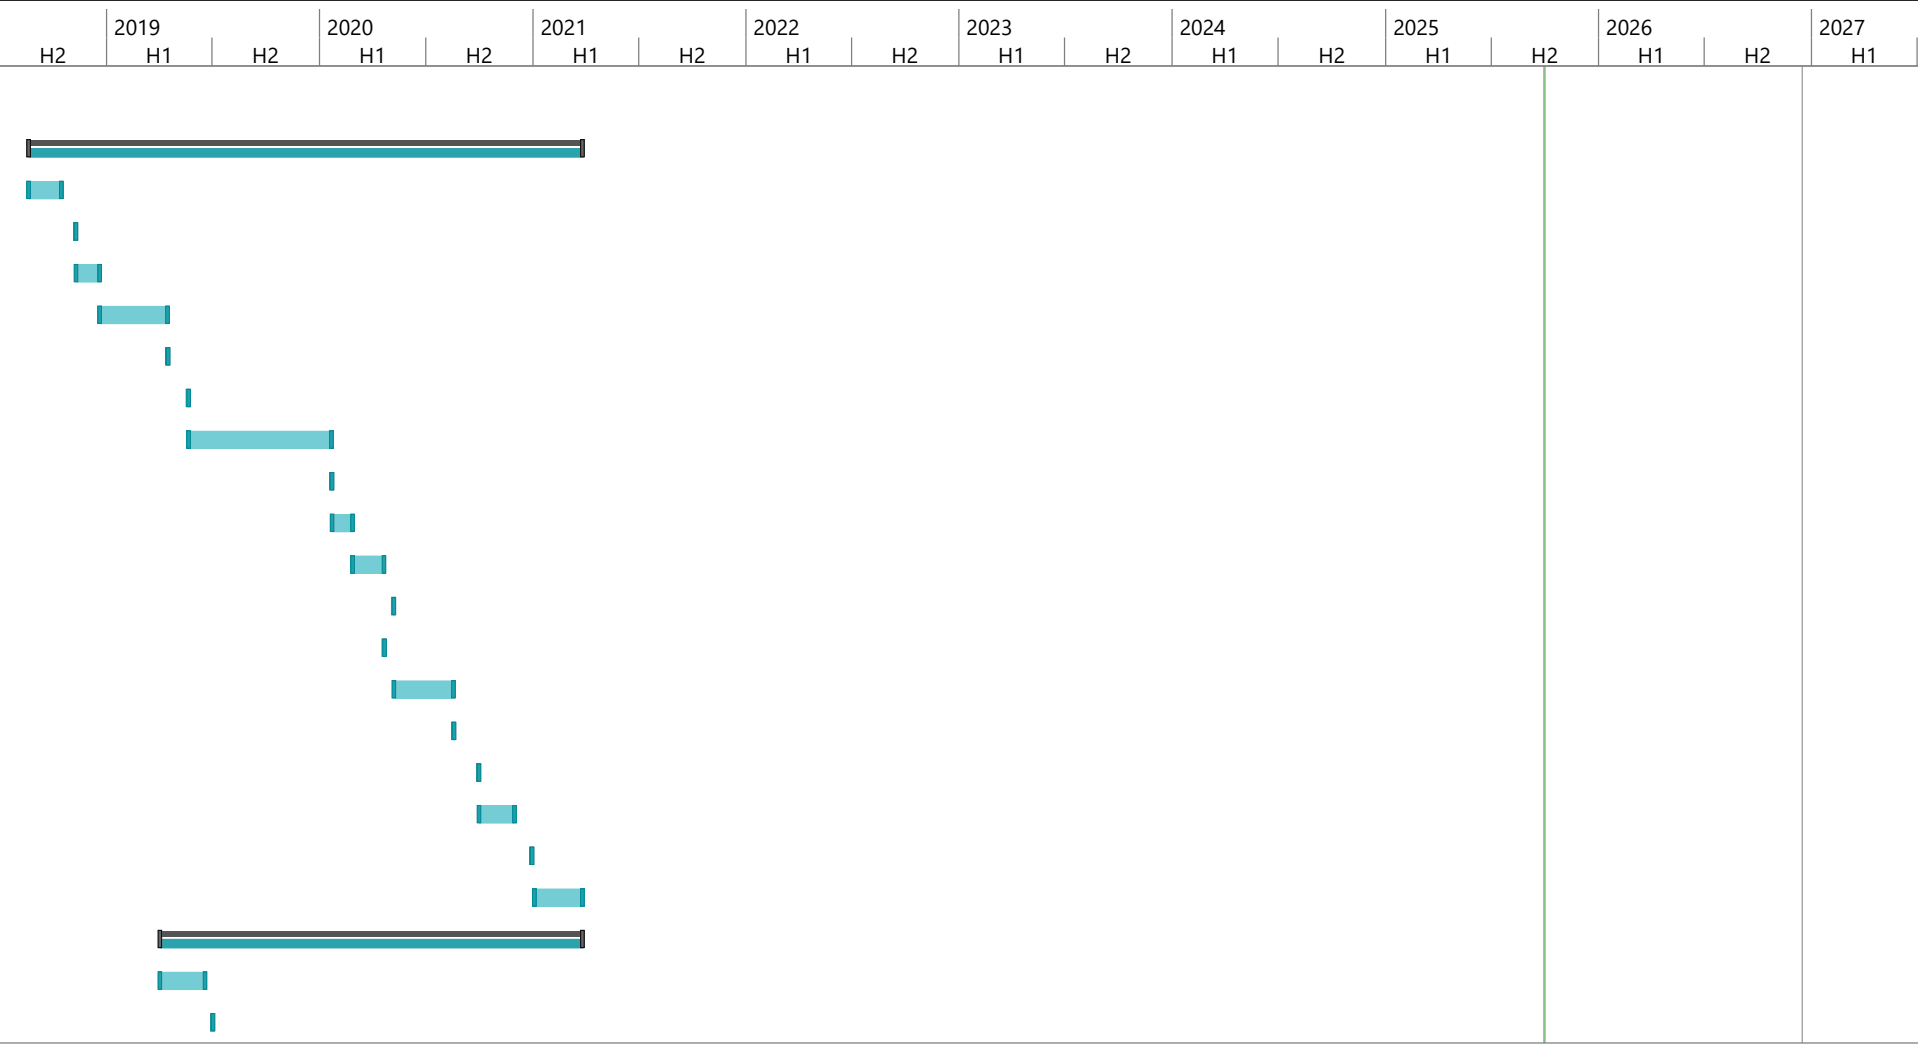
Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	2018 H1
1473		PG&E - RFP Preparation	122 days	Fri 5/2/25	Mon 10/20/25	
1474		PG&E - RFP Release	1 day	Wed 10/22/25	Wed 10/22/25	
1475		PG&E - RFP Proposal Creation Duration	41 days	Wed 10/22/25	Wed 12/17/25	
1476		PG&E - RFP Evaluation	32 days	Thu 12/18/25	Fri 1/30/26	
1477		PG&E - RFP Review with EE PRG	4 days	Tue 2/24/26	Fri 2/27/26	
1478		PG&E - RFP Estimated Bidder Notification	1 day	Mon 3/2/26	Mon 3/2/26	
1479		PG&E - Contract Negotiation and Development	79 days	Mon 3/2/26	Thu 6/18/26	
1480		PG&E - Contract Review with EE PRG	1 day	Tue 6/23/26	Tue 6/23/26	
1481		PG&E - Final Award and Contract Signed	1 day	Mon 8/31/26	Mon 8/31/26	
1482		PG&E - Submit Advice Letter	1 day	Tue 9/15/26	Tue 9/15/26	
1483		PG&E - Advice Letter Approved	1 day	Thu 10/15/26	Thu 10/15/26	
1484		PG&E - Implementation Plan	1 day	Tue 12/15/26	Tue 12/15/26	

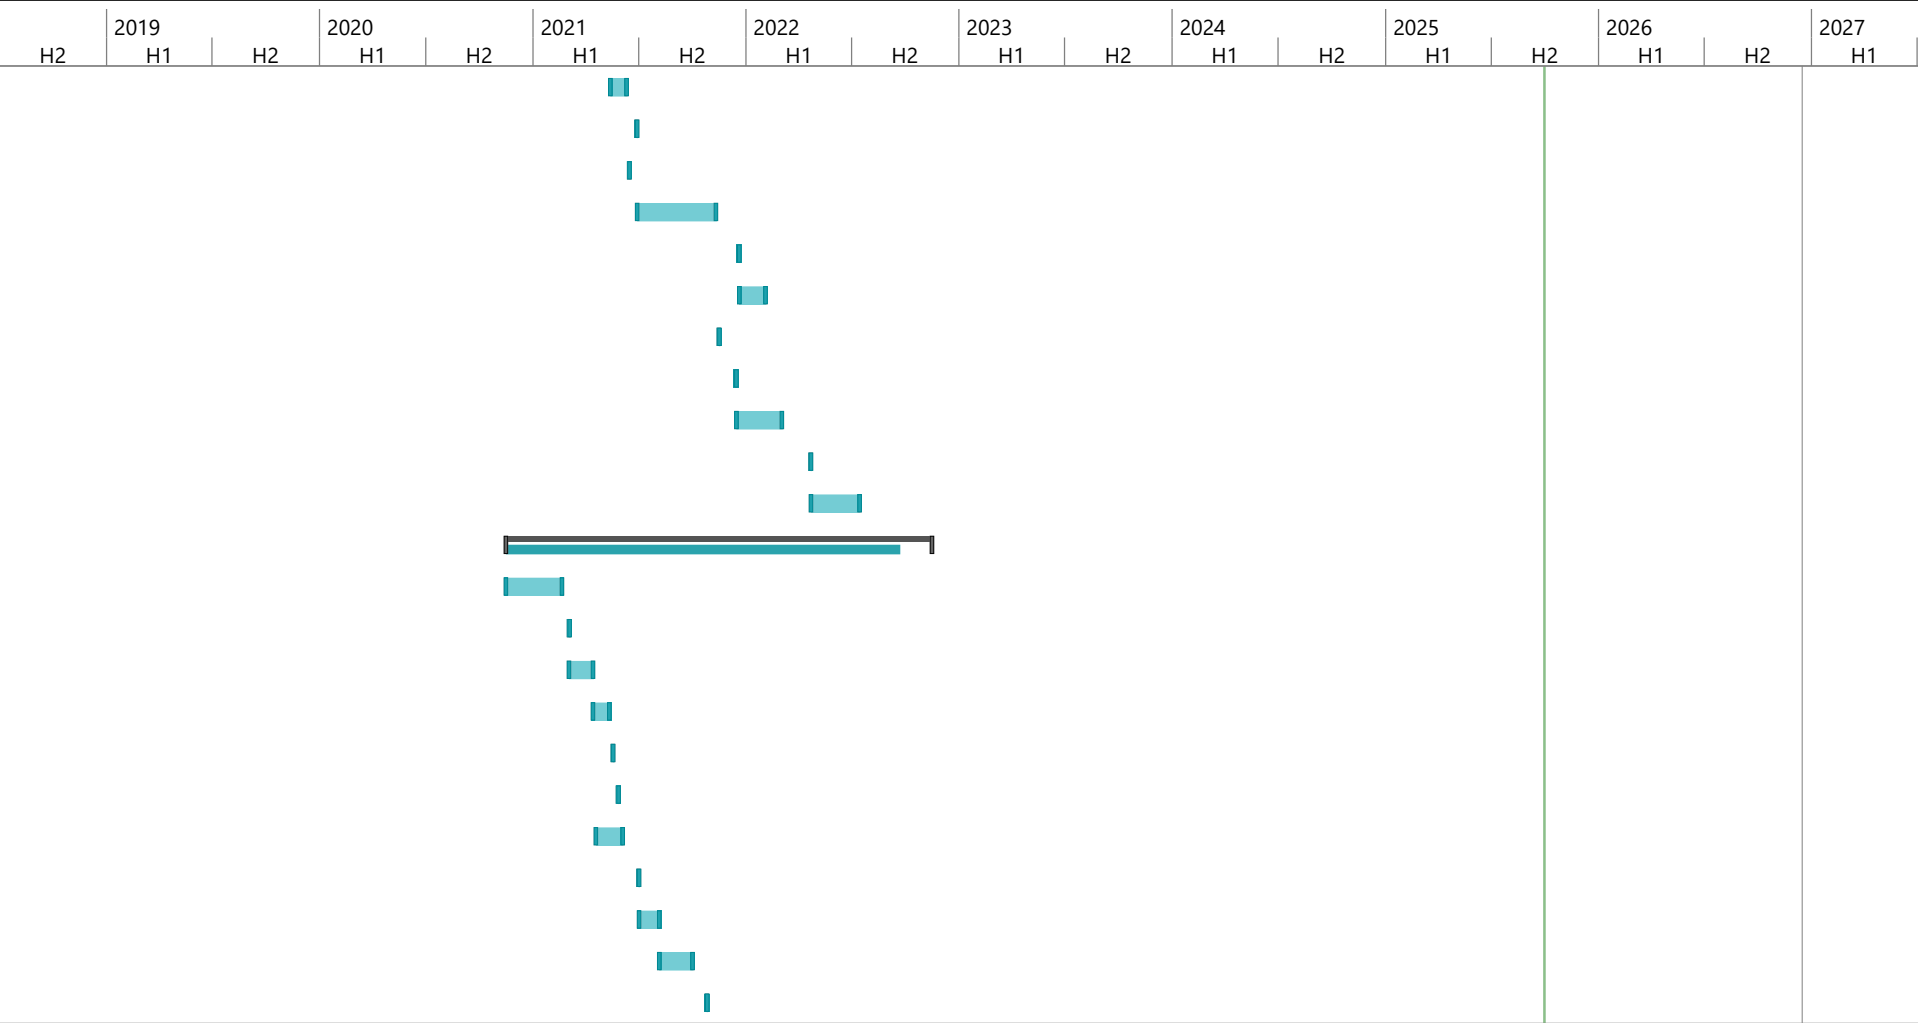
Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



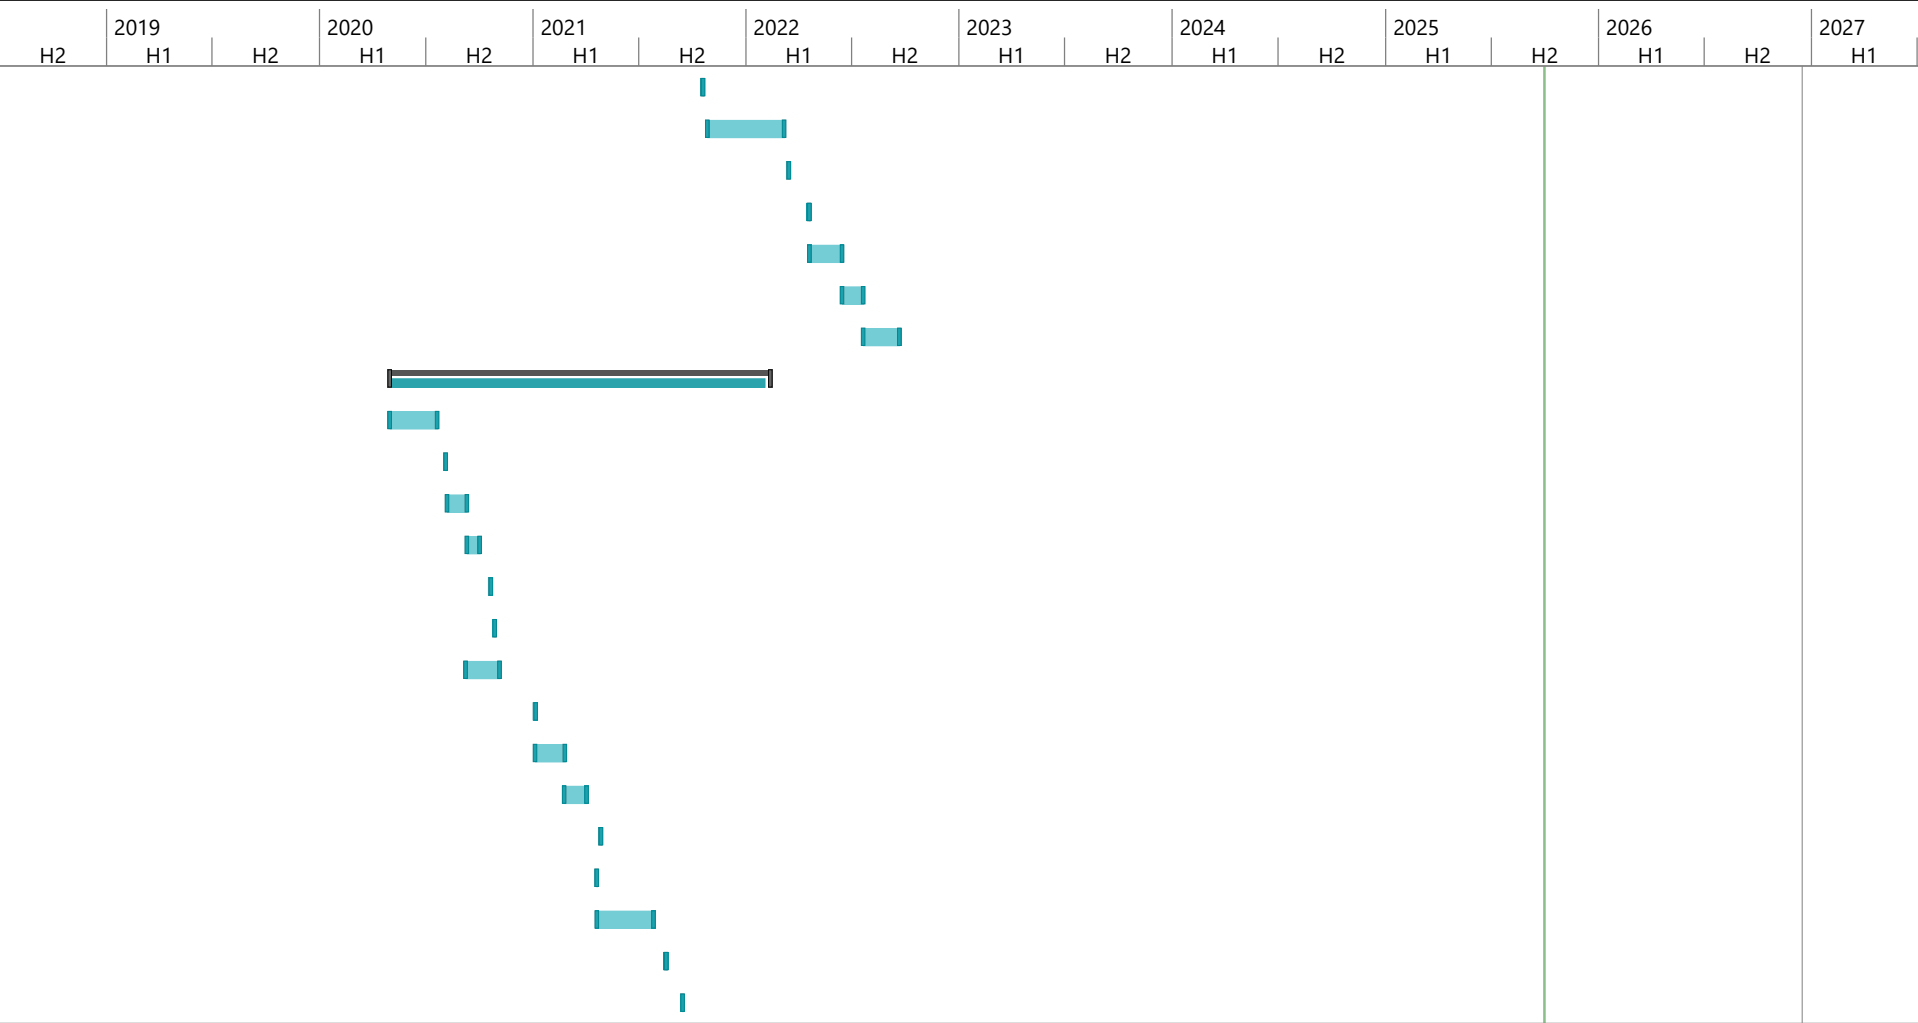
Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

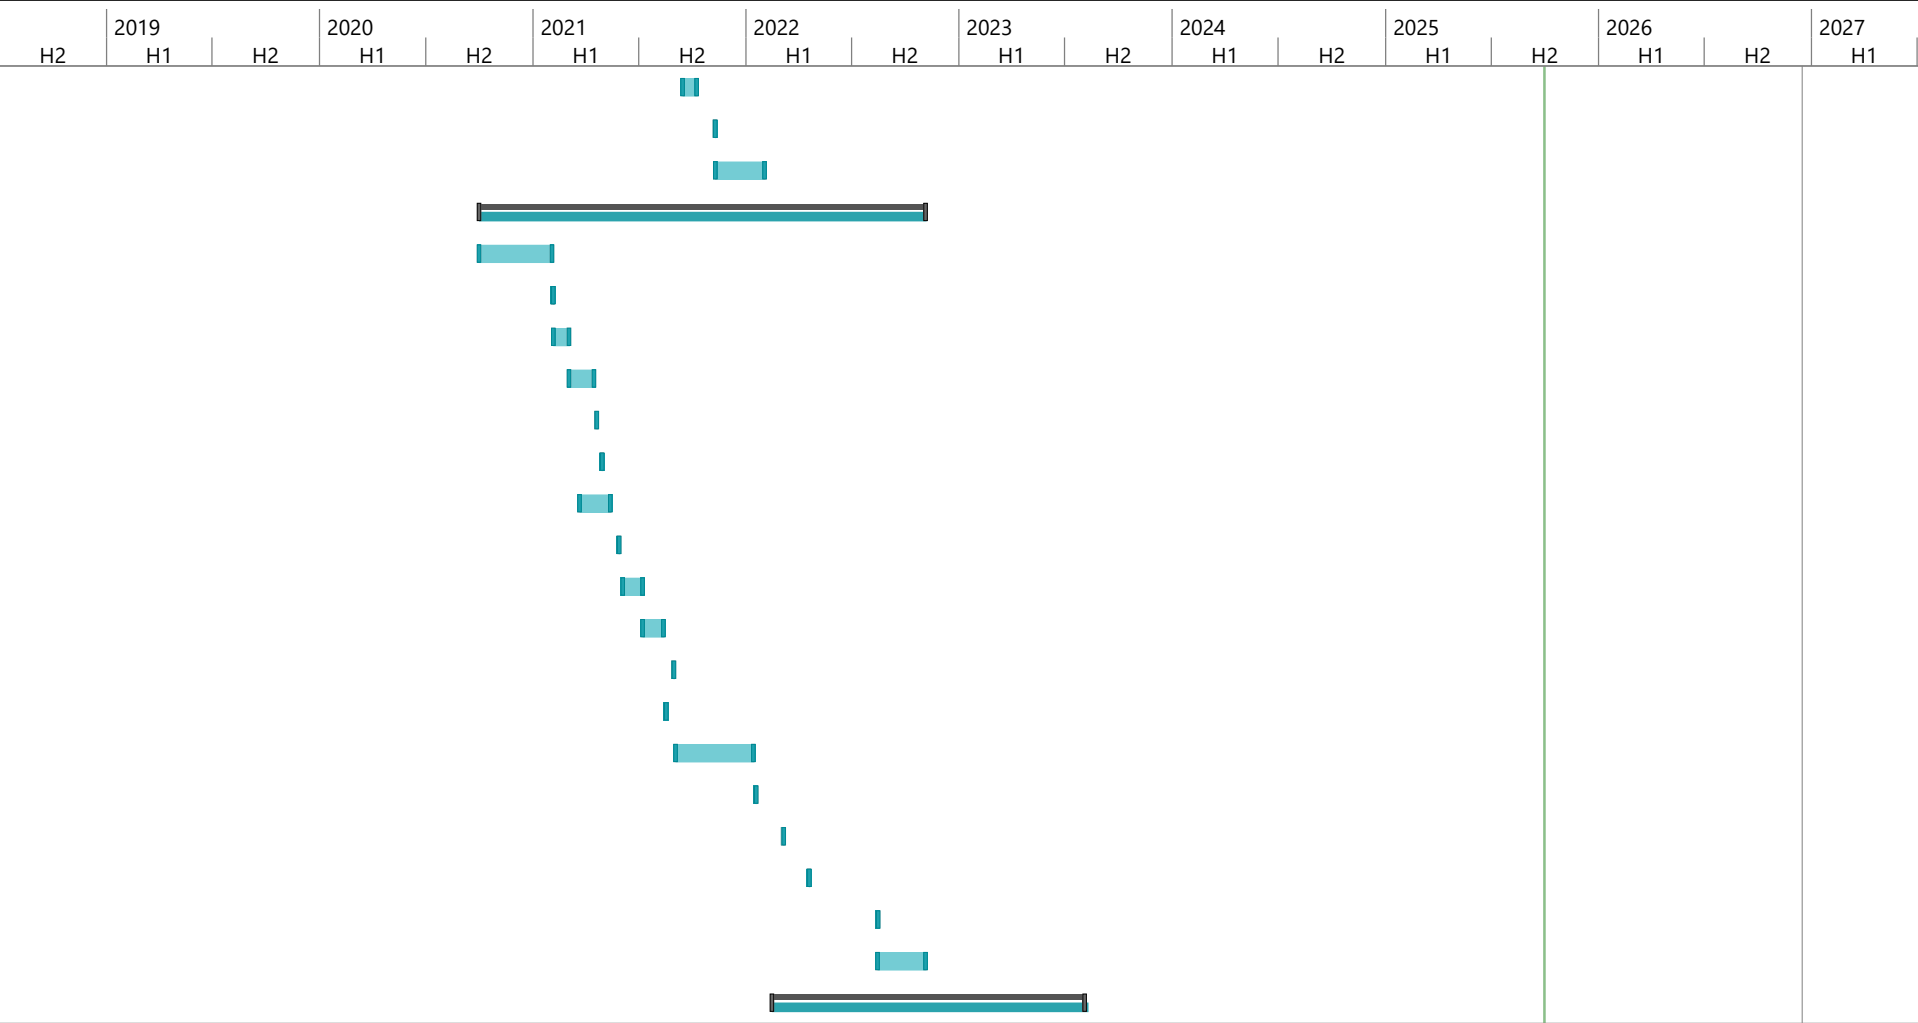


Project: IOU Master Task Timeli
Date: Tue 9/30/25

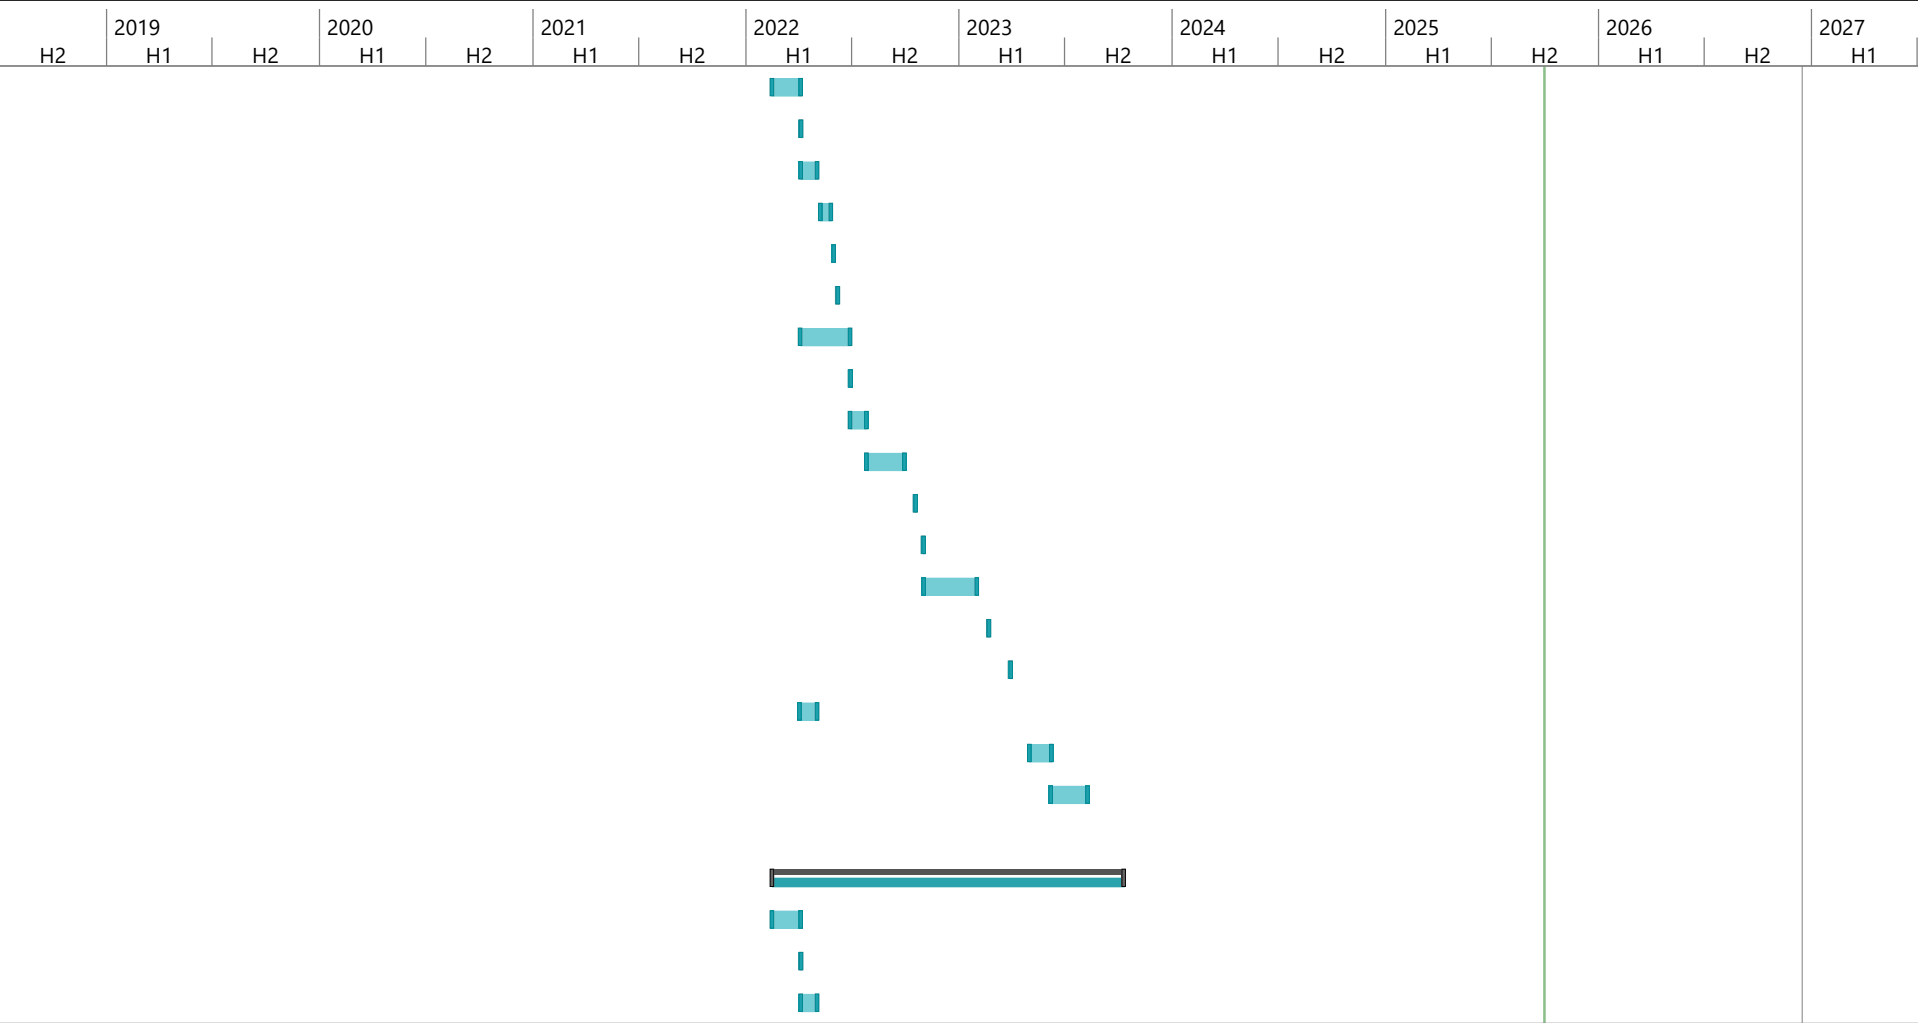
Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



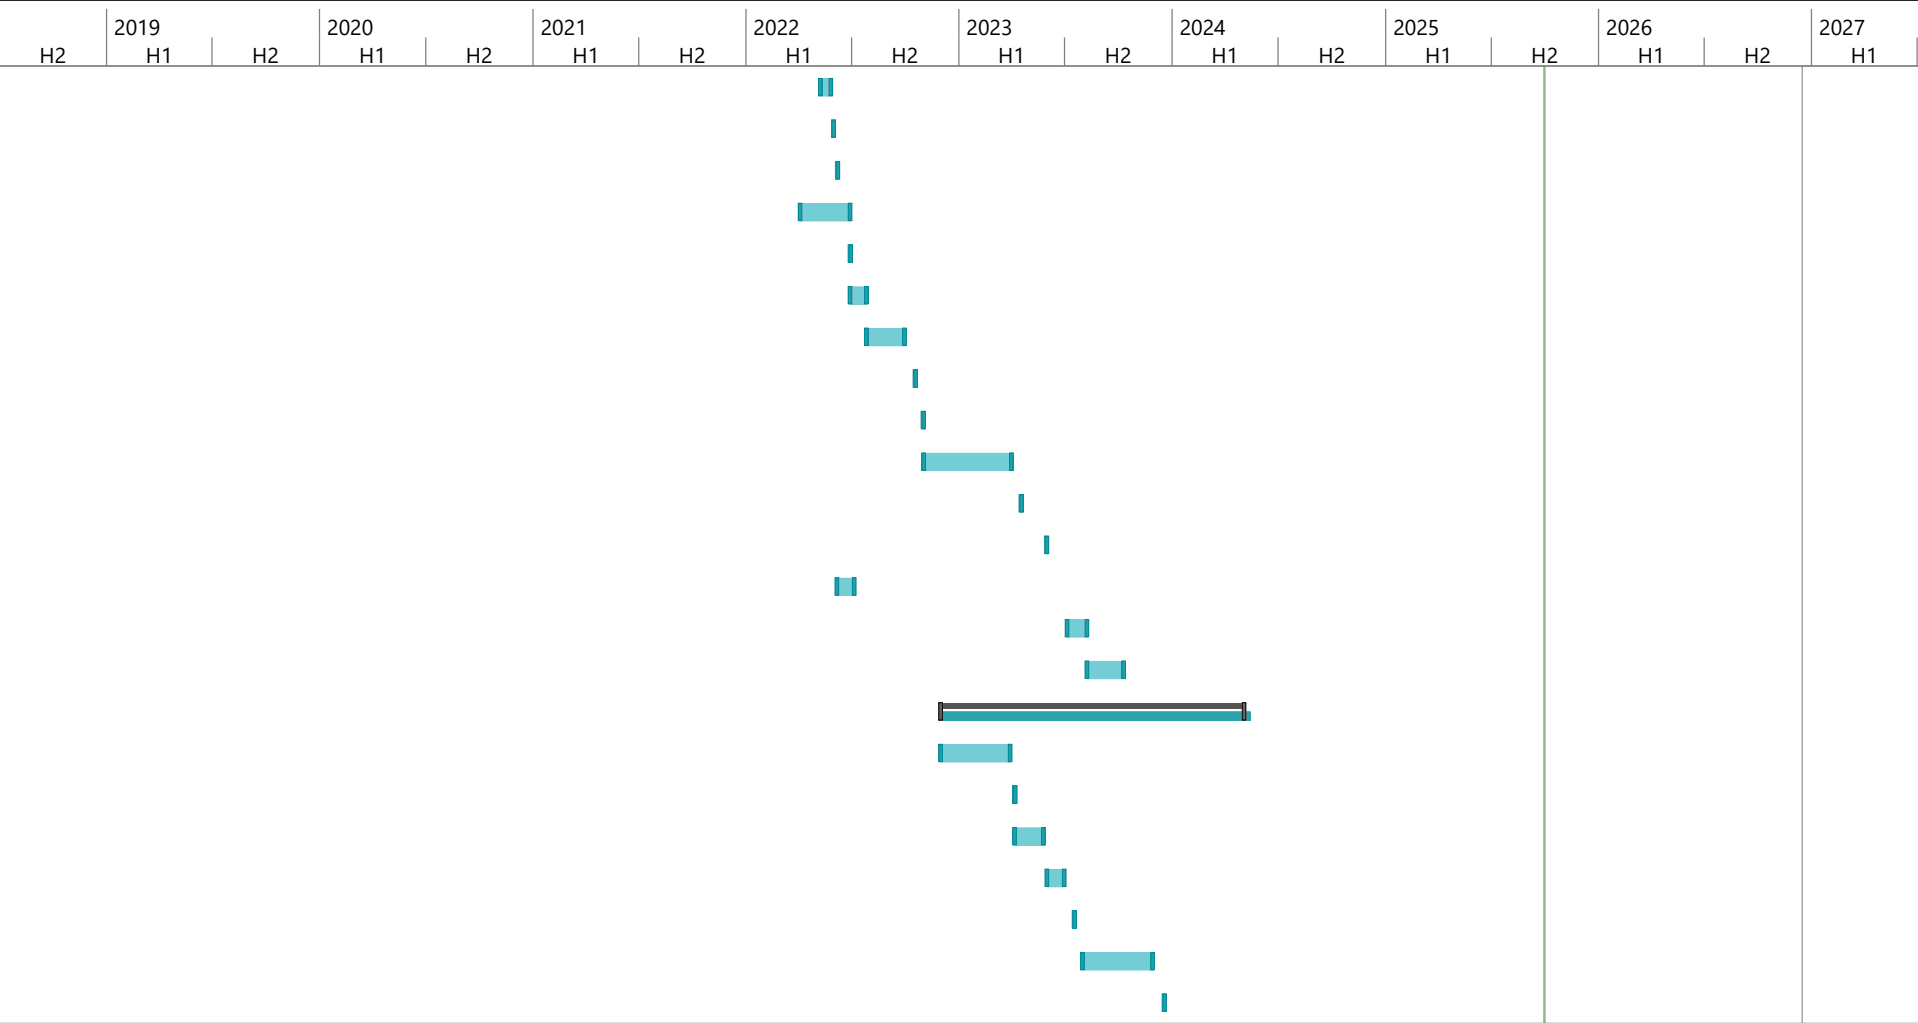
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



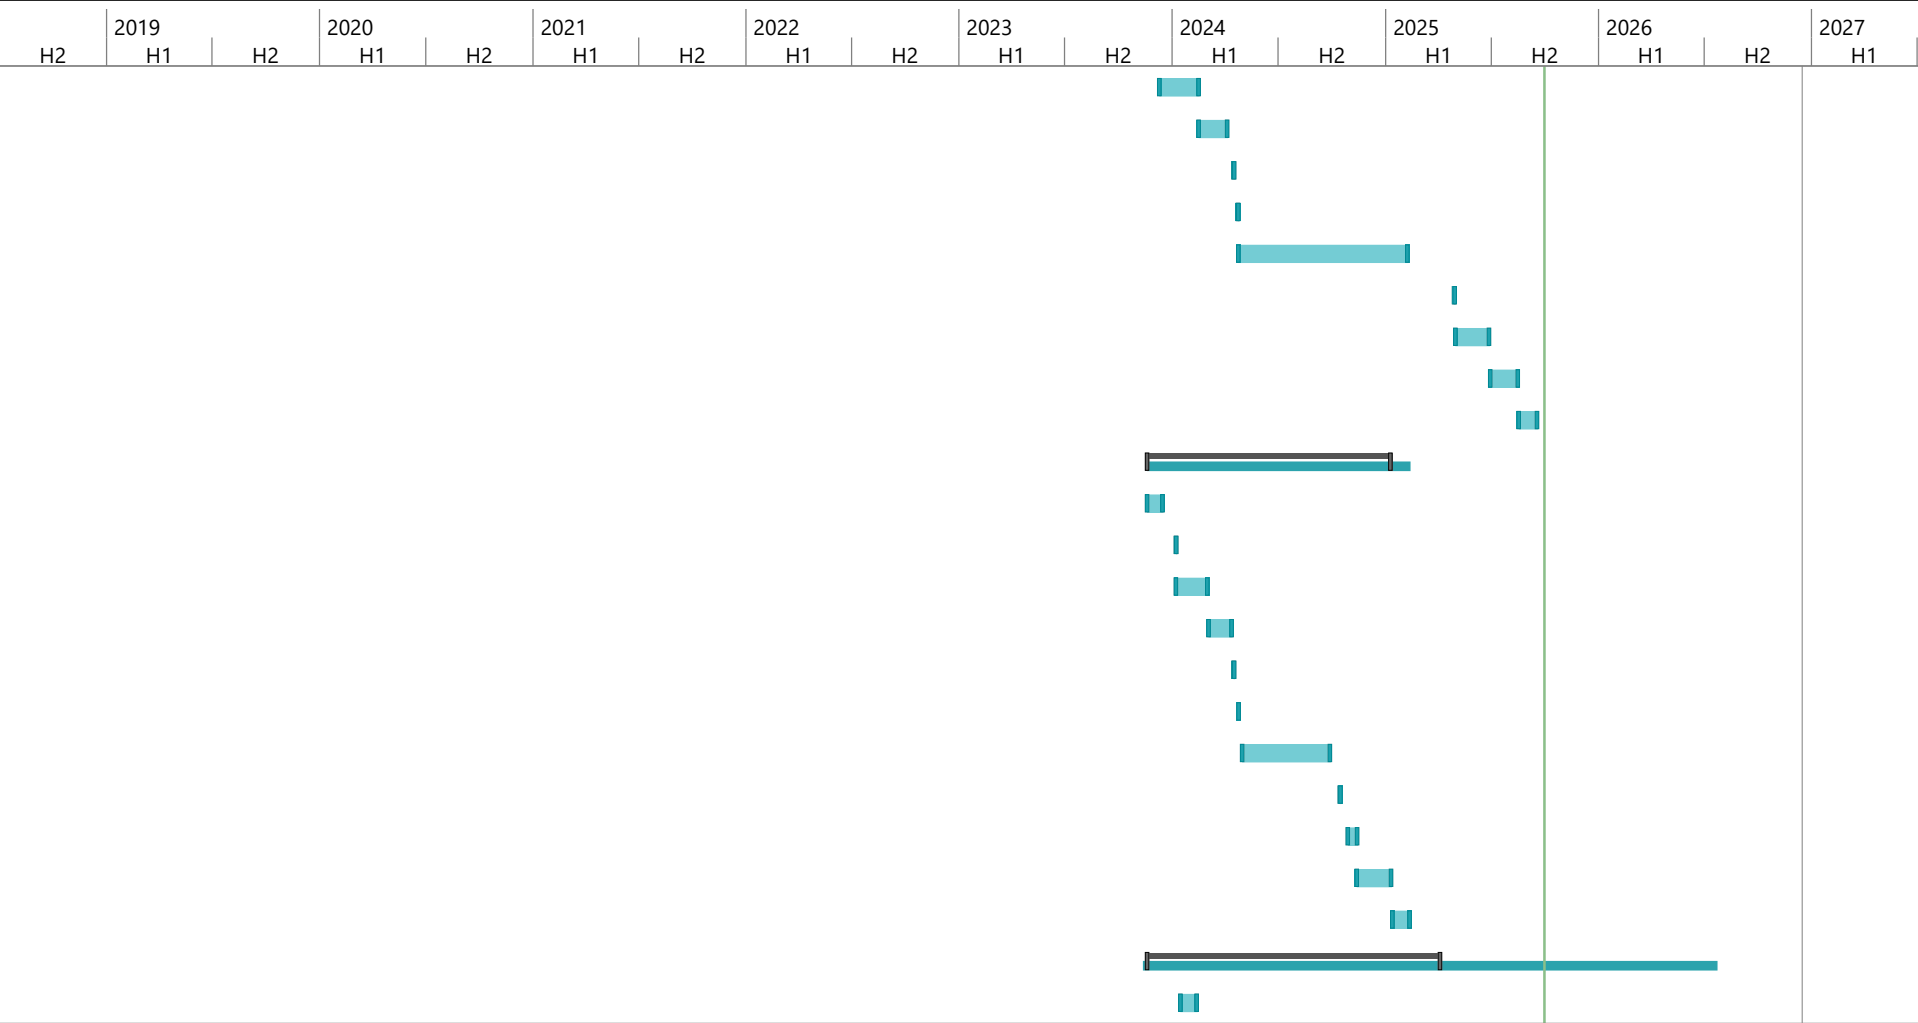
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



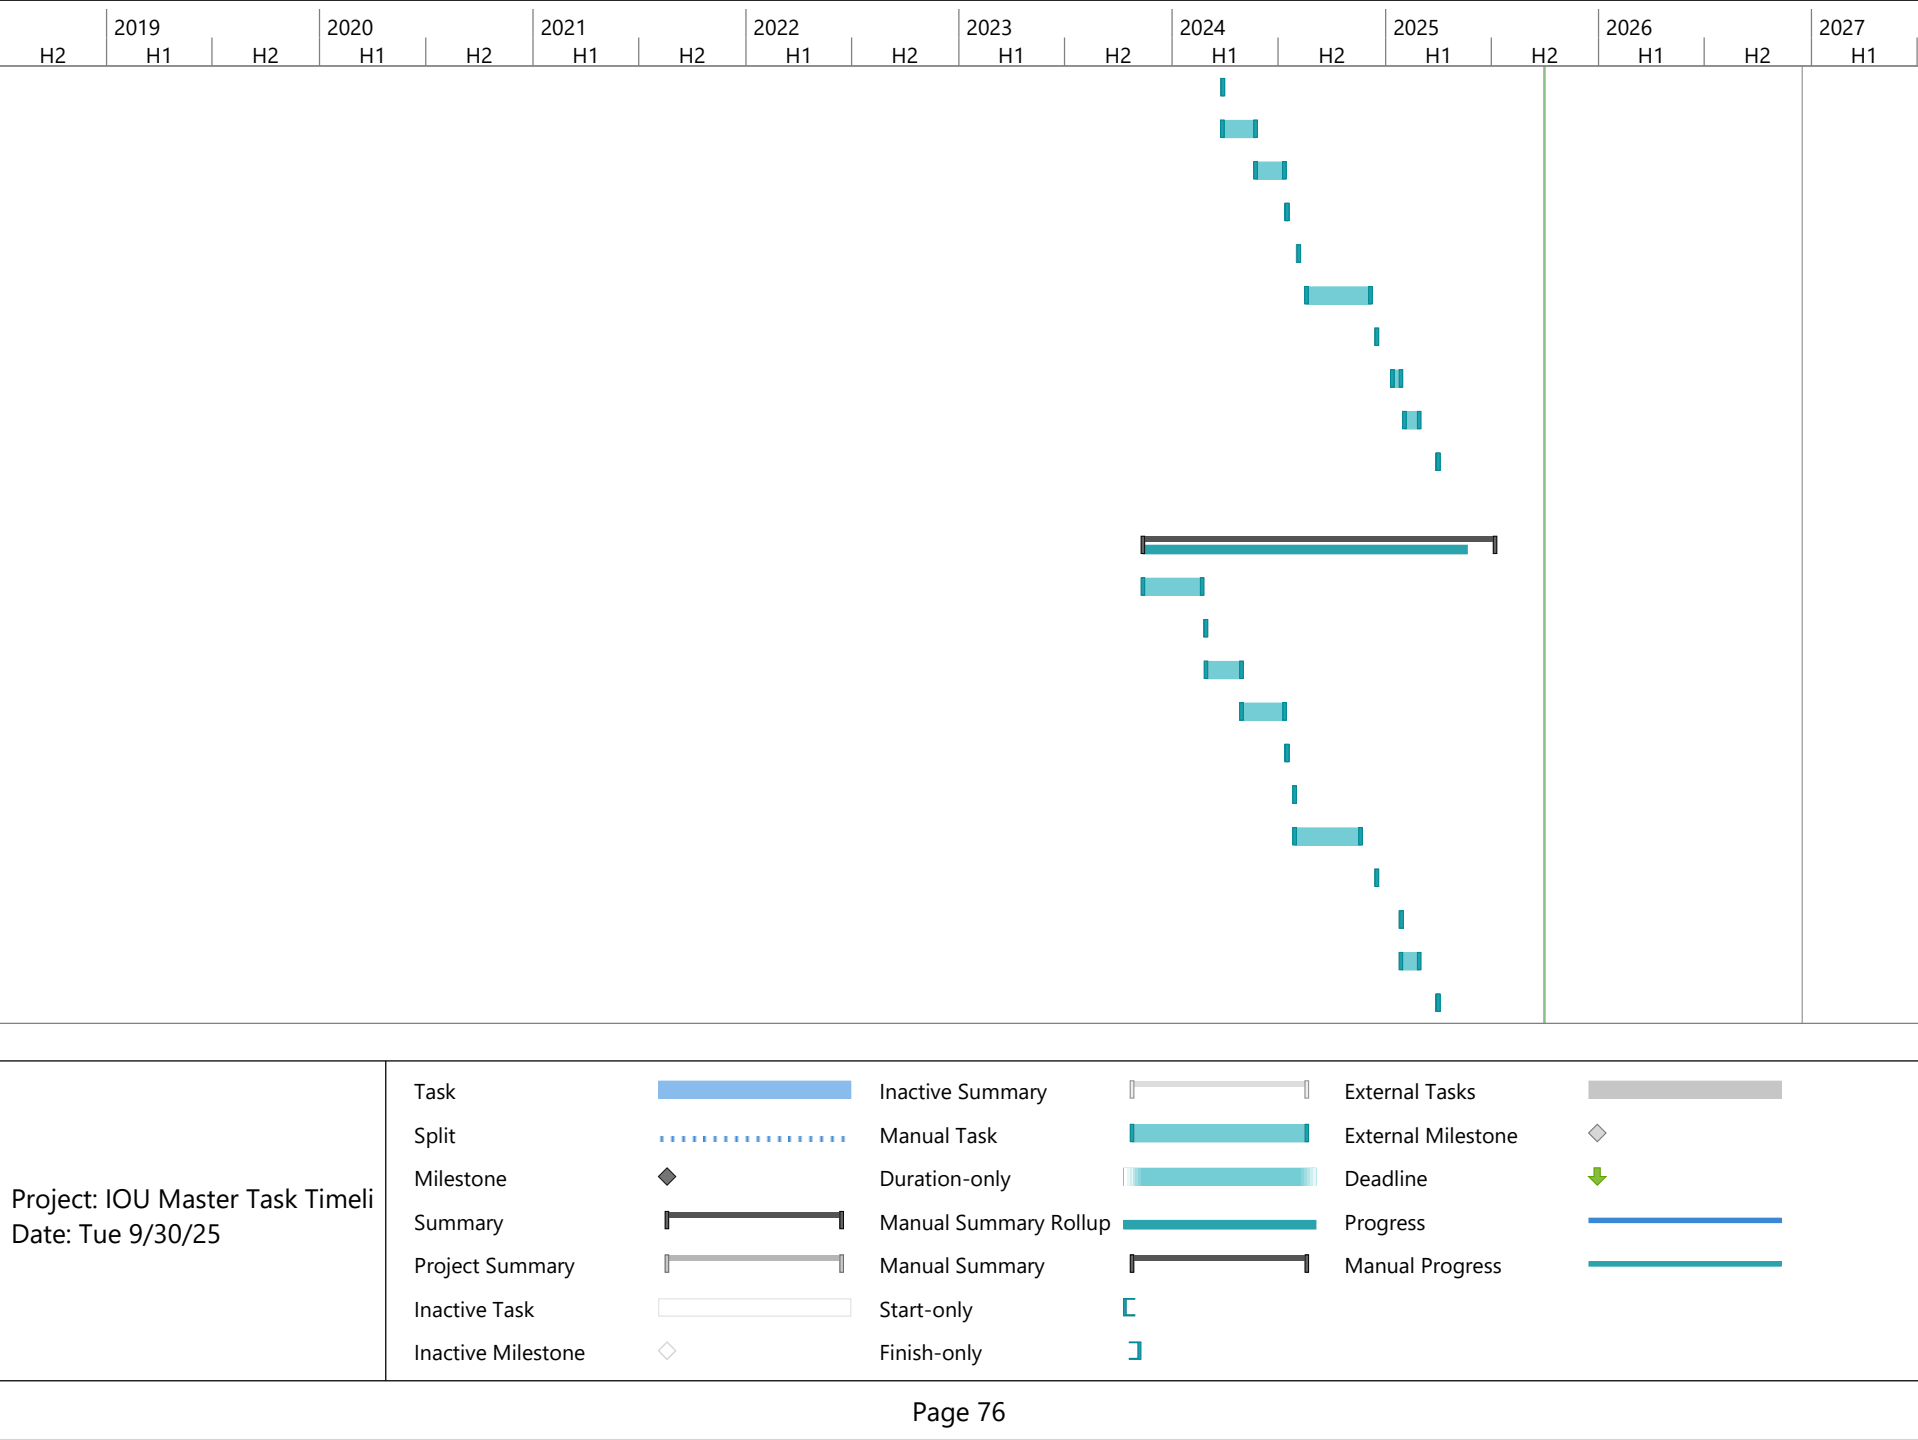
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

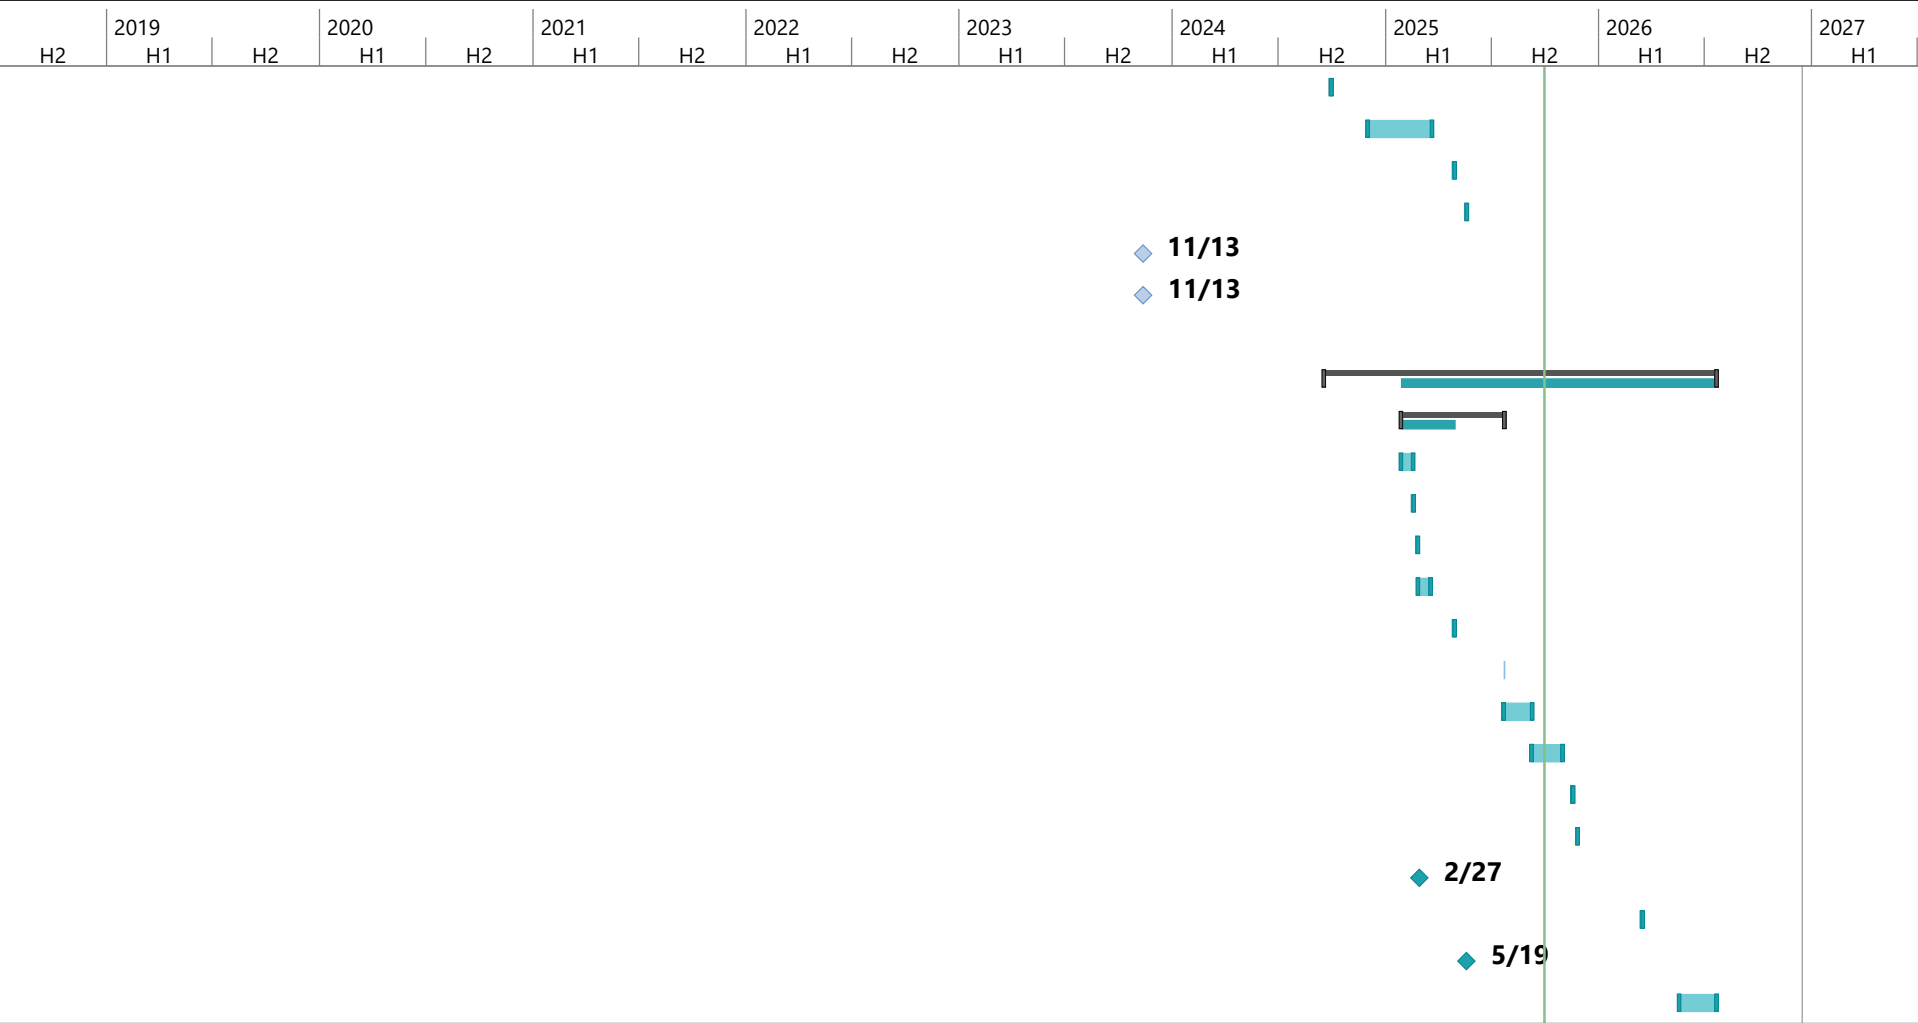


Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

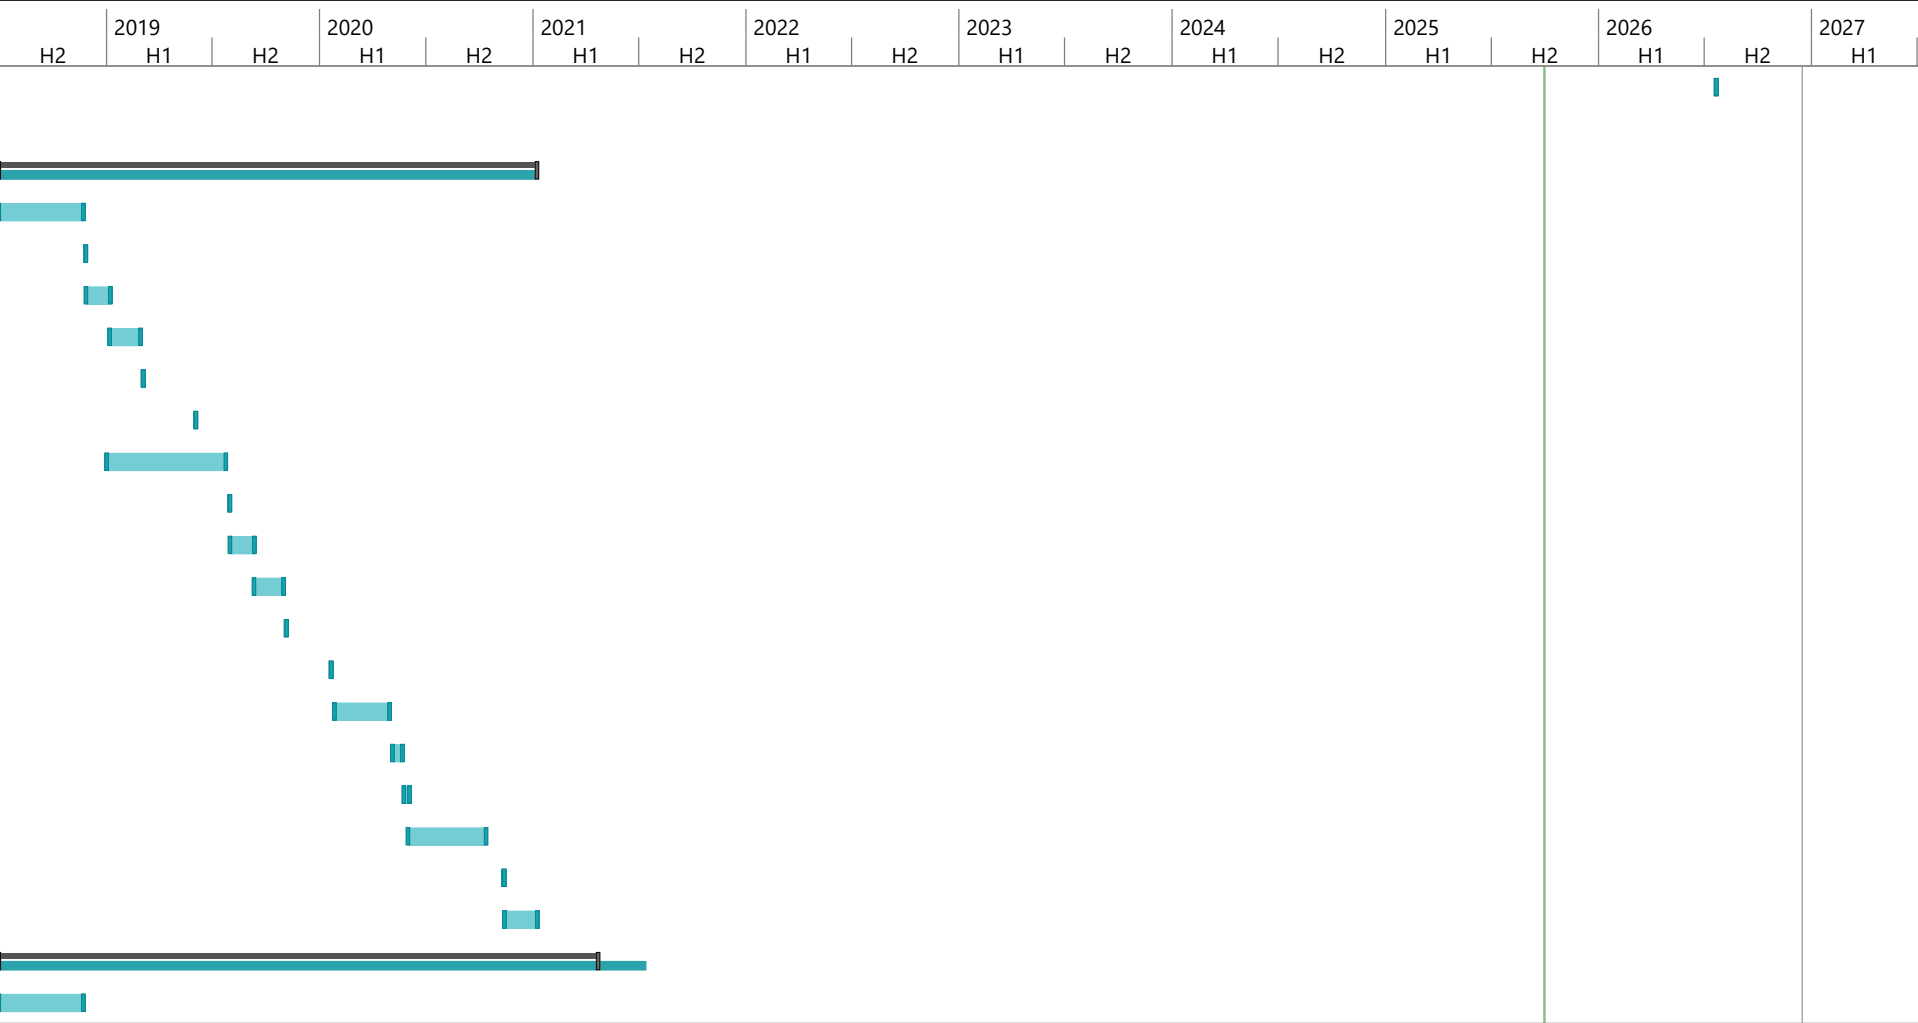


Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

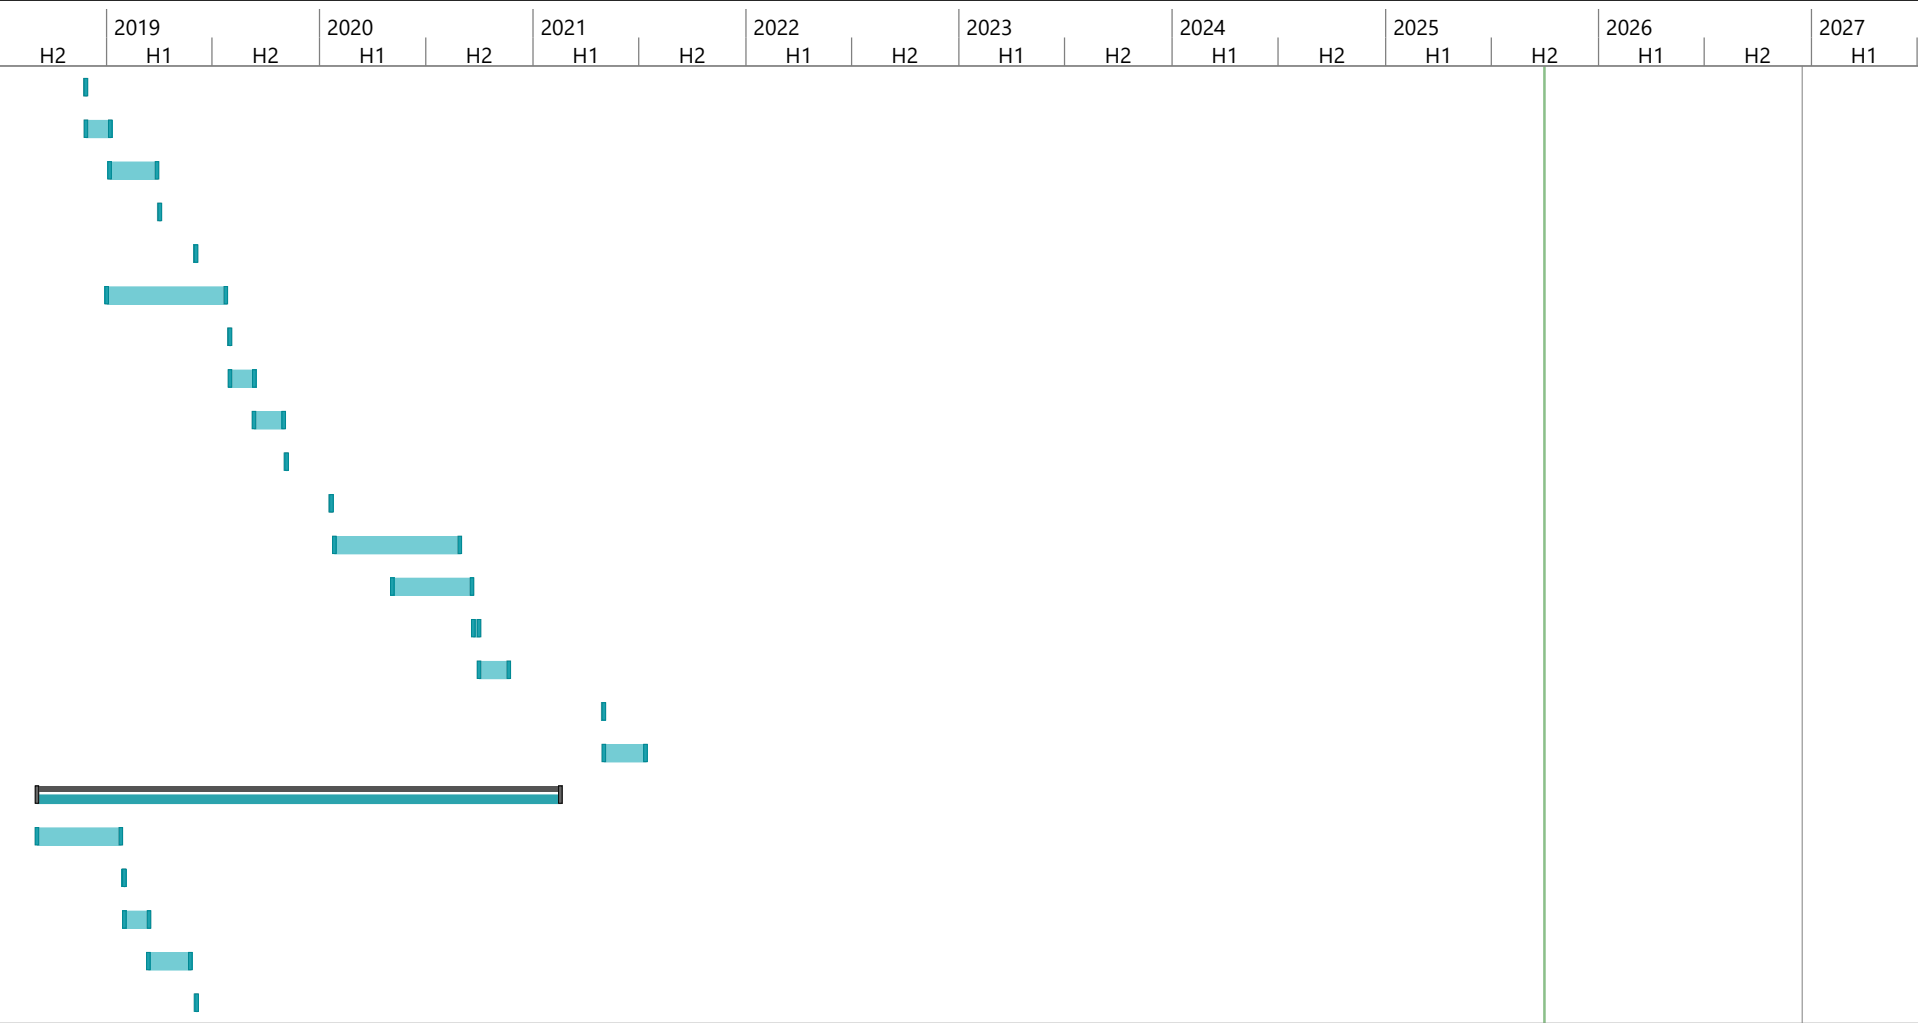




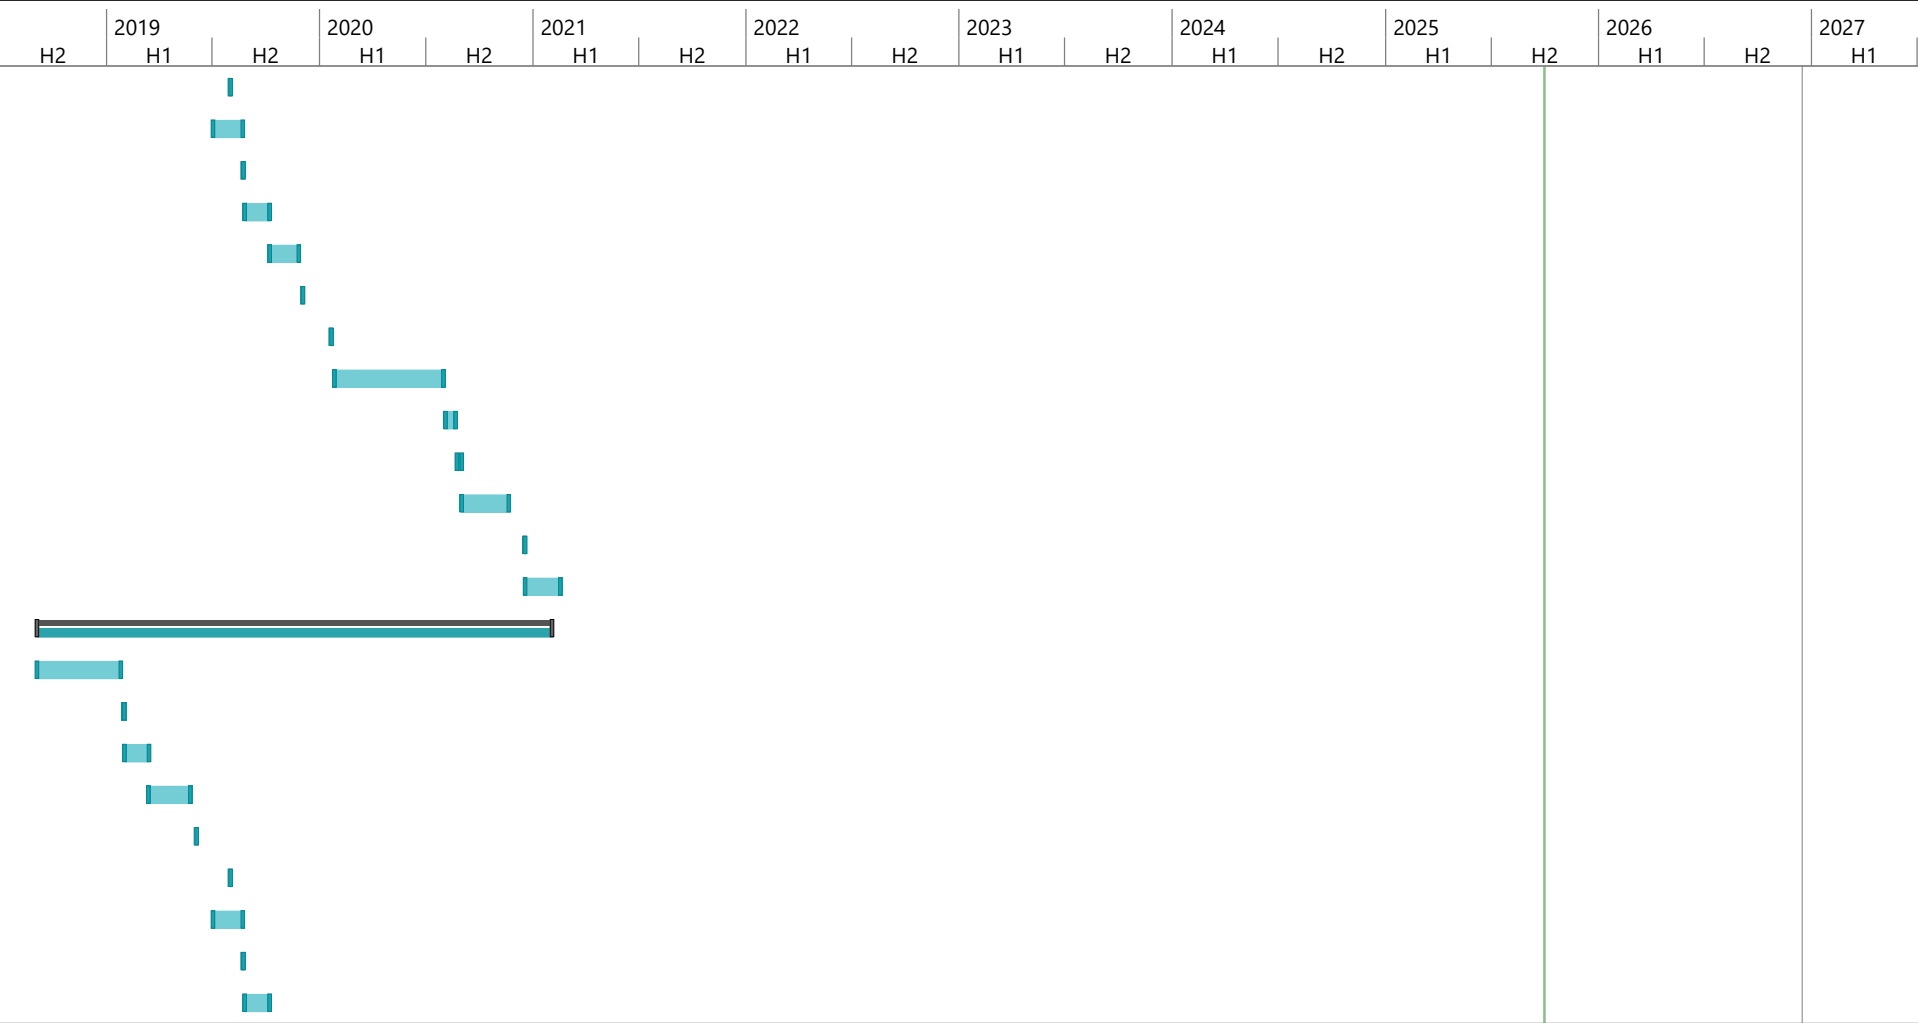
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



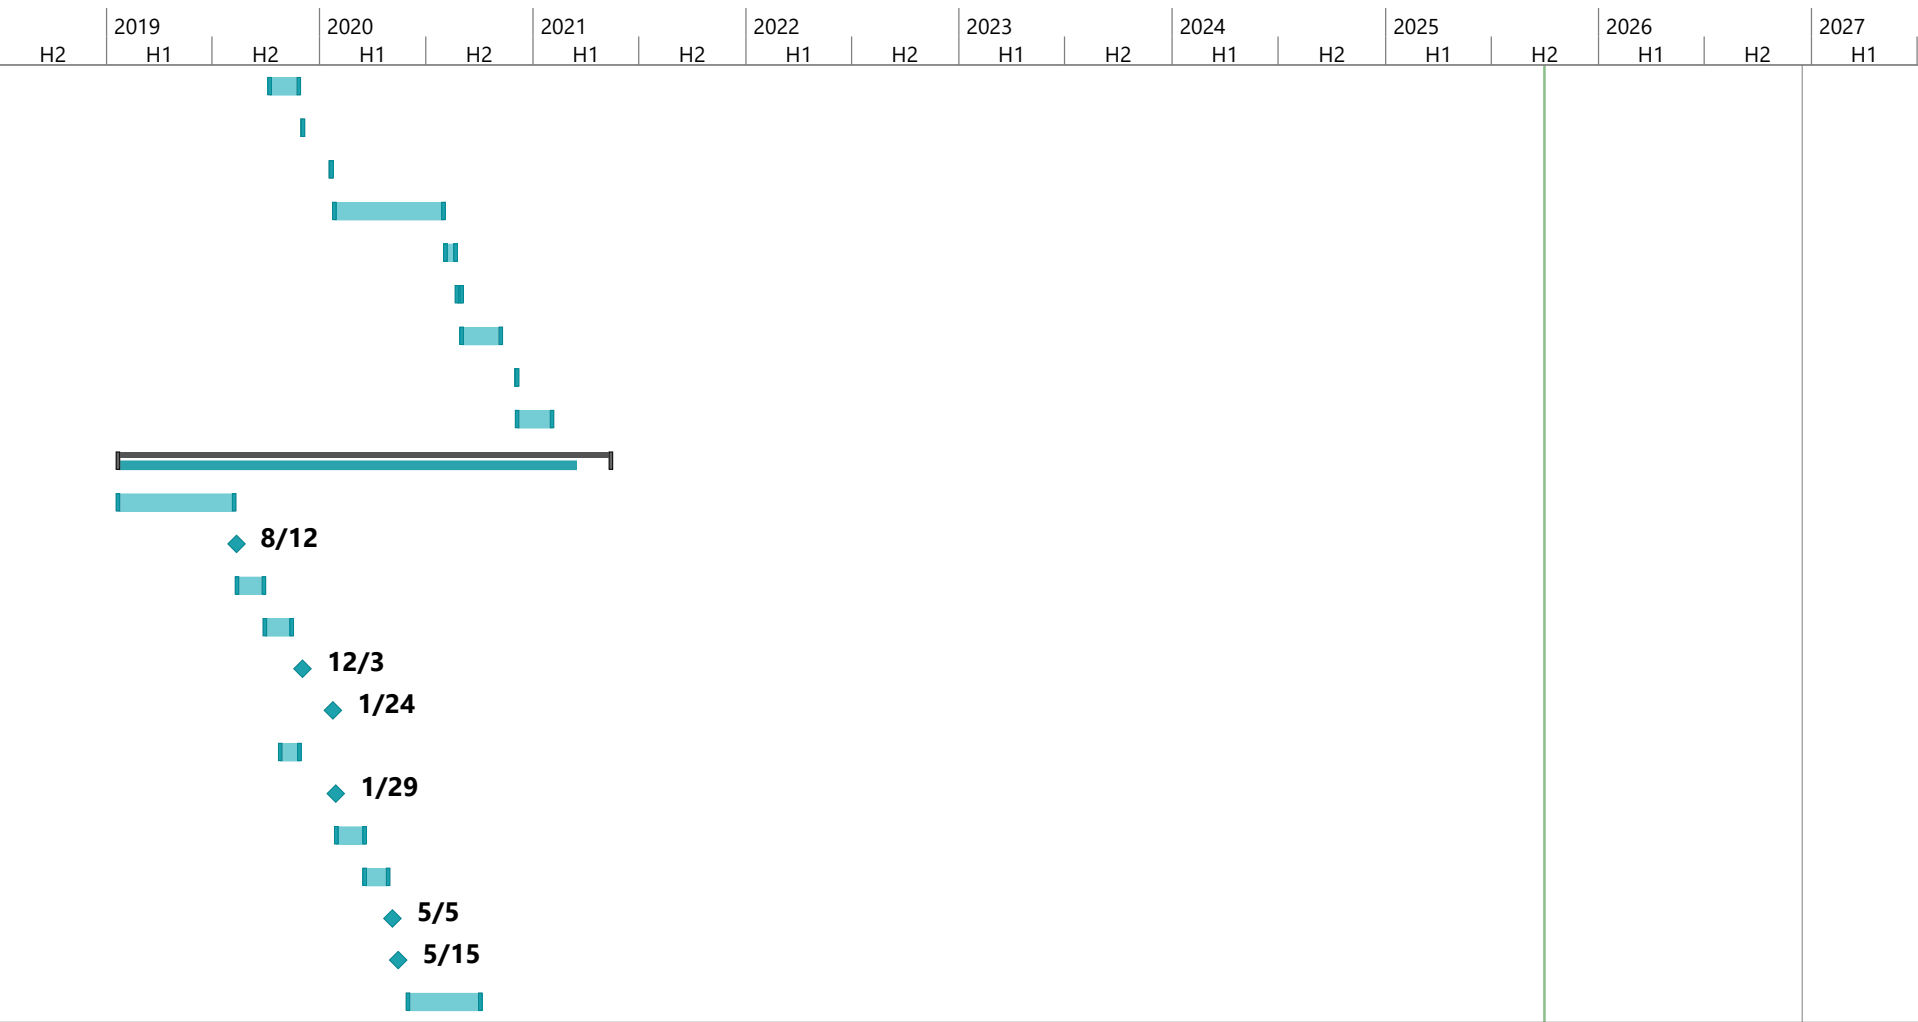
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



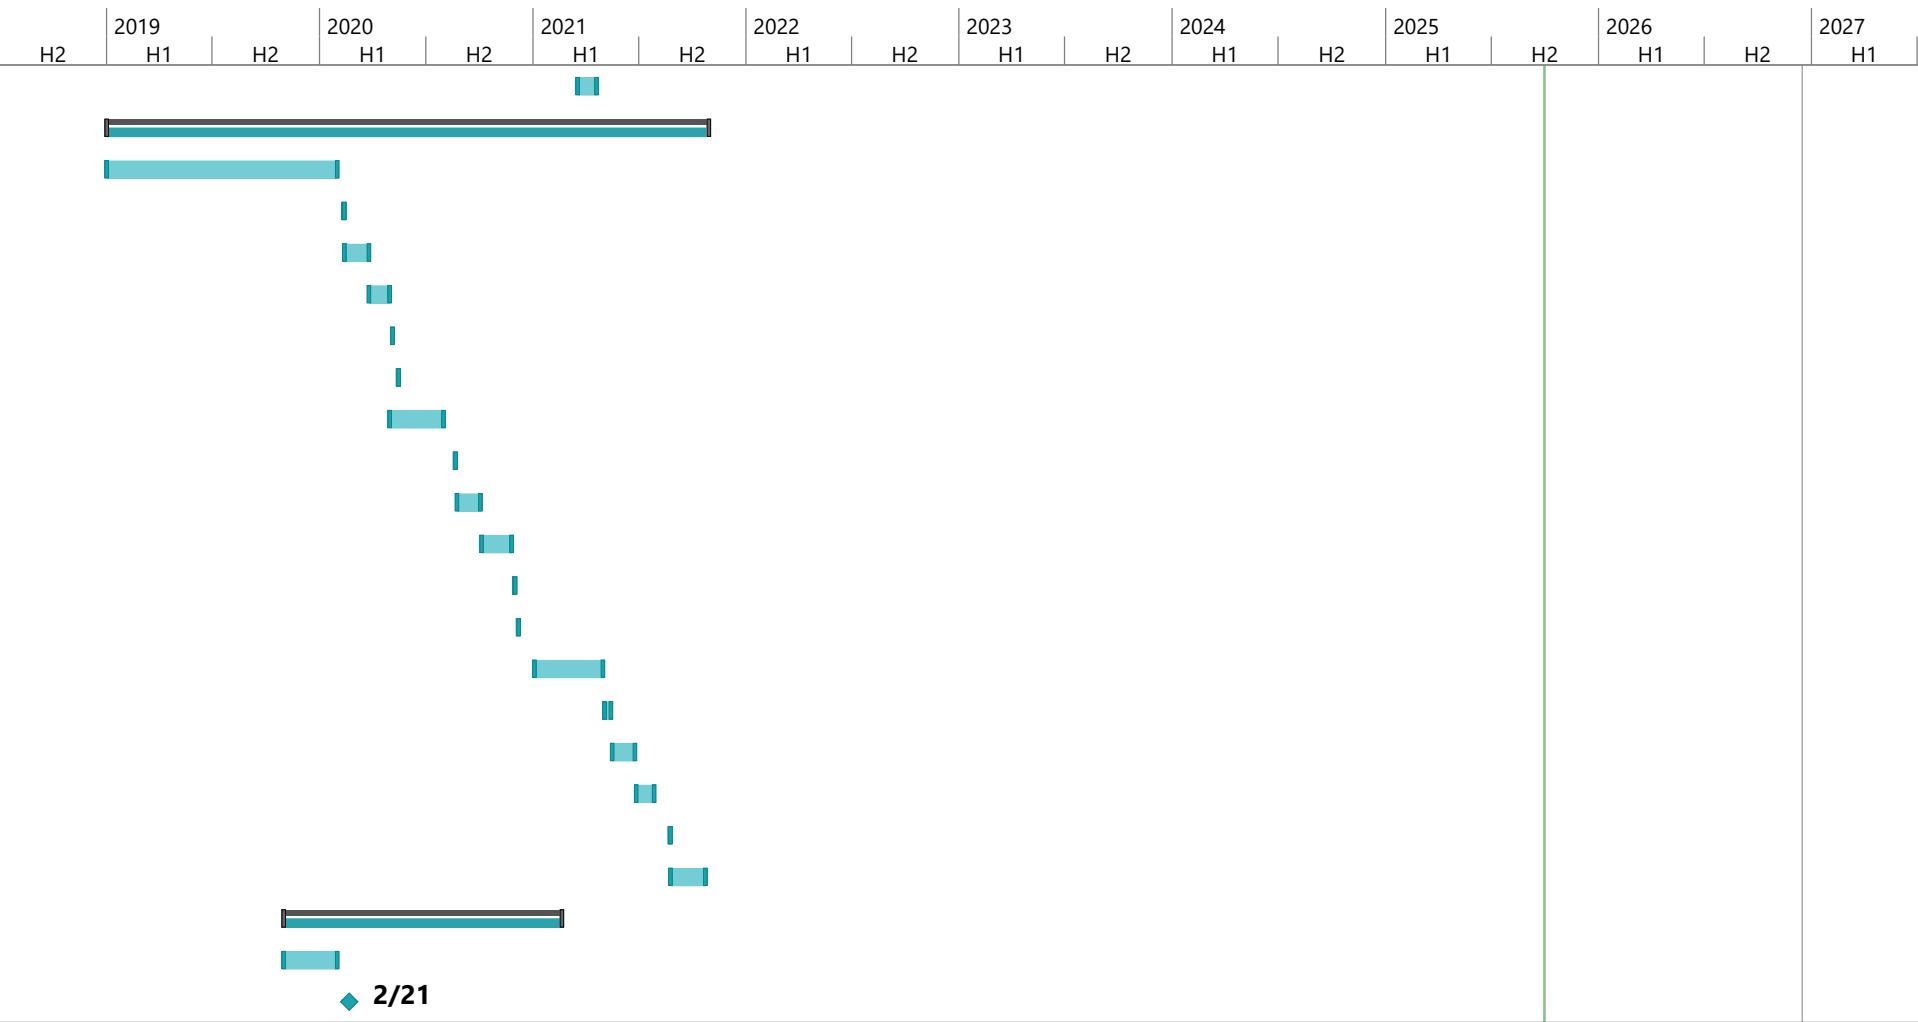
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



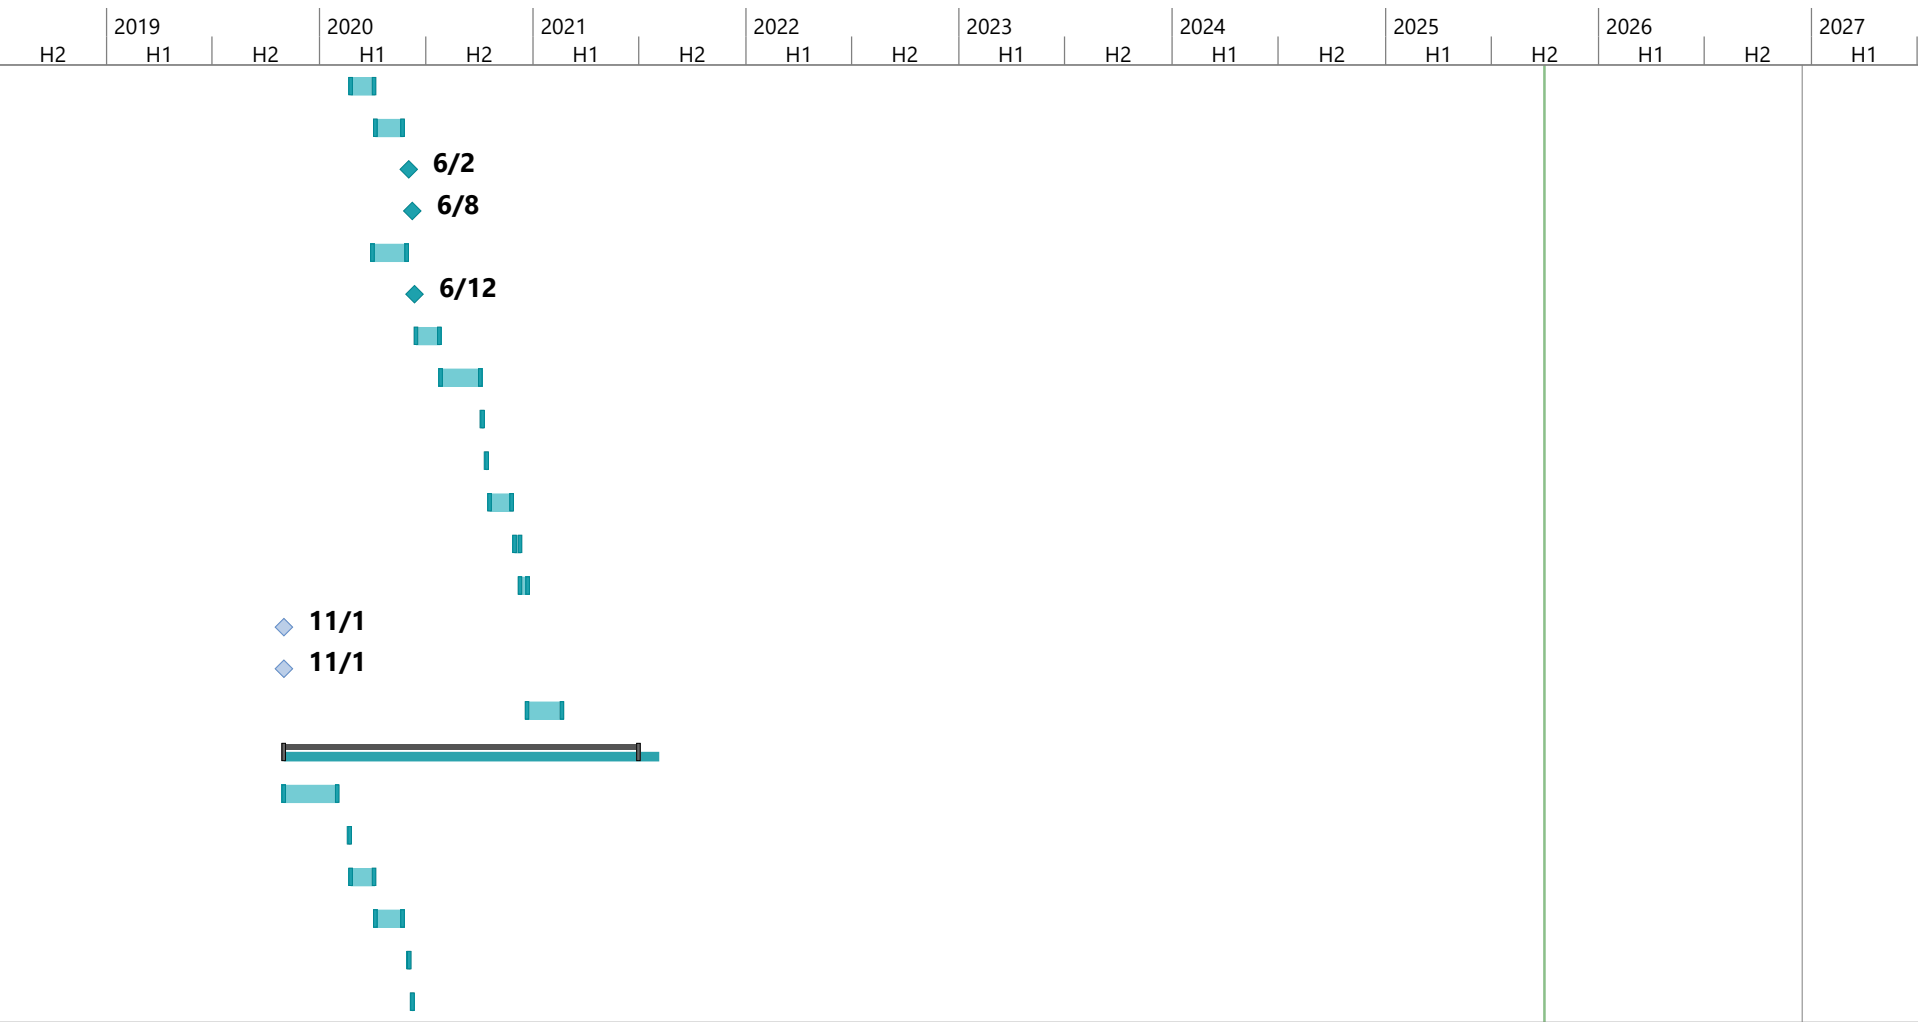
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



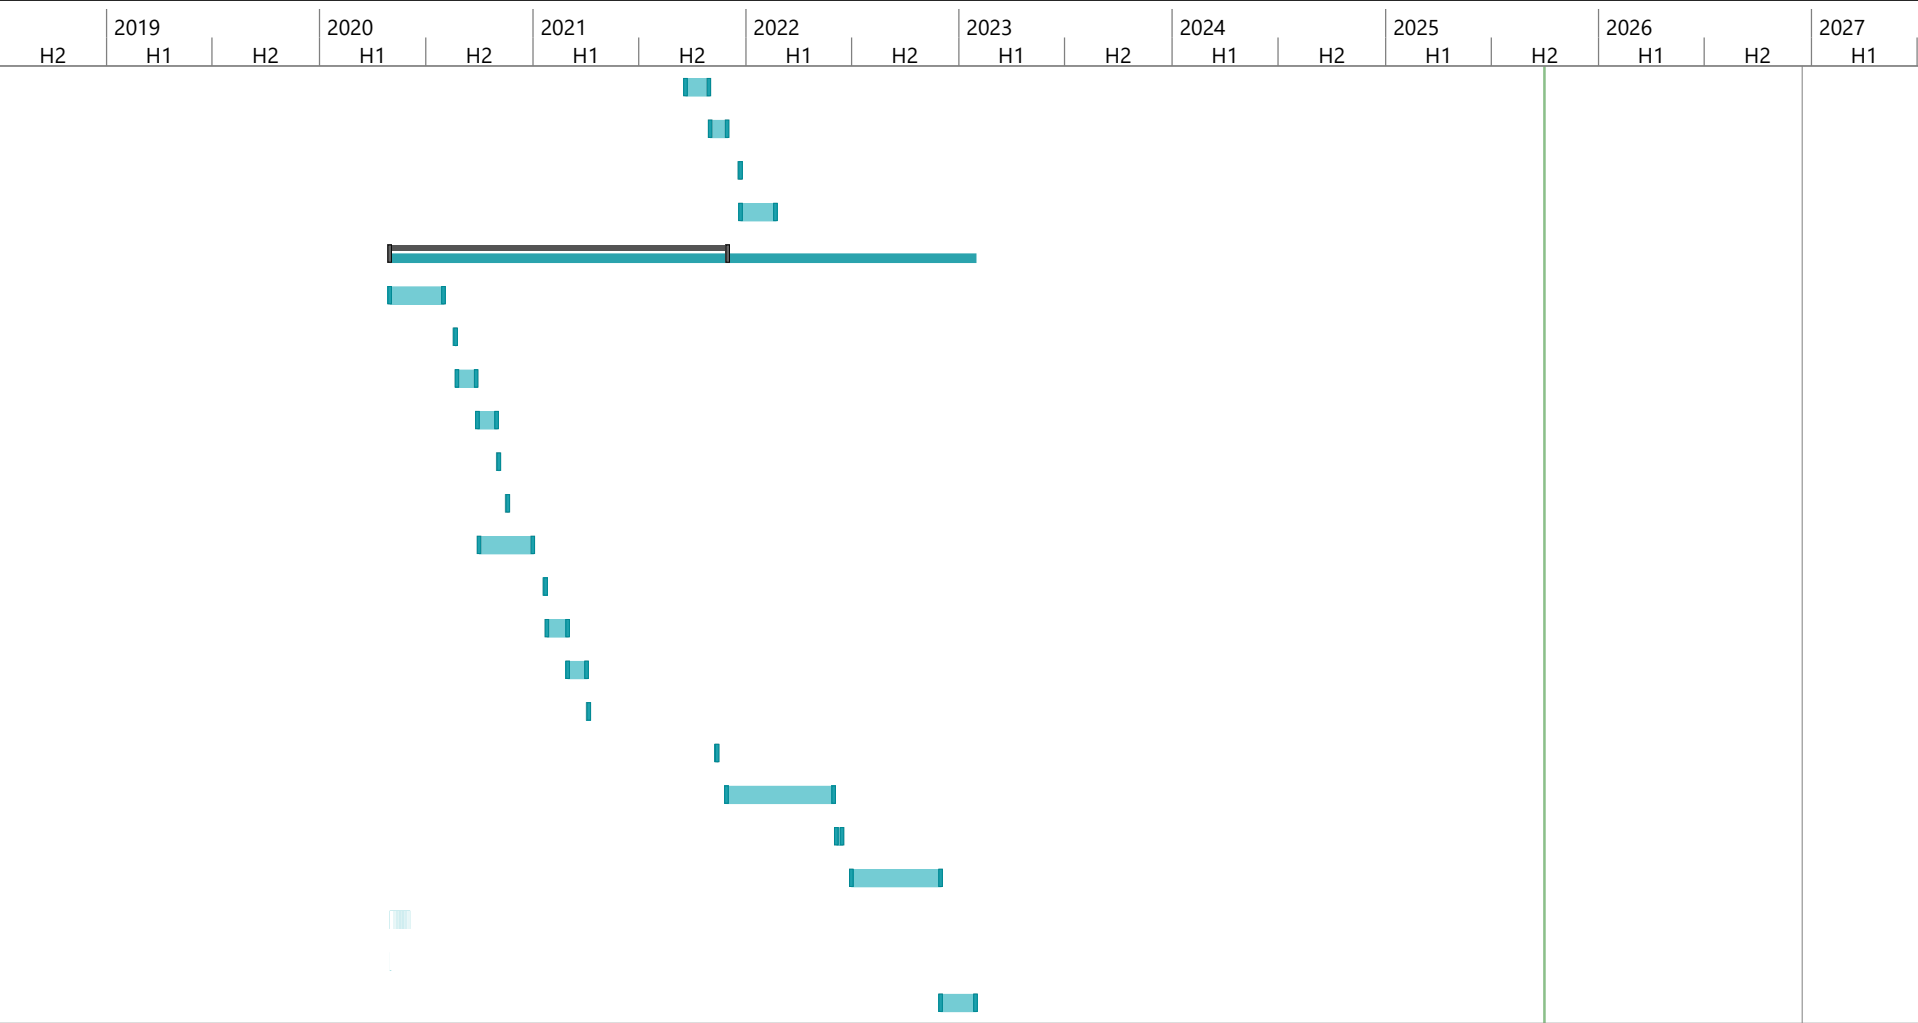
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



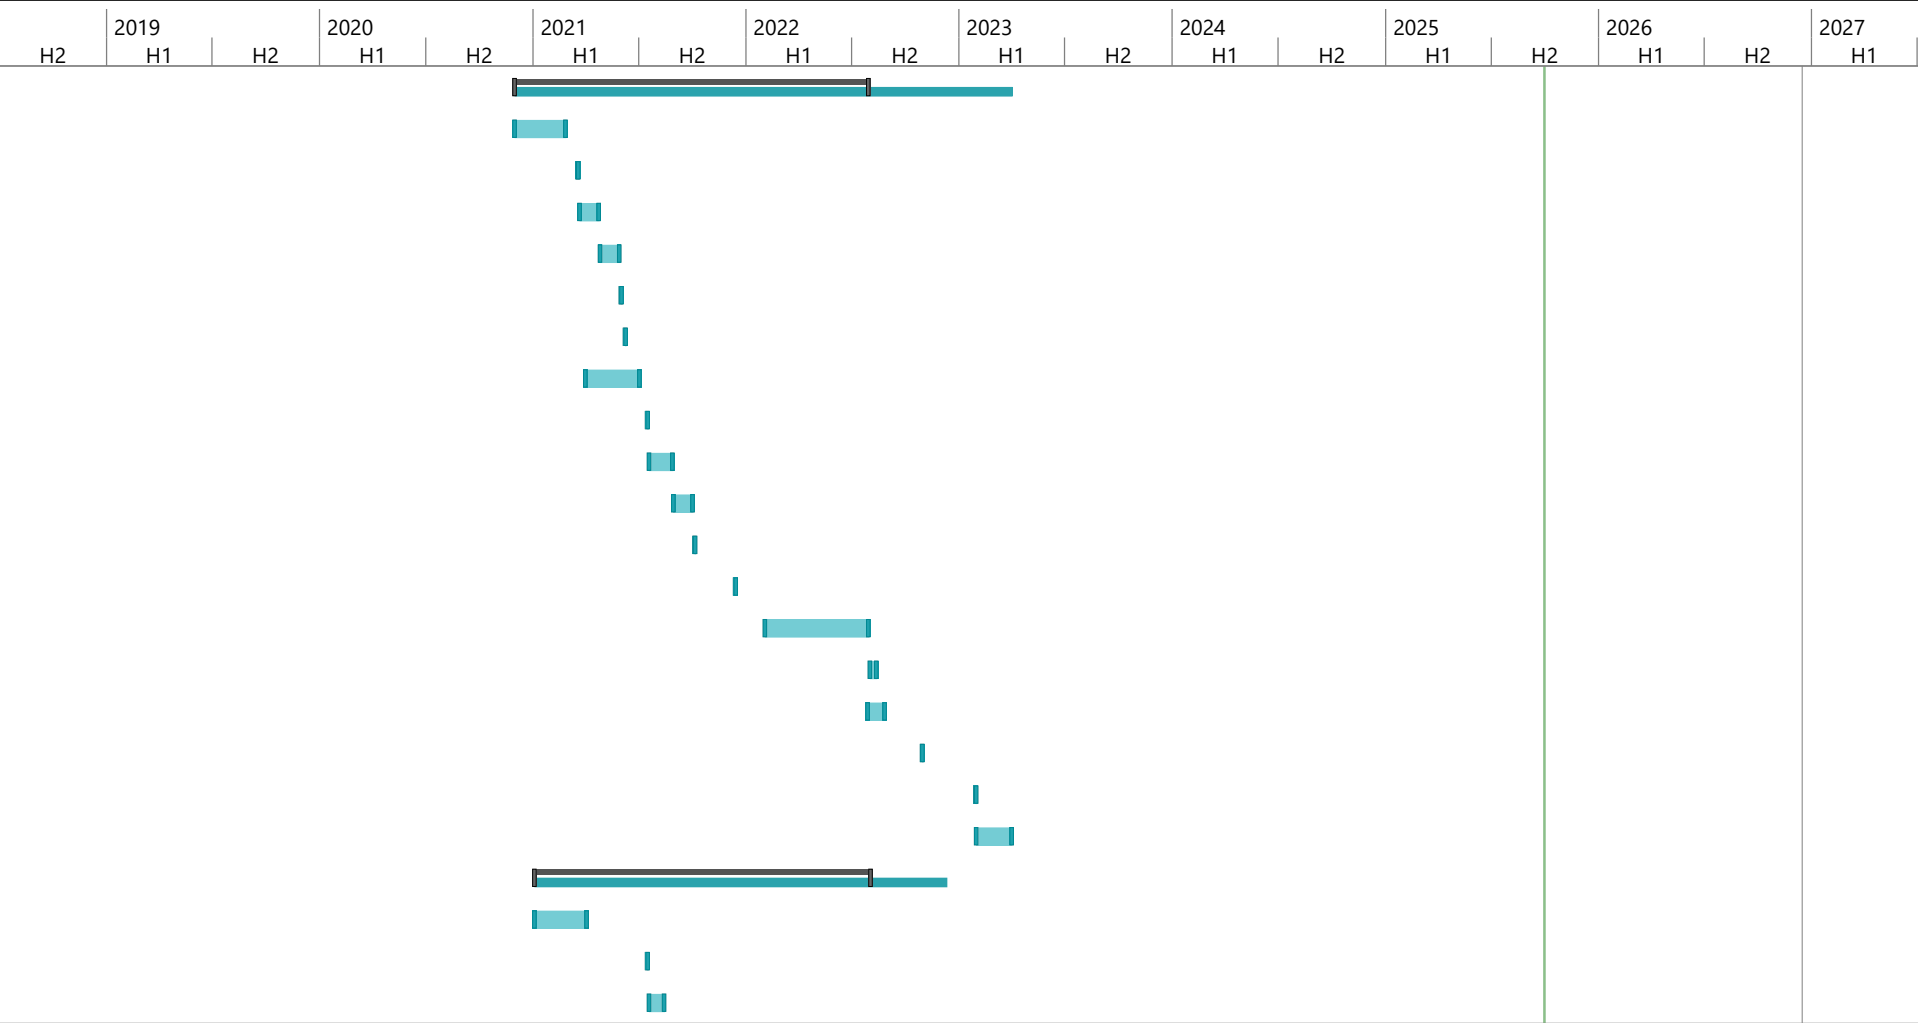
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



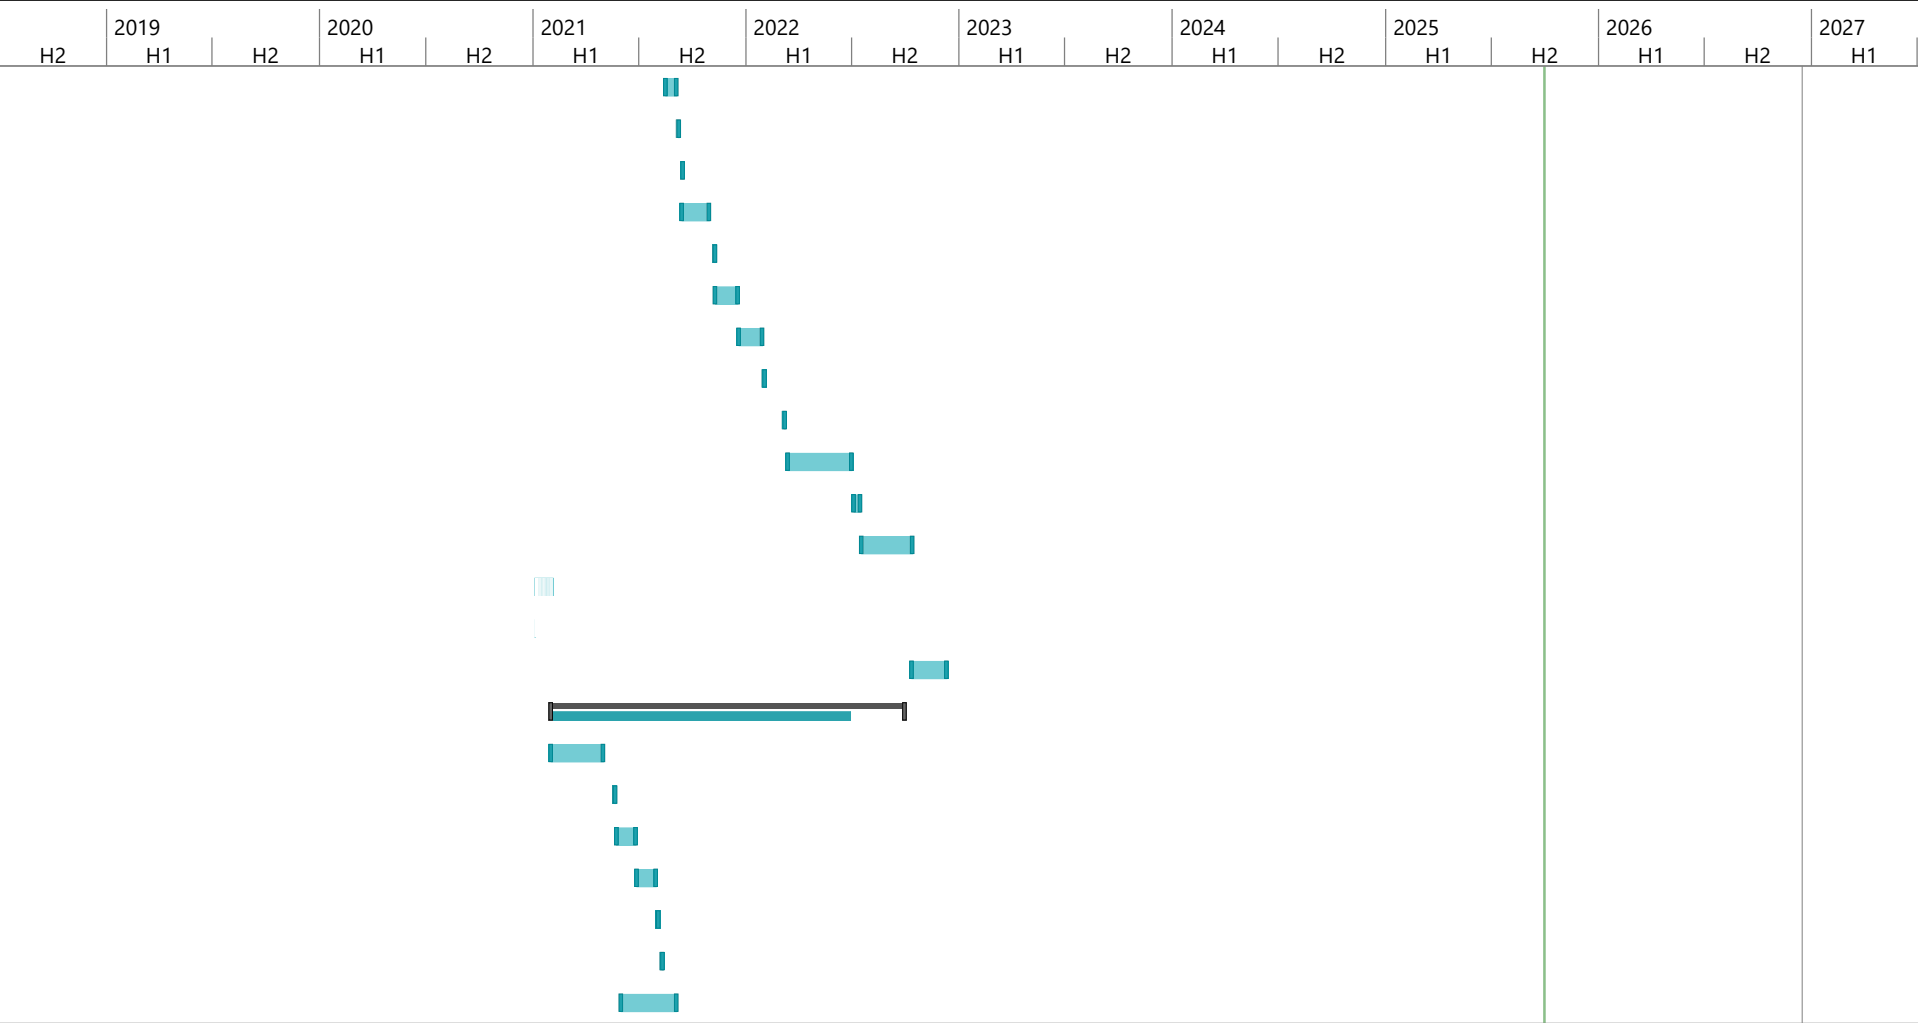
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

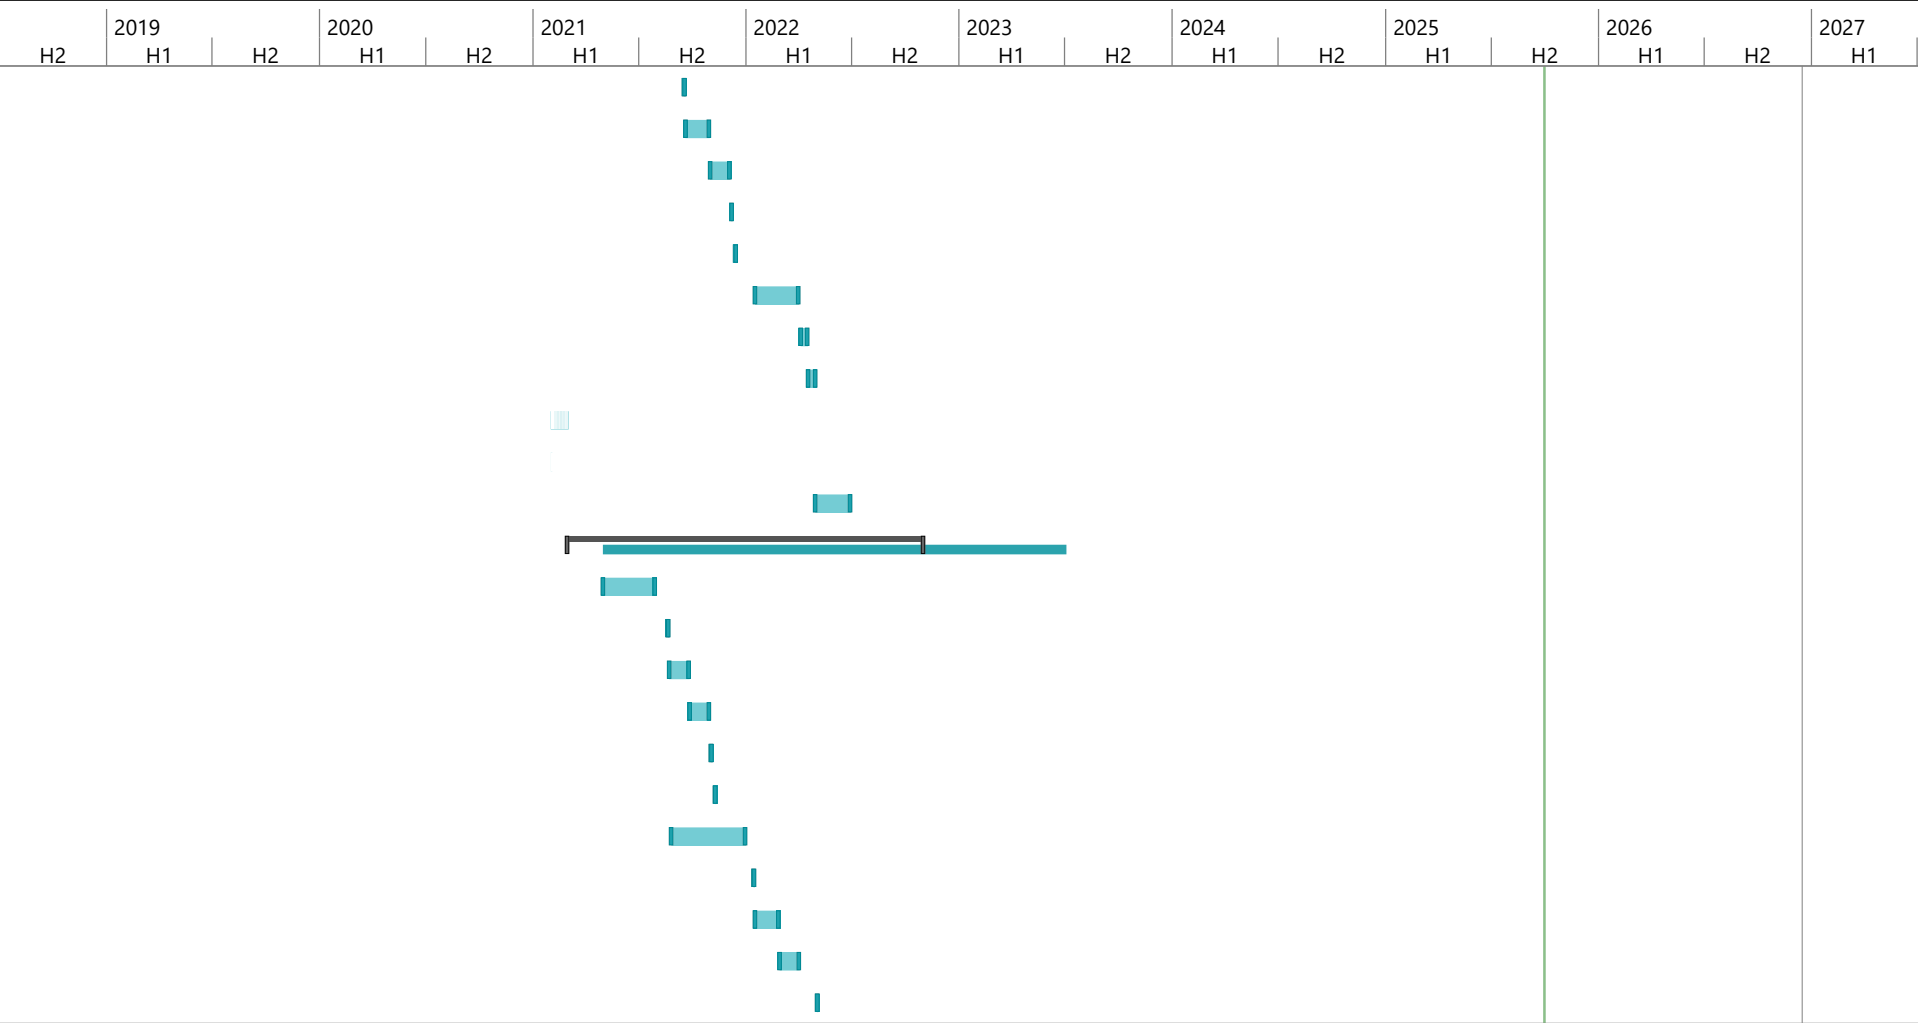


Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

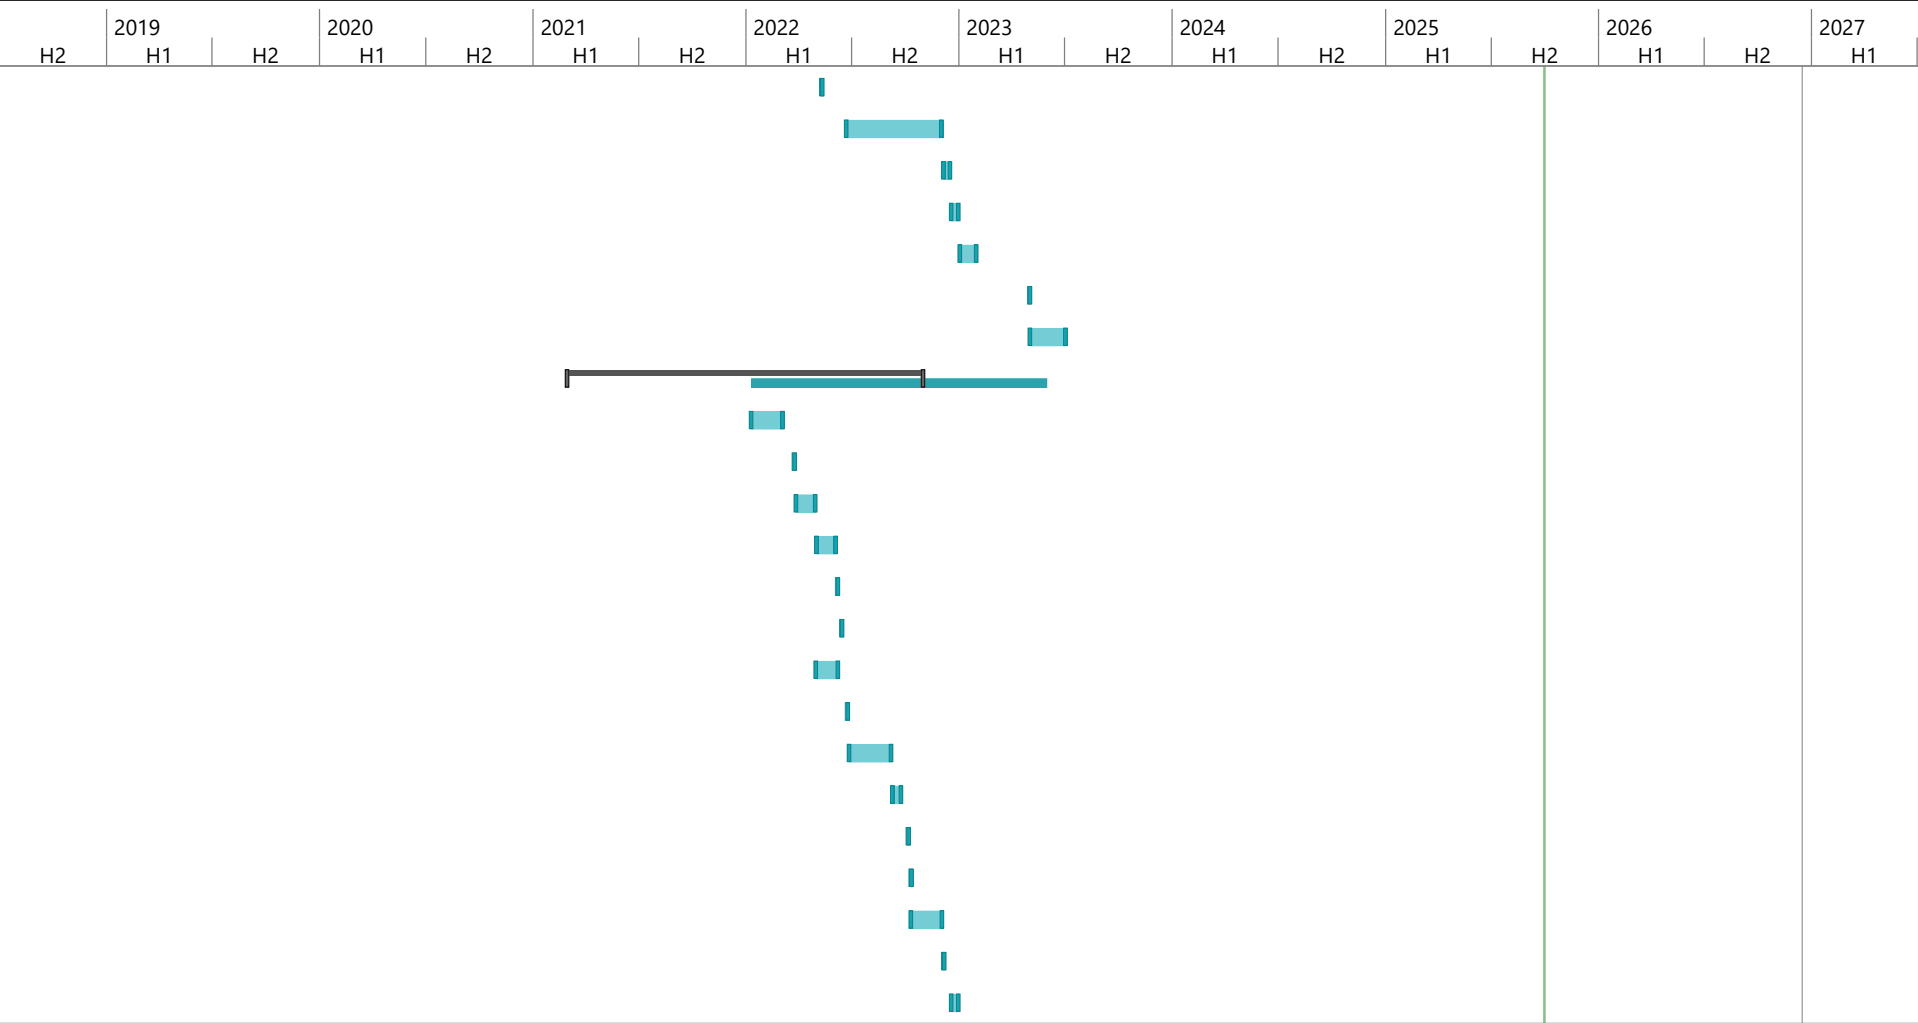


Project: IOU Master Task Timeli
Date: Tue 9/30/25

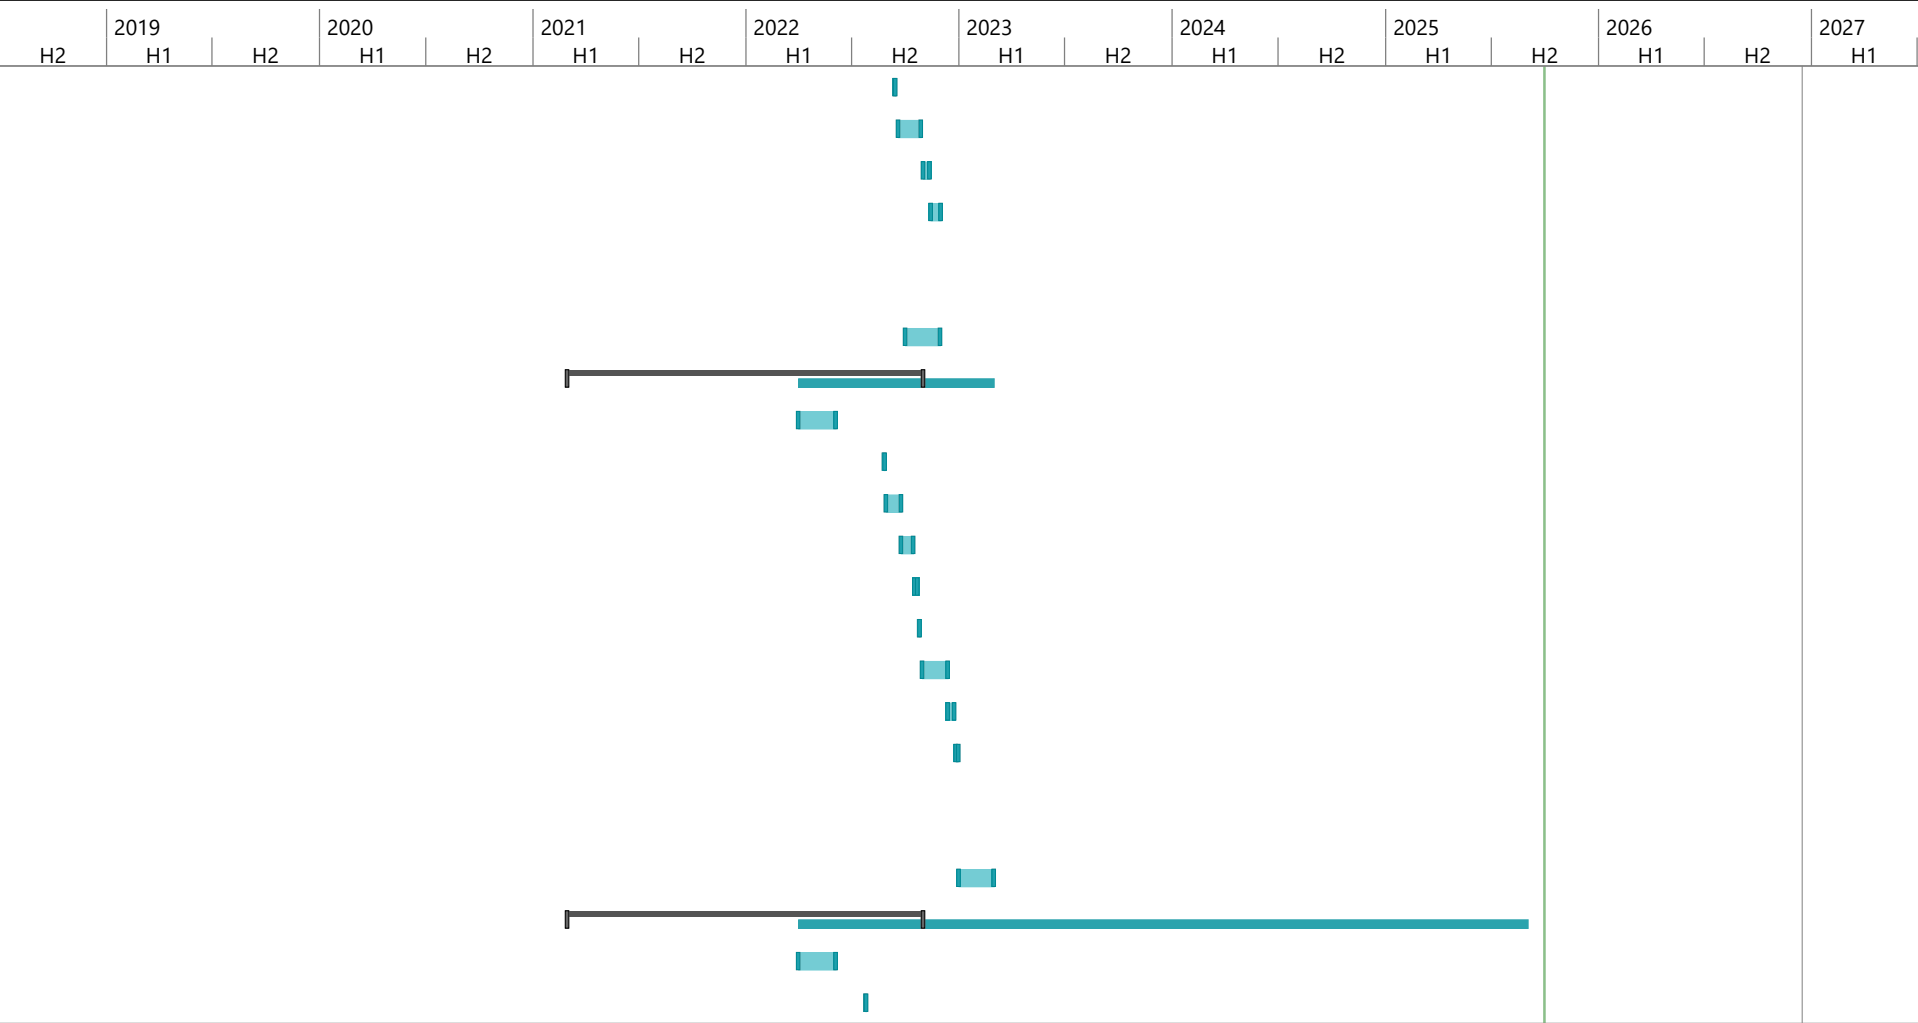
Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

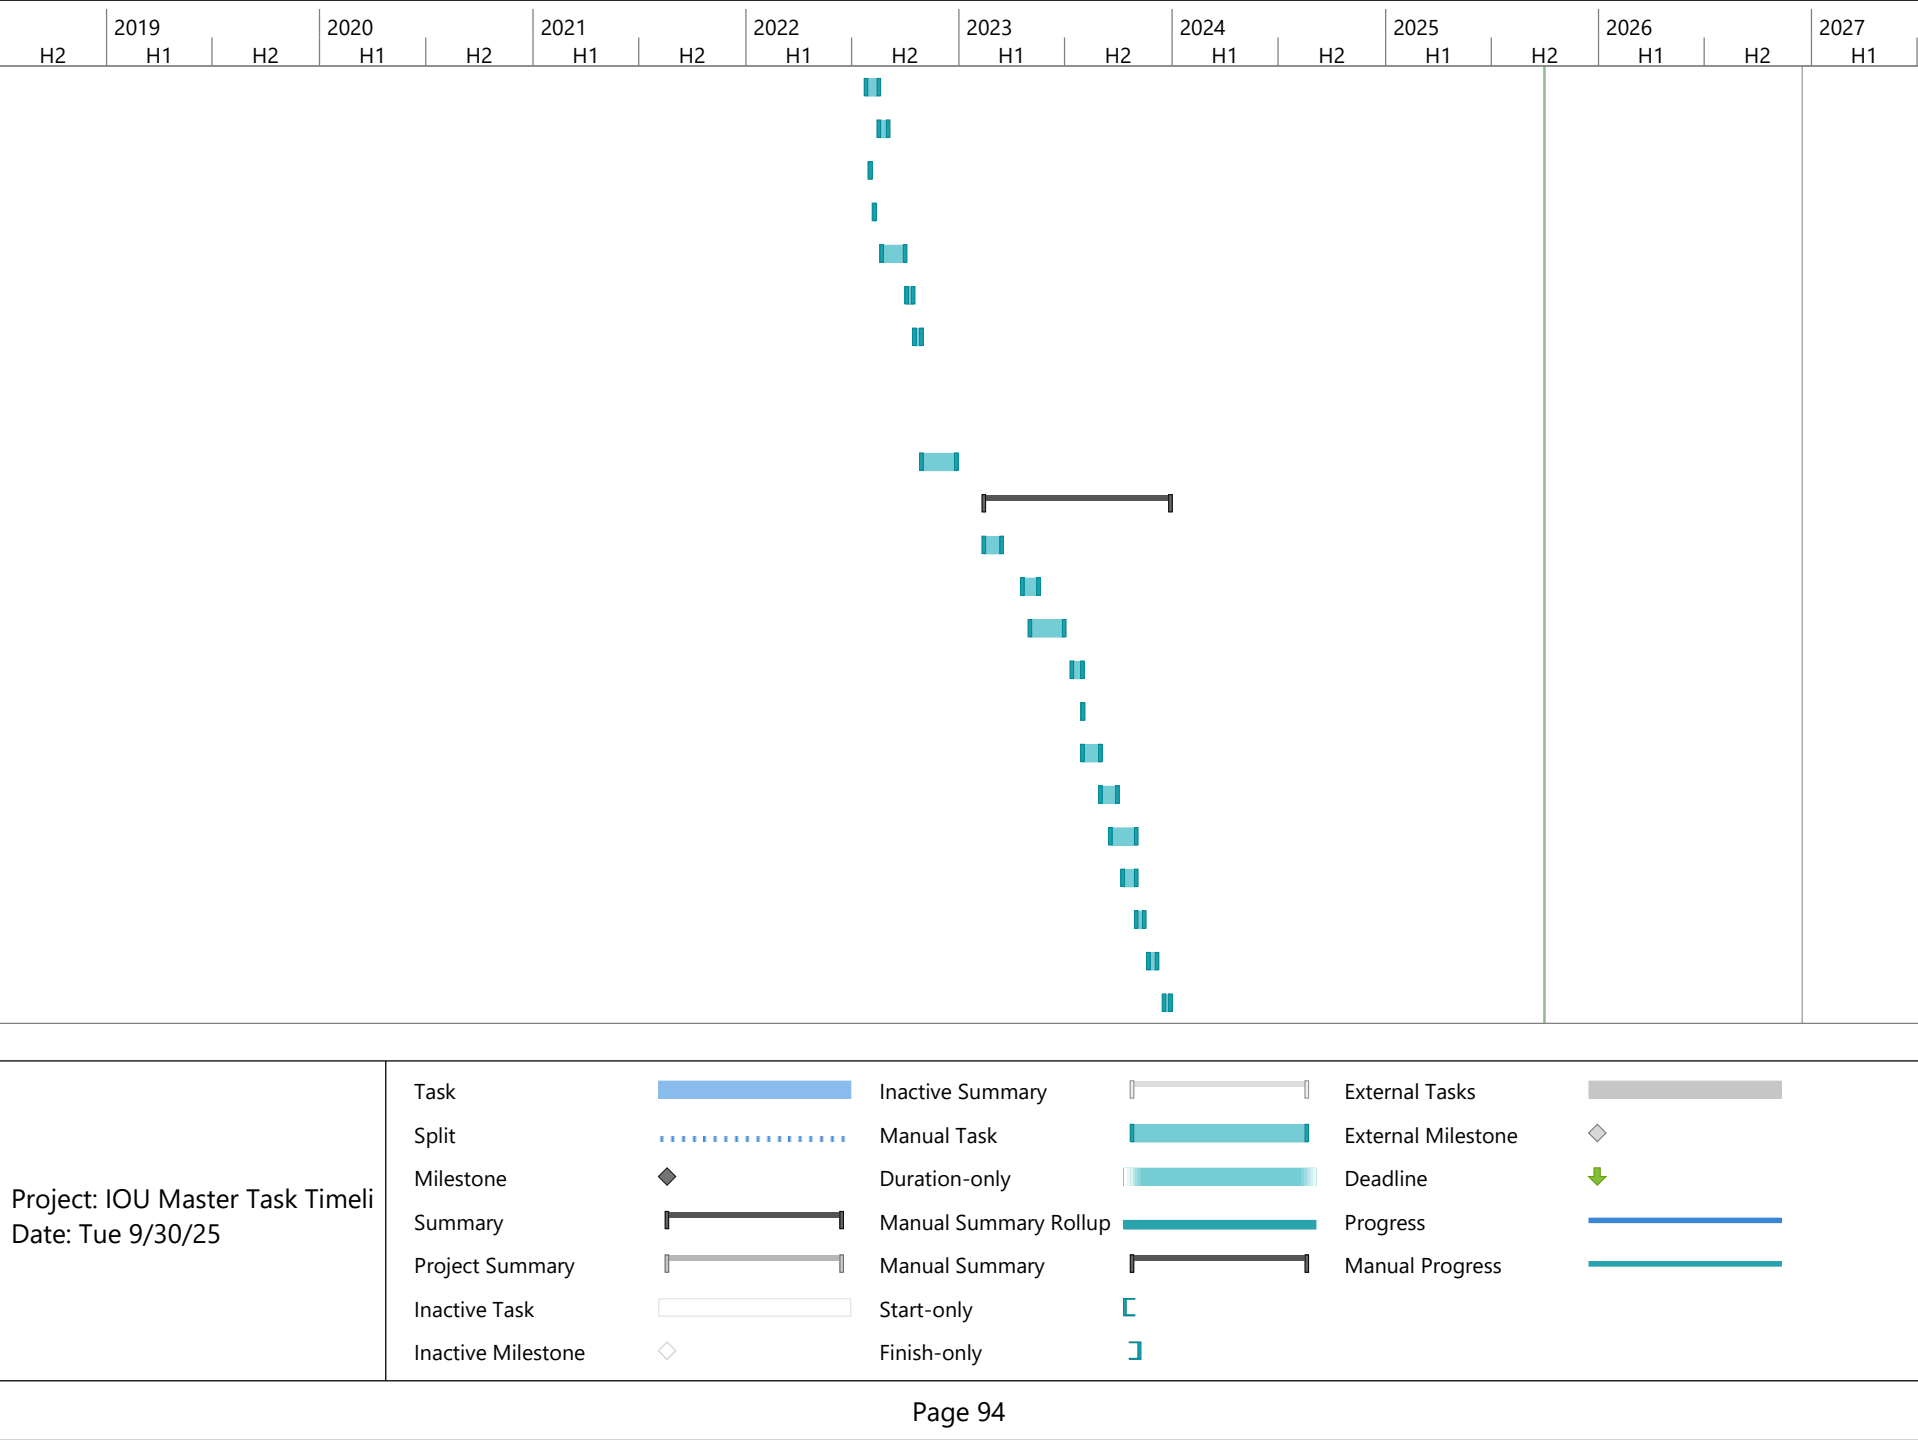
External Milestone

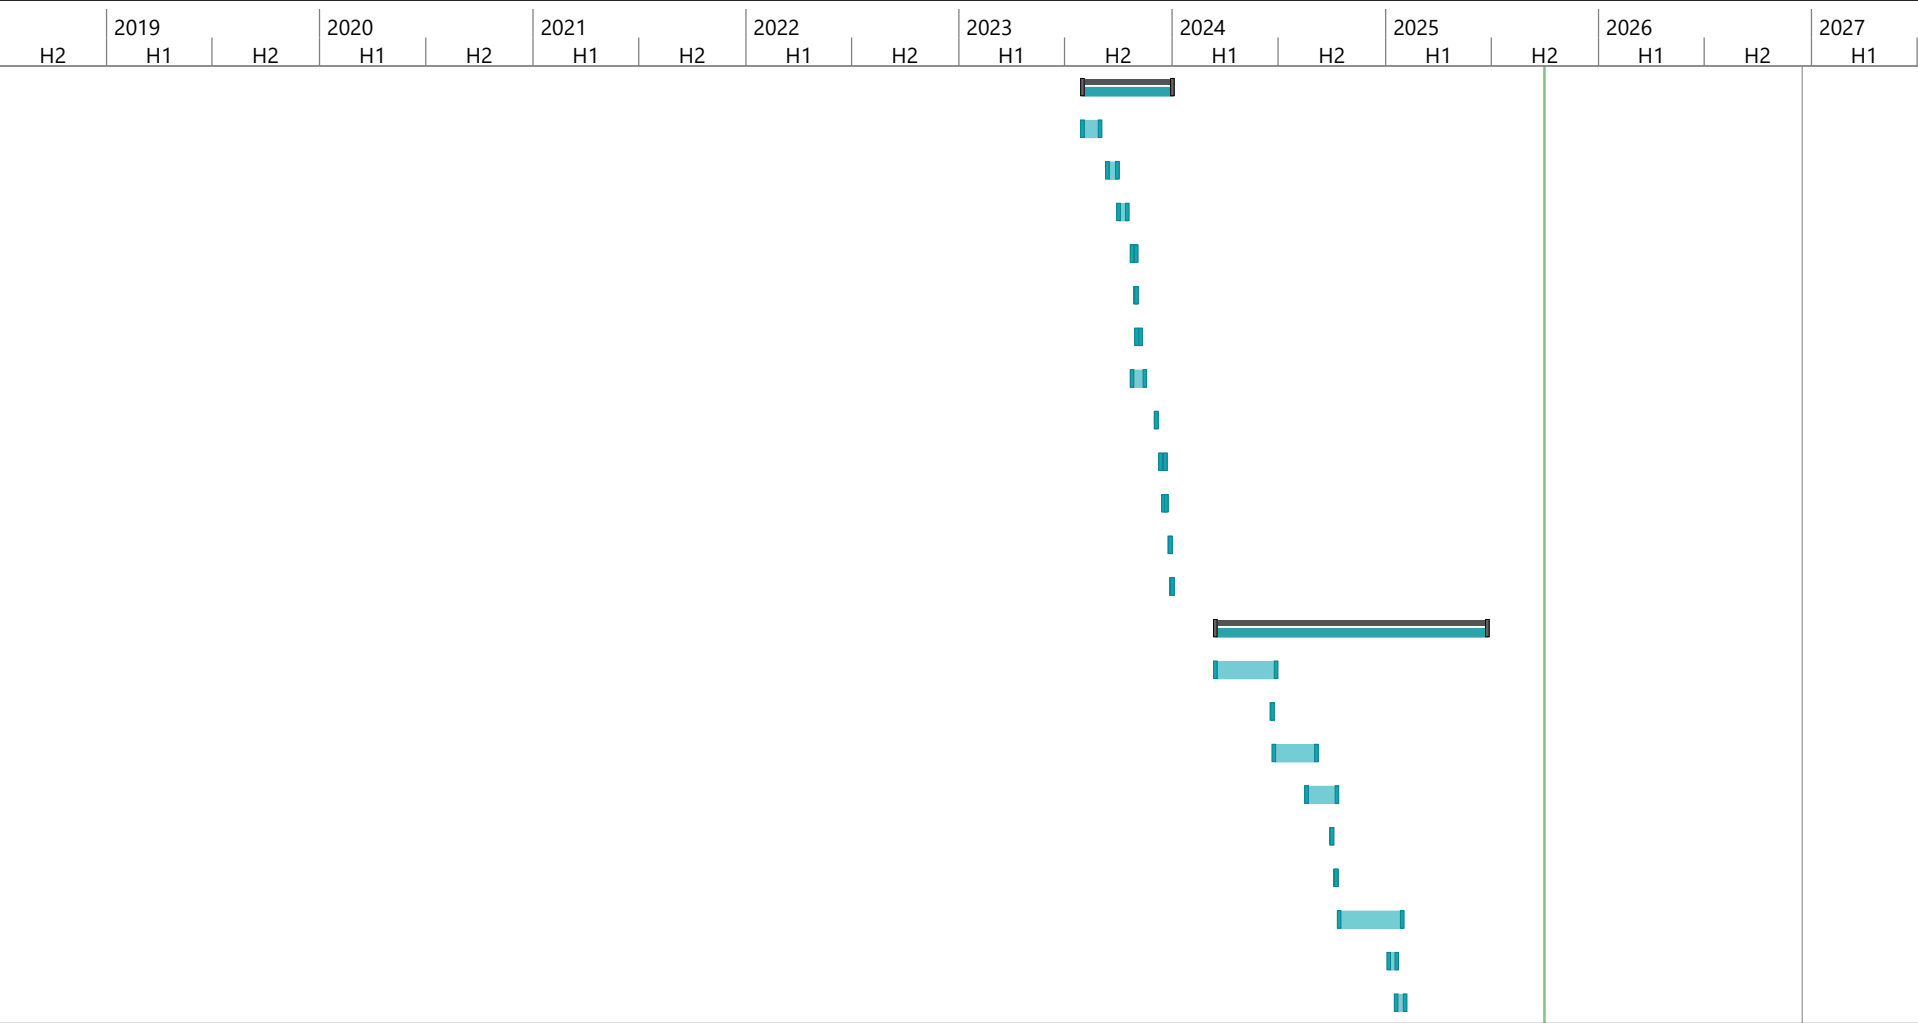
Deadline

Progress

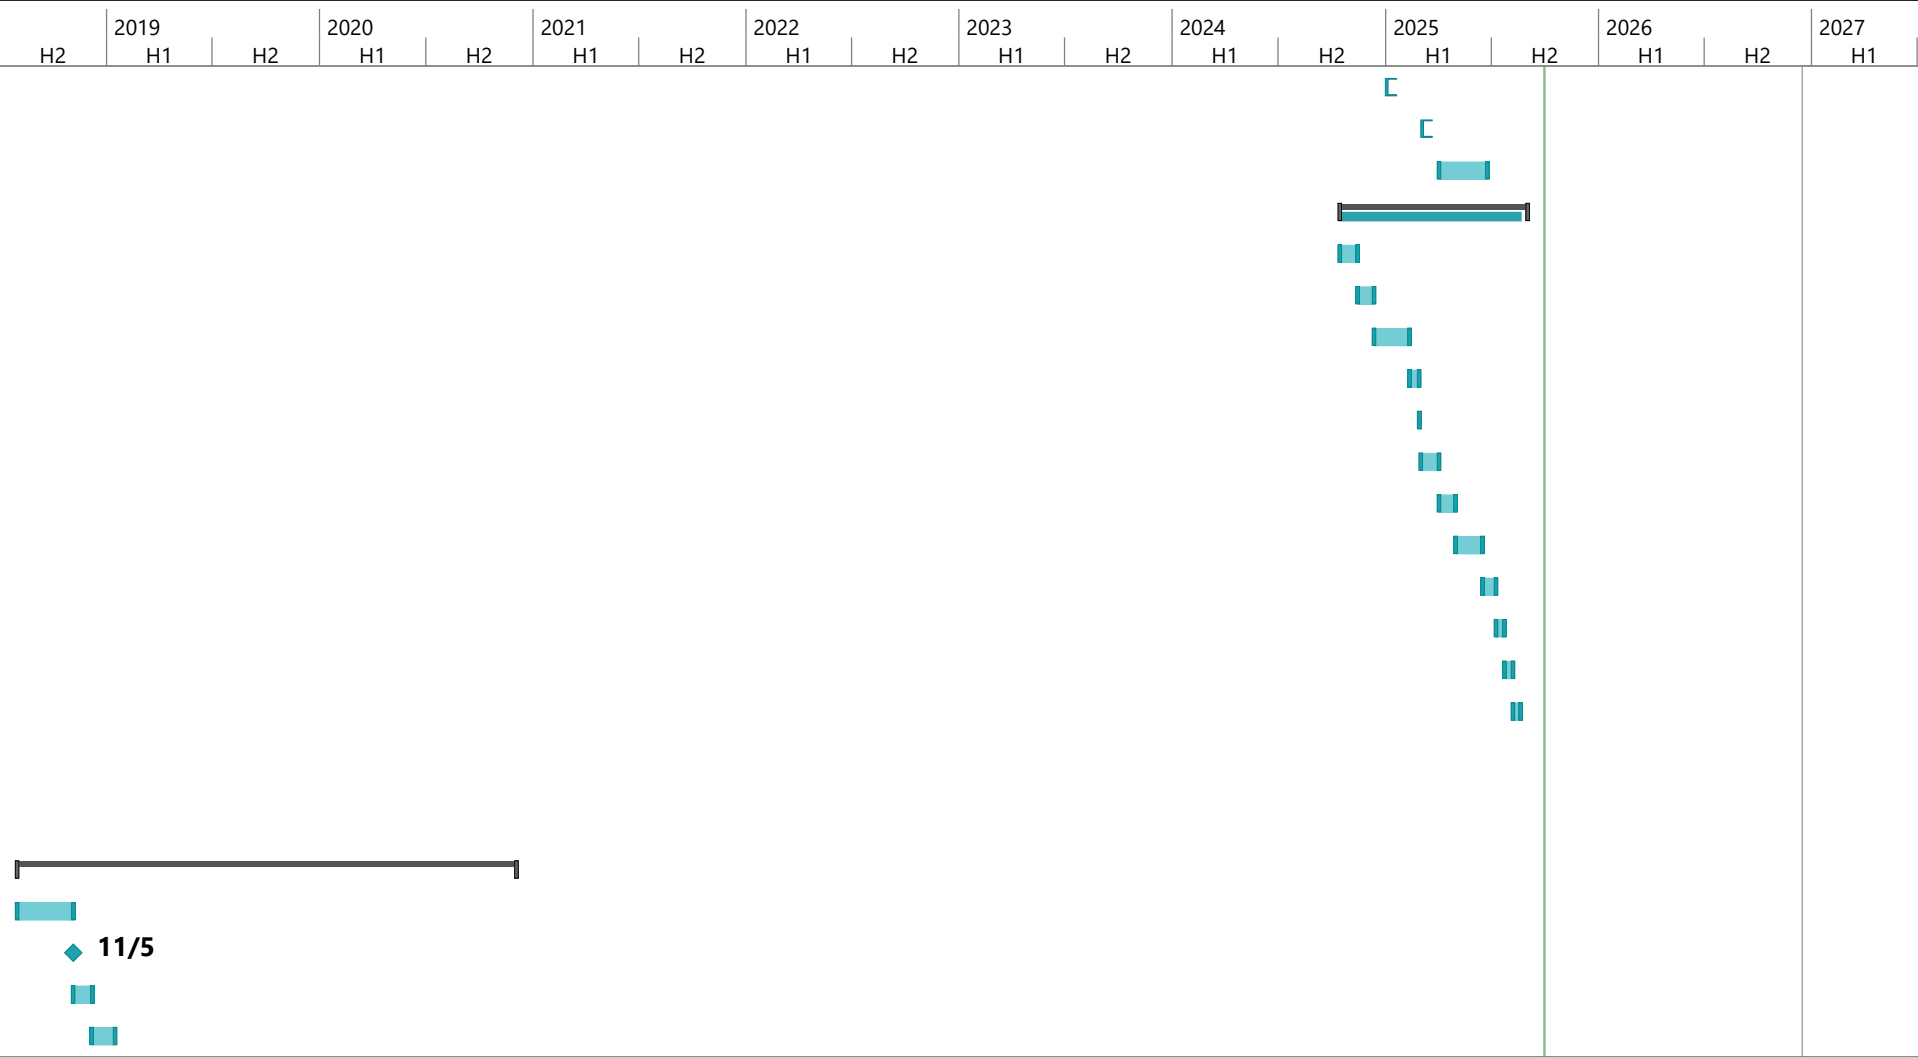
Manual Progress

Page 93

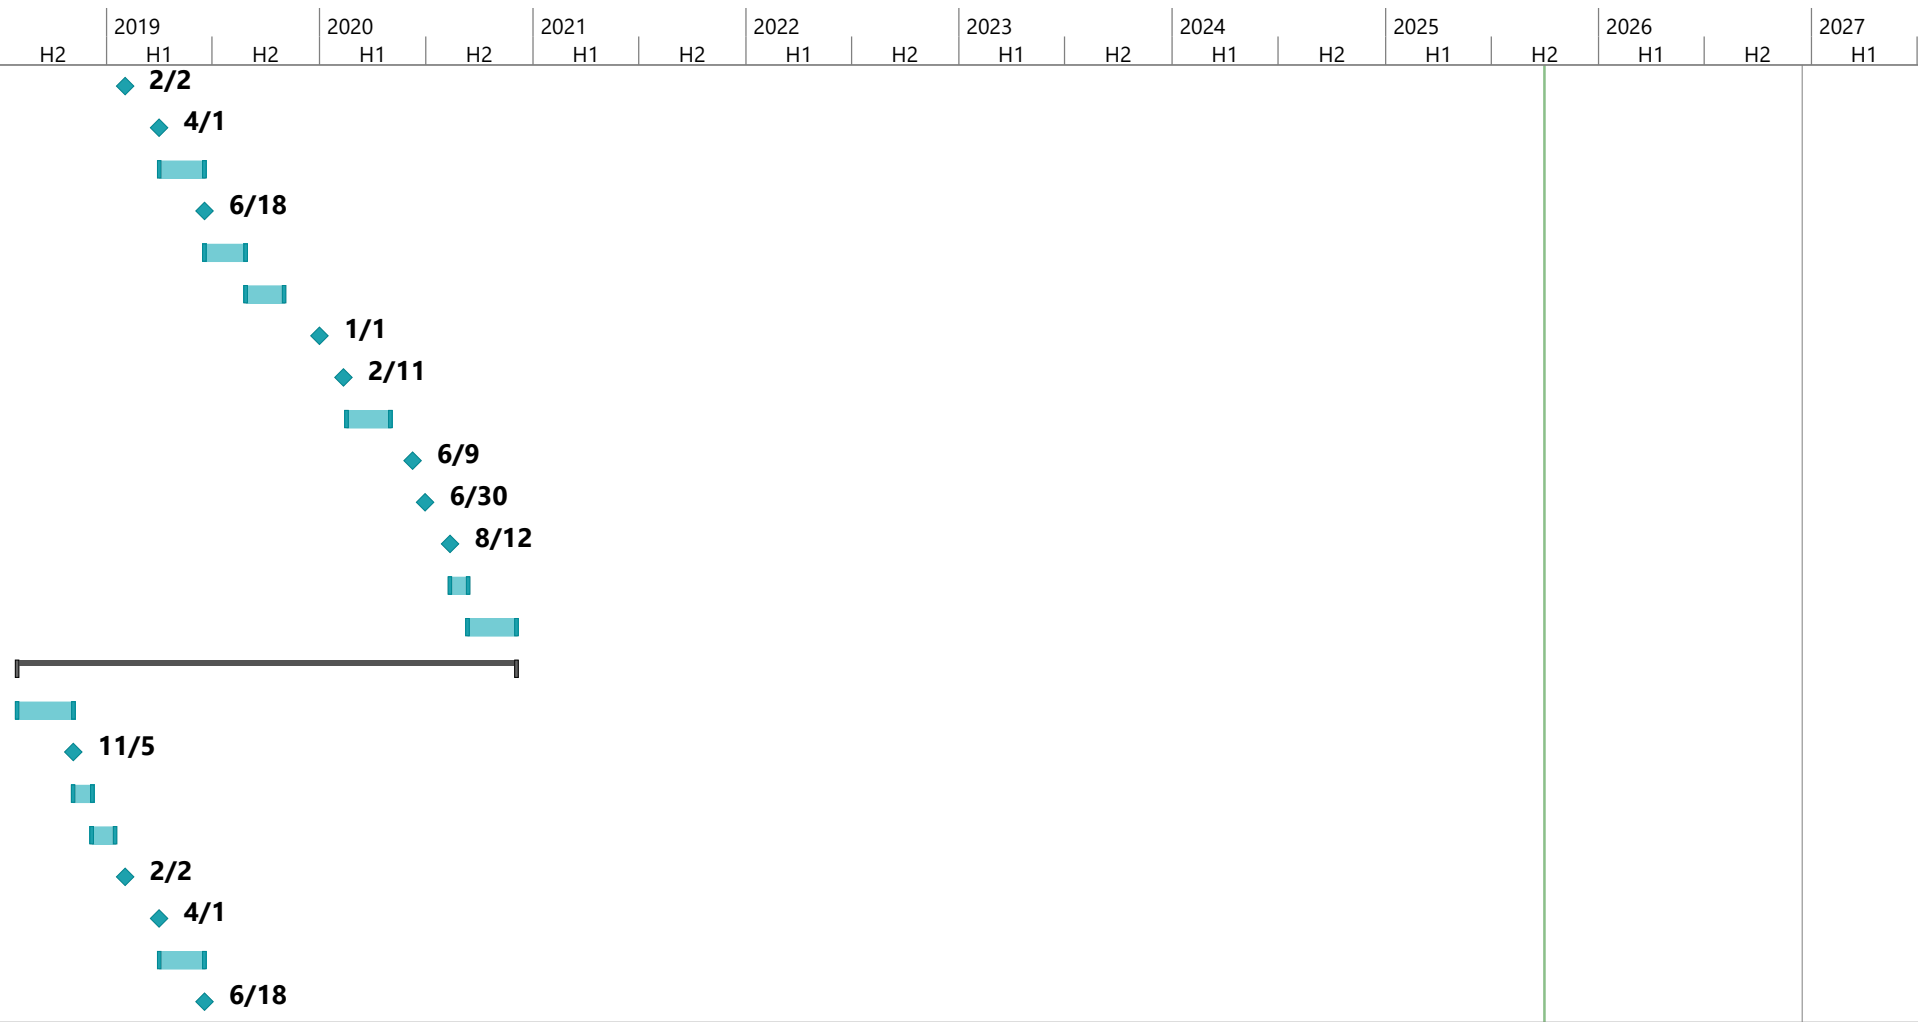




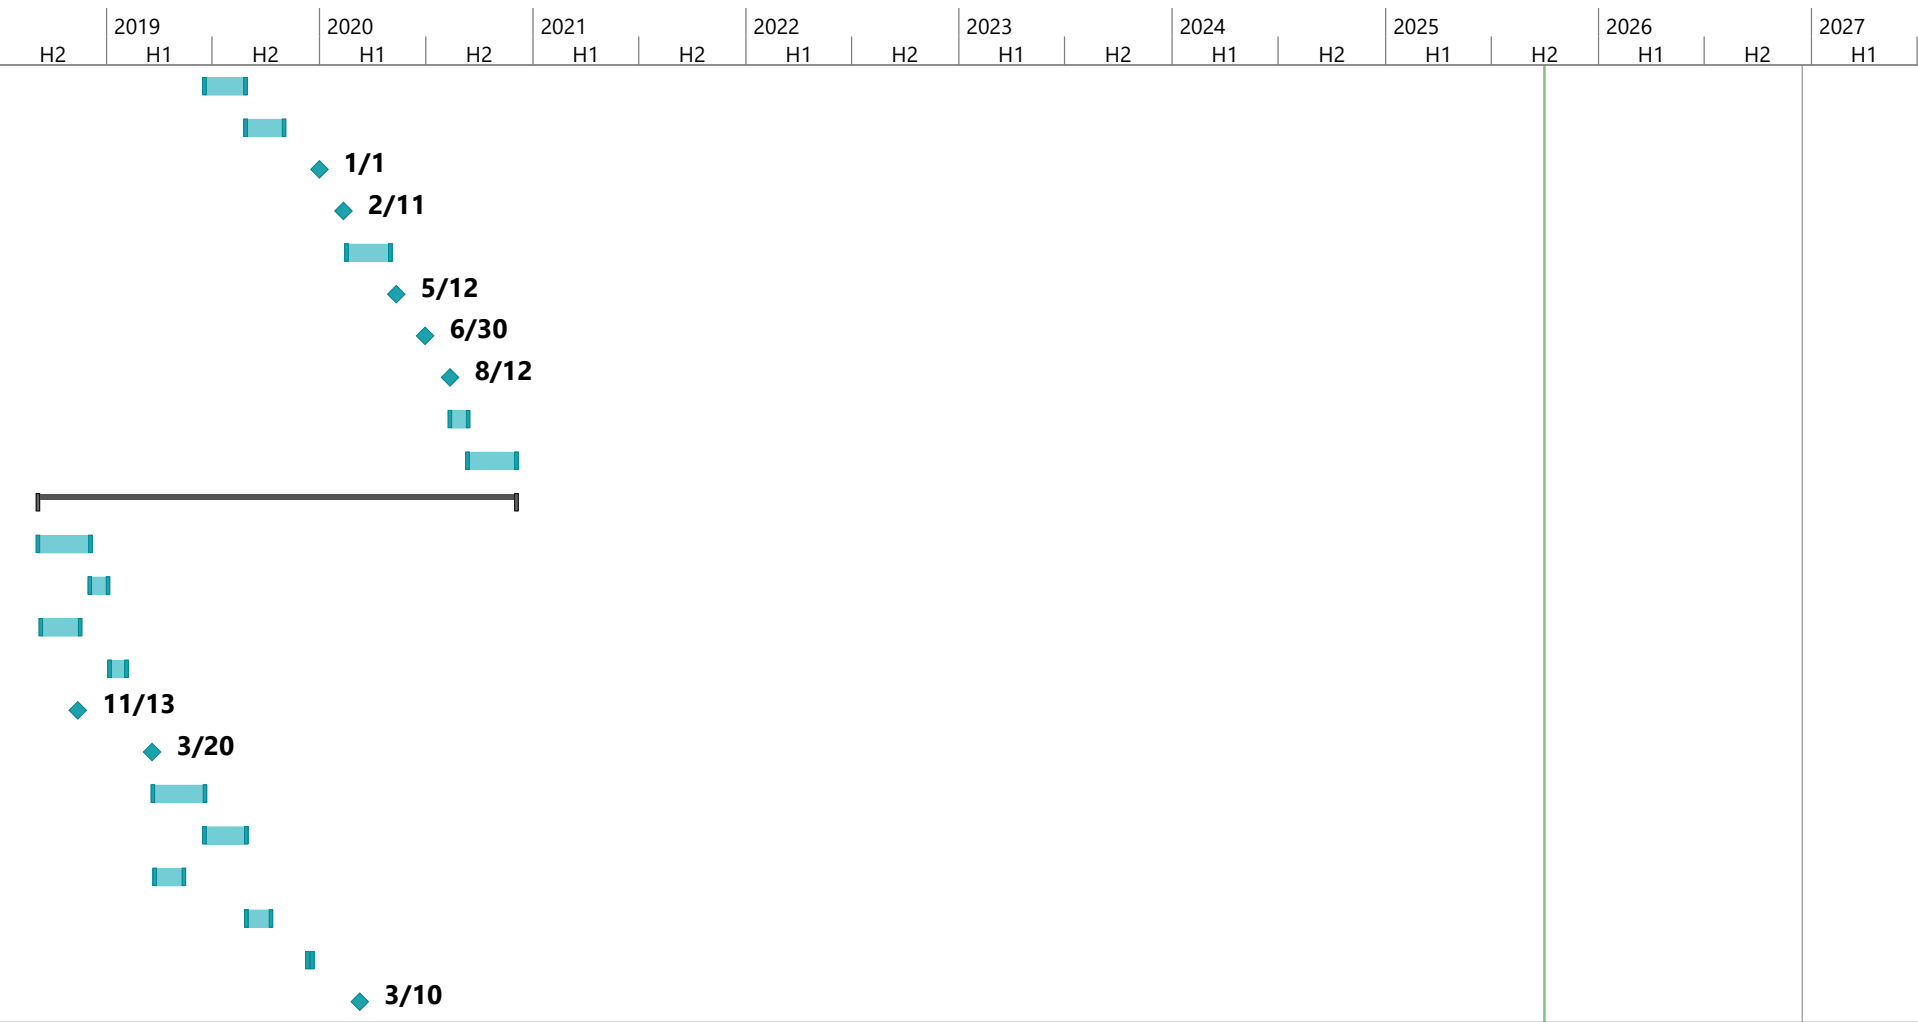
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



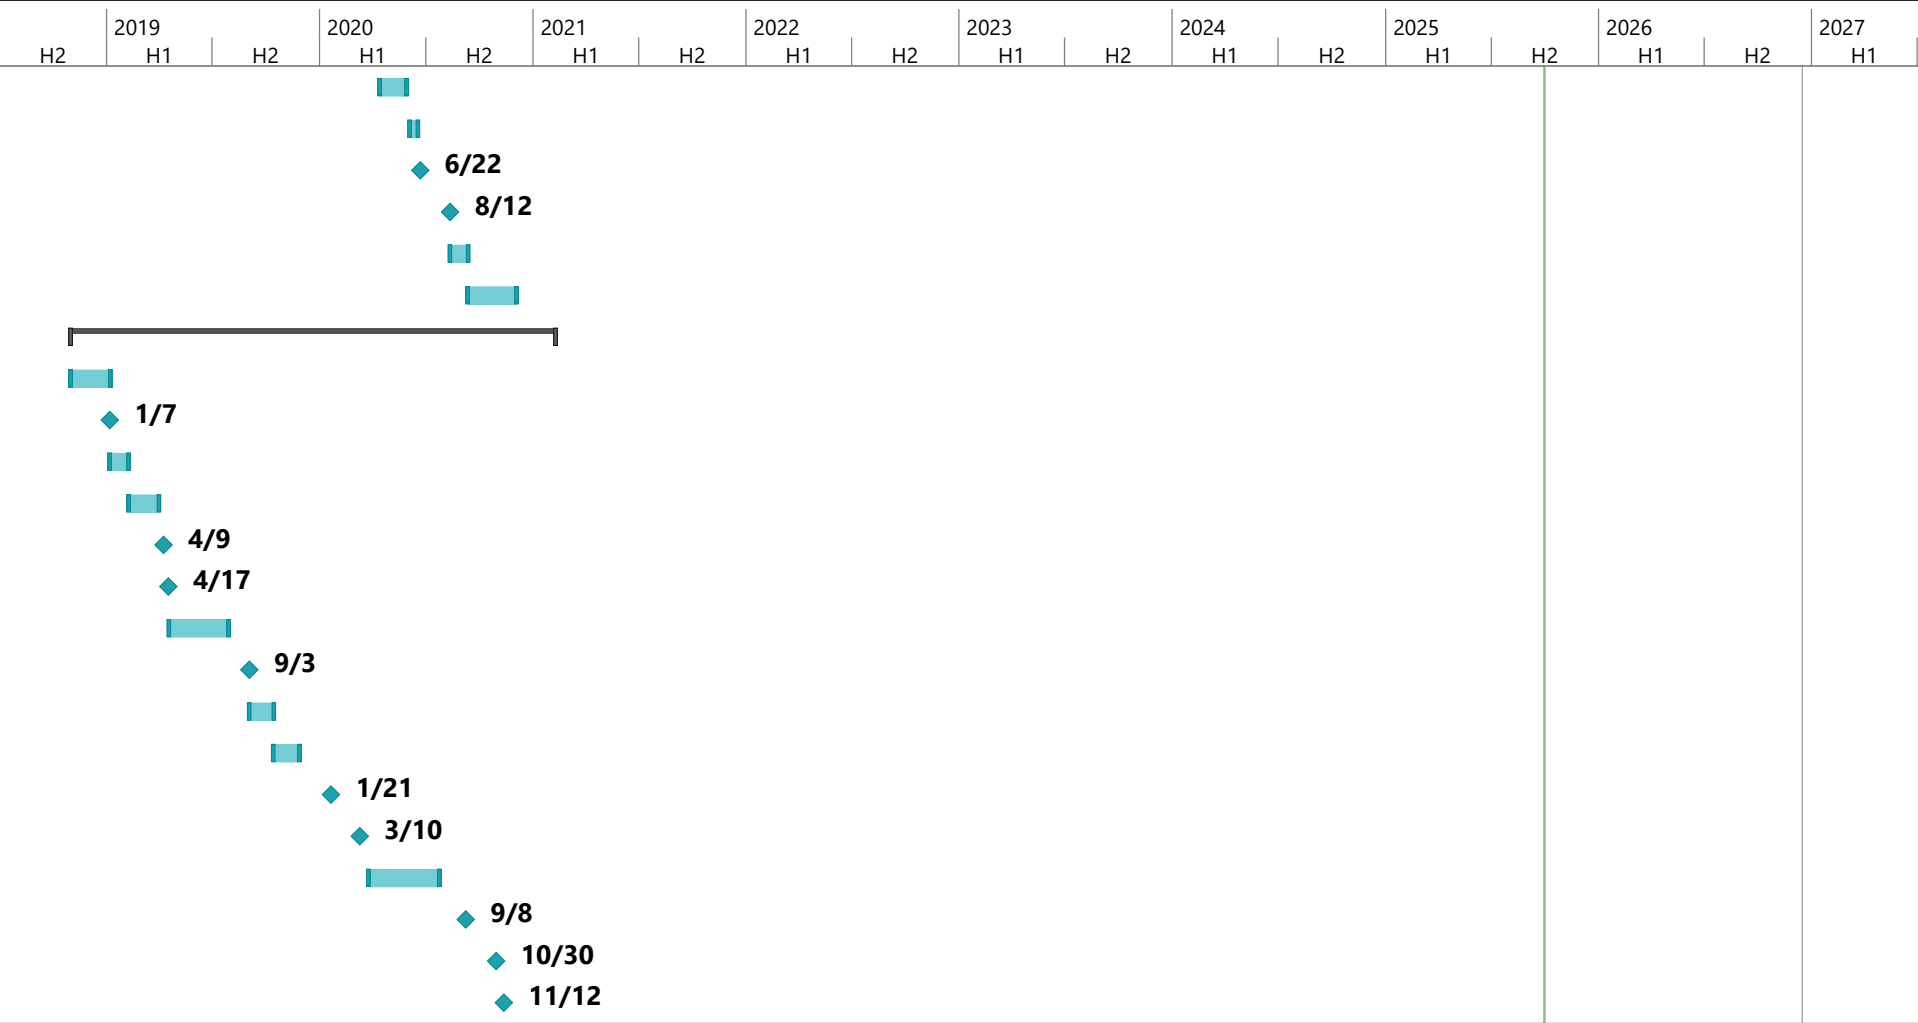
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




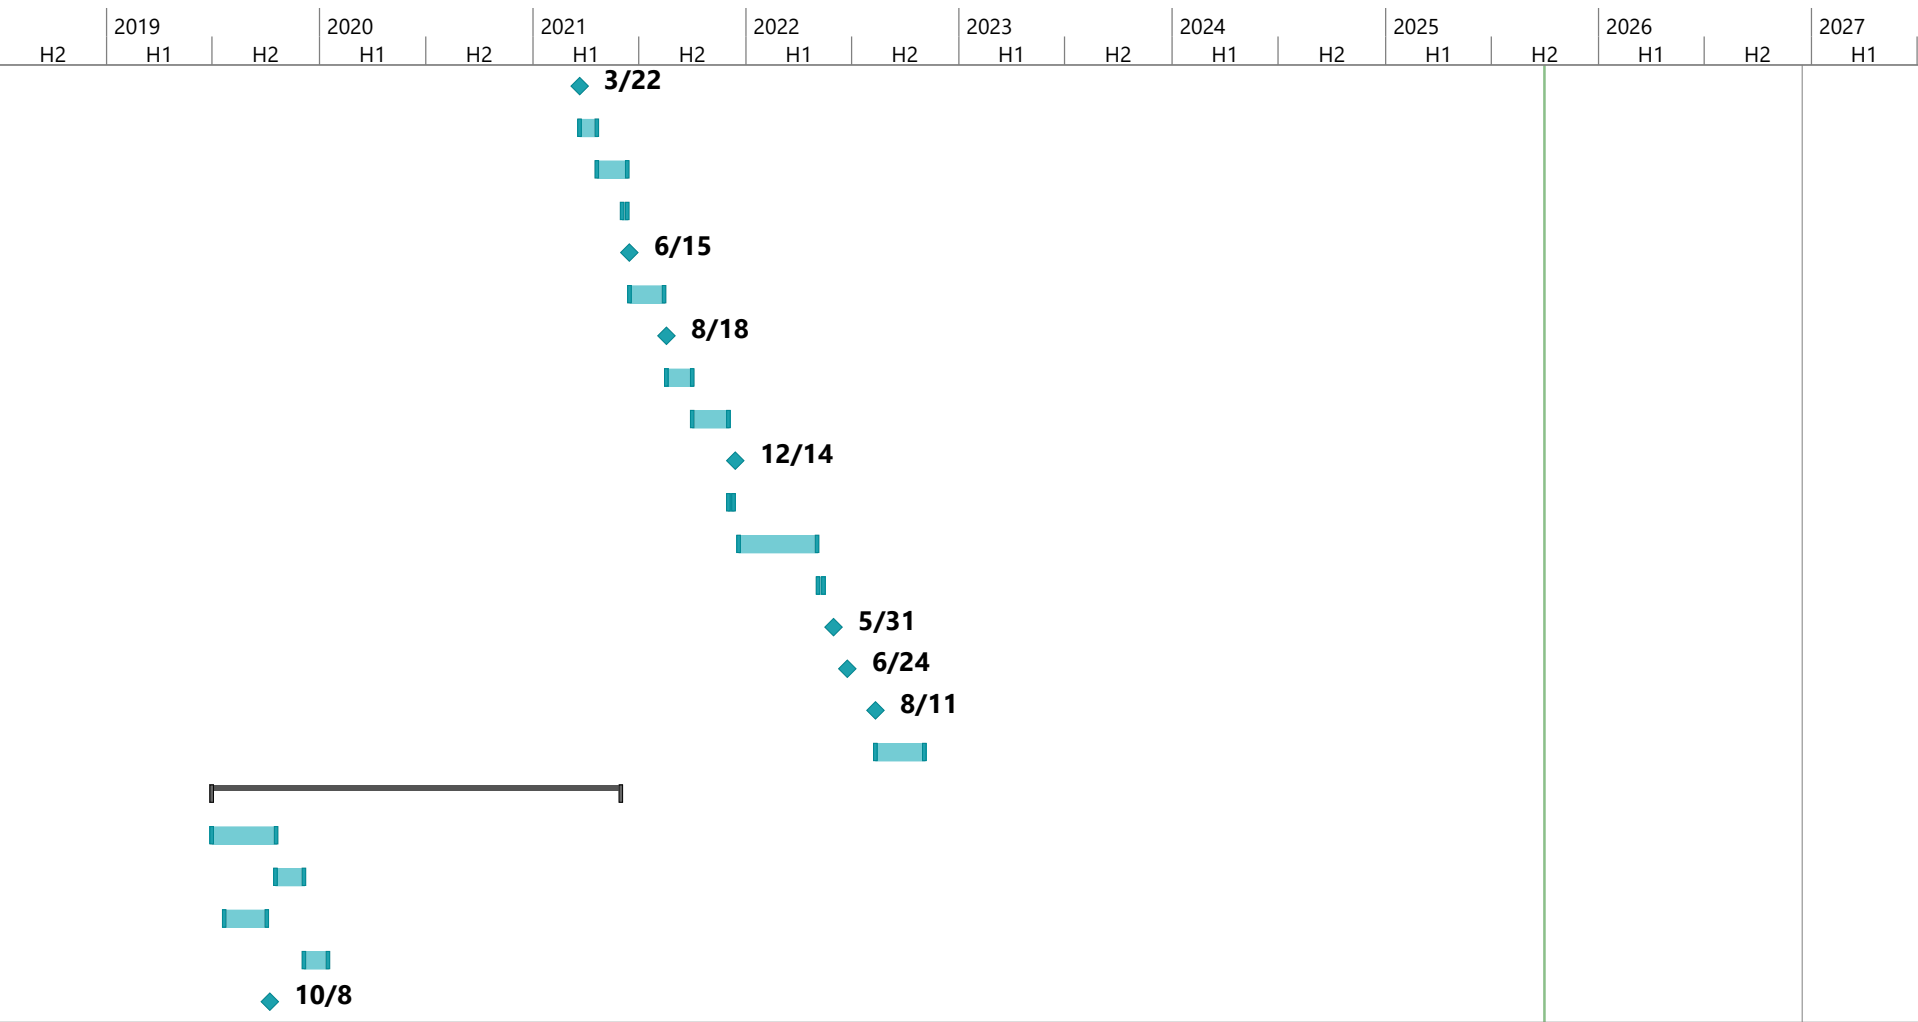
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



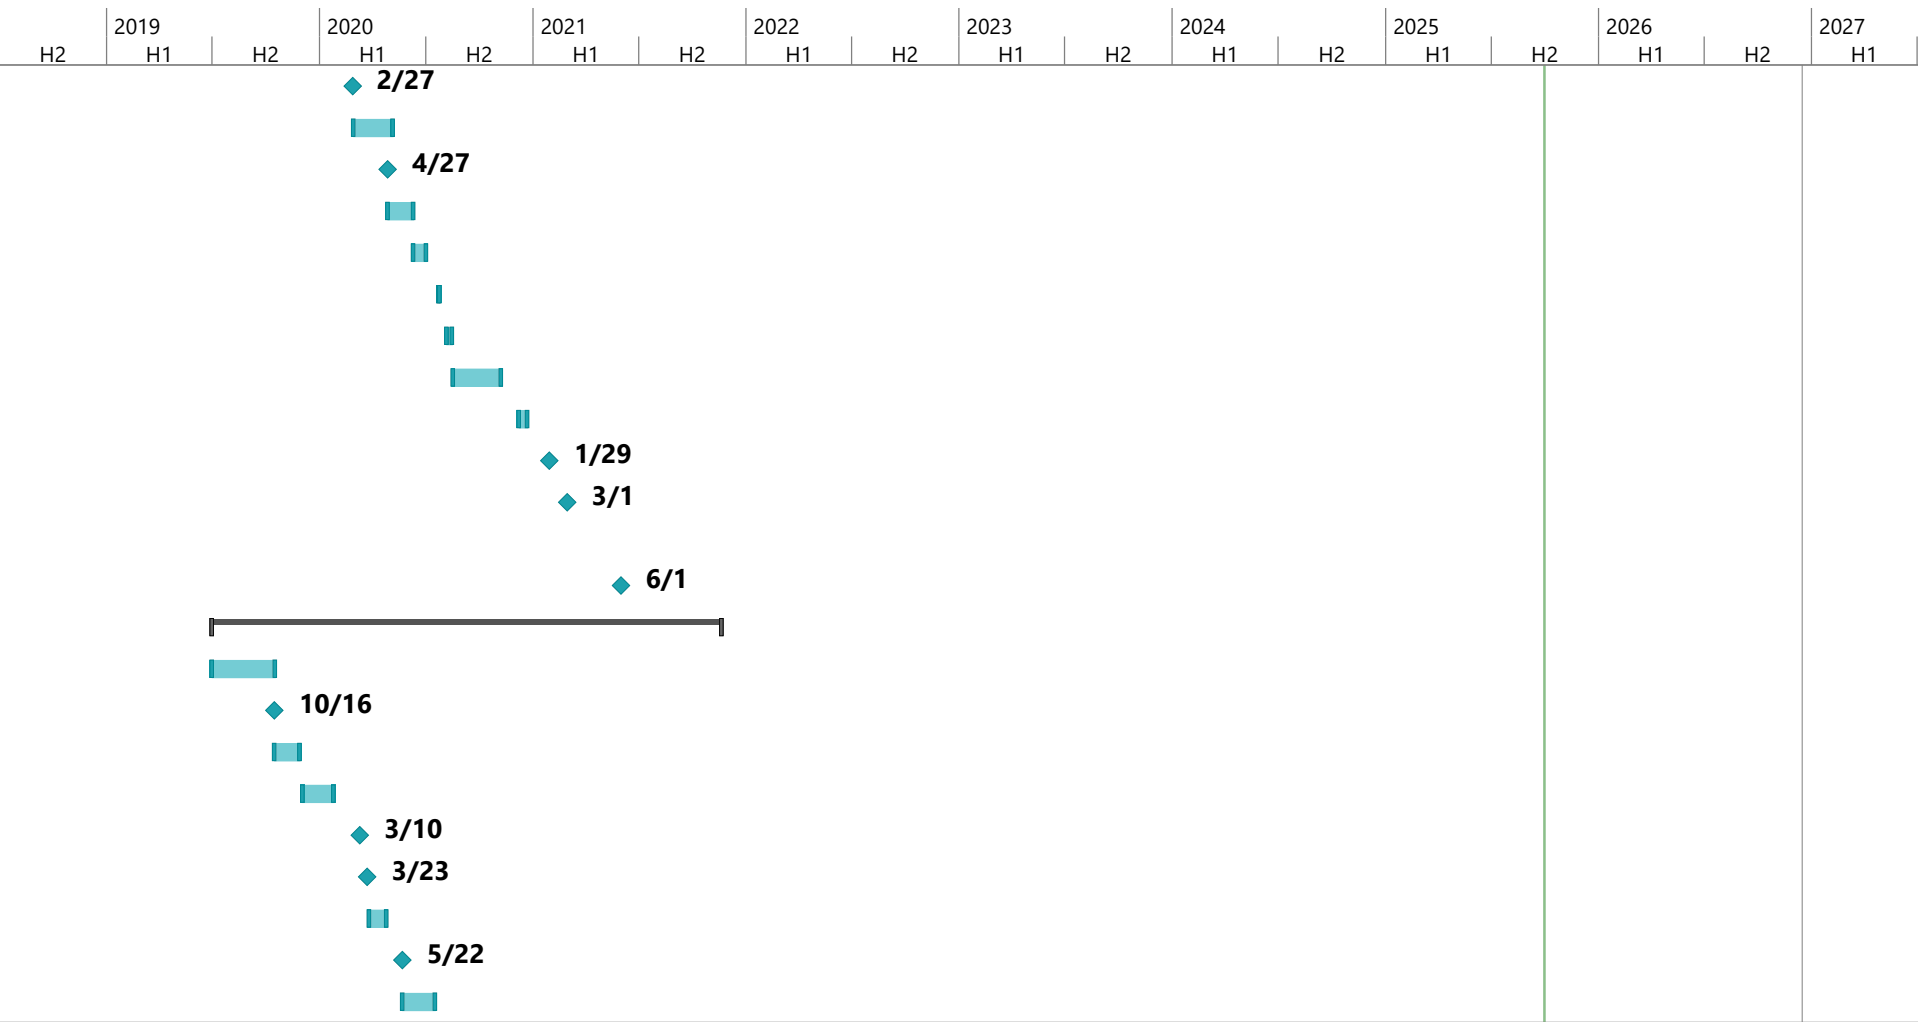
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



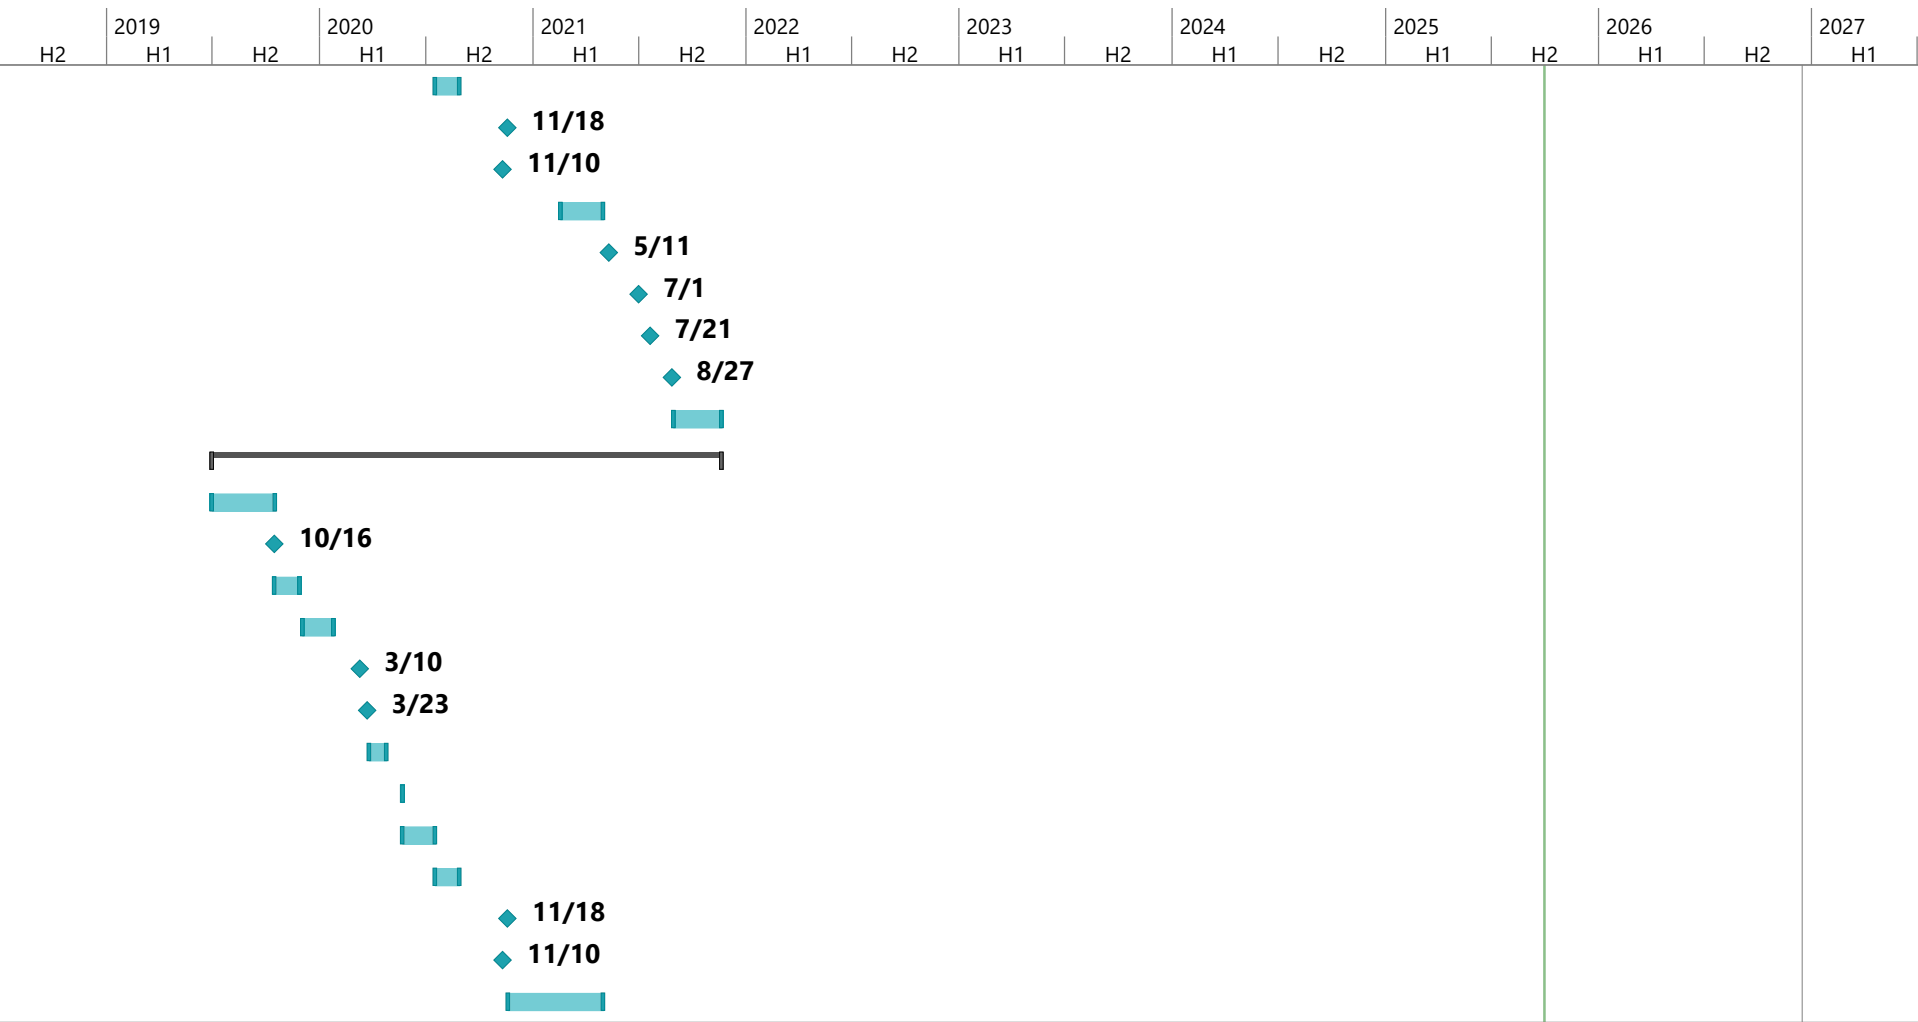
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



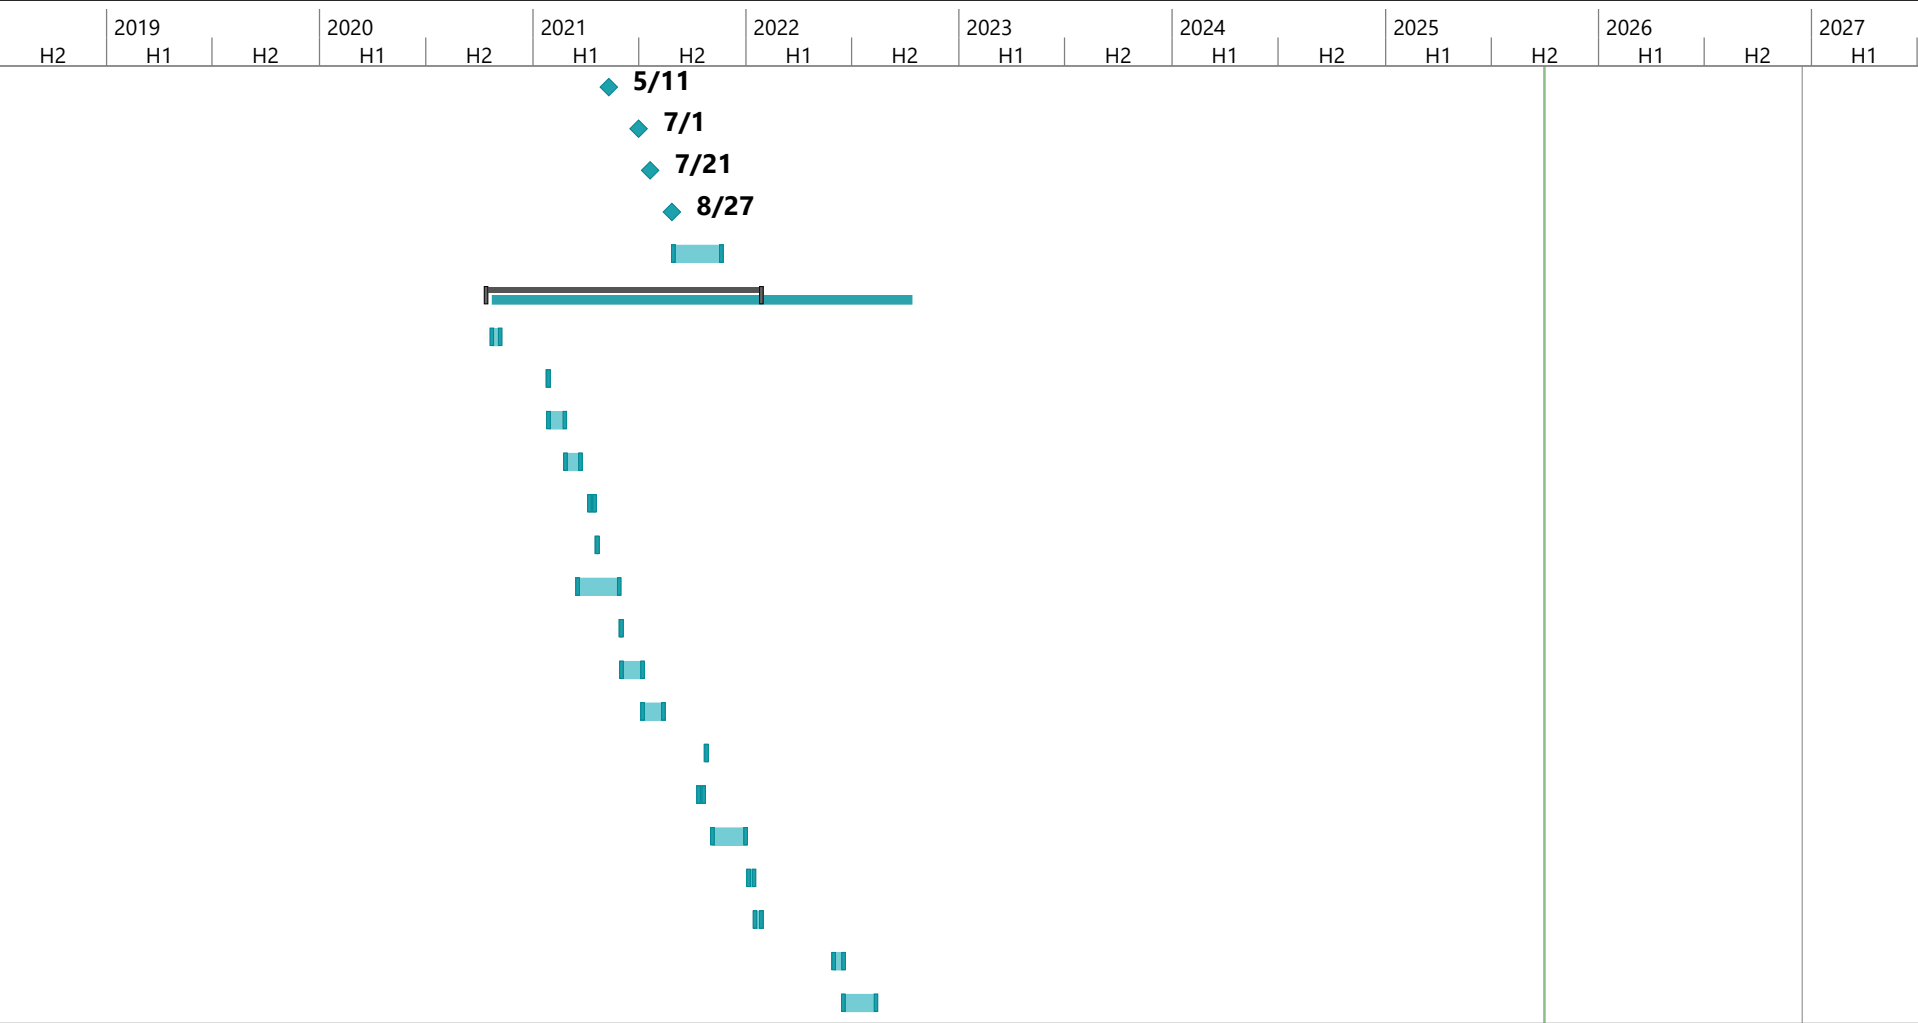
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



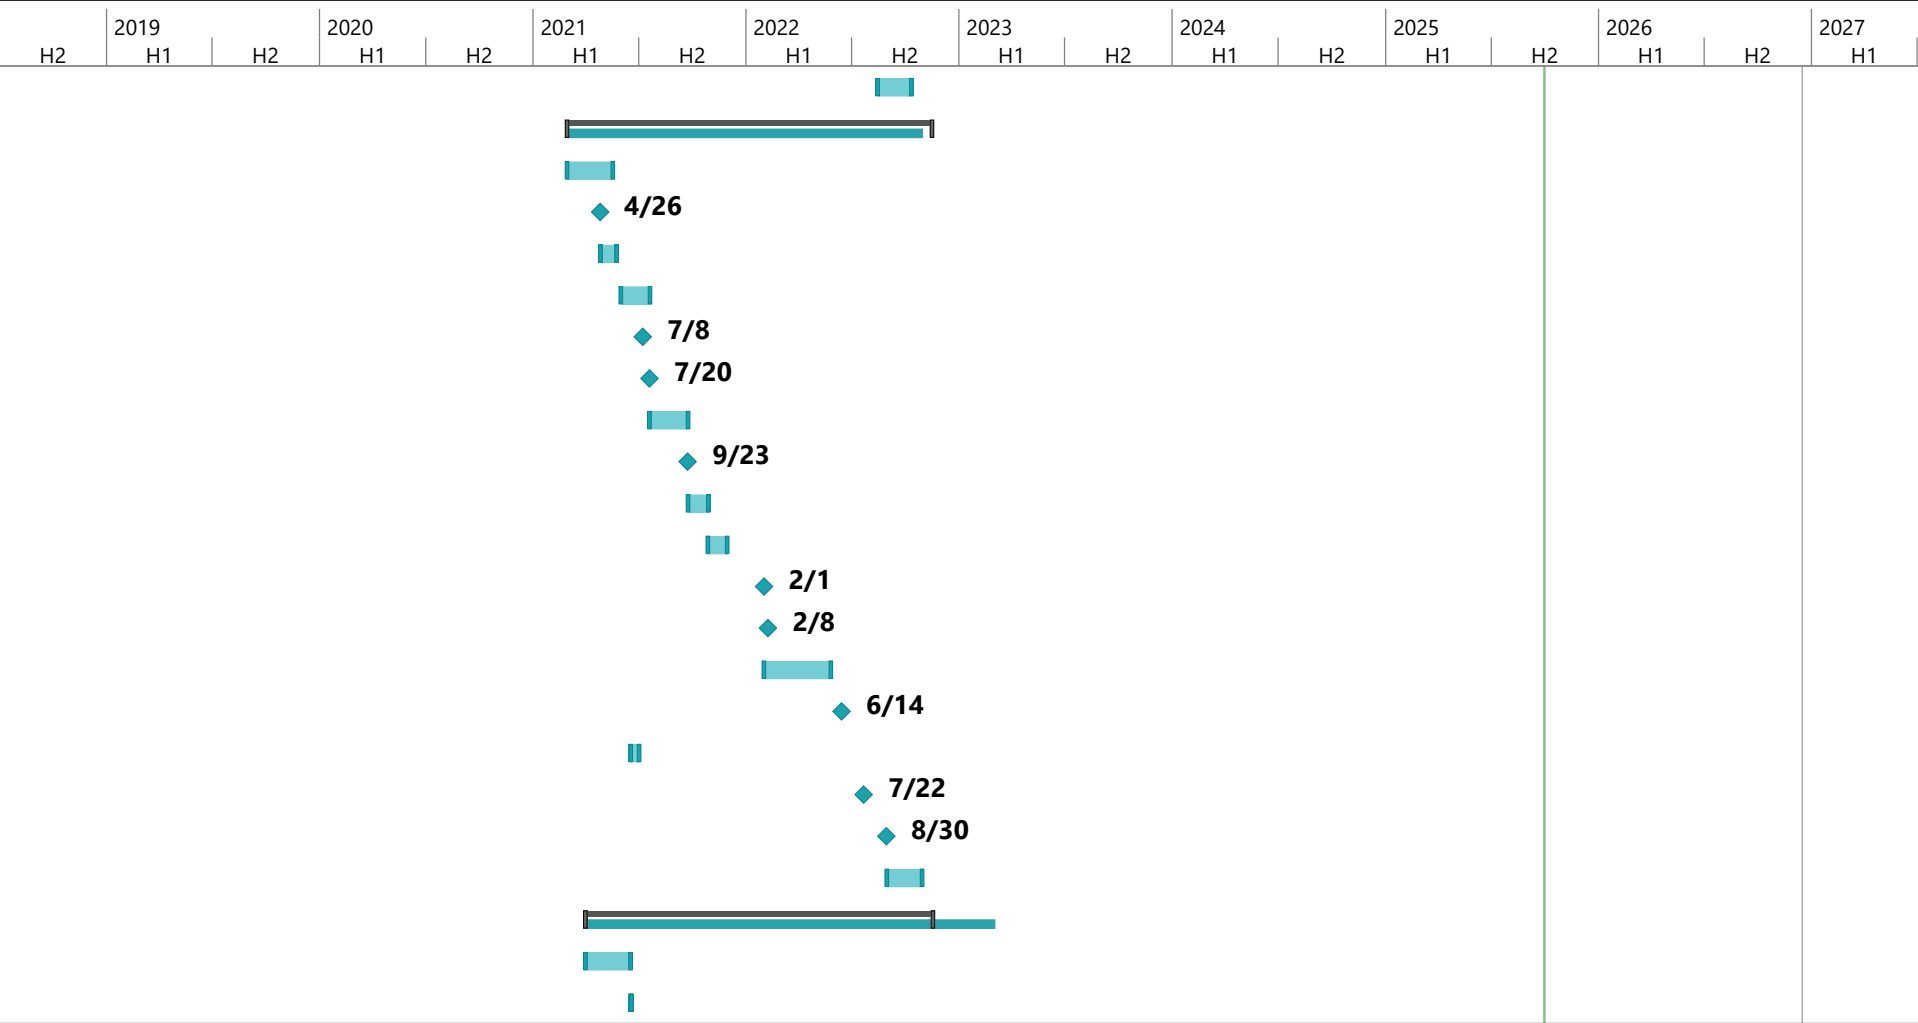
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



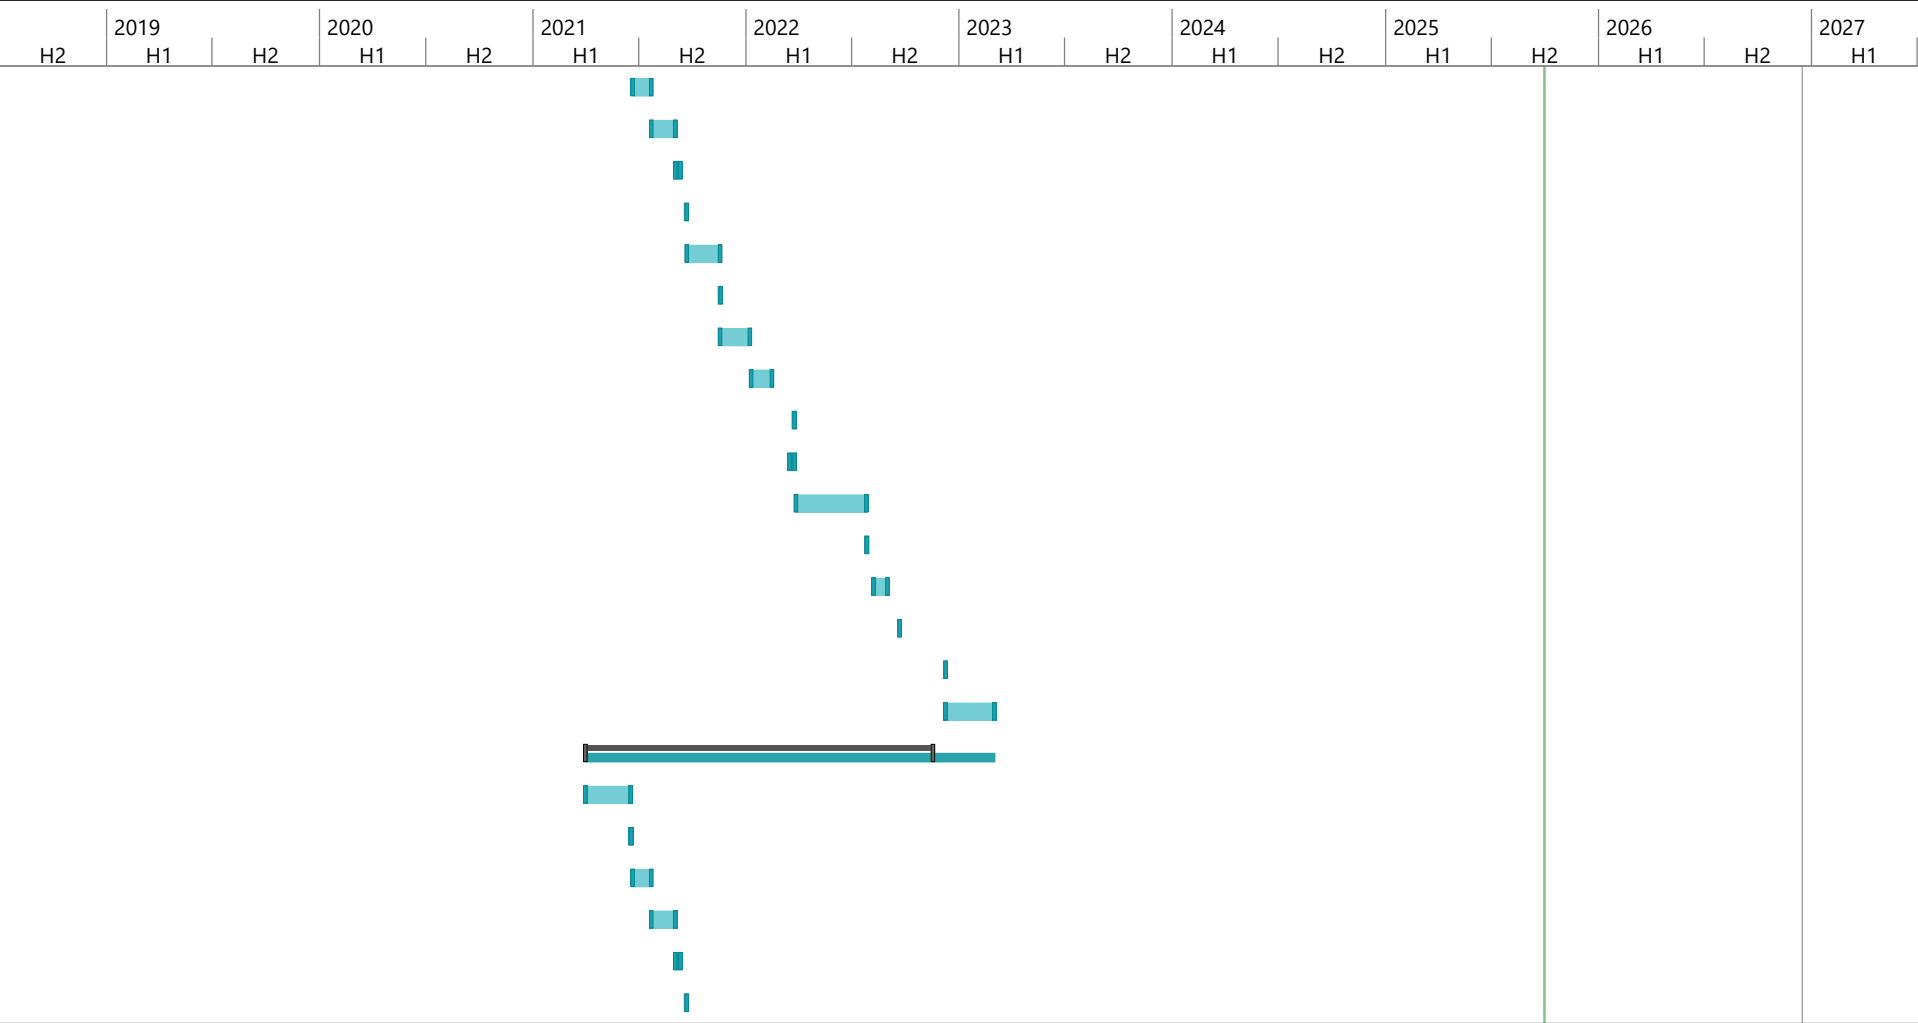
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

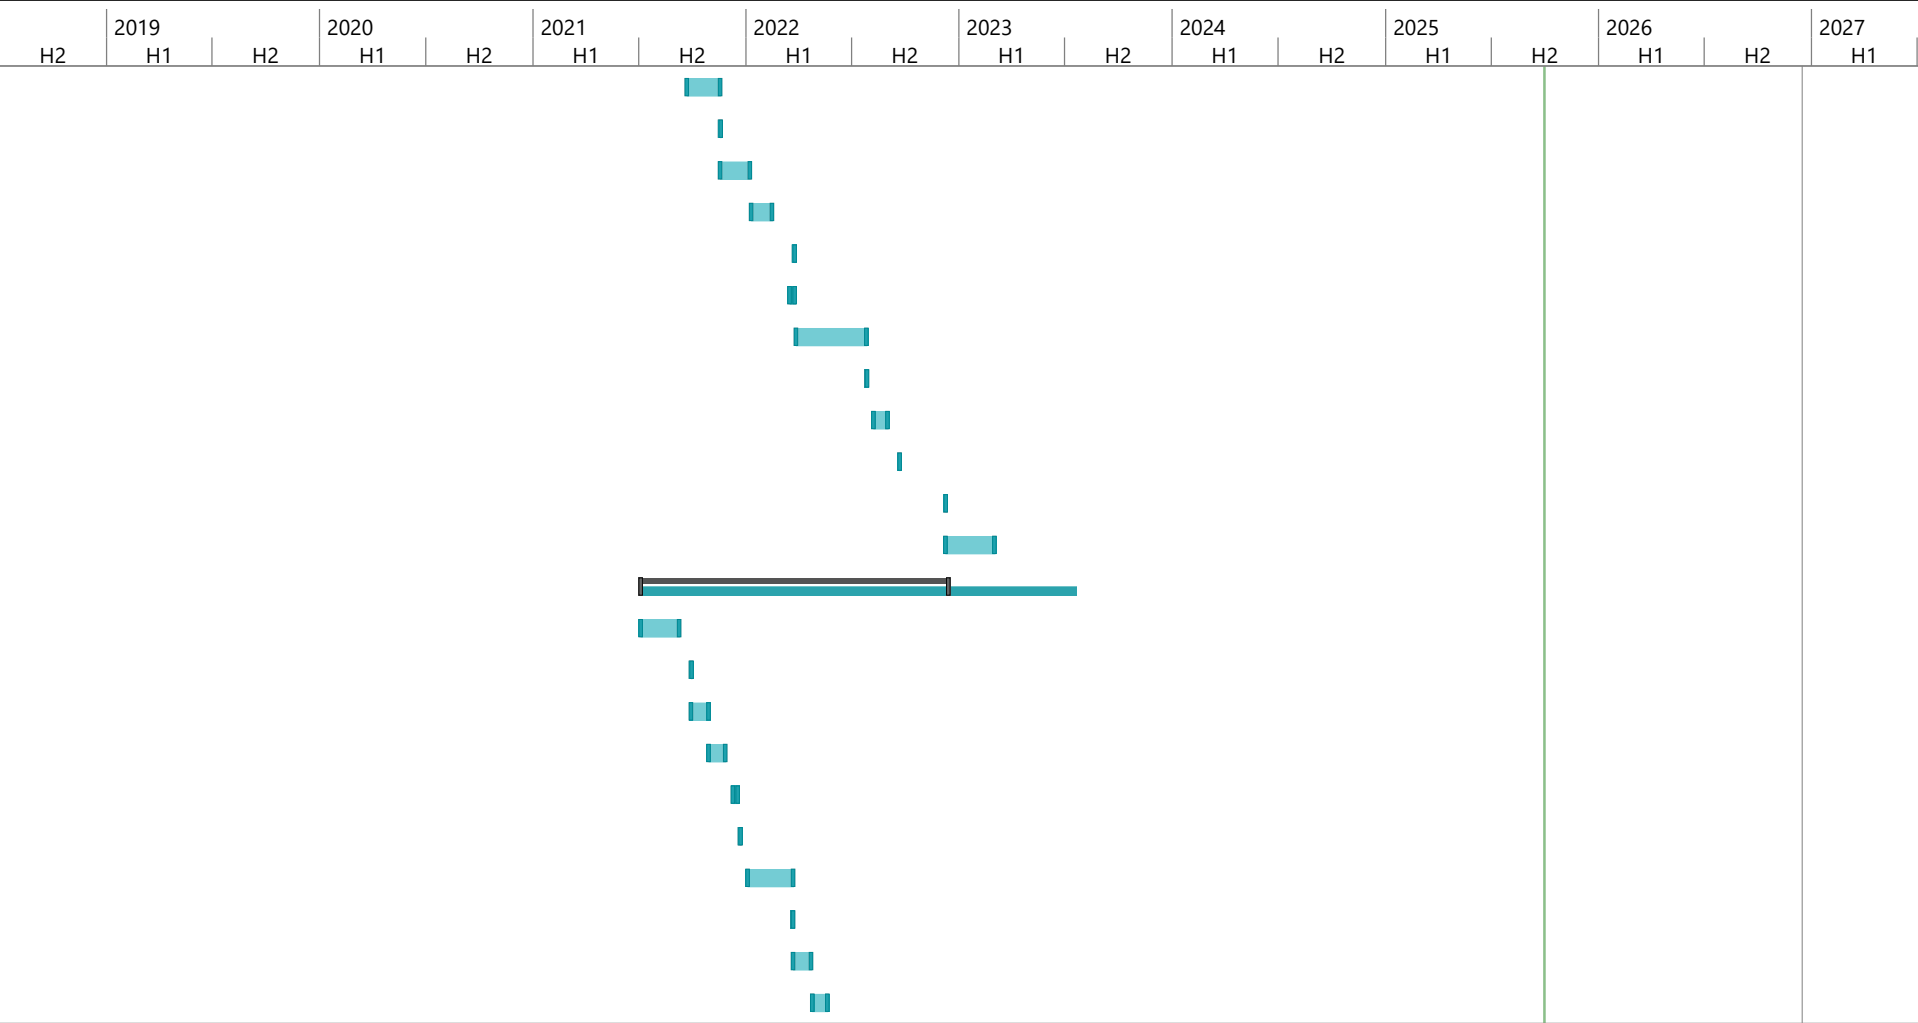


Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

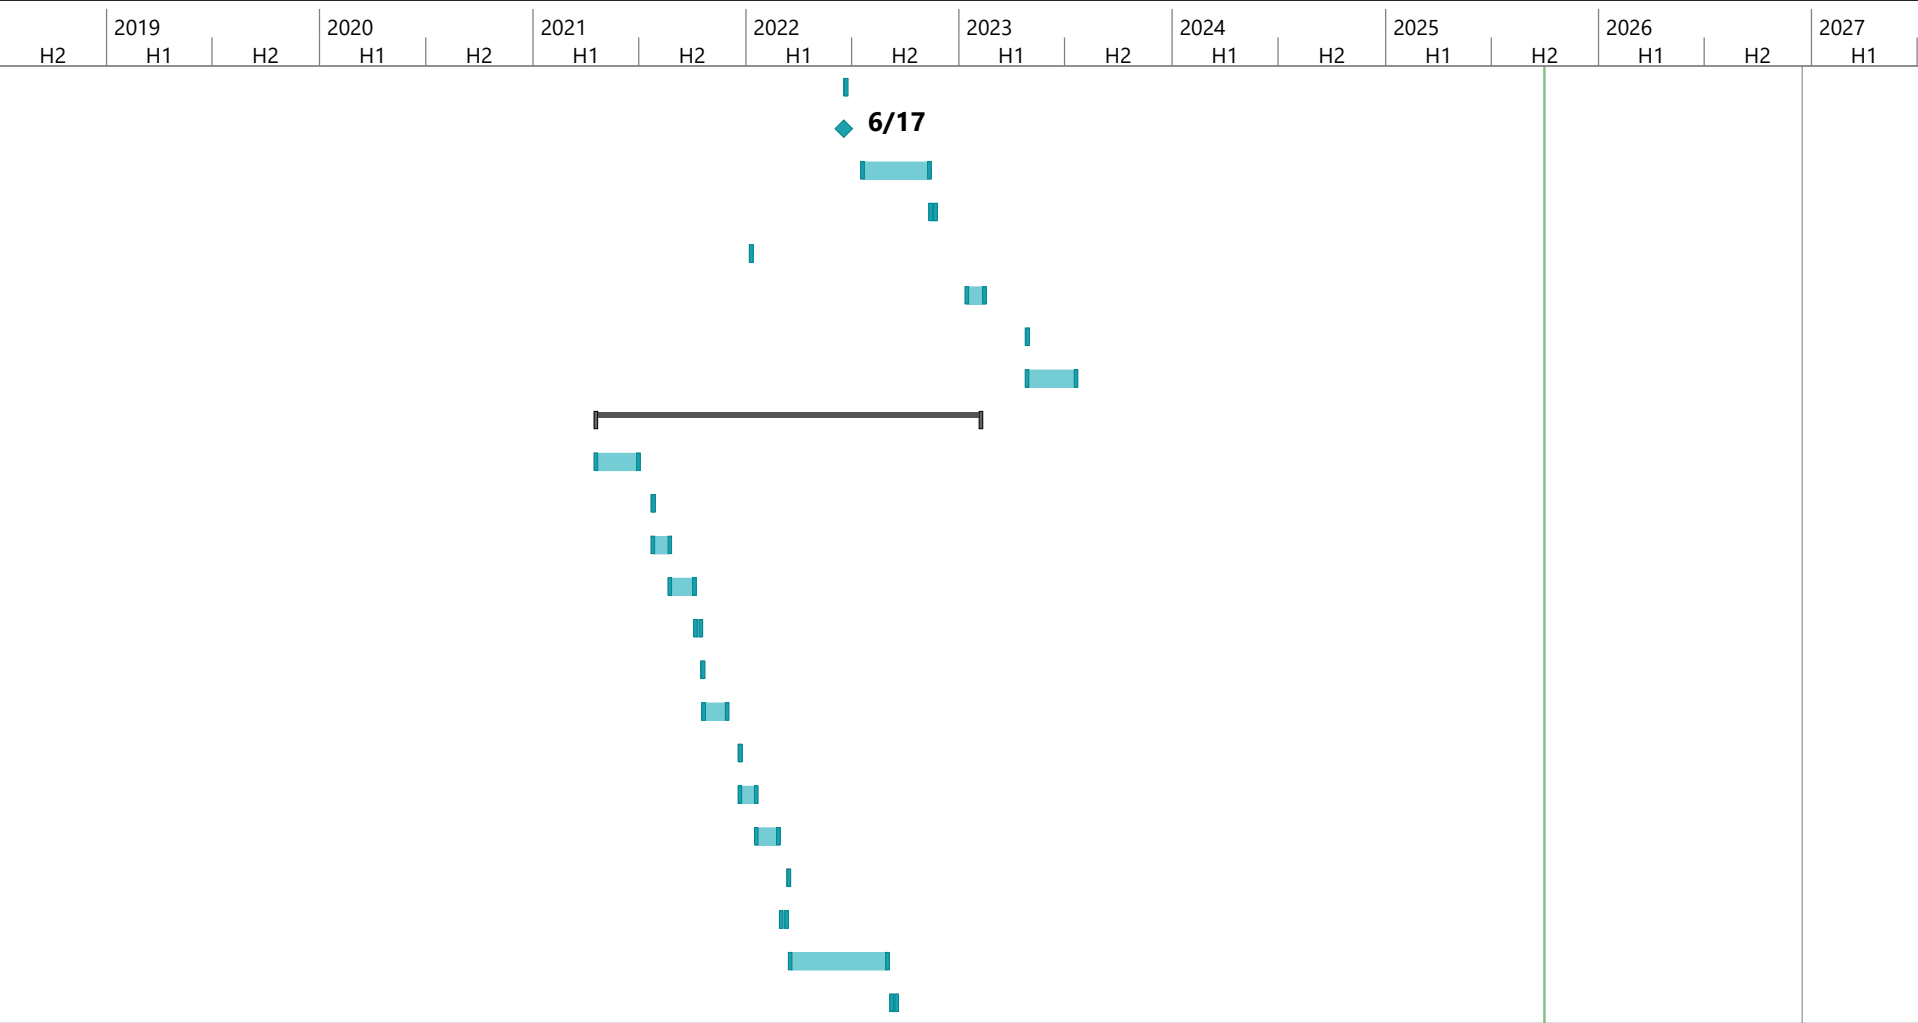


Project: IOU Master Task Timeli
Date: Tue 9/30/25

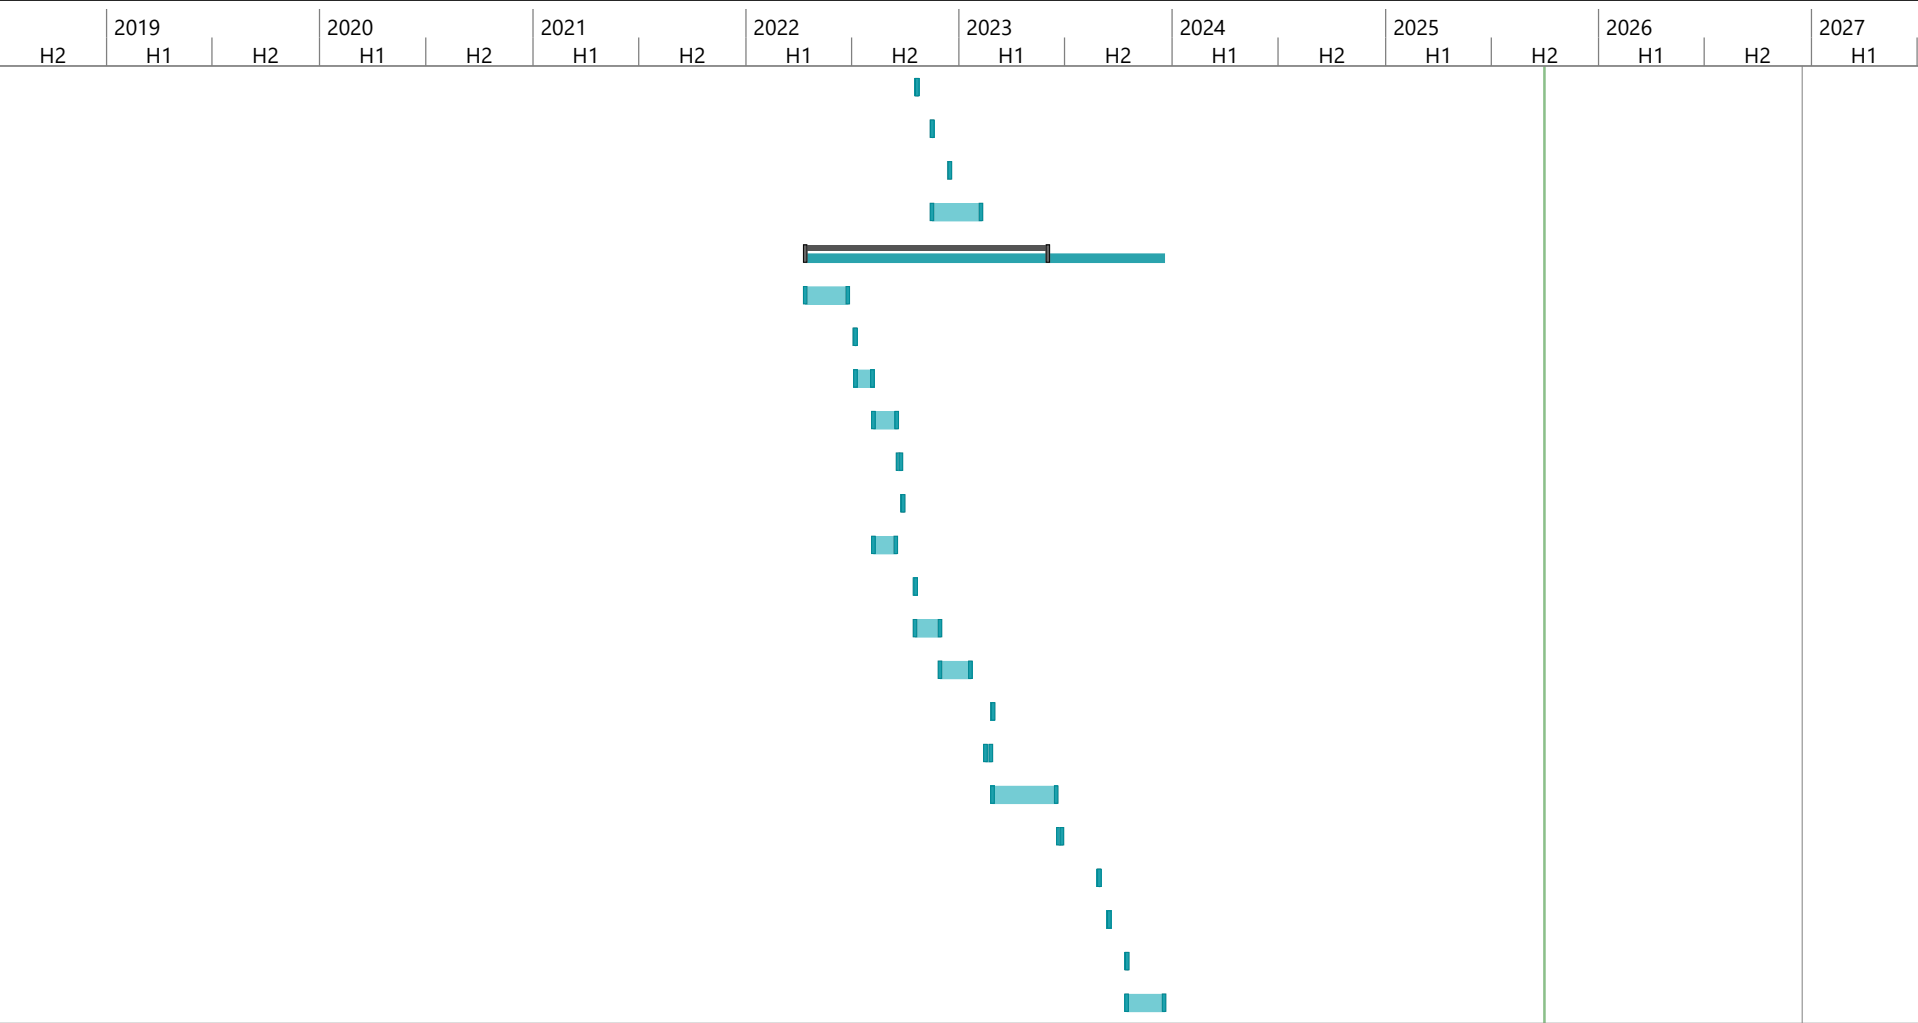
Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




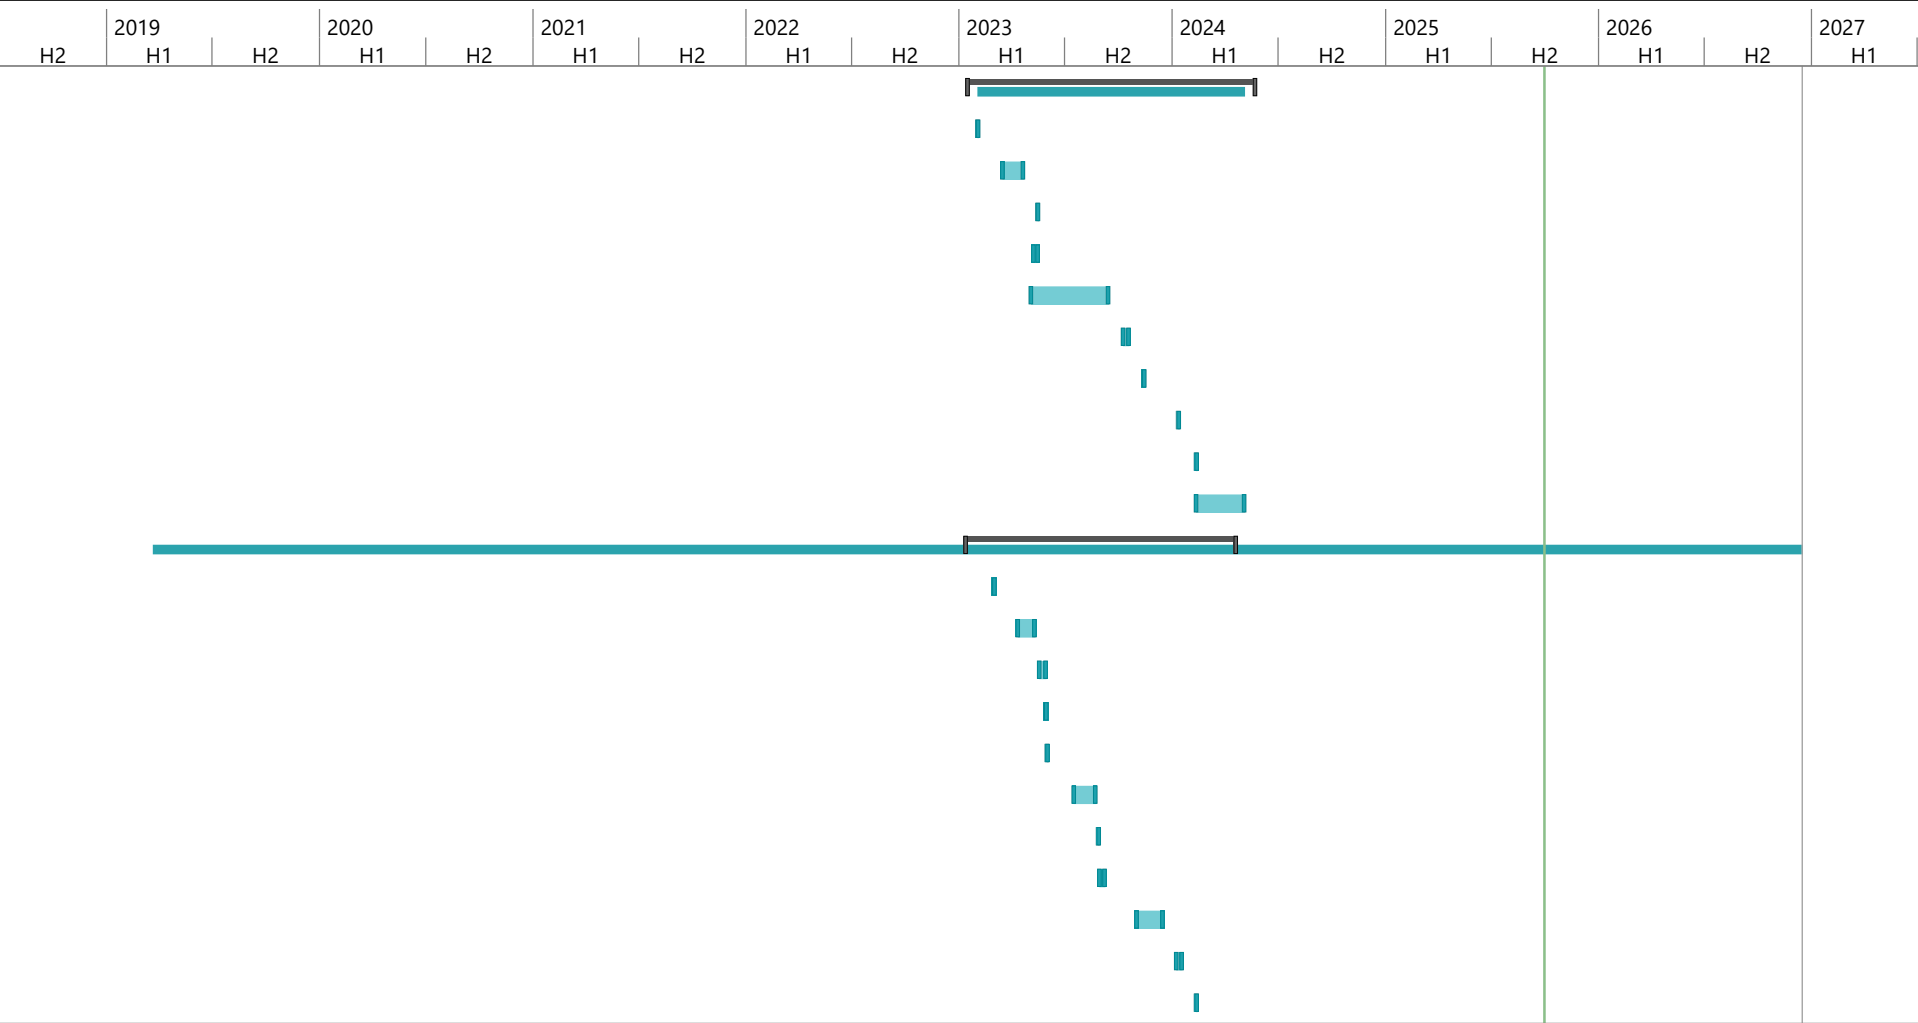
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



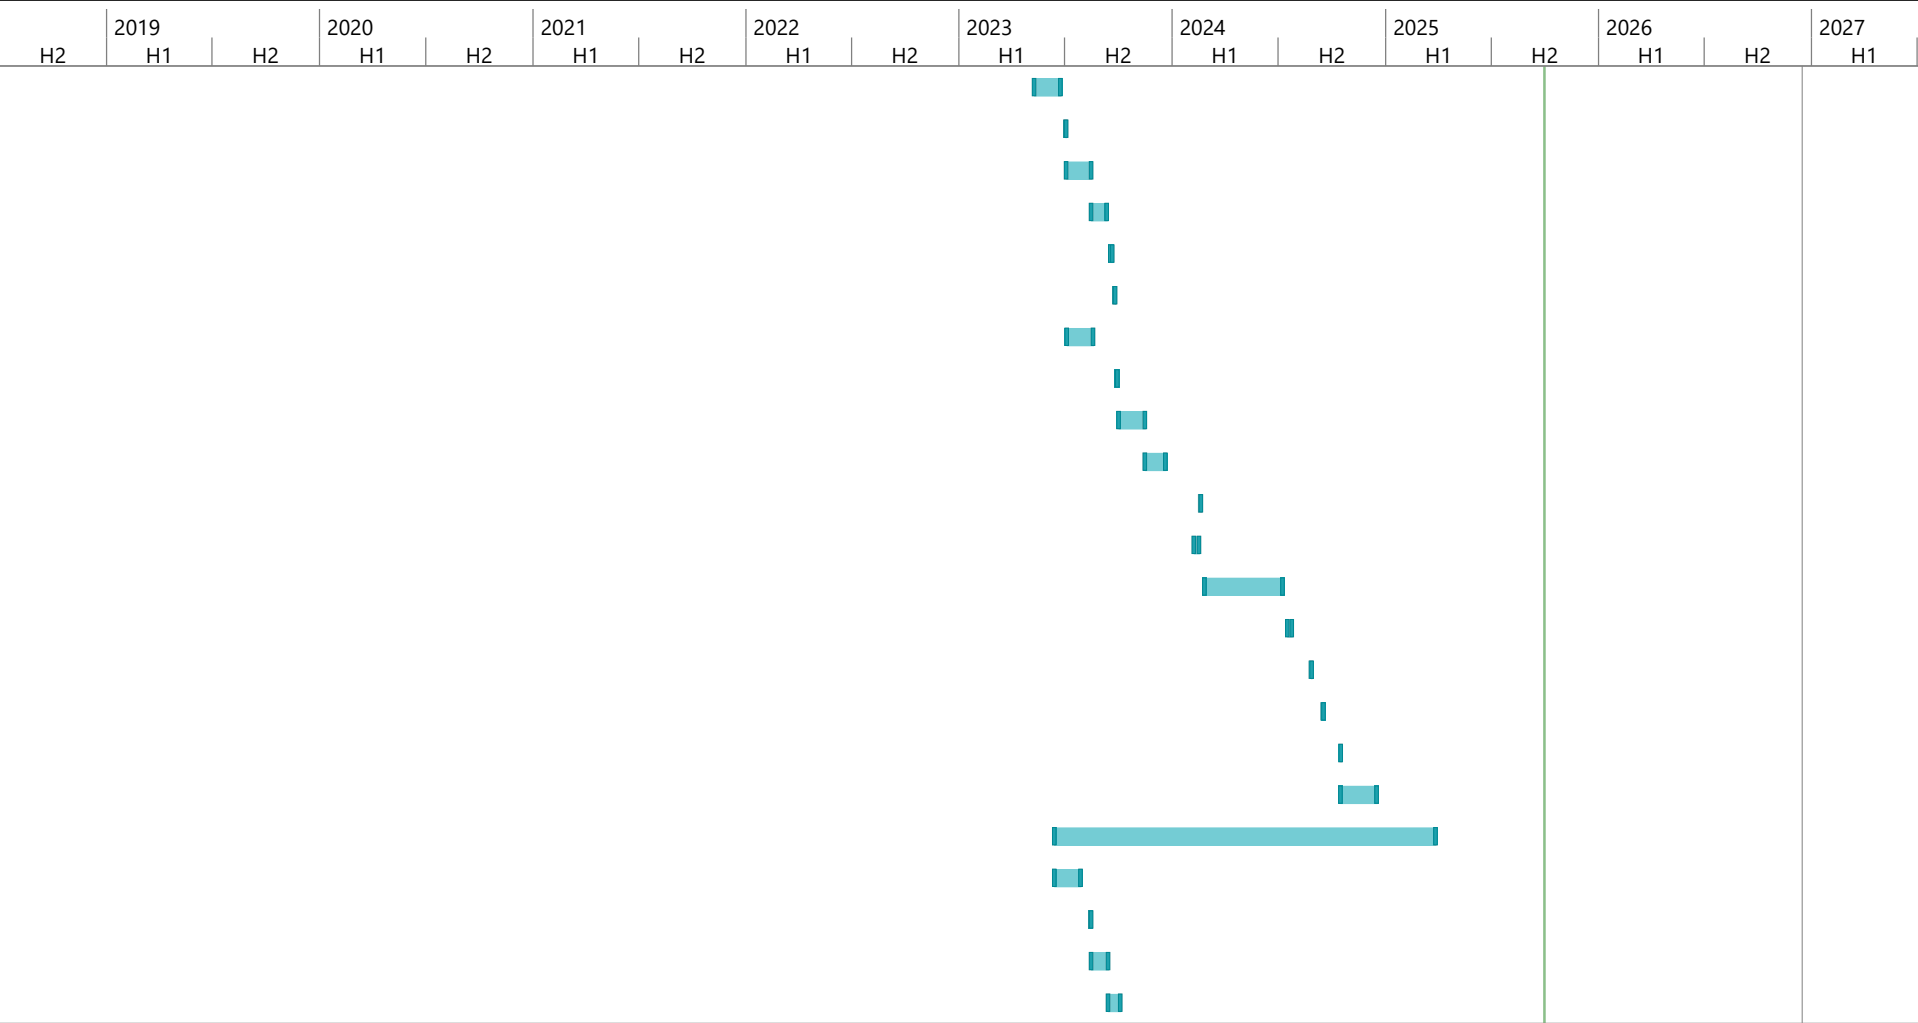
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



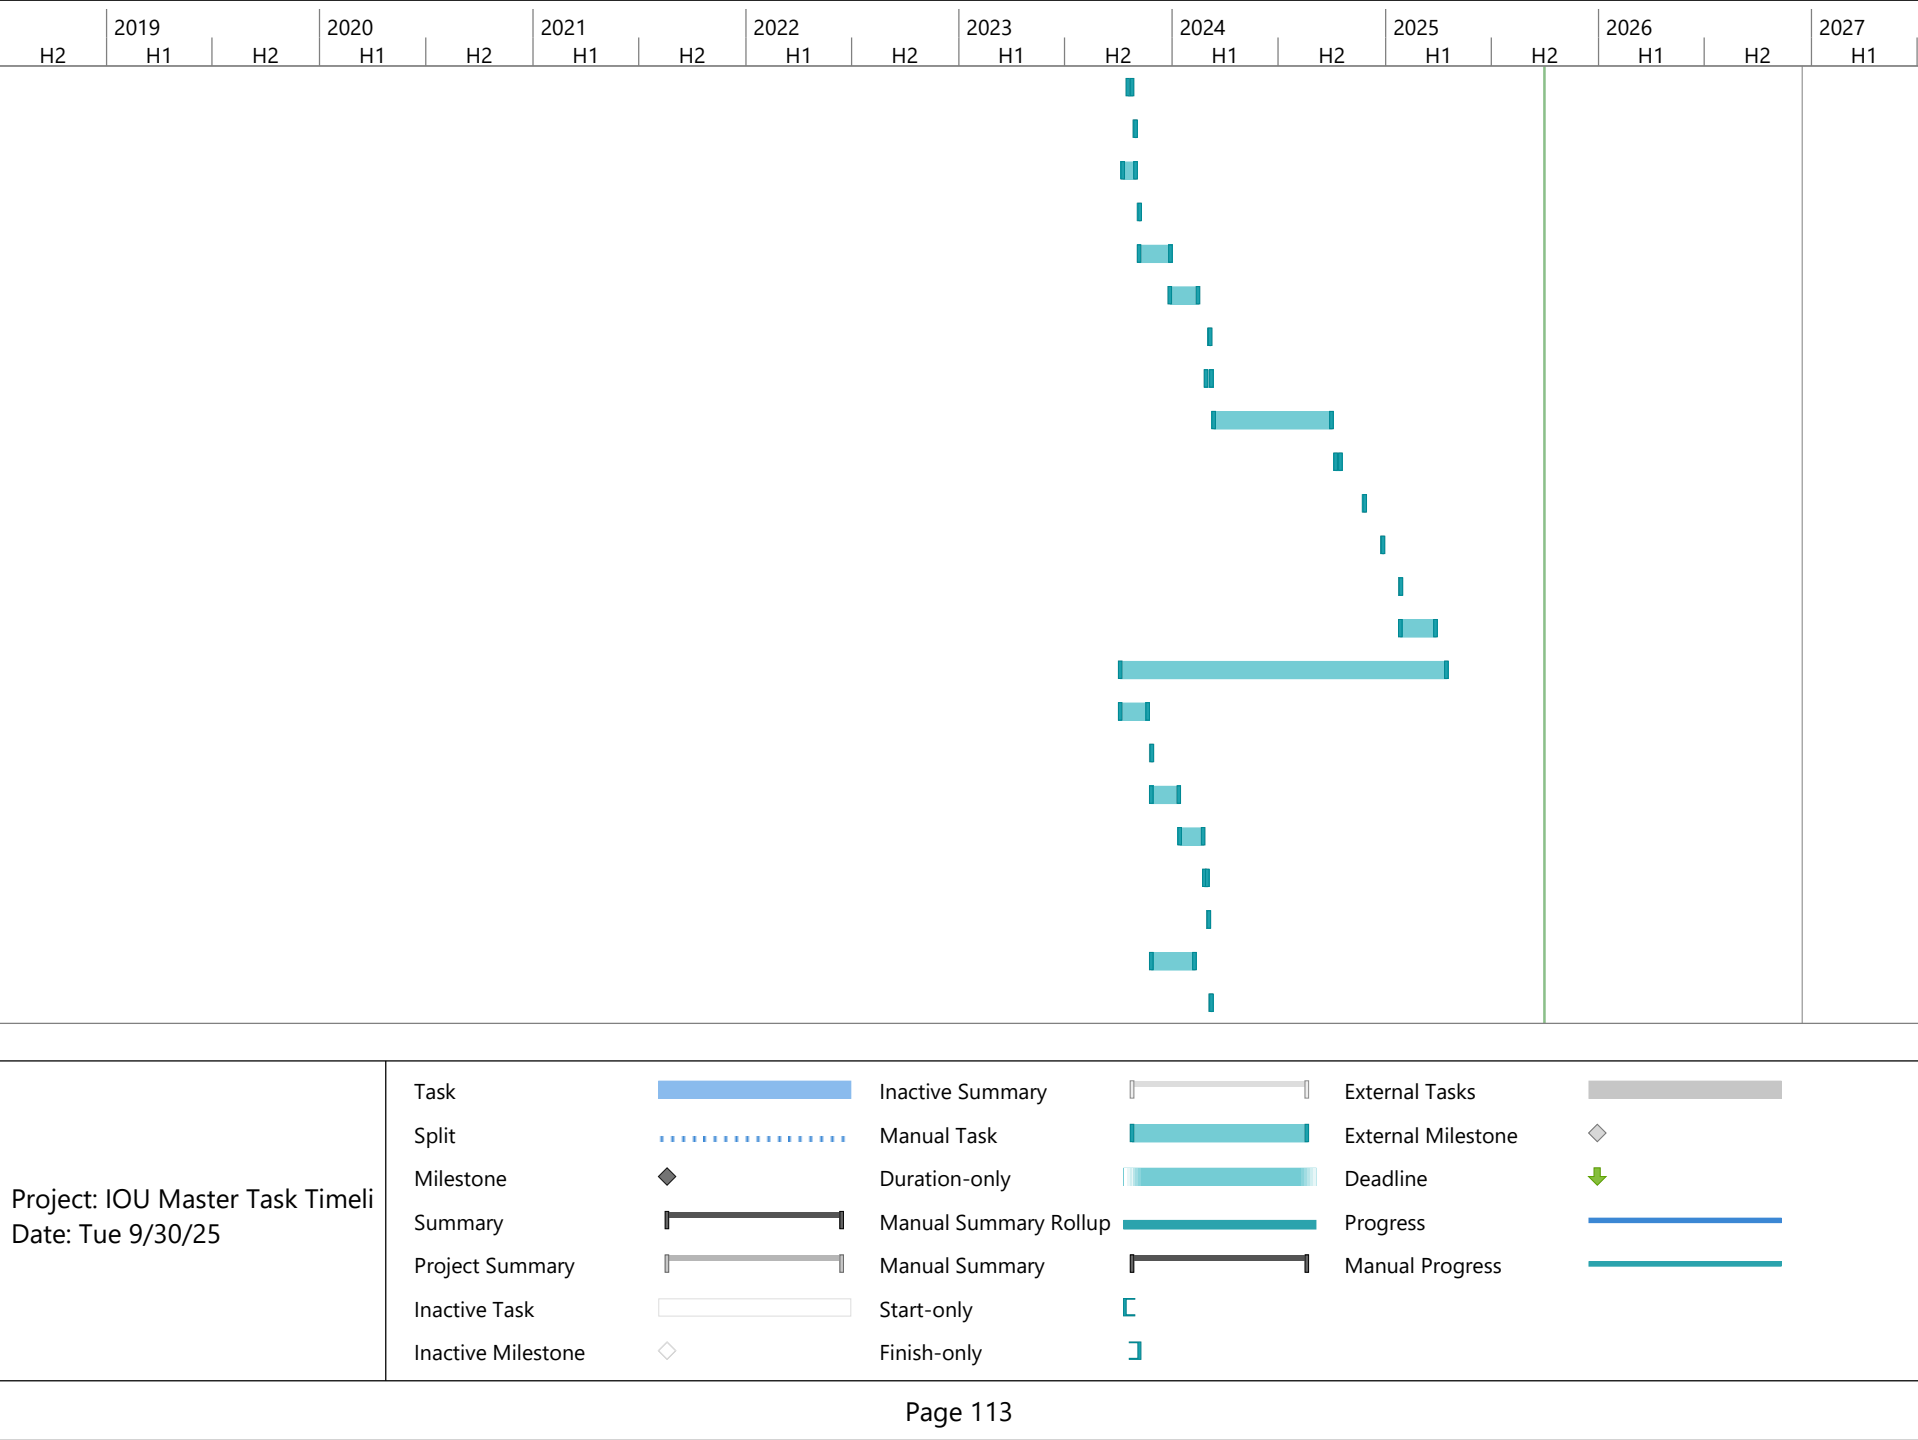
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

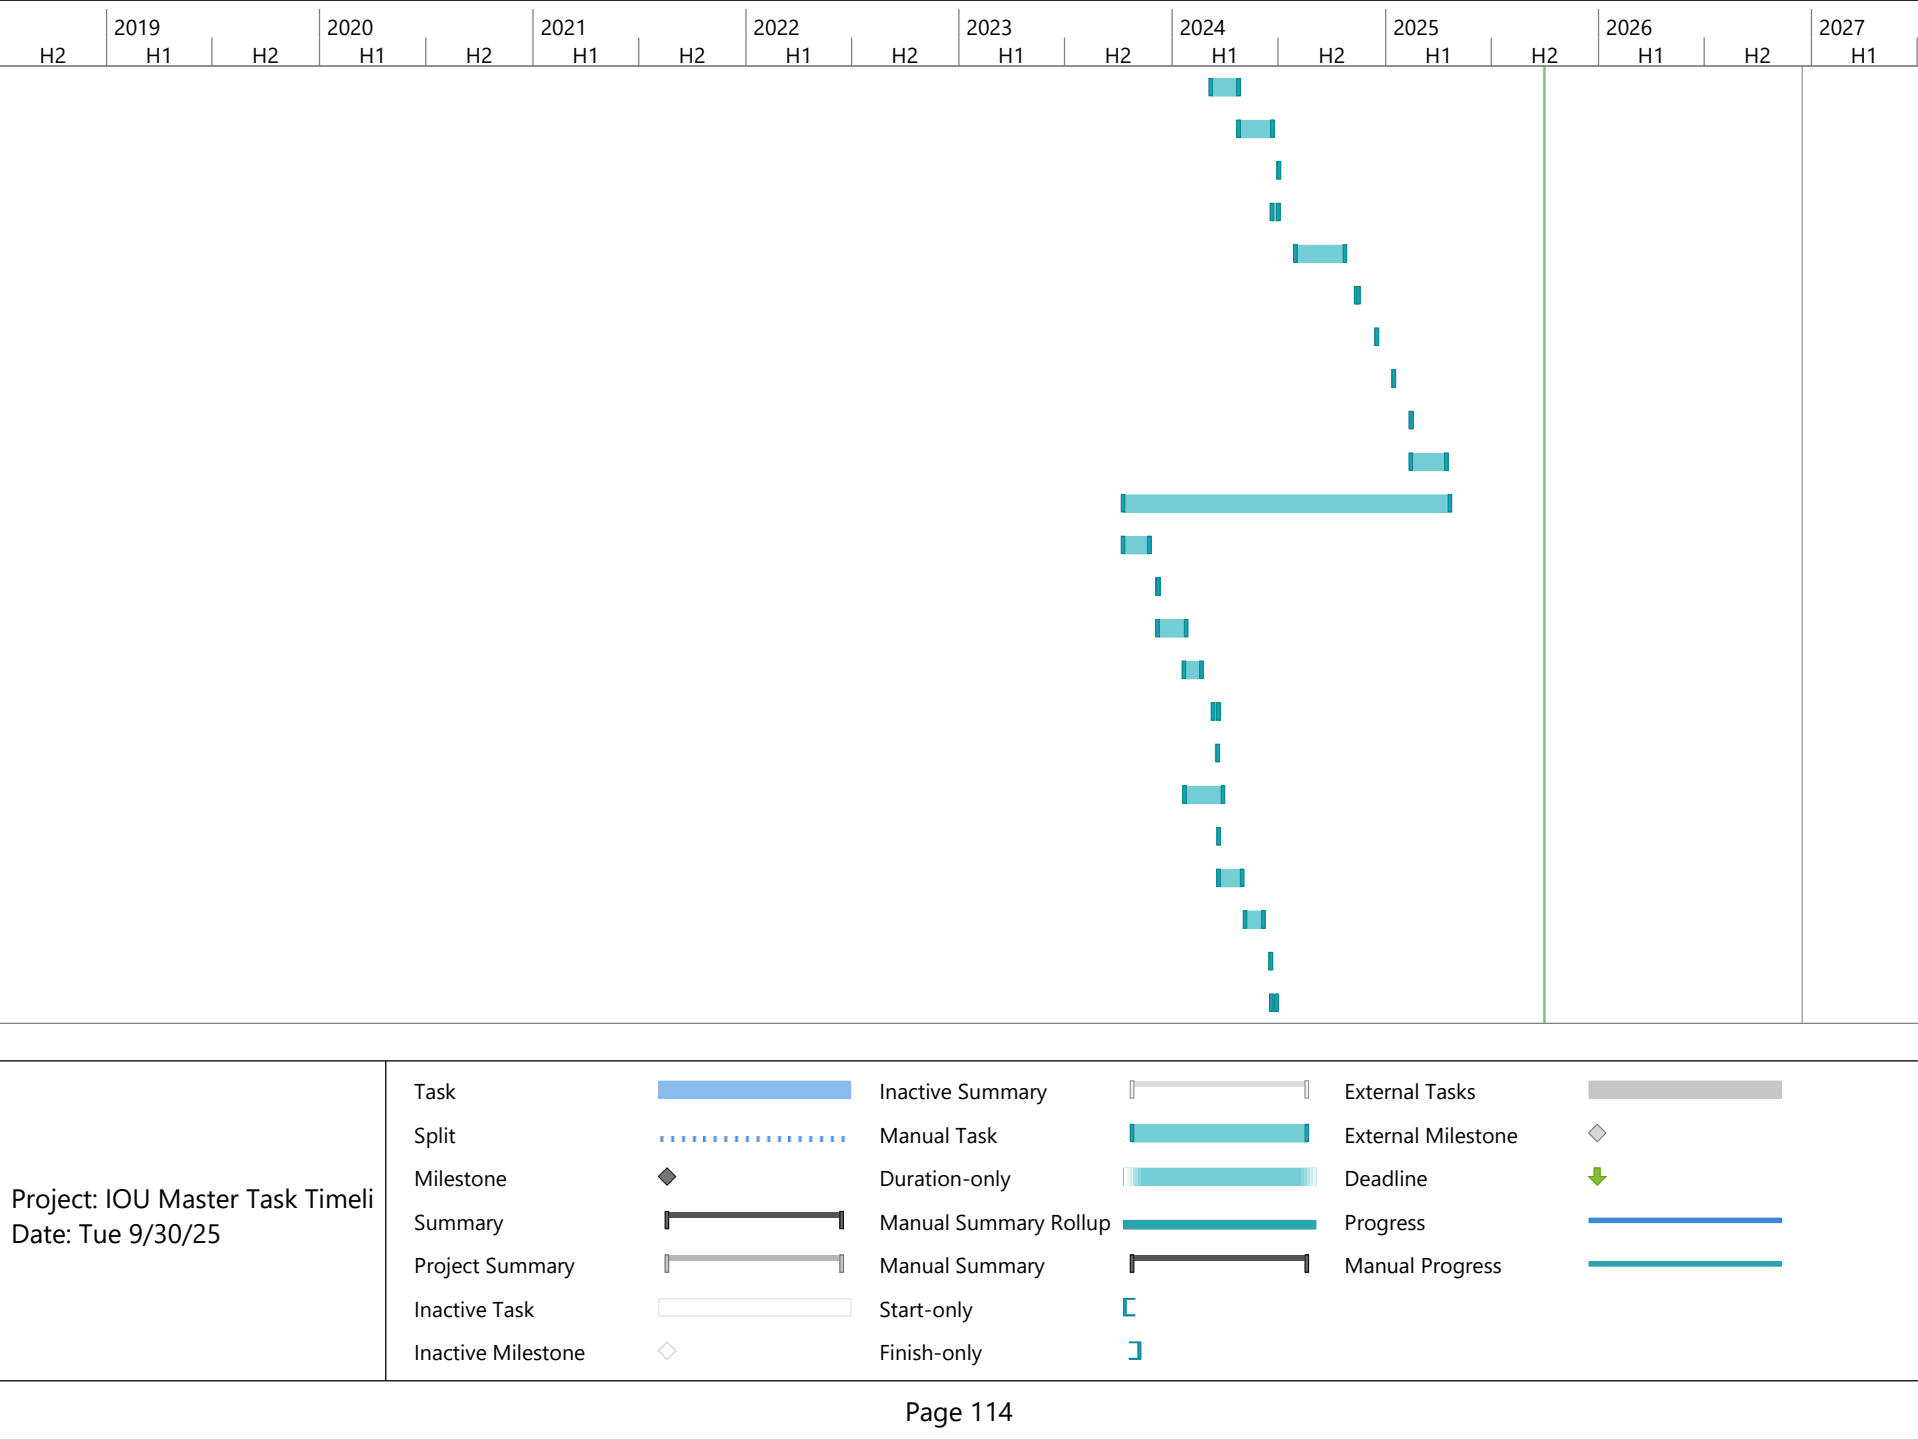


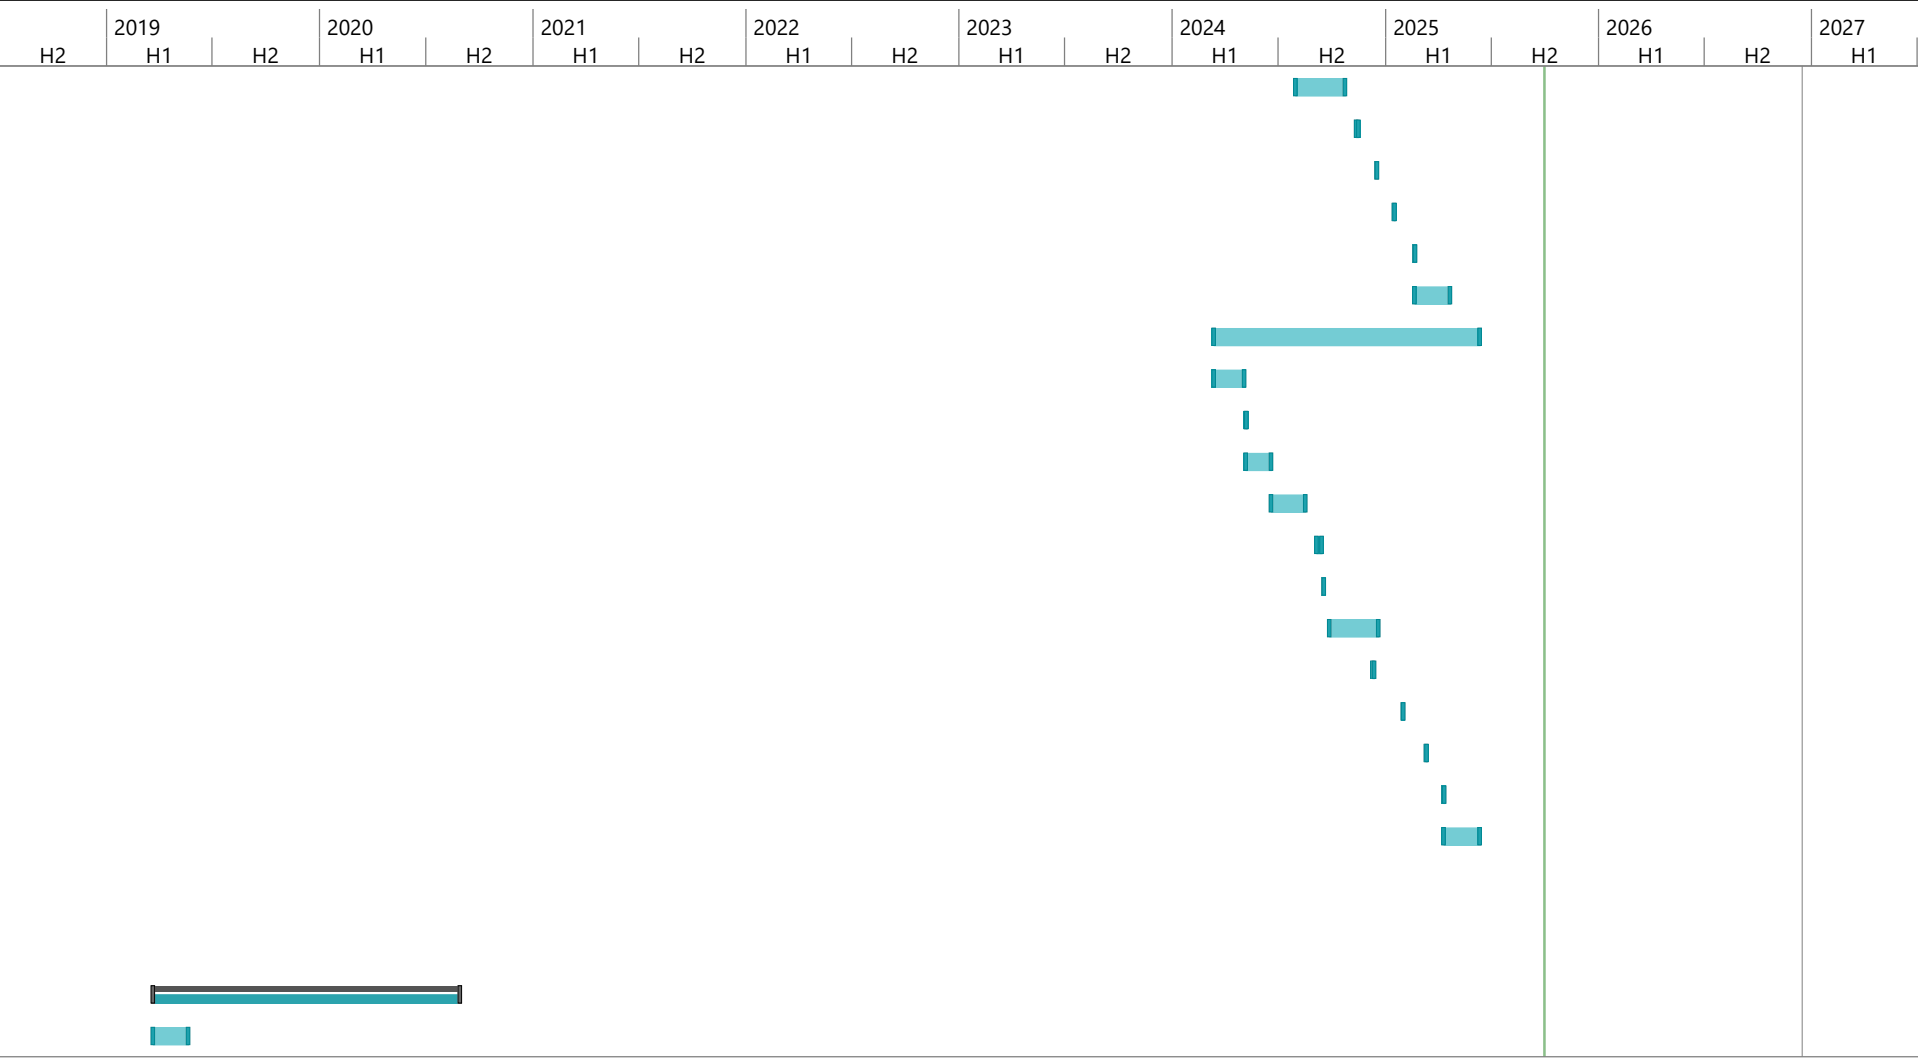
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



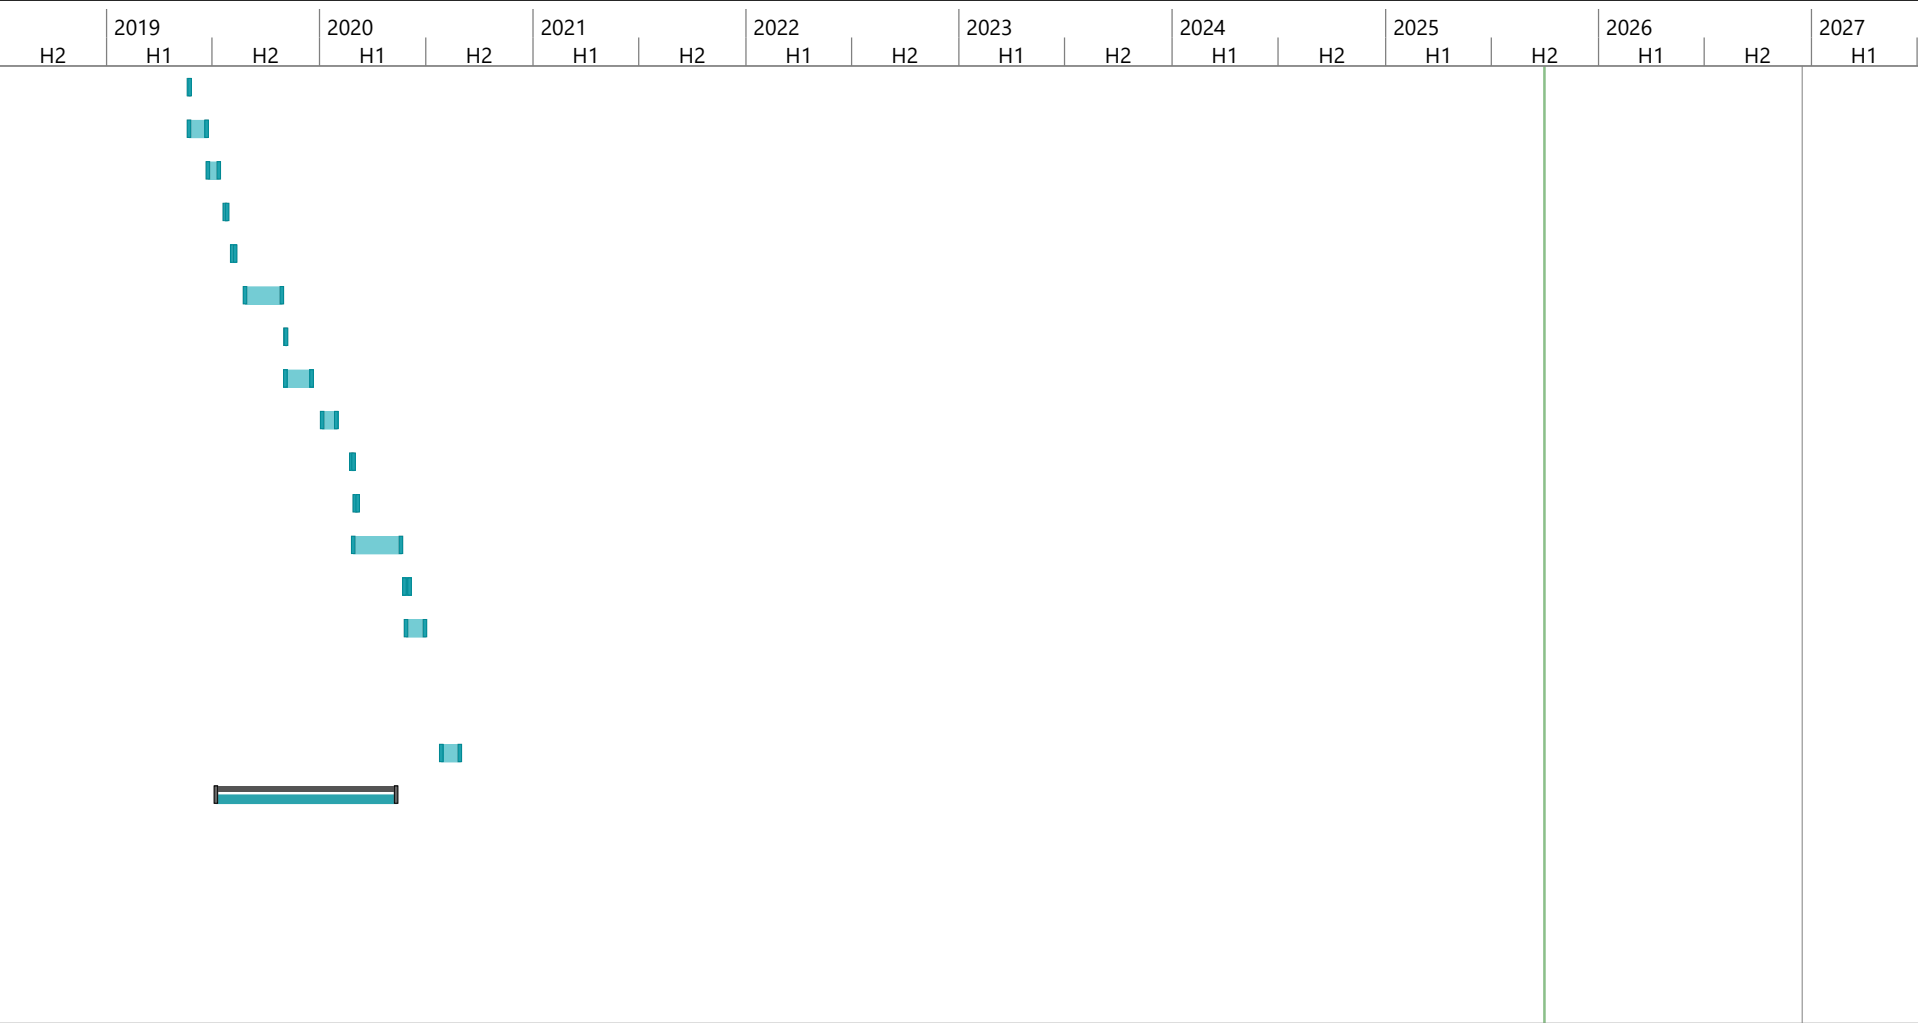
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



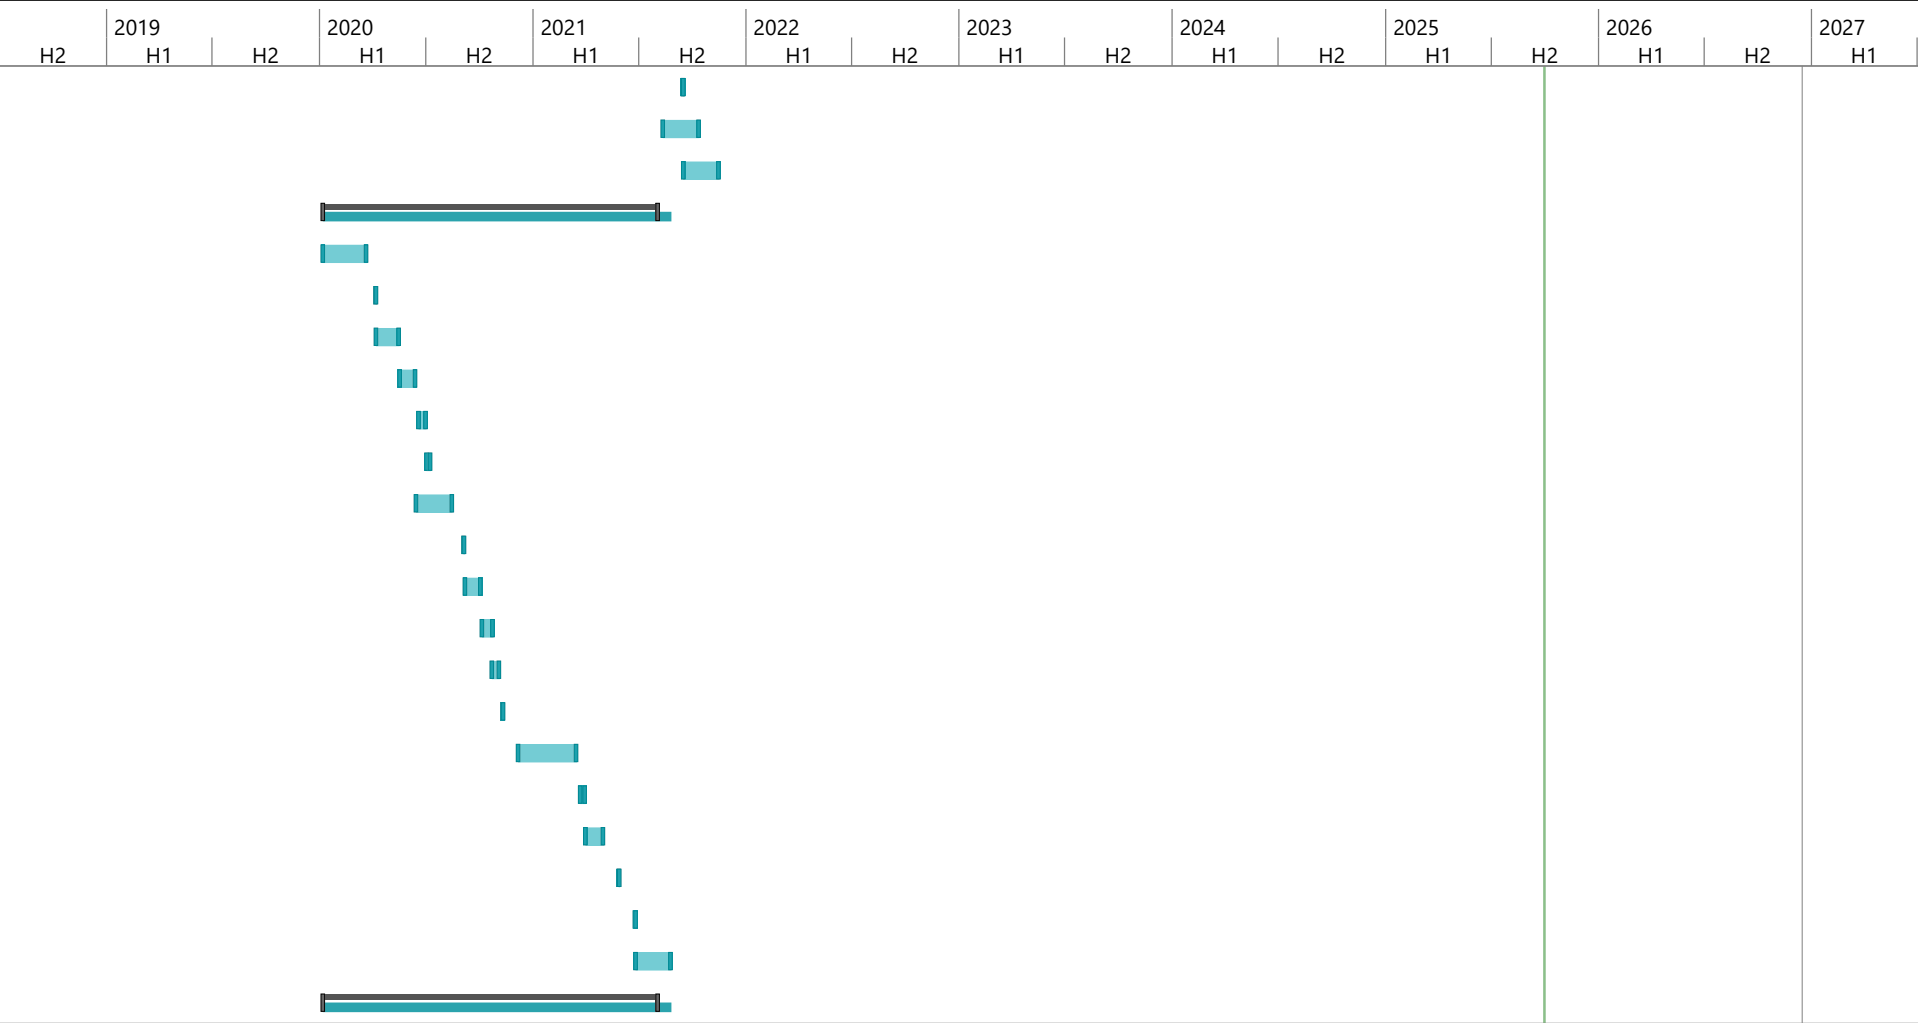




Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

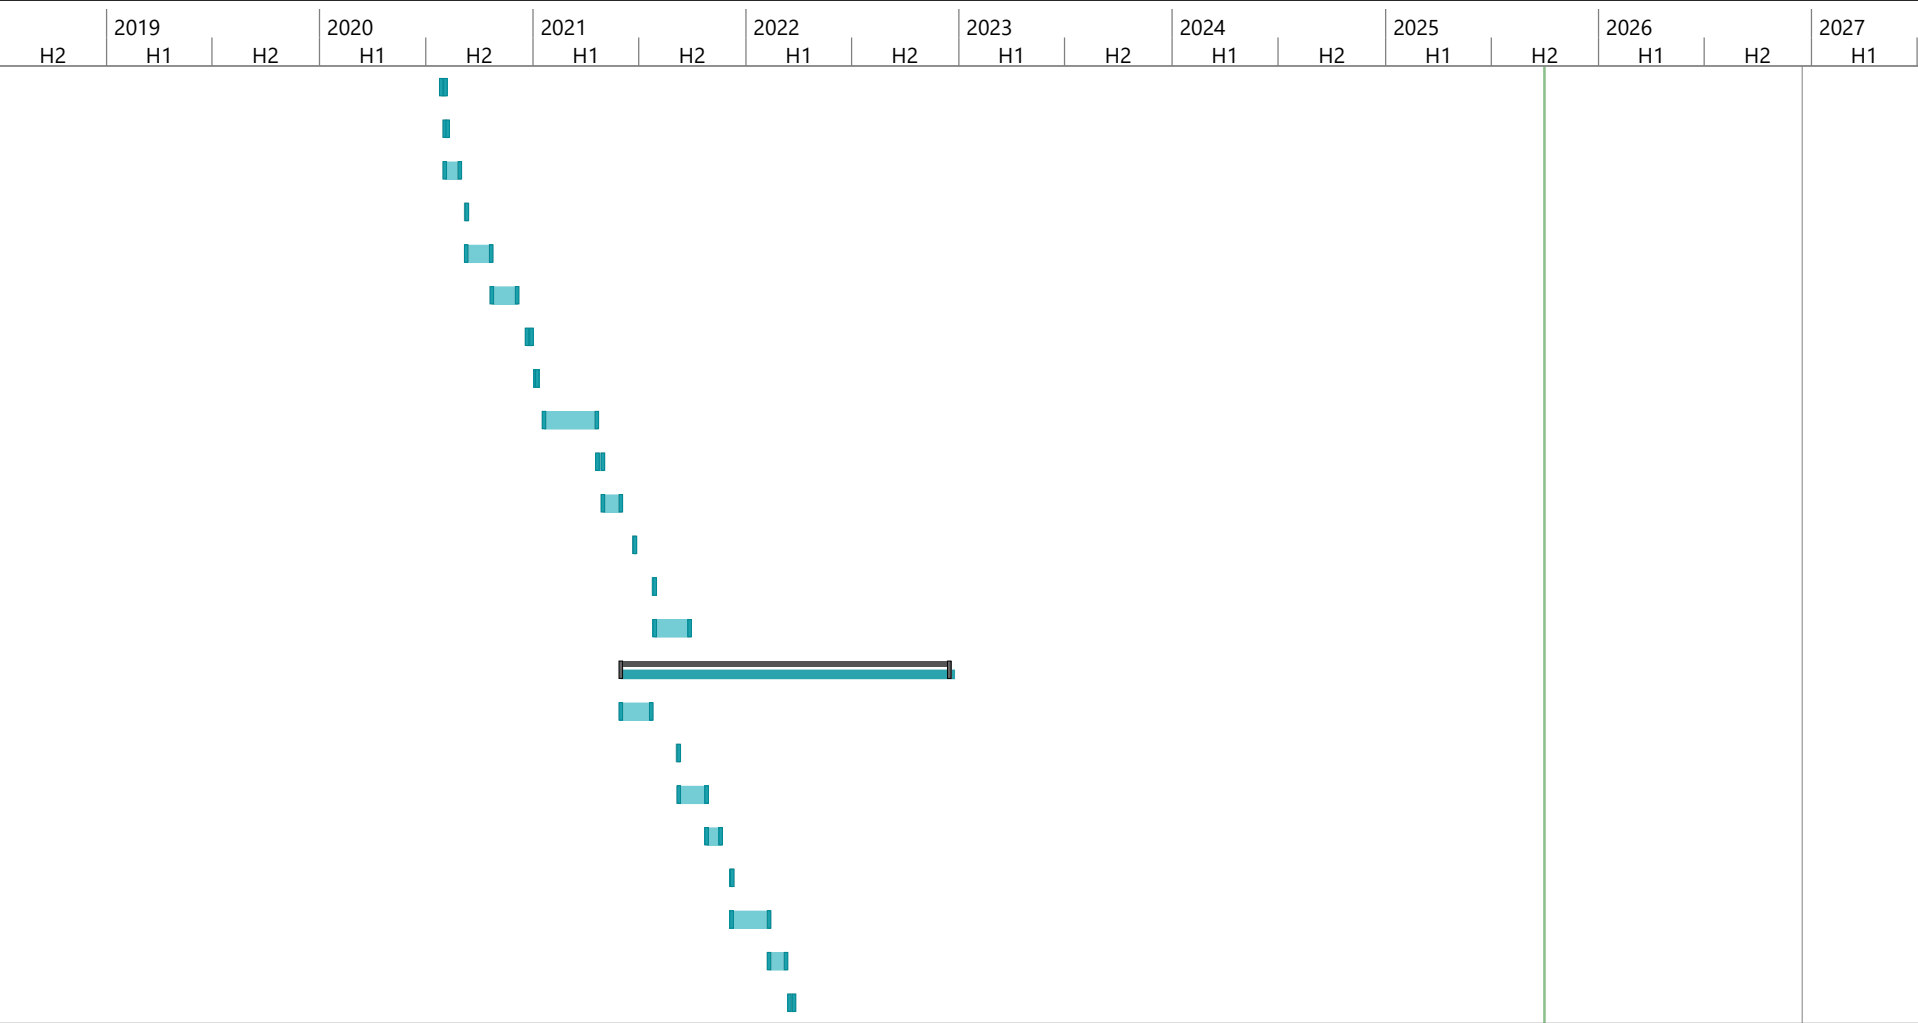
External Milestone

Deadline

Progress

Manual Progress

Page 120



Project: IOU Master Task Timeli
Date: Tue 9/30/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

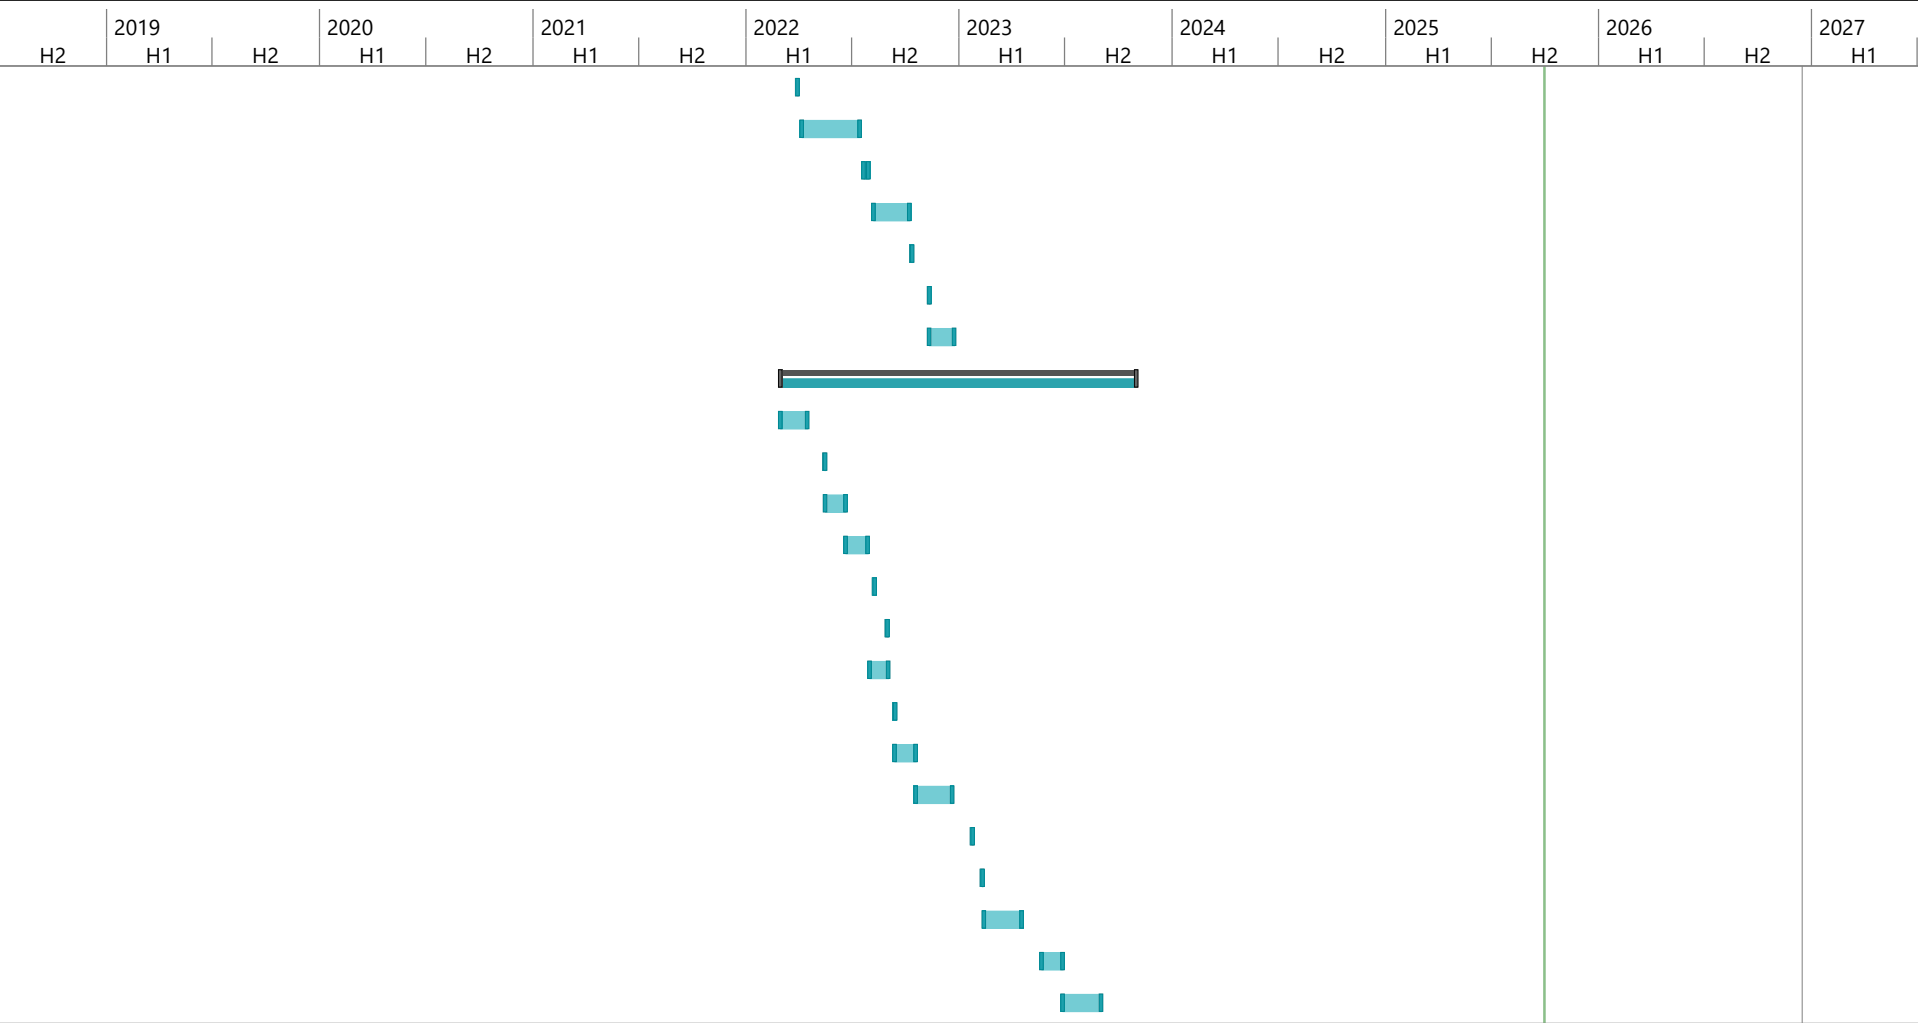
External Milestone

Deadline

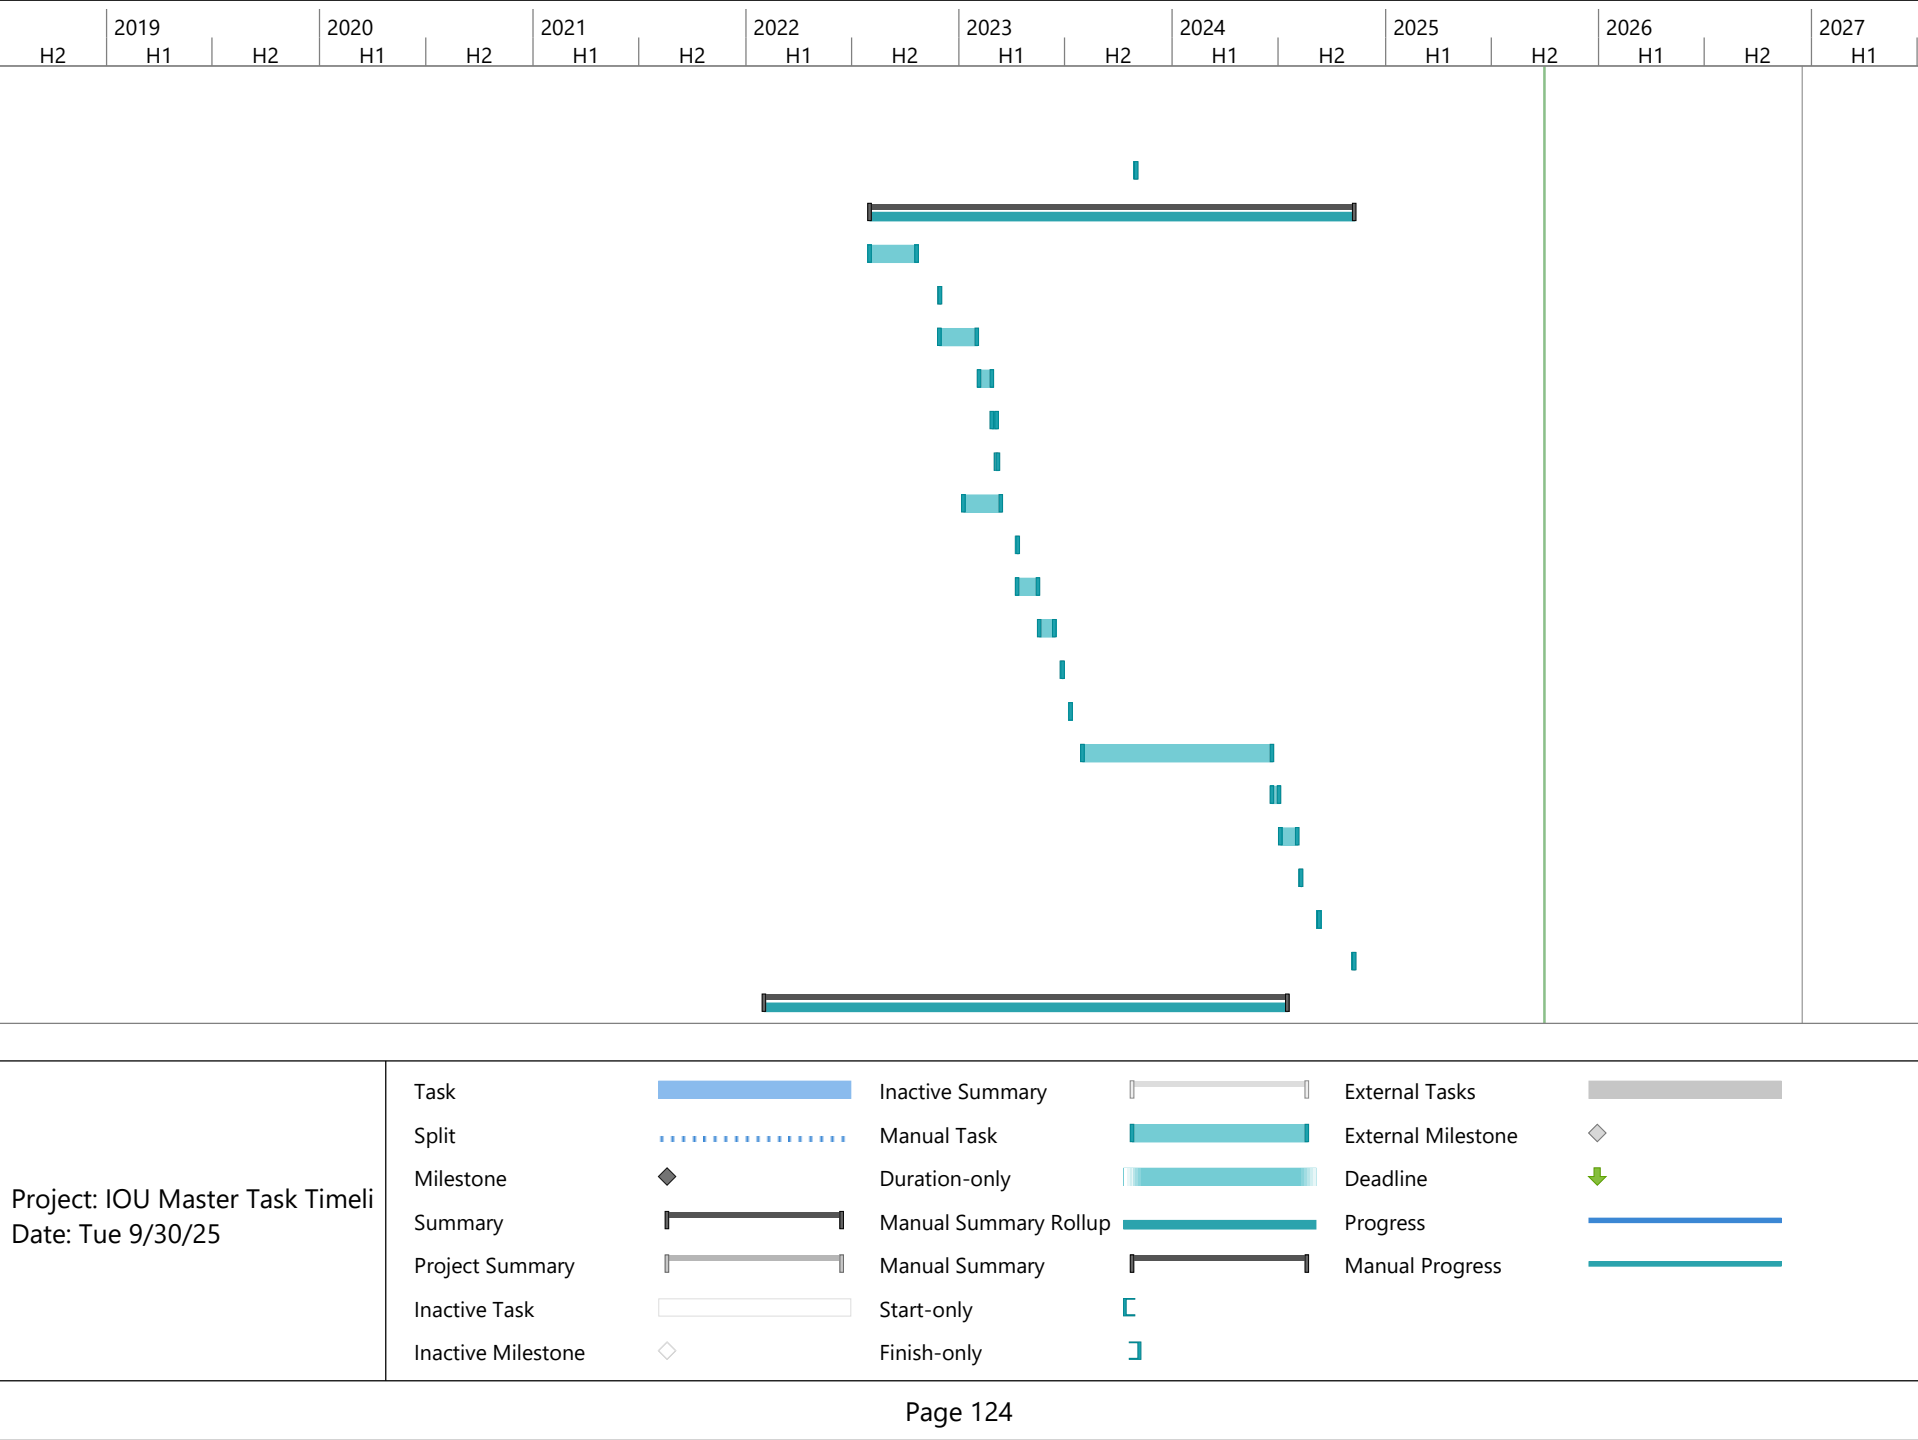
Progress

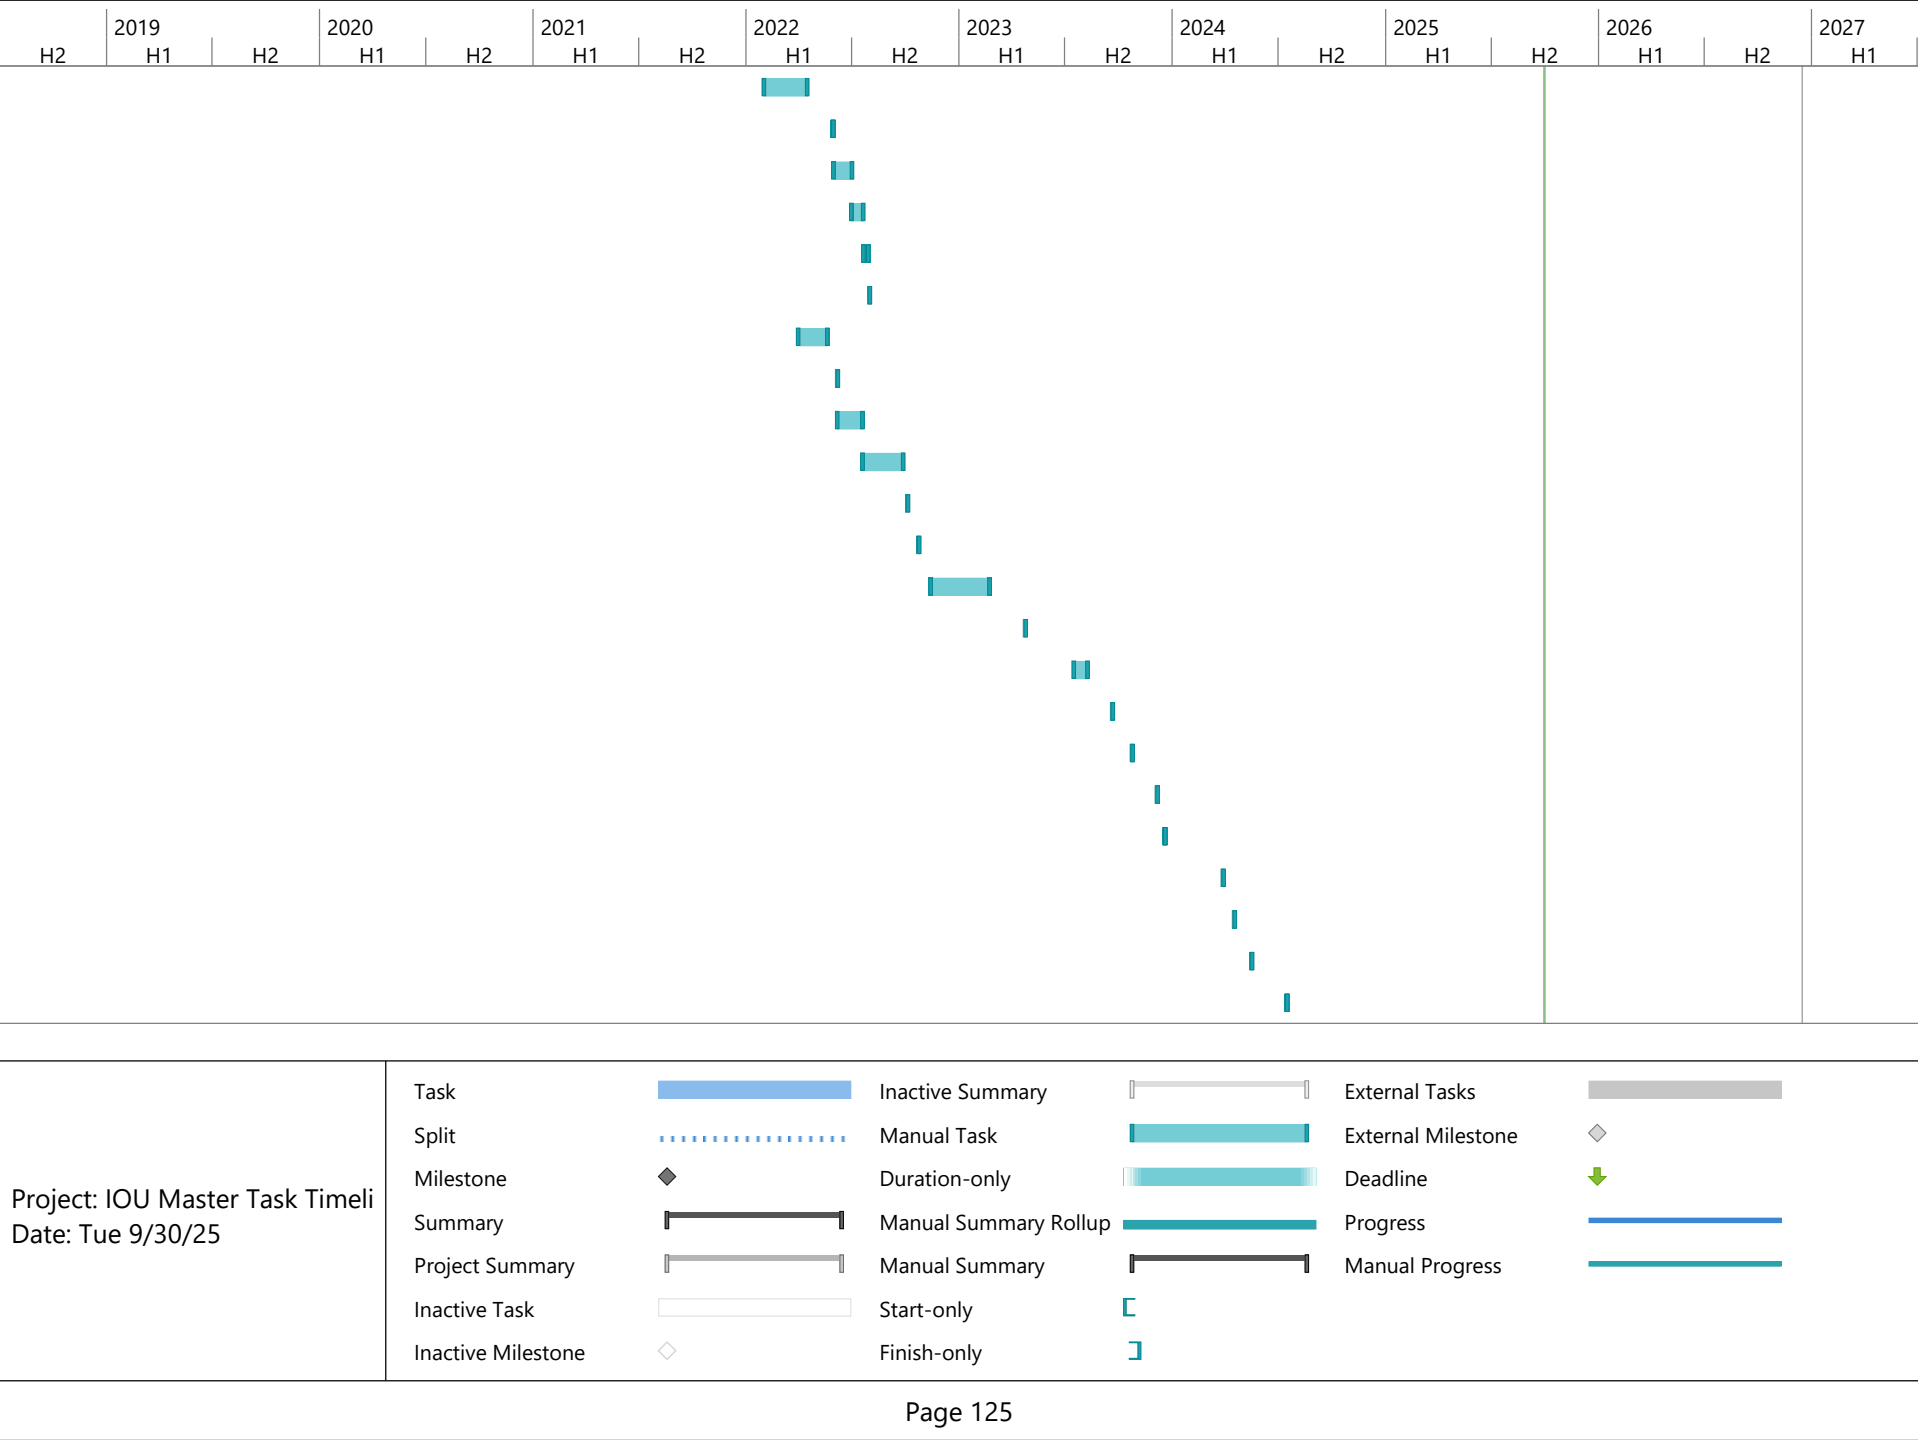
Manual Progress

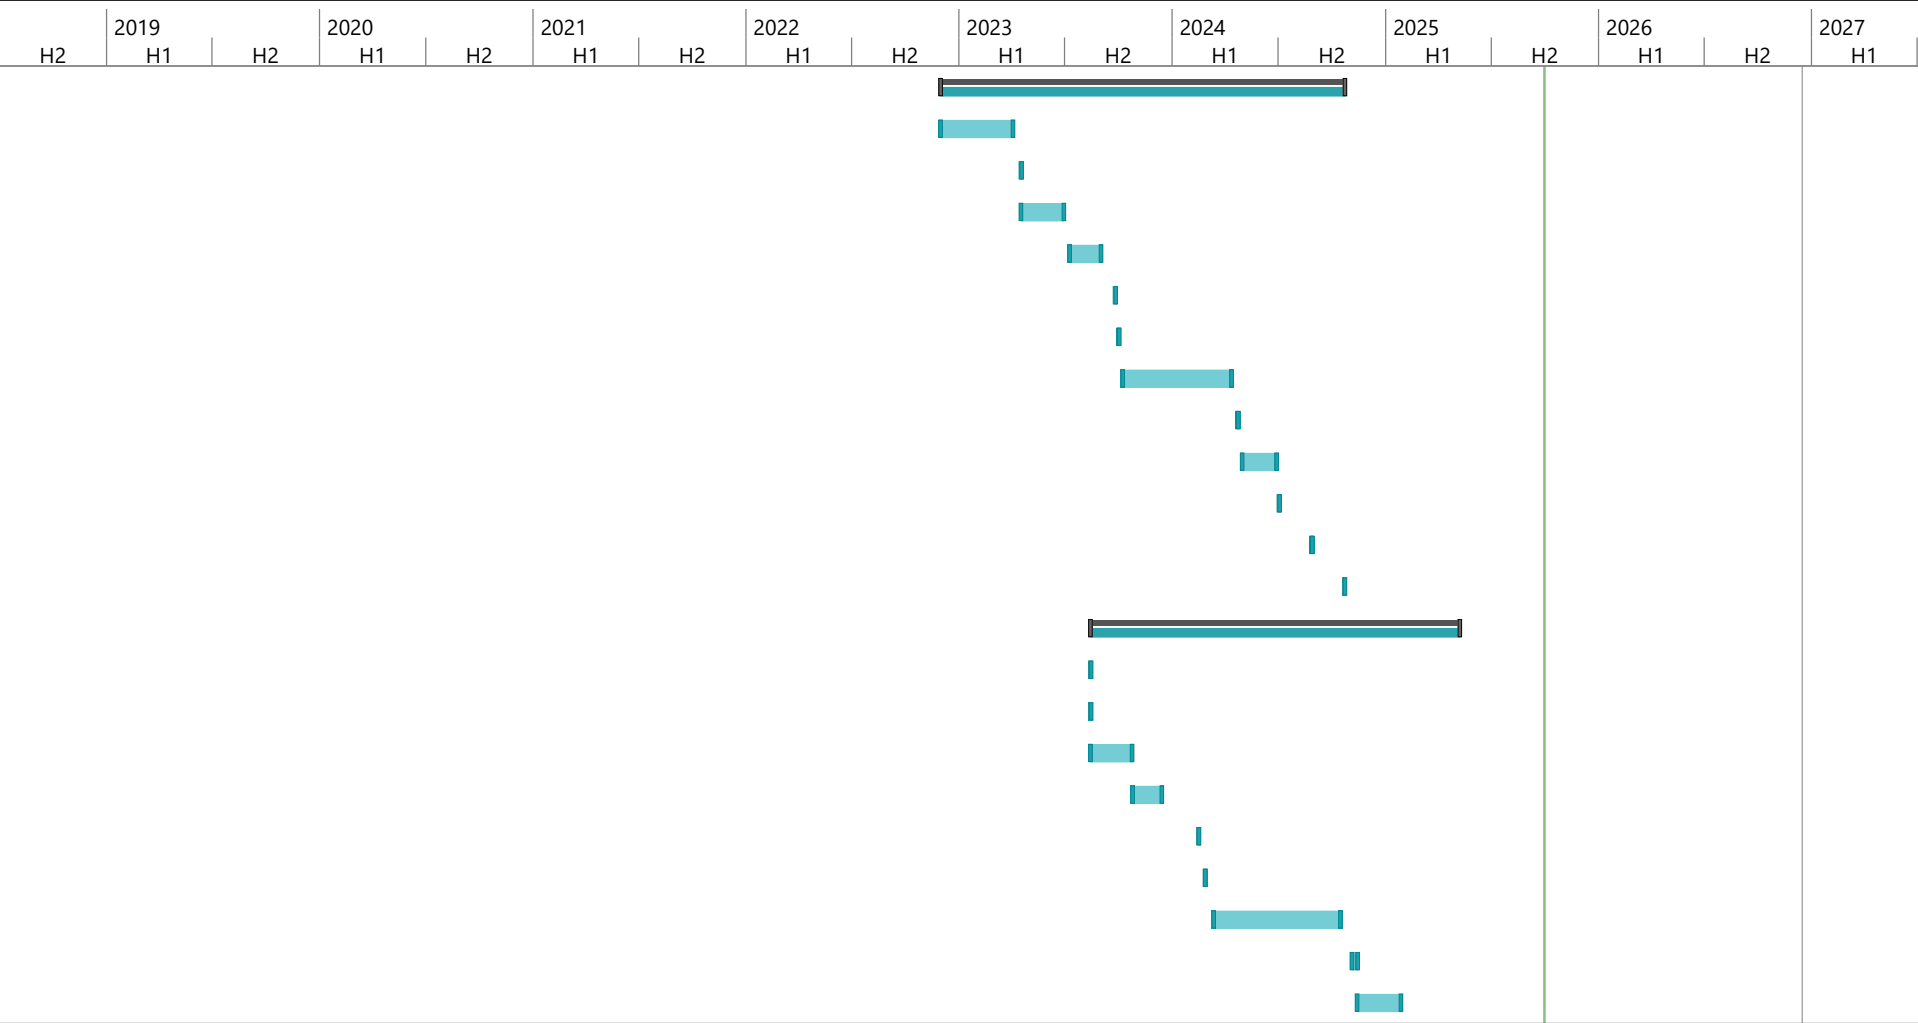
Page 122



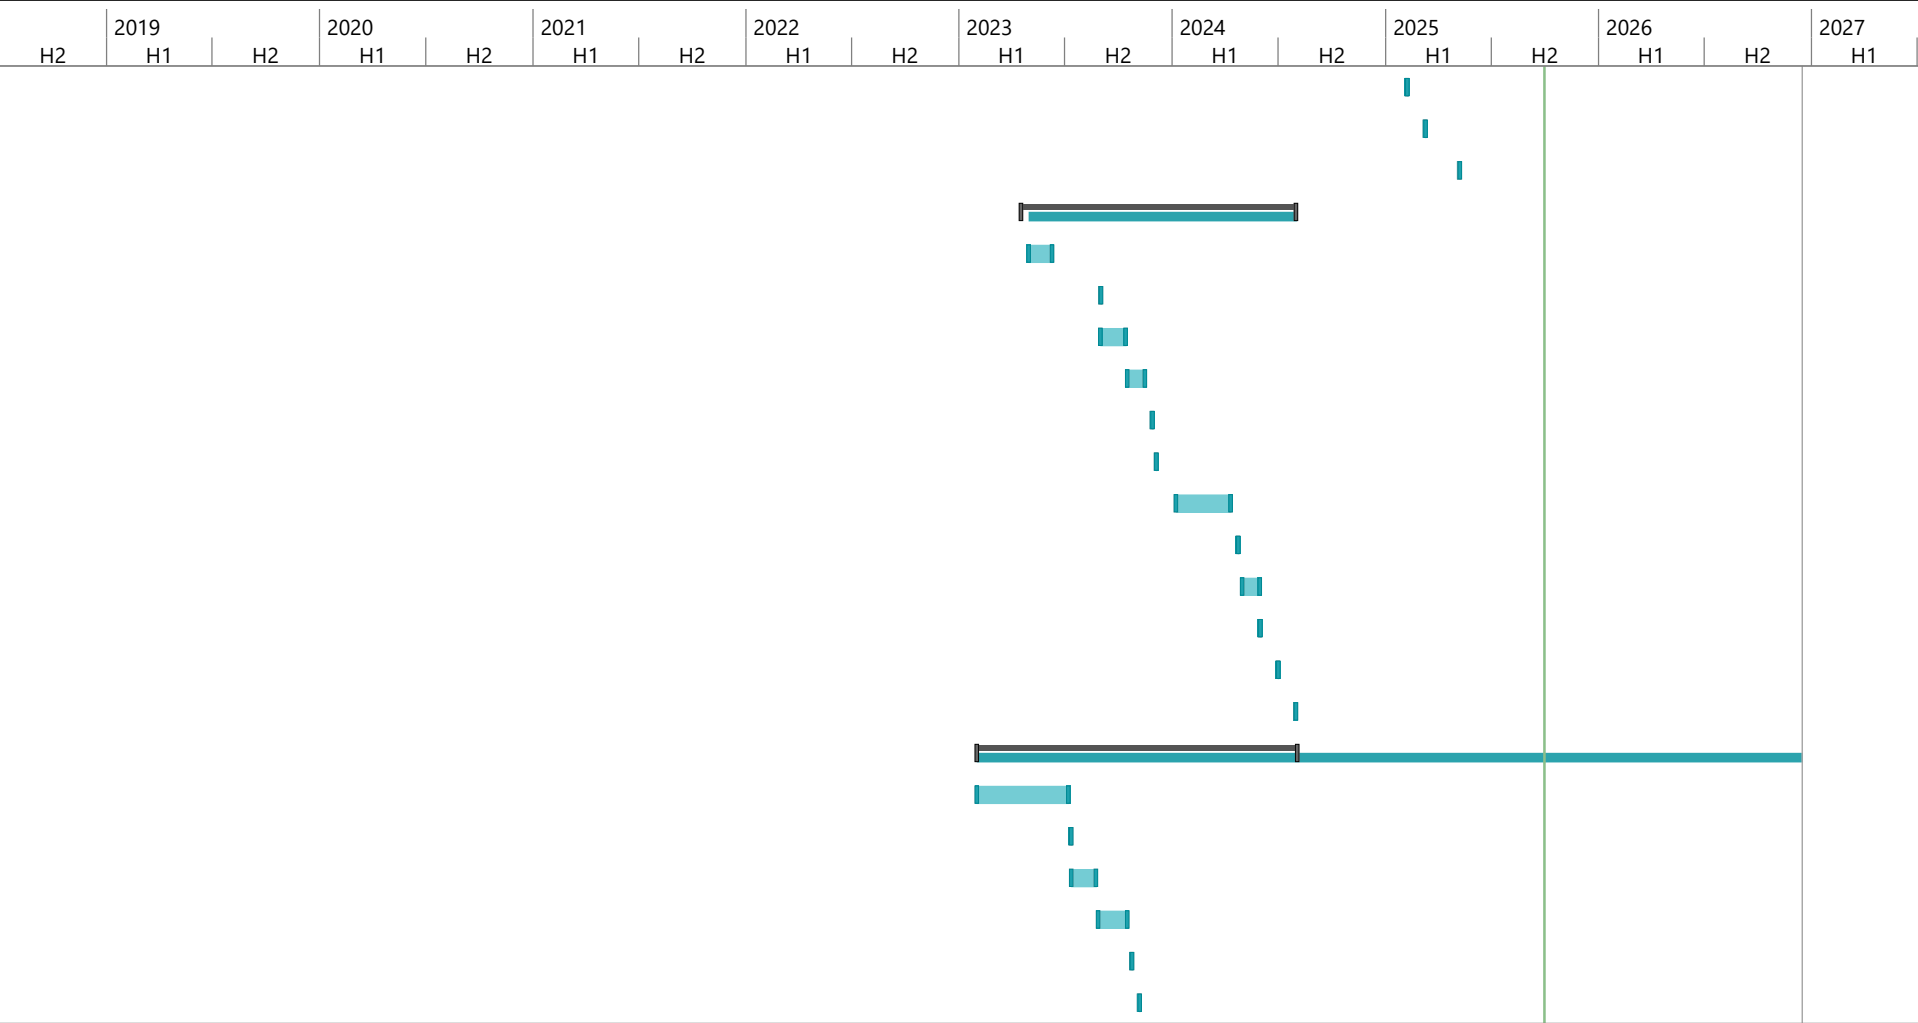
Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			







Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Tue 9/30/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

