



ID		Task Name	Duration	Start	Finish	H2	2005 H1
1		UPDATED as of April 1, 2025					
2		SCE - Local RCI Solicitation	679 days	Tue 8/21/18	Fri 3/26/21		
3		SCE - RFA Preparation	40 days	Tue 8/21/18	Mon 10/15/18		
4		SCE - RFA Release	1 day	Fri 11/9/18	Fri 11/9/18		
5		SCE - RFA Abstract Creation Duration	30 days	Sat 11/10/18	Thu 12/20/18		
6		SCE - RFA Evaluation	82 days	Fri 12/21/18	Mon 4/15/19		
7		SCE - RFA Review with EE PRG	1 day	Tue 4/16/19	Tue 4/16/19		
8		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/21/19	Tue 5/21/19		
9		SCE - RFP Preparation	175 days	Wed 5/22/19	Tue 1/21/20		
10		SCE - RFP Release	1 day	Wed 1/22/20	Wed 1/22/20		
11		SCE - RFP Proposal Creation Duration	25 days	Thu 1/23/20	Wed 2/26/20		
12		SCE - RFP Evaluation	38 days	Thu 2/27/20	Mon 4/20/20		
13		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20		
14		SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20		
15		SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20		
16		SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20		
17		SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20		
18		SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20		
19		SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20		
20		SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21		
21		SCE - SW Lighting	518 days	Wed 4/3/19	Fri 3/26/21		
22		SCE - RFA Preparation	55 days	Wed 4/3/19	Tue 6/18/19		
23		SCE - RFA Release	1 day	Tue 7/2/19	Tue 7/2/19		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
24		SCE - RFA Abstract Creation Duration	20 days	Wed 7/3/19	Tue 7/30/19		
25		SCE - RFA Evaluation	34 days	Wed 7/31/19	Mon 9/16/19		
26		SCE - RFA Review with EE PRG	1 day	Tue 9/17/19	Tue 9/17/19		
27		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/24/19	Tue 9/24/19		
28		SCE - RFP Preparation	84 days	Wed 9/25/19	Mon 1/20/20		
29		SCE - RFP Release	1 day	Thu 2/6/20	Thu 2/6/20		
30		SCE - RFP Proposal Creation Duration	27 days	Fri 2/7/20	Mon 3/16/20		
31		SCE - RFP Evaluation	25 days	Tue 3/17/20	Mon 4/20/20		
32		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20		
33		SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20		
34		SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20		
35		SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20		
36		SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20		
37		SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20		
38		SCE - Advice Letter Approved	1 day	Wed 12/23/20	Wed 12/23/20		
39		SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21		
40		SCE - Local Public Sector Solicitation	573 days	Mon 8/31/20	Wed 11/9/22		
41		SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20		
42		SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20		
43		SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20		
44		SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21		
45		SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21		
46		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
47		SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21		
48		SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21		
49		SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21		
50		SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21		
51		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21		
52		SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21		
53		SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21		
54		SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21		
55		SCE - Final Award and Contract Signed	1 day	Tue 12/14/21	Tue 12/14/21		
56		SCE - Submit Advice Letter	37 days	Wed 12/15/21	Thu 2/3/22		
57		SCE - Submit Advice Letter	48 days	Wed 12/15/21	Fri 2/18/22		
58		SCE - Advice Letter Approved	1 day	Thu 8/18/22	Thu 8/18/22		
59		SCE - Implementation Plan	60 days	Thu 8/18/22	Wed 11/9/22		
60		SCE - Local Agriculture Solicitation	512 days	Mon 8/31/20	Tue 8/16/22		
61		SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20		
62		SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20		
63		SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20		
64		SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21		
65		SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21		
66		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21		
67		SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21		
68		SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21		
69		SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
70		SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21		
71		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21		
72		SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21		
73		SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21		
74		SCE - Final Award and Contract Signed	1 day	Mon 12/20/21	Mon 12/20/21		
75		SCE - Submit Advice Letter	33 days	Tue 12/21/21	Thu 2/3/22		
76		SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21		
77		SCE - Final Award and Contract Signed	1 day	Wed 12/15/21	Wed 12/15/21		
78		SCE - Submit Advice Letter	56 days	Thu 12/16/21	Thu 3/3/22		
79		SCE - Advice Letter Approved	1 day	Fri 4/22/22	Fri 4/22/22		
80		SCE - Implementation Plan	60 days	Sat 4/23/22	Thu 7/14/22		
81		SCE - SW Water/Wastewater Solicitation	522 days	Mon 11/16/20	Tue 11/15/22		
82		SCE - RFA Preparation	70 days	Mon 11/16/20	Fri 2/19/21		
83		SCE - RFA Release	1 day	Thu 3/4/21	Thu 3/4/21		
84		SCE - RFA Abstract Creation Duration	29 days	Thu 3/4/21	Tue 4/13/21		
85		SCE - RFA Evaluation	20 days	Wed 4/14/21	Tue 5/11/21		
86		SCE - RFA Review with EE PRG	1 day	Tue 5/18/21	Tue 5/18/21		
87		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/27/21	Thu 5/27/21		
88		SCE - RFP Preparation	34 days	Mon 4/19/21	Thu 6/3/21		
89		SCE - RFP Release	1 day	Thu 7/1/21	Thu 7/1/21		
90		SCE - RFP Proposal Creation Duration	25 days	Fri 7/2/21	Thu 8/5/21		
91		SCE - RFP Evaluation	41 days	Fri 8/6/21	Fri 10/1/21		
92		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/26/21	Tue 10/26/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
93		SCE - RFP Review with EE PRG	1 day	Tue 10/19/21	Tue 10/19/21		
94		SCE - Contract Negotiation and Development	94 days	Wed 10/27/21	Mon 3/7/22		
95		SCE - Contract Review with EE PRG	1 day	Tue 3/15/22	Tue 3/15/22		
96		SCE - Final Award and Contract Signed	1 day	Tue 4/19/22	Tue 4/19/22		
97		SCE - Submit Advice Letter	40 days	Wed 4/20/22	Tue 6/14/22		
98		SCE - Advice Letter Approved	26 days	Wed 6/15/22	Wed 7/20/22		
99		SCE - Implementation Plan	44 days	Thu 7/21/22	Tue 9/20/22		
100		SCE - SW ETP Solicitation	466 days	Fri 5/1/20	Fri 2/11/22		
101		SCE - RFA Preparation	57 days	Fri 5/1/20	Mon 7/20/20		
102		SCE - RFA Release	1 day	Tue 8/4/20	Tue 8/4/20		
103		SCE - RFA Abstract Creation Duration	24 days	Fri 8/7/20	Wed 9/9/20		
104		SCE - RFA Evaluation	16 days	Thu 9/10/20	Thu 10/1/20		
105		SCE - RFA Review with EE PRG	1 day	Tue 10/20/20	Tue 10/20/20		
106		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/27/20	Tue 10/27/20		
107		SCE - RFP Preparation	42 days	Tue 9/8/20	Wed 11/4/20		
108		SCE - RFP Release	1 day	Tue 1/5/21	Tue 1/5/21		
109		SCE - RFP Proposal Creation Duration	37 days	Tue 1/5/21	Wed 2/24/21		
110		SCE - RFP Evaluation	28 days	Wed 2/24/21	Fri 4/2/21		
111		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/27/21	Tue 4/27/21		
112		SCE - RFP Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21		
113		SCE - Contract Negotiation and Development	69 days	Wed 4/21/21	Mon 7/26/21		
114		SCE - Contract Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21		
115		SCE - Final Award and Contract Signed	1 day	Tue 9/14/21	Tue 9/14/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
116		SCE - Submit Advice Letter	18 days	Wed 9/15/21	Fri 10/8/21		
117		SCE - Advice Letter Approved	1 day	Tue 11/9/21	Tue 11/9/21		
118		SCE - Implementation Plan	60 days	Wed 11/10/21	Tue 2/1/22		
119		SCE - SW Higher-Education Solicitation	547 days?	Thu 10/1/20	Fri 11/4/22		
120		SCE - RFA Preparation	89 days	Thu 10/1/20	Tue 2/2/21		
121		SCE - RFA Release	1 day	Thu 2/4/21	Thu 2/4/21		
122		SCE - RFA Abstract Creation Duration	19 days	Fri 2/5/21	Wed 3/3/21		
123		SCE - RFA Evaluation	31 days	Thu 3/4/21	Thu 4/15/21		
124		SCE - RFA Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21		
125		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 4/29/21	Thu 4/29/21		
126		SCE - RFP Preparation	39 days	Mon 3/22/21	Thu 5/13/21		
127		SCE - RFP Release	1 day	Fri 5/28/21	Fri 5/28/21		
128		SCE - RFP Proposal Creation Duration	24 days	Fri 6/4/21	Wed 7/7/21		
129		SCE - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21		
130		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/30/21	Mon 8/30/21		
131		SCE - RFP Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21		
132		SCE - Contract Negotiation and Development	95 days	Fri 9/3/21	Thu 1/13/22		
133		SCE - Contract Review with EE PRG	1 day	Tue 1/18/22	Tue 1/18/22		
134		SCE - Final Award and Contract Signed	1 day	Sun 3/6/22	Sun 3/6/22		
135		SCE - Submit Advice Letter	1 day	Tue 4/19/22	Tue 4/19/22		
136		SCE - Advice Letter Approved	1 day	Mon 8/15/22	Mon 8/15/22		
137		SCE - Implementation Plan	60 days	Mon 8/15/22	Fri 11/4/22		
138		SCE - Local Equity Residential and SMB	384 days?	Tue 2/15/22	Fri 8/4/23		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
139		SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22		
140		SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22		
141		SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22		
142		SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22		
143		SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22		
144		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22		
145		SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22		
146		SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22		
147		SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22		
148		SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22		
149		SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22		
150		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22		
151		SCE - Contract Negotiation and Development	65 days	Wed 11/2/22	Tue 1/31/23		
152		SCE - Contract Review with EE PRG	1 day	Tue 2/21/23	Tue 2/21/23		
153		SCE - Final Award and Contract Signed	1 day	Thu 3/30/23	Thu 3/30/23		
154		SCE - Submit Advice Letter	22 days	Sun 4/3/22	Mon 5/2/22		
155		SCE - Advice Letter Approved	28 days	Tue 5/2/23	Thu 6/8/23		
156		SCE - Implementation Plan	45 days	Thu 6/8/23	Wed 8/9/23		
157							
158		SCE - Local Equity SMB	431 days?	Tue 2/15/22	Tue 10/10/23		
159		SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22		
160		SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22		
161		SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
162		SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22		
163		SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22		
164		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22		
165		SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22		
166		SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22		
167		SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22		
168		SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22		
169		SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22		
170		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22		
171		SCE - Contract Negotiation and Development	108 days	Wed 11/2/22	Fri 3/31/23		
172		SCE - Contract Review with EE PRG	1 day	Tue 4/18/23	Tue 4/18/23		
173		SCE - Final Award and Contract Signed	1 day	Wed 5/31/23	Wed 5/31/23		
174		SCE - Submit Advice Letter	22 days	Mon 6/6/22	Tue 7/5/22		
175		SCE - Advice Letter Approved	24 days	Thu 7/6/23	Tue 8/8/23		
176		SCE - Implementation Plan	45 days	Wed 8/9/23	Tue 10/10/23		
177		SCE - Local Strategic Energy Management Solicitation	372 days?	Thu 12/1/22	Fri 5/3/24		
178		SCE - RFP Preparation	85 days	Thu 12/1/22	Wed 3/29/23		
179		SCE - RFP Release	1 day	Fri 4/7/23	Fri 4/7/23		
180		SCE - RFP Proposal Creation Duration	35 days	Fri 4/7/23	Thu 5/25/23		
181		SCE - RFP Evaluation	22 days	Thu 6/1/23	Fri 6/30/23		
182		SCE - RFP Review with EE PRG	1 day	Tue 7/18/23	Tue 7/18/23		
183		SCE - Contract Negotiation and Development	86 days	Tue 8/1/23	Tue 11/28/23		
184		SCE - Contract Review with EE PRG	1 day	Tue 12/19/23	Tue 12/19/23		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
185		SCE - Final Award and Contract Signed	6 days	Fri 1/19/24	Fri 1/26/24		
186		SCE - Submit Advice Letter	34 days	Wed 1/31/24	Mon 3/18/24		
187		SCE - Advice Letter Approved	40 days	Tue 3/19/24	Mon 5/13/24		
188		SCE - Local Large Commercial Solicitation	488 days?	Mon 6/26/23	Wed 5/7/25		
189		SCE - RFP Preparation	35 days	Mon 6/26/23	Fri 8/11/23		
190		SCE - RFP Release	1 day	Thu 8/17/23	Thu 8/17/23		
191		SCE - RFP Proposal Creation Duration	41 days	Thu 8/17/23	Thu 10/12/23		
192		SCE - RFP Paused	1 day	Fri 10/13/23	Fri 10/13/23		
193		SCE - Residential Multifamily	326 days?	Fri 9/1/23	Fri 11/29/24		
194		SCE - RFP Preparation	47 days	Fri 9/1/23	Mon 11/6/23		
195		SCE - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23		
196		SCE - RFP Proposal Creation Duration	48 days	Mon 11/6/23	Wed 1/10/24		
197		SCE - RFP Evaluation	25 days	Thu 1/11/24	Wed 2/14/24		
198		SCE - RFP Review with EE PRG	1 day	Tue 2/20/24	Tue 2/20/24		
199		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 2/28/24	Wed 2/28/24		
200		SCE - Contract Negotiation and Development	70 days	Mon 3/4/24	Fri 6/7/24		
201		SCE - Contract Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
202		SCE - Final Award and Contract Signed	15 days	Mon 7/29/24	Fri 8/16/24		
203		SCE - Submit Advice Letter	30 days	Mon 8/19/24	Fri 9/27/24		
204		SCE - Advice Letter Approved	1 day	Mon 10/28/24	Mon 10/28/24		
205		SCE - Local Large Industrial	442 days	Fri 11/3/23	Mon 7/14/25		
206		SCE - RFP Preparation	17 days	Fri 11/3/23	Mon 11/27/23		
207		SCE - RFP Release	1 day	Mon 12/11/23	Mon 12/11/23		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
208		SCE - RFP Proposal Creation Duration	49 days	Mon 12/11/23	Thu 2/15/24		
209		SCE - RFP Evaluation	35 days	Fri 2/16/24	Thu 4/4/24		
210		SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24		
211		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/23/24	Tue 4/23/24		
212		SCE - Contract Negotiation and Development	208 days	Wed 4/24/24	Fri 2/7/25		
213		SCE - Contract Review with EE PRG	21 days	Tue 3/18/25	Tue 4/15/25		
214		SCE - Final Award and Contract Signed	30 days	Mon 3/31/25	Fri 5/9/25		
215		SCE - Submit Advice Letter	45 days	Mon 4/14/25	Fri 6/13/25		
216		SCE - Advice Letter Approved	41 days	Mon 5/19/25	Mon 7/14/25		
217		SCE - MAP - All Sectors	299 days?	Mon 11/20/23	Thu 1/9/25		
218		SCE - RFP Preparation	20 days	Mon 11/20/23	Fri 12/15/23		
219		SCE - RFP Release	1 day	Mon 1/8/24	Mon 1/8/24		
220		SCE - RFP Proposal Creation Duration	40 days	Mon 1/8/24	Fri 3/1/24		
221		SCE - RFP Evaluation	30 days	Mon 3/4/24	Fri 4/12/24		
222		SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24		
223		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/24/24	Wed 4/24/24		
224		SCE - Contract Negotiation and Development	108 days	Wed 5/1/24	Fri 9/27/24		
225		SCE - Contract Review with EE PRG	1 day	Tue 10/15/24	Tue 10/15/24		
226		SCE - Final Award and Contract Signed	12 days	Tue 10/29/24	Wed 11/13/24		
227		SCE - Submit Advice Letter	43 days	Wed 11/13/24	Fri 1/10/25		
228		SCE - Advice Letter Approved	22 days	Mon 1/13/25	Tue 2/11/25		
229		SCE - Residential	360 days?	Mon 11/20/23	Fri 4/4/25		
230		SCE - RFP Preparation	20 days	Tue 1/16/24	Mon 2/12/24		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
231		SCE - RFP Release	1 day	Thu 3/28/24	Thu 3/28/24		
232		SCE - RFP Proposal Creation Duration	41 days	Thu 3/28/24	Thu 5/23/24		
233		SCE - RFP Evaluation	35 days	Fri 5/24/24	Thu 7/11/24		
234		SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
235		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/5/24	Mon 8/5/24		
236		SCE - Contract Negotiation and Development	80 days	Mon 8/19/24	Fri 12/6/24		
237		SCE - Contract Review with EE PRG	1 day	Tue 12/17/24	Tue 12/17/24		
238		SCE - Final Award and Contract Signed	11 days	Mon 1/13/25	Mon 1/27/25		
239		SCE - Submit Advice Letter	19 days	Mon 2/3/25	Thu 2/27/25		
240		SCE - Advice Letter Approved	22 days	Thu 3/6/25	Fri 4/4/25		
241							
242		SCE - Local Comprehensive Commercial Solicitation	431 days?	Mon 11/13/23	Mon 7/7/25		
243		SCE - RFP Preparation	73 days	Mon 11/13/23	Wed 2/21/24		
244		SCE - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24		
245		SCE - RFP Proposal Creation Duration	43 days	Thu 2/29/24	Mon 4/29/24		
246		SCE - RFP Evaluation	54 days	Tue 4/30/24	Fri 7/12/24		
247		SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
248		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Phase 1	1 day	Mon 7/29/24	Mon 7/29/24		
249		SCE - Contract Negotiation and Development - Phase 1	81 days	Tue 7/30/24	Tue 11/19/24		
250		SCE - Contract Review with EE PRG - Phase 1	1 day	Tue 12/17/24	Tue 12/17/24		
251		SCE - Final Award and Contract Signed - Phase 1	1 day	Tue 1/28/25	Tue 1/28/25		
252		SCE - Submit Advice Letter - Phase 1	23 days	Tue 1/28/25	Thu 2/27/25		
253		SCE - Advice Letter Approved - Phase 1	1 day	Fri 3/28/25	Fri 3/28/25		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
254		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Phase 1	1 day	Mon 9/30/24	Mon 9/30/24		
255		SCE - Contract Negotiation and Development - Phase 2	80 days	Mon 12/2/24	Fri 3/21/25		
256		SCE - Contract Review with EE PRG - Phase 2	1 day	Tue 4/15/25	Tue 4/15/25		
257		SCE - Final Award and Contract Signed - Phase 2	1 day	Wed 5/14/25	Wed 5/14/25		
258		SCE - Submit Advice Letter - Phase 2	5245 days	Thu 5/19/05	Wed 6/25/25		
259		SCE - Advice Letter Approved - Phase 2	1 day	Fri 7/25/25	Fri 7/25/25		
260							
261		SCG - Local Single Family Solicitation	660 days	Sun 7/1/18	Thu 1/7/21		
262		SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18		
263		SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18		
264		SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19		
265		SCG - RFA Evaluation	39 days	Mon 1/7/19	Thu 2/28/19		
266		SCG - RFA Review with EE PRG	1 day	Tue 3/5/19	Tue 3/5/19		
267		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19		
268		SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19		
269		SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19		
270		SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19		
271		SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19		
272		SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19		
273		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
274		SCG - Contract Negotiation and Development	69 days	Mon 1/27/20	Thu 4/30/20		
275		SCG - Contract Review with EE PRG	14 days	Tue 5/5/20	Fri 5/22/20		
276		SCG - Final Award and Contract Signed	8 days	Mon 5/25/20	Wed 6/3/20		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
277		SCG - Submit Advice Letter	96 days	Mon 6/1/20	Mon 10/12/20		
278		SCG - Advice Letter Approved	1 day	Thu 11/12/20	Thu 11/12/20		
279		SCG - Implementation Plan	41 days	Fri 11/13/20	Fri 1/8/21		
280		SCG - Local Multi-family Solicitation	735 days	Sun 7/1/18	Thu 4/22/21		
281		SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18		
282		SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18		
283		SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19		
284		SCG - RFA Evaluation	59 days	Mon 1/7/19	Thu 3/28/19		
285		SCG - RFA Review with EE PRG	1 day	Tue 4/2/19	Tue 4/2/19		
286		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19		
287		SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19		
288		SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19		
289		SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19		
290		SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19		
291		SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19		
292		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
293		SCG - Contract Negotiation and Development	155 days	Mon 1/27/20	Fri 8/28/20		
294		SCG - Contract Review with EE PRG	99 days	Tue 5/5/20	Fri 9/18/20		
295		SCG - Final Award and Contract Signed	8 days	Mon 9/21/20	Wed 9/30/20		
296		SCG - Submit Advice Letter	37 days	Thu 10/1/20	Fri 11/20/20		
297		SCG - Advice Letter Approved	1 day	Sun 5/2/21	Sun 5/2/21		
298		SCG - Implementation Plan	51 days	Mon 5/3/21	Mon 7/12/21		
299		SCG - Local Small/Medium Commercial Solicitation	641 days	Tue 9/4/18	Tue 2/16/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
300		SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19		
301		SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19		
302		SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19		
303		SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19		
304		SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19		
305		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19		
306		SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19		
307		SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19		
308		SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19		
309		SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19		
310		SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19		
311		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
312		SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20		
313		SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20		
314		SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20		
315		SCG - Submit Advice Letter	59 days	Tue 9/1/20	Fri 11/20/20		
316		SCG - Advice Letter Approved	1 day	Fri 12/18/20	Fri 12/18/20		
317		SCG - Implementation Plan	43 days	Sat 12/19/20	Tue 2/16/21		
318		SCG - Local Small/Medium Public Solicitation	631 days	Tue 9/4/18	Tue 2/2/21		
319		SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19		
320		SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19		
321		SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19		
322		SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
323		SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19		
324		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19		
325		SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19		
326		SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19		
327		SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19		
328		SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19		
329		SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19		
330		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
331		SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20		
332		SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20		
333		SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20		
334		SCG - Submit Advice Letter	49 days	Tue 9/1/20	Fri 11/6/20		
335		SCG - Advice Letter Approved	1 day	Fri 12/4/20	Fri 12/4/20		
336		SCG - Implementation Plan	43 days	Sat 12/5/20	Tue 2/2/21		
337		SCG - Statewide POS Food Service Solicitation	605 days	Mon 1/21/19	Fri 5/14/21		
338		SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19		
339		SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19		
340		SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19		
341		SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19		
342		SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19		
343		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20		
344		SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19		
345		SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
346		SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20		
347		SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20		
348		SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20		
349		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20		
350		SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20		
351		SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20		
352		SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20		
353		SCG - Submit Advice Letter	32 days	Mon 11/2/20	Tue 12/15/20		
354		SCG - Advice Letter Approved	1 day	Thu 1/14/21	Thu 1/14/21		
355		SCG - Implementation Plan	42 days	Fri 1/15/21	Mon 3/15/21		
356		SCG - Statewide Midstream Water Heating Solicitation	597 days	Mon 1/21/19	Tue 5/4/21		
357		SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19		
358		SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19		
359		SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19		
360		SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19		
361		SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19		
362		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20		
363		SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19		
364		SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20		
365		SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20		
366		SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20		
367		SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20		
368		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
369		SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20		
370		SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20		
371		SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20		
372		SCG - Submit Advice Letter	25 days	Mon 11/2/20	Fri 12/4/20		
373		SCG - Advice Letter Approved	1 day	Thu 3/18/21	Thu 3/18/21		
374		SCG - Implementation Plan	22 days	Fri 3/19/21	Mon 4/19/21		
375		SCG - Statewide Gas Emerging Technology Solicitation	738 days	Wed 1/2/19	Fri 10/29/21		
376		SCG - RFA Preparation	283 days	Wed 1/2/19	Fri 1/31/20		
377		SCG - RFA Release	1 day	Wed 2/12/20	Wed 2/12/20		
378		SCG - RFA Abstract Creation Duration	30 days	Thu 2/13/20	Wed 3/25/20		
379		SCG - RFA Evaluation	26 days	Thu 3/26/20	Thu 4/30/20		
380		SCG - RFA Review with EE PRG	1 day	Tue 5/5/20	Tue 5/5/20		
381		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 5/15/20	Fri 5/15/20		
382		SCG - RFP Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
383		SCG - RFP Release	1 day	Fri 8/21/20	Fri 8/21/20		
384		SCG - RFP Proposal Creation Duration	30 days	Mon 8/24/20	Fri 10/2/20		
385		SCG - RFP Evaluation	38 days	Mon 10/5/20	Wed 11/25/20		
386		SCG - RFP Review with EE PRG	1 day	Tue 12/1/20	Tue 12/1/20		
387		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 12/7/20	Mon 12/7/20		
388		SCG - Contract Negotiation and Development	85 days	Mon 1/4/21	Fri 4/30/21		
389		SCG - Contract Review with EE PRG	9 days	Tue 5/4/21	Fri 5/14/21		
390		SCG - Final Award and Contract Signed	29 days	Mon 5/17/21	Thu 6/24/21		
391		SCG - Submit Advice Letter	23 days	Sun 6/27/21	Tue 7/27/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
392		SCG - Advice Letter Approved	1 day	Tue 8/24/21	Tue 8/24/21		
393		SCG - Implementation Plan	44 days	Wed 8/25/21	Sat 10/23/21		
394		SCG - Local Manufactured Housing Solicitation	341 days	Fri 11/1/19	Fri 2/19/21		
395		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		
396		SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20		
397		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
398		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
399		SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20		
400		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20		
401		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
402		SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20		
403		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
404		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
405		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
406		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
407		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
408		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
409		SCG - Final Award and Contract Signed	9 days	Thu 12/10/20	Tue 12/22/20		
410		SCG - Submit Advice Letter	0 days	N/A	N/A		
411		SCG - Advice Letter Approved	0 days	N/A	N/A		
412		SCG - Implementation Plan	44 days	Tue 12/22/20	Fri 2/19/21		
413		SCG - Local Large Commercial Solicitation	434 days	Fri 11/1/19	Wed 6/30/21		
414		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
415		SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20		
416		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
417		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
418		SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20		
419		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20		
420		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
421		SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20		
422		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
423		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
424		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
425		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
426		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
427		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
428		SCG - Final Award and Contract Signed	10 days	Thu 12/10/20	Wed 12/23/20		
429		SCG - Submit Advice Letter	64 days	Fri 1/1/21	Wed 3/31/21		
430		SCG - Advice Letter Approved	1 day	Fri 6/4/21	Fri 6/4/21		
431		SCG - Implementation Plan	43 days	Sat 6/5/21	Tue 8/3/21		
432		SCG - Local Agricultural Solicitation	434 days	Fri 11/1/19	Wed 6/30/21		
433		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		
434		SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20		
435		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
436		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
437		SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
438		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20		
439		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
440		SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20		
441		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
442		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
443		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
444		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
445		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
446		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
447		SCG - Final Award and Contract Signed	2 days	Fri 12/11/20	Mon 12/14/20		
448		SCG - Submit Advice Letter	41 days	Fri 1/1/21	Fri 2/26/21		
449		SCG - Advice Letter Approved	1 day	Wed 4/7/21	Wed 4/7/21		
450		SCG - Implementation Plan	43 days	Thu 4/8/21	Mon 6/7/21		
451		SCG - Local Behavioral Solicitation - Residential	413 days?	Fri 5/1/20	Tue 11/30/21		
452		SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
453		SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20		
454		SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20		
455		SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20		
456		SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20		
457		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20		
458		SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20		
459		SCG - RFP Release	1 day	Fri 1/15/21	Fri 1/15/21		
460		SCG - RFP Proposal Creation Duration	26 days	Mon 1/18/21	Mon 2/22/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
461		SCG - RFP Evaluation	29 days	Tue 2/23/21	Fri 4/2/21		
462		SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21		
463		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/13/21	Tue 4/13/21		
464		SCG - Contract Negotiation and Development	95 days	Mon 4/26/21	Fri 9/3/21		
465		SCG - Contract Review with EE PRG	9 days	Tue 9/7/21	Fri 9/17/21		
466		SCG - Final Award and Contract Signed	30 days	Mon 9/20/21	Fri 10/29/21		
467		SCG - Submit Advice Letter	21 days	Mon 11/1/21	Mon 11/29/21		
468		SCG - Advice Letter Approved	1 day	Wed 12/22/21	Wed 12/22/21		
469		SCG - Implementation Plan	43 days	Thu 12/23/21	Sun 2/20/22		
470		SCG - Local Behavioral Solicitation - Commercial	413 days?	Fri 5/1/20	Tue 11/30/21		
471		SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
472		SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20		
473		SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20		
474		SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20		
475		SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20		
476		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20		
477		SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20		
478		SCG - RFP Release	1 day	Fri 1/22/21	Fri 1/22/21		
479		SCG - RFP Proposal Creation Duration	26 days	Mon 1/25/21	Mon 3/1/21		
480		SCG - RFP Evaluation	24 days	Tue 3/2/21	Fri 4/2/21		
481		SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21		
482		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 11/12/21	Fri 11/12/21		
483		SCG - Contract Negotiation and Development	132 days	Mon 11/29/21	Tue 5/31/22		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
484		SCG - Contract Review with EE PRG	8 days	Sun 6/5/22	Tue 6/14/22		
485		SCG - Final Award and Contract Signed	109 days	Fri 7/1/22	Wed 11/30/22		
486		SCG - Submit Advice Letter	23 days	N/A	N/A		
487		SCG - Advice Letter Approved	1 day	N/A	N/A		
488		SCG - Implementation Plan	43 days	Thu 12/1/22	Sun 1/29/23		
489		SCG - Local Industrial Solicitation	434 days?	Tue 12/1/20	Fri 7/29/22		
490		SCG - RFA Preparation	63 days?	Tue 12/1/20	Thu 2/25/21		
491		SCG - RFA Release	1 day?	Fri 3/19/21	Fri 3/19/21		
492		SCG - RFA Abstract Creation Duration	25 days?	Mon 3/22/21	Fri 4/23/21		
493		SCG - RFA Evaluation	25 days?	Mon 4/26/21	Fri 5/28/21		
494		SCG - RFA Review with EE PRG	1 day?	Tue 6/1/21	Tue 6/1/21		
495		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 6/8/21	Tue 6/8/21		
496		SCG - RFP Preparation	67 days?	Thu 4/1/21	Fri 7/2/21		
497		SCG - RFP Release	1 day?	Fri 7/16/21	Fri 7/16/21		
498		SCG - RFP Proposal Creation Duration	30 days?	Mon 7/19/21	Fri 8/27/21		
499		SCG - RFP Evaluation	25 days?	Mon 8/30/21	Fri 10/1/21		
500		SCG - RFP Review with EE PRG	1 day?	Tue 10/5/21	Tue 10/5/21		
501		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 12/14/21	Tue 12/14/21		
502		SCG - Contract Negotiation and Development	127 days?	Thu 2/3/22	Fri 7/29/22		
503		SCG - Contract Review with EE PRG	9 days?	Tue 8/2/22	Fri 8/12/22		
504		SCG - Final Award and Contract Signed	21 days?	Fri 7/29/22	Fri 8/26/22		
505		SCG - Submit Advice Letter	1 day?	Sun 10/30/22	Sun 10/30/22		
506		SCG - Advice Letter Approved	1 day?	Mon 1/30/23	Mon 1/30/23		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
507		SCG - Implementation Plan	45 days?	Tue 1/31/23	Sat 4/1/23		
508		SCG - Large Public Sector Solicitation (re-Bid)	412 days	Mon 1/4/21	Tue 8/2/22		
509		SCG - RFA Preparation	65 days	Mon 1/4/21	Fri 4/2/21		
510		SCG - RFA Release	1 day	Fri 7/16/21	Fri 7/16/21		
511		SCG - RFA Abstract Creation Duration	20 days	Mon 7/19/21	Fri 8/13/21		
512		SCG - RFA Evaluation	15 days	Mon 8/16/21	Fri 9/3/21		
513		SCG - RFA Review with EE PRG	1 day	Tue 9/7/21	Tue 9/7/21		
514		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/14/21	Tue 9/14/21		
515		SCG - RFP Preparation	35 days	Mon 9/13/21	Fri 10/29/21		
516		SCG - RFP Release	1 day	Mon 11/8/21	Mon 11/8/21		
517		SCG - RFP Proposal Creation Duration	29 days	Tue 11/9/21	Fri 12/17/21		
518		SCG - RFP Evaluation	30 days	Mon 12/20/21	Fri 1/28/22		
519		SCG - RFP Review with EE PRG	1 day	Tue 2/1/22	Tue 2/1/22		
520		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/8/22	Tue 3/8/22		
521		SCG - Contract Negotiation and Development	79 days	Mon 3/14/22	Thu 6/30/22		
522		SCG - Contract Review with EE PRG	9 days	Tue 7/5/22	Fri 7/15/22		
523		SCG - Final Award and Contract Signed	63 days	Mon 7/18/22	Wed 10/12/22		
524		SCG - Submit Advice Letter	23 days	N/A	N/A		
525		SCG - Advice Letter Approved	1 day	N/A	N/A		
526		SCG - Implementation Plan	44 days	Wed 10/12/22	Sat 12/10/22		
527		SCG - Outreach Solicitation	434 days	Mon 2/1/21	Thu 9/29/22		
528		SCG - RFA Preparation	65 days	Mon 2/1/21	Fri 4/30/21		
529		SCG - RFA Release	1 day	Fri 5/21/21	Fri 5/21/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
530		SCG - RFA Abstract Creation Duration	25 days	Mon 5/24/21	Fri 6/25/21		
531		SCG - RFA Evaluation	25 days	Mon 6/28/21	Fri 7/30/21		
532		SCG - RFA Review with EE PRG	1 day	Tue 8/3/21	Tue 8/3/21		
533		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/10/21	Tue 8/10/21		
534		SCG - RFP Preparation	69 days	Tue 6/1/21	Fri 9/3/21		
535		SCG - RFP Release	1 day	Fri 9/17/21	Fri 9/17/21		
536		SCG - RFP Proposal Creation Duration	30 days	Mon 9/20/21	Fri 10/29/21		
537		SCG - RFP Evaluation	25 days	Mon 11/1/21	Fri 12/3/21		
538		SCG - RFP Review with EE PRG	1 day	Tue 12/7/21	Tue 12/7/21		
539		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 12/14/21	Tue 12/14/21		
540		SCG - Contract Negotiation and Development	54 days	Mon 1/17/22	Thu 3/31/22		
541		SCG - Contract Review with EE PRG	9 days	Tue 4/5/22	Fri 4/15/22		
542		SCG - Final Award and Contract Signed	10 days	Mon 4/18/22	Fri 4/29/22		
543		SCG - Submit Advice Letter	21 days	N/A	N/A		
544		SCG - Advice Letter Approved	1 day	N/A	N/A		
545		SCG - Implementation Plan	43 days	Sat 4/30/22	Tue 6/28/22		
546		SCG - Marketplace Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
547		SCG - RFA Preparation	64 days	Sat 5/1/21	Wed 7/28/21		
548		SCG - RFA Release	1 day	Fri 8/20/21	Fri 8/20/21		
549		SCG - RFA Abstract Creation Duration	25 days	Mon 8/23/21	Fri 9/24/21		
550		SCG - RFA Evaluation	25 days	Mon 9/27/21	Fri 10/29/21		
551		SCG - RFA Review with EE PRG	1 day	Tue 11/2/21	Tue 11/2/21		
552		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/9/21	Tue 11/9/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
553		SCG - RFP Preparation	91 days	Thu 8/26/21	Thu 12/30/21		
554		SCG - RFP Release	1 day	Fri 1/14/22	Fri 1/14/22		
555		SCG - RFP Proposal Creation Duration	30 days	Mon 1/17/22	Fri 2/25/22		
556		SCG - RFP Evaluation	25 days	Mon 2/28/22	Fri 4/1/22		
557		SCG - RFP Review with EE PRG	1 day	Tue 5/3/22	Tue 5/3/22		
558		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 5/11/22	Wed 5/11/22		
559		SCG - Contract Negotiation and Development	117 days	Wed 6/22/22	Thu 12/1/22		
560		SCG - Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22		
561		SCG - Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22		
562		SCG - Submit Advice Letter	20 days	Tue 1/3/23	Mon 1/30/23		
563		SCG - Advice Letter Approved	1 day	Tue 5/2/23	Tue 5/2/23		
564		SCG - Implementation Plan	44 days	Wed 5/3/23	Sun 7/2/23		
565		SCG - Residential Multi-Family - Whole Building	436 days?	Mon 3/1/21	Mon 10/31/22		
566		RFA Preparation	40 days	Mon 1/10/22	Fri 3/4/22		
567		RFA Release	1 day	Fri 3/25/22	Fri 3/25/22		
568		RFA Abstract Creation Duration	25 days	Mon 3/28/22	Fri 4/29/22		
569		RFA Evaluation	25 days	Mon 5/2/22	Fri 6/3/22		
570		RFA Review with EE PRG	1 day	Tue 6/7/22	Tue 6/7/22		
571		RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/14/22	Tue 6/14/22		
572		RFP Preparation	28 days	Sun 5/1/22	Tue 6/7/22		
573		RFP Release	1 day	Fri 6/24/22	Fri 6/24/22		
574		RFP Proposal Creation Duration	52 days	Mon 6/27/22	Tue 9/6/22		
575		RFP Evaluation	11 days	Fri 9/9/22	Fri 9/23/22		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
576		RFP Review with EE PRG	1 day	Thu 10/6/22	Thu 10/6/22		
577		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/11/22	Tue 10/11/22		
578		Contract Negotiation and Development	39 days	Tue 10/11/22	Fri 12/2/22		
579		Contract Review with EE PRG	1 day	Tue 12/6/22	Tue 12/6/22		
580		Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22		
581		Submit Advice Letter	22 days	Mon 1/2/23	Tue 1/31/23		
582		Advice Letter Approved	1 day	Fri 3/31/23	Fri 3/31/23		
583		Implementation Plan	43 days	Sat 4/1/23	Tue 5/30/23		
584		SCG—Youth Education Outreach Solicitation	331 days	Tue 3/1/22	Tue 6/6/23		
585		SCG - HERS Rater Training Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
586		RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22		
587		RFP Release	1 day	Fri 5/13/22	Fri 5/13/22		
588		RFP Proposal Creation Duration	20 days	Mon 5/16/22	Fri 6/10/22		
589		RFP Evaluation	59 days	Mon 6/13/22	Thu 9/1/22		
590		RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22		
591		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 8/31/22	Wed 8/31/22		
592		Contract Negotiation and Development	53 days	Fri 9/16/22	Tue 11/29/22		
593		Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22		
594		Final Award and Contract Signed	9 days	Mon 12/19/22	Thu 12/29/22		
595		Submit Advice Letter	N/A	N/A	N/A		
596		Advice Letter Approved	N/A	N/A	N/A		
597		Implementation Plan	42 days	Fri 12/30/22	Mon 2/27/23		
598		SCG - Retail Partnering Solicitation	29 days?	Tue 9/27/22	Fri 11/4/22		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
599		RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22		
600		RFP Release	1 day	Fri 6/17/22	Fri 6/17/22		
601		RFP Proposal Creation Duration	30 days	Mon 6/20/22	Fri 7/29/22		
602		RFP Evaluation	24 days	Mon 8/1/22	Thu 9/1/22		
603		RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22		
604		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/13/22	Tue 9/13/22		
605		Contract Negotiation and Development	29 days	Mon 9/19/22	Thu 10/27/22		
606		Contract Review with EE PRG	9 days	Tue 11/1/22	Fri 11/11/22		
607		Final Award and Contract Signed	13 days	Mon 11/14/22	Wed 11/30/22		
608		Submit Advice Letter	N/A	N/A	N/A		
609		Advice Letter Approved	N/A	N/A	N/A		
610		Implementation Plan	43 days	Sat 10/1/22	Tue 11/29/22		
611		SCG - Non-Residential EE Advisor Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
612		RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22		
613		RFP Release	1 day	Fri 8/26/22	Fri 8/26/22		
614		RFP Proposal Creation Duration	20 days	Mon 8/29/22	Fri 9/23/22		
615		RFP Evaluation	16 days	Sat 9/24/22	Fri 10/14/22		
616		RFP Review with EE PRG	5 days	Mon 10/17/22	Fri 10/21/22		
617		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/25/22	Tue 10/25/22		
618		Contract Negotiation and Development	32 days	Sun 10/30/22	Mon 12/12/22		
619		Contract Review with EE PRG	9 days	Tue 12/13/22	Fri 12/23/22		
620		Final Award and Contract Signed	4 days	Tue 12/27/22	Fri 12/30/22		
621		Submit Advice Letter	N/A	N/A	N/A		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
622		Advice Letter Approved	N/A	N/A	N/A		
623		Implementation Plan	44 days	Sun 1/1/23	Wed 3/1/23		
624		SCG - Residential EE Kits Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
625		RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22		
626		RFP Release	1 day	Mon 7/25/22	Mon 7/25/22		
627		RFP Proposal Creation Duration	16 days	Tue 7/26/22	Tue 8/16/22		
628		RFP Evaluation	12 days	Wed 8/17/22	Thu 9/1/22		
629		RFP Review with EE PRG	1 day	Tue 8/2/22	Tue 8/2/22		
630		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/9/22	Tue 8/9/22		
631		Contract Negotiation and Development	30 days	Mon 8/22/22	Fri 9/30/22		
632		Contract Review with EE PRG	9 days	Tue 10/4/22	Fri 10/14/22		
633		Final Award and Contract Signed	10 days	Mon 10/17/22	Fri 10/28/22		
634		Submit Advice Letter	N/A	N/A	N/A		
635		Advice Letter Approved	N/A	N/A	N/A		
636		Implementation Plan	43 days	Sat 10/29/22	Tue 12/27/22		
637		SCG - IDEEA 365	230 days	Mon 2/13/23	Fri 12/29/23		
638		RFP Preparation	23 days	Mon 2/13/23	Wed 3/15/23		
639		RFP Release	20 days	Thu 4/20/23	Wed 5/17/23		
640		RFP Proposal Creation Duration	43 days	Wed 5/3/23	Fri 6/30/23		
641		RFP Evaluation	12 days	Fri 7/14/23	Mon 7/31/23		
642		RFP Review with EE PRG	1 day	Tue 8/1/23	Tue 8/1/23		
643		RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Tue 8/1/23	Thu 8/31/23		
644		Contract Negotiation and Development	21 days	Fri 9/1/23	Fri 9/29/23		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
645		Contract Review with EE PRG	32 days	Mon 9/18/23	Tue 10/31/23		
646		Final Award and Contract Signed	17 days	Mon 10/9/23	Tue 10/31/23		
647		Submit Advice Letter	10 days	Wed 11/1/23	Tue 11/14/23		
648		Advice Letter Approved	11 days	Wed 11/22/23	Wed 12/6/23		
649		Implementation Plan	9 days	Tue 12/19/23	Fri 12/29/23		
650		SCG - Commercial SEM	110 days?	Tue 8/1/23	Mon 1/1/24		
651		RFP Preparation	22 days	Tue 8/1/23	Wed 8/30/23		
652		RFP Release	13 days	Wed 9/13/23	Fri 9/29/23		
653		RFP Proposal Creation Duration	11 days	Mon 10/2/23	Mon 10/16/23		
654		RFP Evaluation	5 days	Wed 10/25/23	Tue 10/31/23		
655		RFP Review with EE PRG	2 days	Tue 10/31/23	Wed 11/1/23		
656		RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Thu 11/2/23	Wed 11/8/23		
657		Contract Negotiation and Development	16 days	Wed 10/25/23	Wed 11/15/23		
658		Contract Review with EE PRG	1 day	Tue 12/5/23	Tue 12/5/23		
659		Final Award and Contract Signed	6 days	Wed 12/13/23	Wed 12/20/23		
660		Submit Advice Letter	5 days	Mon 12/18/23	Fri 12/22/23		
661		Advice Letter Approved	1 day	Fri 12/29/23	Fri 12/29/23		
662		Implementation Plan	1 day	Mon 1/1/24	Mon 1/1/24		
663		SCG - Market Access Program	333 days?	Sat 3/16/24	Tue 6/24/25		
664		RFP Preparation	75 days	Sat 3/16/24	Thu 6/27/24		
665		RFP Release	1 day	Fri 6/21/24	Fri 6/21/24		
666		RFP Proposal Creation Duration	53 days	Mon 6/24/24	Wed 9/4/24		
667		RFP Evaluation	38 days	Mon 8/19/24	Wed 10/9/24		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
668		RFP Review with EE PRG	1 day	Tue 10/1/24	Tue 10/1/24		
669		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/8/24	Tue 10/8/24		
670		Contract Negotiation and Development	78 days	Mon 10/14/24	Wed 1/29/25		
671		Contract Review with EE PRG	10 days	Tue 1/7/25	Mon 1/20/25		
672		Final Award and Contract Signed	11 days	Mon 1/20/25	Mon 2/3/25		
673		Submit Advice Letter	N/A	Wed 1/1/25			
674		Advice Letter Approved	N/A	Mon 3/3/25			
675		Implementation Plan	59 days	Thu 4/3/25	Tue 6/24/25		
676		SCG - IDEEA 365 (Round 3)	230 days?	Tue 10/15/24	Mon 9/1/25		
677		RFP Preparation	23 days	Tue 10/15/24	Thu 11/14/24		
678		RFP Release	20 days	Fri 11/15/24	Thu 12/12/24		
679		RFP Proposal Creation Duration	43 days	Fri 12/13/24	Tue 2/11/25		
680		RFP Evaluation	12 days	Wed 2/12/25	Thu 2/27/25		
681		RFP Review with EE PRG	1 day	Fri 2/28/25	Fri 2/28/25		
682		RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Mon 3/3/25	Wed 4/2/25		
683		Contract Negotiation and Development	21 days	Thu 4/3/25	Thu 5/1/25		
684		Contract Review with EE PRG	32 days	Fri 5/2/25	Mon 6/16/25		
685		Final Award and Contract Signed	17 days	Tue 6/17/25	Wed 7/9/25		
686		Submit Advice Letter	10 days	Thu 7/10/25	Wed 7/23/25		
687		Advice Letter Approved	11 days	Thu 7/24/25	Thu 8/7/25		
688		Implementation Plan	9 days	Fri 8/8/25	Wed 8/20/25		
689							
690		<i>Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change</i>					

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
691		SDG&E - Small Commercial (<20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20		
692		SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18		
693		SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18		
694		SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18		
695		SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19		
696		SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19		
697		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19		
698		SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19		
699		SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19		
700		SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19		
701		SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19		
702		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20		
703		SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20		
704		SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20		
705		SDG&E - Contract Review with EE PRG	0 days	Tue 6/9/20	Tue 6/9/20		
706		SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20		
707		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
708		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
709		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
710		SDG&E - Large Commercial (>20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20		
711		SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18		
712		SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18		
713		SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
714		SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19		
715		SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19		
716		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19		
717		SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19		
718		SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19		
719		SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19		
720		SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19		
721		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20		
722		SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20		
723		SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20		
724		SDG&E - Contract Review with EE PRG	0 days	Tue 5/12/20	Tue 5/12/20		
725		SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20		
726		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
727		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
728		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
729		SDG&E - Residential Multi-Family Solicitation	586 days	Thu 9/6/18	Thu 12/3/20		
730		SDG&E - RFA Preparation	64 days	Thu 9/6/18	Tue 12/4/18		
731		SDG&E - RFA Release	23 days	Tue 12/4/18	Thu 1/3/19		
732		SDG&E - RFA Abstract Creation Duration	49 days	Tue 9/11/18	Fri 11/16/18		
733		SDG&E - RFA Evaluation	21 days	Mon 1/7/19	Mon 2/4/19		
734		SDG&E - RFA Review with EE PRG	0 days	Tue 11/13/18	Tue 11/13/18		
735		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 3/20/19	Wed 3/20/19		
736		SDG&E - RFP Preparation	63 days	Fri 3/22/19	Tue 6/18/19		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
737		SDG&E - RFP Release	52 days	Tue 6/18/19	Wed 8/28/19		
738		SDG&E - RFP Proposal Creation Duration	36 days	Mon 3/25/19	Mon 5/13/19		
739		SDG&E - RFP Evaluation	30 days	Thu 8/29/19	Wed 10/9/19		
740		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Thu 12/12/19	Thu 12/19/19		
741		SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
742		SDG&E - Contract Negotiation and Development	35 days	Mon 4/13/20	Fri 5/29/20		
743		SDG&E - Contract Review with EE PRG	10 days	Thu 6/4/20	Wed 6/17/20		
744		SDG&E - Final Award and Contract Signed	0 days	Mon 6/22/20	Mon 6/22/20		
745		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
746		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
747		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
748		SDG&E - SW HVAC Solicitation	593 days	Thu 11/1/18	Tue 2/9/21		
749		SDG&E - RFA Preparation	48 days	Thu 11/1/18	Mon 1/7/19		
750		SDG&E - RFA Release	0 days	Mon 1/7/19	Mon 1/7/19		
751		SDG&E - RFA Abstract Creation Duration	24 days	Mon 1/7/19	Thu 2/7/19		
752		SDG&E - RFA Evaluation	37 days	Fri 2/8/19	Sun 3/31/19		
753		SDG&E - RFA Review with EE PRG	0 days	Tue 4/9/19	Tue 4/9/19		
754		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 4/17/19	Wed 4/17/19		
755		SDG&E - RFP Preparation	73 days	Thu 4/18/19	Mon 7/29/19		
756		SDG&E - RFP Release	0 days	Tue 9/3/19	Tue 9/3/19		
757		SDG&E - RFP Proposal Creation Duration	30 days	Tue 9/3/19	Mon 10/14/19		
758		SDG&E - RFP Evaluation	33 days	Mon 10/14/19	Wed 11/27/19		
759		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
760		SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
761		SDG&E - Contract Negotiation and Development	88 days	Wed 3/25/20	Fri 7/24/20		
762		SDG&E - Contract Review with EE PRG	0 days	Tue 9/8/20	Tue 9/8/20		
763		SDG&E - Final Award and Contract Signed	0 days	Fri 10/30/20	Fri 10/30/20		
764		SDG&E - Submit Advice Letter	0 days	Thu 11/12/20	Thu 11/12/20		
765		SDG&E - Advice Letter Approved	0 days	Fri 12/11/20	Fri 12/11/20		
766		SDG&E - Implementation Plan	0 days	Tue 2/9/21	Tue 2/9/21		
767		SDG&E - SW PLA Solicitation	853 days	Mon 1/28/19	Wed 5/4/22		
768		SDG&E - RFA Preparation	75 days	Mon 1/28/19	Fri 5/10/19		
769		SDG&E - RFA Release	0 days	Fri 5/10/19	Fri 5/10/19		
770		SDG&E - RFA Abstract Creation Duration	31 days	Fri 5/10/19	Fri 6/21/19		
771		SDG&E - RFA Evaluation	65 days	Mon 6/24/19	Fri 9/20/19		
772		SDG&E - RFA Review with EE PRG	0 days	Tue 9/10/19	Tue 9/10/19		
773		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 9/20/19	Fri 9/20/19		
774		SDG&E - RFP Preparation	52 days	Fri 9/20/19	Mon 12/2/19		
775		SDG&E - RFP Release	0 days	Mon 1/27/20	Mon 1/27/20		
776		SDG&E - RFP Proposal Creation Duration	31 days	Mon 1/27/20	Mon 3/9/20		
777		SDG&E - RFP Evaluation	82 days	Mon 3/9/20	Tue 6/30/20		
778		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/17/20	Mon 8/17/20		
779		SDG&E - Selection Review with EE PRG	66 days	Tue 10/13/20	Tue 1/12/21		
780		SDG&E - Contract Negotiation and Development	197 days	Fri 1/29/21	Mon 11/1/21		
781		SDG&E - Contract Review with EE PRG	0 days	Tue 11/9/21	Tue 11/9/21		
782		SDG&E - Final Award and Contract Signed	0 days	Fri 1/7/22	Fri 1/7/22		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
783		SDG&E - Submit Advice Letter	0 days	Mon 1/10/22	Mon 1/10/22		
784		SDG&E - Advice Letter Approved	0 days	Thu 2/10/22	Thu 2/10/22		
785		SDG&E - Implementation Plan	60 days	Thu 2/10/22	Wed 5/4/22		
786		SDG&E - Residential Single-Family 2.0 Solicitation	467 days	Tue 1/19/21	Wed 11/2/22		
787		SDG&E - RFA Preparation	43 days	Tue 1/19/21	Thu 3/18/21		
788		SDG&E - RFA Release	0 days	Mon 3/22/21	Mon 3/22/21		
789		SDG&E - RFA Abstract Creation Duration	22 days	Mon 3/22/21	Tue 4/20/21		
790		SDG&E - RFA Evaluation	38 days	Wed 4/21/21	Fri 6/11/21		
791		SDG&E - RFA Review with EE PRG	7 days	Thu 6/3/21	Fri 6/11/21		
792		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 6/15/21	Tue 6/15/21		
793		SDG&E - RFP Preparation	43 days	Wed 6/16/21	Fri 8/13/21		
794		SDG&E - RFP Release	0 days	Wed 8/18/21	Wed 8/18/21		
795		SDG&E - RFP Proposal Creation Duration	32 days	Wed 8/18/21	Thu 9/30/21		
796		SDG&E - RFP Evaluation	44 days	Fri 10/1/21	Wed 12/1/21		
797		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 12/14/21	Tue 12/14/21		
798		SDG&E - Selection Review with EE PRG	7 days	Thu 12/2/21	Fri 12/10/21		
799		SDG&E - Contract Negotiation and Development	96 days	Mon 12/20/21	Mon 5/2/22		
800		SDG&E - Contract Review with EE PRG	7 days	Thu 5/5/22	Fri 5/13/22		
801		SDG&E - Final Award and Contract Signed	0 days	Tue 5/31/22	Tue 5/31/22		
802		SDG&E - Submit Advice Letter	0 days	Fri 6/24/22	Fri 6/24/22		
803		SDG&E - Advice Letter Approved	0 days	Thu 8/11/22	Thu 8/11/22		
804		SDG&E - Implementation Plan	60 days	Thu 8/11/22	Wed 11/2/22		
805		SDG&E - Residential Single-Family Solicitation	501 days	Mon 7/1/19	Tue 6/1/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
806		SDG&E - RFA Preparation	80 days	Mon 7/1/19	Fri 10/18/19		
807		SDG&E - RFA Release	35 days	Fri 10/18/19	Thu 12/5/19		
808		SDG&E - RFA Abstract Creation Duration	53 days	Mon 7/22/19	Wed 10/2/19		
809		SDG&E - RFA Evaluation	29 days	Fri 12/6/19	Wed 1/15/20		
810		SDG&E - RFA Review with EE PRG	0 days	Tue 10/8/19	Tue 10/8/19		
811		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 2/27/20	Thu 2/27/20		
812		SDG&E - RFP Preparation	48 days	Fri 2/28/20	Tue 5/5/20		
813		SDG&E - RFP Release	0 days	Mon 4/27/20	Mon 4/27/20		
814		SDG&E - RFP Proposal Creation Duration	32 days	Mon 4/27/20	Tue 6/9/20		
815		SDG&E - RFP Evaluation	16 days	Wed 6/10/20	Wed 7/1/20		
816		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 7/23/20	Fri 7/24/20		
817		SDG&E - Selection Review with EE PRG	7 days	Thu 8/6/20	Fri 8/14/20		
818		SDG&E - Contract Negotiation and Development	60 days	Mon 8/17/20	Fri 11/6/20		
819		SDG&E - Contract Review with EE PRG	10 days	Tue 12/8/20	Mon 12/21/20		
820		SDG&E - Final Award and Contract Signed	0 days	Fri 1/29/21	Fri 1/29/21		
821		SDG&E - Submit Advice Letter	0 days	Mon 3/1/21	Mon 3/1/21		
822		SDG&E - Advice Letter Approved					
823		SDG&E - Implementation Plan	0 days	Tue 6/1/21	Tue 6/1/21		
824		SDG&E - Public Sector: Federal Solicitation	625 days	Mon 7/1/19	Fri 11/19/21		
825		SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19		
826		SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19		
827		SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19		
828		SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
829		SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
830		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20		
831		SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20		
832		SDG&E - RFP Release	0 days	Fri 5/22/20	Fri 5/22/20		
833		SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20		
834		SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20		
835		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20		
836		SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20		
837		SDG&E - Contract Negotiation and Development	53 days	Wed 2/17/21	Fri 4/30/21		
838		SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21		
839		SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21		
840		SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21		
841		SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21		
842		SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21		
843		SDG&E - Public Sector: K-12 Solicitation	625 days	Mon 7/1/19	Fri 11/19/21		
844		SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19		
845		SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19		
846		SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19		
847		SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20		
848		SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
849		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20		
850		SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20		
851		SDG&E - RFP Release	1 day	Fri 5/22/20	Fri 5/22/20		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
852		SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20		
853		SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20		
854		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20		
855		SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20		
856		SDG&E - Contract Negotiation and Development	117 days	Thu 11/19/20	Fri 4/30/21		
857		SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21		
858		SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21		
859		SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21		
860		SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21		
861		SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21		
862		SDG&E - Public Sector: Local Government Solicitation	338 days	Tue 10/13/20	Thu 1/27/22		
863		SDG&E - RFA Preparation	10 days	Fri 10/23/20	Thu 11/5/20		
864		SDG&E - RFA Release	1 day	Wed 1/27/21	Wed 1/27/21		
865		SDG&E - RFA Abstract Creation Duration	20 days	Thu 1/28/21	Wed 2/24/21		
866		SDG&E - RFA Evaluation	18 days	Fri 2/26/21	Tue 3/23/21		
867		SDG&E - RFA Review with EE PRG	7 days	Thu 4/8/21	Fri 4/16/21		
868		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/21/21	Wed 4/21/21		
869		SDG&E - RFP Preparation	51 days	Fri 3/19/21	Fri 5/28/21		
870		SDG&E - RFP Release	1 day	Tue 6/1/21	Tue 6/1/21		
871		SDG&E - RFP Proposal Creation Duration	26 days	Wed 6/2/21	Wed 7/7/21		
872		SDG&E - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21		
873		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/25/21	Mon 10/25/21		
874		SDG&E - Selection Review with EE PRG	7 days	Tue 10/12/21	Wed 10/20/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
875		SDG&E - Contract Negotiation and Development	41 days	Fri 11/5/21	Fri 12/31/21		
876		SDG&E - Contract Review with EE PRG	7 days	Thu 1/6/22	Fri 1/14/22		
877		SDG&E - Final Award and Contract Signed	9 days	Mon 1/17/22	Thu 1/27/22		
878		SDG&E - Submit Advice Letter	13 days	Wed 6/1/22	Fri 6/17/22		
879		SDG&E - Advice Letter Approved	40 days	Fri 6/17/22	Thu 8/11/22		
880		SDG&E - Implementation Plan	42 days	Mon 8/15/22	Tue 10/11/22		
881		SDG&E - Agricultural Sector: Local Agriculture Solicitation	447 days	Mon 3/1/21	Tue 11/15/22		
882		SDG&E - RFA Preparation	56 days	Mon 3/1/21	Mon 5/17/21		
883		SDG&E - RFA Release	0 days	Mon 4/26/21	Mon 4/26/21		
884		SDG&E - RFA Abstract Creation Duration	20 days	Tue 4/27/21	Mon 5/24/21		
885		SDG&E - RFA Evaluation	36 days	Tue 6/1/21	Tue 7/20/21		
886		SDG&E - RFA Review with EE PRG	0 days	Thu 7/8/21	Thu 7/8/21		
887		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 7/20/21	Tue 7/20/21		
888		SDG&E - RFP Preparation	48 days	Tue 7/20/21	Thu 9/23/21		
889		SDG&E - RFP Release	0 days	Thu 9/23/21	Thu 9/23/21		
890		SDG&E - RFP Proposal Creation Duration	25 days	Fri 9/24/21	Thu 10/28/21		
891		SDG&E - RFP Evaluation	23 days	Thu 10/28/21	Mon 11/29/21		
892		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 2/1/22	Tue 2/1/22		
893		SDG&E - Selection Review with EE PRG	0 days	Tue 2/8/22	Tue 2/8/22		
894		SDG&E - Contract Negotiation and Development	83 days	Tue 2/1/22	Thu 5/26/22		
895		SDG&E - Contract Review with EE PRG	0 days	Tue 6/14/22	Tue 6/14/22		
896		SDG&E - Final Award and Contract Signed	10 days	Fri 6/18/21	Thu 7/1/21		
897		SDG&E - Submit Advice Letter	0 days	Fri 7/22/22	Fri 7/22/22		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
898		SDG&E - Advice Letter Approved	0 days	Tue 8/30/22	Tue 8/30/22		
899		SDG&E - Implementation Plan	44 days	Wed 8/31/22	Sat 10/29/22		
900		*SDG&E - Industrial Solicitation	426 days	Thu 4/1/21	Thu 11/17/22		
901		SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21		
902		SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21		
903		SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21		
904		SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21		
905		SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21		
906		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21		
907		SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21		
908		SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21		
909		SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22		
910		SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22		
911		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22		
912		SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22		
913		SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22		
914		SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22		
915		SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22		
916		SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22		
917		SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22		
918		SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23		
919		*SDG&E - Industrial-Port Tenants Solicitation	426 days	Thu 4/1/21	Thu 11/17/22		
920		SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
921		SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21		
922		SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21		
923		SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21		
924		SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21		
925		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21		
926		SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21		
927		SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21		
928		SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22		
929		SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22		
930		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22		
931		SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22		
932		SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22		
933		SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22		
934		SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22		
935		SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22		
936		SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22		
937		SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23		
938		*SDG&E - SW Residential HVAC QI/QM Solicitation	377 days	Mon 7/5/21	Tue 12/13/22		
939		SDG&E - RFA Preparation	48 days	Mon 7/5/21	Wed 9/8/21		
940		SDG&E - RFA Release	1 day	Wed 9/29/21	Wed 9/29/21		
941		SDG&E - RFA Abstract Creation Duration	22 days	Wed 9/29/21	Thu 10/28/21		
942		SDG&E - RFA Evaluation	21 days	Fri 10/29/21	Fri 11/26/21		
943		SDG&E - RFA Review with EE PRG	6 days	Fri 12/10/21	Fri 12/17/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	H2	2005 H1
944		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 12/22/21	Wed 12/22/21		
945		SDG&E - RFP Preparation	56 days	Tue 1/4/22	Tue 3/22/22		
946		SDG&E - RFP Release	1 day	Tue 3/22/22	Tue 3/22/22		
947		SDG&E - RFP Proposal Creation Duration	23 days	Wed 3/23/22	Fri 4/22/22		
948		SDG&E - RFP Evaluation	20 days	Mon 4/25/22	Fri 5/20/22		
949		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/21/22	Tue 6/21/22		
950		SDG&E - Selection Review with EE PRG	0 days	Fri 6/17/22	Fri 6/17/22		
951		SDG&E - Contract Negotiation and Development	83 days	Wed 7/20/22	Fri 11/11/22		
952		SDG&E - Contract Review with EE PRG	6 days	Mon 11/14/22	Mon 11/21/22		
953		SDG&E - Final Award and Contract Signed	1 day	Mon 1/10/22	Mon 1/10/22		
954		SDG&E - Submit Advice Letter	22 days	Sun 1/15/23	Mon 2/13/23		
955		SDG&E - Advice Letter Approved	1 day	Fri 4/28/23	Fri 4/28/23		
956		SDG&E - Implementation Plan	60 days	Fri 4/28/23	Thu 7/20/23		
957		*SDG&E - Local/Residential Behavioral Solicitation	472 days	Mon 4/19/21	Tue 2/7/23		
958		SDG&E - RFA Preparation	53 days	Mon 4/19/21	Wed 6/30/21		
959		SDG&E - RFA Release	1 day	Mon 7/26/21	Mon 7/26/21		
960		SDG&E - RFA Abstract Creation Duration	21 days	Mon 7/26/21	Mon 8/23/21		
961		SDG&E - RFA Evaluation	30 days	Tue 8/24/21	Mon 10/4/21		
962		SDG&E - RFA Review with EE PRG	7 days	Thu 10/7/21	Fri 10/15/21		
963		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/19/21	Tue 10/19/21		
964		SDG&E - RFP Preparation	28 days	Thu 10/21/21	Mon 11/29/21		
965		SDG&E - RFP Release	1 day	Wed 12/22/21	Wed 12/22/21		
966		SDG&E - RFP Proposal Creation Duration	20 days	Wed 12/22/21	Tue 1/18/22		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	H2	2005 H1
967		SDG&E - RFP Evaluation	28 days	Wed 1/19/22	Fri 2/25/22		
968		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/15/22	Tue 3/15/22		
969		SDG&E - Selection Review with EE PRG	7 days	Thu 3/3/22	Fri 3/11/22		
970		SDG&E - Contract Negotiation and Development	119 days	Fri 3/18/22	Wed 8/31/22		
971		SDG&E - Contract Review with EE PRG	7 days	Thu 9/8/22	Fri 9/16/22		
972		SDG&E - Final Award and Contract Signed	1 day	Fri 10/21/22	Fri 10/21/22		
973		SDG&E - Submit Advice Letter	1 day	Wed 11/16/22	Wed 11/16/22		
974		SDG&E - Advice Letter Approved	1 day	Fri 12/16/22	Fri 12/16/22		
975		SDG&E - Implementation Plan	60 days	Wed 11/16/22	Tue 2/7/23		
976		*SDG&E - Small Business Outreach Solicitation	298 days?	Wed 4/13/22	Fri 6/2/23		
977		SDG&E - RFA Preparation	53 days	Wed 4/13/22	Fri 6/24/22		
978		SDG&E - RFA Release	1 day	Thu 7/7/22	Thu 7/7/22		
979		SDG&E - RFA Abstract Creation Duration	21 days	Fri 7/8/22	Fri 8/5/22		
980		SDG&E - RFA Evaluation	30 days	Mon 8/8/22	Fri 9/16/22		
981		SDG&E - RFA Review with EE PRG	5 days	Mon 9/19/22	Fri 9/23/22		
982		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/27/22	Tue 9/27/22		
983		SDG&E - RFP Preparation	28 days	Mon 8/8/22	Wed 9/14/22		
984		SDG&E - RFP Release	1 day	Tue 10/18/22	Tue 10/18/22		
985		SDG&E - RFP Proposal Creation Duration	31 days	Tue 10/18/22	Tue 11/29/22		
986		SDG&E - RFP Evaluation	38 days	Wed 11/30/22	Fri 1/20/23		
987		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/28/23	Tue 2/28/23		
988		SDG&E - Selection Review with EE PRG	7 days	Thu 2/16/23	Fri 2/24/23		
989		SDG&E - Contract Negotiation and Development	79 days	Tue 2/28/23	Fri 6/16/23		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




ID		Task Name	Duration	Start	Finish	H2	2005 H1
990		SDG&E - Contract Review with EE PRG	4 days	Wed 6/21/23	Mon 6/26/23		
991		SDG&E - Final Award and Contract Signed	1 day	Tue 8/29/23	Tue 8/29/23		
992		SDG&E - Submit Advice Letter	1 day	Fri 9/15/23	Fri 9/15/23		
993		SDG&E - Advice Letter Approved	1 day	Mon 10/16/23	Mon 10/16/23		
994		SDG&E - Implementation Plan	46 days	Mon 10/16/23	Mon 12/18/23		
995		*SDG&E - Workforce Education & Training /Integrated Energy Education Solicitatio	353 days?	Mon 1/16/23	Wed 5/22/24		
996		SDG&E - RFP Release	1 day?	Thu 2/2/23	Thu 2/2/23		
997		SDG&E - RFP Evaluation	25 days	Fri 3/17/23	Thu 4/20/23		
998		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/16/23	Tue 5/16/23		
999		SDG&E - Selection Review with EE PRG	5 days	Tue 5/9/23	Mon 5/15/23		
1000		SDG&E - Contract Negotiation and Development	94 days	Fri 5/5/23	Wed 9/13/23		
1001		SDG&E - Contract Review with EE PRG	7 days	Tue 10/10/23	Wed 10/18/23		
1002		SDG&E - Final Award and Contract Signed	1 day	Tue 11/14/23	Tue 11/14/23		
1003		SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24		
1004		SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24		
1005		SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24		
1006		*SDG&E - Residential Equity Education & Outreach Solicitation	331 days?	Fri 1/13/23	Fri 4/19/24		
1007		SDG&E - RFA Release	1 day	Thu 3/2/23	Thu 3/2/23		
1008		SDG&E - RFA Evaluation	21 days	Wed 4/12/23	Wed 5/10/23		
1009		SDG&E - RFA Review with EE PRG	7 days	Fri 5/19/23	Mon 5/29/23		
1010		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/30/23	Tue 5/30/23		
1011		SDG&E - RFP Release	1 day	Thu 6/1/23	Thu 6/1/23		
1012		SDG&E - RFP Evaluation	27 days	Mon 7/17/23	Tue 8/22/23		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1013		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/28/23	Mon 8/28/23		
1014		SDG&E - Selection Review with EE PRG	7 days	Wed 8/30/23	Thu 9/7/23		
1015		SDG&E - Contract Negotiation and Development	32 days	Thu 11/2/23	Fri 12/15/23		
1016		SDG&E - Contract Review with EE PRG	7 days	Tue 1/9/24	Wed 1/17/24		
1017		SDG&E - Final Award and Contract Signed	1 day	Mon 2/12/24	Mon 2/12/24		
1018		SDG&E - Submit Advice Letter	1 day	Mon 2/26/24	Mon 2/26/24		
1019		SDG&E - Advice Letter Approved	1 day	Mon 4/8/24	Mon 4/8/24		
1020		SDG&E - Implementation Plan	60 days	Tue 4/9/24	Mon 7/1/24		
1021		*SDG&E - Non-Residential Behavioral Solicitation	398 days	Mon 8/15/22	Wed 2/21/24		
1022		SDG&E - RFA Preparation	67 days	Mon 8/15/22	Tue 11/15/22		
1023		SDG&E - RFA Release	1 day	Mon 10/24/22	Mon 10/24/22		
1024		SDG&E - RFA Abstract Creation Duration	27 days	Tue 8/23/22	Wed 9/28/22		
1025		SDG&E - RFA Evaluation	16 days	Tue 11/29/22	Tue 12/20/22		
1026		SDG&E - RFA Review with EE PRG	7 days	Thu 1/5/23	Fri 1/13/23		
1027		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 1/18/23	Wed 1/18/23		
1028		SDG&E - RFP Preparation	26 days	Mon 11/14/22	Mon 12/19/22		
1029		SDG&E - RFP Release	1 day	Mon 1/23/23	Mon 1/23/23		
1030		SDG&E - RFP Proposal Creation Duration	26 days	Mon 1/23/23	Mon 2/27/23		
1031		SDG&E - RFP Evaluation	58 days	Tue 2/28/23	Thu 5/18/23		
1032		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/20/23	Tue 6/20/23		
1033		SDG&E - Selection Review with EE PRG	7 days	Thu 6/8/23	Fri 6/16/23		
1034		SDG&E - Contract Negotiation and Development	60 days	Wed 6/21/23	Tue 9/12/23		
1035		SDG&E - Contract Review with EE PRG	7 days	Thu 10/5/23	Fri 10/13/23		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1036		SDG&E - Final Award and Contract Signed	1 day	Thu 12/21/23	Thu 12/21/23		
1037		SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24		
1038		SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24		
1039		SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24		
1040		*SDG&E - Retail Offices and Wholesale Solicitation	398 days	Wed 5/10/23	Fri 11/15/24		
1041		SDG&E - RFA Preparation	33 days	Wed 5/10/23	Fri 6/23/23		
1042		SDG&E - RFA Release	1 day	Mon 7/3/23	Mon 7/3/23		
1043		SDG&E - RFA Abstract Creation Duration	31 days	Tue 7/4/23	Tue 8/15/23		
1044		SDG&E - RFA Evaluation	19 days	Wed 8/16/23	Mon 9/11/23		
1045		SDG&E - RFA Review with EE PRG	3 days	Mon 9/18/23	Wed 9/20/23		
1046		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 9/25/23	Mon 9/25/23		
1047		SDG&E - RFP Preparation	33 days	Wed 7/5/23	Fri 8/18/23		
1048		SDG&E - RFP Release	1 day	Fri 9/29/23	Fri 9/29/23		
1049		SDG&E - RFP Proposal Creation Duration	33 days	Mon 10/2/23	Wed 11/15/23		
1050		SDG&E - RFP Evaluation	25 days	Thu 11/16/23	Wed 12/20/23		
1051		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 2/19/24	Mon 2/19/24		
1052		SDG&E - Selection Review with EE PRG	7 days	Thu 2/8/24	Fri 2/16/24		
1053		SDG&E - Contract Negotiation and Development	96 days	Mon 2/26/24	Mon 7/8/24		
1054		SDG&E - Contract Review with EE PRG	6 days	Wed 7/17/24	Wed 7/24/24		
1055		SDG&E - Final Award and Contract Signed	1 day	Tue 8/27/24	Tue 8/27/24		
1056		SDG&E - Submit Advice Letter	1 day	Mon 9/16/24	Mon 9/16/24		
1057		SDG&E - Advice Letter Approved	1 day	Mon 10/14/24	Mon 10/14/24		
1058		SDG&E - Implementation Plan	46 days	Mon 10/14/24	Mon 12/16/24		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1059		*SDG&E - Groceries, Restaurants and Food Storage Solicitation	398 days	Wed 6/14/23	Fri 12/20/24		
1060		SDG&E - RFA Preparation	33 days	Wed 6/14/23	Fri 7/28/23		
1061		SDG&E - RFA Release	1 day	Tue 8/15/23	Tue 8/15/23		
1062		SDG&E - RFA Abstract Creation Duration	21 days	Wed 8/16/23	Wed 9/13/23		
1063		SDG&E - RFA Evaluation	15 days	Thu 9/14/23	Wed 10/4/23		
1064		SDG&E - RFA Review with EE PRG	5 days	Wed 10/18/23	Tue 10/24/23		
1065		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/30/23	Mon 10/30/23		
1066		SDG&E - RFP Preparation	16 days	Mon 10/9/23	Mon 10/30/23		
1067		SDG&E - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23		
1068		SDG&E - RFP Proposal Creation Duration	33 days	Mon 11/6/23	Wed 12/20/23		
1069		SDG&E - RFP Evaluation	34 days	Thu 12/21/23	Tue 2/6/24		
1070		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/22/24	Thu 2/22/24		
1071		SDG&E - Selection Review with EE PRG	7 days	Thu 2/29/24	Fri 3/8/24		
1072		SDG&E - Contract Negotiation and Development	60 days	Tue 2/27/24	Mon 5/20/24		
1073		SDG&E - Contract Review with EE PRG	9 days	Thu 6/27/24	Tue 7/9/24		
1074		SDG&E - Final Award and Contract Signed	1 day	Mon 7/15/24	Mon 7/15/24		
1075		SDG&E - Submit Advice Letter	1 day	Mon 7/22/24	Mon 7/22/24		
1076		SDG&E - Advice Letter Approved	1 day	Tue 9/3/24	Tue 9/3/24		
1077		SDG&E - Implementation Plan	60 days	Wed 9/4/24	Tue 11/26/24		
1078		*SDG&E - Private Institutions and Healthcare Solicitation	398 days	Thu 10/5/23	Mon 4/14/25		
1079		SDG&E - RFA Preparation	33 days	Thu 10/5/23	Mon 11/20/23		
1080		SDG&E - RFA Release	1 day	Mon 11/27/23	Mon 11/27/23		
1081		SDG&E - RFA Abstract Creation Duration	35 days	Mon 11/27/23	Fri 1/12/24		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1082		SDG&E - RFA Evaluation	30 days	Mon 1/15/24	Fri 2/23/24		
1083		SDG&E - RFA Review with EE PRG	5 days	Mon 2/26/24	Fri 3/1/24		
1084		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 3/4/24	Mon 3/4/24		
1085		SDG&E - RFP Preparation	54 days	Mon 11/27/23	Thu 2/8/24		
1086		SDG&E - RFP Release	1 day	Fri 3/8/24	Fri 3/8/24		
1087		SDG&E - RFP Proposal Creation Duration	34 days	Fri 3/8/24	Wed 4/24/24		
1088		SDG&E - RFP Evaluation	42 days	Thu 4/25/24	Fri 6/21/24		
1089		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 7/2/24	Tue 7/2/24		
1090		SDG&E - Selection Review with EE PRG	7 days	Fri 6/21/24	Mon 7/1/24		
1091		SDG&E - Contract Negotiation and Development	62 days	Mon 7/15/24	Tue 10/8/24		
1092		SDG&E - Contract Review with EE PRG	7 days	Mon 10/21/24	Tue 10/29/24		
1093		SDG&E - Final Award and Contract Signed	1 day	Fri 12/6/24	Fri 12/6/24		
1094		SDG&E - Submit Advice Letter	1 day	Fri 12/13/24	Fri 12/13/24		
1095		SDG&E - Advice Letter Approved	1 day	Tue 1/14/25	Tue 1/14/25		
1096		SDG&E - Implementation Plan	46 days	Wed 1/15/25	Wed 3/19/25		
1097		*SDG&E - Lodging: Hotels/Motels Solicitation	398 days	Tue 10/10/23	Thu 4/17/25		
1098		SDG&E - RFA Preparation	33 days	Tue 10/10/23	Thu 11/23/23		
1099		SDG&E - RFA Release	1 day	Fri 12/8/23	Fri 12/8/23		
1100		SDG&E - RFA Abstract Creation Duration	35 days	Fri 12/8/23	Thu 1/25/24		
1101		SDG&E - RFA Evaluation	22 days	Mon 1/22/24	Tue 2/20/24		
1102		SDG&E - RFA Review with EE PRG	7 days	Tue 3/12/24	Wed 3/20/24		
1103		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/19/24	Tue 3/19/24		
1104		SDG&E - RFP Preparation	48 days	Tue 1/23/24	Thu 3/28/24		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1105		SDG&E - RFP Release	1 day	Thu 3/21/24	Thu 3/21/24		
1106		SDG&E - RFP Proposal Creation Duration	29 days	Thu 3/21/24	Tue 4/30/24		
1107		SDG&E - RFP Evaluation	23 days	Mon 5/6/24	Wed 6/5/24		
1108		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/18/24	Tue 6/18/24		
1109		SDG&E - Selection Review with EE PRG	7 days	Thu 6/20/24	Fri 6/28/24		
1110		SDG&E - Contract Negotiation and Development	60 days	Wed 7/17/24	Tue 10/8/24		
1111		SDG&E - Contract Review with EE PRG	9 days	Thu 10/24/24	Tue 11/5/24		
1112		SDG&E - Final Award and Contract Signed	1 day	Tue 12/10/24	Tue 12/10/24		
1113		SDG&E - Submit Advice Letter	1 day	Tue 12/17/24	Tue 12/17/24		
1114		SDG&E - Advice Letter Approved	1 day	Tue 1/14/25	Tue 1/14/25		
1115		SDG&E - Implementation Plan	46 days	Mon 1/20/25	Mon 3/24/25		
1116		*SDG&E - Market Access Program (MAP)	317 days	Wed 3/13/24	Thu 5/29/25		
1117		SDG&E - RFP Preparation	38 days	Wed 3/13/24	Fri 5/3/24		
1118		SDG&E - RFP Release	1 day	Tue 5/7/24	Tue 5/7/24		
1119		SDG&E - RFP Proposal Creation Duration	31 days	Tue 5/7/24	Tue 6/18/24		
1120		SDG&E - RFP Evaluation	43 days	Wed 6/19/24	Fri 8/16/24		
1121		SDG&E - Selection Review with EE PRG	7 days	Thu 9/5/24	Fri 9/13/24		
1122		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/17/24	Tue 9/17/24		
1123		SDG&E - Contract Negotiation and Development	60 days	Fri 9/27/24	Thu 12/19/24		
1124		SDG&E - Contract Review with EE PRG	7 days	Thu 1/9/25	Fri 1/17/25		
1125		SDG&E - Final Award and Contract Signed	1 day	Fri 1/31/25	Fri 1/31/25		
1126		SDG&E - Submit Advice Letter	1 day	Fri 2/14/25	Fri 2/14/25		
1127		SDG&E - Advice Letter Approved	1 day	Mon 3/31/25	Mon 3/31/25		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1128		SDG&E - Implementation Plan	44 days	Mon 3/31/25	Thu 5/29/25		
1129		Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change					
1130							
1131		PG&E - Local Government Partnerships (non-resource programs) Solicitation	376 days?	Fri 3/22/19	Fri 8/28/20		
1132		PG&E - RFA Preparation	42 days	Fri 3/22/19	Mon 5/20/19		
1133		PG&E - RFA Release	1 day	Thu 5/23/19	Thu 5/23/19		
1134		PG&E - RFA Abstract Creation Duration	22 days	Thu 5/23/19	Fri 6/21/19		
1135		PG&E - RFA Evaluation	15 days	Mon 6/24/19	Fri 7/12/19		
1136		PG&E - RFA Review with EE PRG	4 days	Tue 7/23/19	Fri 7/26/19		
1137		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/5/19	Fri 8/9/19		
1138		PG&E - RFP Preparation	45 days	Tue 8/27/19	Mon 10/28/19		
1139		PG&E - RFP Release	1 day	Mon 11/4/19	Mon 11/4/19		
1140		PG&E - RFP Proposal Creation Duration	33 days	Mon 11/4/19	Wed 12/18/19		
1141		PG&E - RFP Evaluation	18 days	Mon 1/6/20	Wed 1/29/20		
1142		PG&E - RFP Review with EE PRG	4 days	Tue 2/25/20	Fri 2/28/20		
1143		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/2/20	Fri 3/6/20		
1144		PG&E - Contract Negotiation and Development	58 days	Fri 2/28/20	Tue 5/19/20		
1145		PG&E - Contract Review with EE PRG	7 days	Tue 5/26/20	Wed 6/3/20		
1146		PG&E - Final Award and Contract Signed	22 days	Fri 5/29/20	Mon 6/29/20		
1147		PG&E - Submit Advice Letter		N/A	N/A		
1148		PG&E - Advice Letter Approved					
1149		PG&E - Implementation Plan	24 days	Tue 7/28/20	Fri 8/28/20		
1150		PG&E - Statewide Codes & Standards (RFP only) Solicitation	221 days?	Mon 7/8/19	Mon 5/11/20		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1151		PG&E - RFA Preparation		N/A	N/A		
1152		PG&E - RFA Release		N/A	N/A		
1153		PG&E - RFA Abstract Creation Duration		N/A	N/A		
1154		PG&E - RFA Evaluation		N/A	N/A		
1155		PG&E - RFA Review with EE PRG		N/A	N/A		
1156		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A		
1157		PG&E - RFP Preparation	36 days	Mon 7/8/19	Mon 8/26/19		
1158		PG&E - RFP Release	1 day	Tue 9/10/19	Tue 9/10/19		
1159		PG&E - RFP Proposal Creation Duration	24 days	Tue 9/10/19	Fri 10/11/19		
1160		PG&E - RFP Evaluation	10 days	Mon 10/14/19	Fri 10/25/19		
1161		PG&E - RFP Review with EE PRG	4 days	Thu 11/21/19	Tue 11/26/19		
1162		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 11/27/19	Fri 11/29/19		
1163		PG&E - Contract Negotiation and Development	35 days	Mon 12/2/19	Fri 1/17/20		
1164		PG&E - Contract Review with EE PRG	4 days	Tue 1/21/20	Fri 1/24/20		
1165		PG&E - Final Award and Contract Signed	32 days	Wed 1/29/20	Thu 3/12/20		
1166		PG&E - Submit Advice Letter		N/A	N/A		
1167		PG&E - Advice Letter Approved					
1168		PG&E - Implementation Plan	32 days	Fri 3/27/20	Mon 5/11/20		
1169		PG&E - Local Multi-Sector (40% outsource) Solicitation	251 days?	Tue 4/28/20	Tue 4/13/21		
1170		PG&E - RFA Preparation		N/A	N/A		
1171		PG&E - RFA Release		N/A	N/A		
1172		PG&E - RFA Abstract Creation Duration		N/A	N/A		
1173		PG&E - RFA Evaluation		N/A	N/A		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1174		PG&E - RFA Review with EE PRG		N/A	N/A		
1175		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A		
1176		PG&E - RFP Preparation		N/A	N/A		
1177		PG&E - RFP Release		N/A	N/A		
1178		PG&E - RFP Proposal Creation Duration		N/A	N/A		
1179		PG&E - RFP Evaluation		N/A	N/A		
1180		PG&E - RFP Review with EE PRG	4 days	Tue 4/28/20	Fri 5/1/20		
1181		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder					
1182		PG&E - Contract Negotiation and Development	81 days	Thu 7/2/20	Thu 10/22/20		
1183		PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20		
1184		PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20		
1185		PG&E - Submit Advice Letter	1 day	Wed 1/13/21	Wed 1/13/21		
1186		PG&E - Advice Letter Approved	1 day?	Fri 2/12/21	Fri 2/12/21		
1187		PG&E - Implementation Plan	43 days	Sat 2/13/21	Tue 4/13/21		
1188		PG&E - Statewide New Constructions (Non-Residential) Solicitation	591 days	Mon 3/25/19	Sun 6/27/21		
1189		PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19		
1190		PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19		
1191		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19		
1192		PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19		
1193		PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19		
1194		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19		
1195		PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20		
1196		PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1197		PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20		
1198		PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20		
1199		PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20		
1200		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20		
1201		PG&E - Contract Negotiation and Development	49 days	Mon 8/17/20	Thu 10/22/20		
1202		PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20		
1203		PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20		
1204		PG&E - Submit Advice Letter	1 day	Fri 2/19/21	Fri 2/19/21		
1205		PG&E - Advice Letter Approved	1 day	Wed 4/28/21	Wed 4/28/21		
1206		PG&E - Implementation Plan	43 days	Thu 4/29/21	Sun 6/27/21		
1207		PG&E - Statewide New Construction (Residential) Solicitation	640 days?	Mon 3/25/19	Fri 9/3/21		
1208		PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19		
1209		PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19		
1210		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19		
1211		PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19		
1212		PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19		
1213		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19		
1214		PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20		
1215		PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20		
1216		PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20		
1217		PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20		
1218		PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20		
1219		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	H2	2005 H1
1220		PG&E - Contract Negotiation and Development	177 days	Mon 8/17/20	Tue 4/20/21		
1221		PG&E - Contract Review with EE PRG	16 days	Thu 4/22/21	Thu 5/13/21		
1222		PG&E - Final Award and Contract Signed	32 days	Sat 5/15/21	Mon 6/28/21		
1223		PG&E - Submit Advice Letter	1 day	Mon 7/12/21	Mon 7/12/21		
1224		PG&E - Advice Letter Approved (all electric)	1 day	Wed 8/11/21	Wed 8/11/21		
1225		PG&E - Advice Letter Approved (mixed fuel)	1 day	Wed 9/15/21	Wed 9/15/21		
1226		PG&E - Implementation Plan (all electric)	43 days	Thu 8/12/21	Mon 10/11/21		
1227		PG&E - Implementation Plan (mixed fuel)	43 days	Thu 9/16/21	Sun 11/14/21		
1228		PG&E - Statewide WE&T Career Connections Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21		
1229		PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20		
1230		PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20		
1231		PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20		
1232		PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20		
1233		PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20		
1234		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20		
1235		PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20		
1236		PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20		
1237		PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20		
1238		PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20		
1239		PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20		
1240		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20		
1241		PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21		
1242		PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	H2	2005 H1
1243		PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21		
1244		PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21		
1245		PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21		
1246		PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21		
1247		PG&E - Statewide WE&T Career and Workforce Readiness Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21		
1248		PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20		
1249		PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20		
1250		PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20		
1251		PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20		
1252		PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20		
1253		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20		
1254		PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20		
1255		PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20		
1256		PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20		
1257		PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20		
1258		PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20		
1259		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20		
1260		PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21		
1261		PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21		
1262		PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21		
1263		PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21		
1264		PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21		
1265		PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task



Inactive Summary



External Tasks



Split



Manual Task



External Milestone



Milestone



Duration-only



Deadline



Summary



Manual Summary Rollup



Progress



Project Summary



Manual Summary



Manual Progress



Inactive Task



Start-only



Inactive Milestone




Finish-only




ID		Task Name	Duration	Start	Finish	H2	2005 H1
1266		PG&E - Statewide State of CA (Dept. of Corrections) Solicitation	348 days?	Sun 3/1/20	Tue 6/29/21		
1267		PG&E - RFA Preparation	46 days	Sun 3/1/20	Fri 5/1/20		
1268		PG&E - RFA Release	1 day	Wed 5/13/20	Wed 5/13/20		
1269		PG&E - RFA Abstract Creation Duration	31 days	Wed 5/13/20	Wed 6/24/20		
1270		PG&E - RFA Evaluation	15 days	Mon 6/29/20	Fri 7/17/20		
1271		PG&E - RFA Review with EE PRG	5 days	Tue 7/28/20	Mon 8/3/20		
1272		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/3/20	Fri 8/7/20		
1273		PG&E - RFP Preparation	20 days	Mon 8/3/20	Fri 8/28/20		
1274		PG&E - RFP Release	1 day	Wed 9/9/20	Wed 9/9/20		
1275		PG&E - RFP Proposal Creation Duration	31 days	Wed 9/9/20	Wed 10/21/20		
1276		PG&E - RFP Evaluation	31 days	Fri 10/23/20	Fri 12/4/20		
1277		PG&E - RFP Review with EE PRG	6 days	Tue 12/22/20	Tue 12/29/20		
1278		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 1/6/21	Fri 1/8/21		
1279		PG&E - Contract Negotiation and Development	65 days	Wed 1/20/21	Tue 4/20/21		
1280		PG&E - Contract Review with EE PRG	7 days	Thu 4/22/21	Fri 4/30/21		
1281		PG&E - Final Award and Contract Signed	22 days	Sat 5/1/21	Mon 5/31/21		
1282		PG&E - Submit Advice Letter	1 day	Thu 6/24/21	Thu 6/24/21		
1283		PG&E - Advice Letter Approved	1 day	Wed 7/28/21	Wed 7/28/21		
1284		PG&E - Implementation Plan	43 days	Thu 7/29/21	Sun 9/26/21		
1285		PG&E - Local (Micro and Small Business Equity Program) Solicitation	403 days?	Tue 6/1/21	Thu 12/15/22		
1286		PG&E - RFA Preparation	38 days	Tue 6/1/21	Thu 7/22/21		
1287		PG&E - RFA Release	1 day	Tue 9/7/21	Tue 9/7/21		
1288		PG&E - RFA Abstract Creation Duration	34 days	Wed 9/8/21	Mon 10/25/21		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1289		PG&E - RFA Evaluation	18 days	Tue 10/26/21	Thu 11/18/21		
1290		PG&E - RFP Release	1 day	Wed 12/8/21	Wed 12/8/21		
1291		PG&E - RFP Proposal Creation Duration	46 days	Wed 12/8/21	Wed 2/9/22		
1292		PG&E - RFP Evaluation	21 days	Thu 2/10/22	Thu 3/10/22		
1293		PG&E - RFP Review with EE PRG	6 days	Thu 3/17/22	Thu 3/24/22		
1294		PG&E - RFP Estimated Bidder Notification	1 day	Wed 3/30/22	Wed 3/30/22		
1295		PG&E - Contract Negotiation and Development	71 days	Thu 4/7/22	Thu 7/14/22		
1296		PG&E - Contract Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22		
1297		PG&E - Final Award and Contract Signed	45 days	Mon 8/8/22	Fri 10/7/22		
1298		PG&E - Submit Advice Letter	1 day	Wed 10/12/22	Wed 10/12/22		
1299		PG&E - Advice Letter Approved	1 day	Fri 11/11/22	Fri 11/11/22		
1300		PG&E - Implementation Plan	31 days	Fri 11/11/22	Fri 12/23/22		
1301		PG&E - Local (C&S Compliance Improvement) Solicitation	436 days	Tue 3/1/22	Tue 10/31/23		
1302		PG&E - RFA Preparation	34 days	Tue 3/1/22	Fri 4/15/22		
1303		PG&E - RFA Release	1 day	Mon 5/16/22	Mon 5/16/22		
1304		PG&E - RFA Abstract Creation Duration	25 days	Tue 5/17/22	Mon 6/20/22		
1305		PG&E - RFA Evaluation	28 days	Tue 6/21/22	Thu 7/28/22		
1306		PG&E - RFA Review with EE PRG	1 day	Tue 8/9/22	Tue 8/9/22		
1307		PG&E - RFA Estimated Bidder Notification	1 day	Wed 8/31/22	Wed 8/31/22		
1308		PG&E - RFP Preparation	24 days	Mon 8/1/22	Thu 9/1/22		
1309		PG&E - RFP Release	1 day	Tue 9/13/22	Tue 9/13/22		
1310		PG&E - RFP Proposal Creation Duration	26 days	Tue 9/13/22	Tue 10/18/22		
1311		PG&E - RFP Evaluation	45 days	Wed 10/19/22	Tue 12/20/22		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1312		PG&E - RFP Review with EE PRG	1 day	Tue 1/24/23	Tue 1/24/23		
1313		PG&E - RFP Estimated Bidder Notification	1 day	Fri 2/10/23	Fri 2/10/23		
1314		PG&E - Contract Negotiation and Development	47 days	Mon 2/13/23	Tue 4/18/23		
1315		PG&E - Contract Review with EE PRG	26 days	Tue 5/23/23	Tue 6/27/23		
1316		PG&E - Final Award and Contract Signed	48 days	Wed 6/28/23	Fri 9/1/23		
1317		PG&E - Submit Advice Letter		N/A			
1318		PG&E - Advice Letter Approved		N/A			
1319		PG&E - Implementation Plan	1 day	Tue 10/31/23	Tue 10/31/23		
1320		PG&E - Residential Electrification Equity Program Solicitation	595 days	Mon 8/1/22	Fri 11/8/24		
1321		PG&E - RFA Preparation	59 days	Mon 8/1/22	Thu 10/20/22		
1322		PG&E - RFA Release	1 day	Tue 11/29/22	Tue 11/29/22		
1323		PG&E - RFA Abstract Creation Duration	46 days	Tue 11/29/22	Tue 1/31/23		
1324		PG&E - RFA Evaluation	17 days	Sun 2/5/23	Sun 2/26/23		
1325		PG&E - RFA Review with EE PRG	6 days	Mon 2/27/23	Mon 3/6/23		
1326		PG&E - RFA Estimated Bidder Notification	3 days	Mon 3/6/23	Wed 3/8/23		
1327		PG&E - RFP Preparation	46 days	Mon 1/9/23	Mon 3/13/23		
1328		PG&E - RFP Release	1 day	Tue 4/11/23	Tue 4/11/23		
1329		PG&E - RFP Proposal Creation Duration	26 days	Tue 4/11/23	Tue 5/16/23		
1330		PG&E - RFP Evaluation	18 days	Fri 5/19/23	Tue 6/13/23		
1331		PG&E - RFP Review with EE PRG	1 day	Tue 6/27/23	Tue 6/27/23		
1332		PG&E - RFP Estimated Bidder Notification	1 day	Tue 7/11/23	Tue 7/11/23		
1333		PG&E - Contract Negotiation and Development	233 days	Tue 8/1/23	Thu 6/20/24		
1334		PG&E - Contract Review with EE PRG	8 days	Fri 6/21/24	Tue 7/2/24		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1335		PG&E - Final Award and Contract Signed	21 days	Fri 7/5/24	Fri 8/2/24		
1336		PG&E - Submit Advice Letter	1 day	Fri 8/9/24	Fri 8/9/24		
1337		PG&E - Advice Letter Approved	1 day	Mon 9/9/24	Mon 9/9/24		
1338		PG&E - Implementation Plan	1 day	Fri 11/8/24	Fri 11/8/24		
1339		PG&E - Statewide C&S Advocacy Solicitation	641 days	Tue 2/1/22	Tue 7/16/24		
1340		PG&E - RFA Preparation	54 days	Tue 2/1/22	Fri 4/15/22		
1341		PG&E - RFA Release	1 day	Mon 5/30/22	Mon 5/30/22		
1342		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/31/22	Fri 7/1/22		
1343		PG&E - RFA Evaluation	14 days	Fri 7/1/22	Wed 7/20/22		
1344		PG&E - RFA Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22		
1345		PG&E - RFA Estimated Bidder Notification	1 day	Mon 8/1/22	Mon 8/1/22		
1346		PG&E - RFP Preparation	36 days	Fri 4/1/22	Fri 5/20/22		
1347		PG&E - RFP Release	1 day	Tue 6/7/22	Tue 6/7/22		
1348		PG&E - RFP Proposal Creation Duration	31 days	Tue 6/7/22	Tue 7/19/22		
1349		PG&E - RFP Evaluation	50 days	Wed 7/20/22	Tue 9/27/22		
1350		PG&E - RFP Review with EE PRG	1 day	Wed 10/5/22	Wed 10/5/22		
1351		PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/24/22	Mon 10/24/22		
1352		PG&E - Contract Negotiation and Development	73 days	Mon 11/14/22	Wed 2/22/23		
1353		PG&E - Contract Review with EE PRG - Wave 1	1 day	Tue 4/25/23	Tue 4/25/23		
1354		PG&E - Final Award and Contract Signed	18 days	Mon 7/17/23	Wed 8/9/23		
1355		PG&E - Submit Advice Letter (wave 1)	1 day	Thu 9/21/23	Thu 9/21/23		
1356		PG&E - Advice Letter Approved	1 day	Wed 10/25/23	Wed 10/25/23		
1357		PG&E - Implementation Plan	1 day	Thu 12/7/23	Thu 12/7/23		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1358		PG&E - Contract Review with EE PRG - Wave 2	1 day	Wed 12/20/23	Wed 12/20/23		
1359		PG&E - Final Award and Contract Signed	1 day	Fri 3/29/24	Fri 3/29/24		
1360		PG&E - Submit Advice Letter	1 day	Wed 4/17/24	Wed 4/17/24		
1361		PG&E - Advice Letter Approved	1 day	Fri 5/17/24	Fri 5/17/24		
1362		PG&E - Implementation Plan	1 day	Tue 7/16/24	Tue 7/16/24		
1363		PG&E - Zonal Electrification Solicitation	495 days	Thu 12/1/22	Wed 10/23/24		
1364		PG&E - RFP Preparation	88 days	Thu 12/1/22	Mon 4/3/23		
1365		PG&E - RFP Release	1 day	Tue 4/18/23	Tue 4/18/23		
1366		PG&E - RFP Proposal Creation Duration	53 days	Tue 4/18/23	Thu 6/29/23		
1367		PG&E - RFP Evaluation (including interviews)	40 days	Mon 7/10/23	Fri 9/1/23		
1368		PG&E - RFP Review with EE PRG	1 day	Tue 9/26/23	Tue 9/26/23		
1369		PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/2/23	Mon 10/2/23		
1370		PG&E - Contract Negotiation and Development	135 days	Mon 10/9/23	Fri 4/12/24		
1371		PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24		
1372		PG&E - Final Award and Contract Signed	43 days	Wed 5/1/24	Fri 6/28/24		
1373		PG&E - Submit Advice Letter	1 day	Wed 7/3/24	Wed 7/3/24		
1374		PG&E - Advice Letter Approved	1 day	Wed 8/28/24	Wed 8/28/24		
1375		PG&E - Implementation Plan	1 day	Wed 10/23/24	Wed 10/23/24		
1376		PG&E - Residential Whole Home Load Management RFP	453 days	Tue 8/15/23	Thu 5/8/25		
1377		PG&E - RFP Preparation	1 day	Tue 8/15/23	Tue 8/15/23		
1378		PG&E - RFP Release	1 day	Tue 8/15/23	Tue 8/15/23		
1379		PG&E - RFP Proposal Creation Duration	51 days	Tue 8/15/23	Tue 10/24/23		
1380		PG&E - RFP Evaluation	36 days	Thu 10/26/23	Thu 12/14/23		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1381		PG&E - RFP Review with EE PRG	1 day	Fri 2/16/24	Fri 2/16/24		
1382		PG&E - RFP Estimated Bidder Notification	1 day	Tue 2/27/24	Tue 2/27/24		
1383		PG&E - Contract Negotiation and Development	155 days	Wed 3/13/24	Tue 10/15/24		
1384		PG&E - Contract Review with EE PRG	8 days	Tue 11/5/24	Thu 11/14/24		
1385		PG&E - Final Award and Contract Signed	53 days	Thu 11/14/24	Mon 1/27/25		
1386		PG&E - Submit Advice Letter	1 day	Fri 2/7/25	Fri 2/7/25		
1387		PG&E - Advice Letter Approved	1 day	Mon 3/10/25	Mon 3/10/25		
1388		PG&E - Implementation Plan	1 day	Thu 5/8/25	Thu 5/8/25		
1389		PG&E - 2024 Summer Reliability Platform Administrator RFP	337 days?	Tue 4/18/23	Wed 7/31/24		
1390		PG&E - RFP Preparation	30 days	Mon 5/1/23	Fri 6/9/23		
1391		PG&E - RFP Release	1 day	Fri 9/1/23	Fri 9/1/23		
1392		PG&E - RFP Proposal Creation Duration	31 days	Fri 9/1/23	Fri 10/13/23		
1393		PG&E - RFP Evaluation	22 days	Tue 10/17/23	Wed 11/15/23		
1394		PG&E - RFP Review with EE PRG	1 day	Tue 11/28/23	Tue 11/28/23		
1395		PG&E - RFP Estimated Bidder Notification	1 day	Tue 12/5/23	Tue 12/5/23		
1396		PG&E - Contract Negotiation and Development	68 days	Mon 1/8/24	Wed 4/10/24		
1397		PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24		
1398		PG&E - Final Award and Contract Signed	22 days	Wed 5/1/24	Thu 5/30/24		
1399		PG&E - Submit Advice Letter	1 day	Fri 5/31/24	Fri 5/31/24		
1400		PG&E - Advice Letter Approved	1 day	Mon 7/1/24	Mon 7/1/24		
1401		PG&E - Implementation Plan	1 day	Wed 7/31/24	Wed 7/31/24		
1402		PG&E - C&S Code Readiness RFP	393 days?	Wed 2/1/23	Fri 8/2/24		
1403		PG&E - RFP Preparation	113 days	Wed 2/1/23	Fri 7/7/23		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Name	Duration	Start	Finish	H2	2005 H1
1404		PG&E - RFP Release	1 day	Wed 7/12/23	Wed 7/12/23		
1405		PG&E - RFP Proposal Creation Duration	30 days	Thu 7/13/23	Wed 8/23/23		
1406		PG&E - RFP Evaluation	36 days	Mon 8/28/23	Mon 10/16/23		
1407		PG&E - RFP Review with EE PRG	1 day	Tue 10/24/23	Tue 10/24/23		
1408		PG&E - RFP Estimated Bidder Notification	1 day	Mon 11/6/23	Mon 11/6/23		
1409		PG&E - Contract Negotiation and Development	65 days	Wed 11/15/23	Tue 2/13/24		
1410		PG&E - Contract Review with EE PRG	1 day	Tue 2/27/24	Tue 2/27/24		
1411		PG&E - Final Award and Contract Signed	1 day	Fri 4/12/24	Fri 4/12/24		
1412		PG&E - Submit Advice Letter	1 day	Tue 5/7/24	Tue 5/7/24		
1413		PG&E - Advice Letter Approved	1 day	Thu 6/6/24	Thu 6/6/24		
1414		PG&E - Implementation Plan	1 day	Fri 8/2/24	Fri 8/2/24		
1415		PG&E - Residential Electrification - Single Point of Contact	414 days	Tue 8/1/23	Fri 2/28/25		
1416		PG&E - RFP Preparation	133 days	Tue 8/1/23	Thu 2/1/24		
1417		PG&E - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24		
1418		PG&E - RFP Proposal Creation Duration	33 days	Wed 2/28/24	Fri 4/12/24		
1419		PG&E - RFP Evaluation	66 days	Mon 4/15/24	Mon 7/15/24		
1420		PG&E - RFP Review with EE PRG	6 days	Fri 7/19/24	Fri 7/26/24		
1421		PG&E - RFP Estimated Bidder Notification	1 day	Wed 8/7/24	Wed 8/7/24		
1422		PG&E - Contract Negotiation and Development	62 days				
1423		PG&E - Contract Review with EE PRG	6 days				
1424		PG&E - Final Award and Contract Signed	25 days				
1425		PG&E - Submit Advice Letter	1 day				
1426		PG&E - Advice Letter Approved	1 day				

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	H2	2005 H1
1427		PG&E - Implementation Plan	1 day				
1428		PG&E - Commercial SEM FP	430 days	Thu 8/3/23	Wed 3/26/25		
1429		PG&E - RFP Preparation	16 days	Thu 8/3/23	Thu 8/24/23		
1430		PG&E - RFP Release	1 day	Fri 11/3/23	Fri 11/3/23		
1431		PG&E - RFP Proposal Creation Duration	55 days	Fri 11/3/23	Thu 1/18/24		
1432		PG&E - RFP Evaluation	58 days	Tue 1/23/24	Thu 4/11/24		
1433		PG&E - RFP Review with EE PRG	1 day	Wed 4/17/24	Wed 4/17/24		
1434		PG&E - RFP Estimated Bidder Notification	4 days	Tue 4/23/24	Fri 4/26/24		
1435		PG&E - Contract Negotiation and Development	90 days	Thu 5/2/24	Wed 9/4/24		
1436		PG&E - Contract Review with EE PRG	8 days	Mon 9/16/24	Wed 9/25/24		
1437		PG&E - Final Award and Contract Signed	58 days	Thu 9/26/24	Mon 12/16/24		
1438		PG&E - Submit Advice Letter	1 day	Thu 12/19/24	Thu 12/19/24		
1439		PG&E - Advice Letter Approved	0 days	Thu 1/30/25	Thu 1/30/25		
1440		PG&E - Implementation Plan	1 day	Wed 3/26/25	Wed 3/26/25		
1441		PG&E - SW WE&T Career & Workforce Readiness	460 days	Tue 10/8/24	Mon 7/13/26		
1442		PG&E - RFP Preparation	199 days	Tue 10/8/24	Fri 7/11/25		
1443		PG&E - RFP Release	1 day	Thu 7/17/25	Thu 7/17/25		
1444		PG&E - RFP Proposal Creation Duration	31 days	Thu 7/17/25	Thu 8/28/25		
1445		PG&E - RFP Evaluation	34 days	Tue 9/2/25	Fri 10/17/25		
1446		PG&E - RFP Review with EE PRG	11 days	Mon 10/20/25	Mon 11/3/25		
1447		PG&E - RFP Estimated Bidder Notification	1 day	Thu 11/13/25	Thu 11/13/25		
1448		PG&E - Contract Negotiation and Development	65 days	Wed 10/29/25	Tue 1/27/26		
1449		PG&E - Contract Review with EE PRG	11 days	Fri 1/30/26	Fri 2/13/26		

Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Name	Duration	Start	Finish	H2	2005 H1
1450		PG&E - Final Award and Contract Signed	36 days	Wed 2/18/26	Wed 4/8/26		
1451		PG&E - Submit Advice Letter	1 day	Wed 4/15/26	Wed 4/15/26		
1452		PG&E - Advice Letter Approved	1 day	Fri 5/15/26	Fri 5/15/26		
1453		PG&E - Implementation Plan	1 day	Mon 7/13/26	Mon 7/13/26		

Project: IOU Master Task Timeli

Date: Fri 3/28/25

Task



Split



Milestone



Summary



Project Summary



Inactive Task



Inactive Milestone



Inactive Summary



Manual Task



Duration-only



Manual Summary Rollup



Manual Summary



Start-only



Finish-only



External Tasks



External Milestone



Deadline

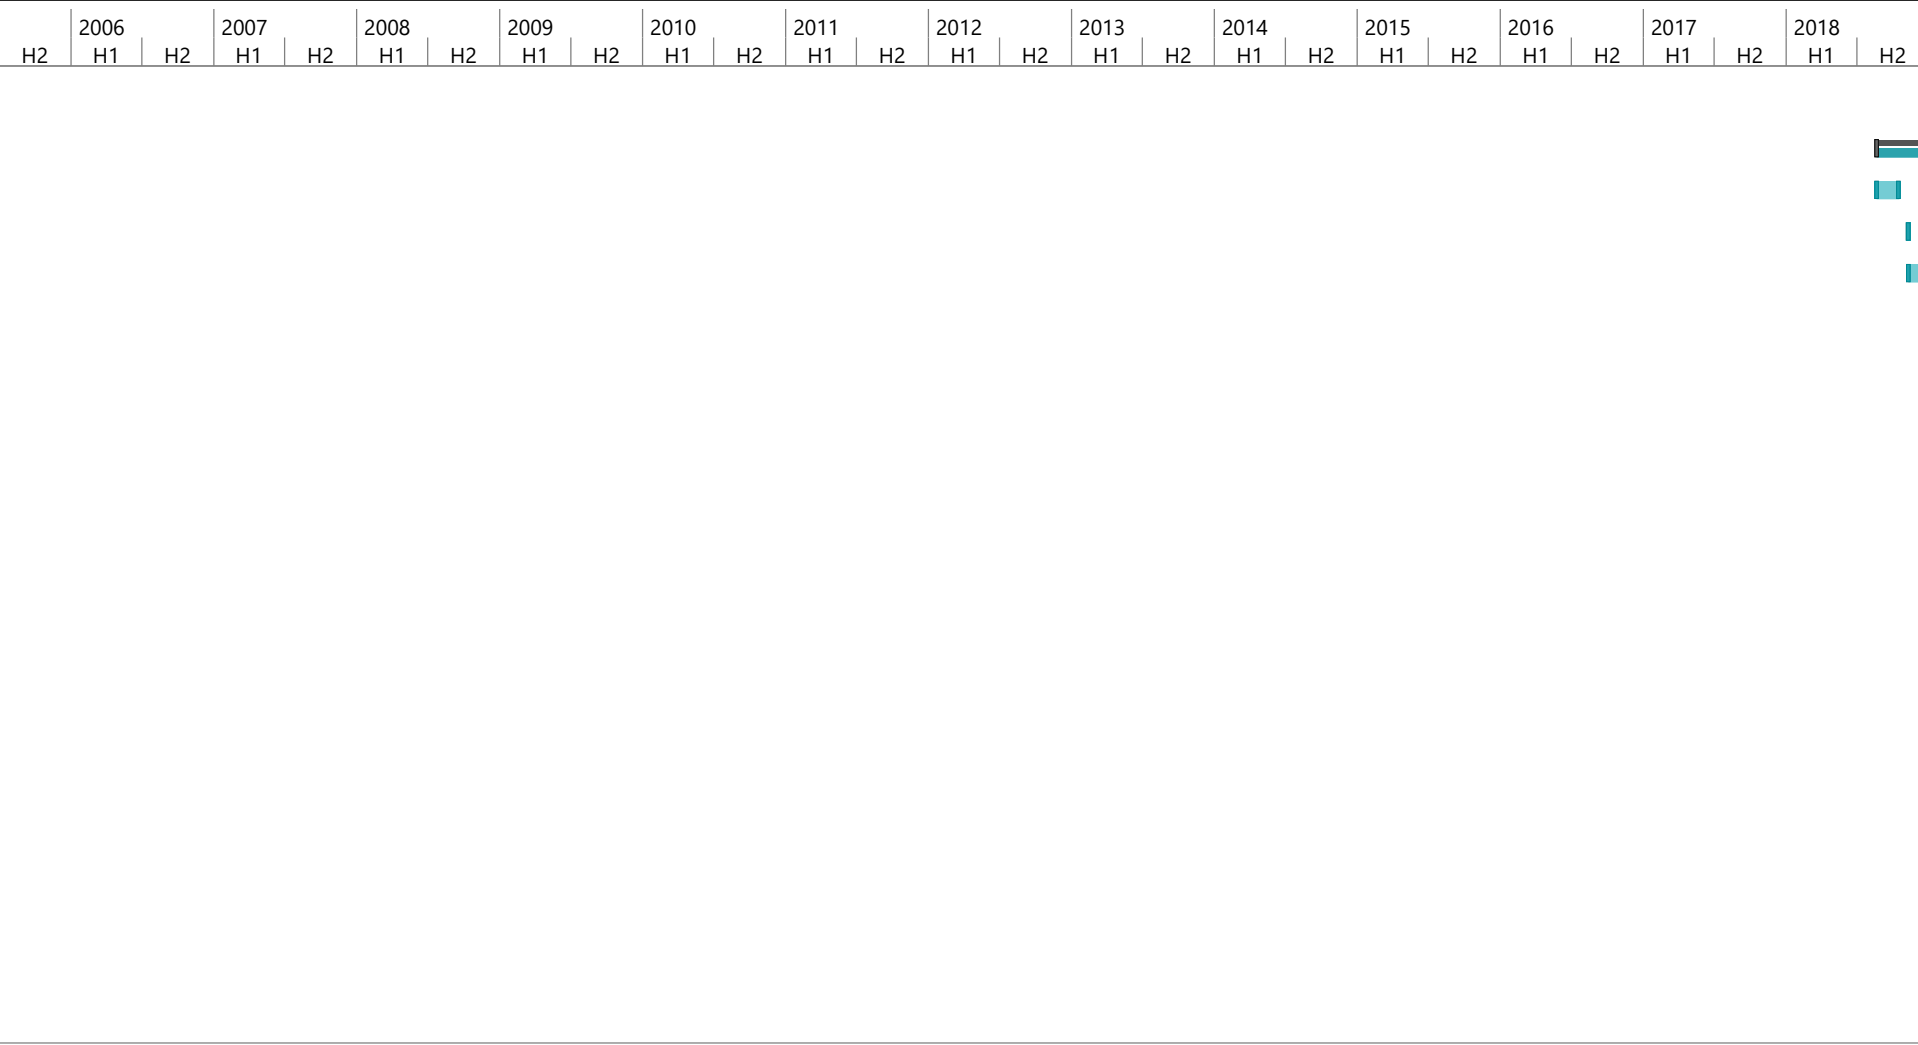



Progress



Manual Progress





Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Project: IOU Master Task Timeli

Date: Fri 3/28/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone


Deadline

Progress


Manual Progress

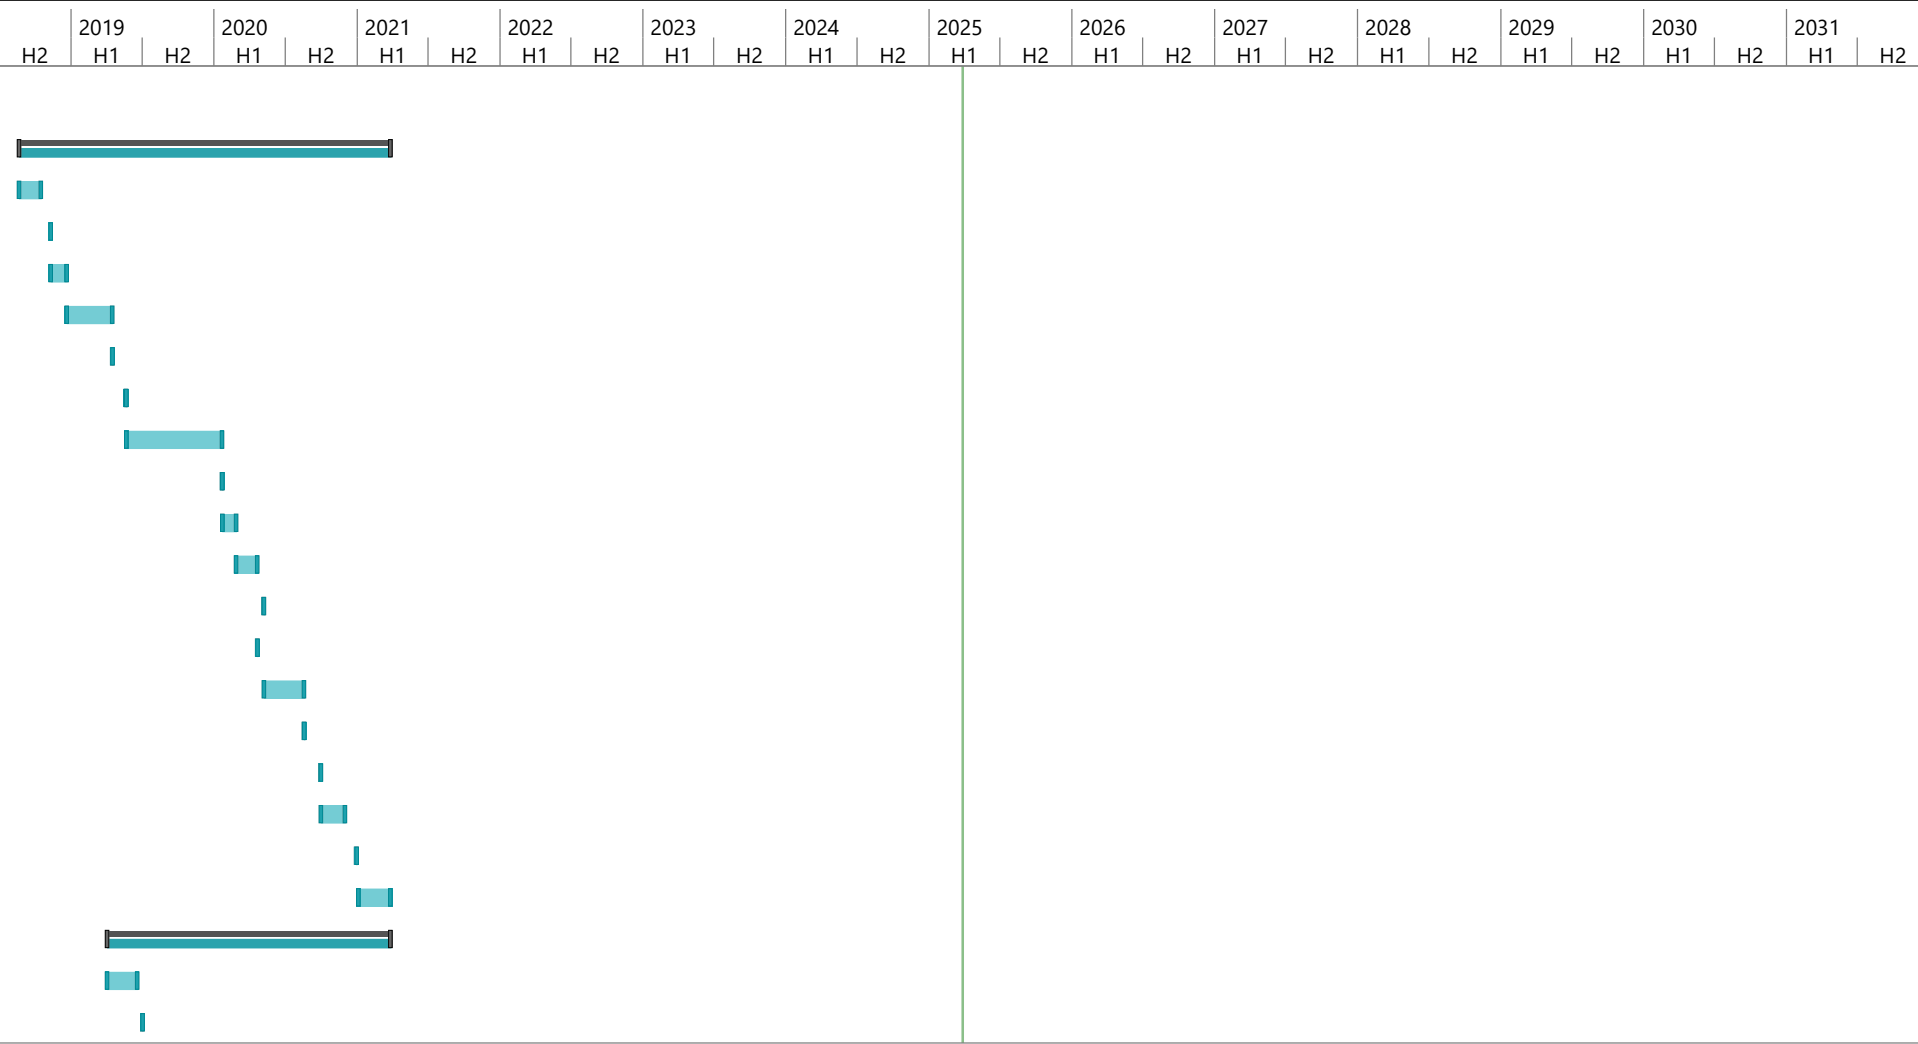
Page 85

H2	2006 H1	H2	2007 H1	H2	2008 H1	H2	2009 H1	H2	2010 H1	H2	2011 H1	H2	2012 H1	H2	2013 H1	H2	2014 H1	H2	2015 H1	H2	2016 H1	H2	2017 H1	H2	2018 H1	H2	

Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

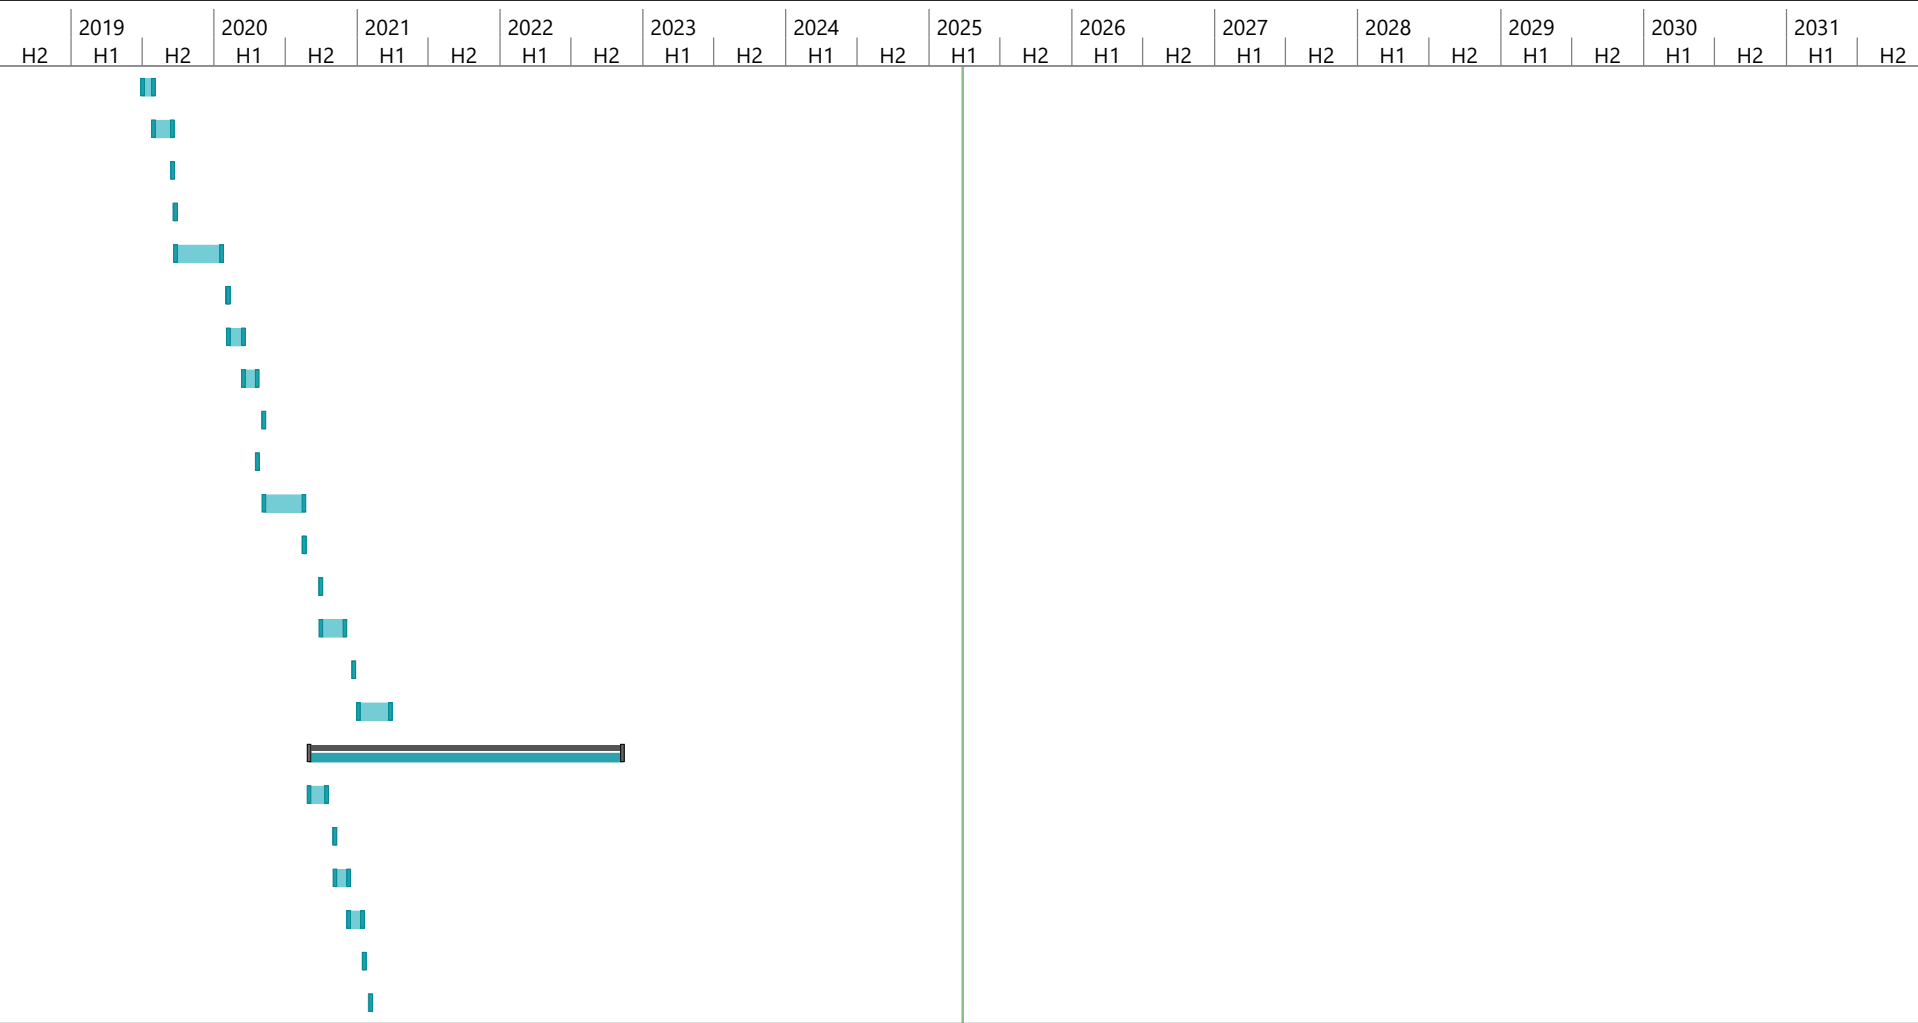
H2	2006 H1	H2	2007 H1	H2	2008 H1	H2	2009 H1	H2	2010 H1	H2	2011 H1	H2	2012 H1	H2	2013 H1	H2	2014 H1	H2	2015 H1	H2	2016 H1	H2	2017 H1	H2	2018 H1	H2	

Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



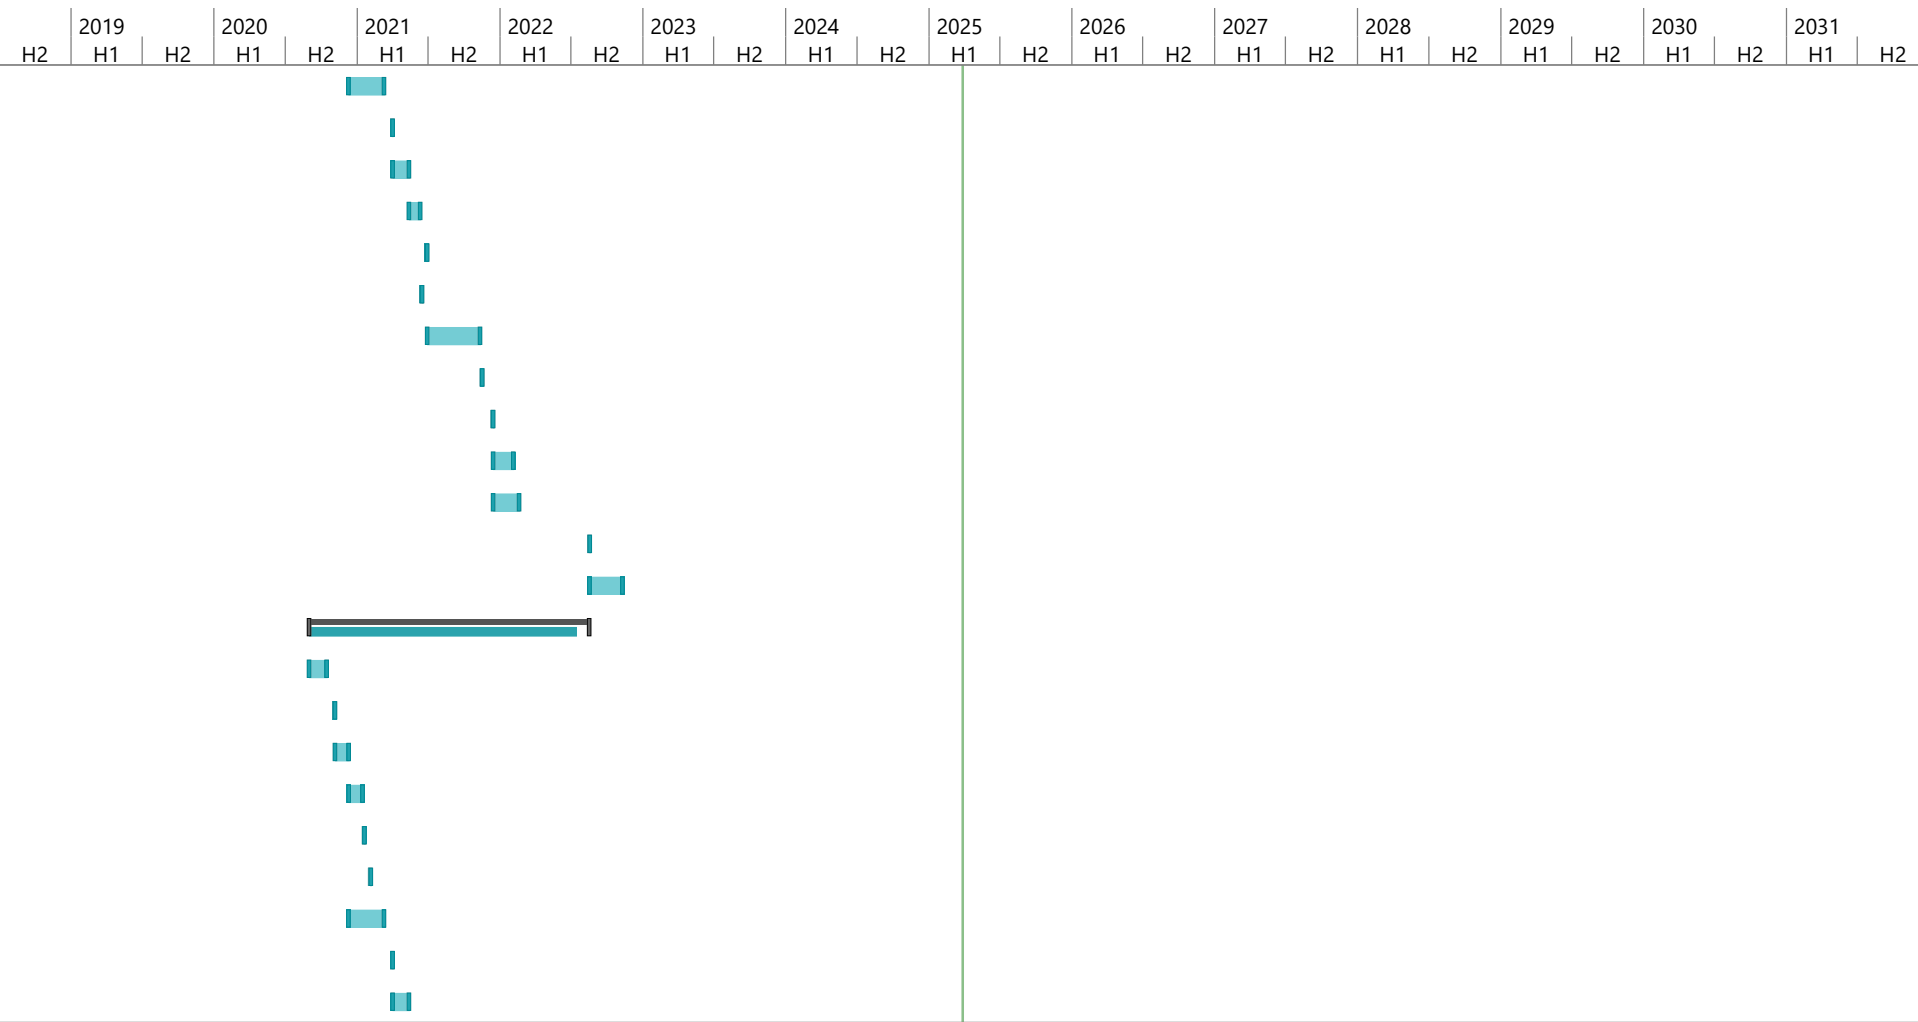
Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



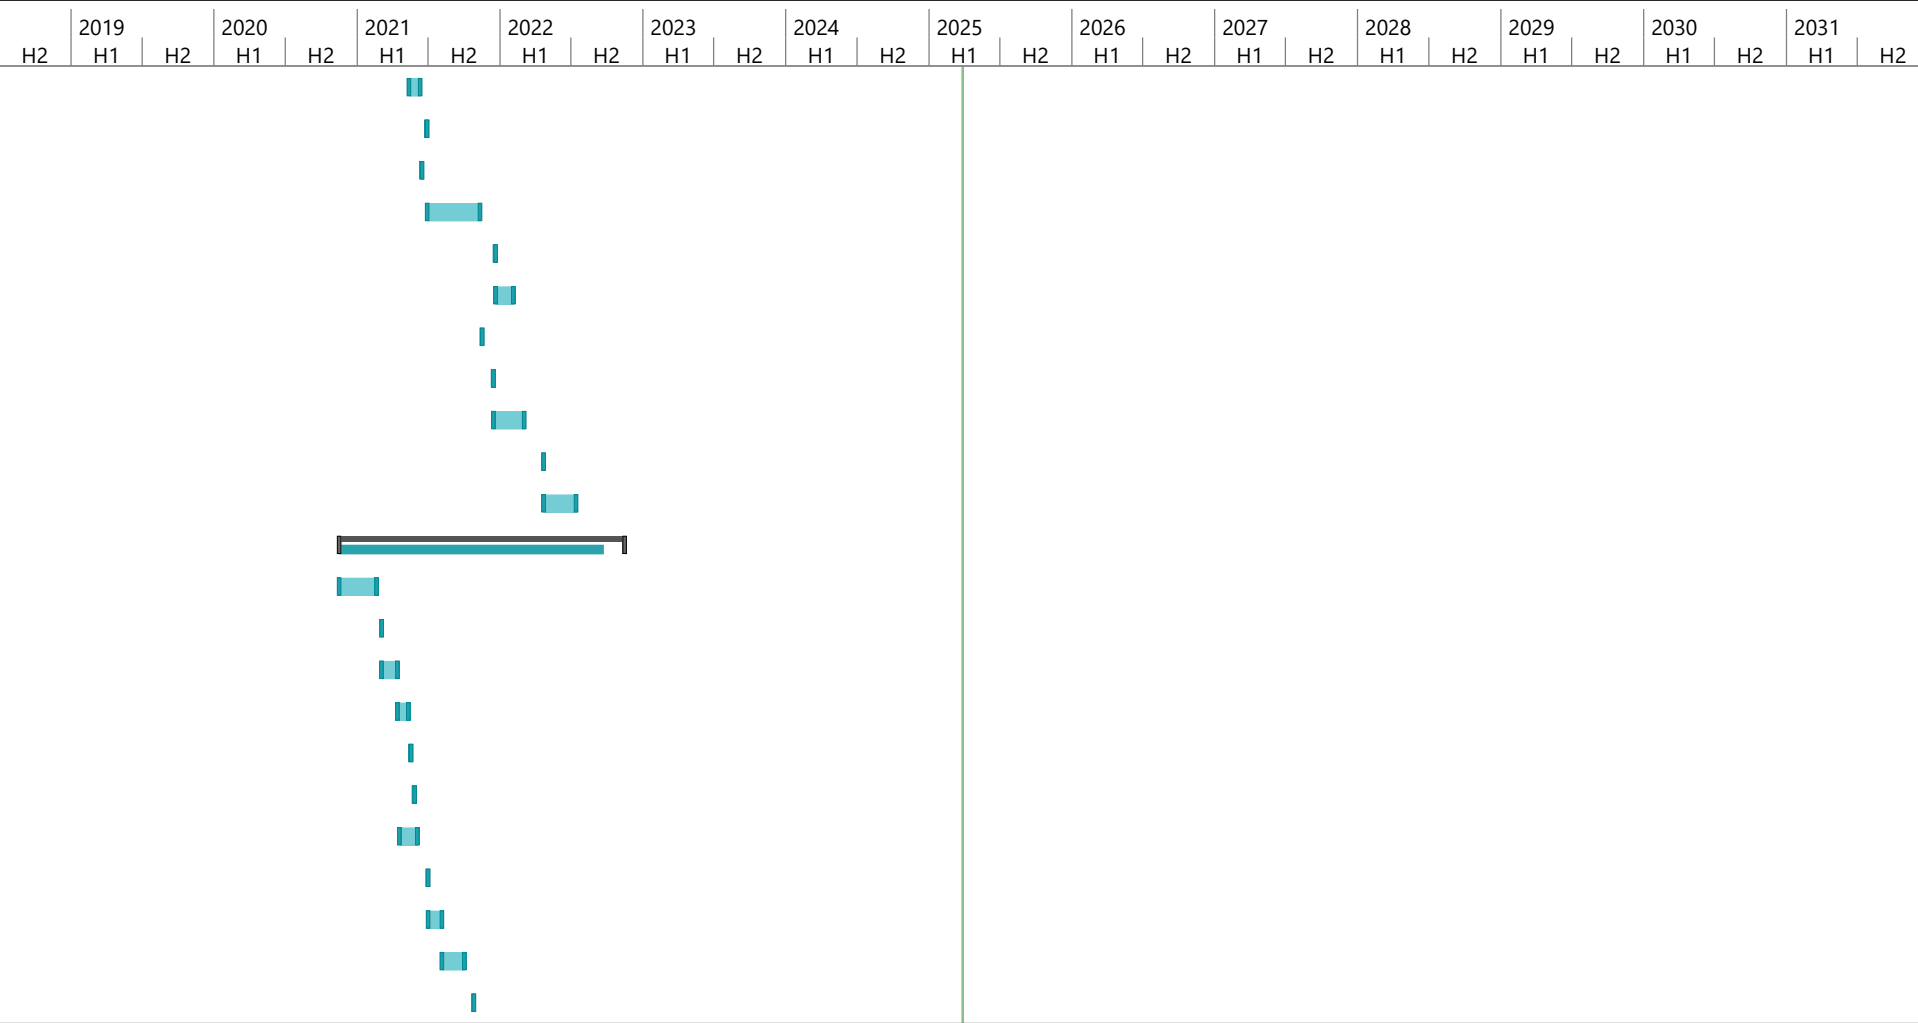
Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

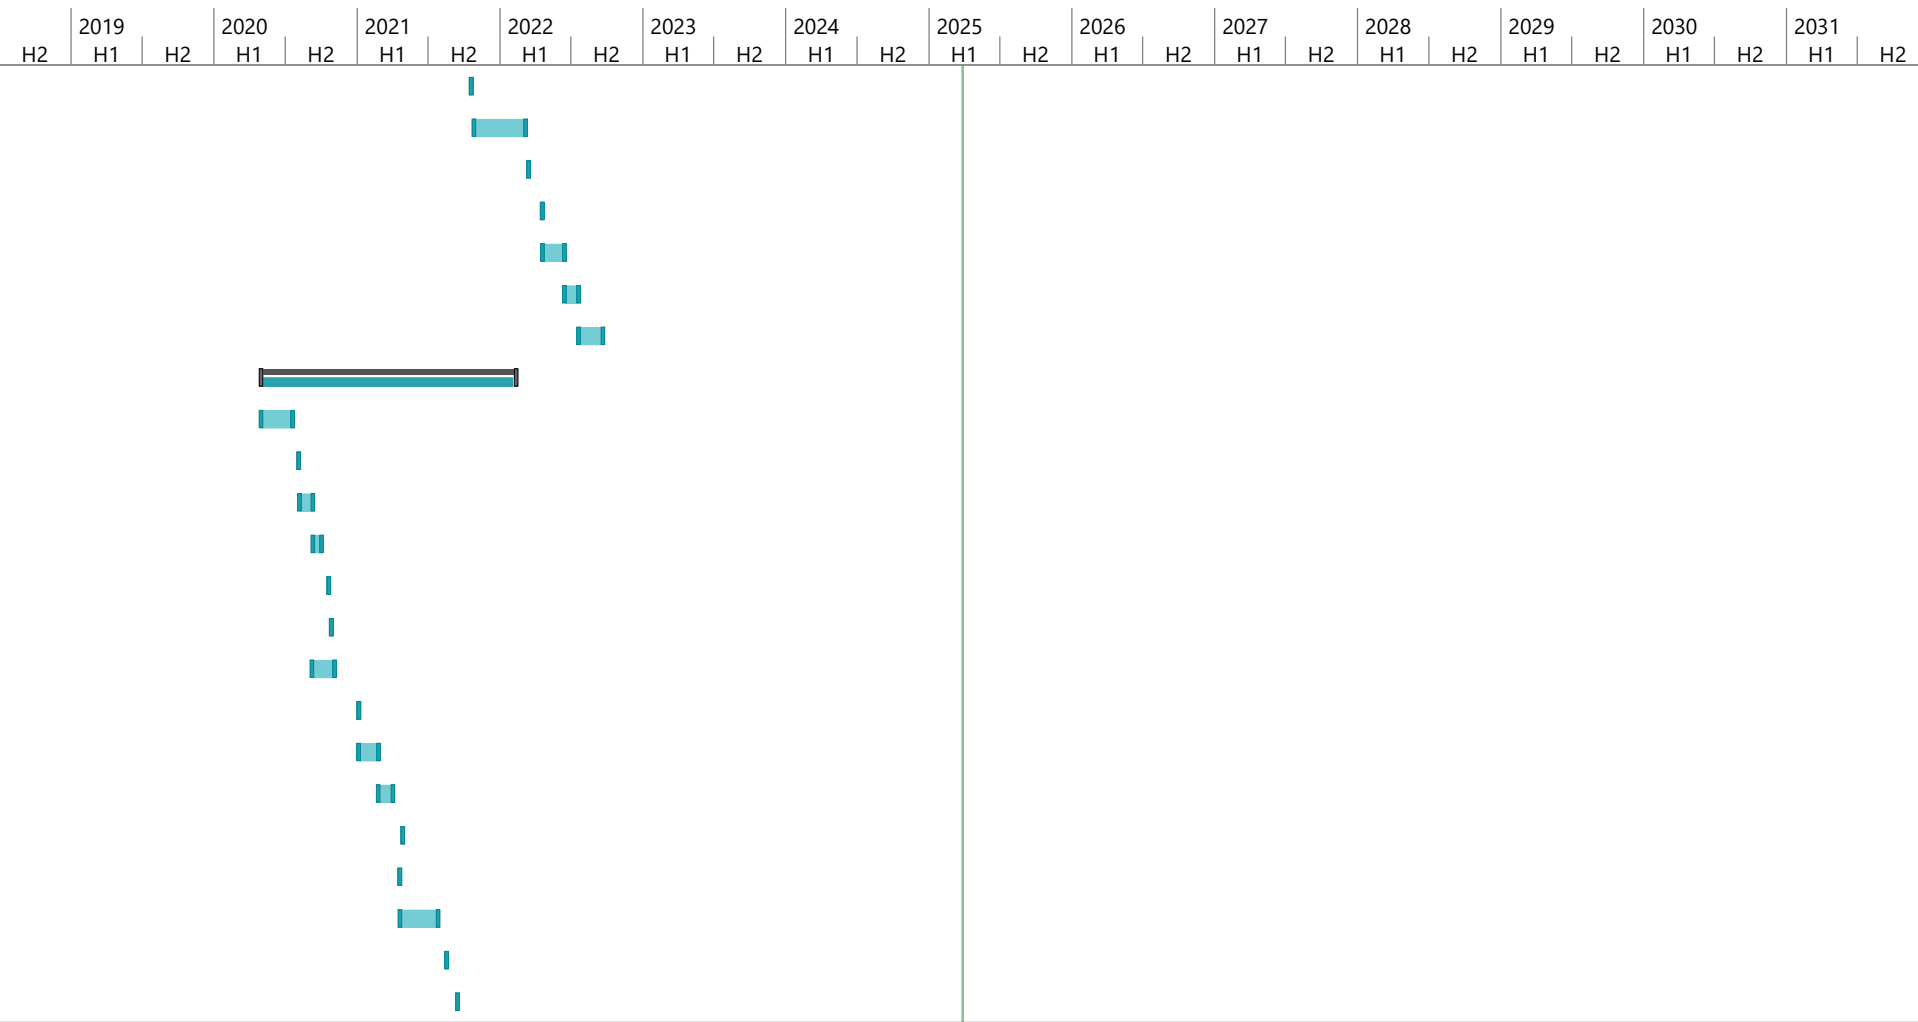


Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

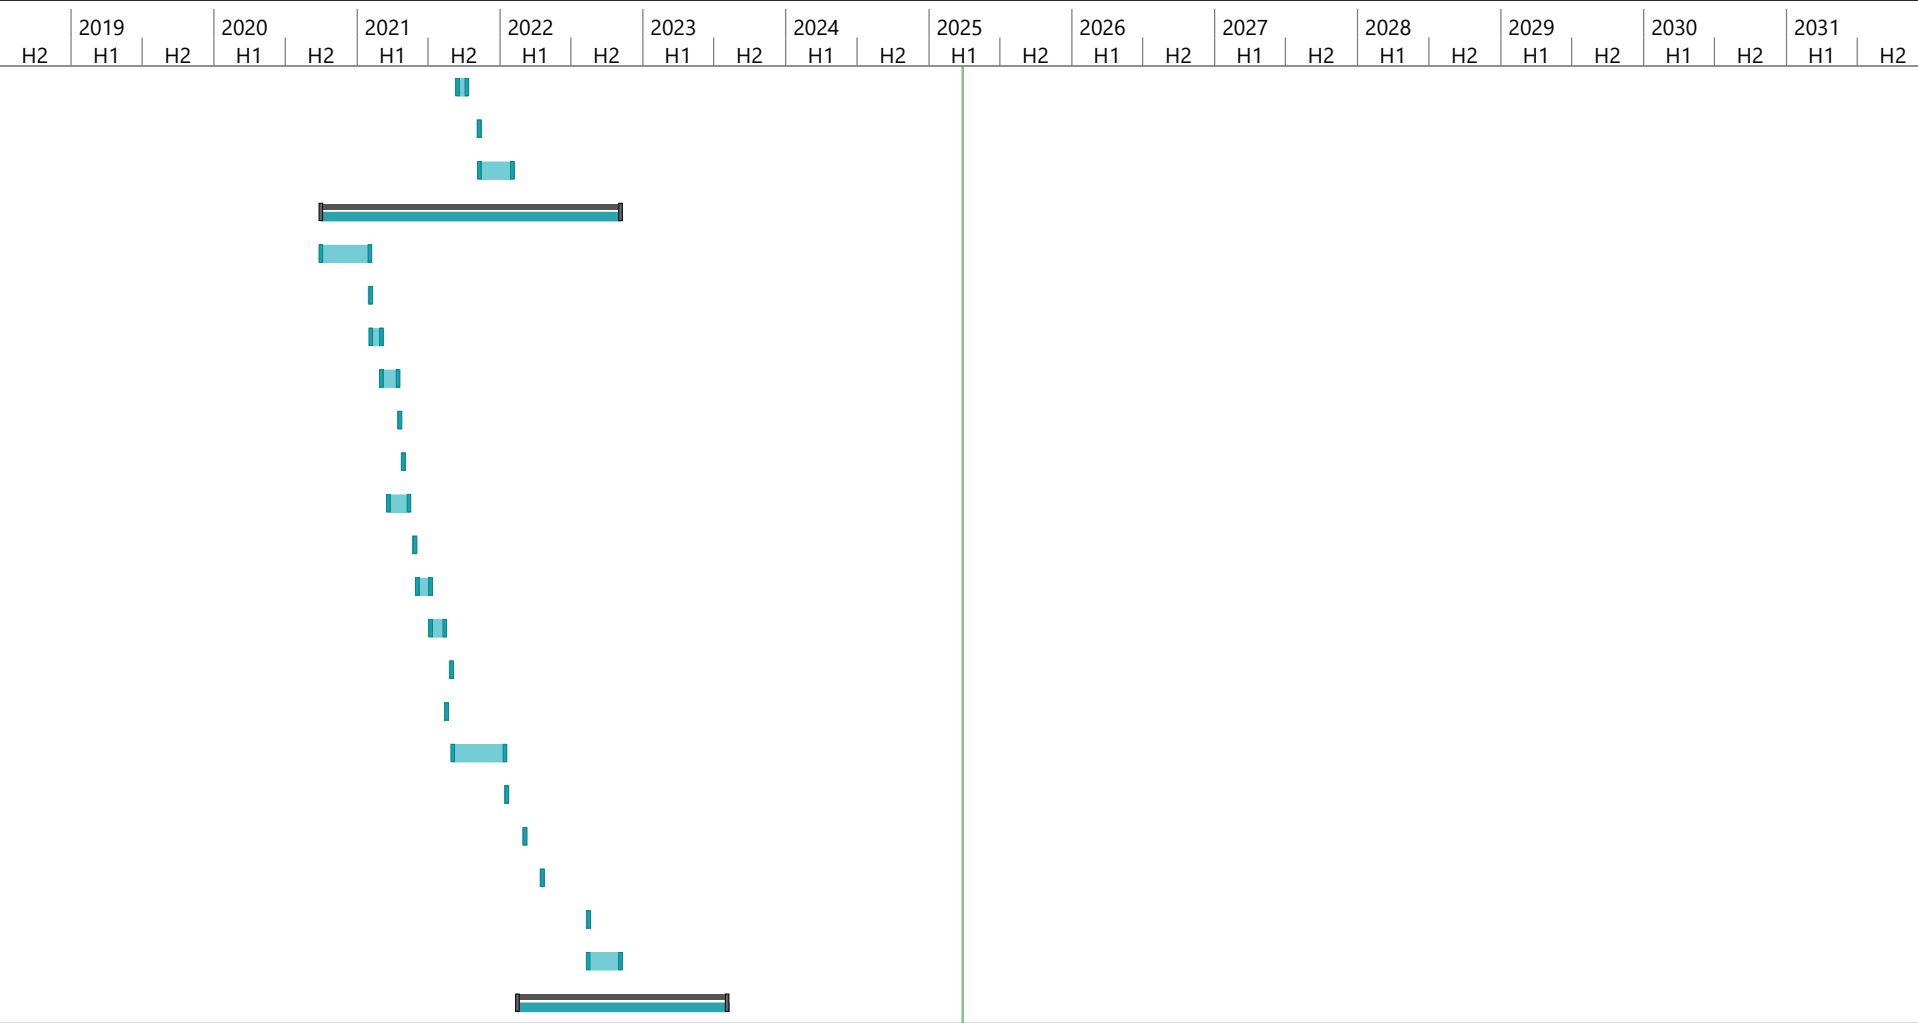


Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



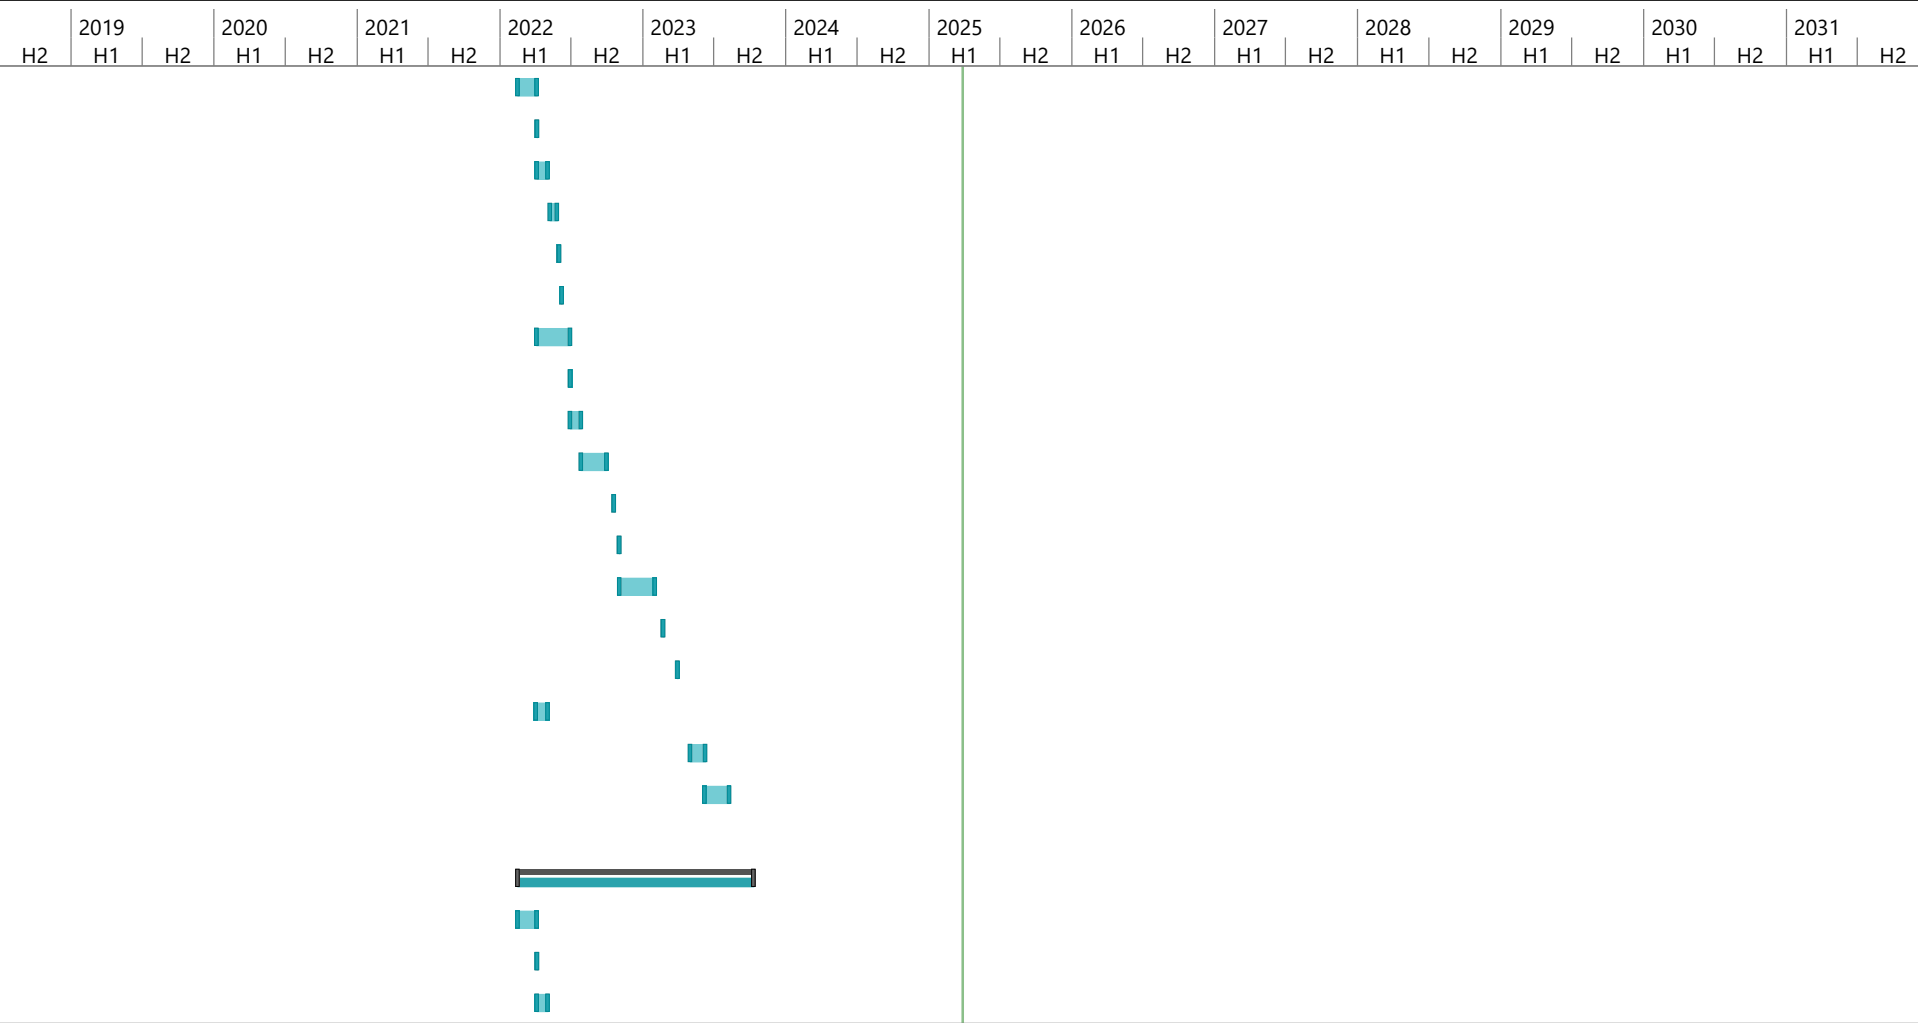
Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

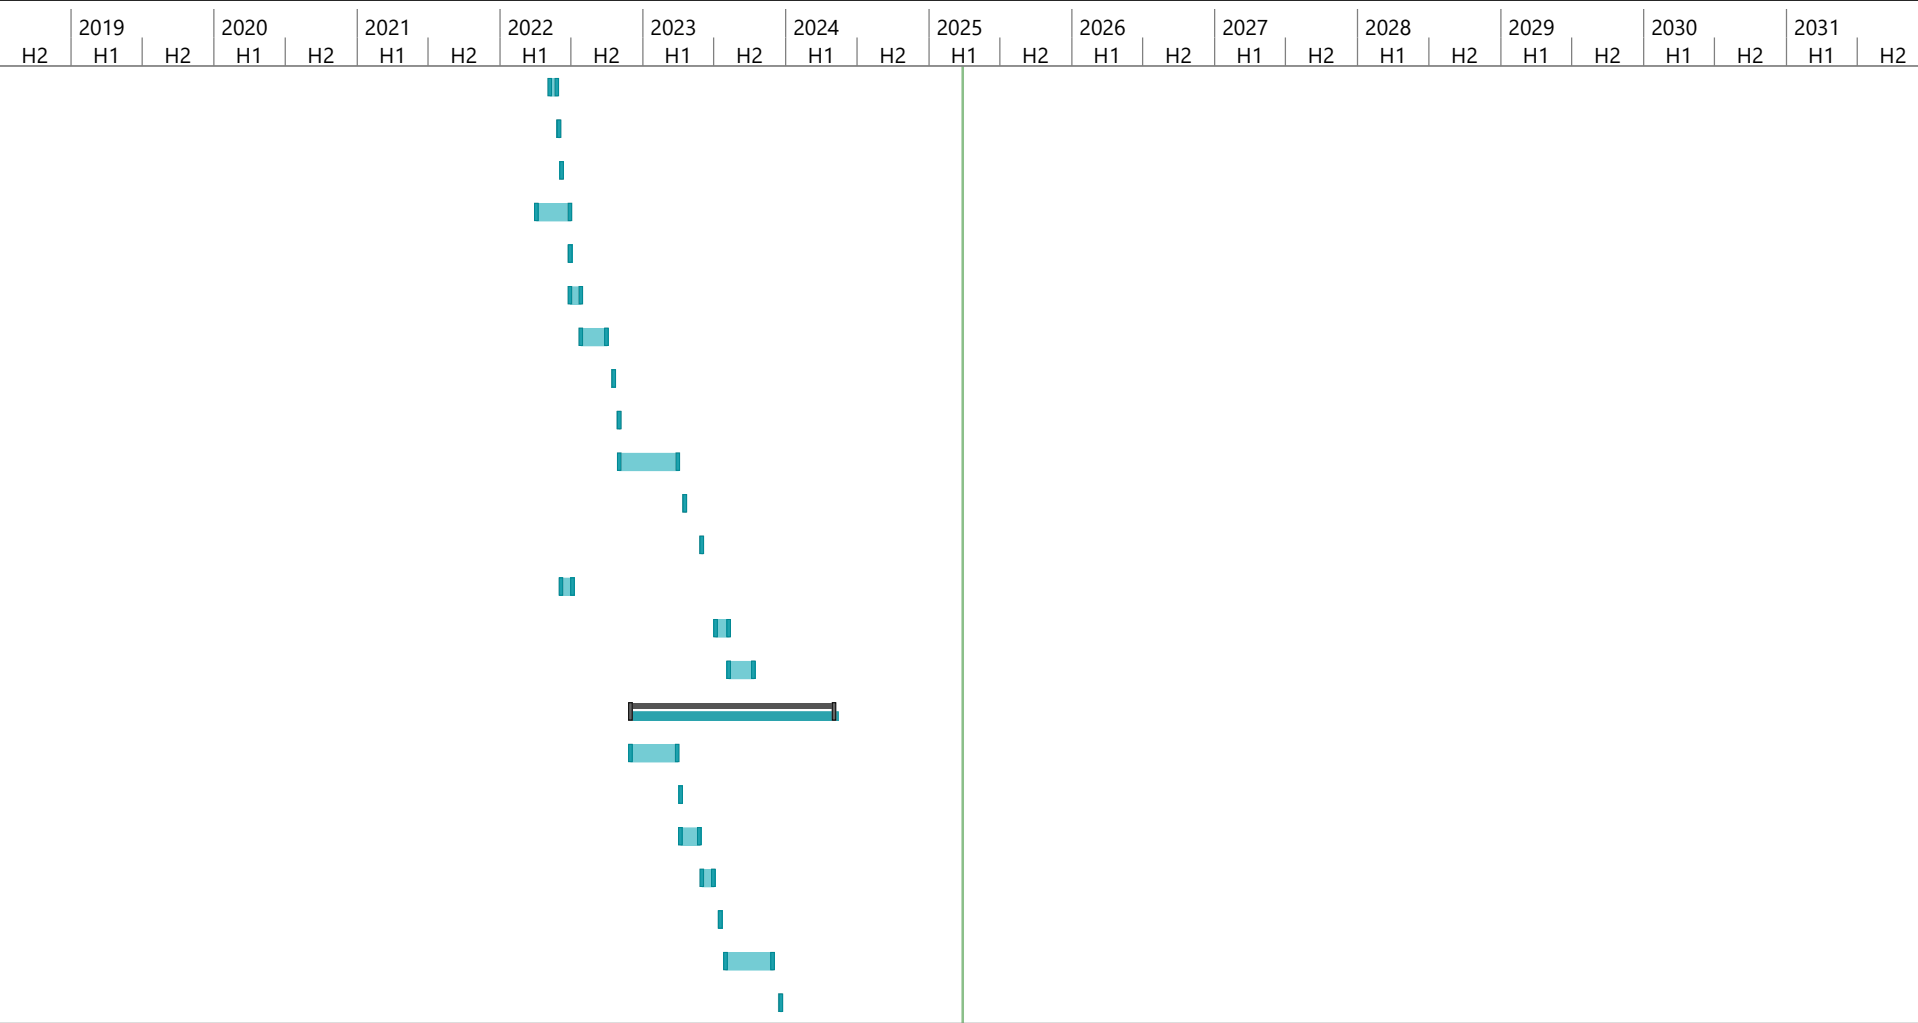
External Milestone

Deadline

Progress

Manual Progress

Page 135



Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

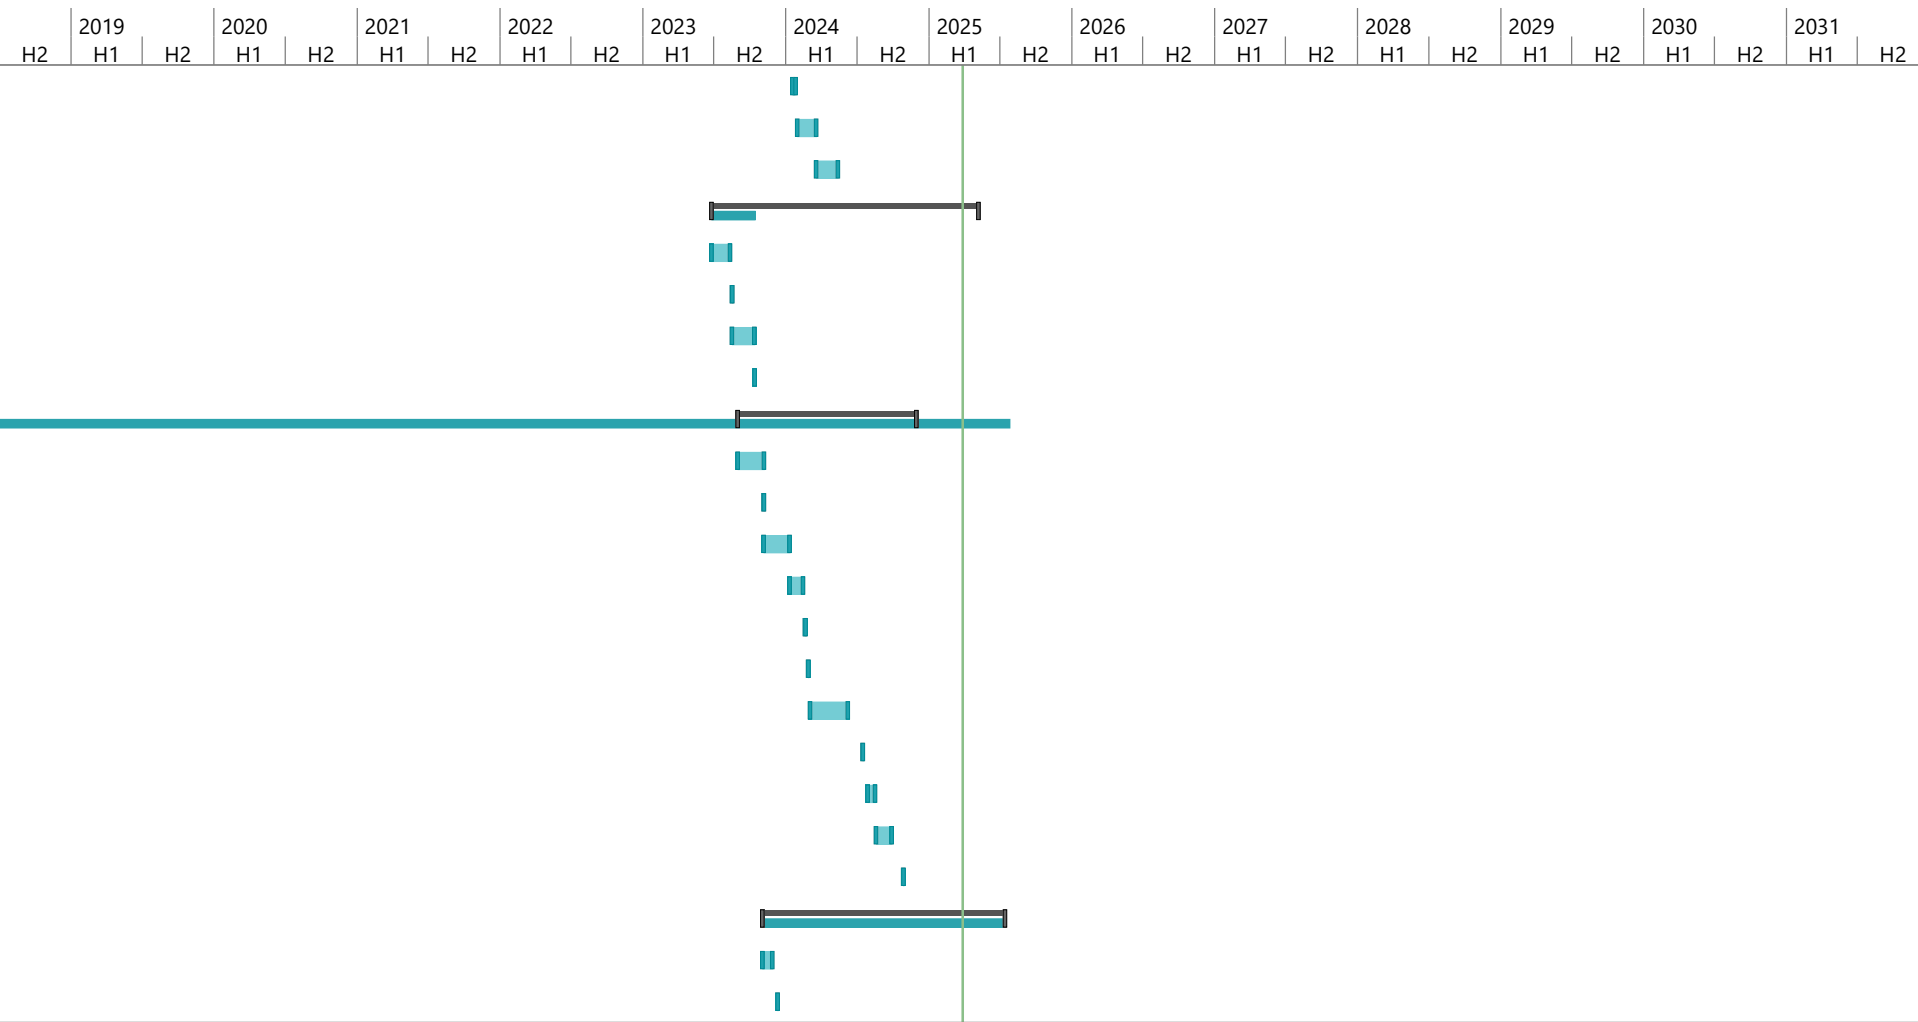
External Milestone

Deadline

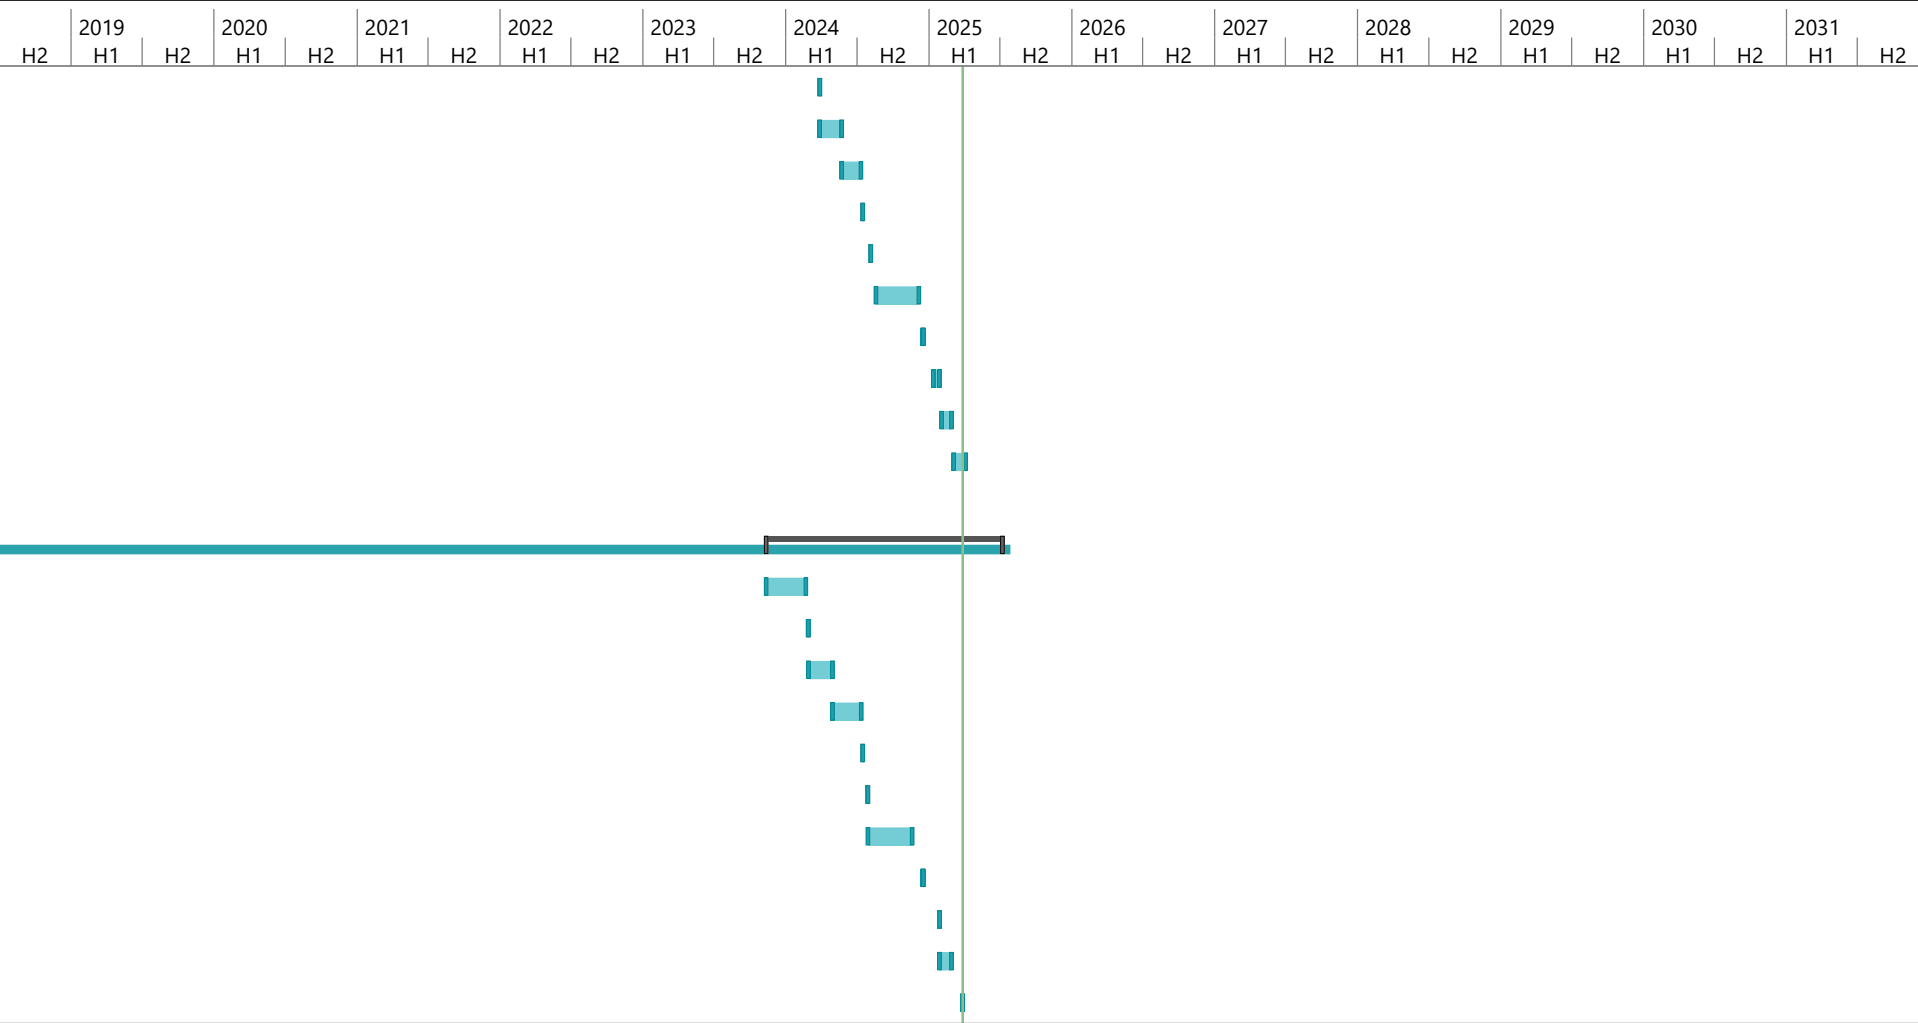
Progress

Manual Progress

Page 136



Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 3/28/25



Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

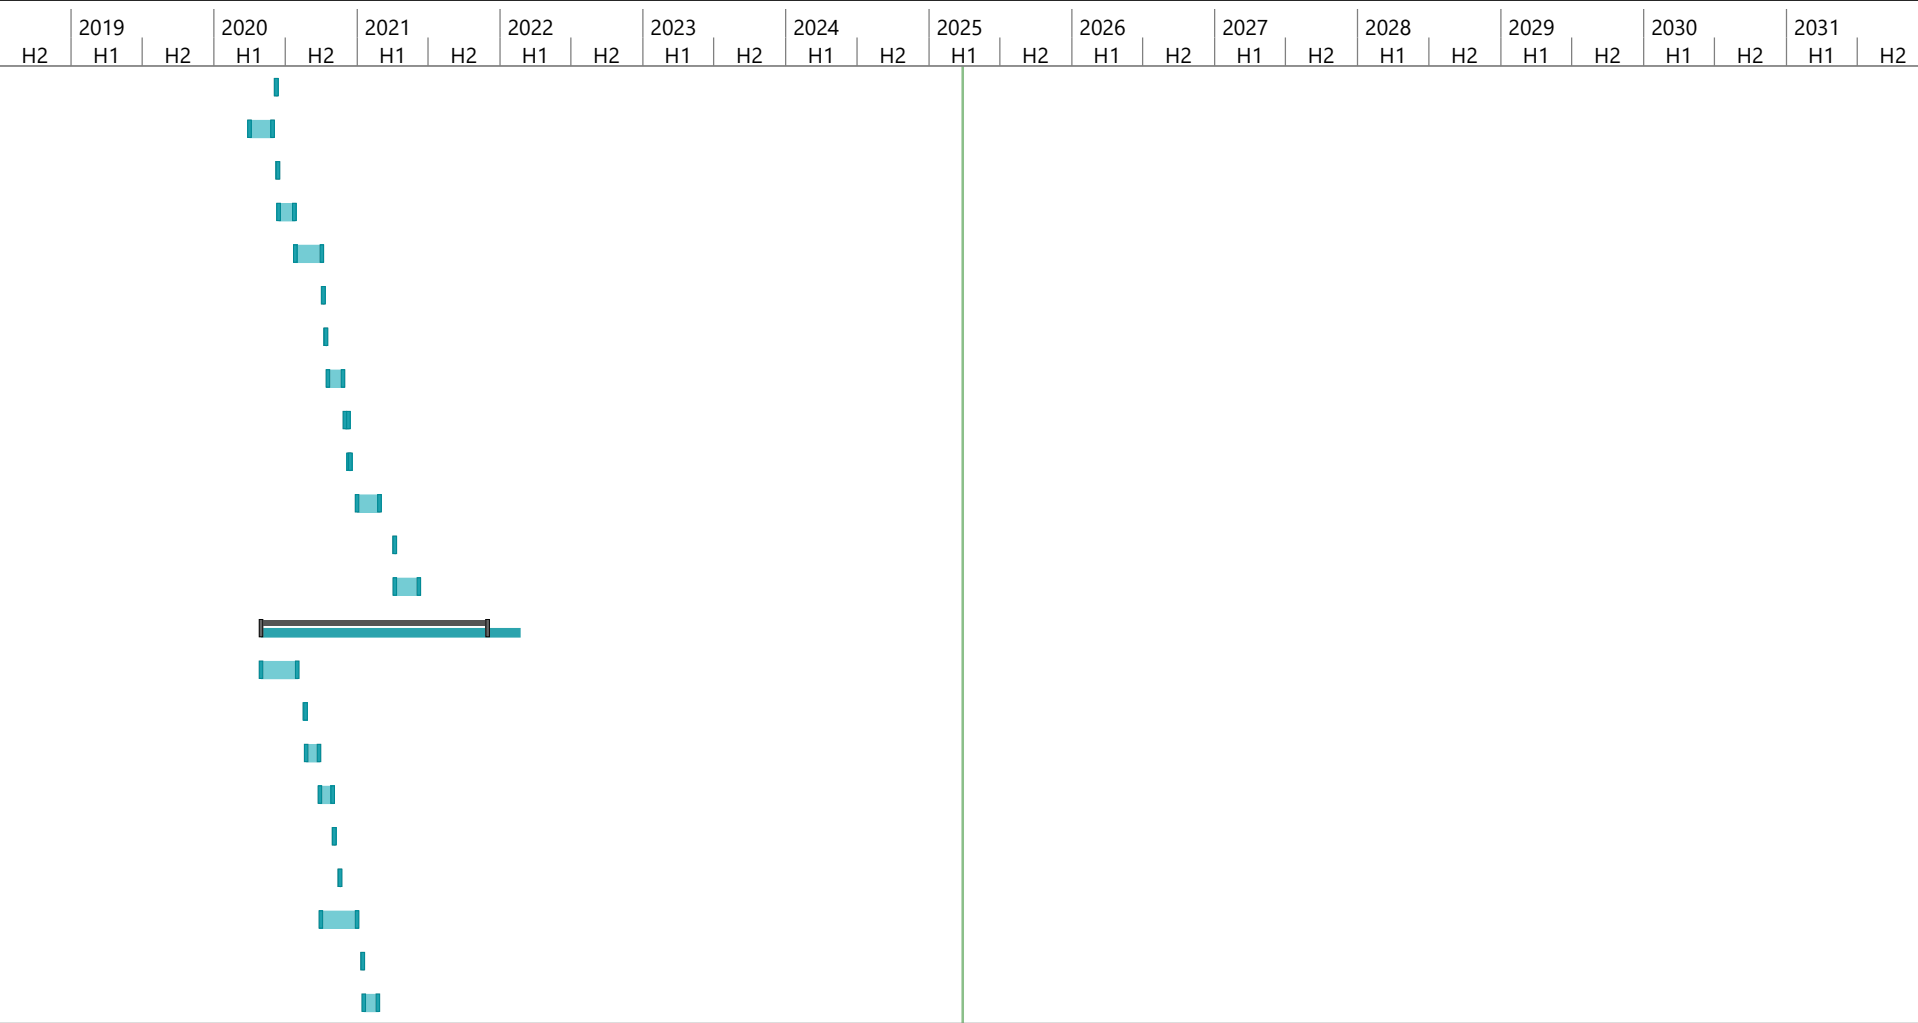


Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

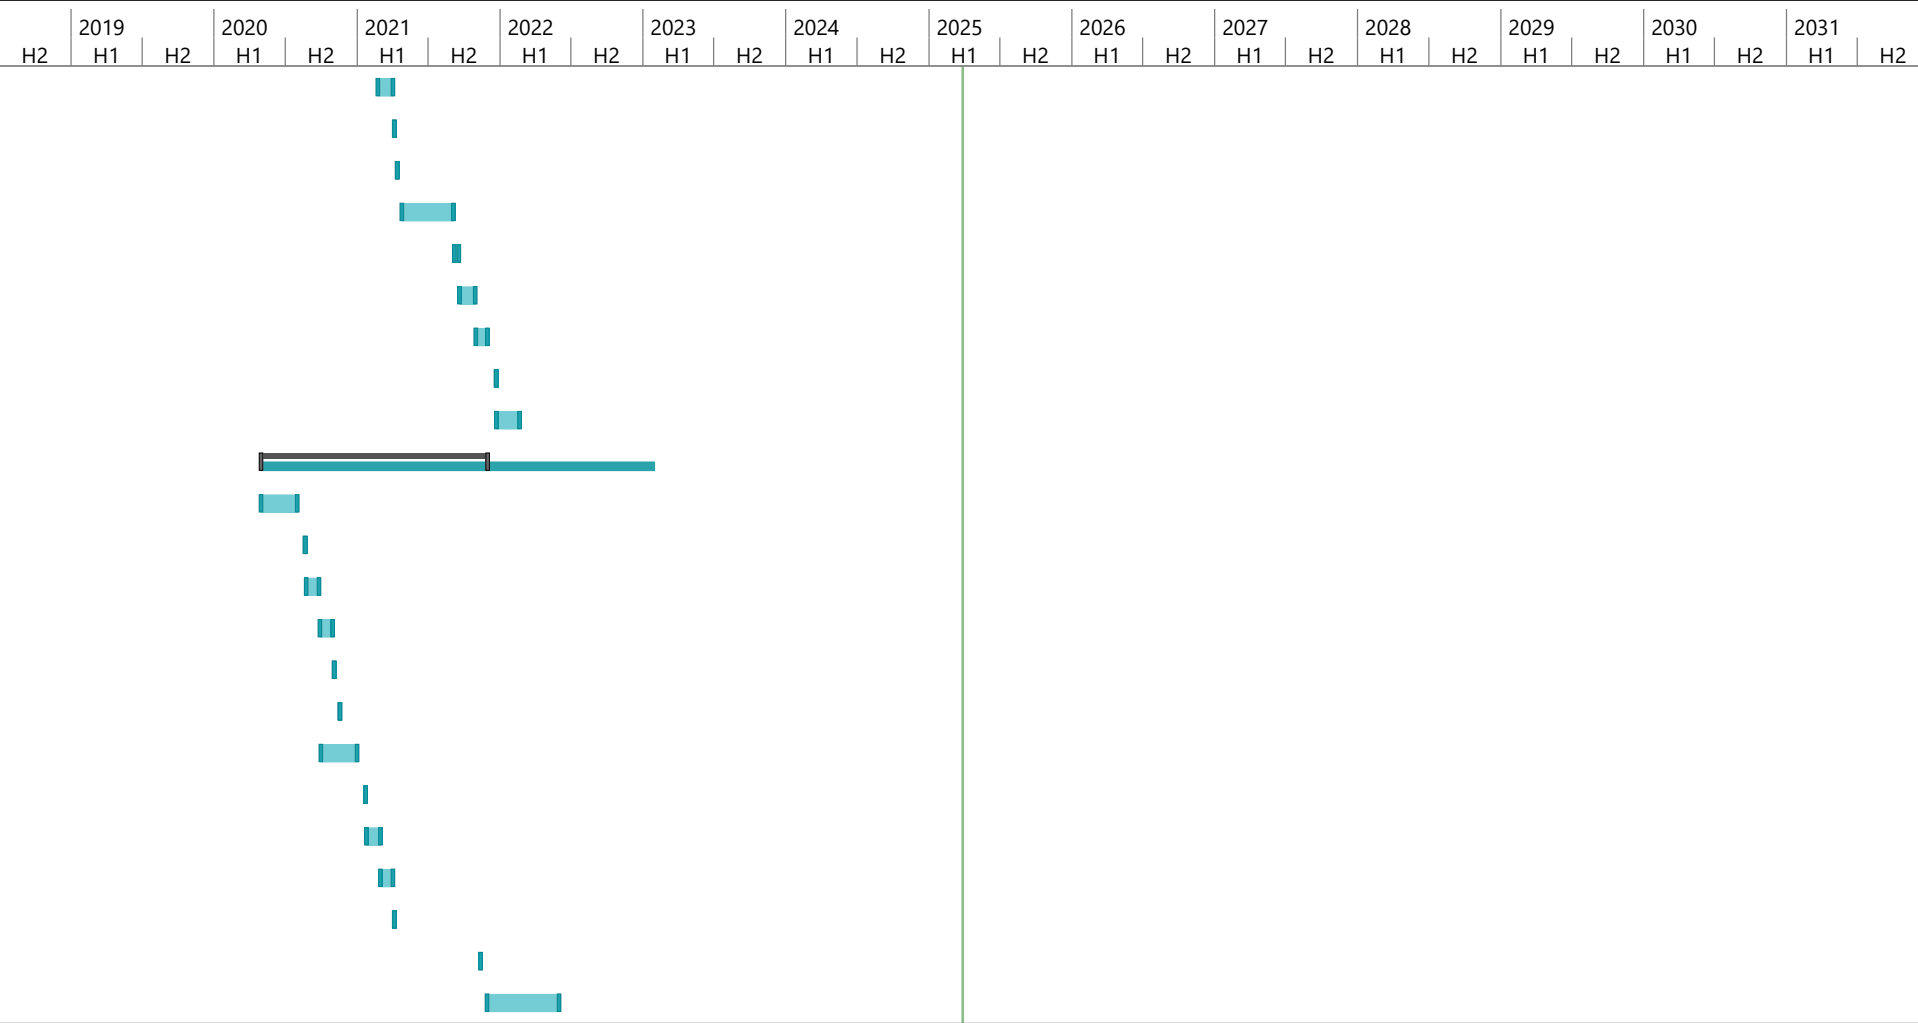
External Tasks

External Milestone

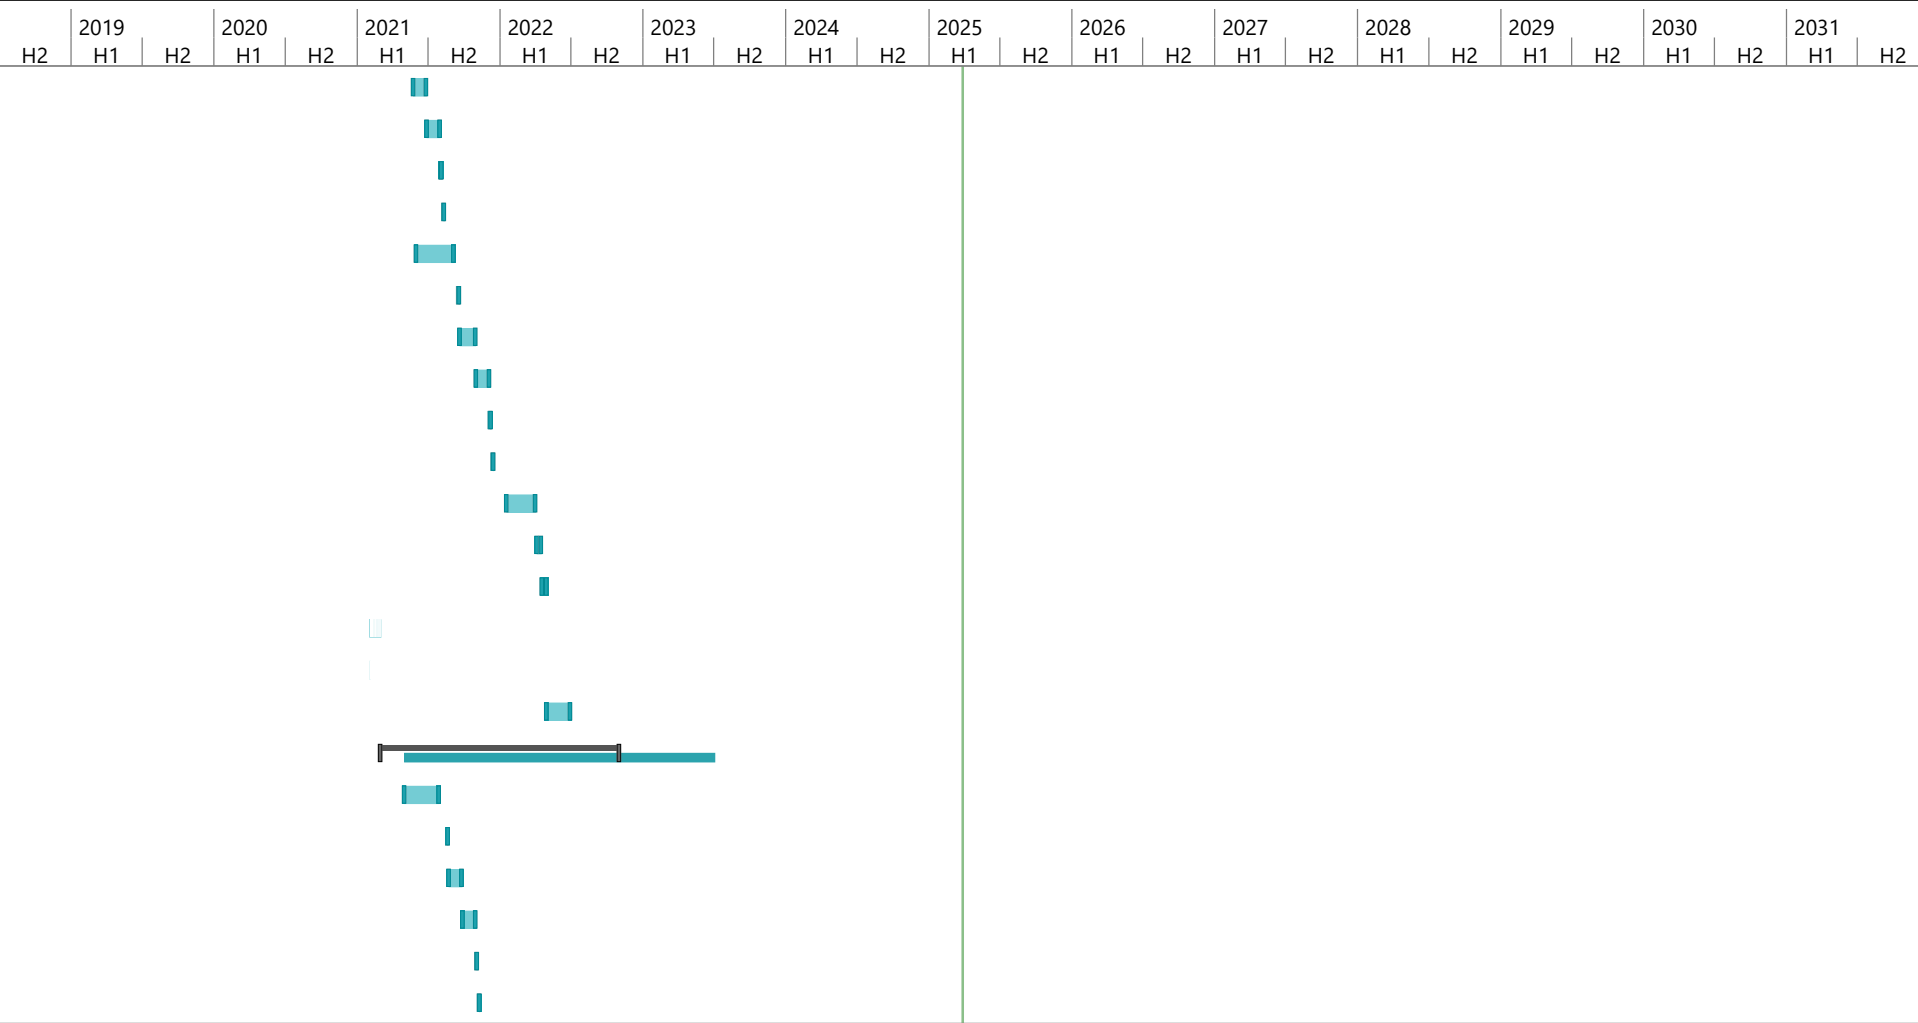
Deadline

Progress

Manual Progress

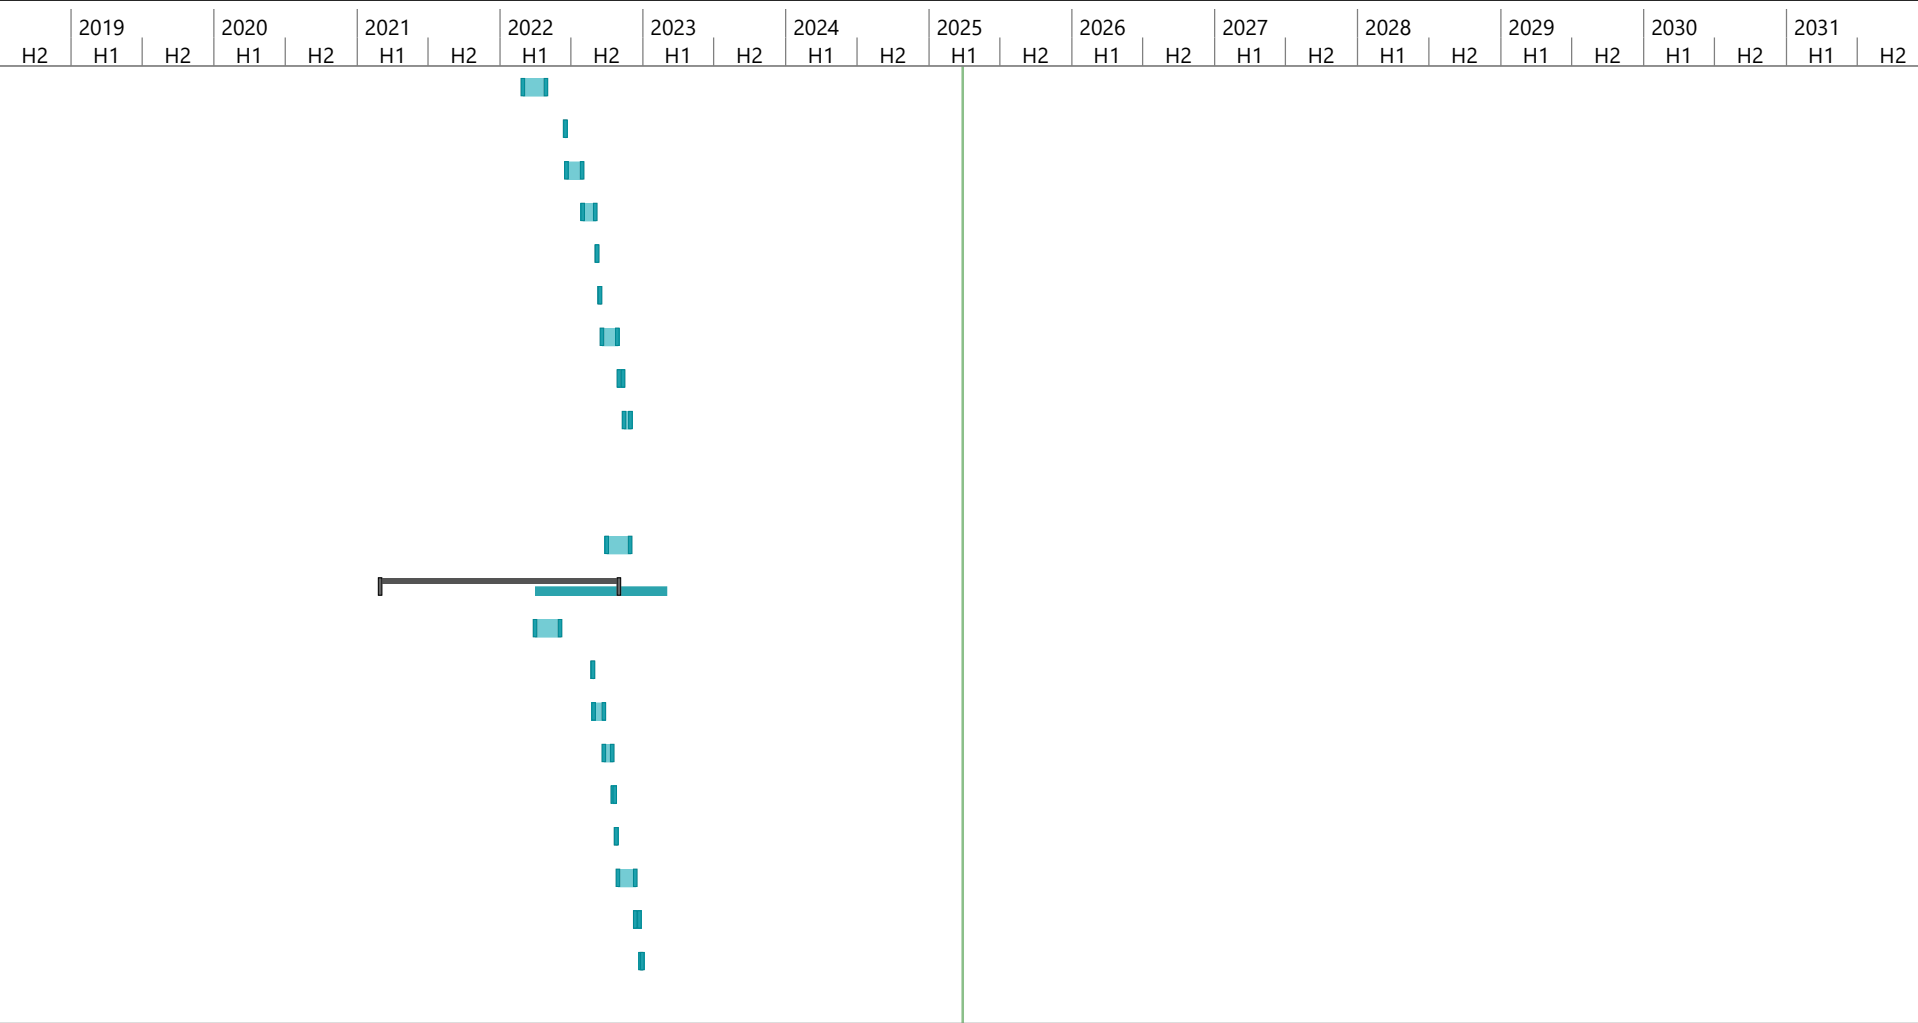


Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

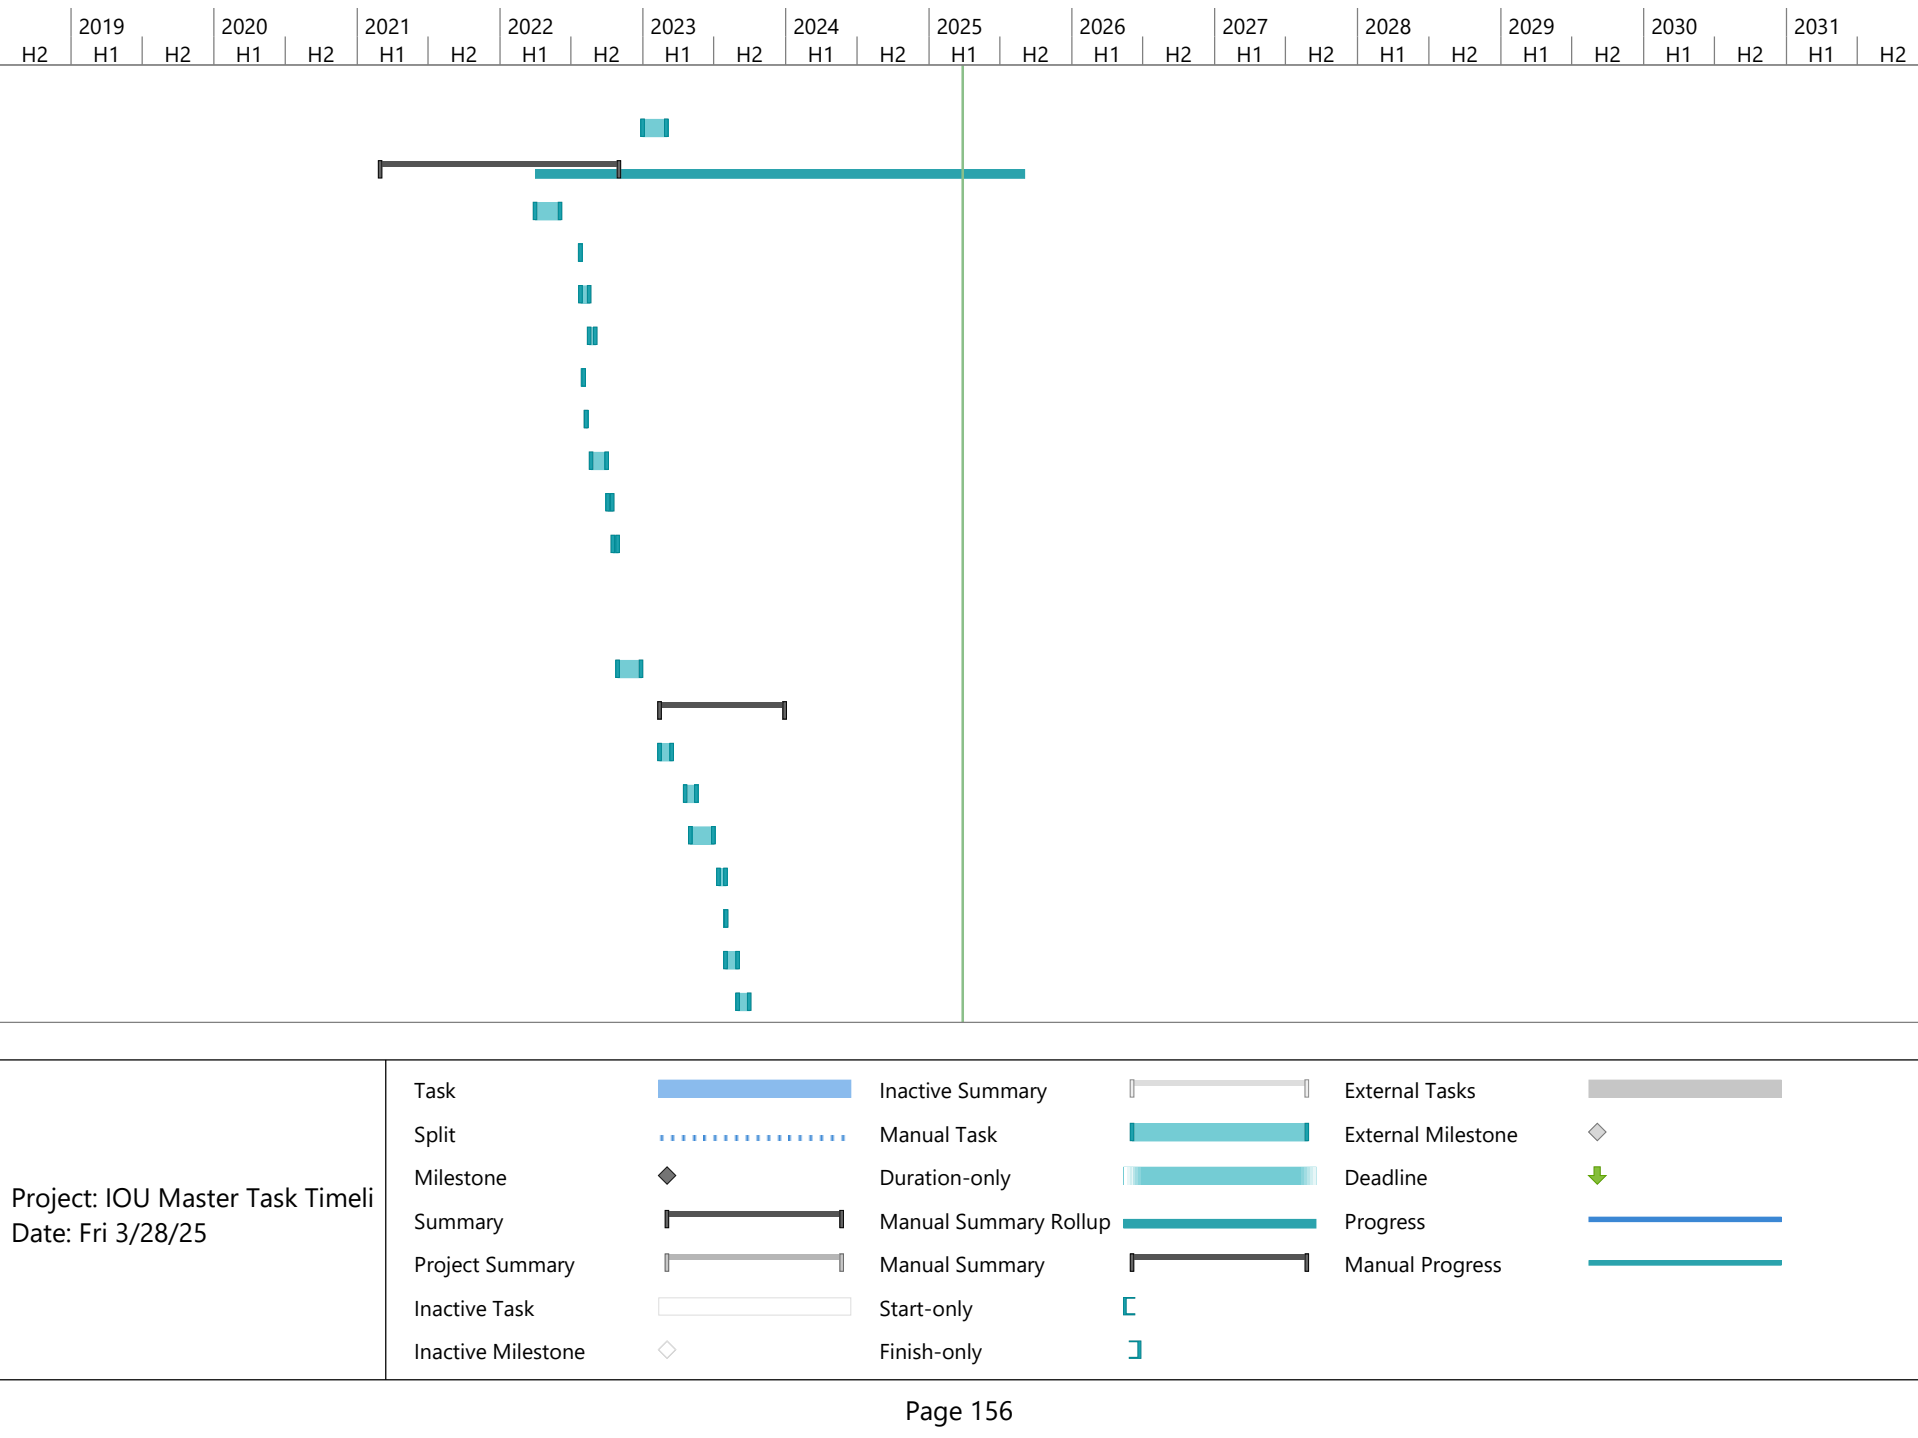


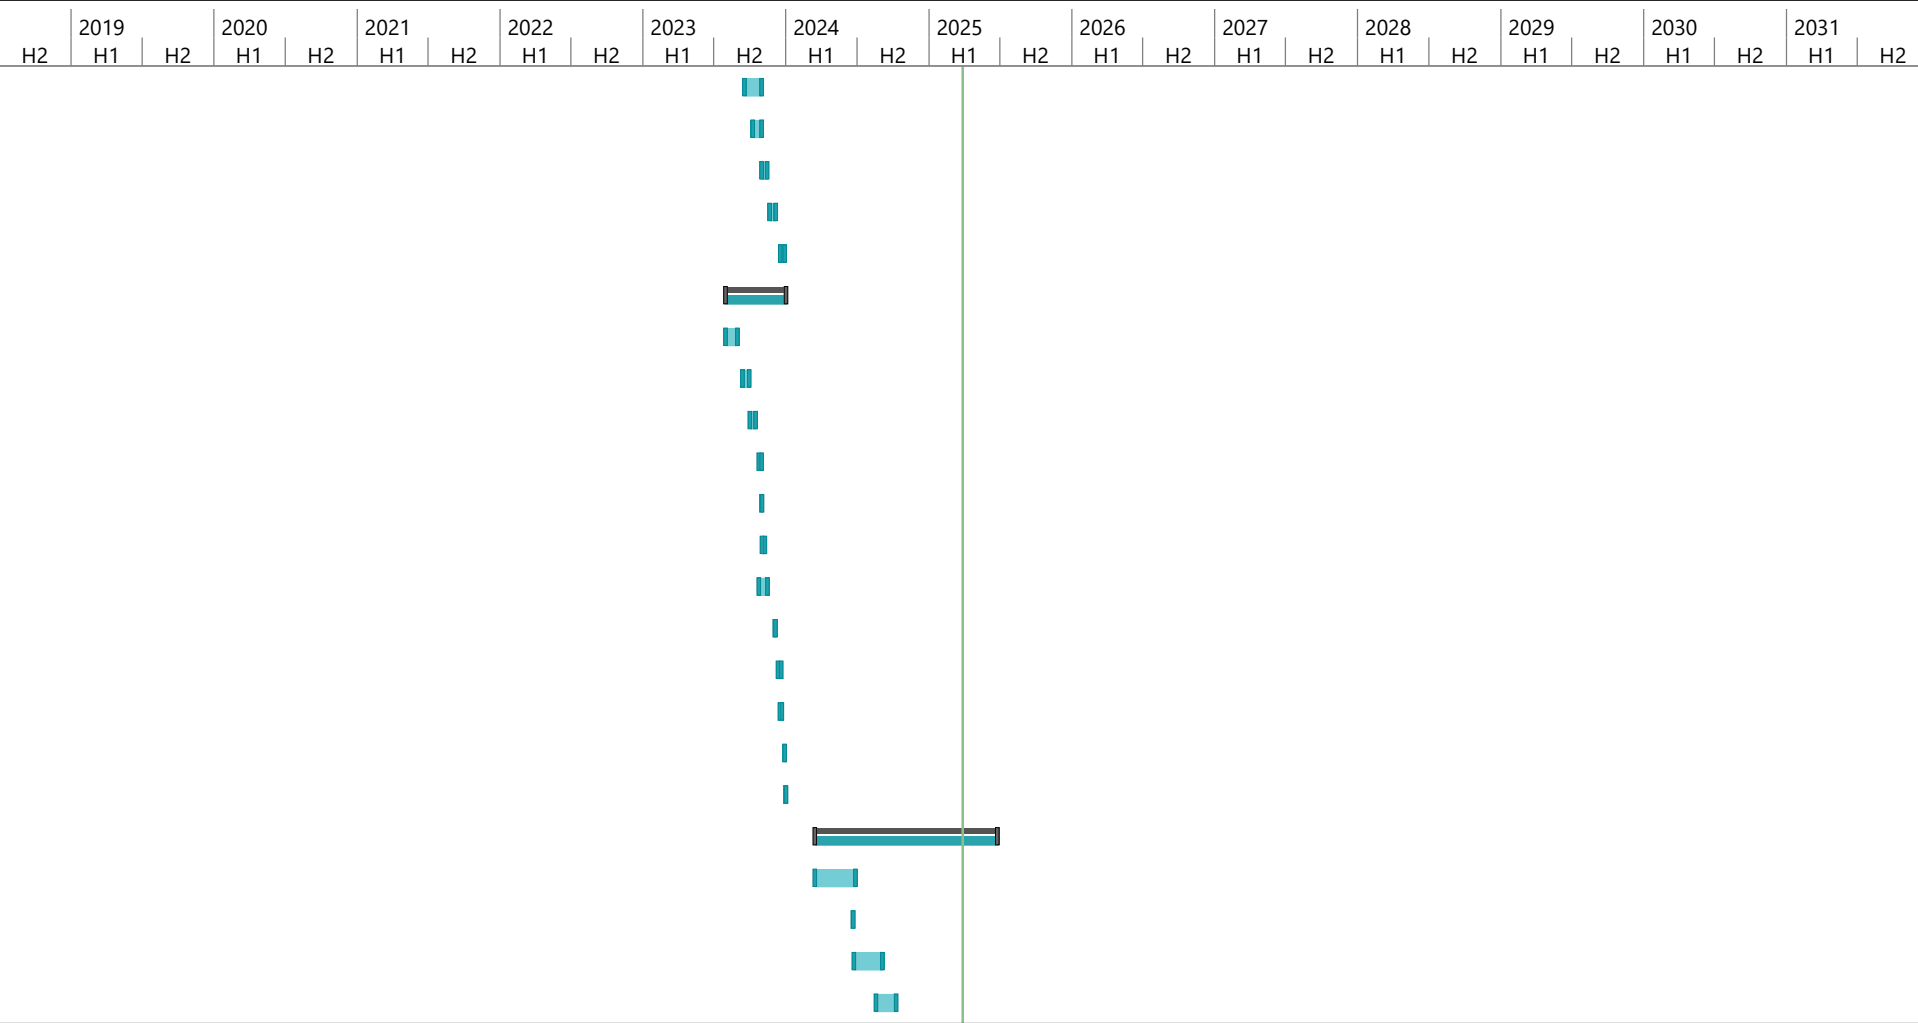
Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

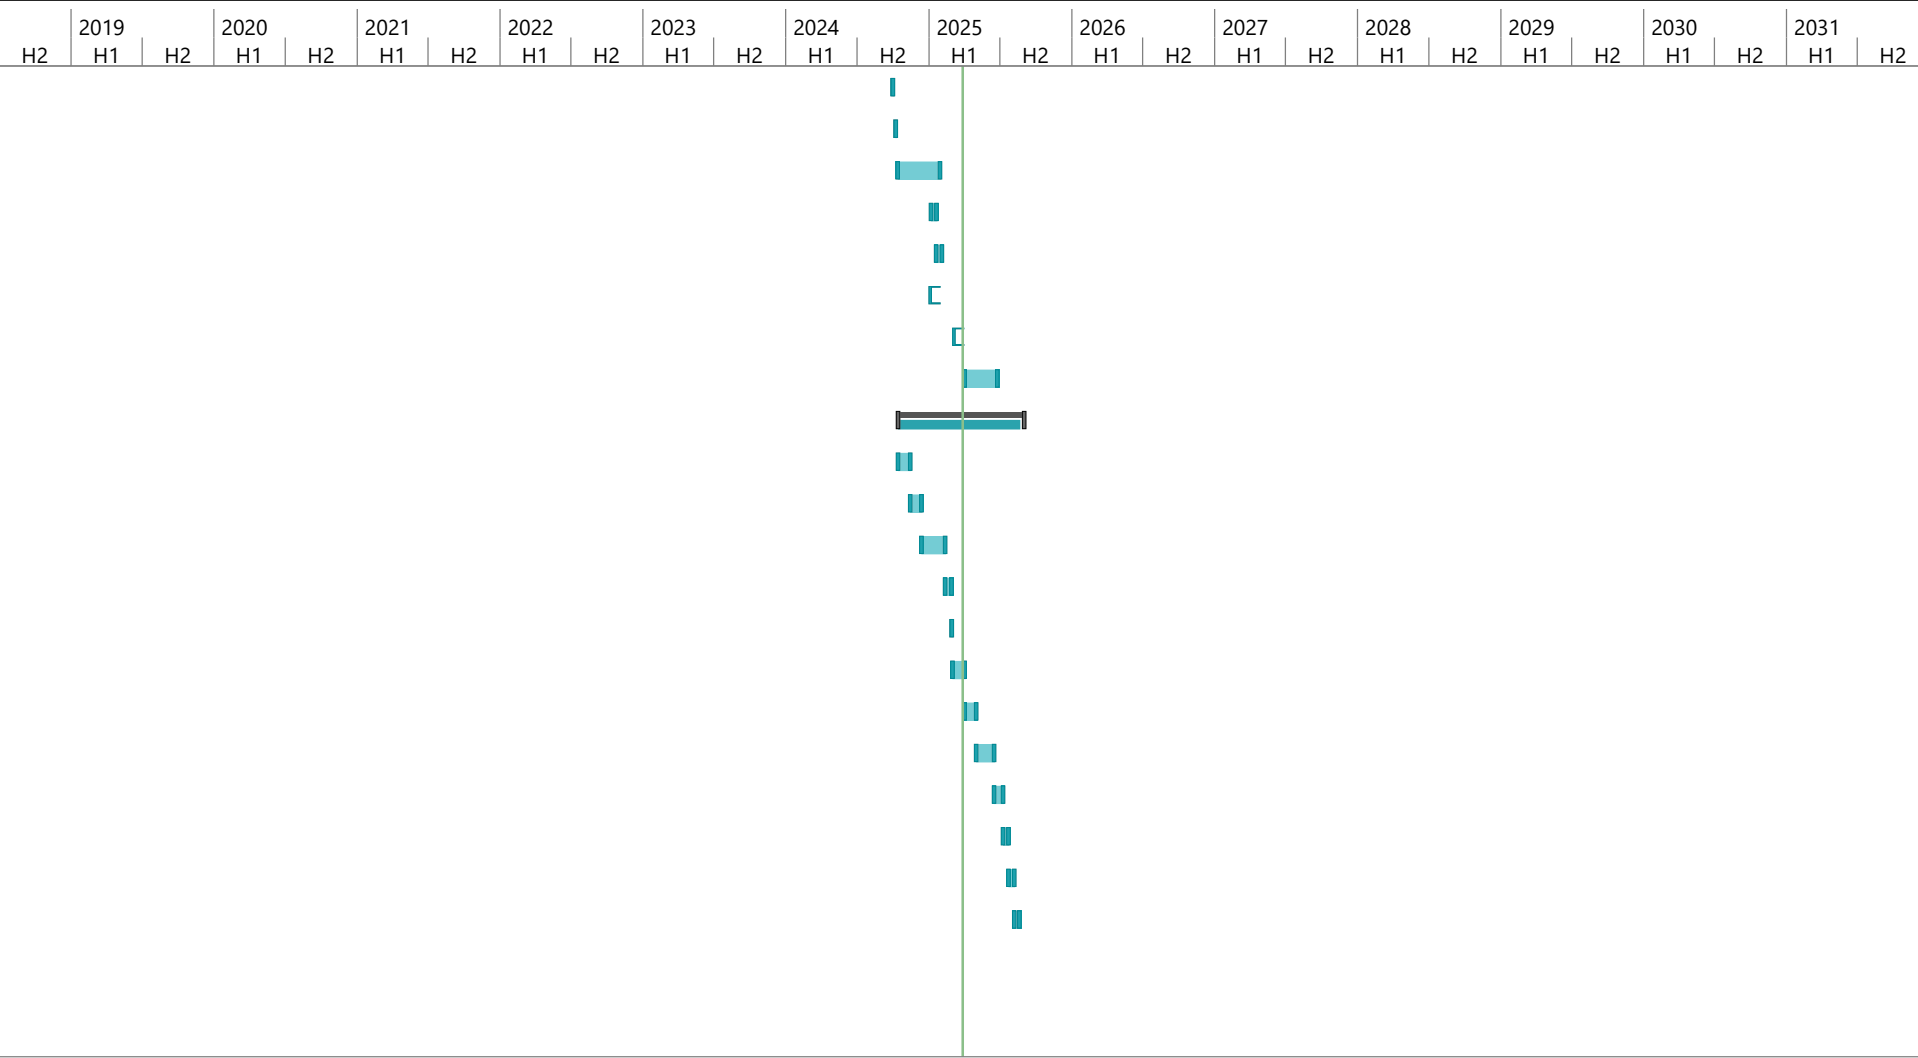


Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			





Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



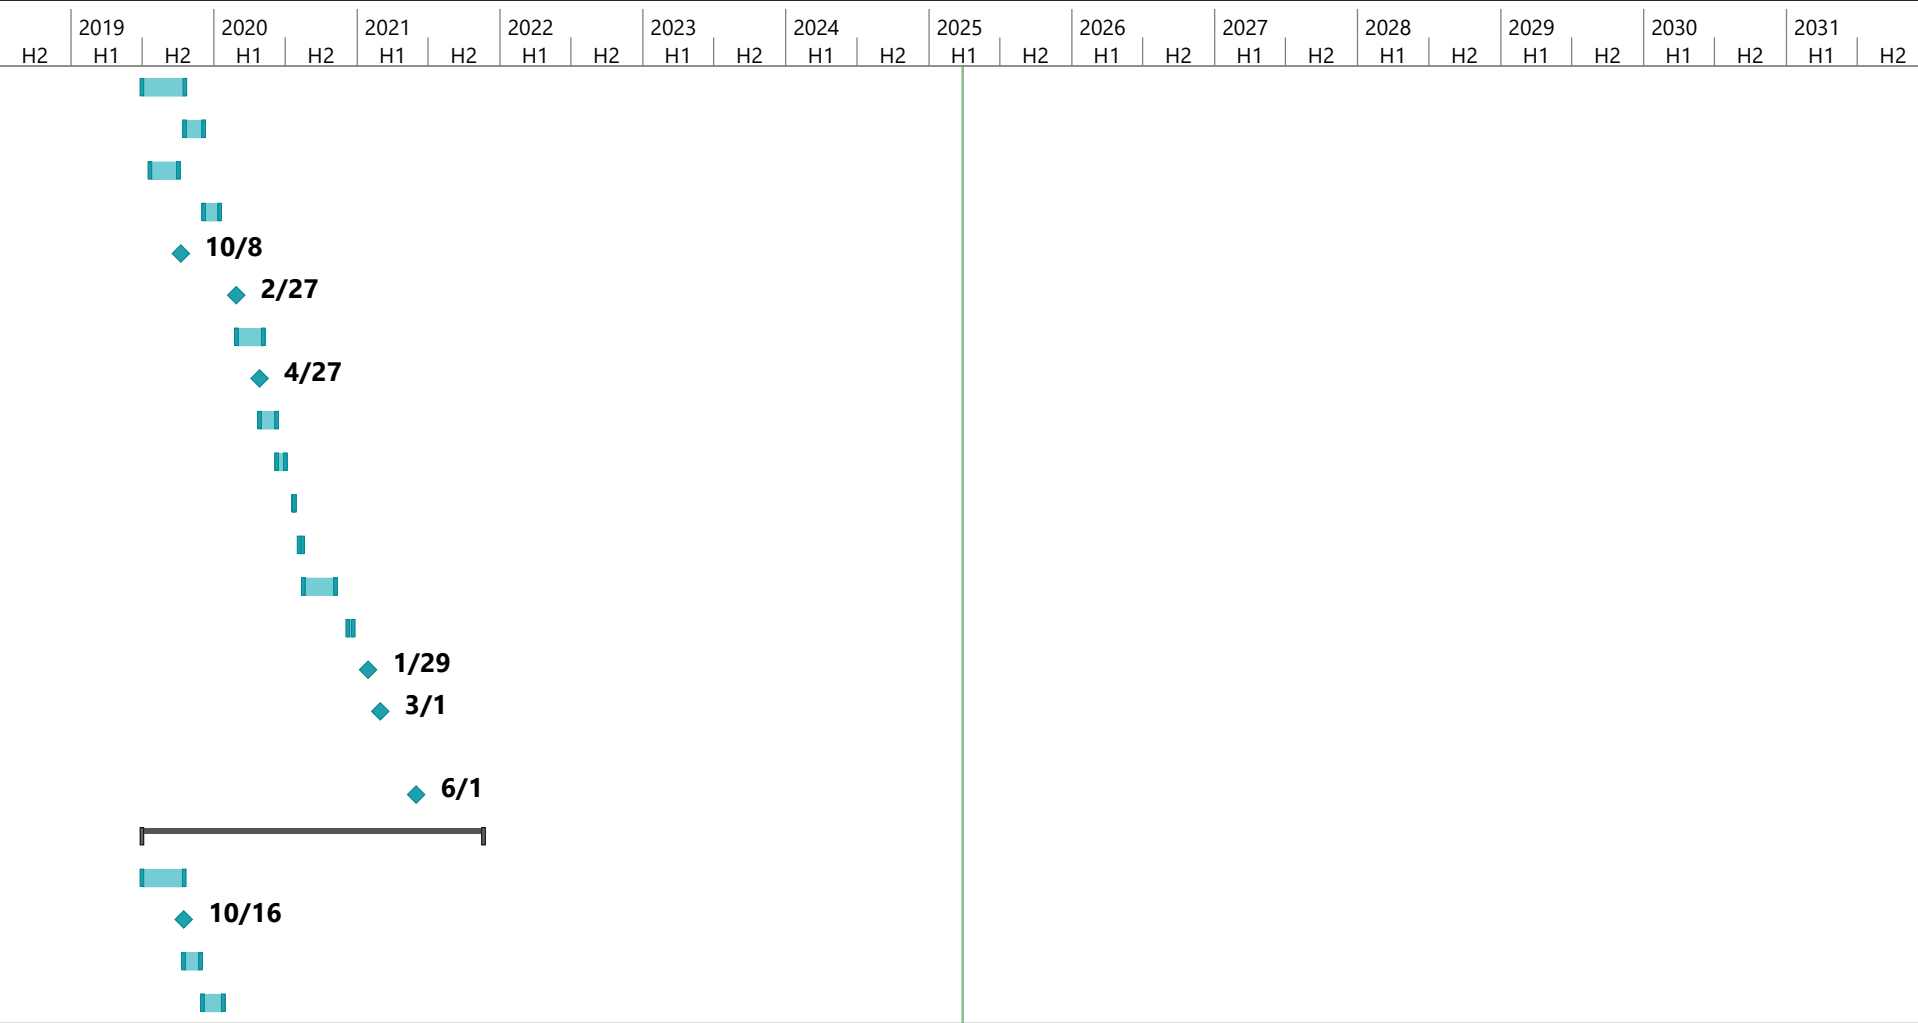
Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



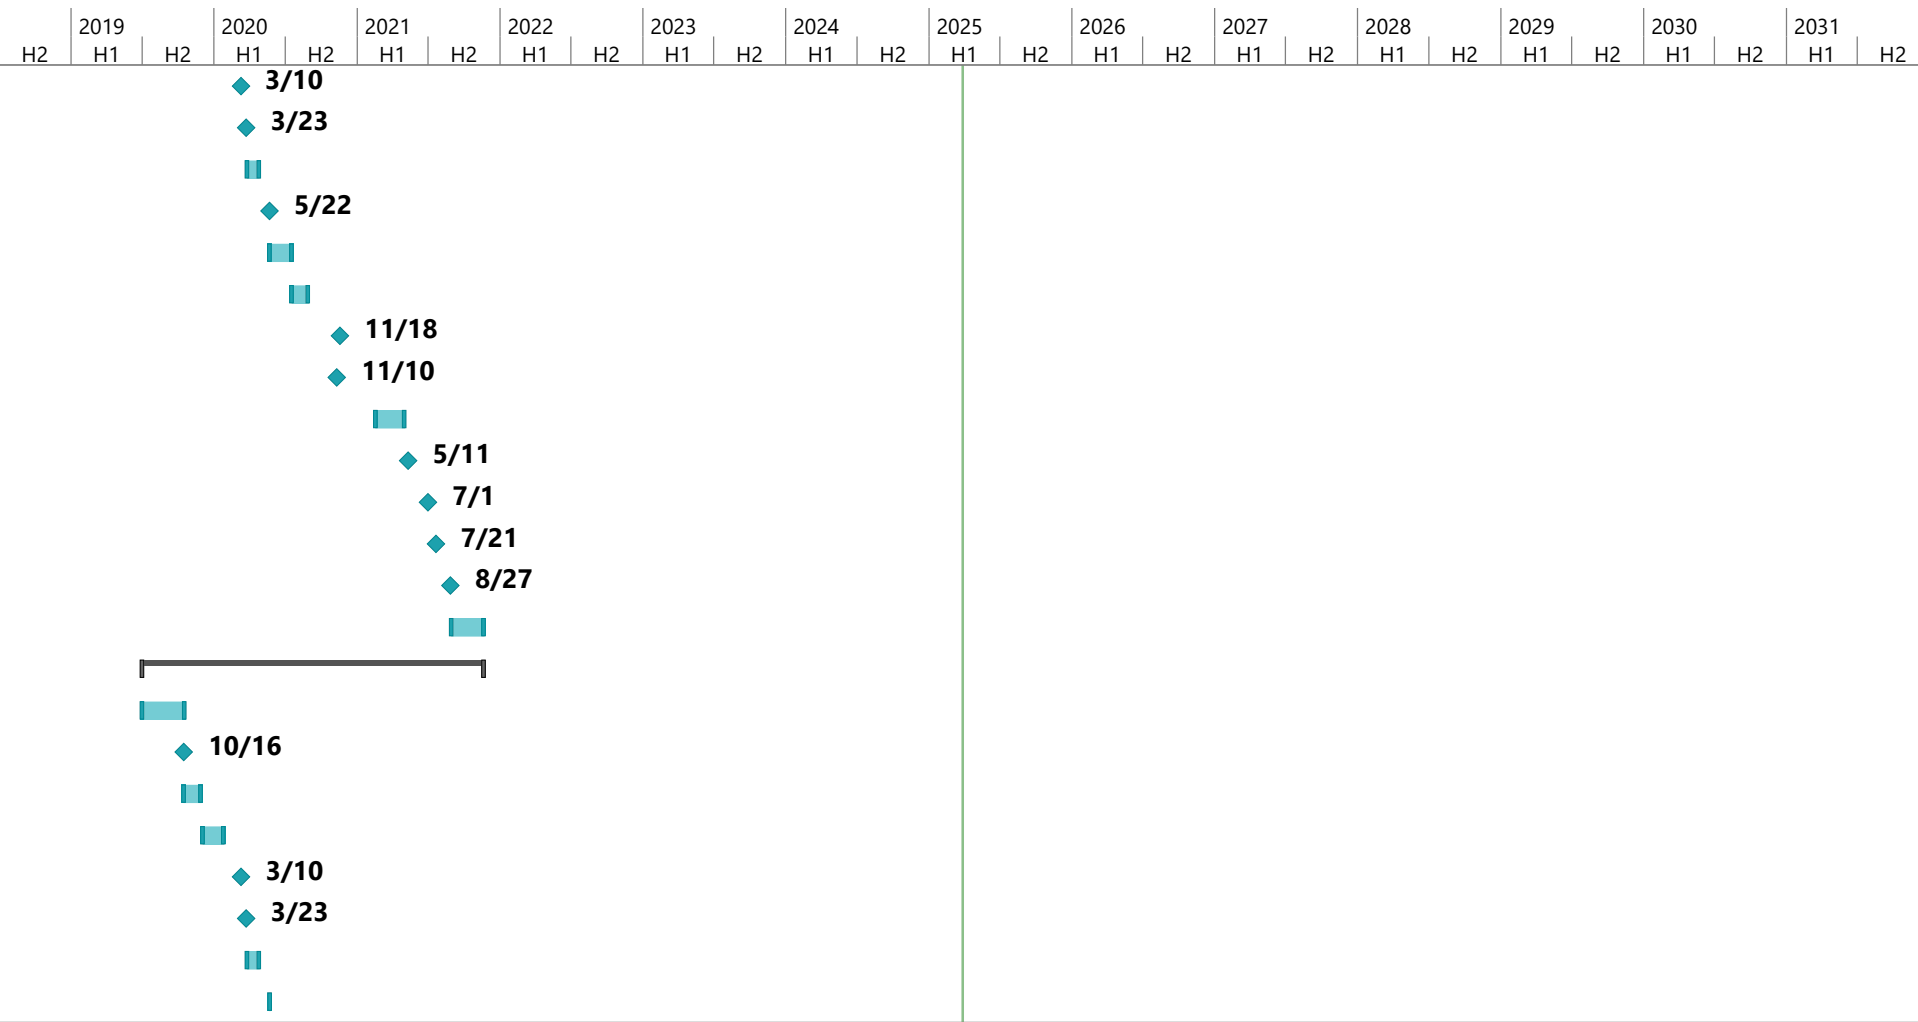
Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



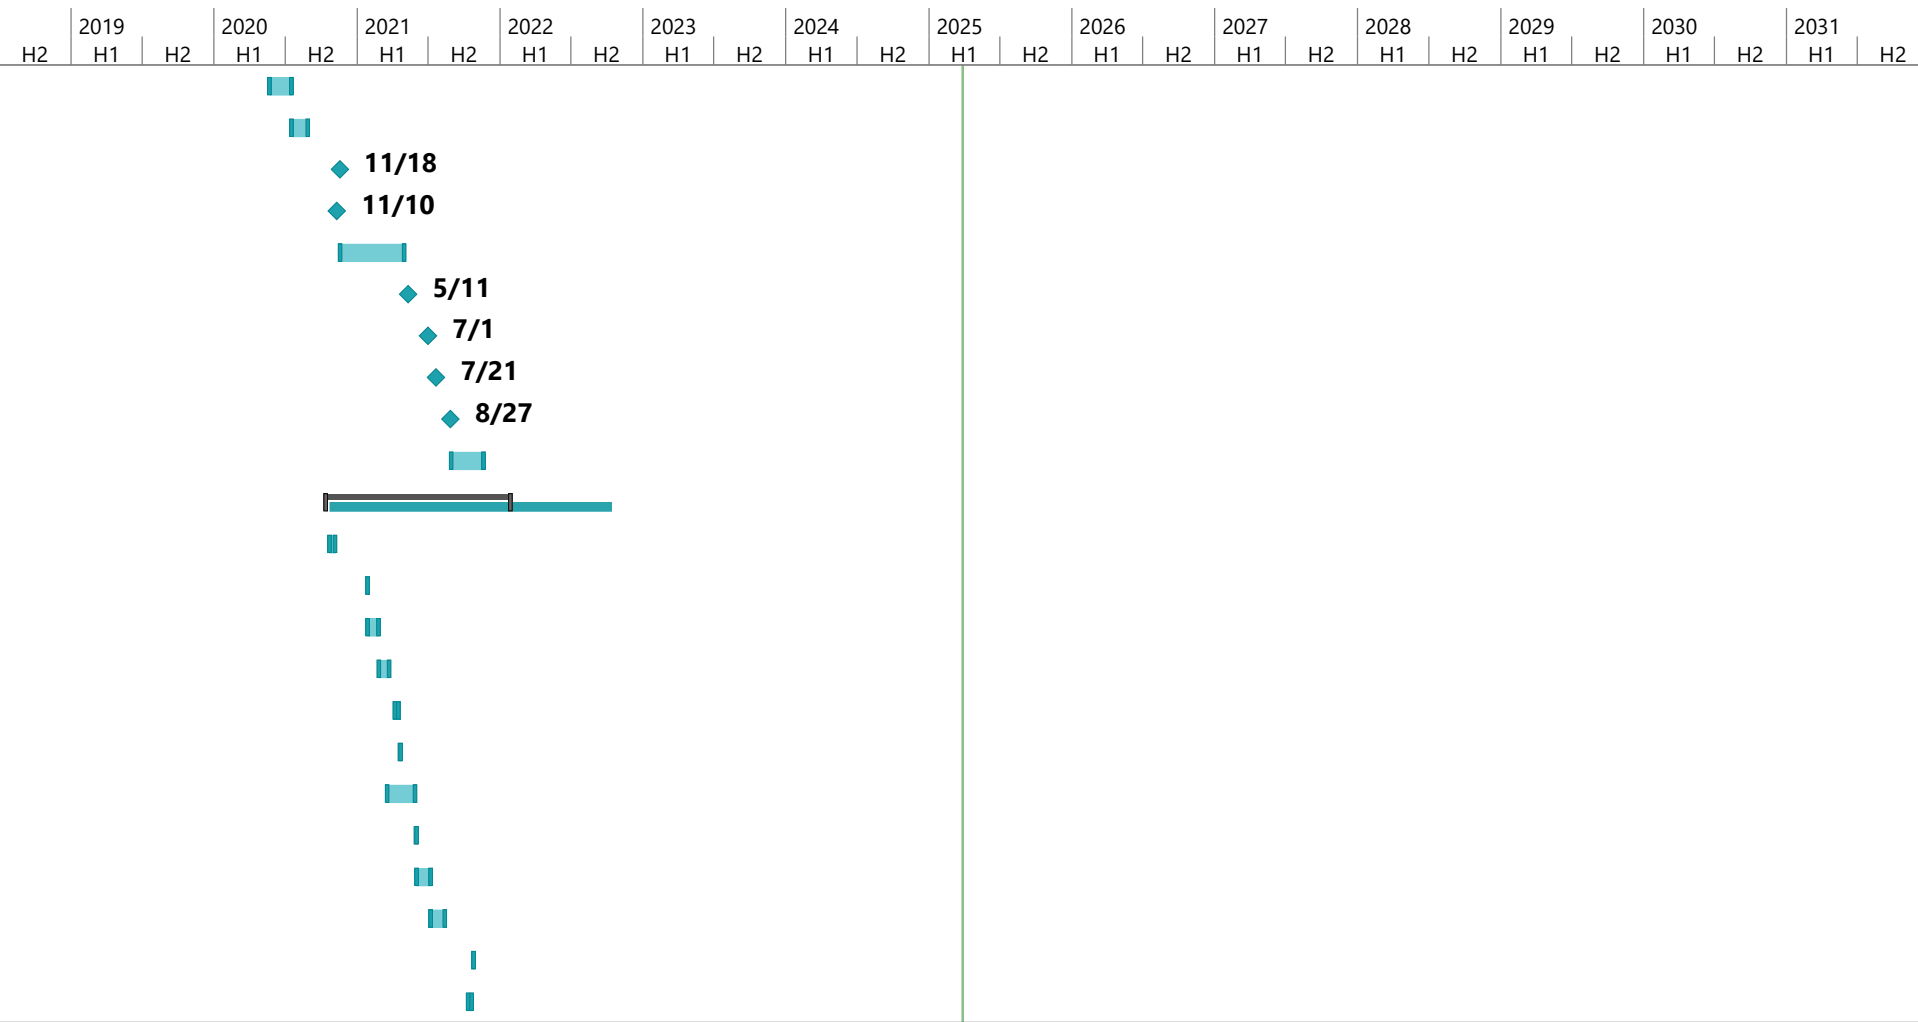
Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



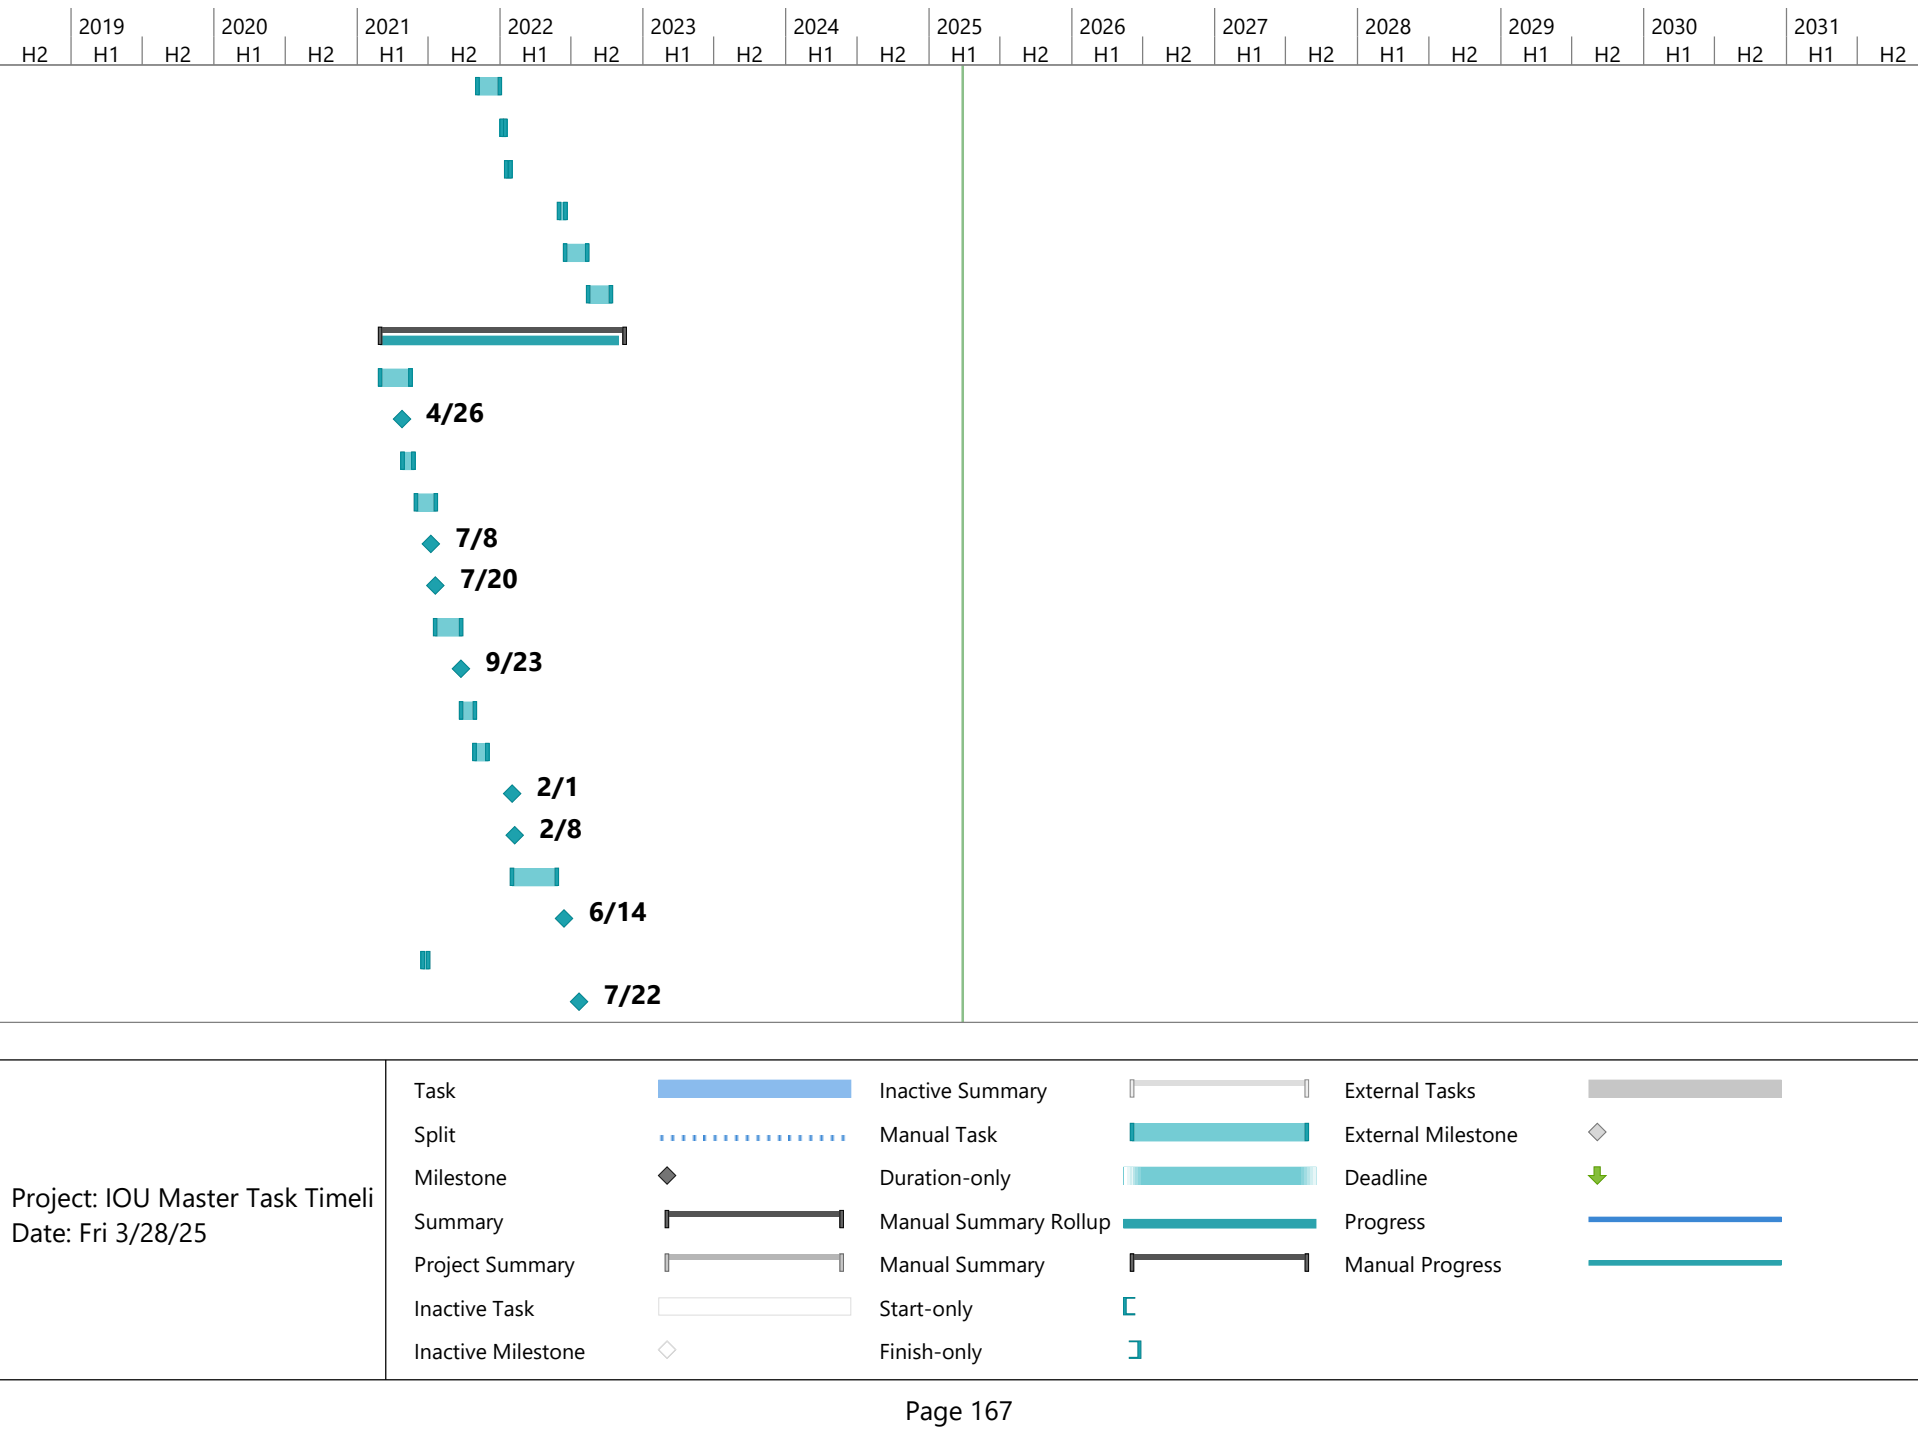
Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

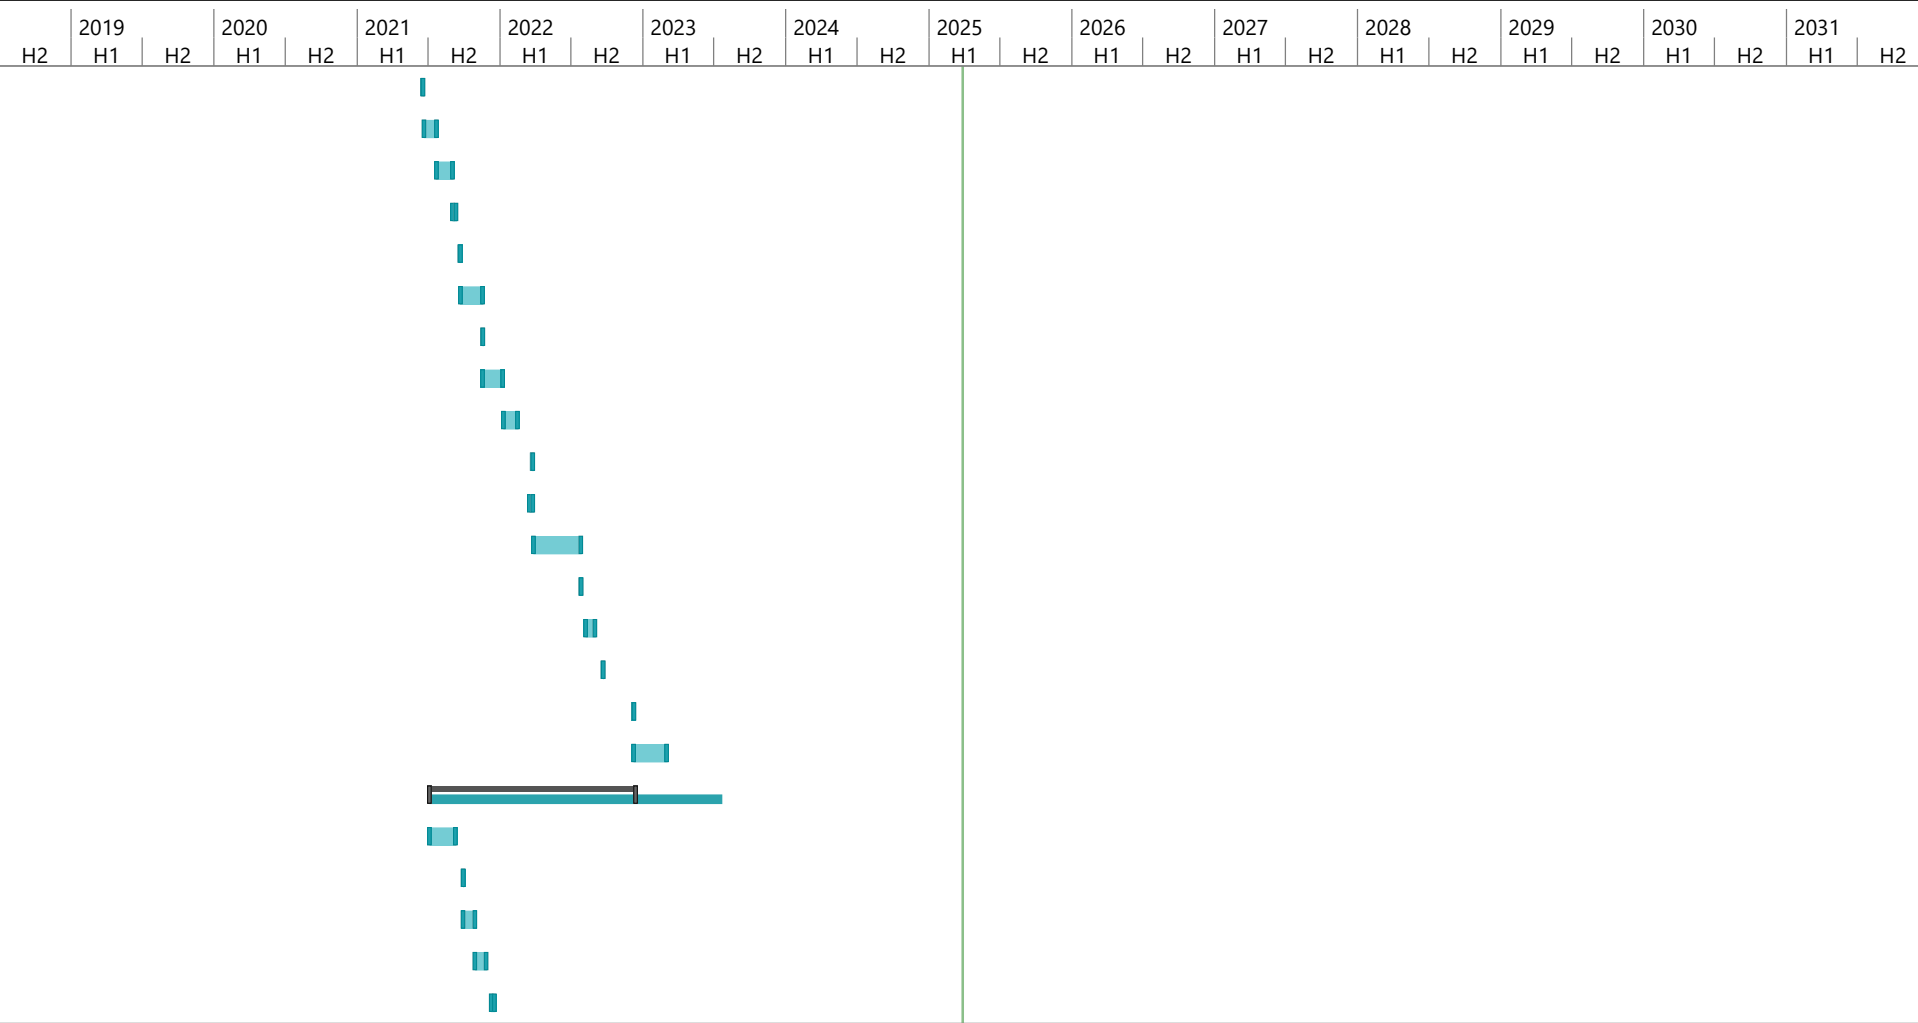


Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			





Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

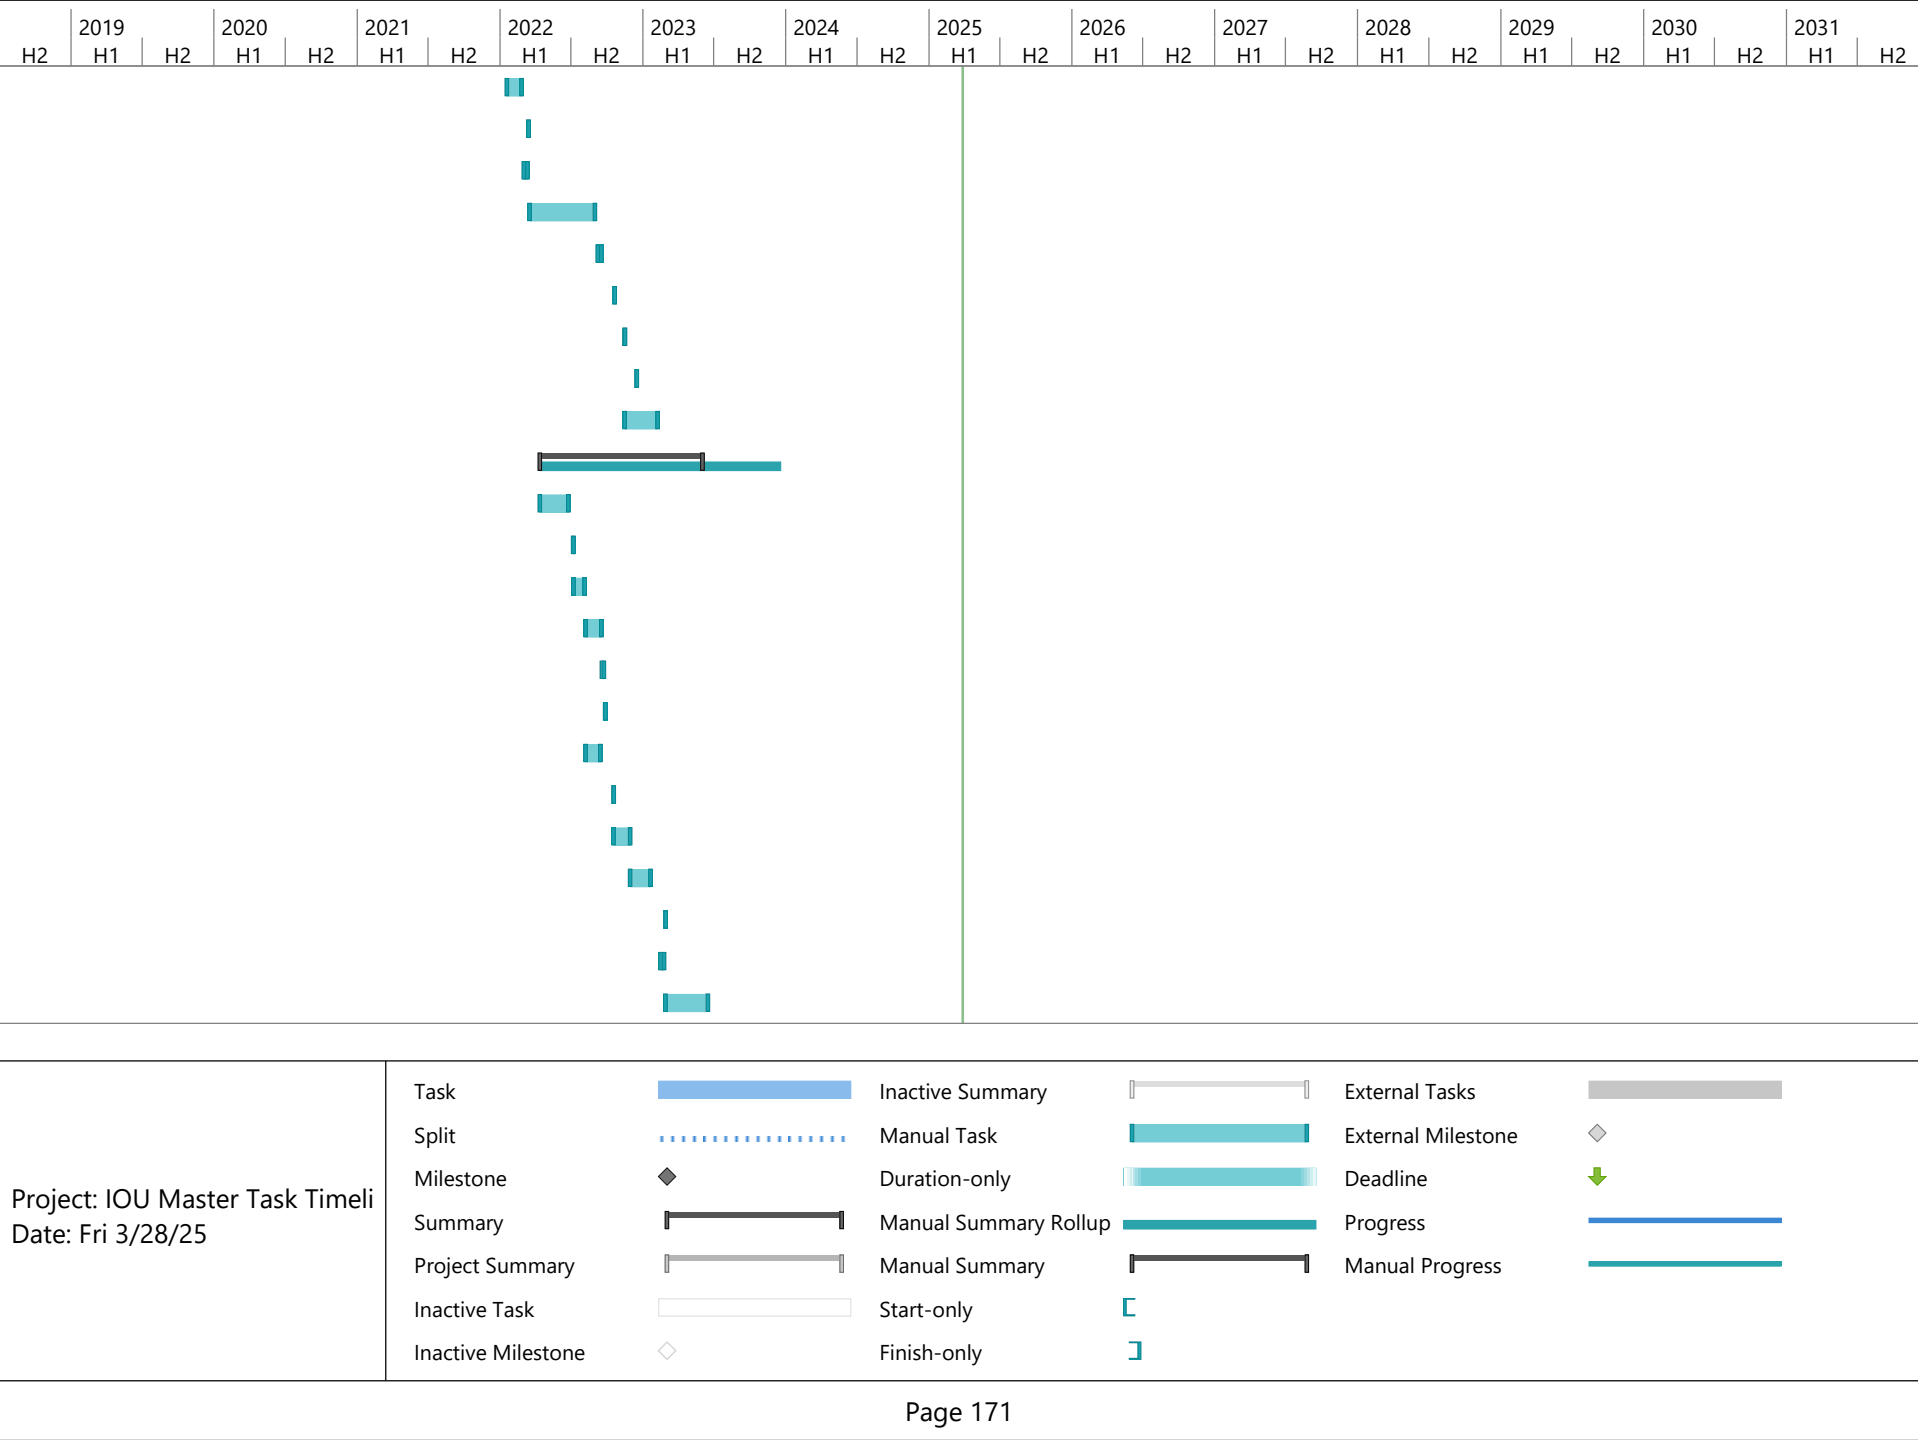
External Milestone

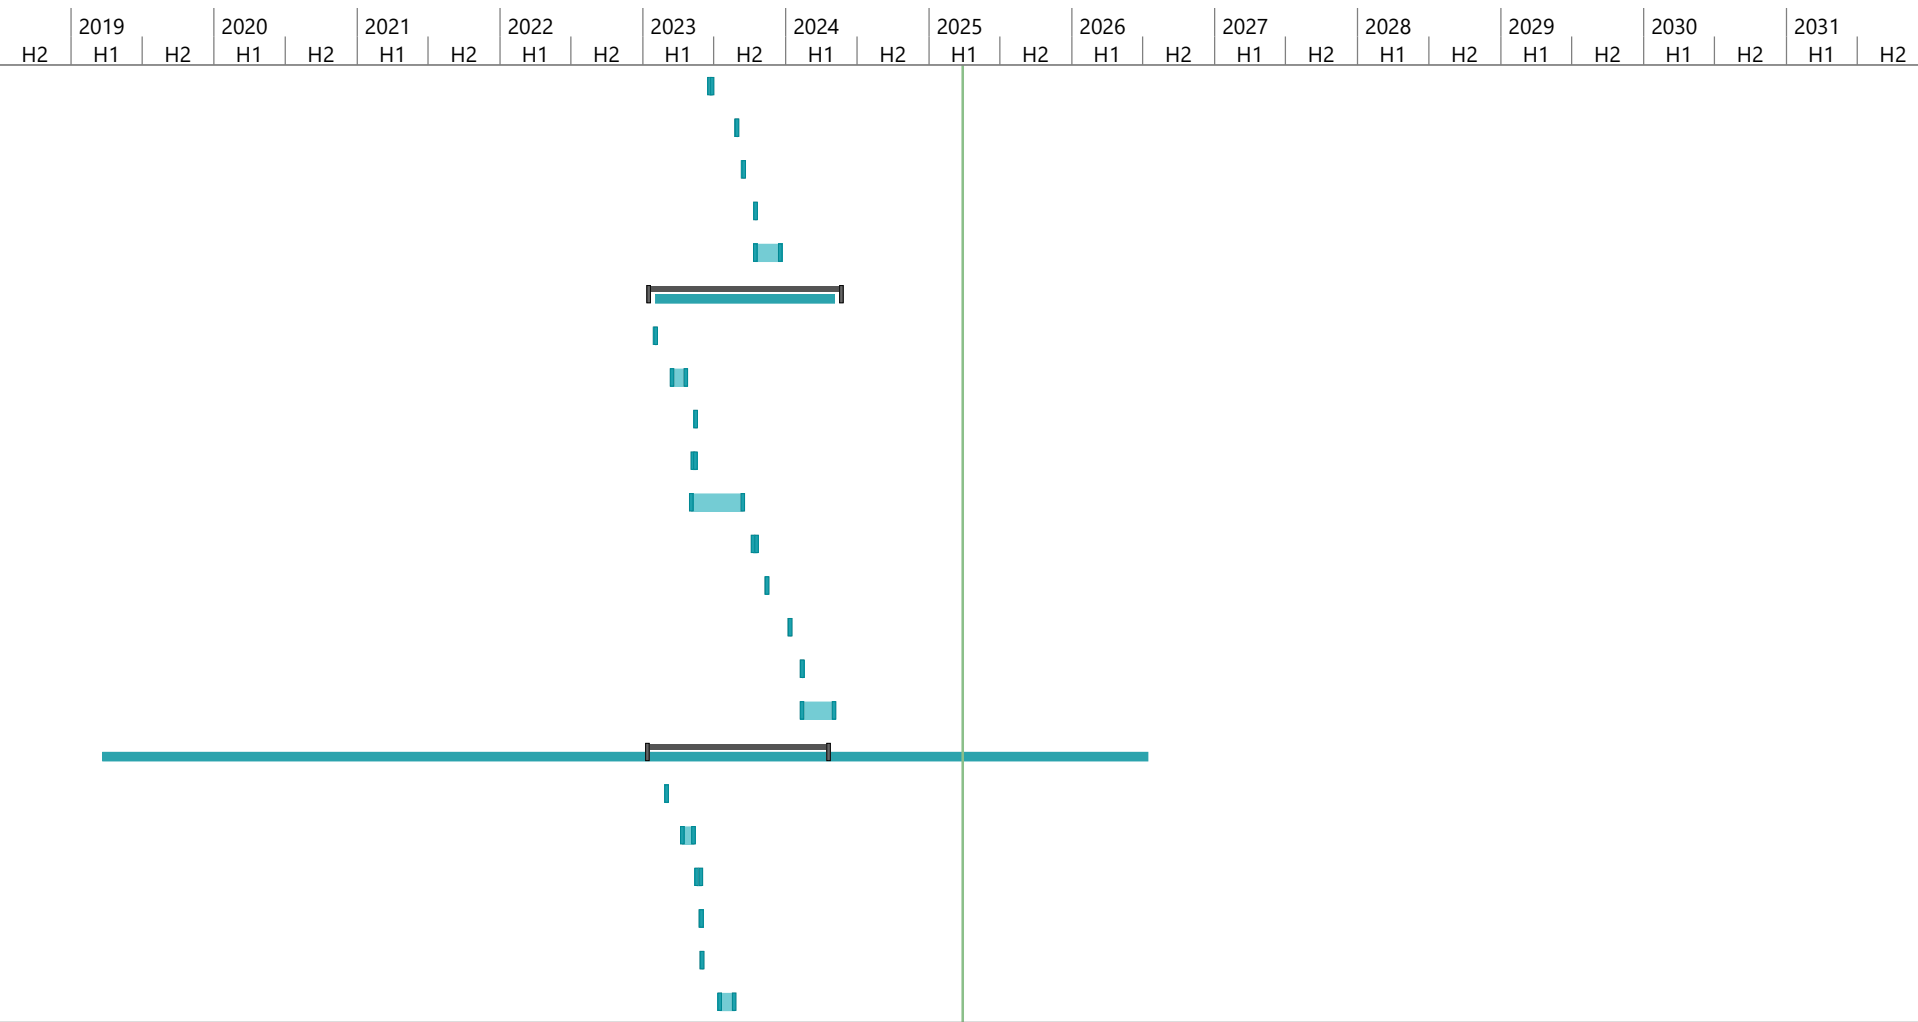
Deadline

Progress

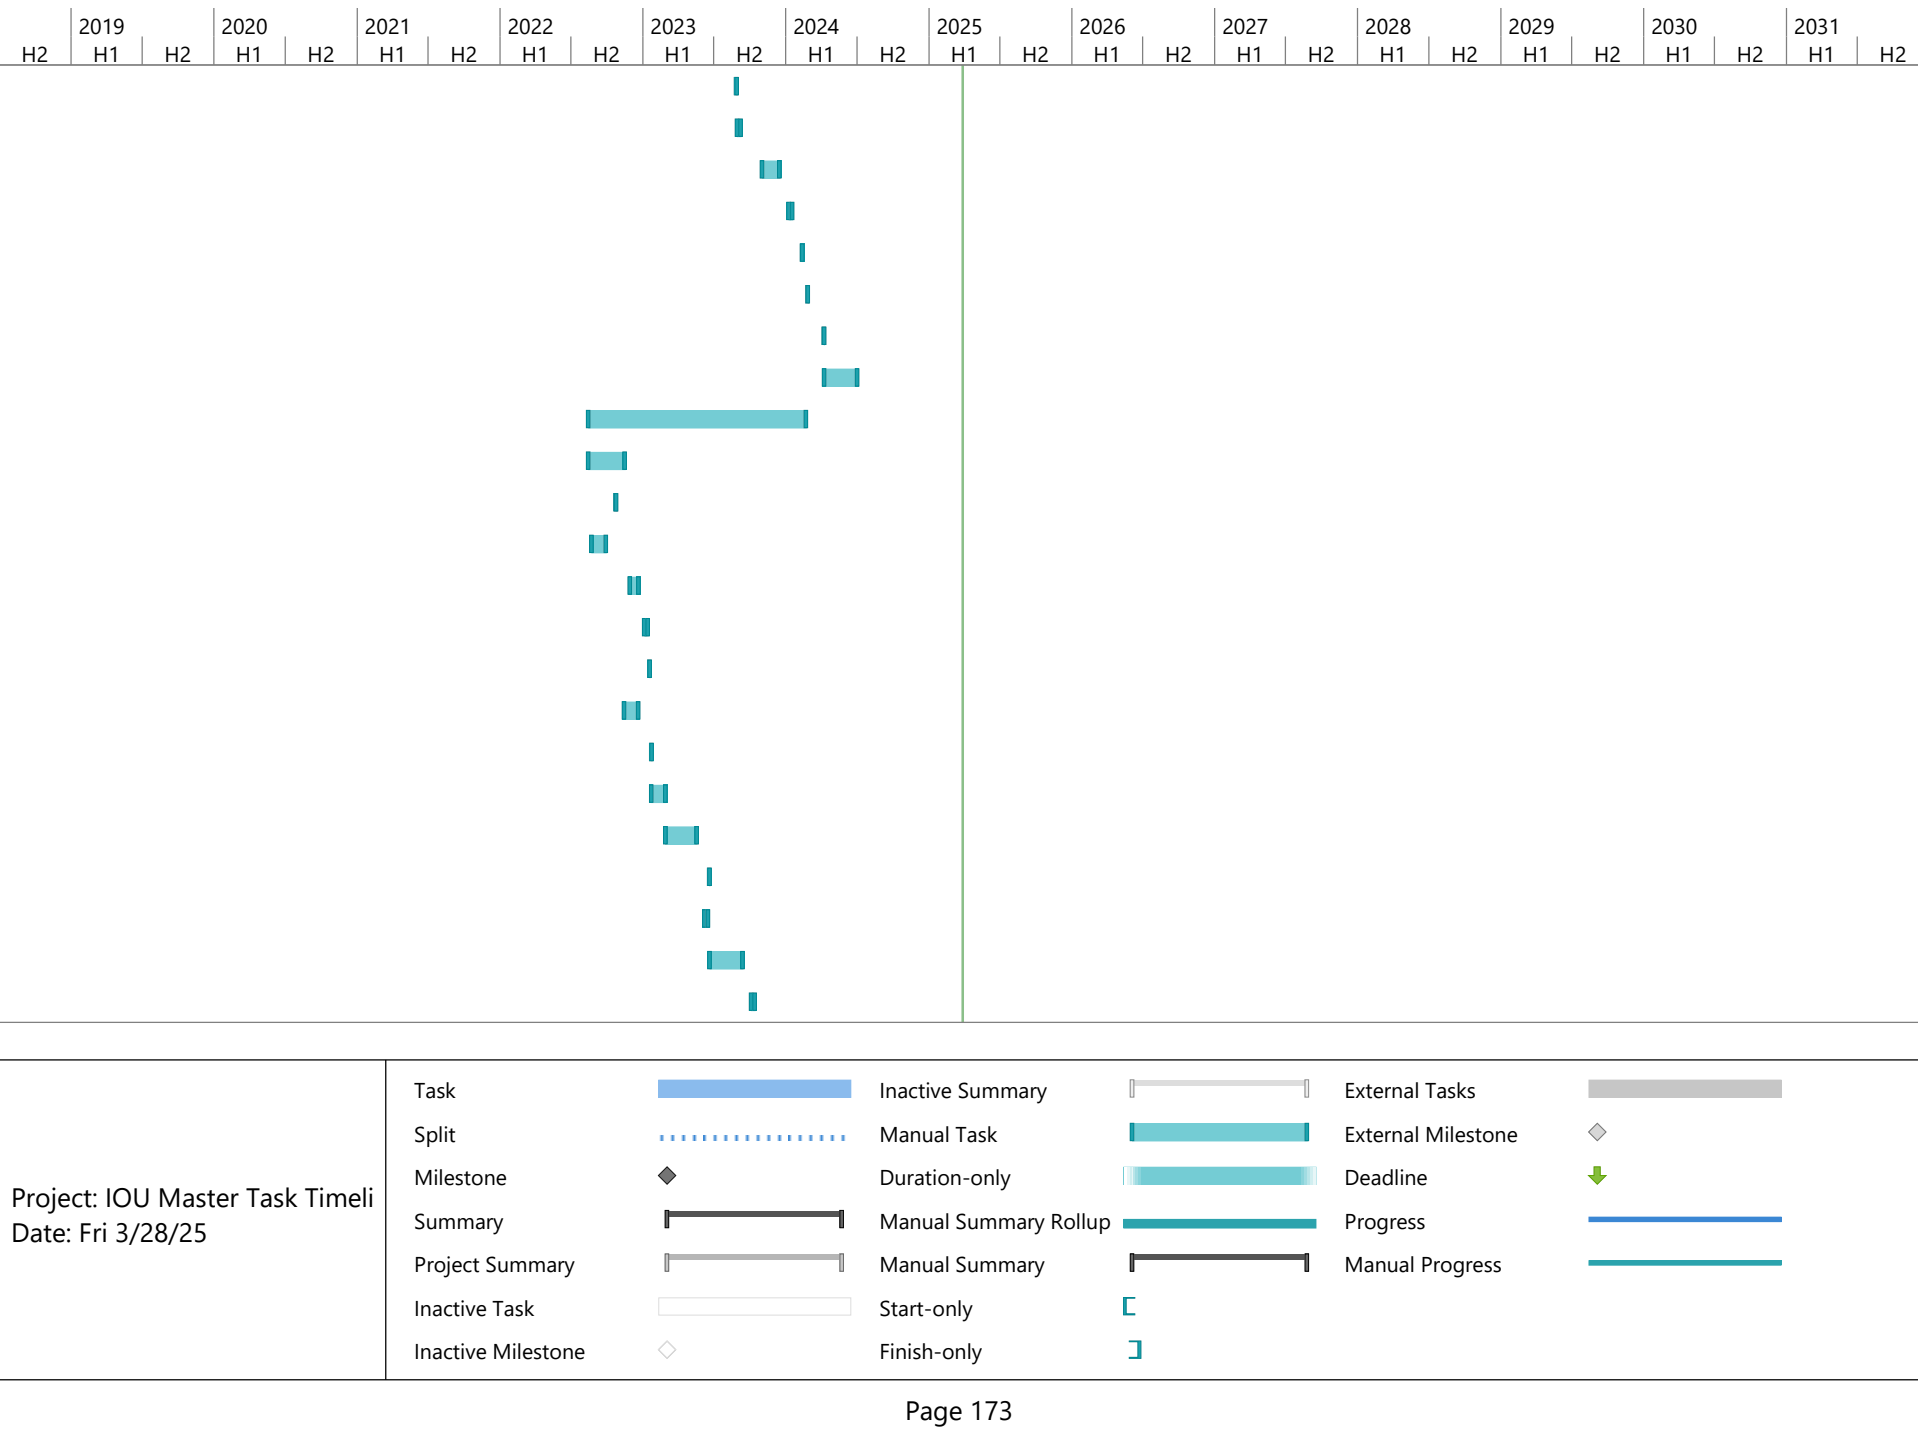
Manual Progress

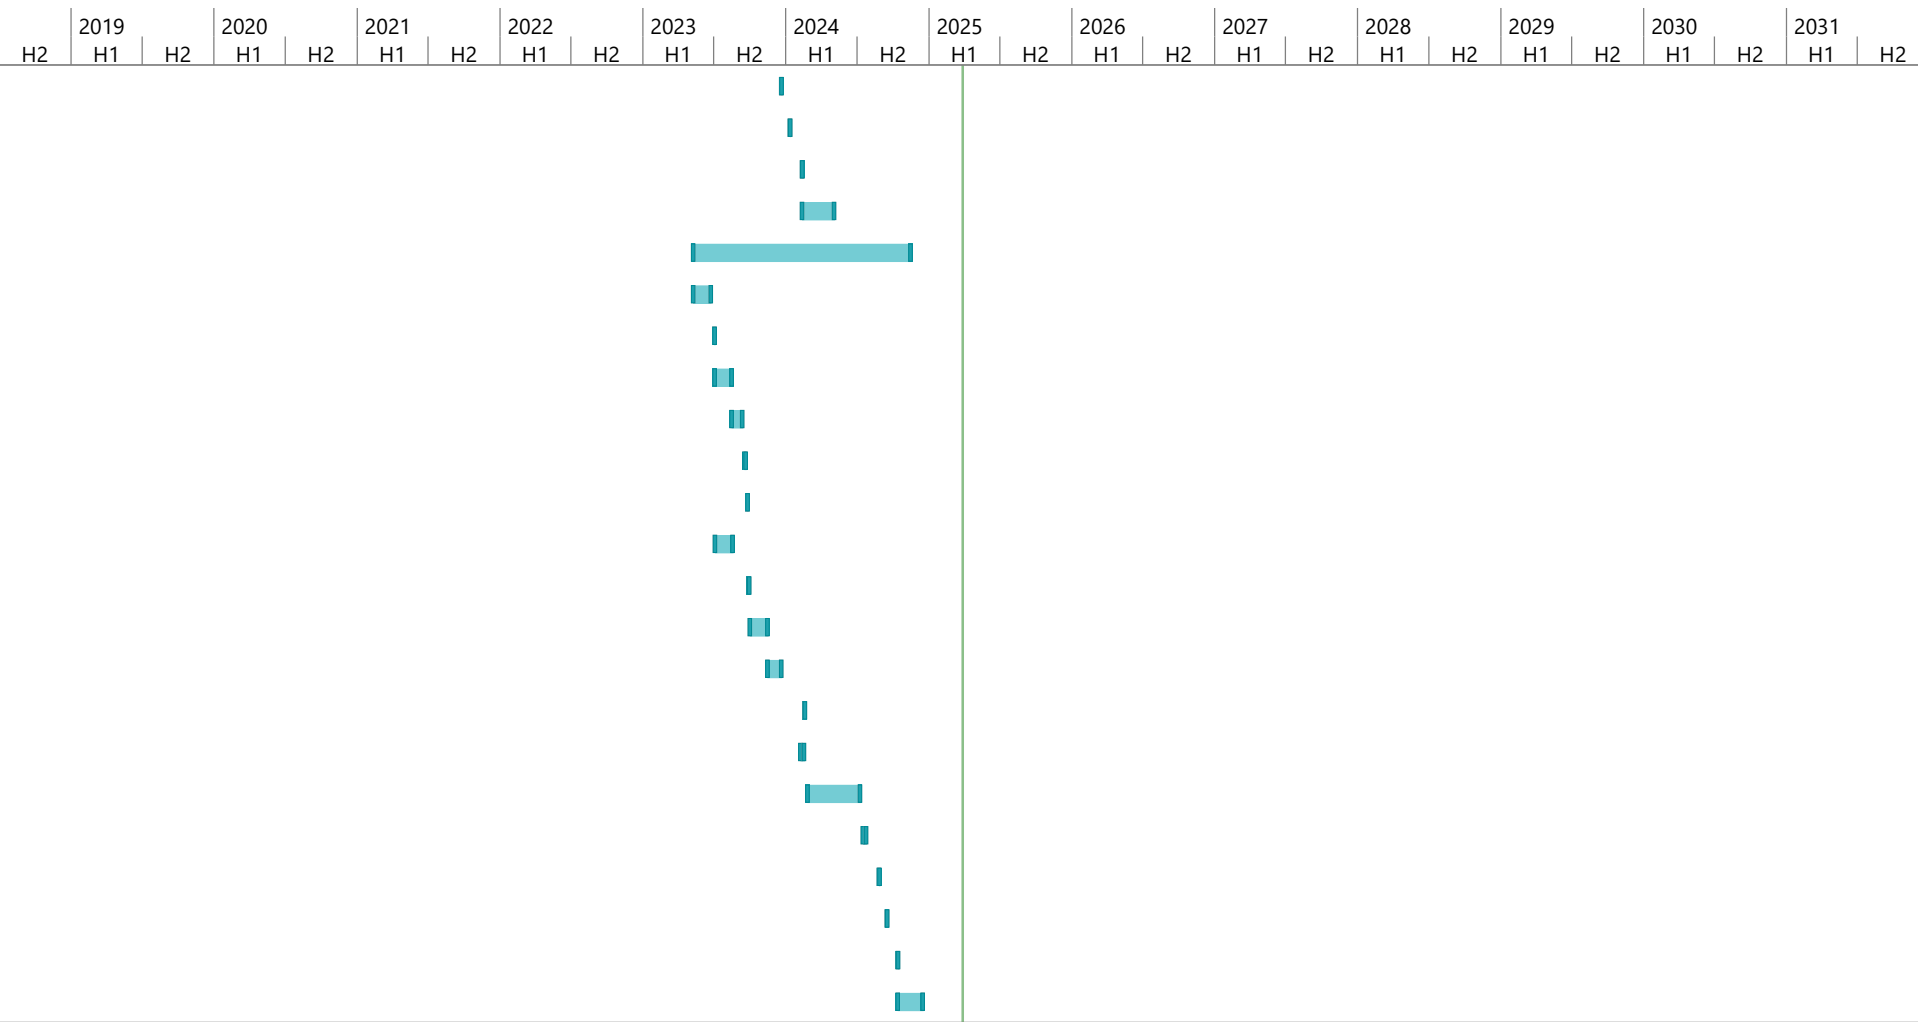
Page 169



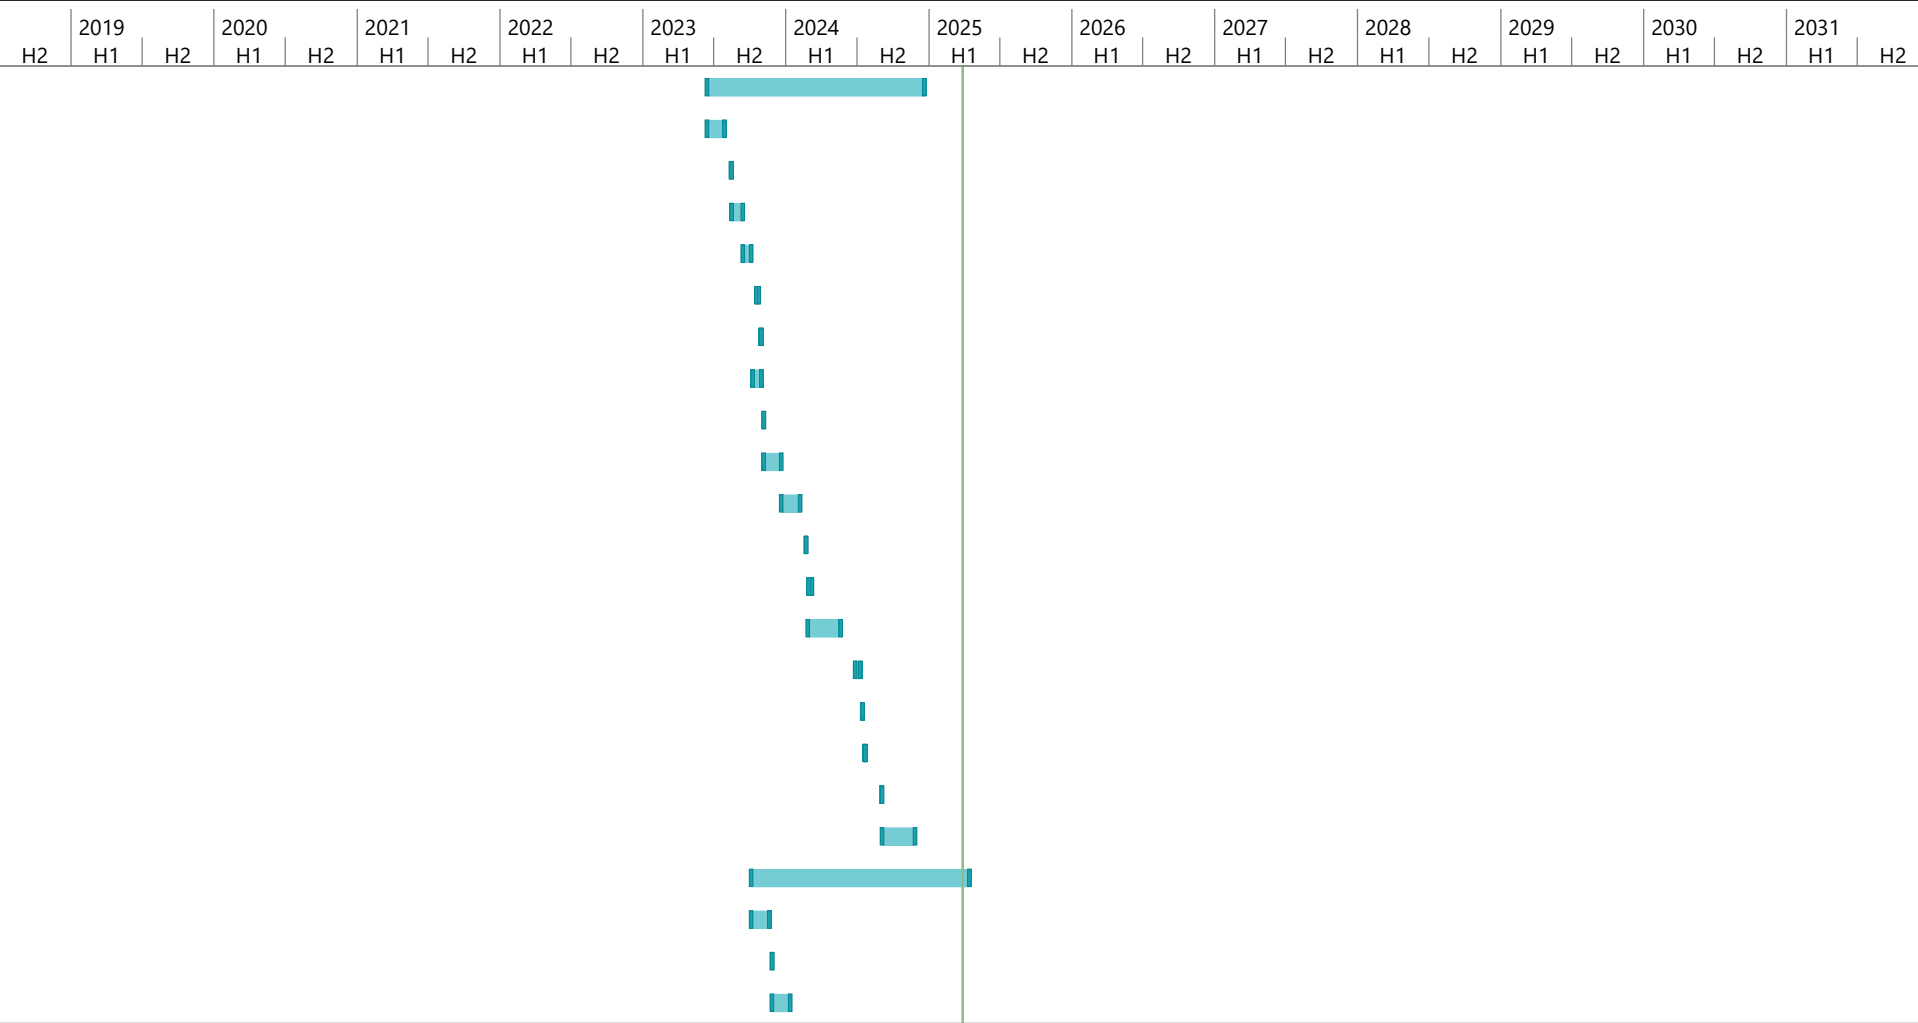


Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

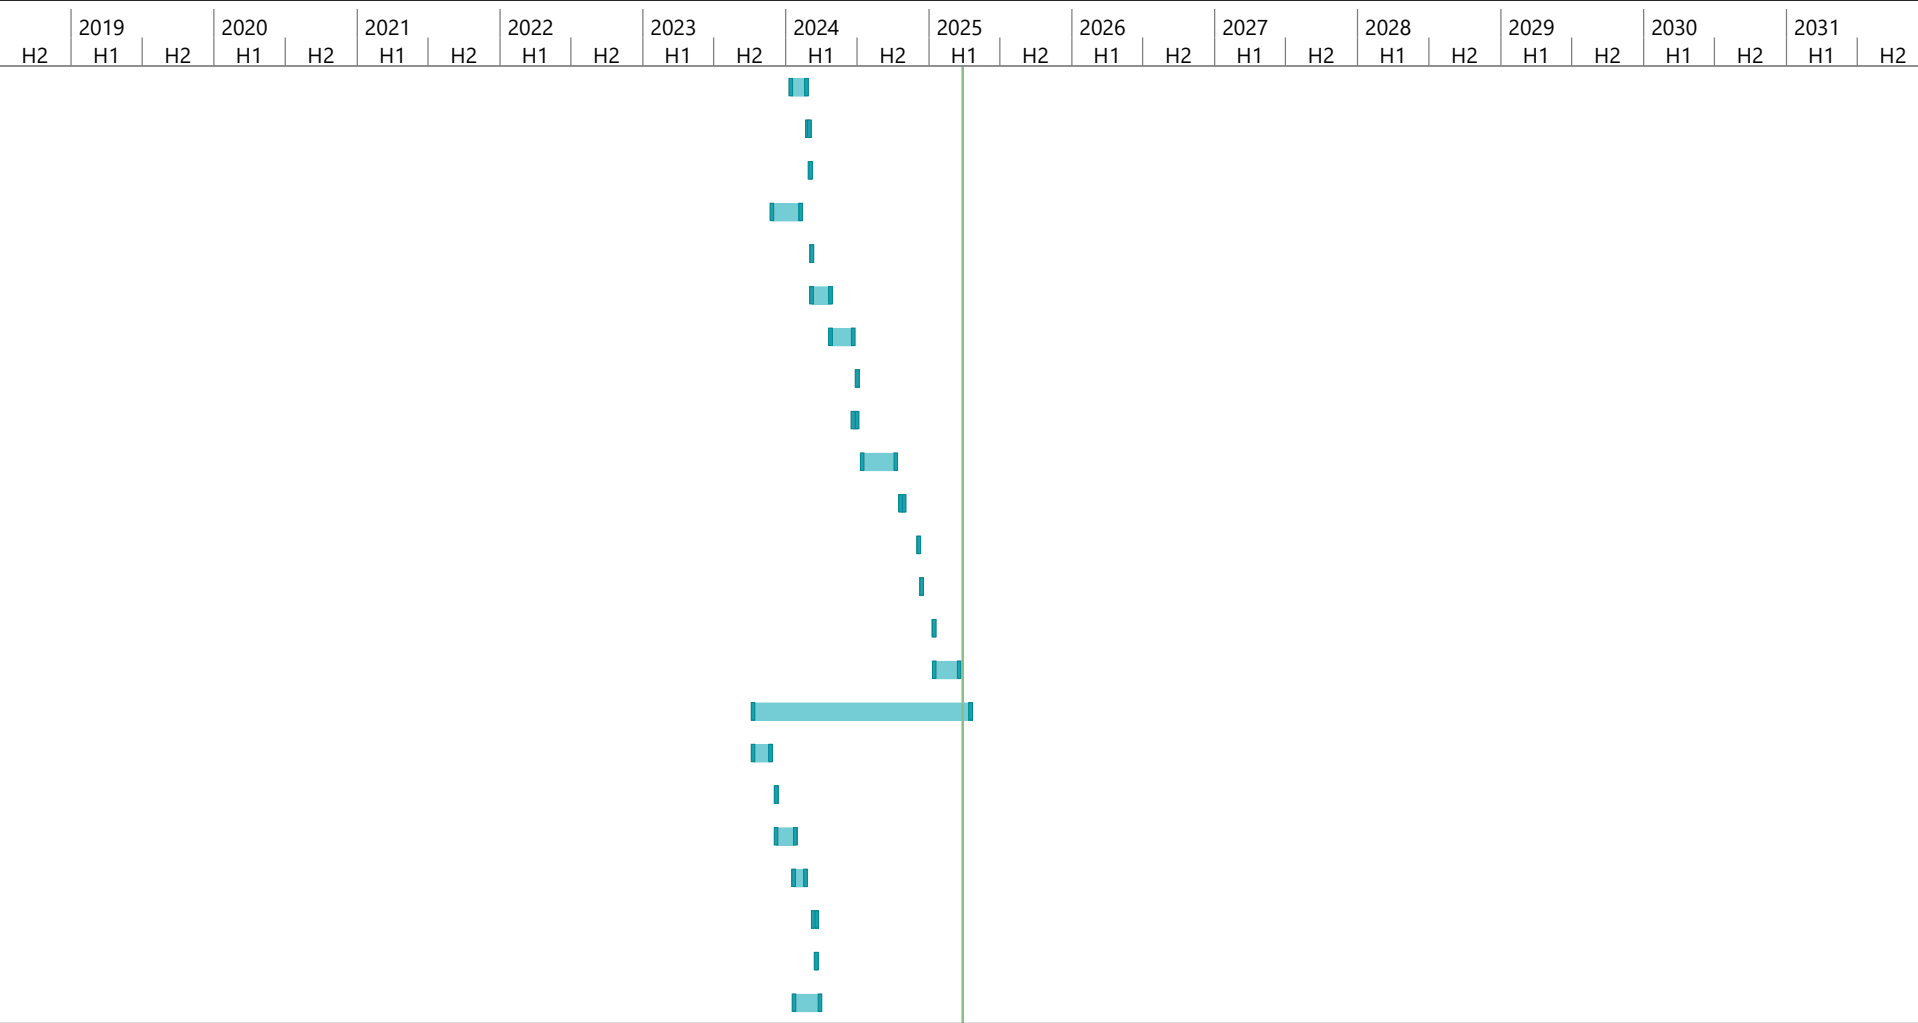




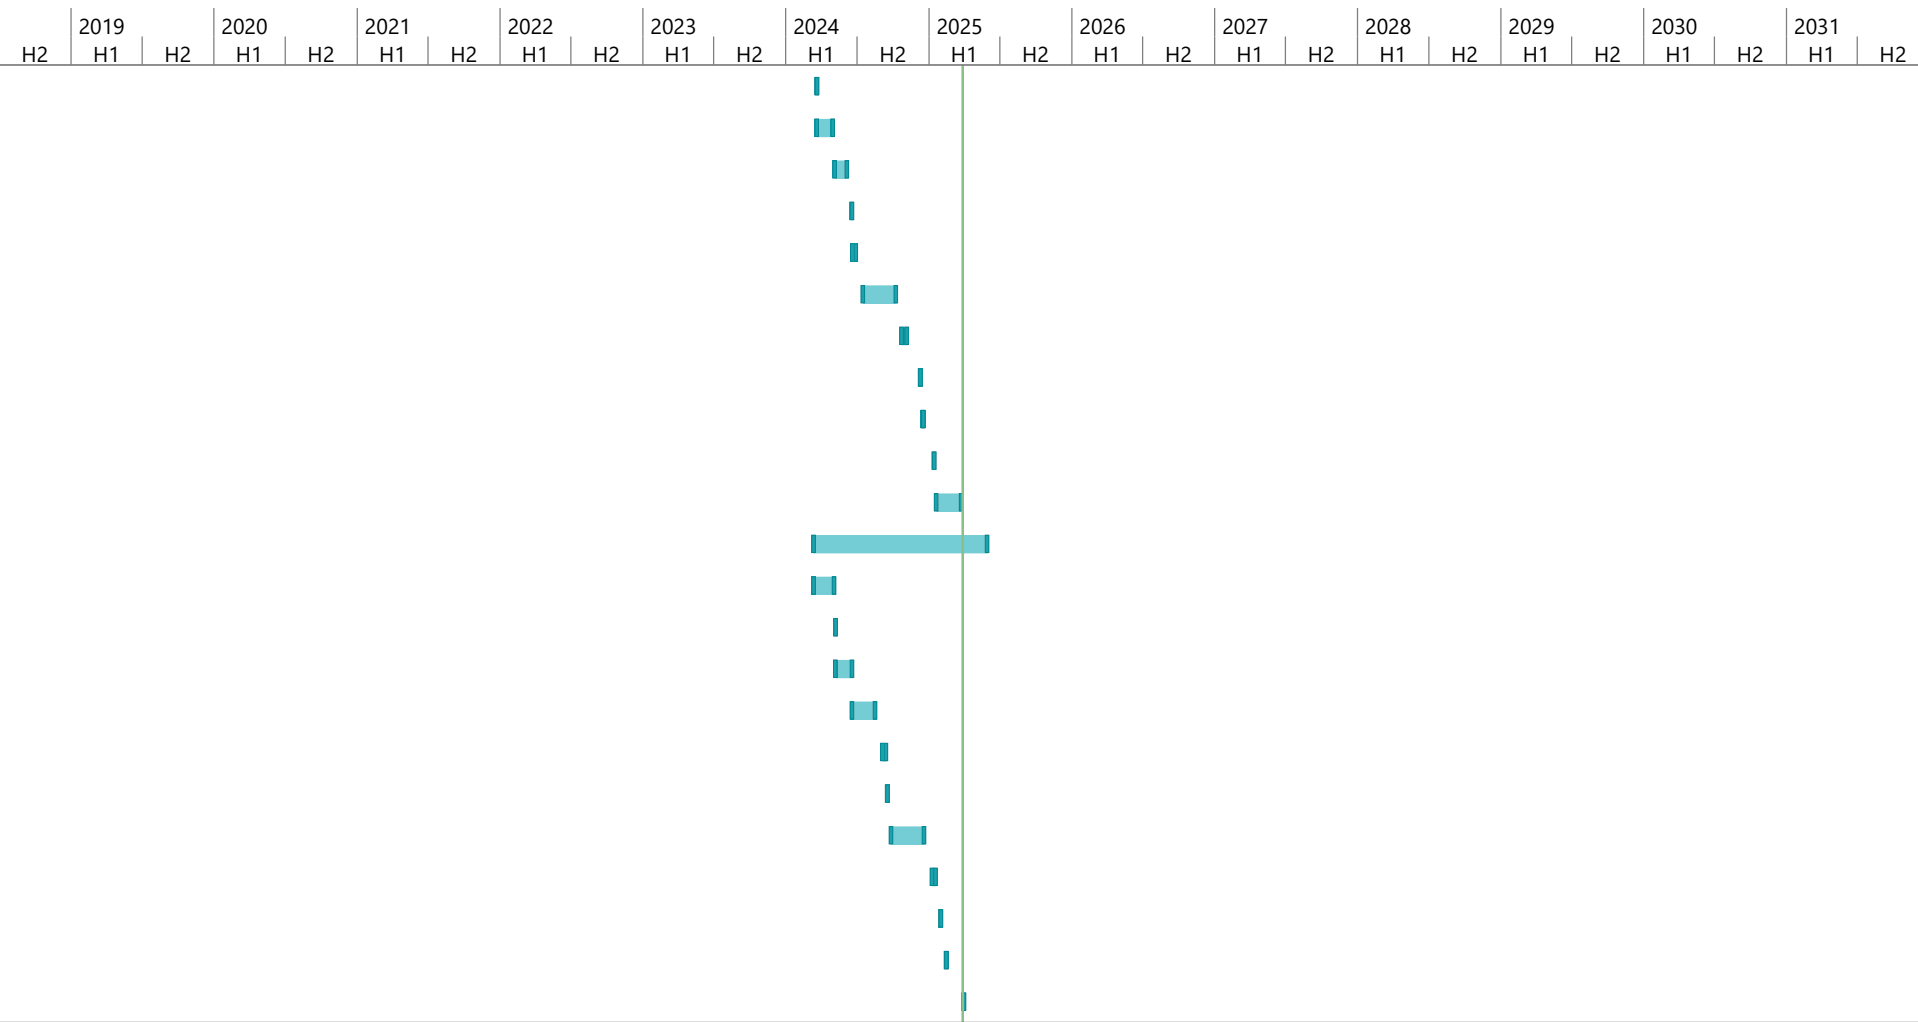
Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

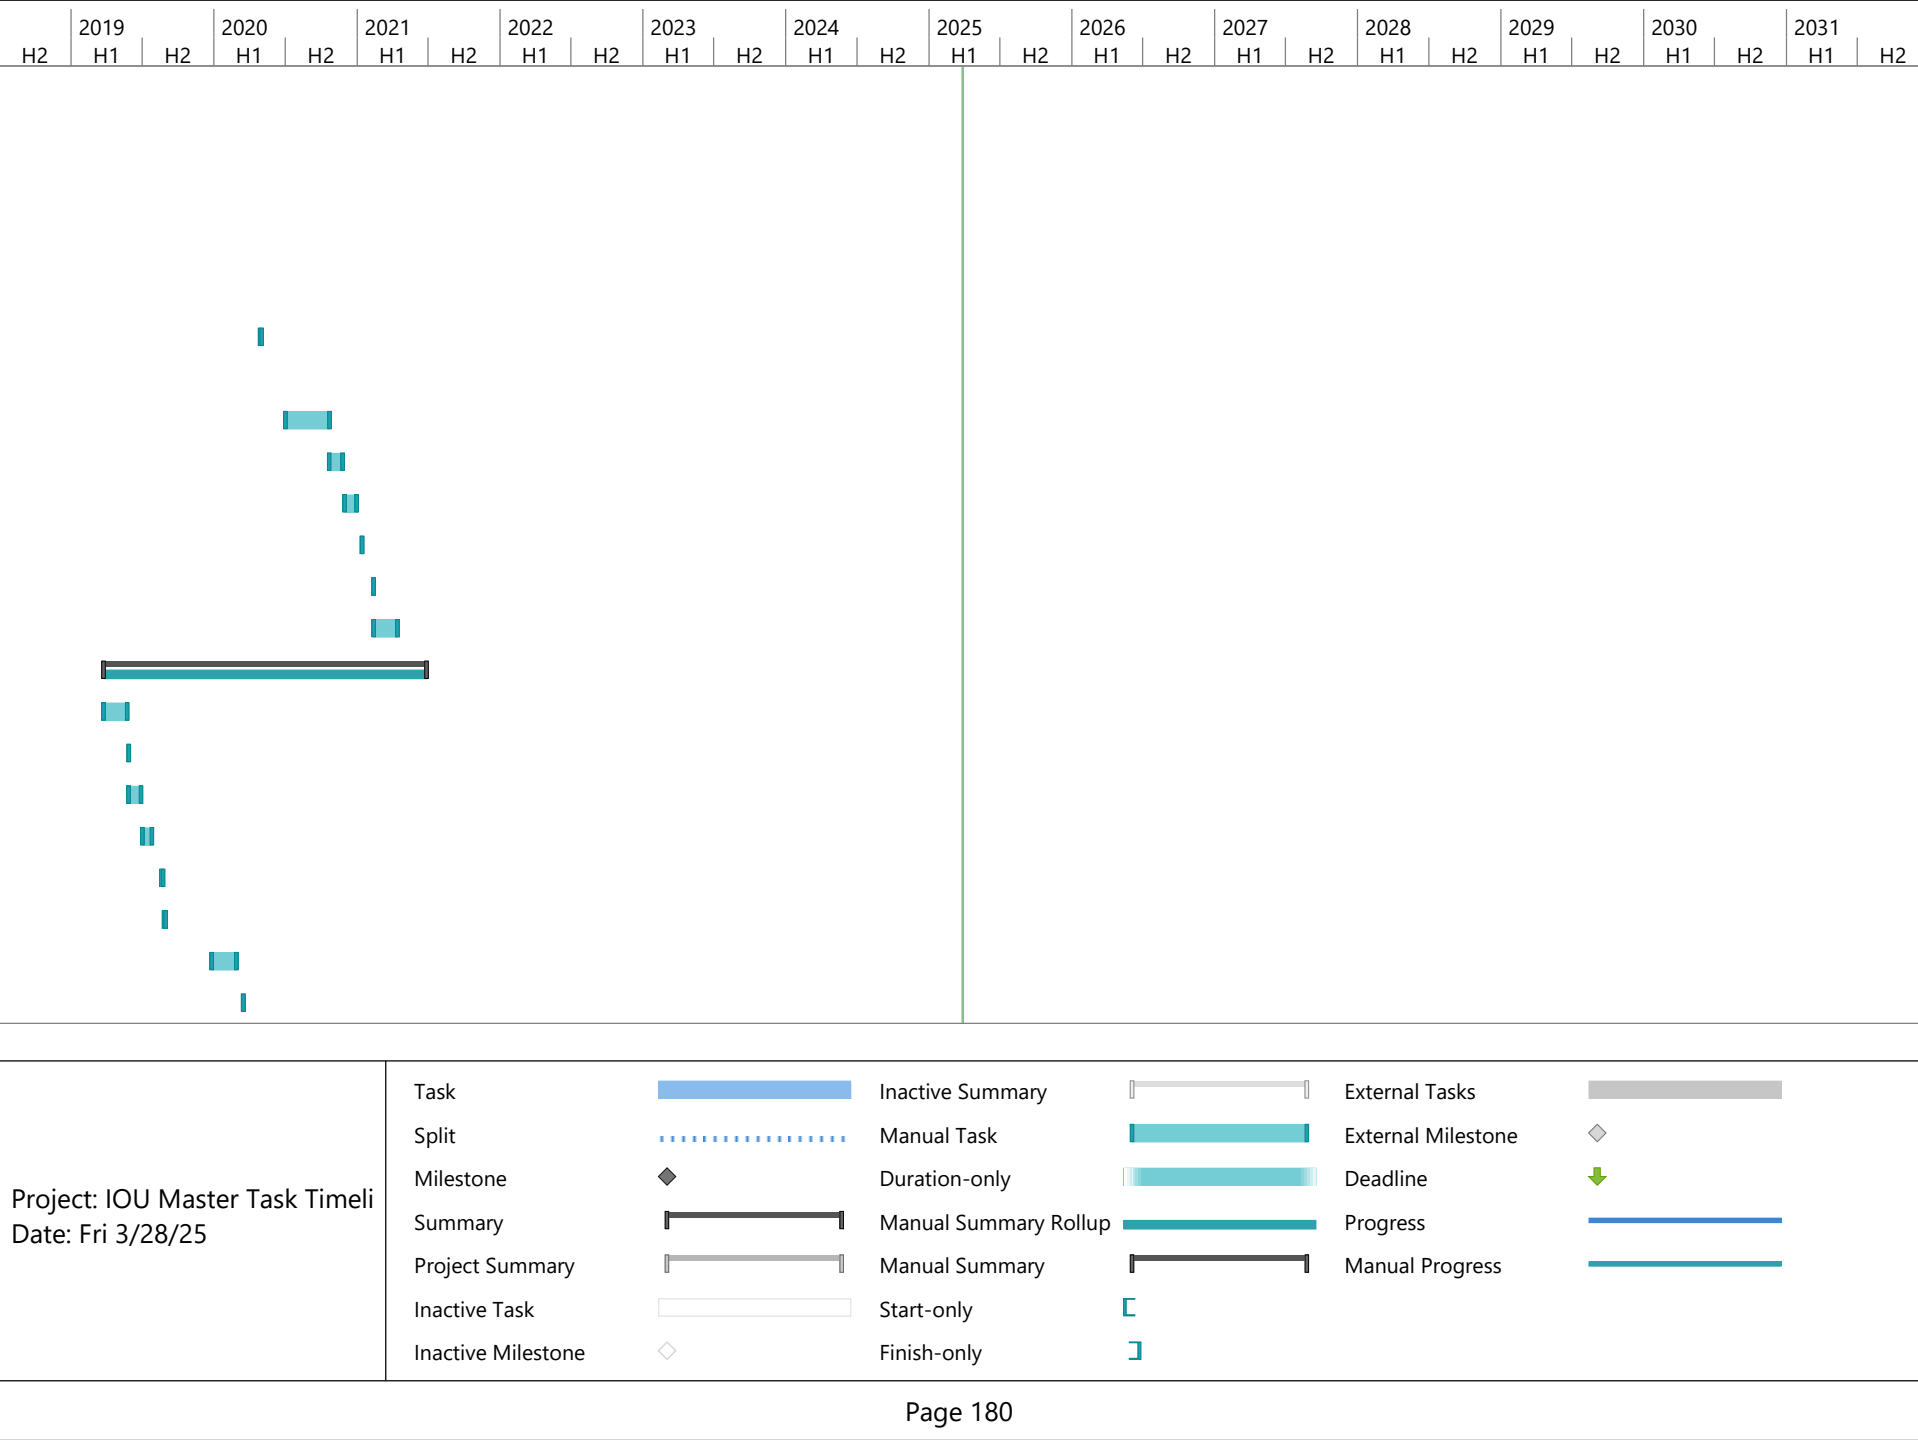


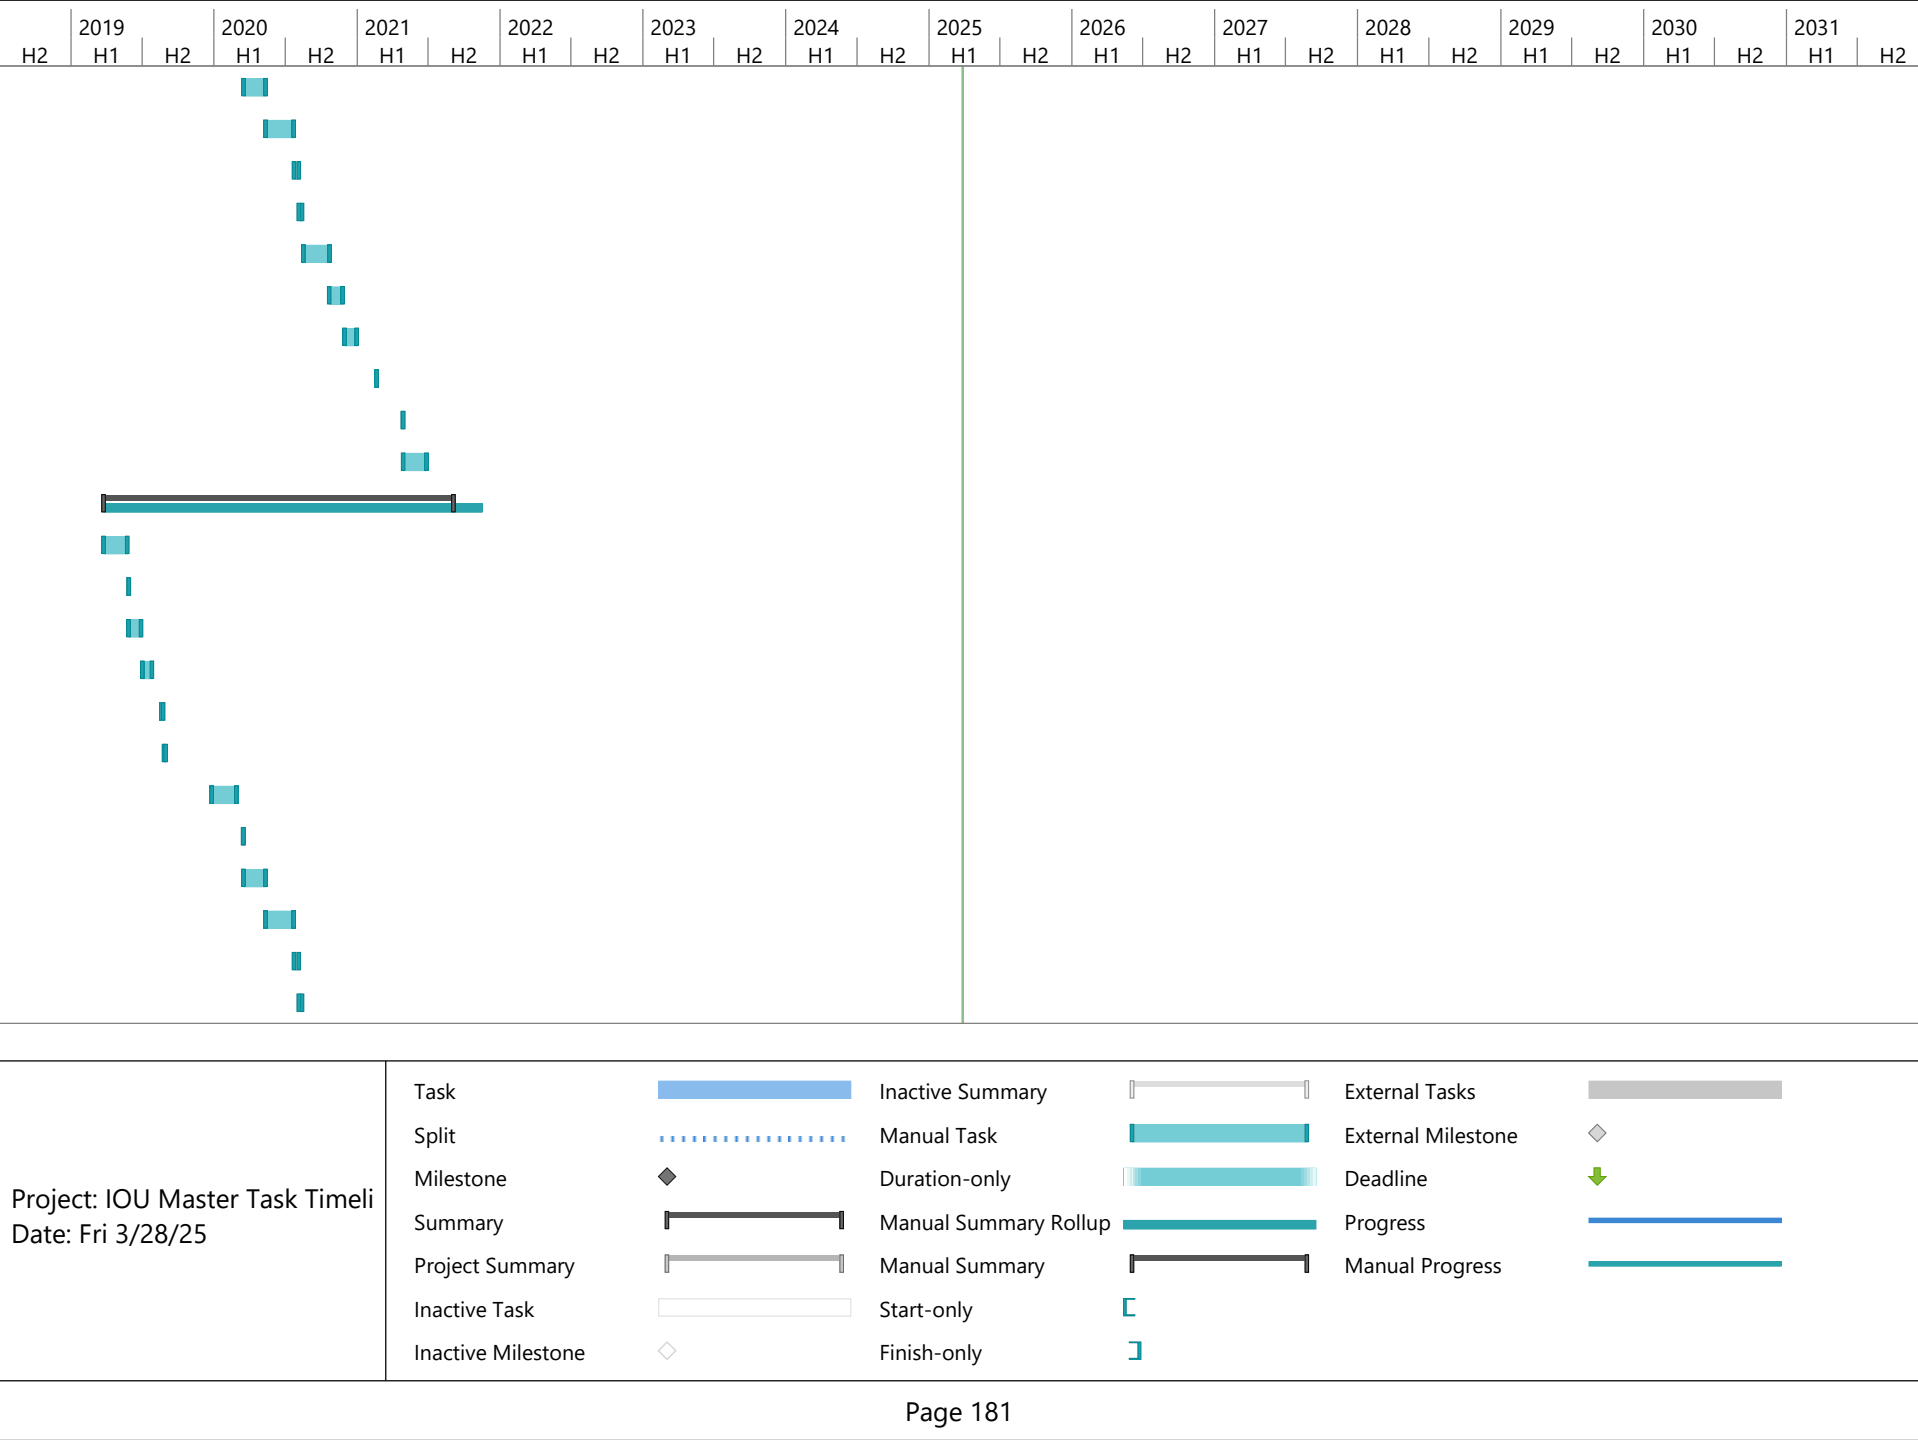
Project: IOU Master Task Timeli
Date: Fri 3/28/25

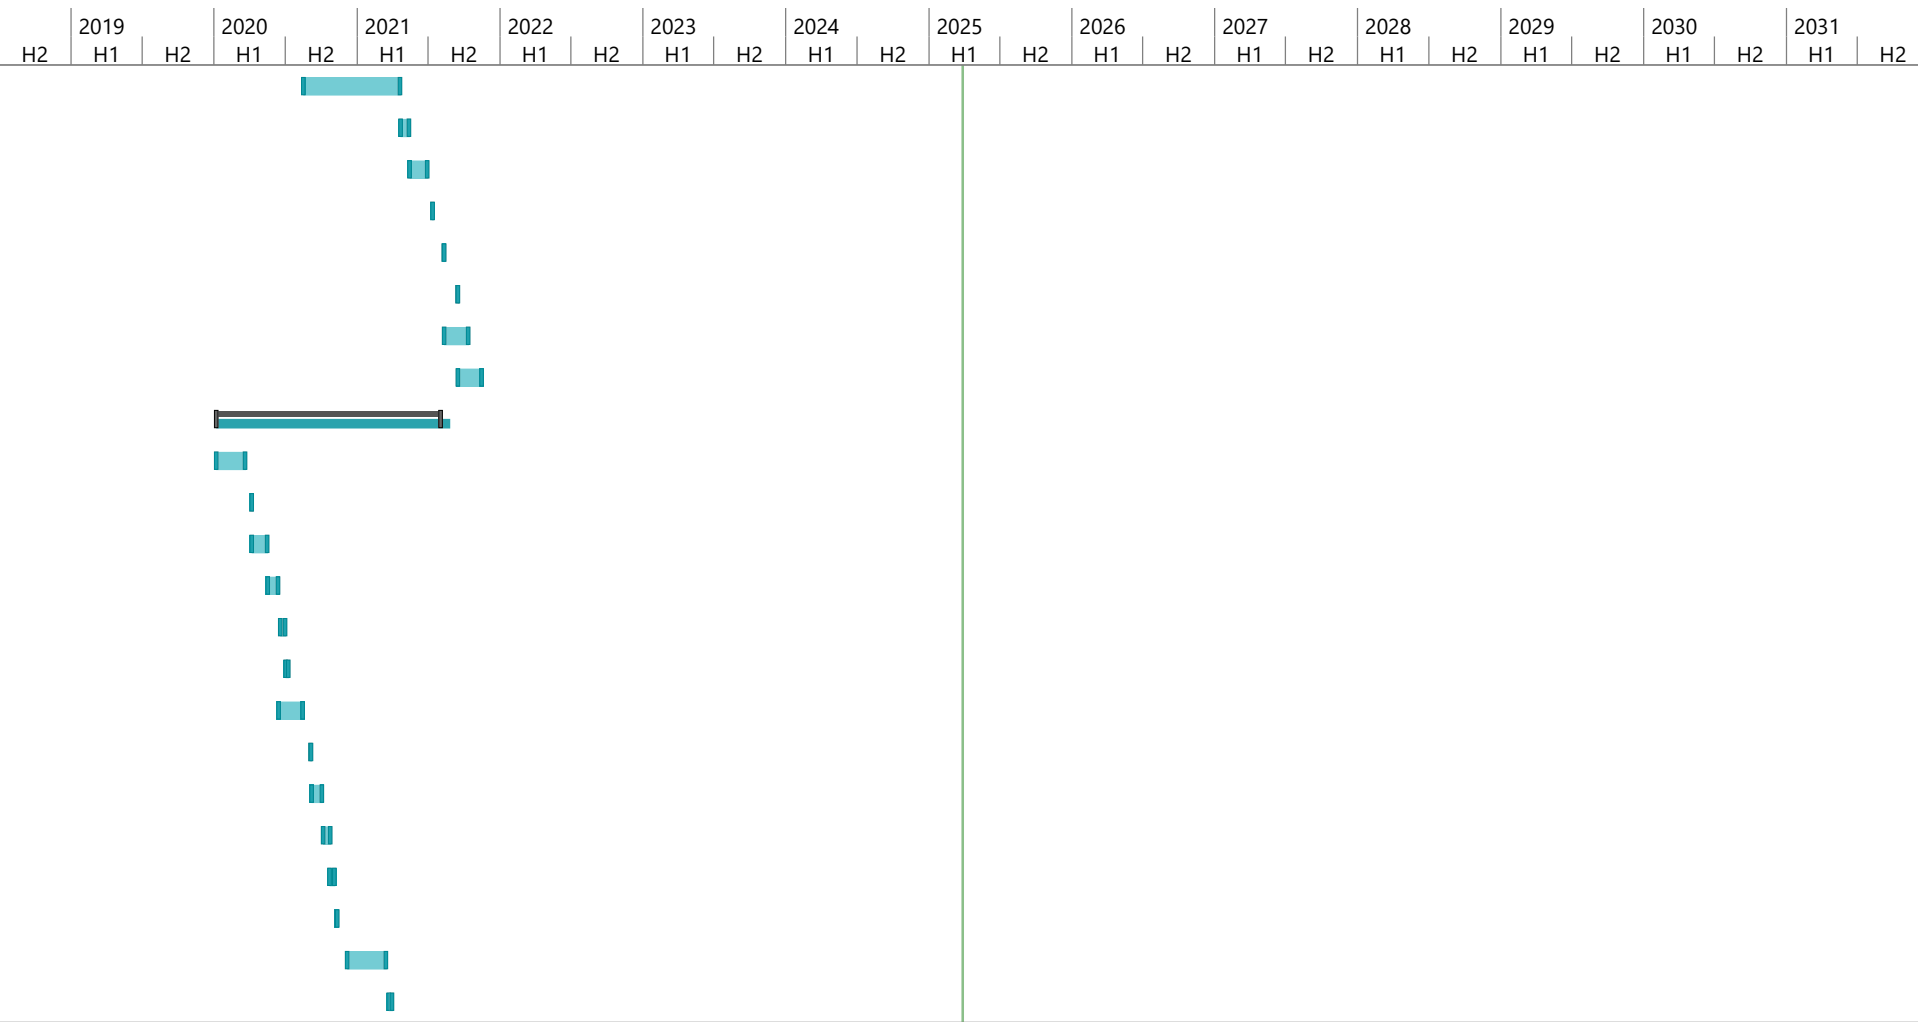
Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



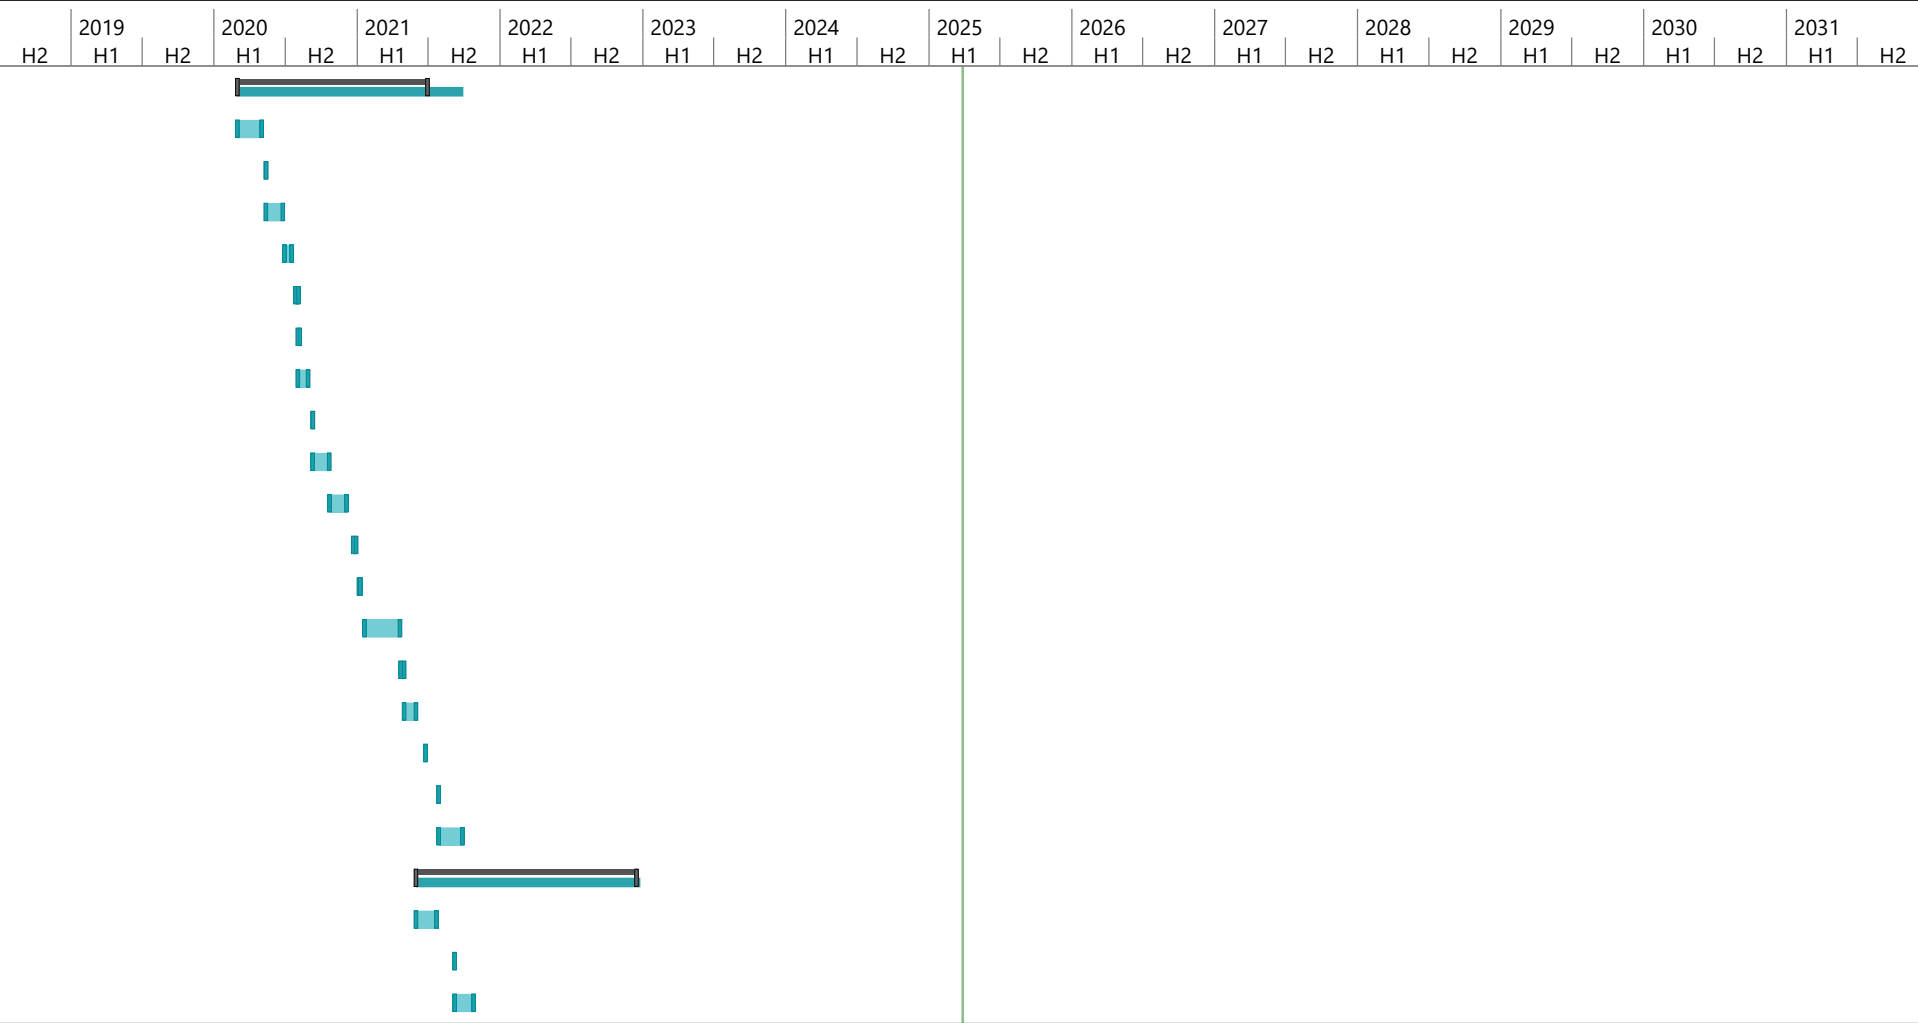
Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



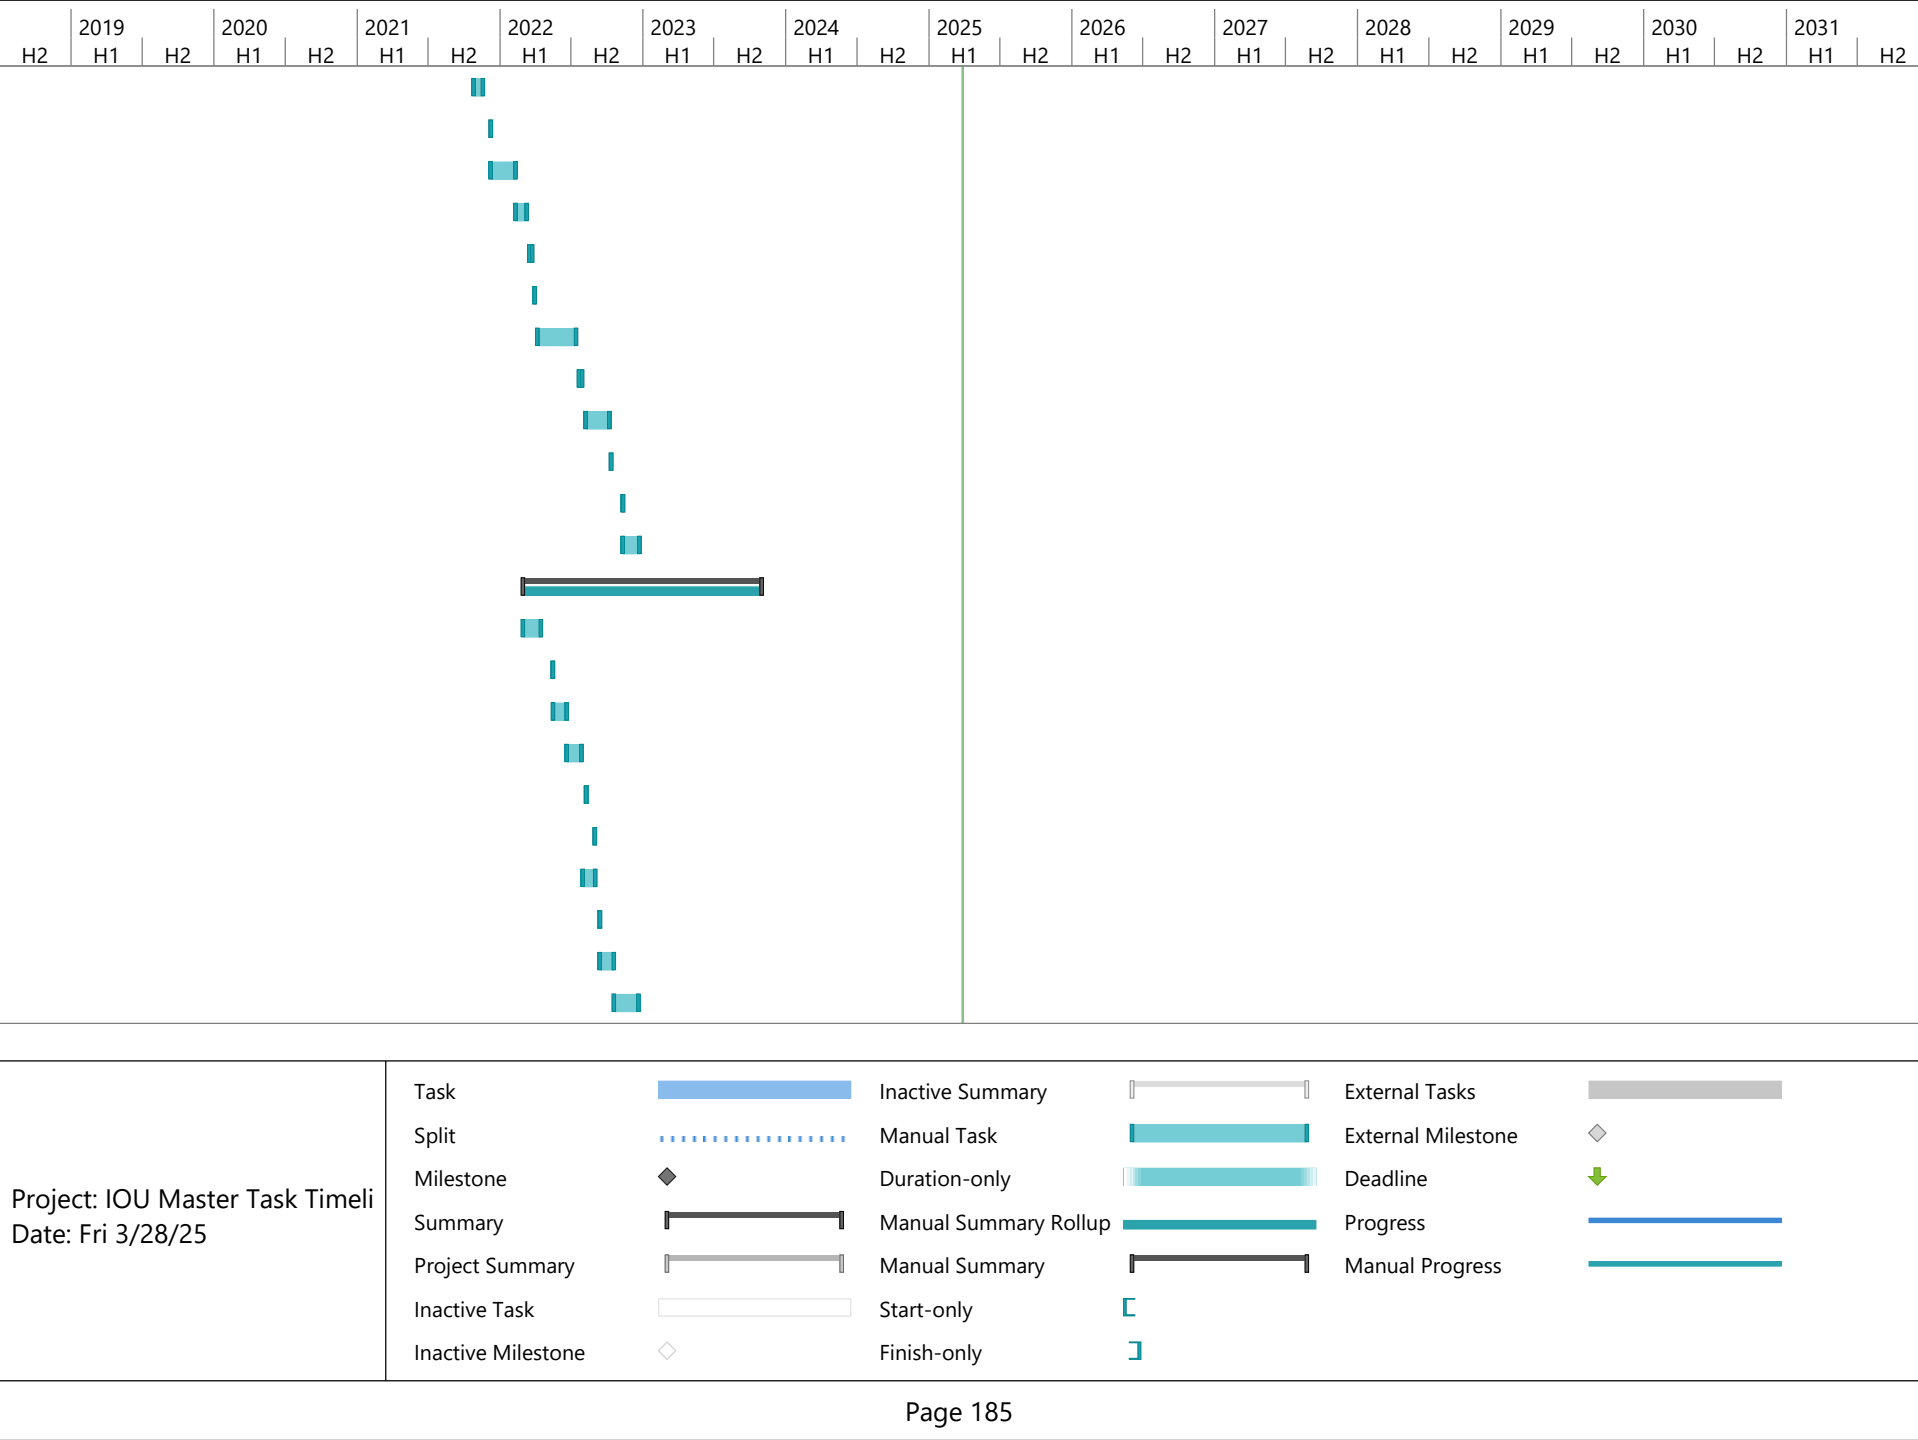


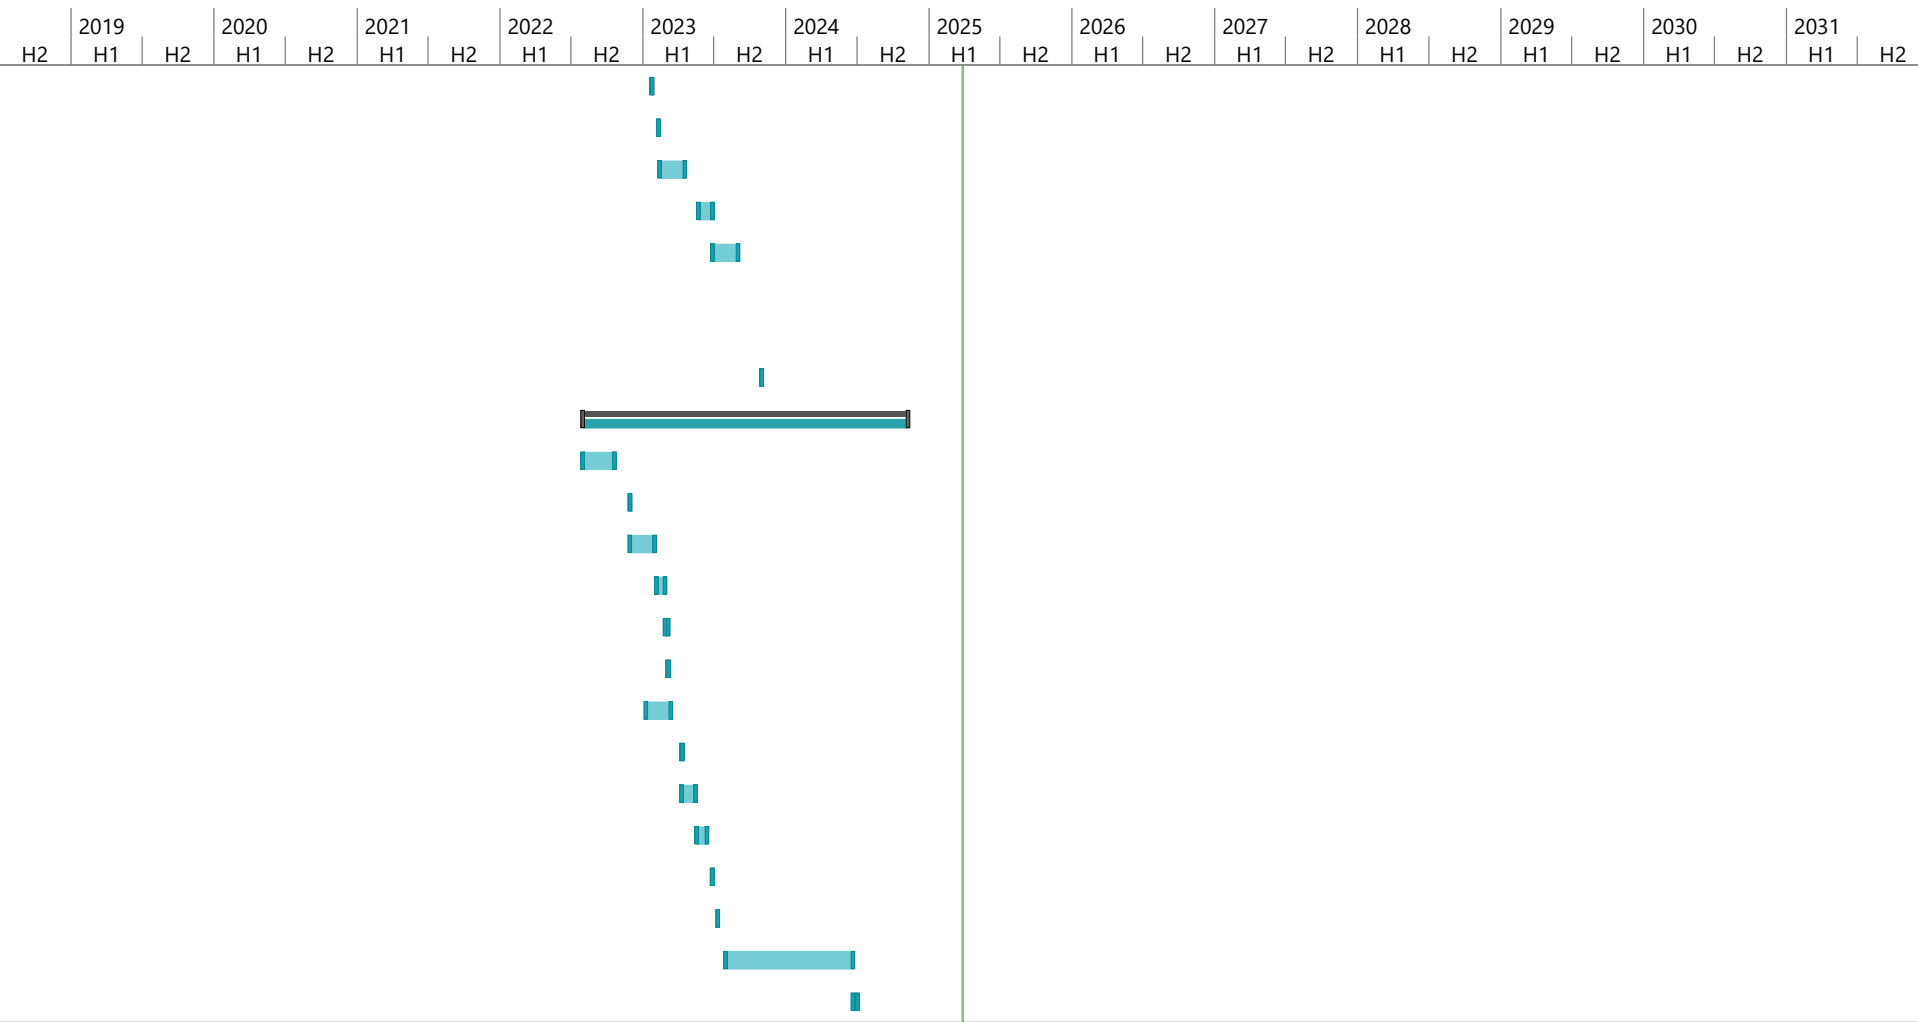


Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



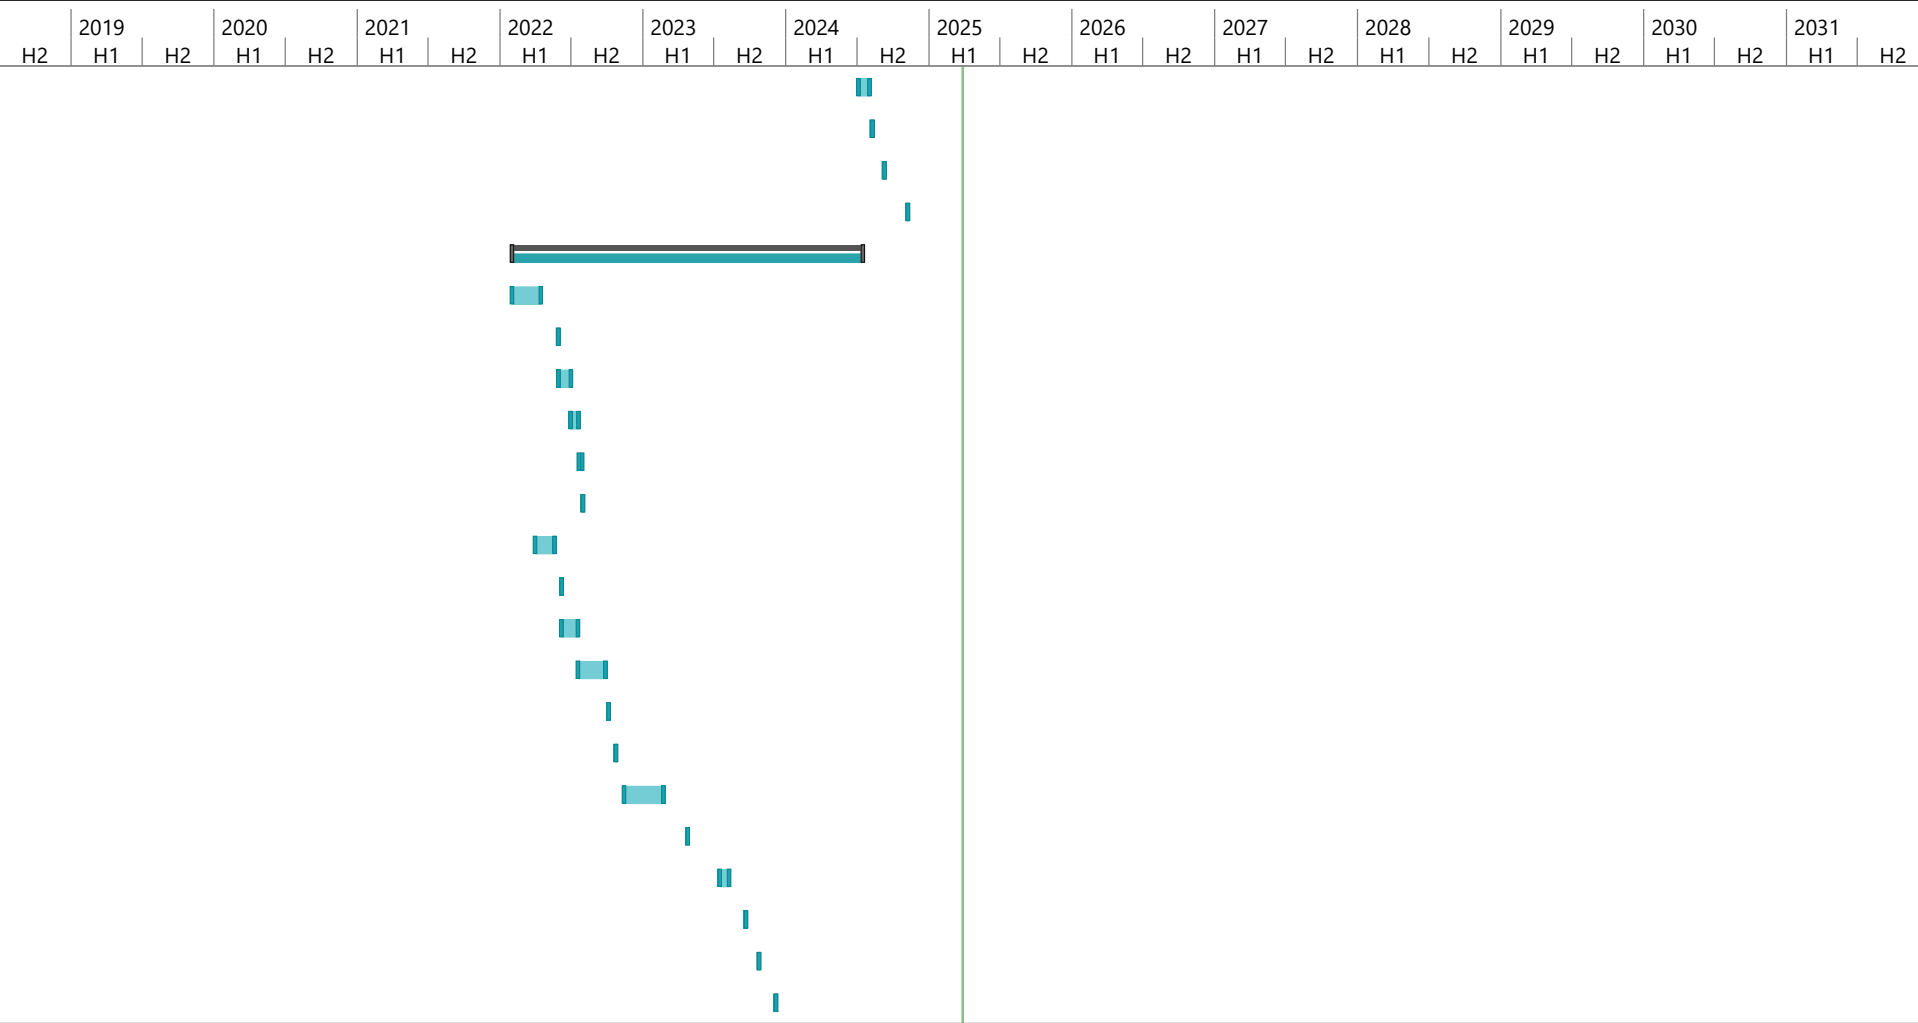
Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



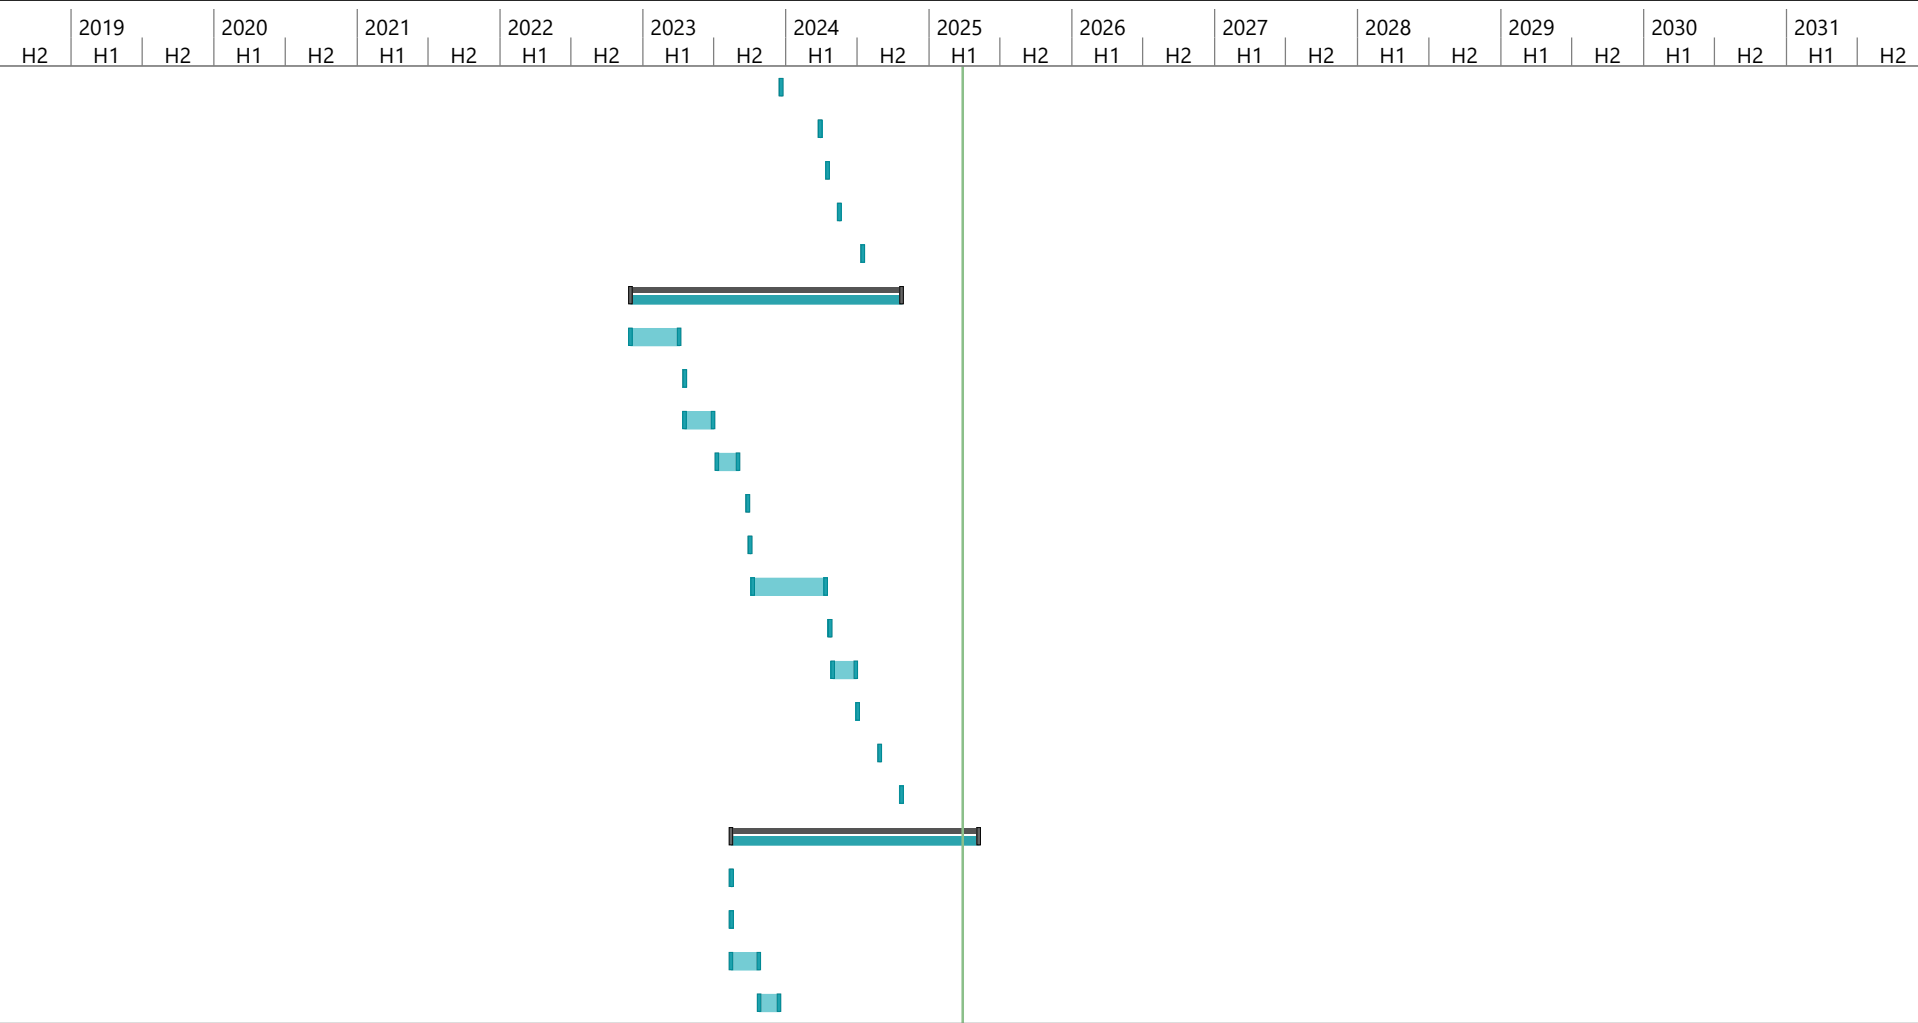


Project: IOU Master Task Timeli
Date: Fri 3/28/25

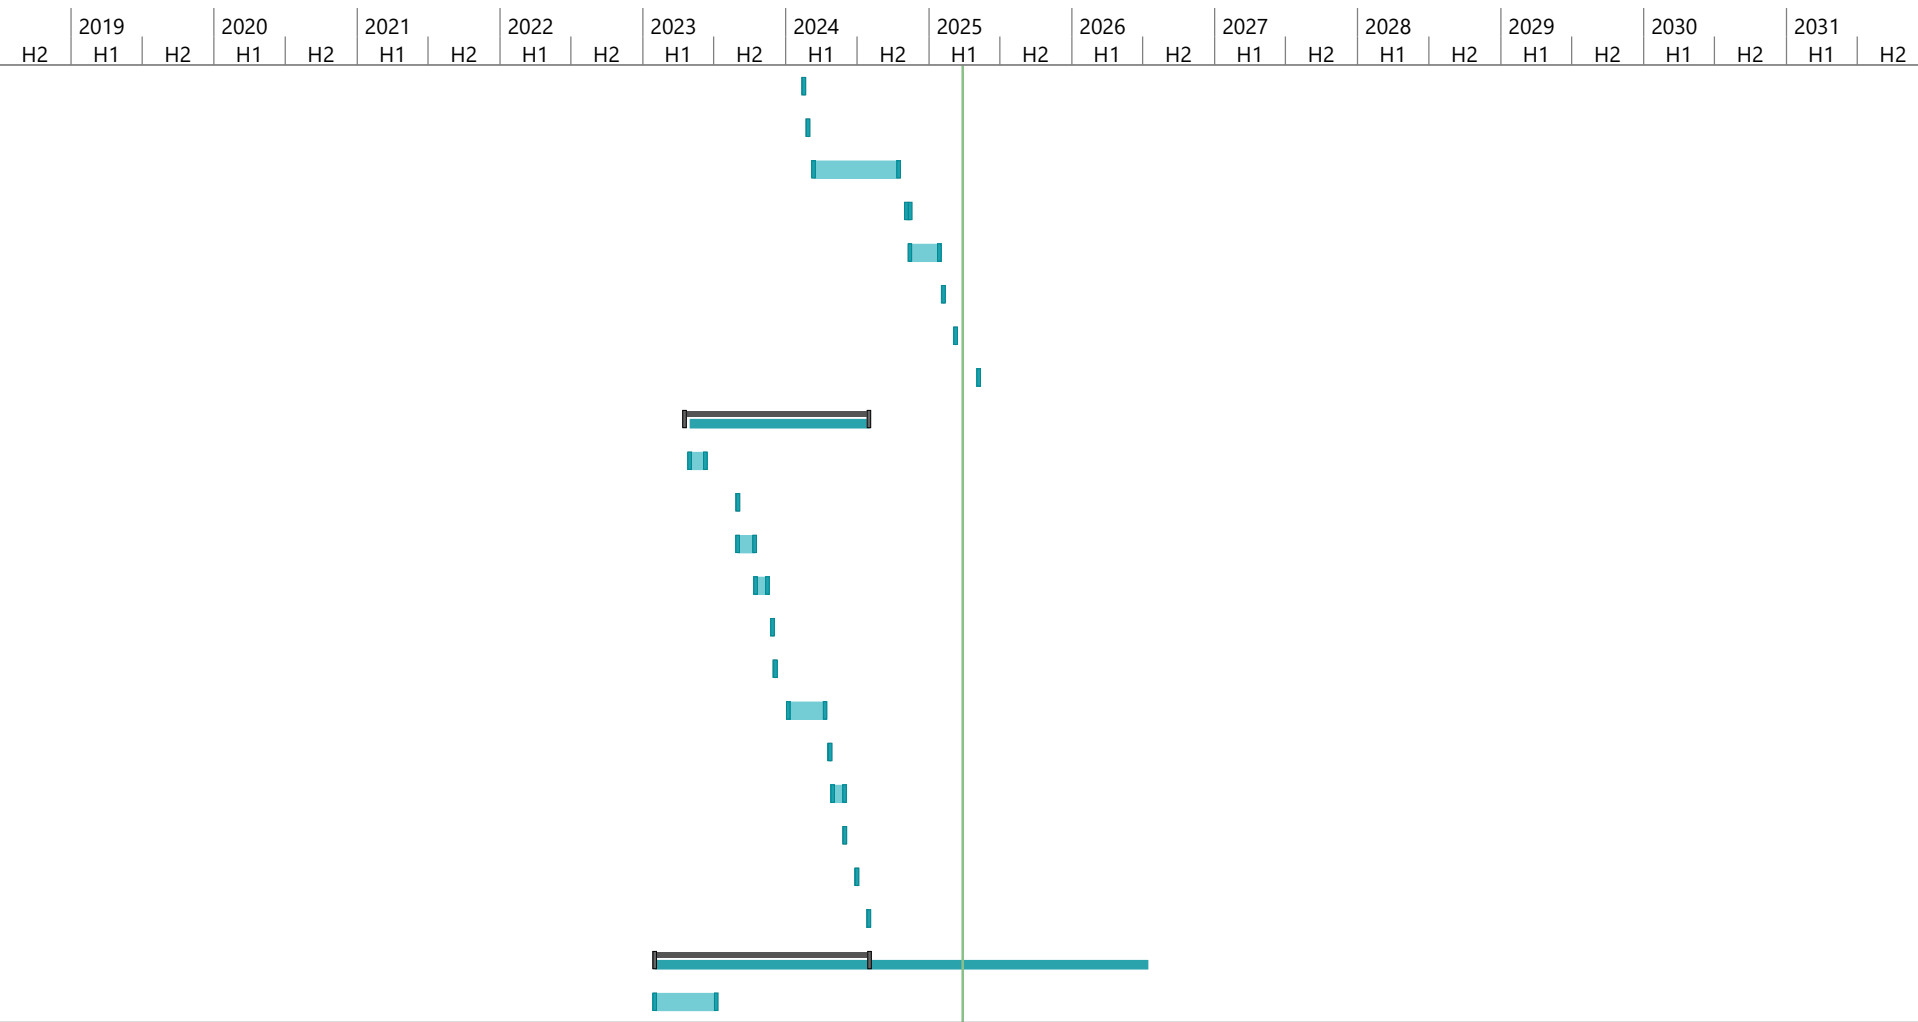
Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 3/28/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

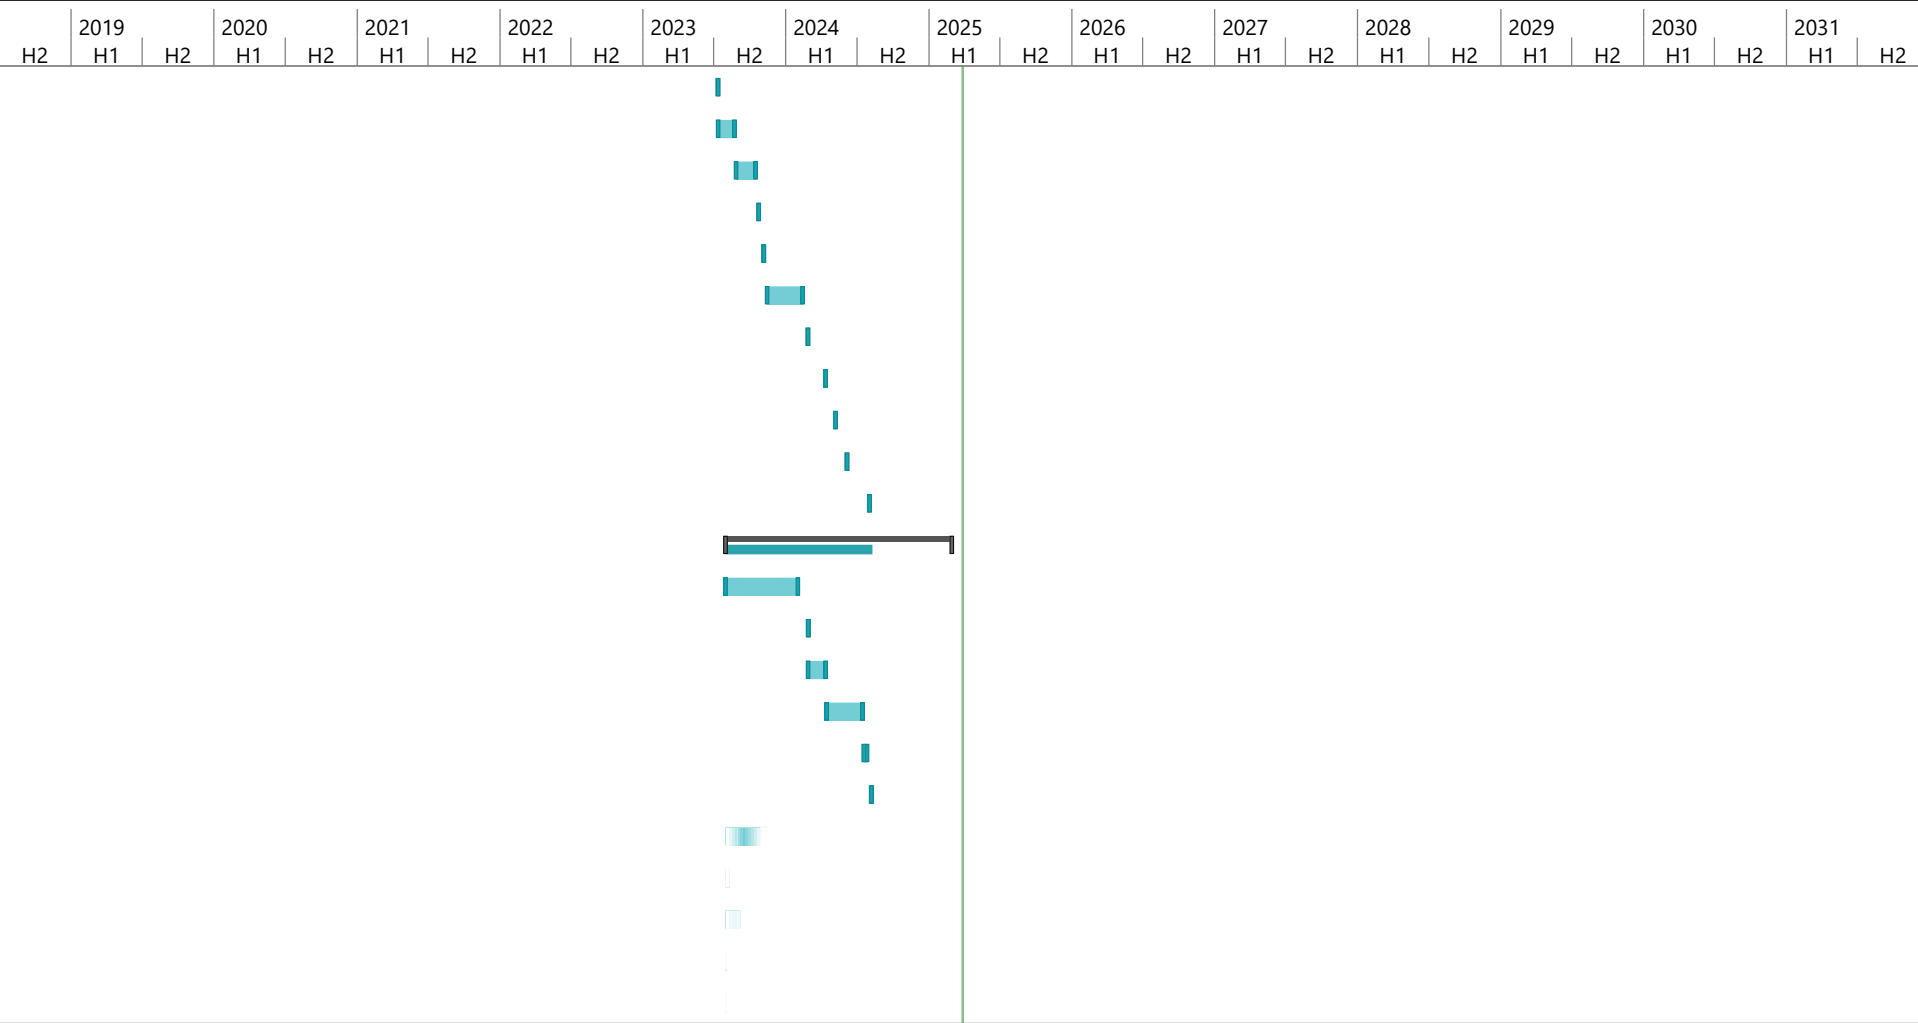
External Milestone

Deadline

Progress


Manual Progress

Page 189




Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


H2	2032 H1	H2	2033 H1	H2	2034 H1	H2	2035 H1	H2	2036 H1	H2	2037 H1	H2	2038 H1	H2	2039 H1	H2	2040 H1	H2	2041 H1	H2	2042 H1	H2	2043 H1	H2	2044 H1	H2

Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

H2	2032 H1	H2	2033 H1	H2	2034 H1	H2	2035 H1	H2	2036 H1	H2	2037 H1	H2	2038 H1	H2	2039 H1	H2	2040 H1	H2	2041 H1	H2	2042 H1	H2	2043 H1	H2	2044 H1	H2

Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

H2	2032 H1	H2	2033 H1	H2	2034 H1	H2	2035 H1	H2	2036 H1	H2	2037 H1	H2	2038 H1	H2	2039 H1	H2	2040 H1	H2	2041 H1	H2	2042 H1	H2	2043 H1	H2	2044 H1	H2

Project: IOU Master Task Timeli Date: Fri 3/28/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

