




















ID	Task Name	Duration	Start	Finish	2018 H1
1	UPDATED as of May 1, 2026				
2	SCE - Local RCI Solicitation	679 days	Tue 8/21/18	Fri 3/26/21	
3	SCE - RFA Preparation	40 days	Tue 8/21/18	Mon 10/15/18	
4	SCE - RFA Release	1 day	Fri 11/9/18	Fri 11/9/18	
5	SCE - RFA Abstract Creation Duration	30 days	Sat 11/10/18	Thu 12/20/18	
6	SCE - RFA Evaluation	82 days	Fri 12/21/18	Mon 4/15/19	
7	SCE - RFA Review with EE PRG	1 day	Tue 4/16/19	Tue 4/16/19	
8	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/21/19	Tue 5/21/19	
9	SCE - RFP Preparation	175 days	Wed 5/22/19	Tue 1/21/20	
10	SCE - RFP Release	1 day	Wed 1/22/20	Wed 1/22/20	
11	SCE - RFP Proposal Creation Duration	25 days	Thu 1/23/20	Wed 2/26/20	
12	SCE - RFP Evaluation	38 days	Thu 2/27/20	Mon 4/20/20	
13	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20	
14	SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20	
15	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20	
16	SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20	
17	SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20	
18	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20	
19	SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20	
20	SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21	
21	SCE - SW Lighting	518 days	Wed 4/3/19	Fri 3/26/21	
22	SCE - RFA Preparation	55 days	Wed 4/3/19	Tue 6/18/19	
23	SCE - RFA Release	1 day	Tue 7/2/19	Tue 7/2/19	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
24	SCE - RFA Abstract Creation Duration	20 days	Wed 7/3/19	Tue 7/30/19	
25	SCE - RFA Evaluation	34 days	Wed 7/31/19	Mon 9/16/19	
26	SCE - RFA Review with EE PRG	1 day	Tue 9/17/19	Tue 9/17/19	
27	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/24/19	Tue 9/24/19	
28	SCE - RFP Preparation	84 days	Wed 9/25/19	Mon 1/20/20	
29	SCE - RFP Release	1 day	Thu 2/6/20	Thu 2/6/20	
30	SCE - RFP Proposal Creation Duration	27 days	Fri 2/7/20	Mon 3/16/20	
31	SCE - RFP Evaluation	25 days	Tue 3/17/20	Mon 4/20/20	
32	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20	
33	SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20	
34	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20	
35	SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20	
36	SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20	
37	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20	
38	SCE - Advice Letter Approved	1 day	Wed 12/23/20	Wed 12/23/20	
39	SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21	
40	SCE - Local Public Sector Solicitation	573 days	Mon 8/31/20	Wed 11/9/22	
41	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20	
42	SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20	
43	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20	
44	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21	
45	SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21	
46	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
47	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21	
48	SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21	
49	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21	
50	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21	
51	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21	
52	SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21	
53	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21	
54	SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21	
55	SCE - Final Award and Contract Signed	1 day	Tue 12/14/21	Tue 12/14/21	
56	SCE - Submit Advice Letter	37 days	Wed 12/15/21	Thu 2/3/22	
57	SCE - Submit Advice Letter	48 days	Wed 12/15/21	Fri 2/18/22	
58	SCE - Advice Letter Approved	1 day	Thu 8/18/22	Thu 8/18/22	
59	SCE - Implementation Plan	60 days	Thu 8/18/22	Wed 11/9/22	
60	SCE - Local Agriculture Solicitation	512 days	Mon 8/31/20	Tue 8/16/22	
61	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20	
62	SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20	
63	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20	
64	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21	
65	SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21	
66	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21	
67	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21	
68	SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21	
69	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
70	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21	
71	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21	
72	SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21	
73	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21	
74	SCE - Final Award and Contract Signed	1 day	Mon 12/20/21	Mon 12/20/21	
75	SCE - Submit Advice Letter	33 days	Tue 12/21/21	Thu 2/3/22	
76	SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21	
77	SCE - Final Award and Contract Signed	1 day	Wed 12/15/21	Wed 12/15/21	
78	SCE - Submit Advice Letter	56 days	Thu 12/16/21	Thu 3/3/22	
79	SCE - Advice Letter Approved	1 day	Fri 4/22/22	Fri 4/22/22	
80	SCE - Implementation Plan	60 days	Sat 4/23/22	Thu 7/14/22	
81	SCE - SW Water/Wastewater Solicitation	522 days	Mon 11/16/20	Tue 11/15/22	
82	SCE - RFA Preparation	70 days	Mon 11/16/20	Fri 2/19/21	
83	SCE - RFA Release	1 day	Thu 3/4/21	Thu 3/4/21	
84	SCE - RFA Abstract Creation Duration	29 days	Thu 3/4/21	Tue 4/13/21	
85	SCE - RFA Evaluation	20 days	Wed 4/14/21	Tue 5/11/21	
86	SCE - RFA Review with EE PRG	1 day	Tue 5/18/21	Tue 5/18/21	
87	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/27/21	Thu 5/27/21	
88	SCE - RFP Preparation	34 days	Mon 4/19/21	Thu 6/3/21	
89	SCE - RFP Release	1 day	Thu 7/1/21	Thu 7/1/21	
90	SCE - RFP Proposal Creation Duration	25 days	Fri 7/2/21	Thu 8/5/21	
91	SCE - RFP Evaluation	41 days	Fri 8/6/21	Fri 10/1/21	
92	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/26/21	Tue 10/26/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
93	SCE - RFP Review with EE PRG	1 day	Tue 10/19/21	Tue 10/19/21	
94	SCE - Contract Negotiation and Development	94 days	Wed 10/27/21	Mon 3/7/22	
95	SCE - Contract Review with EE PRG	1 day	Tue 3/15/22	Tue 3/15/22	
96	SCE - Final Award and Contract Signed	1 day	Tue 4/19/22	Tue 4/19/22	
97	SCE - Submit Advice Letter	40 days	Wed 4/20/22	Tue 6/14/22	
98	SCE - Advice Letter Approved	26 days	Wed 6/15/22	Wed 7/20/22	
99	SCE - Implementation Plan	44 days	Thu 7/21/22	Tue 9/20/22	
100	SCE - SW ETP Solicitation	466 days	Fri 5/1/20	Fri 2/11/22	
101	SCE - RFA Preparation	57 days	Fri 5/1/20	Mon 7/20/20	
102	SCE - RFA Release	1 day	Tue 8/4/20	Tue 8/4/20	
103	SCE - RFA Abstract Creation Duration	24 days	Fri 8/7/20	Wed 9/9/20	
104	SCE - RFA Evaluation	16 days	Thu 9/10/20	Thu 10/1/20	
105	SCE - RFA Review with EE PRG	1 day	Tue 10/20/20	Tue 10/20/20	
106	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/27/20	Tue 10/27/20	
107	SCE - RFP Preparation	42 days	Tue 9/8/20	Wed 11/4/20	
108	SCE - RFP Release	1 day	Tue 1/5/21	Tue 1/5/21	
109	SCE - RFP Proposal Creation Duration	37 days	Tue 1/5/21	Wed 2/24/21	
110	SCE - RFP Evaluation	28 days	Wed 2/24/21	Fri 4/2/21	
111	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/27/21	Tue 4/27/21	
112	SCE - RFP Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21	
113	SCE - Contract Negotiation and Development	69 days	Wed 4/21/21	Mon 7/26/21	
114	SCE - Contract Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21	
115	SCE - Final Award and Contract Signed	1 day	Tue 9/14/21	Tue 9/14/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
116	SCE - Submit Advice Letter	18 days	Wed 9/15/21	Fri 10/8/21	
117	SCE - Advice Letter Approved	1 day	Tue 11/9/21	Tue 11/9/21	
118	SCE - Implementation Plan	60 days	Wed 11/10/21	Tue 2/1/22	
119	SCE - SW Higher-Education Solicitation	547 days?	Thu 10/1/20	Fri 11/4/22	
120	SCE - RFA Preparation	89 days	Thu 10/1/20	Tue 2/2/21	
121	SCE - RFA Release	1 day	Thu 2/4/21	Thu 2/4/21	
122	SCE - RFA Abstract Creation Duration	19 days	Fri 2/5/21	Wed 3/3/21	
123	SCE - RFA Evaluation	31 days	Thu 3/4/21	Thu 4/15/21	
124	SCE - RFA Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21	
125	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 4/29/21	Thu 4/29/21	
126	SCE - RFP Preparation	39 days	Mon 3/22/21	Thu 5/13/21	
127	SCE - RFP Release	1 day	Fri 5/28/21	Fri 5/28/21	
128	SCE - RFP Proposal Creation Duration	24 days	Fri 6/4/21	Wed 7/7/21	
129	SCE - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21	
130	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/30/21	Mon 8/30/21	
131	SCE - RFP Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21	
132	SCE - Contract Negotiation and Development	95 days	Fri 9/3/21	Thu 1/13/22	
133	SCE - Contract Review with EE PRG	1 day	Tue 1/18/22	Tue 1/18/22	
134	SCE - Final Award and Contract Signed	1 day	Sun 3/6/22	Sun 3/6/22	
135	SCE - Submit Advice Letter	1 day	Tue 4/19/22	Tue 4/19/22	
136	SCE - Advice Letter Approved	1 day	Mon 8/15/22	Mon 8/15/22	
137	SCE - Implementation Plan	60 days	Mon 8/15/22	Fri 11/4/22	
138	SCE - Local Equity Residential and SMB	384 days?	Tue 2/15/22	Fri 8/4/23	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
139	SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22	
140	SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22	
141	SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22	
142	SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22	
143	SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22	
144	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22	
145	SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22	
146	SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22	
147	SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22	
148	SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22	
149	SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22	
150	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22	
151	SCE - Contract Negotiation and Development	65 days	Wed 11/2/22	Tue 1/31/23	
152	SCE - Contract Review with EE PRG	1 day	Tue 2/21/23	Tue 2/21/23	
153	SCE - Final Award and Contract Signed	1 day	Thu 3/30/23	Thu 3/30/23	
154	SCE - Submit Advice Letter	22 days	Sun 4/3/22	Mon 5/2/22	
155	SCE - Advice Letter Approved	28 days	Tue 5/2/23	Thu 6/8/23	
156	SCE - Implementation Plan	45 days	Thu 6/8/23	Wed 8/9/23	
157					
158	SCE - Local Equity SMB	431 days?	Tue 2/15/22	Tue 10/10/23	
159	SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22	
160	SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22	
161	SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
162	SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22	
163	SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22	
164	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22	
165	SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22	
166	SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22	
167	SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22	
168	SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22	
169	SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22	
170	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22	
171	SCE - Contract Negotiation and Development	108 days	Wed 11/2/22	Fri 3/31/23	
172	SCE - Contract Review with EE PRG	1 day	Tue 4/18/23	Tue 4/18/23	
173	SCE - Final Award and Contract Signed	1 day	Wed 5/31/23	Wed 5/31/23	
174	SCE - Submit Advice Letter	22 days	Mon 6/6/22	Tue 7/5/22	
175	SCE - Advice Letter Approved	24 days	Thu 7/6/23	Tue 8/8/23	
176	SCE - Implementation Plan	45 days	Wed 8/9/23	Tue 10/10/23	
177	SCE - Local Strategic Energy Management Solicitation	372 days?	Thu 12/1/22	Fri 5/3/24	
178	SCE - RFP Preparation	85 days	Thu 12/1/22	Wed 3/29/23	
179	SCE - RFP Release	1 day	Fri 4/7/23	Fri 4/7/23	
180	SCE - RFP Proposal Creation Duration	35 days	Fri 4/7/23	Thu 5/25/23	
181	SCE - RFP Evaluation	22 days	Thu 6/1/23	Fri 6/30/23	
182	SCE - RFP Review with EE PRG	1 day	Tue 7/18/23	Tue 7/18/23	
183	SCE - Contract Negotiation and Development	86 days	Tue 8/1/23	Tue 11/28/23	
184	SCE - Contract Review with EE PRG	1 day	Tue 12/19/23	Tue 12/19/23	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
185	SCE - Final Award and Contract Signed	6 days	Fri 1/19/24	Fri 1/26/24	
186	SCE - Submit Advice Letter	34 days	Wed 1/31/24	Mon 3/18/24	
187	SCE - Advice Letter Approved	40 days	Tue 3/19/24	Mon 5/13/24	
188	SCE - Local Large Commercial Solicitation	488 days?	Mon 6/26/23	Wed 5/7/25	
189	SCE - RFP Preparation	35 days	Mon 6/26/23	Fri 8/11/23	
190	SCE - RFP Release	1 day	Thu 8/17/23	Thu 8/17/23	
191	SCE - RFP Proposal Creation Duration	41 days	Thu 8/17/23	Thu 10/12/23	
192	SCE - RFP Paused	1 day	Fri 10/13/23	Fri 10/13/23	
193	SCE - Residential Multifamily	326 days?	Fri 9/1/23	Fri 11/29/24	
194	SCE - RFP Preparation	47 days	Fri 9/1/23	Mon 11/6/23	
195	SCE - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23	
196	SCE - RFP Proposal Creation Duration	48 days	Mon 11/6/23	Wed 1/10/24	
197	SCE - RFP Evaluation	25 days	Thu 1/11/24	Wed 2/14/24	
198	SCE - RFP Review with EE PRG	1 day	Tue 2/20/24	Tue 2/20/24	
199	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 2/28/24	Wed 2/28/24	
200	SCE - Contract Negotiation and Development	70 days	Mon 3/4/24	Fri 6/7/24	
201	SCE - Contract Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24	
202	SCE - Final Award and Contract Signed	15 days	Mon 7/29/24	Fri 8/16/24	
203	SCE - Submit Advice Letter	30 days	Mon 8/19/24	Fri 9/27/24	
204	SCE - Advice Letter Approved	1 day	Mon 10/28/24	Mon 10/28/24	
205	SCE - Local Large Industrial	499 days	Fri 11/3/23	Wed 10/1/25	
206	SCE - RFP Preparation	17 days	Fri 11/3/23	Mon 11/27/23	
207	SCE - RFP Release	1 day	Mon 12/11/23	Mon 12/11/23	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
208	SCE - RFP Proposal Creation Duration	49 days	Mon 12/11/23	Thu 2/15/24	
209	SCE - RFP Evaluation	35 days	Fri 2/16/24	Thu 4/4/24	
210	SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24	
211	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/23/24	Tue 4/23/24	
212	SCE - Contract Negotiation and Development	208 days	Wed 4/24/24	Fri 2/7/25	
213	SCE - Contract Review with EE PRG	1 day	Tue 4/29/25	Tue 4/29/25	
214	SCE - Final Award and Contract Signed	42 days	Thu 5/1/25	Fri 6/27/25	
215	SCE - Submit Advice Letter	35 days	Mon 6/30/25	Fri 8/15/25	
216	SCE - Advice Letter Approved	33 days	Mon 8/18/25	Wed 10/1/25	
217	SCE - MAP - All Sectors	299 days?	Mon 11/20/23	Thu 1/9/25	
218	SCE - RFP Preparation	20 days	Mon 11/20/23	Fri 12/15/23	
219	SCE - RFP Release	1 day	Mon 1/8/24	Mon 1/8/24	
220	SCE - RFP Proposal Creation Duration	40 days	Mon 1/8/24	Fri 3/1/24	
221	SCE - RFP Evaluation	30 days	Mon 3/4/24	Fri 4/12/24	
222	SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24	
223	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/24/24	Wed 4/24/24	
224	SCE - Contract Negotiation and Development	108 days	Wed 5/1/24	Fri 9/27/24	
225	SCE - Contract Review with EE PRG	1 day	Tue 10/15/24	Tue 10/15/24	
226	SCE - Final Award and Contract Signed	12 days	Tue 10/29/24	Wed 11/13/24	
227	SCE - Submit Advice Letter	43 days	Wed 11/13/24	Fri 1/10/25	
228	SCE - Advice Letter Approved	22 days	Mon 1/13/25	Tue 2/11/25	
229	SCE - Residential	360 days?	Mon 11/20/23	Fri 4/4/25	
230	SCE - RFP Preparation	20 days	Tue 1/16/24	Mon 2/12/24	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
231	SCE - RFP Release	1 day	Thu 3/28/24	Thu 3/28/24	
232	SCE - RFP Proposal Creation Duration	41 days	Thu 3/28/24	Thu 5/23/24	
233	SCE - RFP Evaluation	35 days	Fri 5/24/24	Thu 7/11/24	
234	SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24	
235	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/5/24	Mon 8/5/24	
236	SCE - Contract Negotiation and Development	80 days	Mon 8/19/24	Fri 12/6/24	
237	SCE - Contract Review with EE PRG	1 day	Tue 12/17/24	Tue 12/17/24	
238	SCE - Final Award and Contract Signed	11 days	Mon 1/13/25	Mon 1/27/25	
239	SCE - Submit Advice Letter	19 days	Mon 2/3/25	Thu 2/27/25	
240	SCE - Advice Letter Approved	1 day	Tue 4/1/25	Tue 4/1/25	
241					
242	SCE - Local Comprehensive Commercial Solicitation	431 days?	Mon 11/13/23	Mon 7/7/25	
243	SCE - RFP Preparation	73 days	Mon 11/13/23	Wed 2/21/24	
244	SCE - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24	
245	SCE - RFP Proposal Creation Duration	43 days	Thu 2/29/24	Mon 4/29/24	
246	SCE - RFP Evaluation	54 days	Tue 4/30/24	Fri 7/12/24	
247	SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24	
248	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Phase 1	1 day	Mon 7/29/24	Mon 7/29/24	
249	SCE - Contract Negotiation and Development - Phase 1	81 days	Tue 7/30/24	Tue 11/19/24	
250	SCE - Contract Review with EE PRG - Phase 1	1 day	Tue 12/17/24	Tue 12/17/24	
251	SCE - Final Award and Contract Signed - Phase 1	1 day	Tue 1/28/25	Tue 1/28/25	
252	SCE - Submit Advice Letter - Phase 1	23 days	Tue 1/28/25	Thu 2/27/25	
253	SCE - Advice Letter Approved - Phase 1	1 day	Tue 4/1/25	Tue 4/1/25	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
254	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Phase 2	1 day	Mon 9/30/24	Mon 9/30/24	
255	SCE - Contract Negotiation and Development - Phase 2	80 days	Mon 12/2/24	Fri 3/21/25	
256	SCE - Contract Review with EE PRG - Phase 2	1 day	Tue 4/29/25	Tue 4/29/25	
257	SCE - Final Award and Contract Signed - Phase 2	1 day	Tue 5/20/25	Tue 5/20/25	
258	SCE - Submit Advice Letter - Phase 2	0 days	N/A	N/A	
259	SCE - Advice Letter Approved - Phase 2	0 days	N/A	N/A	
260					
261	SCG - Local Single Family Solicitation	660 days	Sun 7/1/18	Thu 1/7/21	
262	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18	
263	SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18	
264	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19	
265	SCG - RFA Evaluation	39 days	Mon 1/7/19	Thu 2/28/19	
266	SCG - RFA Review with EE PRG	1 day	Tue 3/5/19	Tue 3/5/19	
267	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19	
268	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19	
269	SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19	
270	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19	
271	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19	
272	SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19	
273	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20	
274	SCG - Contract Negotiation and Development	69 days	Mon 1/27/20	Thu 4/30/20	
275	SCG - Contract Review with EE PRG	14 days	Tue 5/5/20	Fri 5/22/20	
276	SCG - Final Award and Contract Signed	8 days	Mon 5/25/20	Wed 6/3/20	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
277	SCG - Submit Advice Letter	96 days	Mon 6/1/20	Mon 10/12/20	
278	SCG - Advice Letter Approved	1 day	Thu 11/12/20	Thu 11/12/20	
279	SCG - Implementation Plan	41 days	Fri 11/13/20	Fri 1/8/21	
280	SCG - Local Multi-family Solicitation	735 days	Sun 7/1/18	Thu 4/22/21	
281	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18	
282	SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18	
283	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19	
284	SCG - RFA Evaluation	59 days	Mon 1/7/19	Thu 3/28/19	
285	SCG - RFA Review with EE PRG	1 day	Tue 4/2/19	Tue 4/2/19	
286	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19	
287	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19	
288	SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19	
289	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19	
290	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19	
291	SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19	
292	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20	
293	SCG - Contract Negotiation and Development	155 days	Mon 1/27/20	Fri 8/28/20	
294	SCG - Contract Review with EE PRG	99 days	Tue 5/5/20	Fri 9/18/20	
295	SCG - Final Award and Contract Signed	8 days	Mon 9/21/20	Wed 9/30/20	
296	SCG - Submit Advice Letter	37 days	Thu 10/1/20	Fri 11/20/20	
297	SCG - Advice Letter Approved	1 day	Sun 5/2/21	Sun 5/2/21	
298	SCG - Implementation Plan	51 days	Mon 5/3/21	Mon 7/12/21	
299	SCG - Local Small/Medium Commercial Solicitation	641 days	Tue 9/4/18	Tue 2/16/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
300	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19	
301	SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19	
302	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19	
303	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19	
304	SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19	
305	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19	
306	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19	
307	SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19	
308	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19	
309	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19	
310	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19	
311	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20	
312	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20	
313	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20	
314	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20	
315	SCG - Submit Advice Letter	59 days	Tue 9/1/20	Fri 11/20/20	
316	SCG - Advice Letter Approved	1 day	Fri 12/18/20	Fri 12/18/20	
317	SCG - Implementation Plan	43 days	Sat 12/19/20	Tue 2/16/21	
318	SCG - Local Small/Medium Public Solicitation	631 days	Tue 9/4/18	Tue 2/2/21	
319	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19	
320	SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19	
321	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19	
322	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
323	SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19	
324	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19	
325	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19	
326	SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19	
327	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19	
328	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19	
329	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19	
330	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20	
331	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20	
332	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20	
333	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20	
334	SCG - Submit Advice Letter	49 days	Tue 9/1/20	Fri 11/6/20	
335	SCG - Advice Letter Approved	1 day	Fri 12/4/20	Fri 12/4/20	
336	SCG - Implementation Plan	43 days	Sat 12/5/20	Tue 2/2/21	
337	SCG - Statewide POS Food Service Solicitation	605 days	Mon 1/21/19	Fri 5/14/21	
338	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19	
339	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19	
340	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19	
341	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19	
342	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19	
343	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20	
344	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19	
345	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
346	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20	
347	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20	
348	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20	
349	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20	
350	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20	
351	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20	
352	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20	
353	SCG - Submit Advice Letter	32 days	Mon 11/2/20	Tue 12/15/20	
354	SCG - Advice Letter Approved	1 day	Thu 1/14/21	Thu 1/14/21	
355	SCG - Implementation Plan	42 days	Fri 1/15/21	Mon 3/15/21	
356	SCG - Statewide Midstream Water Heating Solicitation	597 days	Mon 1/21/19	Tue 5/4/21	
357	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19	
358	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19	
359	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19	
360	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19	
361	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19	
362	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20	
363	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19	
364	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20	
365	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20	
366	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20	
367	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20	
368	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
369	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20	
370	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20	
371	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20	
372	SCG - Submit Advice Letter	25 days	Mon 11/2/20	Fri 12/4/20	
373	SCG - Advice Letter Approved	1 day	Thu 3/18/21	Thu 3/18/21	
374	SCG - Implementation Plan	22 days	Fri 3/19/21	Mon 4/19/21	
375	SCG - Statewide Gas Emerging Technology Solicitation	738 days	Wed 1/2/19	Fri 10/29/21	
376	SCG - RFA Preparation	283 days	Wed 1/2/19	Fri 1/31/20	
377	SCG - RFA Release	1 day	Wed 2/12/20	Wed 2/12/20	
378	SCG - RFA Abstract Creation Duration	30 days	Thu 2/13/20	Wed 3/25/20	
379	SCG - RFA Evaluation	26 days	Thu 3/26/20	Thu 4/30/20	
380	SCG - RFA Review with EE PRG	1 day	Tue 5/5/20	Tue 5/5/20	
381	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 5/15/20	Fri 5/15/20	
382	SCG - RFP Preparation	66 days	Fri 5/1/20	Fri 7/31/20	
383	SCG - RFP Release	1 day	Fri 8/21/20	Fri 8/21/20	
384	SCG - RFP Proposal Creation Duration	30 days	Mon 8/24/20	Fri 10/2/20	
385	SCG - RFP Evaluation	38 days	Mon 10/5/20	Wed 11/25/20	
386	SCG - RFP Review with EE PRG	1 day	Tue 12/1/20	Tue 12/1/20	
387	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 12/7/20	Mon 12/7/20	
388	SCG - Contract Negotiation and Development	85 days	Mon 1/4/21	Fri 4/30/21	
389	SCG - Contract Review with EE PRG	9 days	Tue 5/4/21	Fri 5/14/21	
390	SCG - Final Award and Contract Signed	29 days	Mon 5/17/21	Thu 6/24/21	
391	SCG - Submit Advice Letter	23 days	Sun 6/27/21	Tue 7/27/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
392	SCG - Advice Letter Approved	1 day	Tue 8/24/21	Tue 8/24/21	
393	SCG - Implementation Plan	44 days	Wed 8/25/21	Sat 10/23/21	
394	SCG - Local Manufactured Housing Solicitation	341 days	Fri 11/1/19	Fri 2/19/21	
395	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20	
396	SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20	
397	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20	
398	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20	
399	SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20	
400	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20	
401	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20	
402	SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20	
403	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20	
404	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20	
405	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20	
406	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20	
407	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20	
408	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20	
409	SCG - Final Award and Contract Signed	9 days	Thu 12/10/20	Tue 12/22/20	
410	SCG - Submit Advice Letter	0 days	N/A	N/A	
411	SCG - Advice Letter Approved	0 days	N/A	N/A	
412	SCG - Implementation Plan	44 days	Tue 12/22/20	Fri 2/19/21	
413	SCG - Local Large Commercial Solicitation	434 days	Fri 11/1/19	Wed 6/30/21	
414	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
415	SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20	
416	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20	
417	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20	
418	SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20	
419	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20	
420	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20	
421	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20	
422	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20	
423	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20	
424	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20	
425	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20	
426	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20	
427	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20	
428	SCG - Final Award and Contract Signed	10 days	Thu 12/10/20	Wed 12/23/20	
429	SCG - Submit Advice Letter	64 days	Fri 1/1/21	Wed 3/31/21	
430	SCG - Advice Letter Approved	1 day	Fri 6/4/21	Fri 6/4/21	
431	SCG - Implementation Plan	43 days	Sat 6/5/21	Tue 8/3/21	
432	SCG - Local Agricultural Solicitation	434 days	Fri 11/1/19	Wed 6/30/21	
433	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20	
434	SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20	
435	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20	
436	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20	
437	SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
438	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20	
439	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20	
440	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20	
441	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20	
442	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20	
443	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20	
444	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20	
445	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20	
446	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20	
447	SCG - Final Award and Contract Signed	2 days	Fri 12/11/20	Mon 12/14/20	
448	SCG - Submit Advice Letter	41 days	Fri 1/1/21	Fri 2/26/21	
449	SCG - Advice Letter Approved	1 day	Wed 4/7/21	Wed 4/7/21	
450	SCG - Implementation Plan	43 days	Thu 4/8/21	Mon 6/7/21	
451	SCG - Local Behavioral Solicitation - Residential	413 days?	Fri 5/1/20	Tue 11/30/21	
452	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20	
453	SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20	
454	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20	
455	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20	
456	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20	
457	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20	
458	SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20	
459	SCG - RFP Release	1 day	Fri 1/15/21	Fri 1/15/21	
460	SCG - RFP Proposal Creation Duration	26 days	Mon 1/18/21	Mon 2/22/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
461	SCG - RFP Evaluation	29 days	Tue 2/23/21	Fri 4/2/21	
462	SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21	
463	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/13/21	Tue 4/13/21	
464	SCG - Contract Negotiation and Development	95 days	Mon 4/26/21	Fri 9/3/21	
465	SCG - Contract Review with EE PRG	9 days	Tue 9/7/21	Fri 9/17/21	
466	SCG - Final Award and Contract Signed	30 days	Mon 9/20/21	Fri 10/29/21	
467	SCG - Submit Advice Letter	21 days	Mon 11/1/21	Mon 11/29/21	
468	SCG - Advice Letter Approved	1 day	Wed 12/22/21	Wed 12/22/21	
469	SCG - Implementation Plan	43 days	Thu 12/23/21	Sun 2/20/22	
470	SCG - Local Behavioral Solicitation - Commercial	413 days?	Fri 5/1/20	Tue 11/30/21	
471	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20	
472	SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20	
473	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20	
474	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20	
475	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20	
476	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20	
477	SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20	
478	SCG - RFP Release	1 day	Fri 1/22/21	Fri 1/22/21	
479	SCG - RFP Proposal Creation Duration	26 days	Mon 1/25/21	Mon 3/1/21	
480	SCG - RFP Evaluation	24 days	Tue 3/2/21	Fri 4/2/21	
481	SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21	
482	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 11/12/21	Fri 11/12/21	
483	SCG - Contract Negotiation and Development	132 days	Mon 11/29/21	Tue 5/31/22	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
484	SCG - Contract Review with EE PRG	8 days	Sun 6/5/22	Tue 6/14/22	
485	SCG - Final Award and Contract Signed	109 days	Fri 7/1/22	Wed 11/30/22	
486	SCG - Submit Advice Letter	23 days	N/A	N/A	
487	SCG - Advice Letter Approved	1 day	N/A	N/A	
488	SCG - Implementation Plan	43 days	Thu 12/1/22	Sun 1/29/23	
489	SCG - Local Industrial Solicitation	434 days?	Tue 12/1/20	Fri 7/29/22	
490	SCG - RFA Preparation	63 days?	Tue 12/1/20	Thu 2/25/21	
491	SCG - RFA Release	1 day?	Fri 3/19/21	Fri 3/19/21	
492	SCG - RFA Abstract Creation Duration	25 days?	Mon 3/22/21	Fri 4/23/21	
493	SCG - RFA Evaluation	25 days?	Mon 4/26/21	Fri 5/28/21	
494	SCG - RFA Review with EE PRG	1 day?	Tue 6/1/21	Tue 6/1/21	
495	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 6/8/21	Tue 6/8/21	
496	SCG - RFP Preparation	67 days?	Thu 4/1/21	Fri 7/2/21	
497	SCG - RFP Release	1 day?	Fri 7/16/21	Fri 7/16/21	
498	SCG - RFP Proposal Creation Duration	30 days?	Mon 7/19/21	Fri 8/27/21	
499	SCG - RFP Evaluation	25 days?	Mon 8/30/21	Fri 10/1/21	
500	SCG - RFP Review with EE PRG	1 day?	Tue 10/5/21	Tue 10/5/21	
501	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 12/14/21	Tue 12/14/21	
502	SCG - Contract Negotiation and Development	127 days?	Thu 2/3/22	Fri 7/29/22	
503	SCG - Contract Review with EE PRG	9 days?	Tue 8/2/22	Fri 8/12/22	
504	SCG - Final Award and Contract Signed	21 days?	Fri 7/29/22	Fri 8/26/22	
505	SCG - Submit Advice Letter	1 day?	Sun 10/30/22	Sun 10/30/22	
506	SCG - Advice Letter Approved	1 day?	Mon 1/30/23	Mon 1/30/23	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
507	SCG - Implementation Plan	45 days?	Tue 1/31/23	Sat 4/1/23	
508	SCG - Large Public Sector Solicitation (re-Bid)	412 days	Mon 1/4/21	Tue 8/2/22	
509	SCG - RFA Preparation	65 days	Mon 1/4/21	Fri 4/2/21	
510	SCG - RFA Release	1 day	Fri 7/16/21	Fri 7/16/21	
511	SCG - RFA Abstract Creation Duration	20 days	Mon 7/19/21	Fri 8/13/21	
512	SCG - RFA Evaluation	15 days	Mon 8/16/21	Fri 9/3/21	
513	SCG - RFA Review with EE PRG	1 day	Tue 9/7/21	Tue 9/7/21	
514	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/14/21	Tue 9/14/21	
515	SCG - RFP Preparation	35 days	Mon 9/13/21	Fri 10/29/21	
516	SCG - RFP Release	1 day	Mon 11/8/21	Mon 11/8/21	
517	SCG - RFP Proposal Creation Duration	29 days	Tue 11/9/21	Fri 12/17/21	
518	SCG - RFP Evaluation	30 days	Mon 12/20/21	Fri 1/28/22	
519	SCG - RFP Review with EE PRG	1 day	Tue 2/1/22	Tue 2/1/22	
520	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/8/22	Tue 3/8/22	
521	SCG - Contract Negotiation and Development	79 days	Mon 3/14/22	Thu 6/30/22	
522	SCG - Contract Review with EE PRG	9 days	Tue 7/5/22	Fri 7/15/22	
523	SCG - Final Award and Contract Signed	63 days	Mon 7/18/22	Wed 10/12/22	
524	SCG - Submit Advice Letter	23 days	N/A	N/A	
525	SCG - Advice Letter Approved	1 day	N/A	N/A	
526	SCG - Implementation Plan	44 days	Wed 10/12/22	Sat 12/10/22	
527	SCG - Outreach Solicitation	434 days	Mon 2/1/21	Thu 9/29/22	
528	SCG - RFA Preparation	65 days	Mon 2/1/21	Fri 4/30/21	
529	SCG - RFA Release	1 day	Fri 5/21/21	Fri 5/21/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
530	SCG - RFA Abstract Creation Duration	25 days	Mon 5/24/21	Fri 6/25/21	
531	SCG - RFA Evaluation	25 days	Mon 6/28/21	Fri 7/30/21	
532	SCG - RFA Review with EE PRG	1 day	Tue 8/3/21	Tue 8/3/21	
533	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/10/21	Tue 8/10/21	
534	SCG - RFP Preparation	69 days	Tue 6/1/21	Fri 9/3/21	
535	SCG - RFP Release	1 day	Fri 9/17/21	Fri 9/17/21	
536	SCG - RFP Proposal Creation Duration	30 days	Mon 9/20/21	Fri 10/29/21	
537	SCG - RFP Evaluation	25 days	Mon 11/1/21	Fri 12/3/21	
538	SCG - RFP Review with EE PRG	1 day	Tue 12/7/21	Tue 12/7/21	
539	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 12/14/21	Tue 12/14/21	
540	SCG - Contract Negotiation and Development	54 days	Mon 1/17/22	Thu 3/31/22	
541	SCG - Contract Review with EE PRG	9 days	Tue 4/5/22	Fri 4/15/22	
542	SCG - Final Award and Contract Signed	10 days	Mon 4/18/22	Fri 4/29/22	
543	SCG - Submit Advice Letter	21 days	N/A	N/A	
544	SCG - Advice Letter Approved	1 day	N/A	N/A	
545	SCG - Implementation Plan	43 days	Sat 4/30/22	Tue 6/28/22	
546	SCG - Marketplace Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22	
547	SCG - RFA Preparation	64 days	Sat 5/1/21	Wed 7/28/21	
548	SCG - RFA Release	1 day	Fri 8/20/21	Fri 8/20/21	
549	SCG - RFA Abstract Creation Duration	25 days	Mon 8/23/21	Fri 9/24/21	
550	SCG - RFA Evaluation	25 days	Mon 9/27/21	Fri 10/29/21	
551	SCG - RFA Review with EE PRG	1 day	Tue 11/2/21	Tue 11/2/21	
552	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/9/21	Tue 11/9/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
553	SCG - RFP Preparation	91 days	Thu 8/26/21	Thu 12/30/21	
554	SCG - RFP Release	1 day	Fri 1/14/22	Fri 1/14/22	
555	SCG - RFP Proposal Creation Duration	30 days	Mon 1/17/22	Fri 2/25/22	
556	SCG - RFP Evaluation	25 days	Mon 2/28/22	Fri 4/1/22	
557	SCG - RFP Review with EE PRG	1 day	Tue 5/3/22	Tue 5/3/22	
558	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 5/11/22	Wed 5/11/22	
559	SCG - Contract Negotiation and Development	117 days	Wed 6/22/22	Thu 12/1/22	
560	SCG - Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22	
561	SCG - Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22	
562	SCG - Submit Advice Letter	20 days	Tue 1/3/23	Mon 1/30/23	
563	SCG - Advice Letter Approved	1 day	Tue 5/2/23	Tue 5/2/23	
564	SCG - Implementation Plan	44 days	Wed 5/3/23	Sun 7/2/23	
565	SCG - Residential Multi-Family - Whole Building	436 days?	Mon 3/1/21	Mon 10/31/22	
566	RFA Preparation	40 days	Mon 1/10/22	Fri 3/4/22	
567	RFA Release	1 day	Fri 3/25/22	Fri 3/25/22	
568	RFA Abstract Creation Duration	25 days	Mon 3/28/22	Fri 4/29/22	
569	RFA Evaluation	25 days	Mon 5/2/22	Fri 6/3/22	
570	RFA Review with EE PRG	1 day	Tue 6/7/22	Tue 6/7/22	
571	RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/14/22	Tue 6/14/22	
572	RFP Preparation	28 days	Sun 5/1/22	Tue 6/7/22	
573	RFP Release	1 day	Fri 6/24/22	Fri 6/24/22	
574	RFP Proposal Creation Duration	52 days	Mon 6/27/22	Tue 9/6/22	
575	RFP Evaluation	11 days	Fri 9/9/22	Fri 9/23/22	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
576	RFP Review with EE PRG	1 day	Thu 10/6/22	Thu 10/6/22	
577	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/11/22	Tue 10/11/22	
578	Contract Negotiation and Development	39 days	Tue 10/11/22	Fri 12/2/22	
579	Contract Review with EE PRG	1 day	Tue 12/6/22	Tue 12/6/22	
580	Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22	
581	Submit Advice Letter	22 days	Mon 1/2/23	Tue 1/31/23	
582	Advice Letter Approved	1 day	Fri 3/31/23	Fri 3/31/23	
583	Implementation Plan	43 days	Sat 4/1/23	Tue 5/30/23	
584	SCG - Youth Education Outreach Solicitation	331 days	Tue 3/1/22	Tue 6/6/23	
585	SCG - HERS Rater Training Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22	
586	RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22	
587	RFP Release	1 day	Fri 5/13/22	Fri 5/13/22	
588	RFP Proposal Creation Duration	20 days	Mon 5/16/22	Fri 6/10/22	
589	RFP Evaluation	59 days	Mon 6/13/22	Thu 9/1/22	
590	RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22	
591	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 8/31/22	Wed 8/31/22	
592	Contract Negotiation and Development	53 days	Fri 9/16/22	Tue 11/29/22	
593	Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22	
594	Final Award and Contract Signed	9 days	Mon 12/19/22	Thu 12/29/22	
595	Submit Advice Letter	N/A	N/A	N/A	
596	Advice Letter Approved	N/A	N/A	N/A	
597	Implementation Plan	42 days	Fri 12/30/22	Mon 2/27/23	
598	SCG - Retail Partnering Solicitation	29 days?	Tue 9/27/22	Fri 11/4/22	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
599	RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22	
600	RFP Release	1 day	Fri 6/17/22	Fri 6/17/22	
601	RFP Proposal Creation Duration	30 days	Mon 6/20/22	Fri 7/29/22	
602	RFP Evaluation	24 days	Mon 8/1/22	Thu 9/1/22	
603	RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22	
604	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/13/22	Tue 9/13/22	
605	Contract Negotiation and Development	29 days	Mon 9/19/22	Thu 10/27/22	
606	Contract Review with EE PRG	9 days	Tue 11/1/22	Fri 11/11/22	
607	Final Award and Contract Signed	13 days	Mon 11/14/22	Wed 11/30/22	
608	Submit Advice Letter	N/A	N/A	N/A	
609	Advice Letter Approved	N/A	N/A	N/A	
610	Implementation Plan	43 days	Sat 10/1/22	Tue 11/29/22	
611	SCG - Non-Residential EE Advisor Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22	
612	RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22	
613	RFP Release	1 day	Fri 8/26/22	Fri 8/26/22	
614	RFP Proposal Creation Duration	20 days	Mon 8/29/22	Fri 9/23/22	
615	RFP Evaluation	16 days	Sat 9/24/22	Fri 10/14/22	
616	RFP Review with EE PRG	5 days	Mon 10/17/22	Fri 10/21/22	
617	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/25/22	Tue 10/25/22	
618	Contract Negotiation and Development	32 days	Sun 10/30/22	Mon 12/12/22	
619	Contract Review with EE PRG	9 days	Tue 12/13/22	Fri 12/23/22	
620	Final Award and Contract Signed	4 days	Tue 12/27/22	Fri 12/30/22	
621	Submit Advice Letter	N/A	N/A	N/A	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
622	Advice Letter Approved	N/A	N/A	N/A	
623	Implementation Plan	44 days	Sun 1/1/23	Wed 3/1/23	
624	SCG - Residential EE Kits Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22	
625	RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22	
626	RFP Release	1 day	Mon 7/25/22	Mon 7/25/22	
627	RFP Proposal Creation Duration	16 days	Tue 7/26/22	Tue 8/16/22	
628	RFP Evaluation	12 days	Wed 8/17/22	Thu 9/1/22	
629	RFP Review with EE PRG	1 day	Tue 8/2/22	Tue 8/2/22	
630	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/9/22	Tue 8/9/22	
631	Contract Negotiation and Development	30 days	Mon 8/22/22	Fri 9/30/22	
632	Contract Review with EE PRG	9 days	Tue 10/4/22	Fri 10/14/22	
633	Final Award and Contract Signed	10 days	Mon 10/17/22	Fri 10/28/22	
634	Submit Advice Letter	N/A	N/A	N/A	
635	Advice Letter Approved	N/A	N/A	N/A	
636	Implementation Plan	43 days	Sat 10/29/22	Tue 12/27/22	
637	SCG - IDEEA 365	230 days	Mon 2/13/23	Fri 12/29/23	
638	RFP Preparation	23 days	Mon 2/13/23	Wed 3/15/23	
639	RFP Release	20 days	Thu 4/20/23	Wed 5/17/23	
640	RFP Proposal Creation Duration	43 days	Wed 5/3/23	Fri 6/30/23	
641	RFP Evaluation	12 days	Fri 7/14/23	Mon 7/31/23	
642	RFP Review with EE PRG	1 day	Tue 8/1/23	Tue 8/1/23	
643	RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Tue 8/1/23	Thu 8/31/23	
644	Contract Negotiation and Development	21 days	Fri 9/1/23	Fri 9/29/23	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
645	Contract Review with EE PRG	32 days	Mon 9/18/23	Tue 10/31/23	
646	Final Award and Contract Signed	17 days	Mon 10/9/23	Tue 10/31/23	
647	Submit Advice Letter	10 days	Wed 11/1/23	Tue 11/14/23	
648	Advice Letter Approved	11 days	Wed 11/22/23	Wed 12/6/23	
649	Implementation Plan	9 days	Tue 12/19/23	Fri 12/29/23	
650	SCG - Commercial SEM	110 days?	Tue 8/1/23	Mon 1/1/24	
651	RFP Preparation	22 days	Tue 8/1/23	Wed 8/30/23	
652	RFP Release	13 days	Wed 9/13/23	Fri 9/29/23	
653	RFP Proposal Creation Duration	11 days	Mon 10/2/23	Mon 10/16/23	
654	RFP Evaluation	5 days	Wed 10/25/23	Tue 10/31/23	
655	RFP Review with EE PRG	2 days	Tue 10/31/23	Wed 11/1/23	
656	RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Thu 11/2/23	Wed 11/8/23	
657	Contract Negotiation and Development	16 days	Wed 10/25/23	Wed 11/15/23	
658	Contract Review with EE PRG	1 day	Tue 12/5/23	Tue 12/5/23	
659	Final Award and Contract Signed	6 days	Wed 12/13/23	Wed 12/20/23	
660	Submit Advice Letter	5 days	Mon 12/18/23	Fri 12/22/23	
661	Advice Letter Approved	1 day	Fri 12/29/23	Fri 12/29/23	
662	Implementation Plan	1 day	Mon 1/1/24	Mon 1/1/24	
663	SCG - Market Access Program	333 days?	Sat 3/16/24	Tue 6/24/25	
664	RFP Preparation	75 days	Sat 3/16/24	Thu 6/27/24	
665	RFP Release	1 day	Fri 6/21/24	Fri 6/21/24	
666	RFP Proposal Creation Duration	53 days	Mon 6/24/24	Wed 9/4/24	
667	RFP Evaluation	38 days	Mon 8/19/24	Wed 10/9/24	

Project: IOU Master Task Timeli
Date: Thu 4/30/26




















Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
668	RFP Review with EE PRG	1 day	Tue 10/1/24	Tue 10/1/24	
669	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/8/24	Tue 10/8/24	
670	Contract Negotiation and Development	78 days	Mon 10/14/24	Wed 1/29/25	
671	Contract Review with EE PRG	10 days	Tue 1/7/25	Mon 1/20/25	
672	Final Award and Contract Signed	11 days	Mon 1/20/25	Mon 2/3/25	
673	Submit Advice Letter	N/A	Wed 1/1/25		
674	Advice Letter Approved	N/A	Mon 3/3/25		
675	Implementation Plan	59 days	Thu 4/3/25	Tue 6/24/25	
676	SCG - IDEEA 365 (Round 3)	230 days?	Tue 10/15/24	Mon 9/1/25	
677	RFP Preparation	23 days	Tue 10/15/24	Thu 11/14/24	
678	RFP Release	20 days	Fri 11/15/24	Thu 12/12/24	
679	RFP Proposal Creation Duration	43 days	Fri 12/13/24	Tue 2/11/25	
680	RFP Evaluation	12 days	Wed 2/12/25	Thu 2/27/25	
681	RFP Review with EE PRG	1 day	Fri 2/28/25	Fri 2/28/25	
682	RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Mon 3/3/25	Wed 4/2/25	
683	Contract Negotiation and Development	21 days	Thu 4/3/25	Thu 5/1/25	
684	Contract Review with EE PRG	32 days	Fri 5/2/25	Mon 6/16/25	
685	Final Award and Contract Signed	17 days	Tue 6/17/25	Wed 7/9/25	
686	Submit Advice Letter	10 days	Thu 7/10/25	Wed 7/23/25	
687	Advice Letter Approved	11 days	Thu 7/24/25	Thu 8/7/25	
688	Implementation Plan	9 days	Fri 8/8/25	Wed 8/20/25	
689					
690	Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change				

Project: IOU Master Task Timeli Date: Thu 4/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
691	SDG&E - Small Commercial (<20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20	
692	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18	
693	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18	
694	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18	
695	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19	
696	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19	
697	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19	
698	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19	
699	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19	
700	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19	
701	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19	
702	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20	
703	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20	
704	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20	
705	SDG&E - Contract Review with EE PRG	0 days	Tue 6/9/20	Tue 6/9/20	
706	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20	
707	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20	
708	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20	
709	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20	
710	SDG&E - Large Commercial (>20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20	
711	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18	
712	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18	
713	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
714	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19	
715	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19	
716	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19	
717	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19	
718	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19	
719	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19	
720	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19	
721	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20	
722	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20	
723	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20	
724	SDG&E - Contract Review with EE PRG	0 days	Tue 5/12/20	Tue 5/12/20	
725	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20	
726	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20	
727	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20	
728	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20	
729	SDG&E - Residential Multi-Family Solicitation	586 days	Thu 9/6/18	Thu 12/3/20	
730	SDG&E - RFA Preparation	64 days	Thu 9/6/18	Tue 12/4/18	
731	SDG&E - RFA Release	23 days	Tue 12/4/18	Thu 1/3/19	
732	SDG&E - RFA Abstract Creation Duration	49 days	Tue 9/11/18	Fri 11/16/18	
733	SDG&E - RFA Evaluation	21 days	Mon 1/7/19	Mon 2/4/19	
734	SDG&E - RFA Review with EE PRG	0 days	Tue 11/13/18	Tue 11/13/18	
735	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 3/20/19	Wed 3/20/19	
736	SDG&E - RFP Preparation	63 days	Fri 3/22/19	Tue 6/18/19	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
737	SDG&E - RFP Release	52 days	Tue 6/18/19	Wed 8/28/19	
738	SDG&E - RFP Proposal Creation Duration	36 days	Mon 3/25/19	Mon 5/13/19	
739	SDG&E - RFP Evaluation	30 days	Thu 8/29/19	Wed 10/9/19	
740	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Thu 12/12/19	Thu 12/19/19	
741	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20	
742	SDG&E - Contract Negotiation and Development	35 days	Mon 4/13/20	Fri 5/29/20	
743	SDG&E - Contract Review with EE PRG	10 days	Thu 6/4/20	Wed 6/17/20	
744	SDG&E - Final Award and Contract Signed	0 days	Mon 6/22/20	Mon 6/22/20	
745	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20	
746	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20	
747	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20	
748	SDG&E - SW HVAC Solicitation	593 days	Thu 11/1/18	Tue 2/9/21	
749	SDG&E - RFA Preparation	48 days	Thu 11/1/18	Mon 1/7/19	
750	SDG&E - RFA Release	0 days	Mon 1/7/19	Mon 1/7/19	
751	SDG&E - RFA Abstract Creation Duration	24 days	Mon 1/7/19	Thu 2/7/19	
752	SDG&E - RFA Evaluation	37 days	Fri 2/8/19	Sun 3/31/19	
753	SDG&E - RFA Review with EE PRG	0 days	Tue 4/9/19	Tue 4/9/19	
754	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 4/17/19	Wed 4/17/19	
755	SDG&E - RFP Preparation	73 days	Thu 4/18/19	Mon 7/29/19	
756	SDG&E - RFP Release	0 days	Tue 9/3/19	Tue 9/3/19	
757	SDG&E - RFP Proposal Creation Duration	30 days	Tue 9/3/19	Mon 10/14/19	
758	SDG&E - RFP Evaluation	33 days	Mon 10/14/19	Wed 11/27/19	
759	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
760	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20	
761	SDG&E - Contract Negotiation and Development	88 days	Wed 3/25/20	Fri 7/24/20	
762	SDG&E - Contract Review with EE PRG	0 days	Tue 9/8/20	Tue 9/8/20	
763	SDG&E - Final Award and Contract Signed	0 days	Fri 10/30/20	Fri 10/30/20	
764	SDG&E - Submit Advice Letter	0 days	Thu 11/12/20	Thu 11/12/20	
765	SDG&E - Advice Letter Approved	0 days	Fri 12/11/20	Fri 12/11/20	
766	SDG&E - Implementation Plan	0 days	Tue 2/9/21	Tue 2/9/21	
767	SDG&E - SW PLA Solicitation	853 days	Mon 1/28/19	Wed 5/4/22	
768	SDG&E - RFA Preparation	75 days	Mon 1/28/19	Fri 5/10/19	
769	SDG&E - RFA Release	0 days	Fri 5/10/19	Fri 5/10/19	
770	SDG&E - RFA Abstract Creation Duration	31 days	Fri 5/10/19	Fri 6/21/19	
771	SDG&E - RFA Evaluation	65 days	Mon 6/24/19	Fri 9/20/19	
772	SDG&E - RFA Review with EE PRG	0 days	Tue 9/10/19	Tue 9/10/19	
773	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 9/20/19	Fri 9/20/19	
774	SDG&E - RFP Preparation	52 days	Fri 9/20/19	Mon 12/2/19	
775	SDG&E - RFP Release	0 days	Mon 1/27/20	Mon 1/27/20	
776	SDG&E - RFP Proposal Creation Duration	31 days	Mon 1/27/20	Mon 3/9/20	
777	SDG&E - RFP Evaluation	82 days	Mon 3/9/20	Tue 6/30/20	
778	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/17/20	Mon 8/17/20	
779	SDG&E - Selection Review with EE PRG	66 days	Tue 10/13/20	Tue 1/12/21	
780	SDG&E - Contract Negotiation and Development	197 days	Fri 1/29/21	Mon 11/1/21	
781	SDG&E - Contract Review with EE PRG	0 days	Tue 11/9/21	Tue 11/9/21	
782	SDG&E - Final Award and Contract Signed	0 days	Fri 1/7/22	Fri 1/7/22	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
783	SDG&E - Submit Advice Letter	0 days	Mon 1/10/22	Mon 1/10/22	
784	SDG&E - Advice Letter Approved	0 days	Thu 2/10/22	Thu 2/10/22	
785	SDG&E - Implementation Plan	60 days	Thu 2/10/22	Wed 5/4/22	
786	SDG&E - Residential Single-Family 2.0 Solicitation	467 days	Tue 1/19/21	Wed 11/2/22	
787	SDG&E - RFA Preparation	43 days	Tue 1/19/21	Thu 3/18/21	
788	SDG&E - RFA Release	0 days	Mon 3/22/21	Mon 3/22/21	
789	SDG&E - RFA Abstract Creation Duration	22 days	Mon 3/22/21	Tue 4/20/21	
790	SDG&E - RFA Evaluation	38 days	Wed 4/21/21	Fri 6/11/21	
791	SDG&E - RFA Review with EE PRG	7 days	Thu 6/3/21	Fri 6/11/21	
792	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 6/15/21	Tue 6/15/21	
793	SDG&E - RFP Preparation	43 days	Wed 6/16/21	Fri 8/13/21	
794	SDG&E - RFP Release	0 days	Wed 8/18/21	Wed 8/18/21	
795	SDG&E - RFP Proposal Creation Duration	32 days	Wed 8/18/21	Thu 9/30/21	
796	SDG&E - RFP Evaluation	44 days	Fri 10/1/21	Wed 12/1/21	
797	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 12/14/21	Tue 12/14/21	
798	SDG&E - Selection Review with EE PRG	7 days	Thu 12/2/21	Fri 12/10/21	
799	SDG&E - Contract Negotiation and Development	96 days	Mon 12/20/21	Mon 5/2/22	
800	SDG&E - Contract Review with EE PRG	7 days	Thu 5/5/22	Fri 5/13/22	
801	SDG&E - Final Award and Contract Signed	0 days	Tue 5/31/22	Tue 5/31/22	
802	SDG&E - Submit Advice Letter	0 days	Fri 6/24/22	Fri 6/24/22	
803	SDG&E - Advice Letter Approved	0 days	Thu 8/11/22	Thu 8/11/22	
804	SDG&E - Implementation Plan	60 days	Thu 8/11/22	Wed 11/2/22	
805	SDG&E - Residential Single-Family Solicitation	501 days	Mon 7/1/19	Tue 6/1/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
806	SDG&E - RFA Preparation	80 days	Mon 7/1/19	Fri 10/18/19	
807	SDG&E - RFA Release	35 days	Fri 10/18/19	Thu 12/5/19	
808	SDG&E - RFA Abstract Creation Duration	53 days	Mon 7/22/19	Wed 10/2/19	
809	SDG&E - RFA Evaluation	29 days	Fri 12/6/19	Wed 1/15/20	
810	SDG&E - RFA Review with EE PRG	0 days	Tue 10/8/19	Tue 10/8/19	
811	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 2/27/20	Thu 2/27/20	
812	SDG&E - RFP Preparation	48 days	Fri 2/28/20	Tue 5/5/20	
813	SDG&E - RFP Release	0 days	Mon 4/27/20	Mon 4/27/20	
814	SDG&E - RFP Proposal Creation Duration	32 days	Mon 4/27/20	Tue 6/9/20	
815	SDG&E - RFP Evaluation	16 days	Wed 6/10/20	Wed 7/1/20	
816	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 7/23/20	Fri 7/24/20	
817	SDG&E - Selection Review with EE PRG	7 days	Thu 8/6/20	Fri 8/14/20	
818	SDG&E - Contract Negotiation and Development	60 days	Mon 8/17/20	Fri 11/6/20	
819	SDG&E - Contract Review with EE PRG	10 days	Tue 12/8/20	Mon 12/21/20	
820	SDG&E - Final Award and Contract Signed	0 days	Fri 1/29/21	Fri 1/29/21	
821	SDG&E - Submit Advice Letter	0 days	Mon 3/1/21	Mon 3/1/21	
822	SDG&E - Advice Letter Approved				
823	SDG&E - Implementation Plan	0 days	Tue 6/1/21	Tue 6/1/21	
824	SDG&E - Public Sector: Federal Solicitation	625 days	Mon 7/1/19	Fri 11/19/21	
825	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19	
826	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19	
827	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19	
828	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
829	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20	
830	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20	
831	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20	
832	SDG&E - RFP Release	0 days	Fri 5/22/20	Fri 5/22/20	
833	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20	
834	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20	
835	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20	
836	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20	
837	SDG&E - Contract Negotiation and Development	53 days	Wed 2/17/21	Fri 4/30/21	
838	SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21	
839	SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21	
840	SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21	
841	SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21	
842	SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21	
843	SDG&E - Public Sector: K-12 Solicitation	625 days	Mon 7/1/19	Fri 11/19/21	
844	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19	
845	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19	
846	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19	
847	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20	
848	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20	
849	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20	
850	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20	
851	SDG&E - RFP Release	1 day	Fri 5/22/20	Fri 5/22/20	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
852	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20	
853	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20	
854	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20	
855	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20	
856	SDG&E - Contract Negotiation and Development	117 days	Thu 11/19/20	Fri 4/30/21	
857	SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21	
858	SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21	
859	SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21	
860	SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21	
861	SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21	
862	SDG&E - Public Sector: Local Government Solicitation	338 days	Tue 10/13/20	Thu 1/27/22	
863	SDG&E - RFA Preparation	10 days	Fri 10/23/20	Thu 11/5/20	
864	SDG&E - RFA Release	1 day	Wed 1/27/21	Wed 1/27/21	
865	SDG&E - RFA Abstract Creation Duration	20 days	Thu 1/28/21	Wed 2/24/21	
866	SDG&E - RFA Evaluation	18 days	Fri 2/26/21	Tue 3/23/21	
867	SDG&E - RFA Review with EE PRG	7 days	Thu 4/8/21	Fri 4/16/21	
868	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/21/21	Wed 4/21/21	
869	SDG&E - RFP Preparation	51 days	Fri 3/19/21	Fri 5/28/21	
870	SDG&E - RFP Release	1 day	Tue 6/1/21	Tue 6/1/21	
871	SDG&E - RFP Proposal Creation Duration	26 days	Wed 6/2/21	Wed 7/7/21	
872	SDG&E - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21	
873	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/25/21	Mon 10/25/21	
874	SDG&E - Selection Review with EE PRG	7 days	Tue 10/12/21	Wed 10/20/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
875	SDG&E - Contract Negotiation and Development	41 days	Fri 11/5/21	Fri 12/31/21	
876	SDG&E - Contract Review with EE PRG	7 days	Thu 1/6/22	Fri 1/14/22	
877	SDG&E - Final Award and Contract Signed	9 days	Mon 1/17/22	Thu 1/27/22	
878	SDG&E - Submit Advice Letter	13 days	Wed 6/1/22	Fri 6/17/22	
879	SDG&E - Advice Letter Approved	40 days	Fri 6/17/22	Thu 8/11/22	
880	SDG&E - Implementation Plan	42 days	Mon 8/15/22	Tue 10/11/22	
881	SDG&E - Agricultural Sector: Local Agriculture Solicitation	447 days	Mon 3/1/21	Tue 11/15/22	
882	SDG&E - RFA Preparation	56 days	Mon 3/1/21	Mon 5/17/21	
883	SDG&E - RFA Release	0 days	Mon 4/26/21	Mon 4/26/21	
884	SDG&E - RFA Abstract Creation Duration	20 days	Tue 4/27/21	Mon 5/24/21	
885	SDG&E - RFA Evaluation	36 days	Tue 6/1/21	Tue 7/20/21	
886	SDG&E - RFA Review with EE PRG	0 days	Thu 7/8/21	Thu 7/8/21	
887	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 7/20/21	Tue 7/20/21	
888	SDG&E - RFP Preparation	48 days	Tue 7/20/21	Thu 9/23/21	
889	SDG&E - RFP Release	0 days	Thu 9/23/21	Thu 9/23/21	
890	SDG&E - RFP Proposal Creation Duration	25 days	Fri 9/24/21	Thu 10/28/21	
891	SDG&E - RFP Evaluation	23 days	Thu 10/28/21	Mon 11/29/21	
892	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 2/1/22	Tue 2/1/22	
893	SDG&E - Selection Review with EE PRG	0 days	Tue 2/8/22	Tue 2/8/22	
894	SDG&E - Contract Negotiation and Development	83 days	Tue 2/1/22	Thu 5/26/22	
895	SDG&E - Contract Review with EE PRG	0 days	Tue 6/14/22	Tue 6/14/22	
896	SDG&E - Final Award and Contract Signed	10 days	Fri 6/18/21	Thu 7/1/21	
897	SDG&E - Submit Advice Letter	0 days	Fri 7/22/22	Fri 7/22/22	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
898	SDG&E - Advice Letter Approved	0 days	Tue 8/30/22	Tue 8/30/22	
899	SDG&E - Implementation Plan	44 days	Wed 8/31/22	Sat 10/29/22	
900	*SDG&E - Industrial Solicitation	426 days	Thu 4/1/21	Thu 11/17/22	
901	SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21	
902	SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21	
903	SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21	
904	SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21	
905	SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21	
906	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21	
907	SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21	
908	SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21	
909	SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22	
910	SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22	
911	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22	
912	SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22	
913	SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22	
914	SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22	
915	SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22	
916	SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22	
917	SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22	
918	SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23	
919	*SDG&E - Industrial-Port Tenants Solicitation	426 days	Thu 4/1/21	Thu 11/17/22	
920	SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
921	SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21	
922	SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21	
923	SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21	
924	SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21	
925	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21	
926	SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21	
927	SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21	
928	SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22	
929	SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22	
930	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22	
931	SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22	
932	SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22	
933	SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22	
934	SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22	
935	SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22	
936	SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22	
937	SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23	
938	*SDG&E - SW Residential HVAC QI/QM Solicitation	377 days	Mon 7/5/21	Tue 12/13/22	
939	SDG&E - RFA Preparation	48 days	Mon 7/5/21	Wed 9/8/21	
940	SDG&E - RFA Release	1 day	Wed 9/29/21	Wed 9/29/21	
941	SDG&E - RFA Abstract Creation Duration	22 days	Wed 9/29/21	Thu 10/28/21	
942	SDG&E - RFA Evaluation	21 days	Fri 10/29/21	Fri 11/26/21	
943	SDG&E - RFA Review with EE PRG	6 days	Fri 12/10/21	Fri 12/17/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
944	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 12/22/21	Wed 12/22/21	
945	SDG&E - RFP Preparation	56 days	Tue 1/4/22	Tue 3/22/22	
946	SDG&E - RFP Release	1 day	Tue 3/22/22	Tue 3/22/22	
947	SDG&E - RFP Proposal Creation Duration	23 days	Wed 3/23/22	Fri 4/22/22	
948	SDG&E - RFP Evaluation	20 days	Mon 4/25/22	Fri 5/20/22	
949	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/21/22	Tue 6/21/22	
950	SDG&E - Selection Review with EE PRG	0 days	Fri 6/17/22	Fri 6/17/22	
951	SDG&E - Contract Negotiation and Development	83 days	Wed 7/20/22	Fri 11/11/22	
952	SDG&E - Contract Review with EE PRG	6 days	Mon 11/14/22	Mon 11/21/22	
953	SDG&E - Final Award and Contract Signed	1 day	Mon 1/10/22	Mon 1/10/22	
954	SDG&E - Submit Advice Letter	22 days	Sun 1/15/23	Mon 2/13/23	
955	SDG&E - Advice Letter Approved	1 day	Fri 4/28/23	Fri 4/28/23	
956	SDG&E - Implementation Plan	60 days	Fri 4/28/23	Thu 7/20/23	
957	*SDG&E - Local/Residential Behavioral Solicitation	472 days	Mon 4/19/21	Tue 2/7/23	
958	SDG&E - RFA Preparation	53 days	Mon 4/19/21	Wed 6/30/21	
959	SDG&E - RFA Release	1 day	Mon 7/26/21	Mon 7/26/21	
960	SDG&E - RFA Abstract Creation Duration	21 days	Mon 7/26/21	Mon 8/23/21	
961	SDG&E - RFA Evaluation	30 days	Tue 8/24/21	Mon 10/4/21	
962	SDG&E - RFA Review with EE PRG	7 days	Thu 10/7/21	Fri 10/15/21	
963	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/19/21	Tue 10/19/21	
964	SDG&E - RFP Preparation	28 days	Thu 10/21/21	Mon 11/29/21	
965	SDG&E - RFP Release	1 day	Wed 12/22/21	Wed 12/22/21	
966	SDG&E - RFP Proposal Creation Duration	20 days	Wed 12/22/21	Tue 1/18/22	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
967	SDG&E - RFP Evaluation	28 days	Wed 1/19/22	Fri 2/25/22	
968	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/15/22	Tue 3/15/22	
969	SDG&E - Selection Review with EE PRG	7 days	Thu 3/3/22	Fri 3/11/22	
970	SDG&E - Contract Negotiation and Development	119 days	Fri 3/18/22	Wed 8/31/22	
971	SDG&E - Contract Review with EE PRG	7 days	Thu 9/8/22	Fri 9/16/22	
972	SDG&E - Final Award and Contract Signed	1 day	Fri 10/21/22	Fri 10/21/22	
973	SDG&E - Submit Advice Letter	1 day	Wed 11/16/22	Wed 11/16/22	
974	SDG&E - Advice Letter Approved	1 day	Fri 12/16/22	Fri 12/16/22	
975	SDG&E - Implementation Plan	60 days	Wed 11/16/22	Tue 2/7/23	
976	*SDG&E - Small Business Outreach Solicitation	298 days?	Wed 4/13/22	Fri 6/2/23	
977	SDG&E - RFA Preparation	53 days	Wed 4/13/22	Fri 6/24/22	
978	SDG&E - RFA Release	1 day	Thu 7/7/22	Thu 7/7/22	
979	SDG&E - RFA Abstract Creation Duration	21 days	Fri 7/8/22	Fri 8/5/22	
980	SDG&E - RFA Evaluation	30 days	Mon 8/8/22	Fri 9/16/22	
981	SDG&E - RFA Review with EE PRG	5 days	Mon 9/19/22	Fri 9/23/22	
982	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/27/22	Tue 9/27/22	
983	SDG&E - RFP Preparation	28 days	Mon 8/8/22	Wed 9/14/22	
984	SDG&E - RFP Release	1 day	Tue 10/18/22	Tue 10/18/22	
985	SDG&E - RFP Proposal Creation Duration	31 days	Tue 10/18/22	Tue 11/29/22	
986	SDG&E - RFP Evaluation	38 days	Wed 11/30/22	Fri 1/20/23	
987	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/28/23	Tue 2/28/23	
988	SDG&E - Selection Review with EE PRG	7 days	Thu 2/16/23	Fri 2/24/23	
989	SDG&E - Contract Negotiation and Development	79 days	Tue 2/28/23	Fri 6/16/23	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
990	SDG&E - Contract Review with EE PRG	4 days	Wed 6/21/23	Mon 6/26/23	
991	SDG&E - Final Award and Contract Signed	1 day	Tue 8/29/23	Tue 8/29/23	
992	SDG&E - Submit Advice Letter	1 day	Fri 9/15/23	Fri 9/15/23	
993	SDG&E - Advice Letter Approved	1 day	Mon 10/16/23	Mon 10/16/23	
994	SDG&E - Implementation Plan	46 days	Mon 10/16/23	Mon 12/18/23	
995	*SDG&E - Workforce Education & Training /Integrated Energy Education Solicitatio	353 days?	Mon 1/16/23	Wed 5/22/24	
996	SDG&E - RFP Release	1 day?	Thu 2/2/23	Thu 2/2/23	
997	SDG&E - RFP Evaluation	25 days	Fri 3/17/23	Thu 4/20/23	
998	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/16/23	Tue 5/16/23	
999	SDG&E - Selection Review with EE PRG	5 days	Tue 5/9/23	Mon 5/15/23	
1000	SDG&E - Contract Negotiation and Development	94 days	Fri 5/5/23	Wed 9/13/23	
1001	SDG&E - Contract Review with EE PRG	7 days	Tue 10/10/23	Wed 10/18/23	
1002	SDG&E - Final Award and Contract Signed	1 day	Tue 11/14/23	Tue 11/14/23	
1003	SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24	
1004	SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24	
1005	SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24	
1006	*SDG&E - Residential Equity Education & Outreach Solicitation	331 days?	Fri 1/13/23	Fri 4/19/24	
1007	SDG&E - RFA Release	1 day	Thu 3/2/23	Thu 3/2/23	
1008	SDG&E - RFA Evaluation	21 days	Wed 4/12/23	Wed 5/10/23	
1009	SDG&E - RFA Review with EE PRG	7 days	Fri 5/19/23	Mon 5/29/23	
1010	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/30/23	Tue 5/30/23	
1011	SDG&E - RFP Release	1 day	Thu 6/1/23	Thu 6/1/23	
1012	SDG&E - RFP Evaluation	27 days	Mon 7/17/23	Tue 8/22/23	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1013	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/28/23	Mon 8/28/23	
1014	SDG&E - Selection Review with EE PRG	7 days	Wed 8/30/23	Thu 9/7/23	
1015	SDG&E - Contract Negotiation and Development	32 days	Thu 11/2/23	Fri 12/15/23	
1016	SDG&E - Contract Review with EE PRG	7 days	Tue 1/9/24	Wed 1/17/24	
1017	SDG&E - Final Award and Contract Signed	1 day	Mon 2/12/24	Mon 2/12/24	
1018	SDG&E - Submit Advice Letter	1 day	Mon 2/26/24	Mon 2/26/24	
1019	SDG&E - Advice Letter Approved	1 day	Mon 4/8/24	Mon 4/8/24	
1020	SDG&E - Implementation Plan	60 days	Tue 4/9/24	Mon 7/1/24	
1021	*SDG&E - Non-Residential Behavioral Solicitation	398 days	Mon 8/15/22	Wed 2/21/24	
1022	SDG&E - RFA Preparation	67 days	Mon 8/15/22	Tue 11/15/22	
1023	SDG&E - RFA Release	1 day	Mon 10/24/22	Mon 10/24/22	
1024	SDG&E - RFA Abstract Creation Duration	27 days	Tue 8/23/22	Wed 9/28/22	
1025	SDG&E - RFA Evaluation	16 days	Tue 11/29/22	Tue 12/20/22	
1026	SDG&E - RFA Review with EE PRG	7 days	Thu 1/5/23	Fri 1/13/23	
1027	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 1/18/23	Wed 1/18/23	
1028	SDG&E - RFP Preparation	26 days	Mon 11/14/22	Mon 12/19/22	
1029	SDG&E - RFP Release	1 day	Mon 1/23/23	Mon 1/23/23	
1030	SDG&E - RFP Proposal Creation Duration	26 days	Mon 1/23/23	Mon 2/27/23	
1031	SDG&E - RFP Evaluation	58 days	Tue 2/28/23	Thu 5/18/23	
1032	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/20/23	Tue 6/20/23	
1033	SDG&E - Selection Review with EE PRG	7 days	Thu 6/8/23	Fri 6/16/23	
1034	SDG&E - Contract Negotiation and Development	60 days	Wed 6/21/23	Tue 9/12/23	
1035	SDG&E - Contract Review with EE PRG	7 days	Thu 10/5/23	Fri 10/13/23	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1036	SDG&E - Final Award and Contract Signed	1 day	Thu 12/21/23	Thu 12/21/23	
1037	SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24	
1038	SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24	
1039	SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24	
1040	*SDG&E - Retail Offices and Wholesale Solicitation	419 days	Wed 5/10/23	Mon 12/16/24	
1041	SDG&E - RFA Preparation	33 days	Wed 5/10/23	Fri 6/23/23	
1042	SDG&E - RFA Release	1 day	Mon 7/3/23	Mon 7/3/23	
1043	SDG&E - RFA Abstract Creation Duration	31 days	Tue 7/4/23	Tue 8/15/23	
1044	SDG&E - RFA Evaluation	19 days	Wed 8/16/23	Mon 9/11/23	
1045	SDG&E - RFA Review with EE PRG	3 days	Mon 9/18/23	Wed 9/20/23	
1046	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 9/25/23	Mon 9/25/23	
1047	SDG&E - RFP Preparation	33 days	Wed 7/5/23	Fri 8/18/23	
1048	SDG&E - RFP Release	1 day	Fri 9/29/23	Fri 9/29/23	
1049	SDG&E - RFP Proposal Creation Duration	33 days	Mon 10/2/23	Wed 11/15/23	
1050	SDG&E - RFP Evaluation	25 days	Thu 11/16/23	Wed 12/20/23	
1051	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 2/19/24	Mon 2/19/24	
1052	SDG&E - Selection Review with EE PRG	7 days	Thu 2/8/24	Fri 2/16/24	
1053	SDG&E - Contract Negotiation and Development	96 days	Mon 2/26/24	Mon 7/8/24	
1054	SDG&E - Contract Review with EE PRG	6 days	Wed 7/17/24	Wed 7/24/24	
1055	SDG&E - Final Award and Contract Signed	1 day	Tue 8/27/24	Tue 8/27/24	
1056	SDG&E - Submit Advice Letter	1 day	Mon 9/16/24	Mon 9/16/24	
1057	SDG&E - Advice Letter Approved	1 day	Wed 10/16/24	Wed 10/16/24	
1058	SDG&E - Implementation Plan	44 days	Wed 10/16/24	Mon 12/16/24	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1059	*SDG&E - Groceries, Restaurants and Food Storage Solicitation	467 days	Wed 6/14/23	Thu 3/27/25	
1060	SDG&E - RFA Preparation	33 days	Wed 6/14/23	Fri 7/28/23	
1061	SDG&E - RFA Release	1 day	Tue 8/15/23	Tue 8/15/23	
1062	SDG&E - RFA Abstract Creation Duration	21 days	Wed 8/16/23	Wed 9/13/23	
1063	SDG&E - RFA Evaluation	15 days	Thu 9/14/23	Wed 10/4/23	
1064	SDG&E - RFA Review with EE PRG	5 days	Wed 10/18/23	Tue 10/24/23	
1065	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/30/23	Mon 10/30/23	
1066	SDG&E - RFP Preparation	16 days	Mon 10/9/23	Mon 10/30/23	
1067	SDG&E - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23	
1068	SDG&E - RFP Proposal Creation Duration	40 days	Mon 11/6/23	Fri 12/29/23	
1069	SDG&E - RFP Evaluation	34 days	Fri 12/29/23	Wed 2/14/24	
1070	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 3/6/24	Wed 3/6/24	
1071	SDG&E - Selection Review with EE PRG	7 days	Thu 2/29/24	Fri 3/8/24	
1072	SDG&E - Contract Negotiation and Development	144 days	Wed 3/13/24	Mon 9/30/24	
1073	SDG&E - Contract Review with EE PRG	6 days	Tue 10/8/24	Tue 10/15/24	
1074	SDG&E - Final Award and Contract Signed	1 day	Tue 11/26/24	Tue 11/26/24	
1075	SDG&E - Submit Advice Letter	1 day	Fri 12/27/24	Fri 12/27/24	
1076	SDG&E - Advice Letter Approved	1 day	Mon 1/27/25	Mon 1/27/25	
1077	SDG&E - Implementation Plan	44 days	Mon 1/27/25	Thu 3/27/25	
1078	*SDG&E - Private Institutions and Healthcare Solicitation	399 days	Thu 10/5/23	Tue 4/15/25	
1079	SDG&E - RFA Preparation	33 days	Thu 10/5/23	Mon 11/20/23	
1080	SDG&E - RFA Release	1 day	Mon 11/27/23	Mon 11/27/23	
1081	SDG&E - RFA Abstract Creation Duration	35 days	Mon 11/27/23	Fri 1/12/24	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
1082	SDG&E - RFA Evaluation	30 days	Mon 1/15/24	Fri 2/23/24	
1083	SDG&E - RFA Review with EE PRG	5 days	Mon 2/26/24	Fri 3/1/24	
1084	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 3/4/24	Mon 3/4/24	
1085	SDG&E - RFP Preparation	54 days	Mon 11/27/23	Thu 2/8/24	
1086	SDG&E - RFP Release	1 day	Fri 3/8/24	Fri 3/8/24	
1087	SDG&E - RFP Proposal Creation Duration	34 days	Fri 3/8/24	Wed 4/24/24	
1088	SDG&E - RFP Evaluation	42 days	Thu 4/25/24	Fri 6/21/24	
1089	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 7/2/24	Tue 7/2/24	
1090	SDG&E - Selection Review with EE PRG	7 days	Fri 6/21/24	Mon 7/1/24	
1091	SDG&E - Contract Negotiation and Development	61 days	Wed 7/31/24	Wed 10/23/24	
1092	SDG&E - Contract Review with EE PRG	4 days	Tue 11/12/24	Fri 11/15/24	
1093	SDG&E - Final Award and Contract Signed	1 day	Tue 12/17/24	Tue 12/17/24	
1094	SDG&E - Submit Advice Letter	1 day	Wed 1/15/25	Wed 1/15/25	
1095	SDG&E - Advice Letter Approved	1 day	Fri 2/14/25	Fri 2/14/25	
1096	SDG&E - Implementation Plan	43 days	Fri 2/14/25	Tue 4/15/25	
1097	*SDG&E - Lodging: Hotels/Motels Solicitation	400 days	Tue 10/10/23	Mon 4/21/25	
1098	SDG&E - RFA Preparation	33 days	Tue 10/10/23	Thu 11/23/23	
1099	SDG&E - RFA Release	1 day	Fri 12/8/23	Fri 12/8/23	
1100	SDG&E - RFA Abstract Creation Duration	35 days	Fri 12/8/23	Thu 1/25/24	
1101	SDG&E - RFA Evaluation	22 days	Mon 1/22/24	Tue 2/20/24	
1102	SDG&E - RFA Review with EE PRG	7 days	Tue 3/12/24	Wed 3/20/24	
1103	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/19/24	Tue 3/19/24	
1104	SDG&E - RFP Preparation	48 days	Tue 1/23/24	Thu 3/28/24	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
1105	SDG&E - RFP Release	1 day	Thu 3/21/24	Thu 3/21/24	
1106	SDG&E - RFP Proposal Creation Duration	29 days	Thu 3/21/24	Tue 4/30/24	
1107	SDG&E - RFP Evaluation	23 days	Mon 5/6/24	Wed 6/5/24	
1108	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/18/24	Tue 6/18/24	
1109	SDG&E - Selection Review with EE PRG	7 days	Thu 6/20/24	Fri 6/28/24	
1110	SDG&E - Contract Negotiation and Development	61 days	Wed 7/31/24	Wed 10/23/24	
1111	SDG&E - Contract Review with EE PRG	4 days	Tue 11/12/24	Fri 11/15/24	
1112	SDG&E - Final Award and Contract Signed	1 day	Tue 12/17/24	Tue 12/17/24	
1113	SDG&E - Submit Advice Letter	1 day	Thu 1/16/25	Thu 1/16/25	
1114	SDG&E - Advice Letter Approved	1 day	Thu 2/20/25	Thu 2/20/25	
1115	SDG&E - Implementation Plan	43 days	Thu 2/20/25	Mon 4/21/25	
1116	*SDG&E - Market Access Program (MAP)	326 days	Wed 3/13/24	Wed 6/11/25	
1117	SDG&E - RFP Preparation	38 days	Wed 3/13/24	Fri 5/3/24	
1118	SDG&E - RFP Release	1 day	Tue 5/7/24	Tue 5/7/24	
1119	SDG&E - RFP Proposal Creation Duration	31 days	Tue 5/7/24	Tue 6/18/24	
1120	SDG&E - RFP Evaluation	43 days	Wed 6/19/24	Fri 8/16/24	
1121	SDG&E - Selection Review with EE PRG	7 days	Thu 9/5/24	Fri 9/13/24	
1122	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/17/24	Tue 9/17/24	
1123	SDG&E - Contract Negotiation and Development	60 days	Fri 9/27/24	Thu 12/19/24	
1124	SDG&E - Contract Review with EE PRG	3 days	Tue 12/10/24	Thu 12/12/24	
1125	SDG&E - Final Award and Contract Signed	1 day	Fri 1/31/25	Fri 1/31/25	
1126	SDG&E - Submit Advice Letter	1 day	Wed 3/12/25	Wed 3/12/25	
1127	SDG&E - Advice Letter Approved	1 day	Fri 4/11/25	Fri 4/11/25	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1128	SDG&E - Implementation Plan	44 days	Fri 4/11/25	Wed 6/11/25	
1129	Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change				
1130					
1131	PG&E - Local Government Partnerships (non-resource programs) Solicitation	376 days?	Fri 3/22/19	Fri 8/28/20	
1132	PG&E - RFA Preparation	42 days	Fri 3/22/19	Mon 5/20/19	
1133	PG&E - RFA Release	1 day	Thu 5/23/19	Thu 5/23/19	
1134	PG&E - RFA Abstract Creation Duration	22 days	Thu 5/23/19	Fri 6/21/19	
1135	PG&E - RFA Evaluation	15 days	Mon 6/24/19	Fri 7/12/19	
1136	PG&E - RFA Review with EE PRG	4 days	Tue 7/23/19	Fri 7/26/19	
1137	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/5/19	Fri 8/9/19	
1138	PG&E - RFP Preparation	45 days	Tue 8/27/19	Mon 10/28/19	
1139	PG&E - RFP Release	1 day	Mon 11/4/19	Mon 11/4/19	
1140	PG&E - RFP Proposal Creation Duration	33 days	Mon 11/4/19	Wed 12/18/19	
1141	PG&E - RFP Evaluation	18 days	Mon 1/6/20	Wed 1/29/20	
1142	PG&E - RFP Review with EE PRG	4 days	Tue 2/25/20	Fri 2/28/20	
1143	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/2/20	Fri 3/6/20	
1144	PG&E - Contract Negotiation and Development	58 days	Fri 2/28/20	Tue 5/19/20	
1145	PG&E - Contract Review with EE PRG	7 days	Tue 5/26/20	Wed 6/3/20	
1146	PG&E - Final Award and Contract Signed	22 days	Fri 5/29/20	Mon 6/29/20	
1147	PG&E - Submit Advice Letter		N/A	N/A	
1148	PG&E - Advice Letter Approved				
1149	PG&E - Implementation Plan	24 days	Tue 7/28/20	Fri 8/28/20	
1150	PG&E - Statewide Codes & Standards (RFP only) Solicitation	221 days?	Mon 7/8/19	Mon 5/11/20	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1151	PG&E - RFA Preparation		N/A	N/A	
1152	PG&E - RFA Release		N/A	N/A	
1153	PG&E - RFA Abstract Creation Duration		N/A	N/A	
1154	PG&E - RFA Evaluation		N/A	N/A	
1155	PG&E - RFA Review with EE PRG		N/A	N/A	
1156	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A	
1157	PG&E - RFP Preparation	36 days	Mon 7/8/19	Mon 8/26/19	
1158	PG&E - RFP Release	1 day	Tue 9/10/19	Tue 9/10/19	
1159	PG&E - RFP Proposal Creation Duration	24 days	Tue 9/10/19	Fri 10/11/19	
1160	PG&E - RFP Evaluation	10 days	Mon 10/14/19	Fri 10/25/19	
1161	PG&E - RFP Review with EE PRG	4 days	Thu 11/21/19	Tue 11/26/19	
1162	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 11/27/19	Fri 11/29/19	
1163	PG&E - Contract Negotiation and Development	35 days	Mon 12/2/19	Fri 1/17/20	
1164	PG&E - Contract Review with EE PRG	4 days	Tue 1/21/20	Fri 1/24/20	
1165	PG&E - Final Award and Contract Signed	32 days	Wed 1/29/20	Thu 3/12/20	
1166	PG&E - Submit Advice Letter		N/A	N/A	
1167	PG&E - Advice Letter Approved				
1168	PG&E - Implementation Plan	32 days	Fri 3/27/20	Mon 5/11/20	
1169	PG&E - Local Multi-Sector (40% outsource) Solicitation	251 days?	Tue 4/28/20	Tue 4/13/21	
1170	PG&E - RFA Preparation		N/A	N/A	
1171	PG&E - RFA Release		N/A	N/A	
1172	PG&E - RFA Abstract Creation Duration		N/A	N/A	
1173	PG&E - RFA Evaluation		N/A	N/A	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1174	PG&E - RFA Review with EE PRG		N/A	N/A	
1175	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A	
1176	PG&E - RFP Preparation		N/A	N/A	
1177	PG&E - RFP Release		N/A	N/A	
1178	PG&E - RFP Proposal Creation Duration		N/A	N/A	
1179	PG&E - RFP Evaluation		N/A	N/A	
1180	PG&E - RFP Review with EE PRG	4 days	Tue 4/28/20	Fri 5/1/20	
1181	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder				
1182	PG&E - Contract Negotiation and Development	81 days	Thu 7/2/20	Thu 10/22/20	
1183	PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20	
1184	PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20	
1185	PG&E - Submit Advice Letter	1 day	Wed 1/13/21	Wed 1/13/21	
1186	PG&E - Advice Letter Approved	1 day?	Fri 2/12/21	Fri 2/12/21	
1187	PG&E - Implementation Plan	43 days	Sat 2/13/21	Tue 4/13/21	
1188	PG&E - Statewide New Constructions (Non-Residential) Solicitation	591 days	Mon 3/25/19	Sun 6/27/21	
1189	PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19	
1190	PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19	
1191	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19	
1192	PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19	
1193	PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19	
1194	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19	
1195	PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20	
1196	PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1197	PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20	
1198	PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20	
1199	PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20	
1200	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20	
1201	PG&E - Contract Negotiation and Development	49 days	Mon 8/17/20	Thu 10/22/20	
1202	PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20	
1203	PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20	
1204	PG&E - Submit Advice Letter	1 day	Fri 2/19/21	Fri 2/19/21	
1205	PG&E - Advice Letter Approved	1 day	Wed 4/28/21	Wed 4/28/21	
1206	PG&E - Implementation Plan	43 days	Thu 4/29/21	Sun 6/27/21	
1207	PG&E - Statewide New Construction (Residential) Solicitation	640 days?	Mon 3/25/19	Fri 9/3/21	
1208	PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19	
1209	PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19	
1210	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19	
1211	PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19	
1212	PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19	
1213	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19	
1214	PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20	
1215	PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20	
1216	PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20	
1217	PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20	
1218	PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20	
1219	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1220	PG&E - Contract Negotiation and Development	177 days	Mon 8/17/20	Tue 4/20/21	
1221	PG&E - Contract Review with EE PRG	16 days	Thu 4/22/21	Thu 5/13/21	
1222	PG&E - Final Award and Contract Signed	32 days	Sat 5/15/21	Mon 6/28/21	
1223	PG&E - Submit Advice Letter	1 day	Mon 7/12/21	Mon 7/12/21	
1224	PG&E - Advice Letter Approved (all electric)	1 day	Wed 8/11/21	Wed 8/11/21	
1225	PG&E - Advice Letter Approved (mixed fuel)	1 day	Wed 9/15/21	Wed 9/15/21	
1226	PG&E - Implementation Plan (all electric)	43 days	Thu 8/12/21	Mon 10/11/21	
1227	PG&E - Implementation Plan (mixed fuel)	43 days	Thu 9/16/21	Sun 11/14/21	
1228	PG&E - Statewide WE&T Career Connections Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21	
1229	PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20	
1230	PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20	
1231	PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20	
1232	PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20	
1233	PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20	
1234	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20	
1235	PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20	
1236	PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20	
1237	PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20	
1238	PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20	
1239	PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20	
1240	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20	
1241	PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21	
1242	PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1243	PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21	
1244	PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21	
1245	PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21	
1246	PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21	
1247	PG&E - Statewide WE&T Career and Workforce Readiness Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21	
1248	PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20	
1249	PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20	
1250	PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20	
1251	PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20	
1252	PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20	
1253	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20	
1254	PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20	
1255	PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20	
1256	PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20	
1257	PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20	
1258	PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20	
1259	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20	
1260	PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21	
1261	PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21	
1262	PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21	
1263	PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21	
1264	PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21	
1265	PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
1266	PG&E - Statewide State of CA (Dept. of Corrections) Solicitation	348 days?	Sun 3/1/20	Tue 6/29/21	
1267	PG&E - RFA Preparation	46 days	Sun 3/1/20	Fri 5/1/20	
1268	PG&E - RFA Release	1 day	Wed 5/13/20	Wed 5/13/20	
1269	PG&E - RFA Abstract Creation Duration	31 days	Wed 5/13/20	Wed 6/24/20	
1270	PG&E - RFA Evaluation	15 days	Mon 6/29/20	Fri 7/17/20	
1271	PG&E - RFA Review with EE PRG	5 days	Tue 7/28/20	Mon 8/3/20	
1272	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/3/20	Fri 8/7/20	
1273	PG&E - RFP Preparation	20 days	Mon 8/3/20	Fri 8/28/20	
1274	PG&E - RFP Release	1 day	Wed 9/9/20	Wed 9/9/20	
1275	PG&E - RFP Proposal Creation Duration	31 days	Wed 9/9/20	Wed 10/21/20	
1276	PG&E - RFP Evaluation	31 days	Fri 10/23/20	Fri 12/4/20	
1277	PG&E - RFP Review with EE PRG	6 days	Tue 12/22/20	Tue 12/29/20	
1278	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 1/6/21	Fri 1/8/21	
1279	PG&E - Contract Negotiation and Development	65 days	Wed 1/20/21	Tue 4/20/21	
1280	PG&E - Contract Review with EE PRG	7 days	Thu 4/22/21	Fri 4/30/21	
1281	PG&E - Final Award and Contract Signed	22 days	Sat 5/1/21	Mon 5/31/21	
1282	PG&E - Submit Advice Letter	1 day	Thu 6/24/21	Thu 6/24/21	
1283	PG&E - Advice Letter Approved	1 day	Wed 7/28/21	Wed 7/28/21	
1284	PG&E - Implementation Plan	43 days	Thu 7/29/21	Sun 9/26/21	
1285	PG&E - Local (Micro and Small Business Equity Program) Solicitation	403 days?	Tue 6/1/21	Thu 12/15/22	
1286	PG&E - RFA Preparation	38 days	Tue 6/1/21	Thu 7/22/21	
1287	PG&E - RFA Release	1 day	Tue 9/7/21	Tue 9/7/21	
1288	PG&E - RFA Abstract Creation Duration	34 days	Wed 9/8/21	Mon 10/25/21	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
1289	PG&E - RFA Evaluation	18 days	Tue 10/26/21	Thu 11/18/21	
1290	PG&E - RFP Release	1 day	Wed 12/8/21	Wed 12/8/21	
1291	PG&E - RFP Proposal Creation Duration	46 days	Wed 12/8/21	Wed 2/9/22	
1292	PG&E - RFP Evaluation	21 days	Thu 2/10/22	Thu 3/10/22	
1293	PG&E - RFP Review with EE PRG	6 days	Thu 3/17/22	Thu 3/24/22	
1294	PG&E - RFP Estimated Bidder Notification	1 day	Wed 3/30/22	Wed 3/30/22	
1295	PG&E - Contract Negotiation and Development	71 days	Thu 4/7/22	Thu 7/14/22	
1296	PG&E - Contract Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22	
1297	PG&E - Final Award and Contract Signed	45 days	Mon 8/8/22	Fri 10/7/22	
1298	PG&E - Submit Advice Letter	1 day	Wed 10/12/22	Wed 10/12/22	
1299	PG&E - Advice Letter Approved	1 day	Fri 11/11/22	Fri 11/11/22	
1300	PG&E - Implementation Plan	31 days	Fri 11/11/22	Fri 12/23/22	
1301	PG&E - Local (C&S Compliance Improvement) Solicitation	436 days	Tue 3/1/22	Tue 10/31/23	
1302	PG&E - RFA Preparation	34 days	Tue 3/1/22	Fri 4/15/22	
1303	PG&E - RFA Release	1 day	Mon 5/16/22	Mon 5/16/22	
1304	PG&E - RFA Abstract Creation Duration	25 days	Tue 5/17/22	Mon 6/20/22	
1305	PG&E - RFA Evaluation	28 days	Tue 6/21/22	Thu 7/28/22	
1306	PG&E - RFA Review with EE PRG	1 day	Tue 8/9/22	Tue 8/9/22	
1307	PG&E - RFA Estimated Bidder Notification	1 day	Wed 8/31/22	Wed 8/31/22	
1308	PG&E - RFP Preparation	24 days	Mon 8/1/22	Thu 9/1/22	
1309	PG&E - RFP Release	1 day	Tue 9/13/22	Tue 9/13/22	
1310	PG&E - RFP Proposal Creation Duration	26 days	Tue 9/13/22	Tue 10/18/22	
1311	PG&E - RFP Evaluation	45 days	Wed 10/19/22	Tue 12/20/22	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
1312	PG&E - RFP Review with EE PRG	1 day	Tue 1/24/23	Tue 1/24/23	
1313	PG&E - RFP Estimated Bidder Notification	1 day	Fri 2/10/23	Fri 2/10/23	
1314	PG&E - Contract Negotiation and Development	47 days	Mon 2/13/23	Tue 4/18/23	
1315	PG&E - Contract Review with EE PRG	26 days	Tue 5/23/23	Tue 6/27/23	
1316	PG&E - Final Award and Contract Signed	48 days	Wed 6/28/23	Fri 9/1/23	
1317	PG&E - Submit Advice Letter		N/A		
1318	PG&E - Advice Letter Approved		N/A		
1319	PG&E - Implementation Plan	1 day	Tue 10/31/23	Tue 10/31/23	
1320	PG&E - Residential Electrification Equity Program Solicitation	595 days	Mon 8/1/22	Fri 11/8/24	
1321	PG&E - RFA Preparation	59 days	Mon 8/1/22	Thu 10/20/22	
1322	PG&E - RFA Release	1 day	Tue 11/29/22	Tue 11/29/22	
1323	PG&E - RFA Abstract Creation Duration	46 days	Tue 11/29/22	Tue 1/31/23	
1324	PG&E - RFA Evaluation	17 days	Sun 2/5/23	Sun 2/26/23	
1325	PG&E - RFA Review with EE PRG	6 days	Mon 2/27/23	Mon 3/6/23	
1326	PG&E - RFA Estimated Bidder Notification	3 days	Mon 3/6/23	Wed 3/8/23	
1327	PG&E - RFP Preparation	46 days	Mon 1/9/23	Mon 3/13/23	
1328	PG&E - RFP Release	1 day	Tue 4/11/23	Tue 4/11/23	
1329	PG&E - RFP Proposal Creation Duration	26 days	Tue 4/11/23	Tue 5/16/23	
1330	PG&E - RFP Evaluation	18 days	Fri 5/19/23	Tue 6/13/23	
1331	PG&E - RFP Review with EE PRG	1 day	Tue 6/27/23	Tue 6/27/23	
1332	PG&E - RFP Estimated Bidder Notification	1 day	Tue 7/11/23	Tue 7/11/23	
1333	PG&E - Contract Negotiation and Development	233 days	Tue 8/1/23	Thu 6/20/24	
1334	PG&E - Contract Review with EE PRG	8 days	Fri 6/21/24	Tue 7/2/24	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1335	PG&E - Final Award and Contract Signed	21 days	Fri 7/5/24	Fri 8/2/24	
1336	PG&E - Submit Advice Letter	1 day	Fri 8/9/24	Fri 8/9/24	
1337	PG&E - Advice Letter Approved	1 day	Mon 9/9/24	Mon 9/9/24	
1338	PG&E - Implementation Plan	1 day	Fri 11/8/24	Fri 11/8/24	
1339	PG&E - Statewide C&S Advocacy Solicitation	641 days	Tue 2/1/22	Tue 7/16/24	
1340	PG&E - RFA Preparation	54 days	Tue 2/1/22	Fri 4/15/22	
1341	PG&E - RFA Release	1 day	Mon 5/30/22	Mon 5/30/22	
1342	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/31/22	Fri 7/1/22	
1343	PG&E - RFA Evaluation	14 days	Fri 7/1/22	Wed 7/20/22	
1344	PG&E - RFA Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22	
1345	PG&E - RFA Estimated Bidder Notification	1 day	Mon 8/1/22	Mon 8/1/22	
1346	PG&E - RFP Preparation	36 days	Fri 4/1/22	Fri 5/20/22	
1347	PG&E - RFP Release	1 day	Tue 6/7/22	Tue 6/7/22	
1348	PG&E - RFP Proposal Creation Duration	31 days	Tue 6/7/22	Tue 7/19/22	
1349	PG&E - RFP Evaluation	50 days	Wed 7/20/22	Tue 9/27/22	
1350	PG&E - RFP Review with EE PRG	1 day	Wed 10/5/22	Wed 10/5/22	
1351	PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/24/22	Mon 10/24/22	
1352	PG&E - Contract Negotiation and Development	73 days	Mon 11/14/22	Wed 2/22/23	
1353	PG&E - Contract Review with EE PRG - Wave 1	1 day	Tue 4/25/23	Tue 4/25/23	
1354	PG&E - Final Award and Contract Signed	18 days	Mon 7/17/23	Wed 8/9/23	
1355	PG&E - Submit Advice Letter (wave 1)	1 day	Thu 9/21/23	Thu 9/21/23	
1356	PG&E - Advice Letter Approved	1 day	Wed 10/25/23	Wed 10/25/23	
1357	PG&E - Implementation Plan	1 day	Thu 12/7/23	Thu 12/7/23	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1358	PG&E - Contract Review with EE PRG - Wave 2	1 day	Wed 12/20/23	Wed 12/20/23	
1359	PG&E - Final Award and Contract Signed	1 day	Fri 3/29/24	Fri 3/29/24	
1360	PG&E - Submit Advice Letter	1 day	Wed 4/17/24	Wed 4/17/24	
1361	PG&E - Advice Letter Approved	1 day	Fri 5/17/24	Fri 5/17/24	
1362	PG&E - Implementation Plan	1 day	Tue 7/16/24	Tue 7/16/24	
1363	PG&E - Zonal Electrification Solicitation	495 days	Thu 12/1/22	Wed 10/23/24	
1364	PG&E - RFP Preparation	88 days	Thu 12/1/22	Mon 4/3/23	
1365	PG&E - RFP Release	1 day	Tue 4/18/23	Tue 4/18/23	
1366	PG&E - RFP Proposal Creation Duration	53 days	Tue 4/18/23	Thu 6/29/23	
1367	PG&E - RFP Evaluation (including interviews)	40 days	Mon 7/10/23	Fri 9/1/23	
1368	PG&E - RFP Review with EE PRG	1 day	Tue 9/26/23	Tue 9/26/23	
1369	PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/2/23	Mon 10/2/23	
1370	PG&E - Contract Negotiation and Development	135 days	Mon 10/9/23	Fri 4/12/24	
1371	PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24	
1372	PG&E - Final Award and Contract Signed	43 days	Wed 5/1/24	Fri 6/28/24	
1373	PG&E - Submit Advice Letter	1 day	Wed 7/3/24	Wed 7/3/24	
1374	PG&E - Advice Letter Approved	1 day	Wed 8/28/24	Wed 8/28/24	
1375	PG&E - Implementation Plan	1 day	Wed 10/23/24	Wed 10/23/24	
1376	PG&E - Residential Whole Home Load Management RFP	453 days	Tue 8/15/23	Thu 5/8/25	
1377	PG&E - RFP Preparation	1 day	Tue 8/15/23	Tue 8/15/23	
1378	PG&E - RFP Release	1 day	Tue 8/15/23	Tue 8/15/23	
1379	PG&E - RFP Proposal Creation Duration	51 days	Tue 8/15/23	Tue 10/24/23	
1380	PG&E - RFP Evaluation	36 days	Thu 10/26/23	Thu 12/14/23	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1381	PG&E - RFP Review with EE PRG	1 day	Fri 2/16/24	Fri 2/16/24	
1382	PG&E - RFP Estimated Bidder Notification	1 day	Tue 2/27/24	Tue 2/27/24	
1383	PG&E - Contract Negotiation and Development	155 days	Wed 3/13/24	Tue 10/15/24	
1384	PG&E - Contract Review with EE PRG	8 days	Tue 11/5/24	Thu 11/14/24	
1385	PG&E - Final Award and Contract Signed	53 days	Thu 11/14/24	Mon 1/27/25	
1386	PG&E - Submit Advice Letter	1 day	Fri 2/7/25	Fri 2/7/25	
1387	PG&E - Advice Letter Approved	1 day	Mon 3/10/25	Mon 3/10/25	
1388	PG&E - Implementation Plan	1 day	Thu 5/8/25	Thu 5/8/25	
1389	PG&E - 2024 Summer Reliability Platform Administrator RFP	337 days?	Tue 4/18/23	Wed 7/31/24	
1390	PG&E - RFP Preparation	30 days	Mon 5/1/23	Fri 6/9/23	
1391	PG&E - RFP Release	1 day	Fri 9/1/23	Fri 9/1/23	
1392	PG&E - RFP Proposal Creation Duration	31 days	Fri 9/1/23	Fri 10/13/23	
1393	PG&E - RFP Evaluation	22 days	Tue 10/17/23	Wed 11/15/23	
1394	PG&E - RFP Review with EE PRG	1 day	Tue 11/28/23	Tue 11/28/23	
1395	PG&E - RFP Estimated Bidder Notification	1 day	Tue 12/5/23	Tue 12/5/23	
1396	PG&E - Contract Negotiation and Development	68 days	Mon 1/8/24	Wed 4/10/24	
1397	PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24	
1398	PG&E - Final Award and Contract Signed	22 days	Wed 5/1/24	Thu 5/30/24	
1399	PG&E - Submit Advice Letter	1 day	Fri 5/31/24	Fri 5/31/24	
1400	PG&E - Advice Letter Approved	1 day	Mon 7/1/24	Mon 7/1/24	
1401	PG&E - Implementation Plan	1 day	Wed 7/31/24	Wed 7/31/24	
1402	PG&E - C&S Code Readiness RFP	393 days?	Wed 2/1/23	Fri 8/2/24	
1403	PG&E - RFP Preparation	113 days	Wed 2/1/23	Fri 7/7/23	

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1404	PG&E - RFP Release	1 day	Wed 7/12/23	Wed 7/12/23	
1405	PG&E - RFP Proposal Creation Duration	30 days	Thu 7/13/23	Wed 8/23/23	
1406	PG&E - RFP Evaluation	36 days	Mon 8/28/23	Mon 10/16/23	
1407	PG&E - RFP Review with EE PRG	1 day	Tue 10/24/23	Tue 10/24/23	
1408	PG&E - RFP Estimated Bidder Notification	1 day	Mon 11/6/23	Mon 11/6/23	
1409	PG&E - Contract Negotiation and Development	65 days	Wed 11/15/23	Tue 2/13/24	
1410	PG&E - Contract Review with EE PRG	1 day	Tue 2/27/24	Tue 2/27/24	
1411	PG&E - Final Award and Contract Signed	1 day	Fri 4/12/24	Fri 4/12/24	
1412	PG&E - Submit Advice Letter	1 day	Tue 5/7/24	Tue 5/7/24	
1413	PG&E - Advice Letter Approved	1 day	Thu 6/6/24	Thu 6/6/24	
1414	PG&E - Implementation Plan	1 day	Fri 8/2/24	Fri 8/2/24	
1415	PG&E - Residential Electrification - Single Point of Contact	414 days	Tue 8/1/23	Fri 2/28/25	
1416	PG&E - RFP Preparation	133 days	Tue 8/1/23	Thu 2/1/24	
1417	PG&E - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24	
1418	PG&E - RFP Proposal Creation Duration	33 days	Wed 2/28/24	Fri 4/12/24	
1419	PG&E - RFP Evaluation	66 days	Mon 4/15/24	Mon 7/15/24	
1420	PG&E - RFP Review with EE PRG	6 days	Fri 7/19/24	Fri 7/26/24	
1421	PG&E - RFP Estimated Bidder Notification	1 day	Wed 8/7/24	Wed 8/7/24	
1422	PG&E - Contract Negotiation and Development	62 days			
1423	PG&E - Contract Review with EE PRG	6 days			
1424	PG&E - Final Award and Contract Signed	25 days			
1425	PG&E - Submit Advice Letter	1 day			
1426	PG&E - Advice Letter Approved	1 day			

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	2018 H1
1427	PG&E - Implementation Plan	1 day			
1428	PG&E - Commercial SEM FP	430 days	Thu 8/3/23	Wed 3/26/25	
1429	PG&E - RFP Preparation	16 days	Thu 8/3/23	Thu 8/24/23	
1430	PG&E - RFP Release	1 day	Fri 11/3/23	Fri 11/3/23	
1431	PG&E - RFP Proposal Creation Duration	55 days	Fri 11/3/23	Thu 1/18/24	
1432	PG&E - RFP Evaluation	58 days	Tue 1/23/24	Thu 4/11/24	
1433	PG&E - RFP Review with EE PRG	1 day	Wed 4/17/24	Wed 4/17/24	
1434	PG&E - RFP Estimated Bidder Notification	4 days	Tue 4/23/24	Fri 4/26/24	
1435	PG&E - Contract Negotiation and Development	90 days	Thu 5/2/24	Wed 9/4/24	
1436	PG&E - Contract Review with EE PRG	8 days	Mon 9/16/24	Wed 9/25/24	
1437	PG&E - Final Award and Contract Signed	58 days	Thu 9/26/24	Mon 12/16/24	
1438	PG&E - Submit Advice Letter	1 day	Thu 12/19/24	Thu 12/19/24	
1439	PG&E - Advice Letter Approved	0 days	Thu 1/30/25	Thu 1/30/25	
1440	PG&E - Implementation Plan	1 day	Wed 3/26/25	Wed 3/26/25	
1441	PG&E - SW WE&T Career & Workforce Readiness	580 days	Tue 10/8/24	Mon 12/28/26	
1442	PG&E - RFP Preparation	199 days	Tue 10/8/24	Fri 7/11/25	
1443	PG&E - RFP Release	1 day	Thu 7/17/25	Thu 7/17/25	
1444	PG&E - RFP Proposal Creation Duration	41 days	Thu 7/17/25	Thu 9/11/25	
1445	PG&E - RFP Evaluation	50 days	Mon 9/15/25	Fri 11/21/25	
1446	PG&E - RFP Review with EE PRG	4 days	Fri 12/5/25	Wed 12/10/25	
1447	PG&E - RFP Estimated Bidder Notification	4 days	Wed 12/10/25	Mon 12/15/25	
1448	PG&E - Contract Negotiation and Development	124 days	Wed 1/7/26	Mon 6/29/26	
1449	PG&E - Contract Review with EE PRG	9 days	Wed 7/8/26	Mon 7/20/26	


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1
1450	PG&E - Final Award and Contract Signed	48 days	Mon 7/20/26	Wed 9/23/26	
1451	PG&E - Submit Advice Letter	1 day	Wed 9/30/26	Wed 9/30/26	
1452	PG&E - Advice Letter Approved	1 day	Fri 10/30/26	Fri 10/30/26	
1453	PG&E - Implementation Plan	42 days	Fri 10/30/26	Mon 12/28/26	
1454	PG&E - Statewide HVAC	423 days	Fri 5/2/25	Tue 12/15/26	
1455	PG&E - RFP Preparation	122 days	Fri 5/2/25	Mon 10/20/25	
1456	PG&E - RFP Release	1 day	Wed 10/22/25	Wed 10/22/25	
1457	PG&E - RFP Proposal Creation Duration	41 days	Wed 10/22/25	Wed 12/17/25	
1458	PG&E - RFP Evaluation	32 days	Thu 12/18/25	Fri 1/30/26	
1459	PG&E - RFP Review with EE PRG	1 day	Thu 3/26/26	Thu 3/26/26	
1460	PG&E - RFP Estimated Bidder Notification	1 day	Mon 4/6/26	Mon 4/6/26	
1461	PG&E - Contract Negotiation and Development	53 days	Tue 4/7/26	Thu 6/18/26	
1462	PG&E - Contract Review with EE PRG	1 day	Tue 6/23/26	Tue 6/23/26	
1463	PG&E - Final Award and Contract Signed	1 day	Mon 8/31/26	Mon 8/31/26	
1464	PG&E - Submit Advice Letter	1 day	Tue 9/15/26	Tue 9/15/26	
1465	PG&E - Advice Letter Approved	1 day	Thu 10/15/26	Thu 10/15/26	
1466	PG&E - Implementation Plan	1 day	Tue 12/15/26	Tue 12/15/26	


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

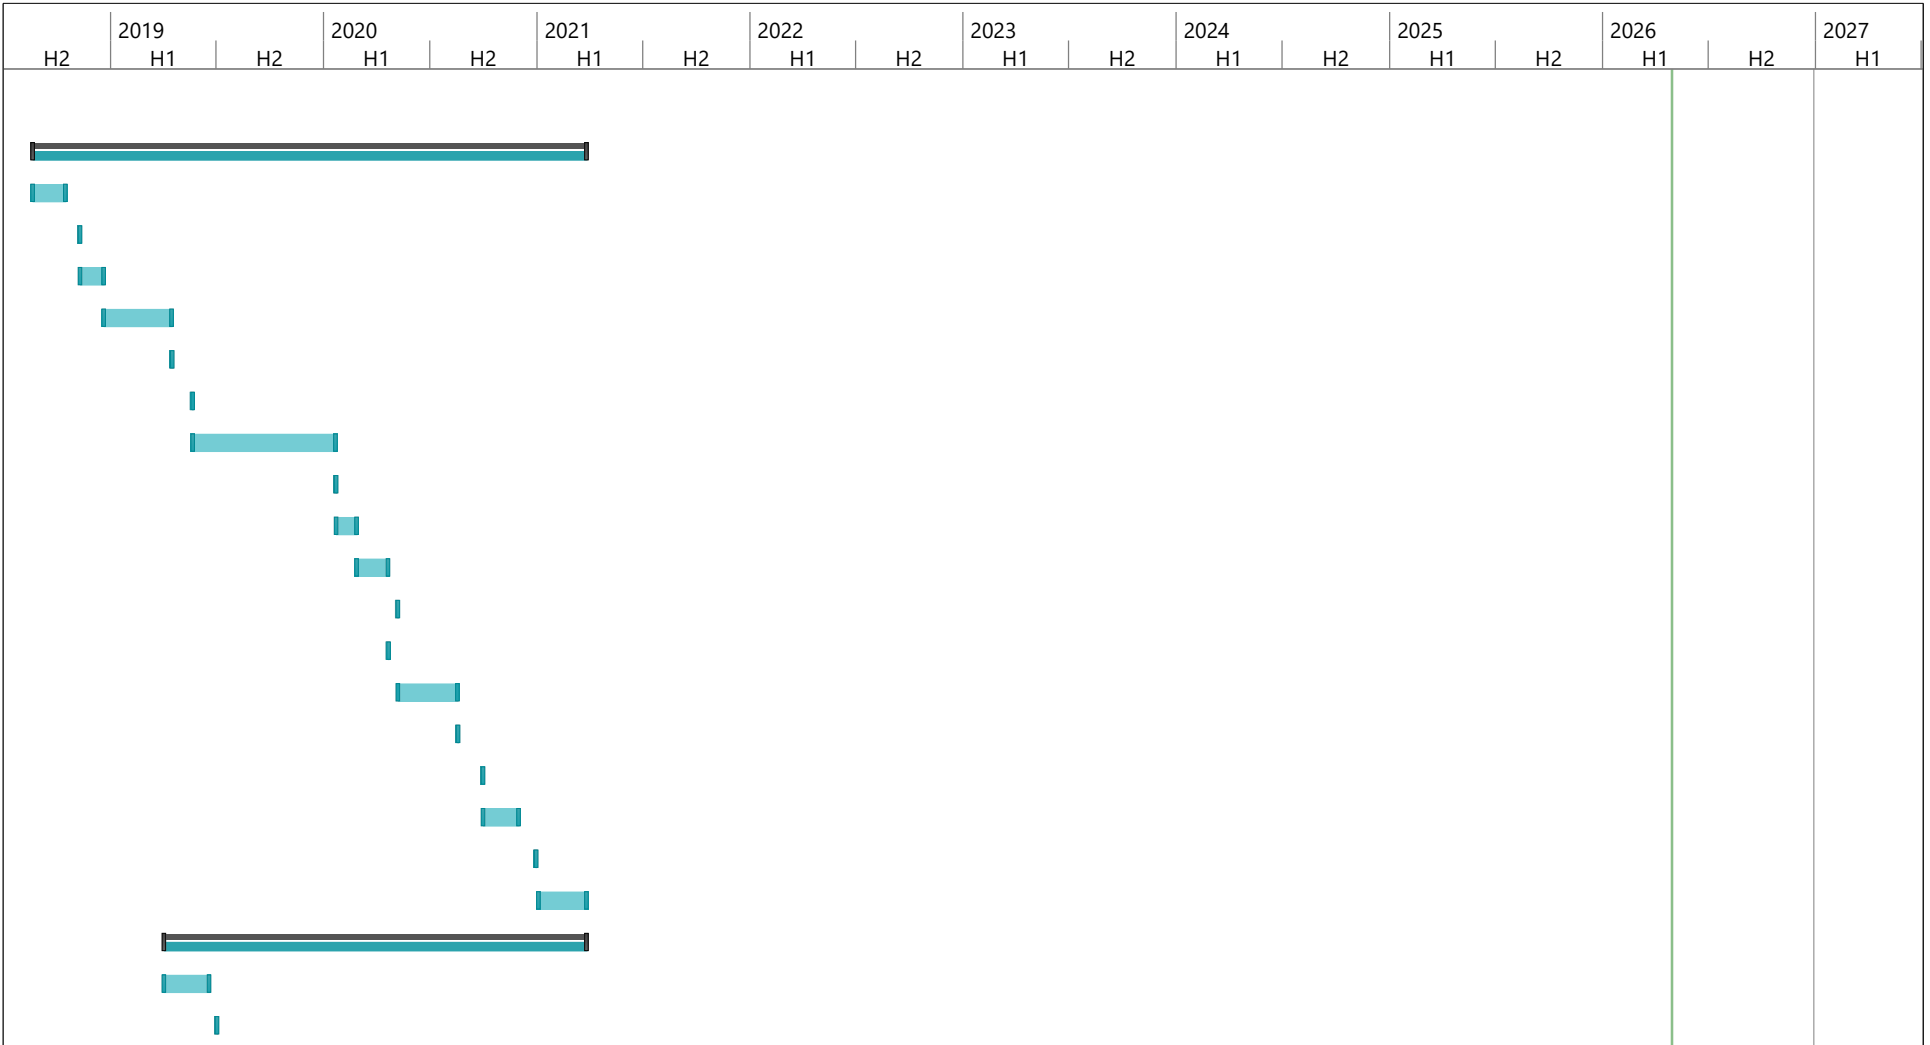


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

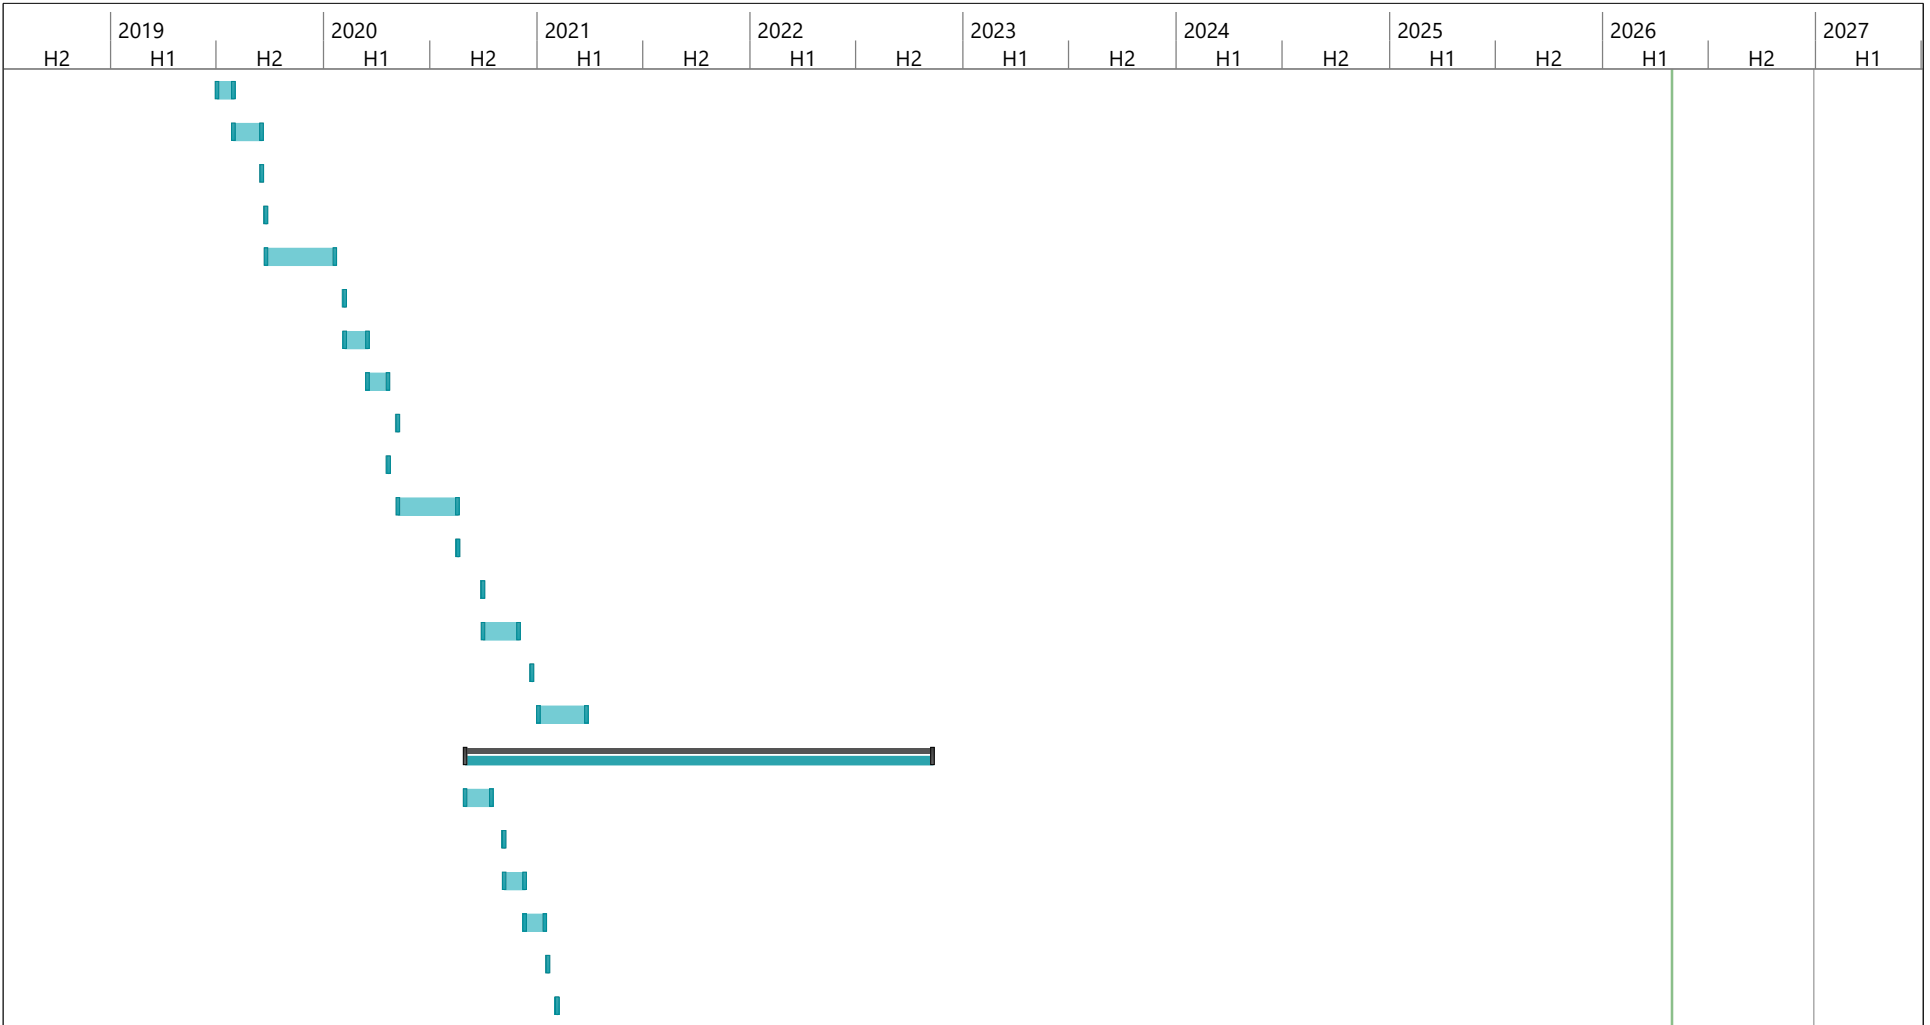


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

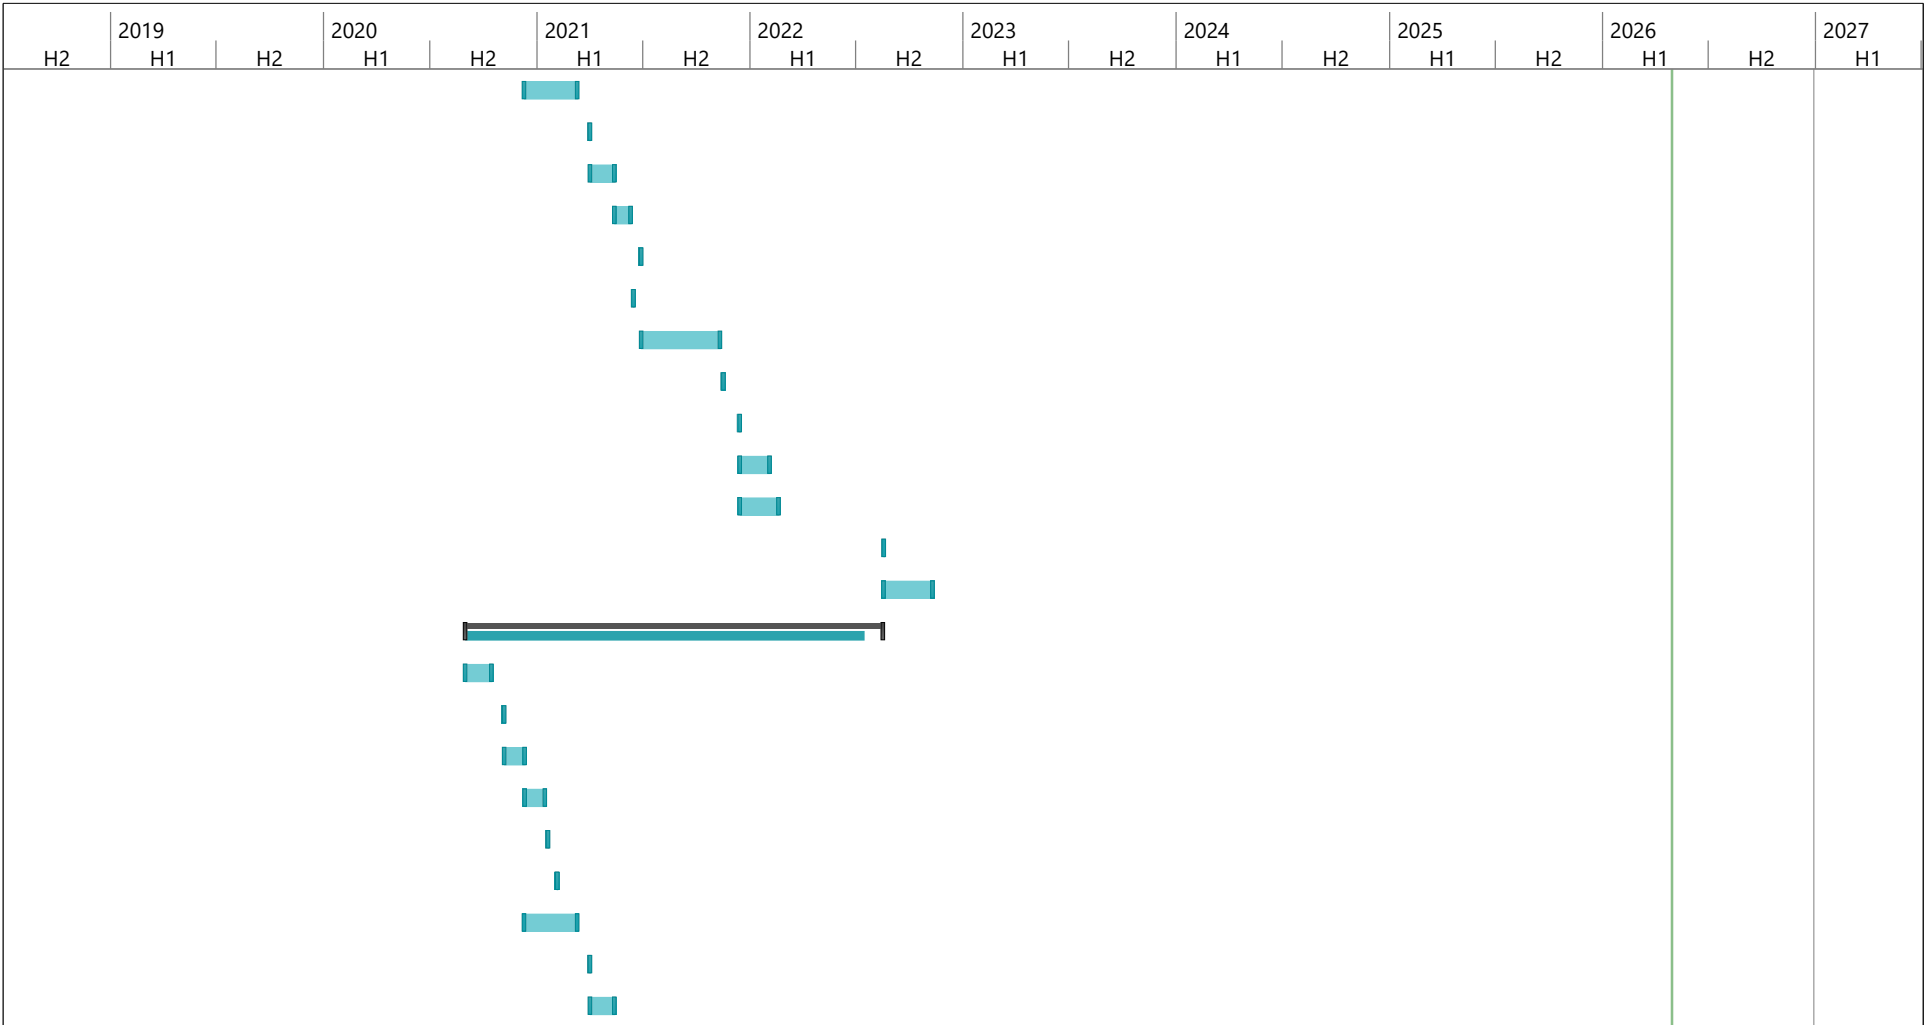


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

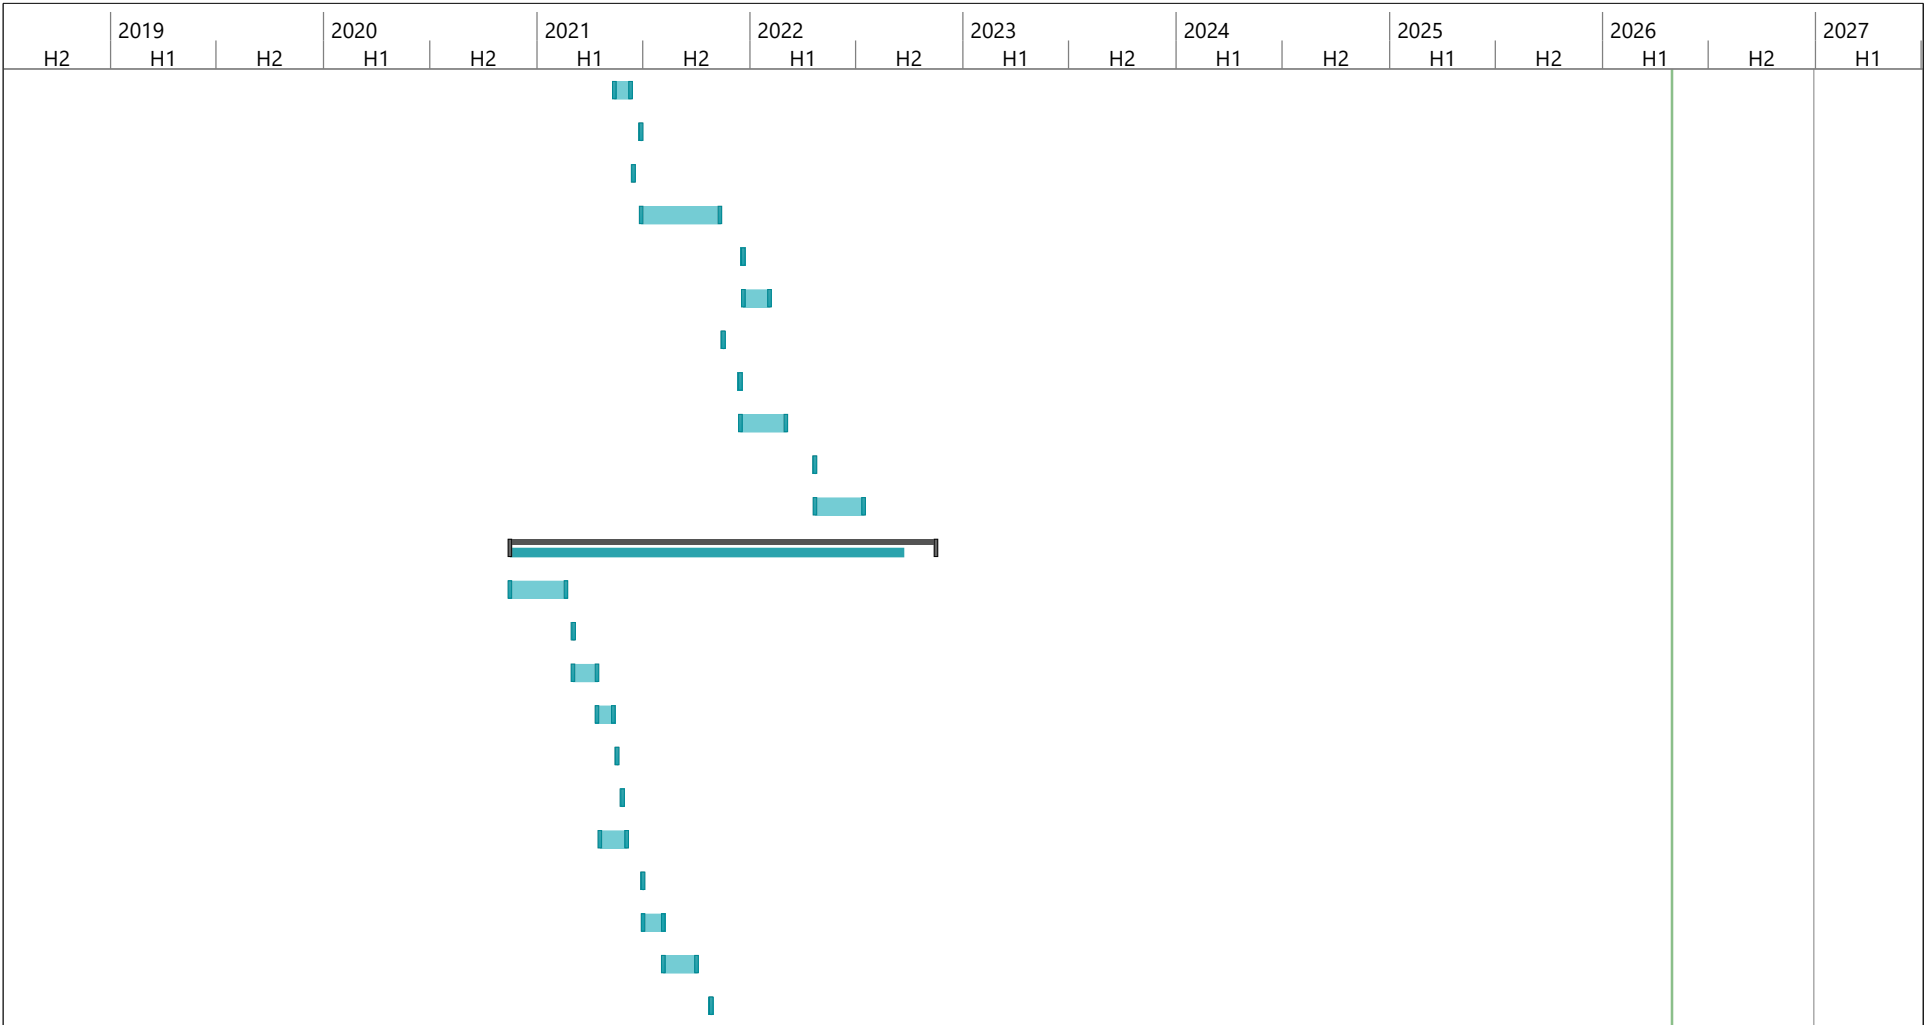


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

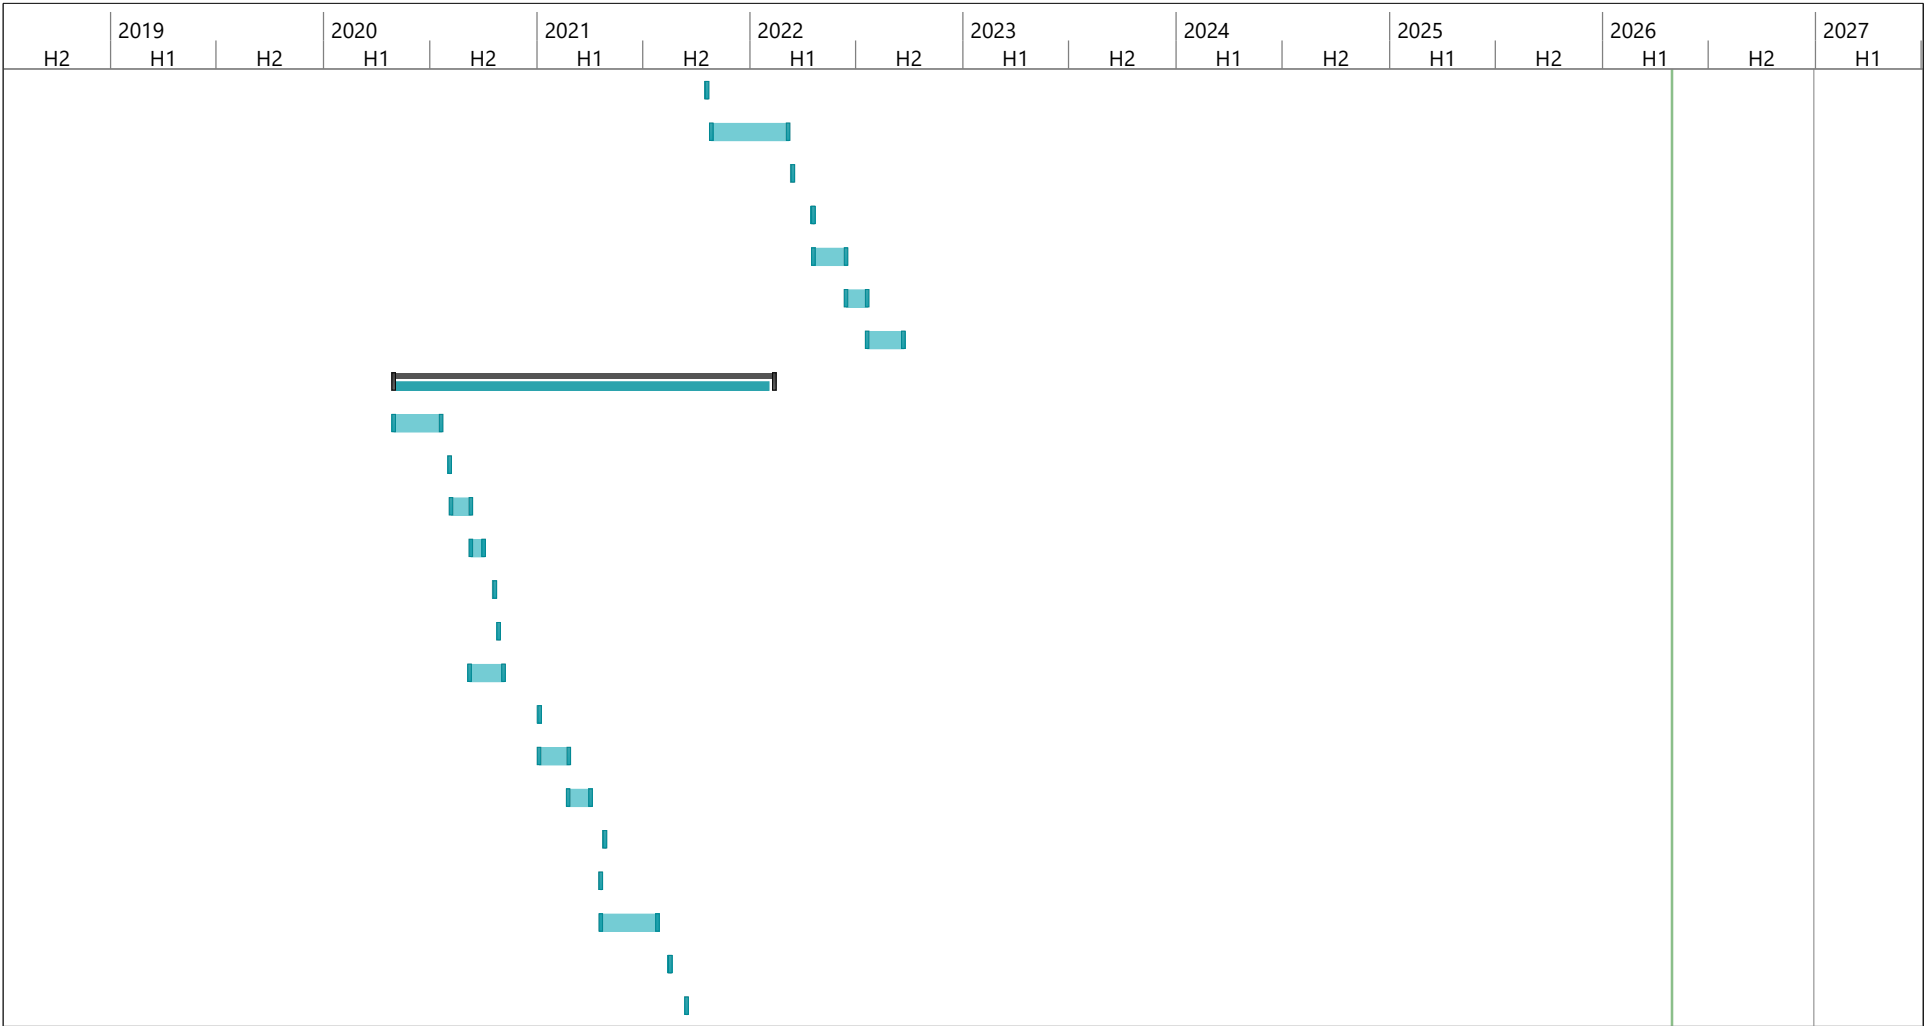


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

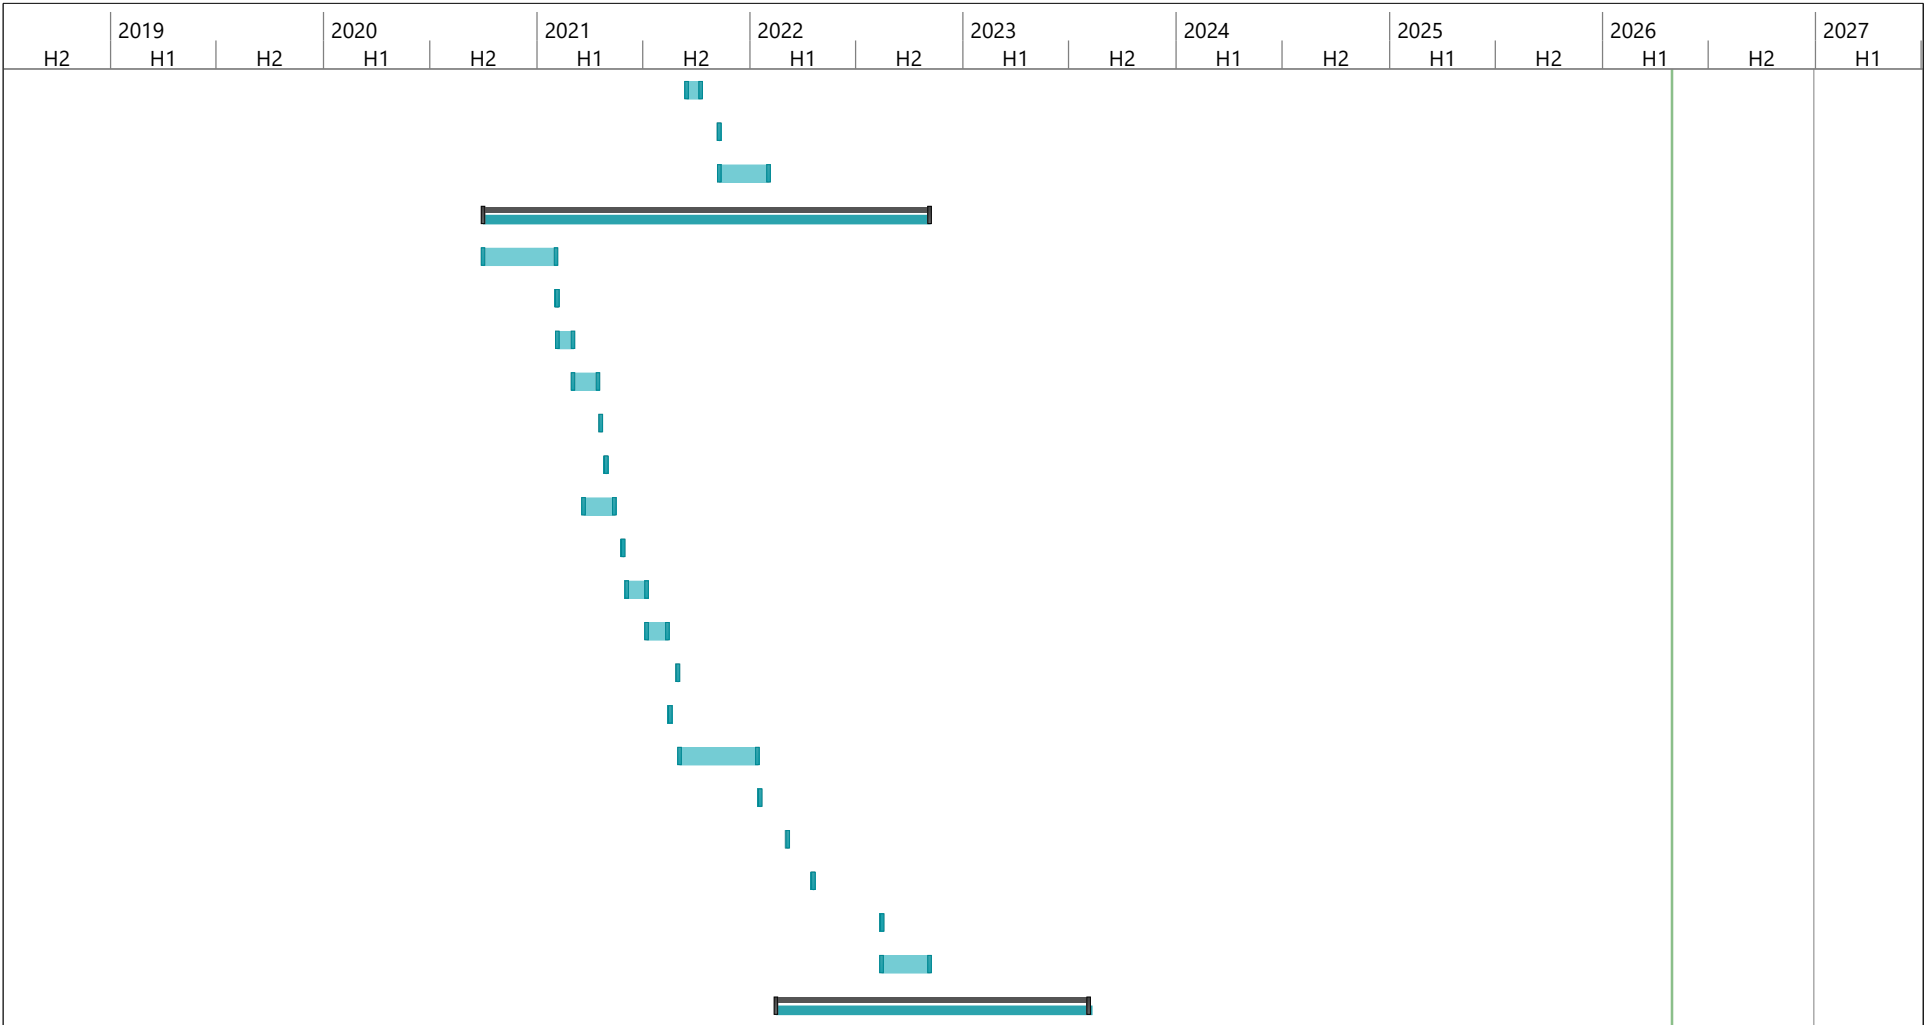


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

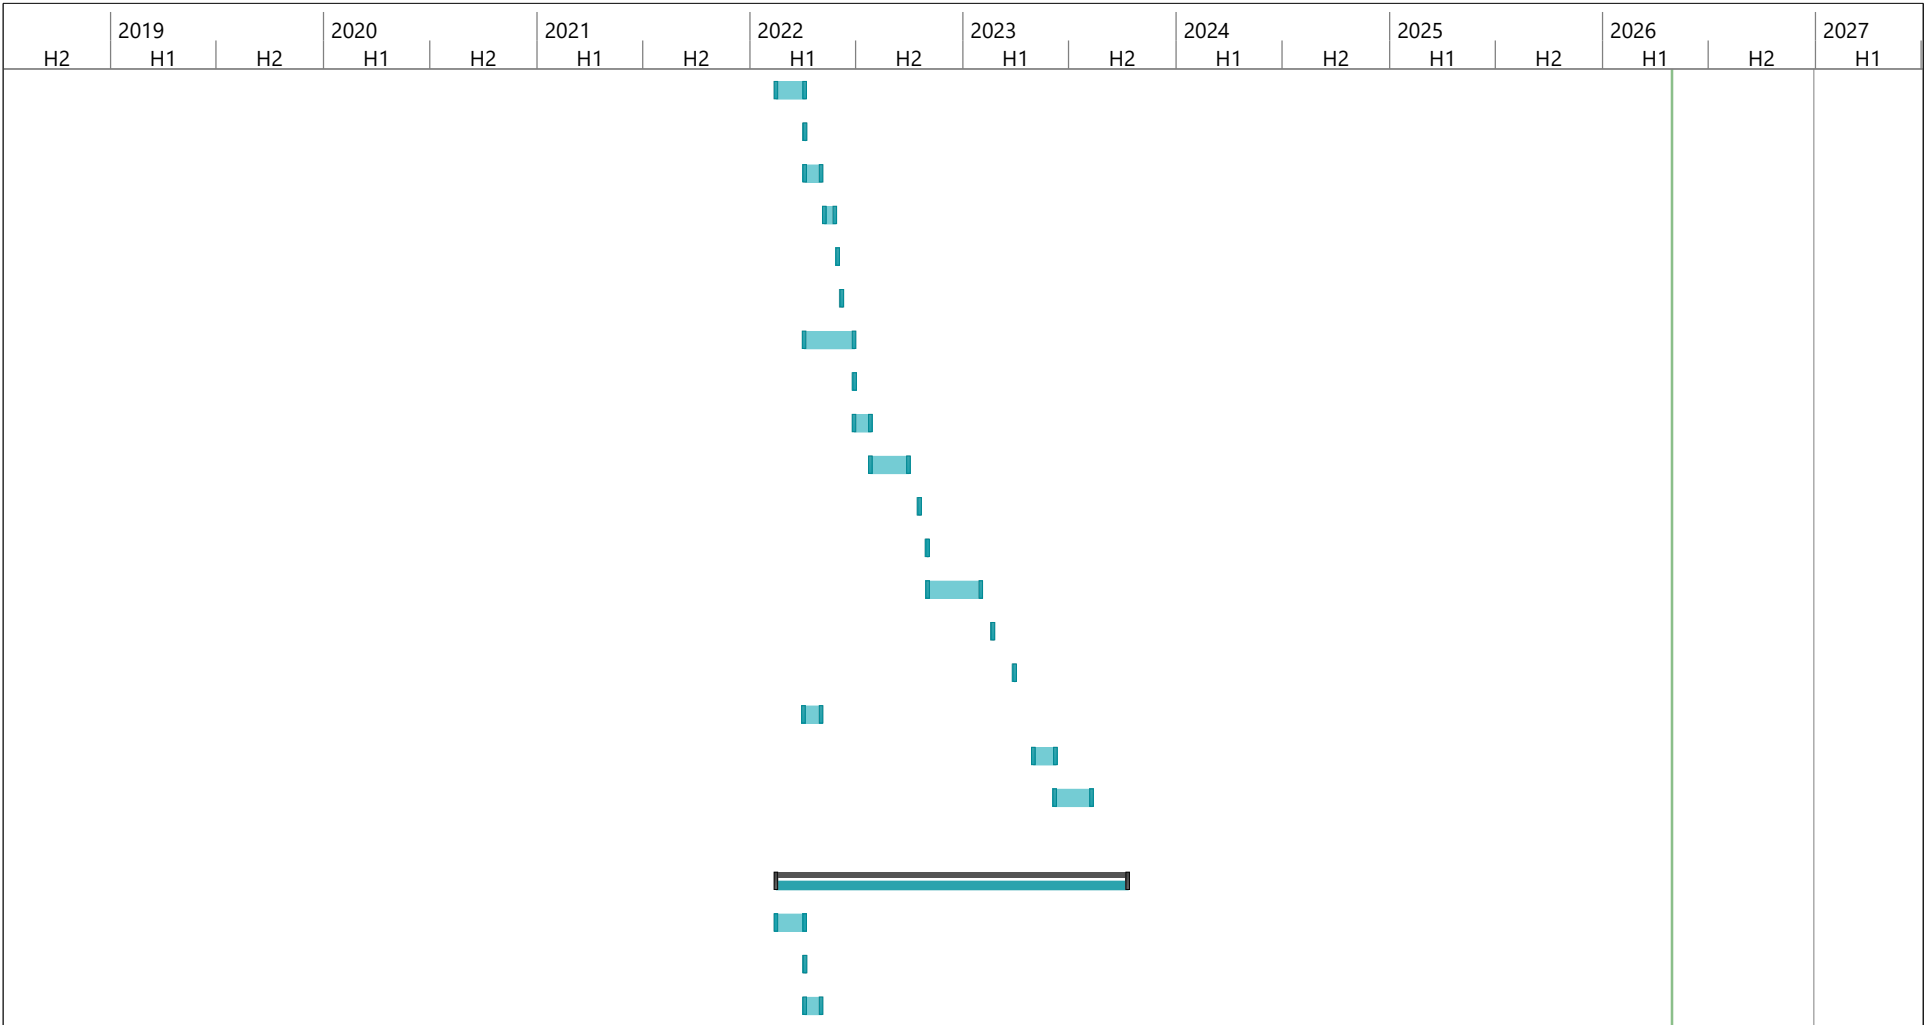


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

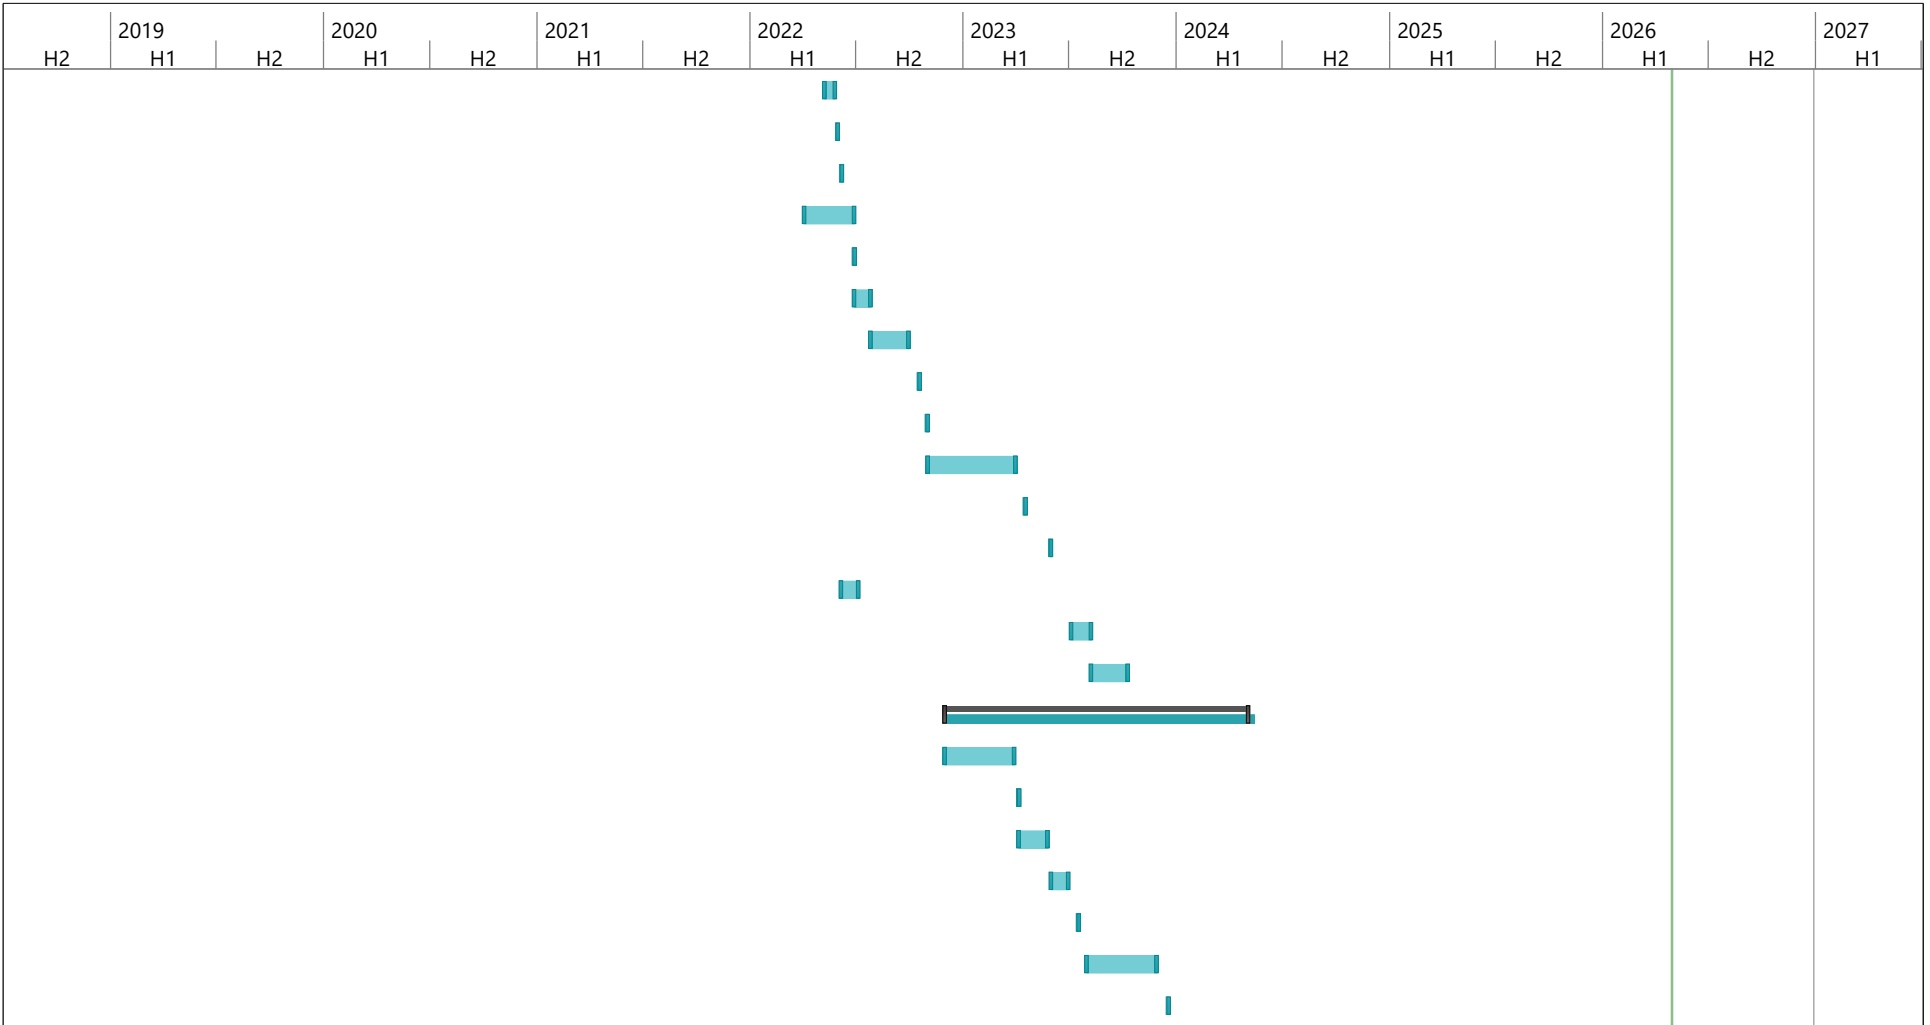


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

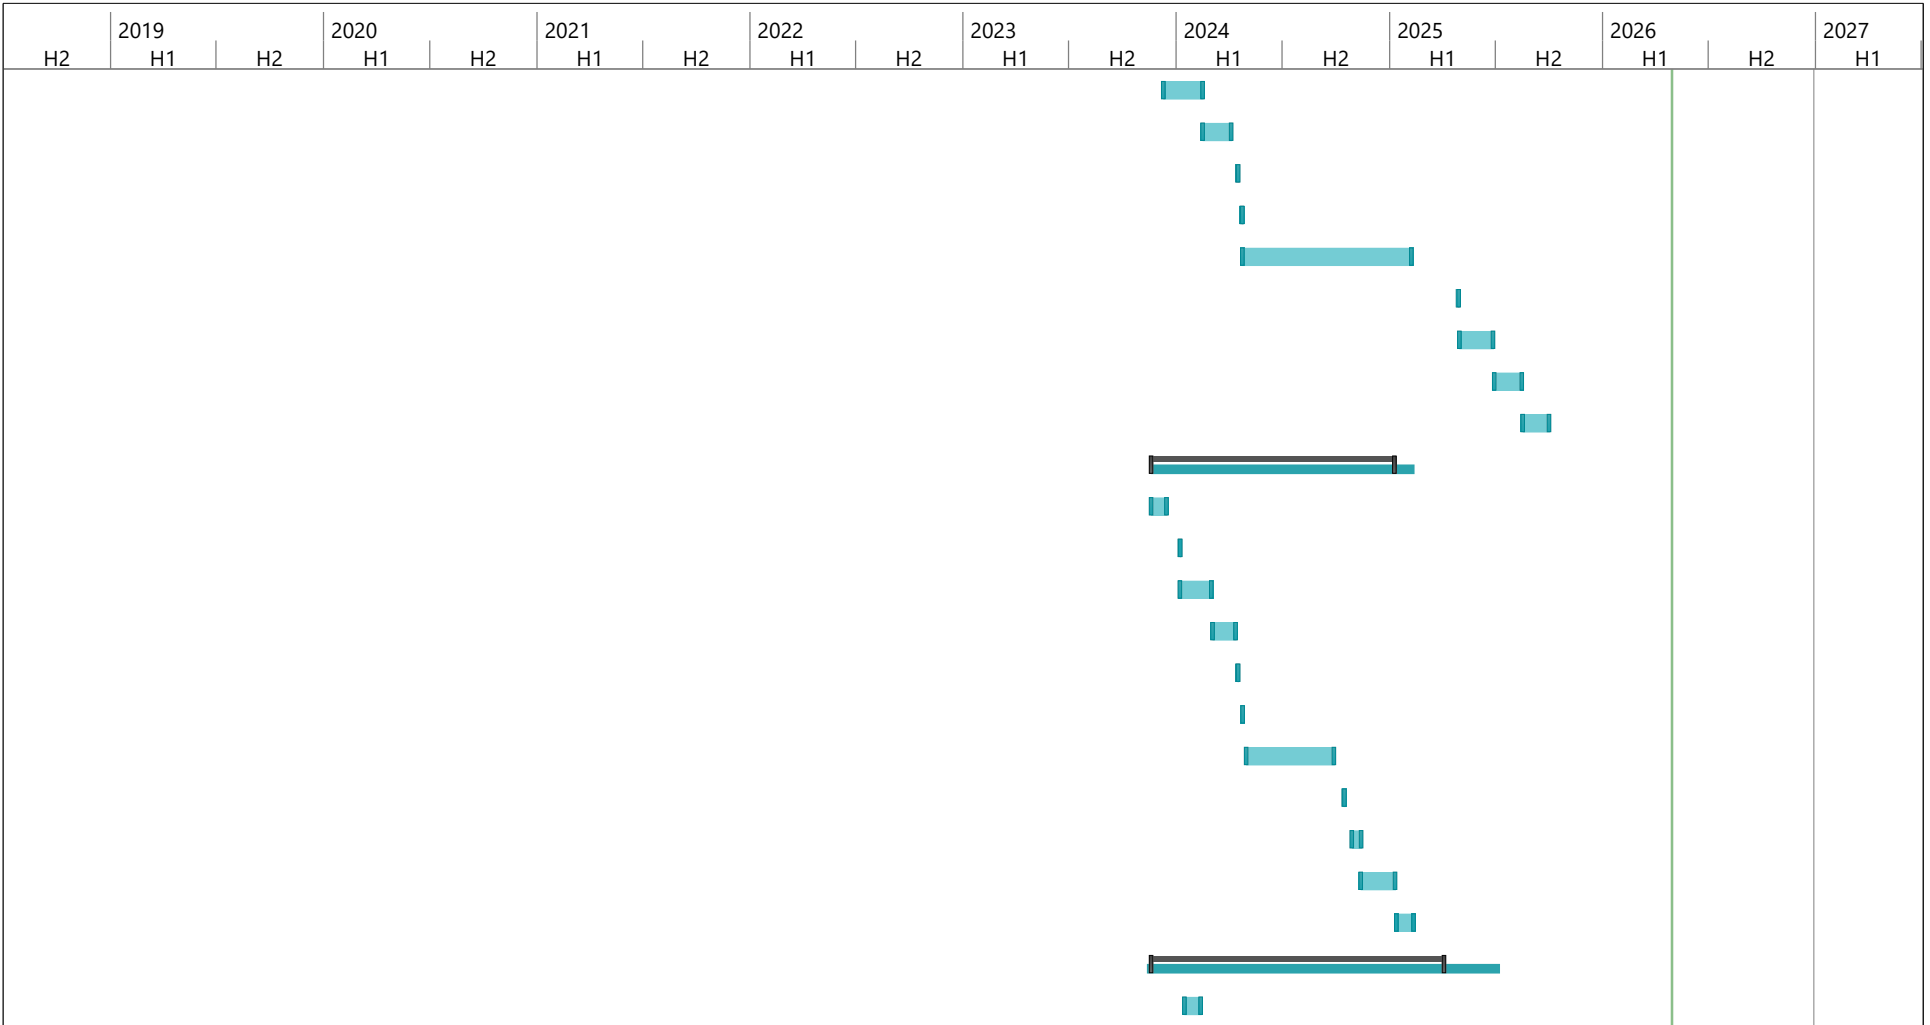


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

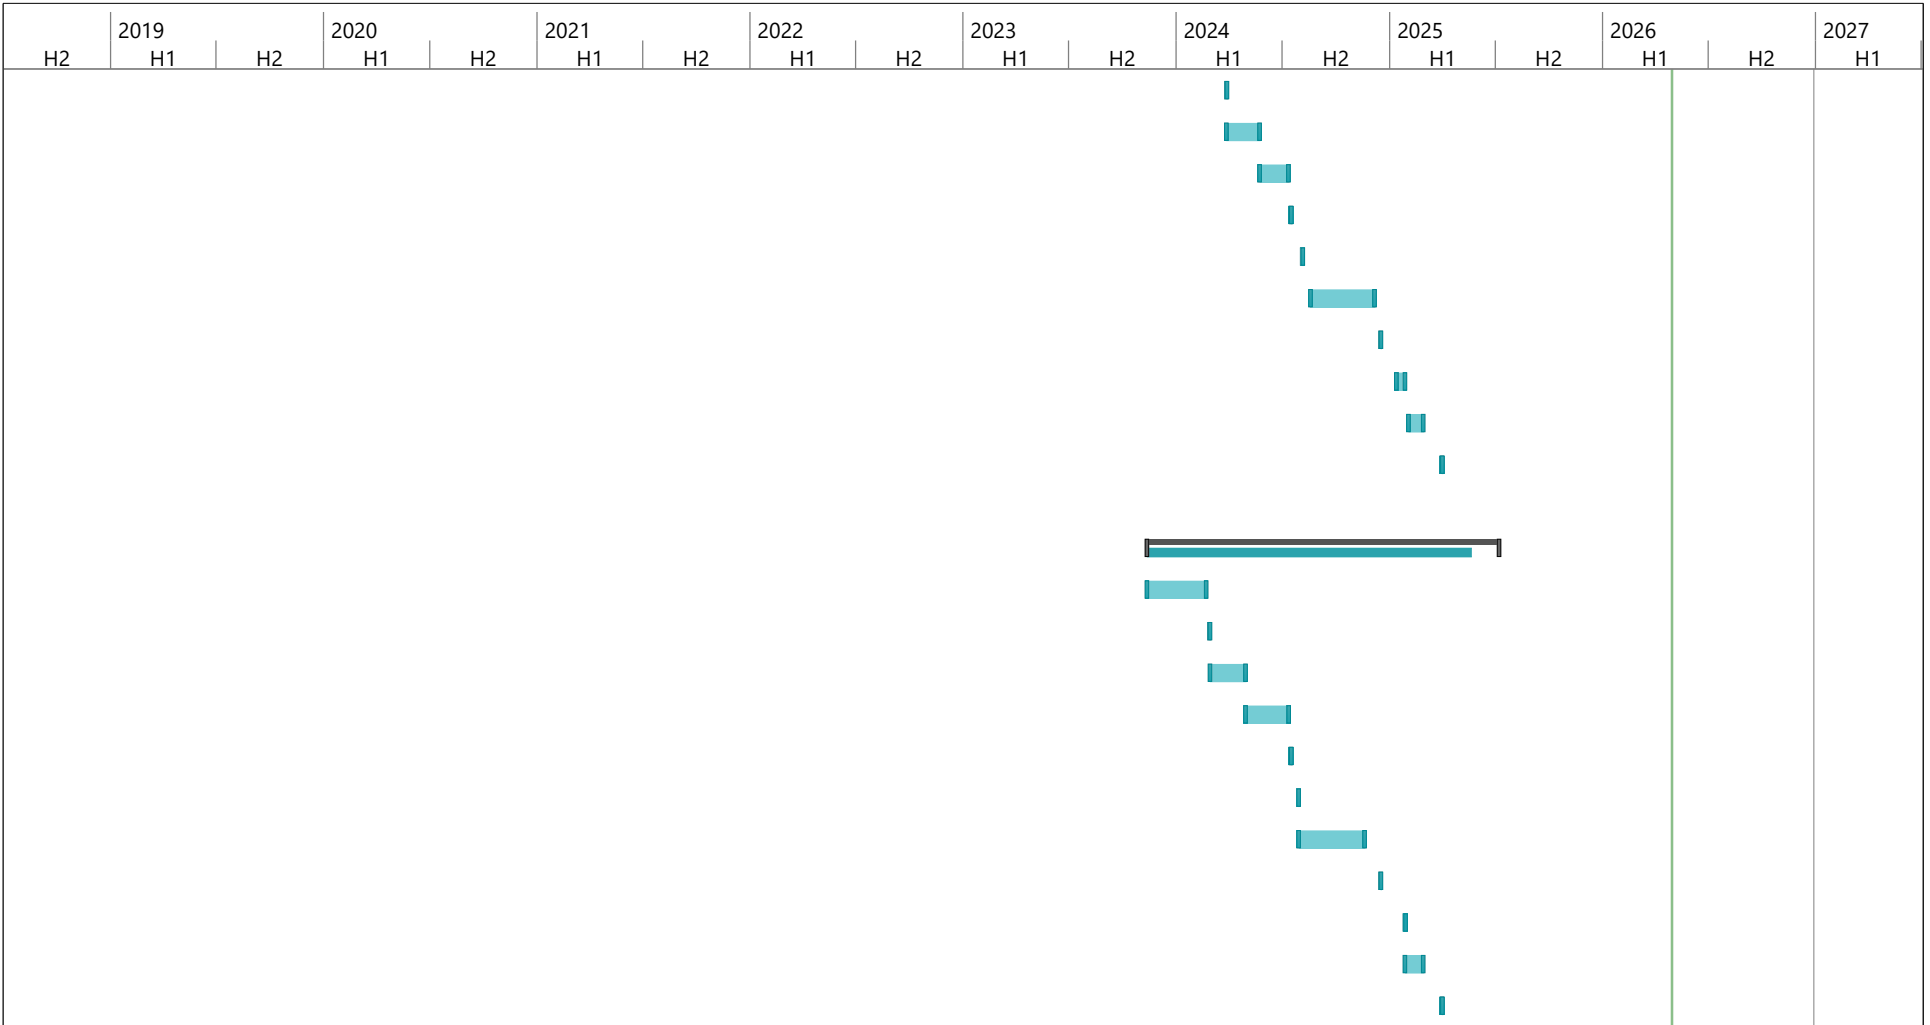


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

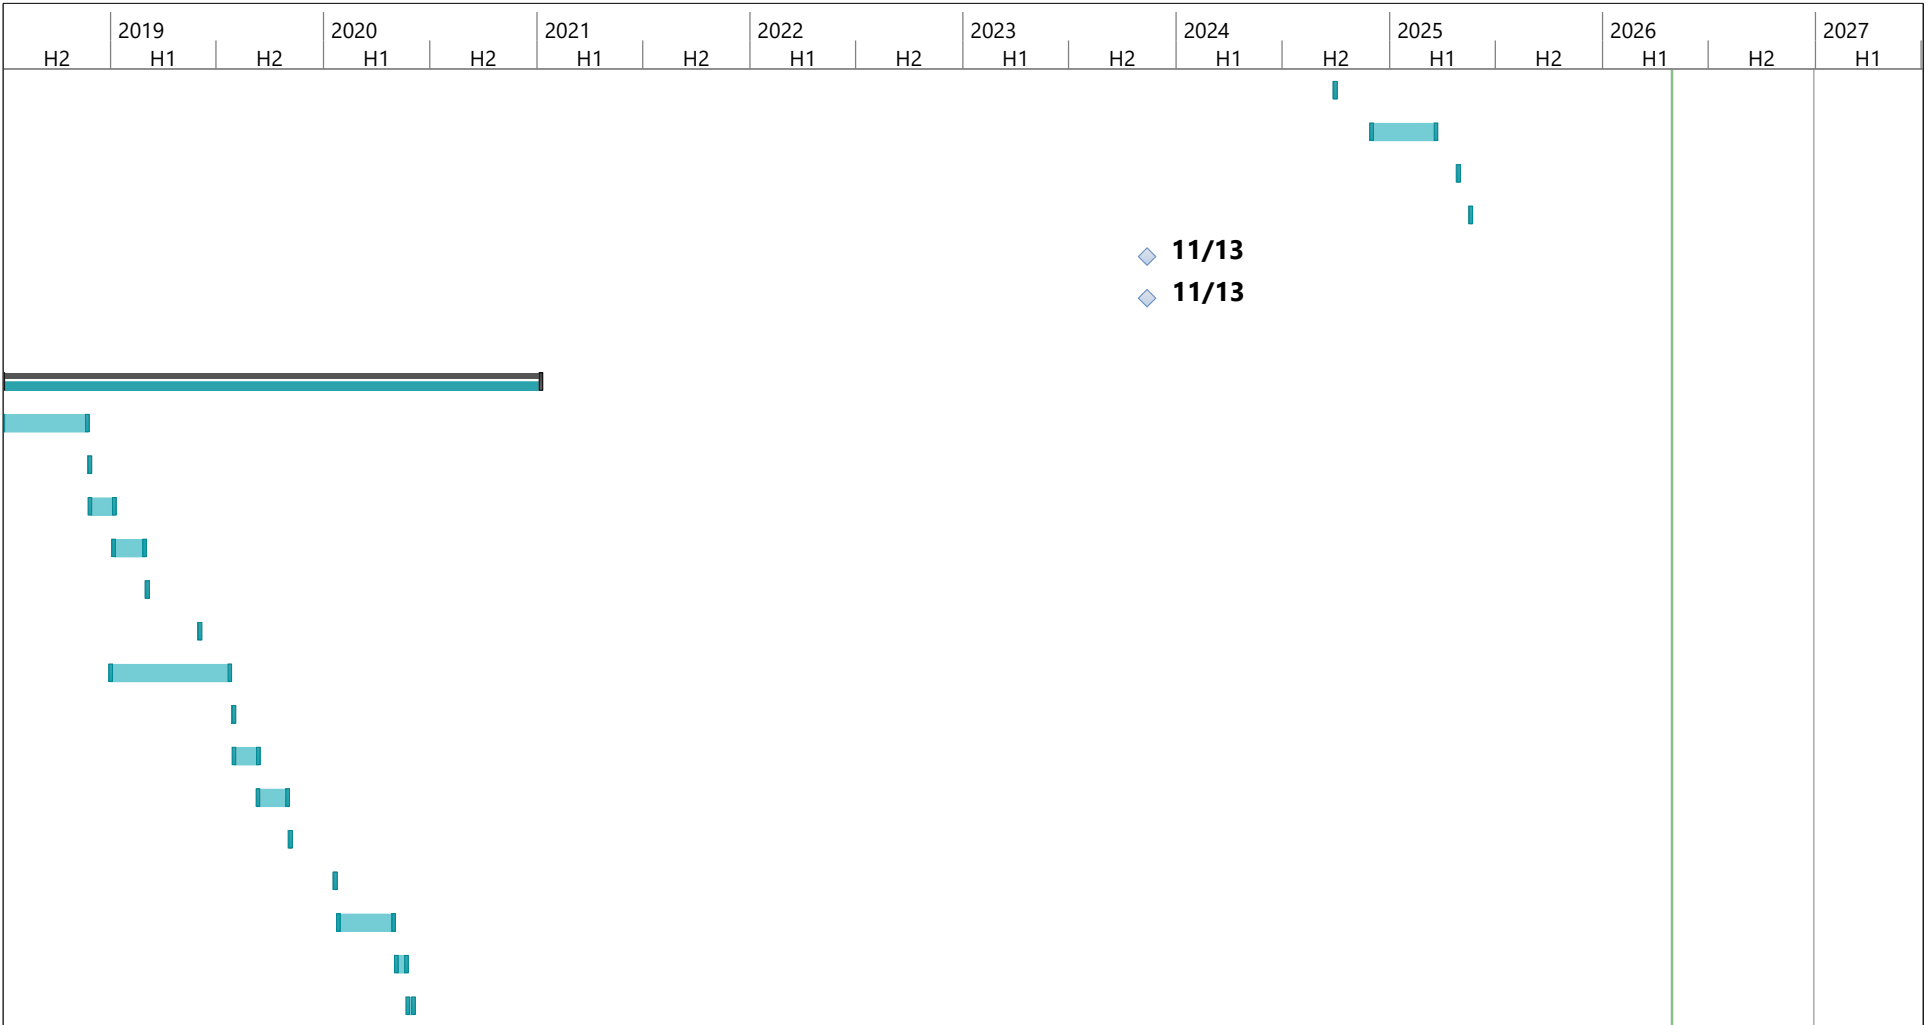


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

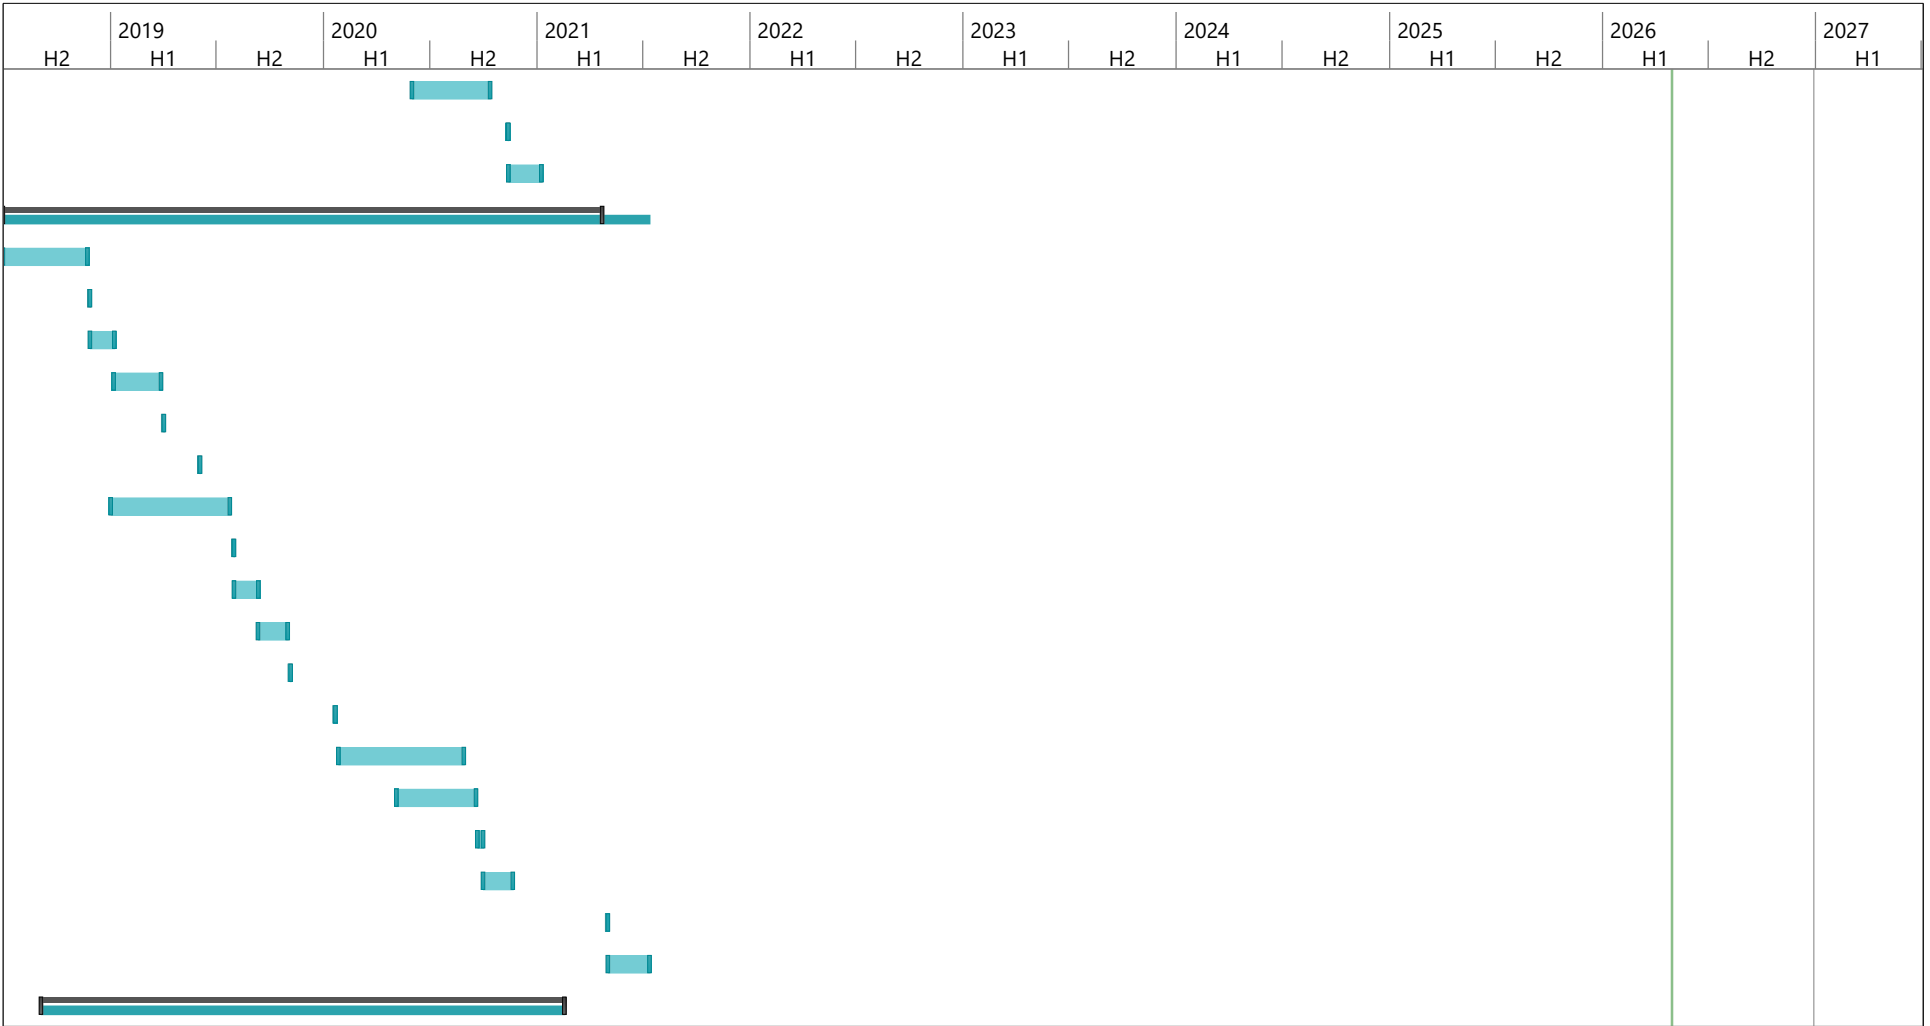


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

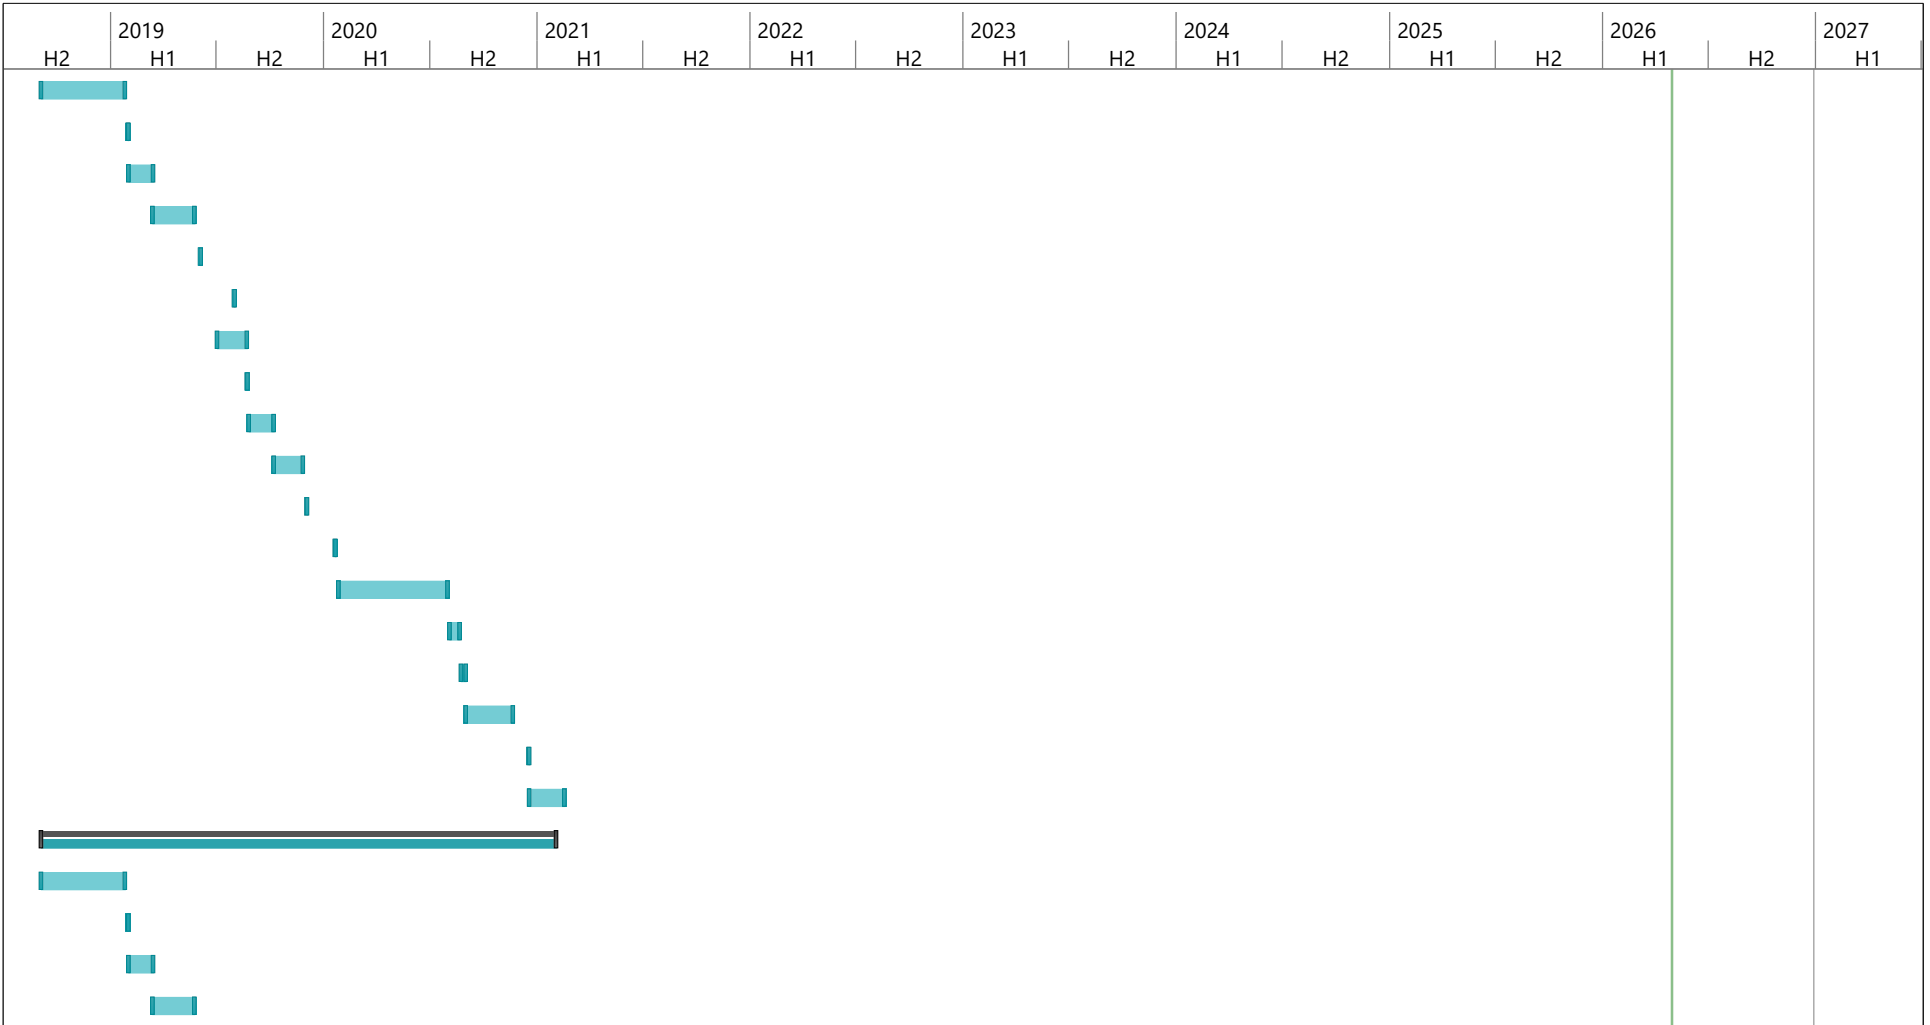


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

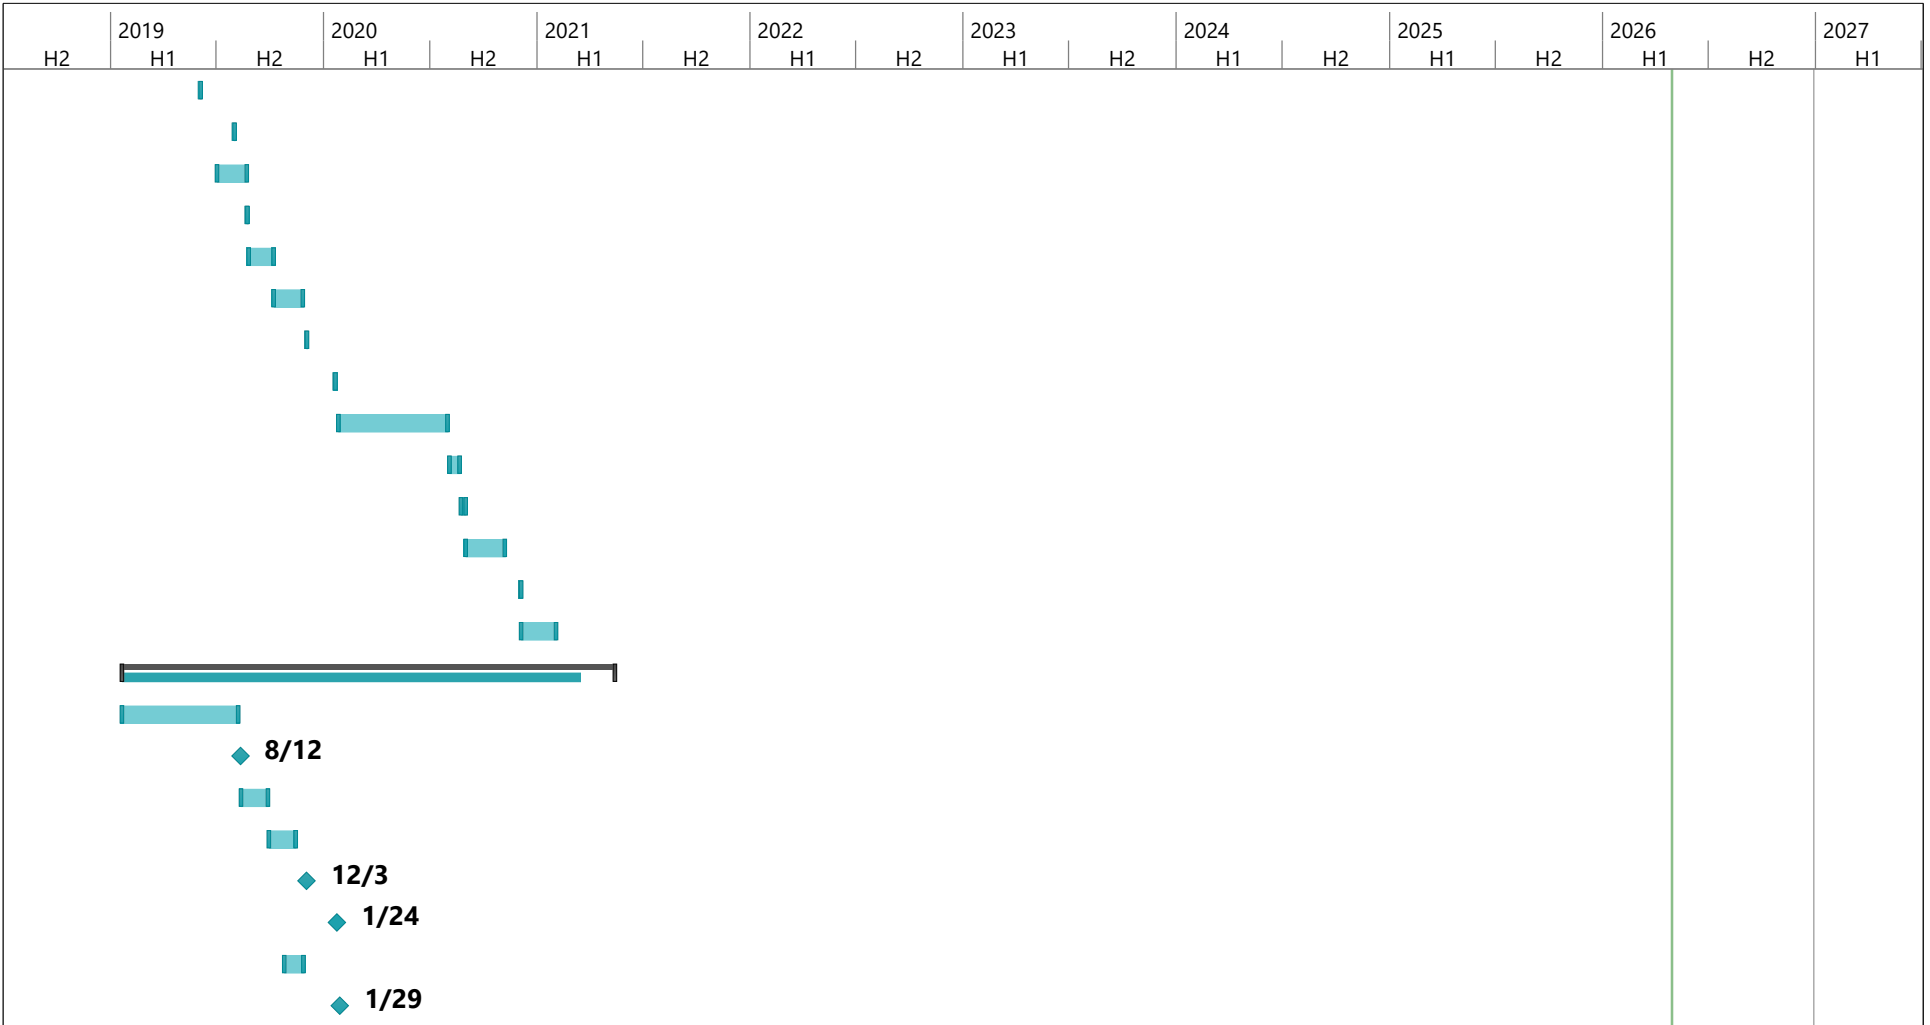


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

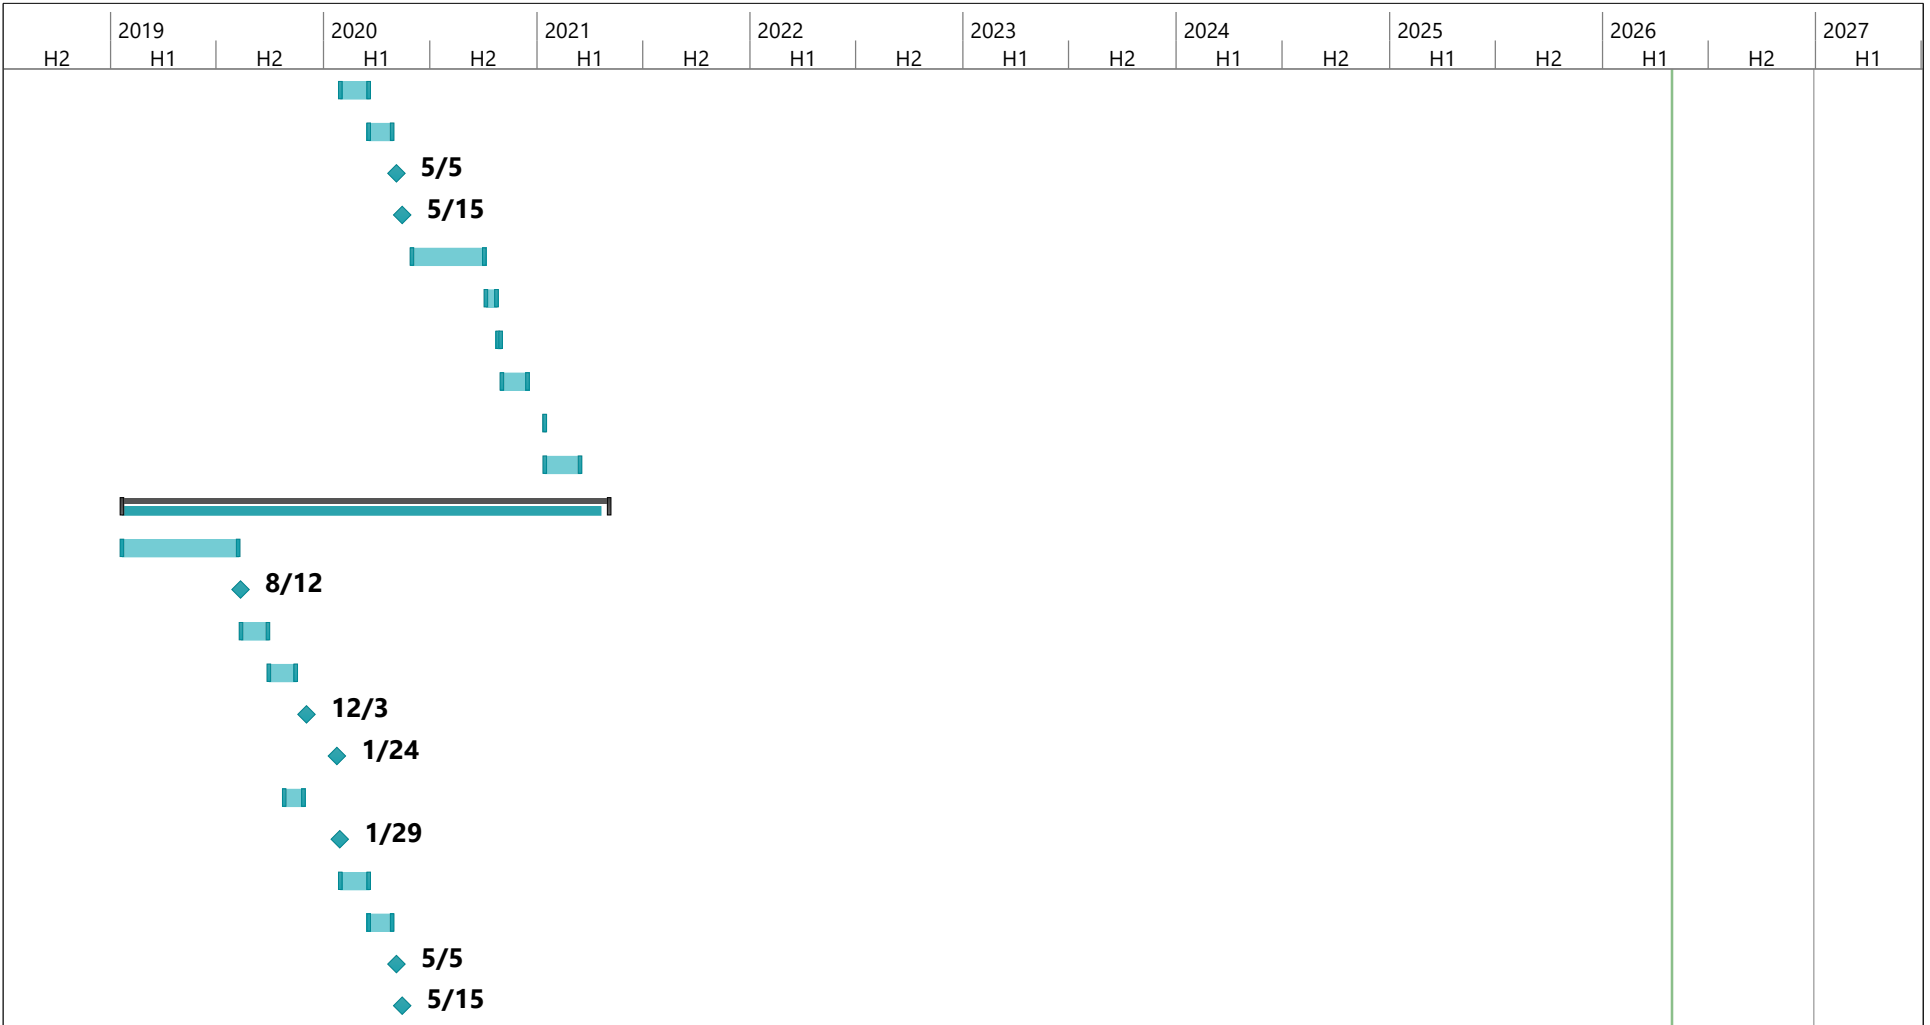


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

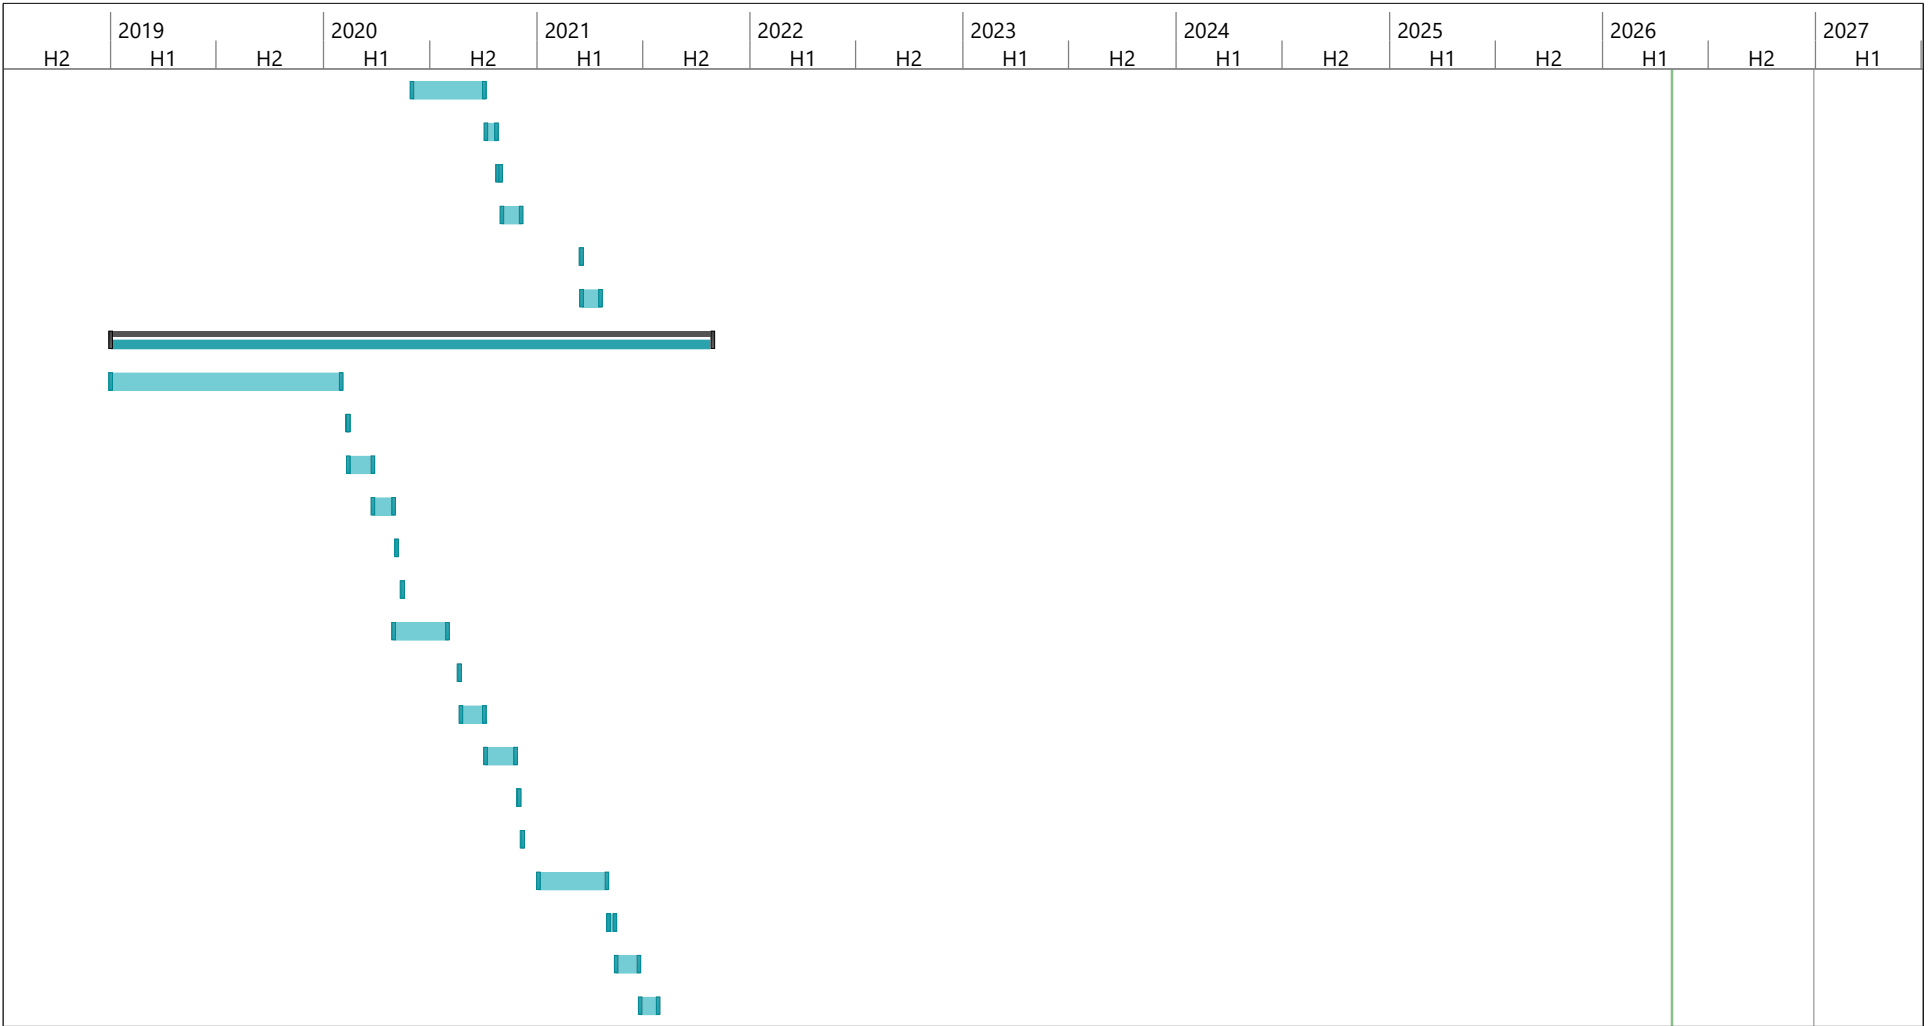


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

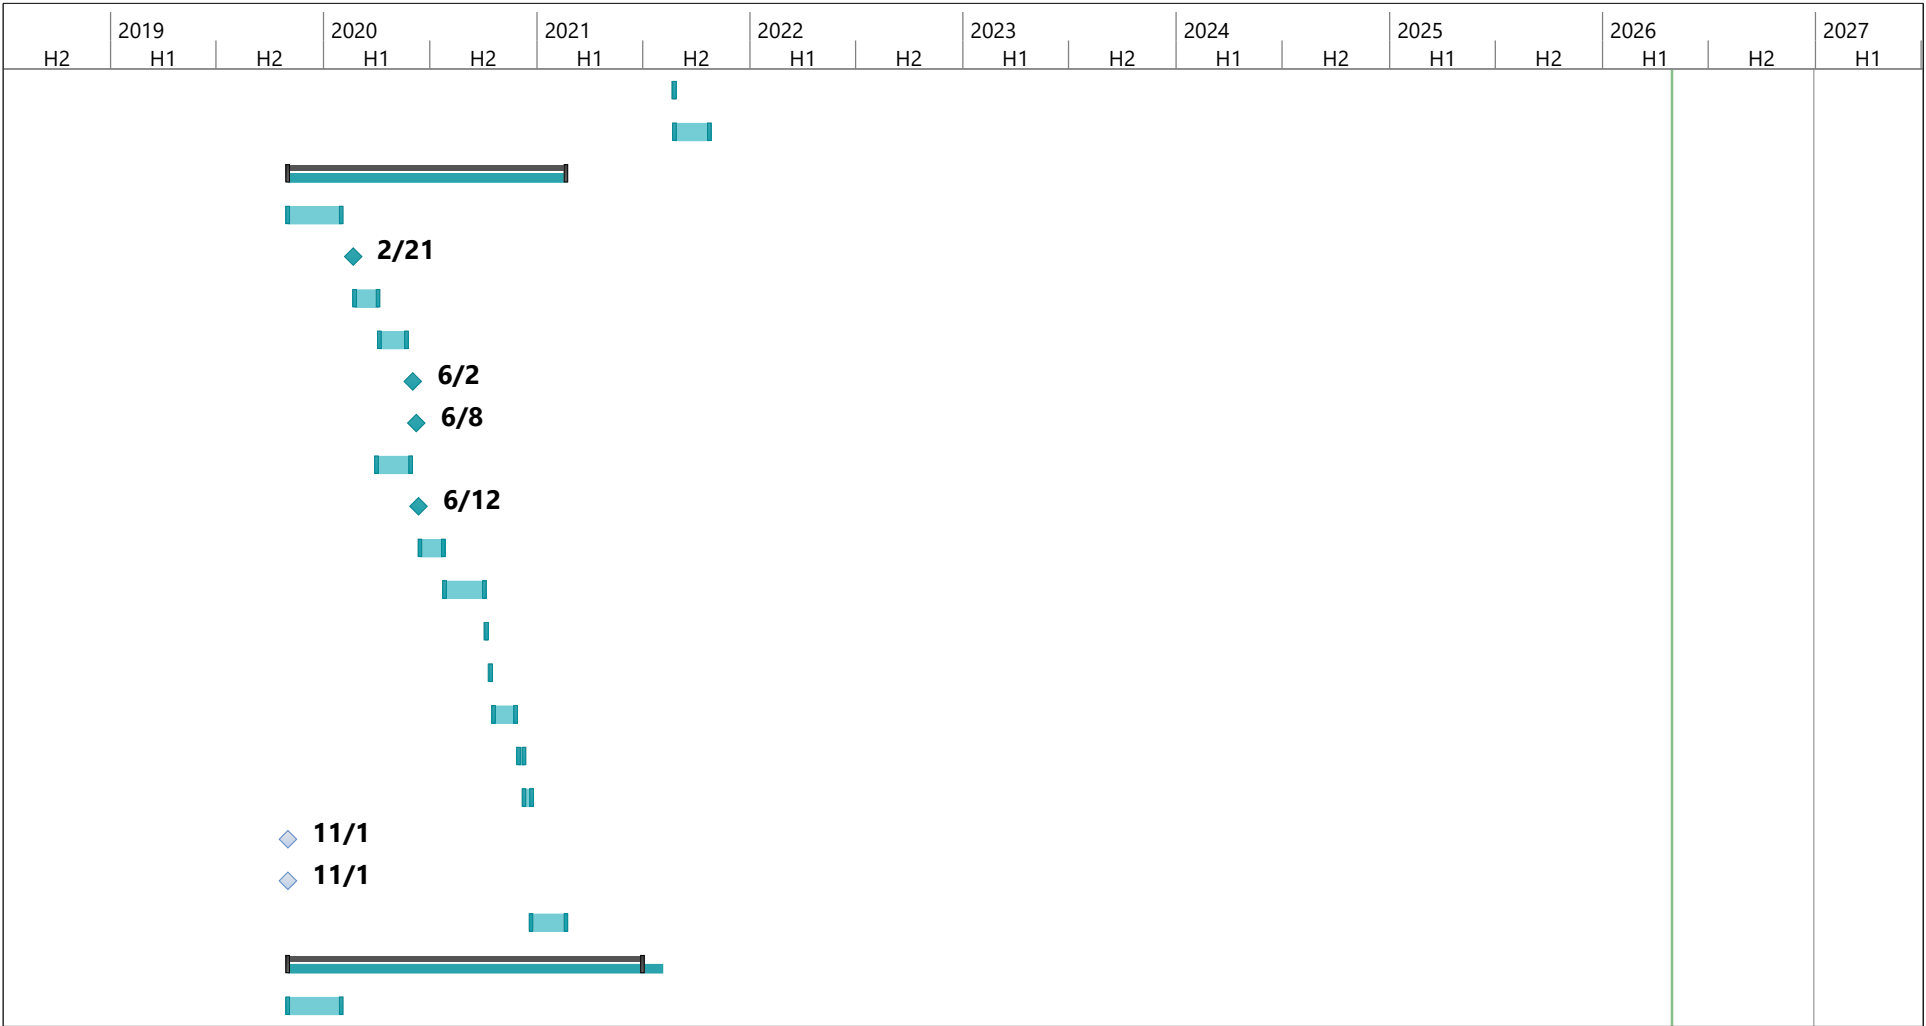


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

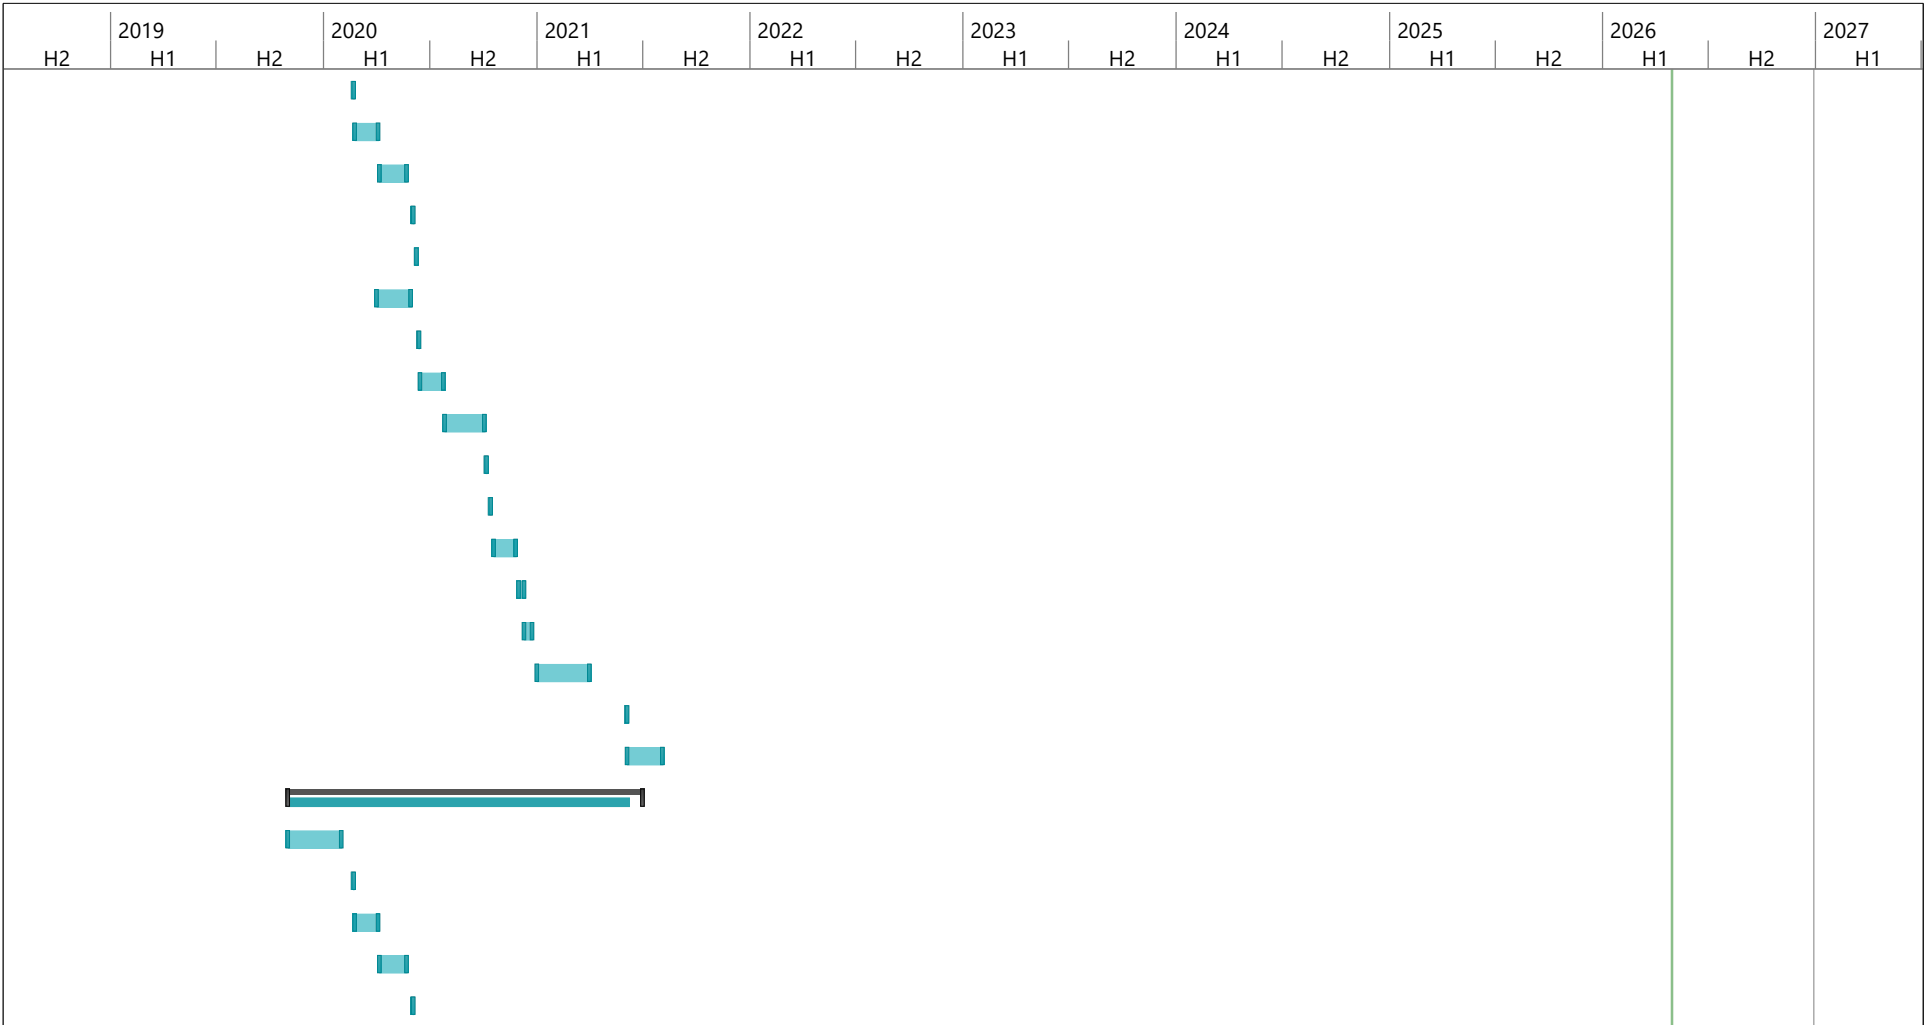


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

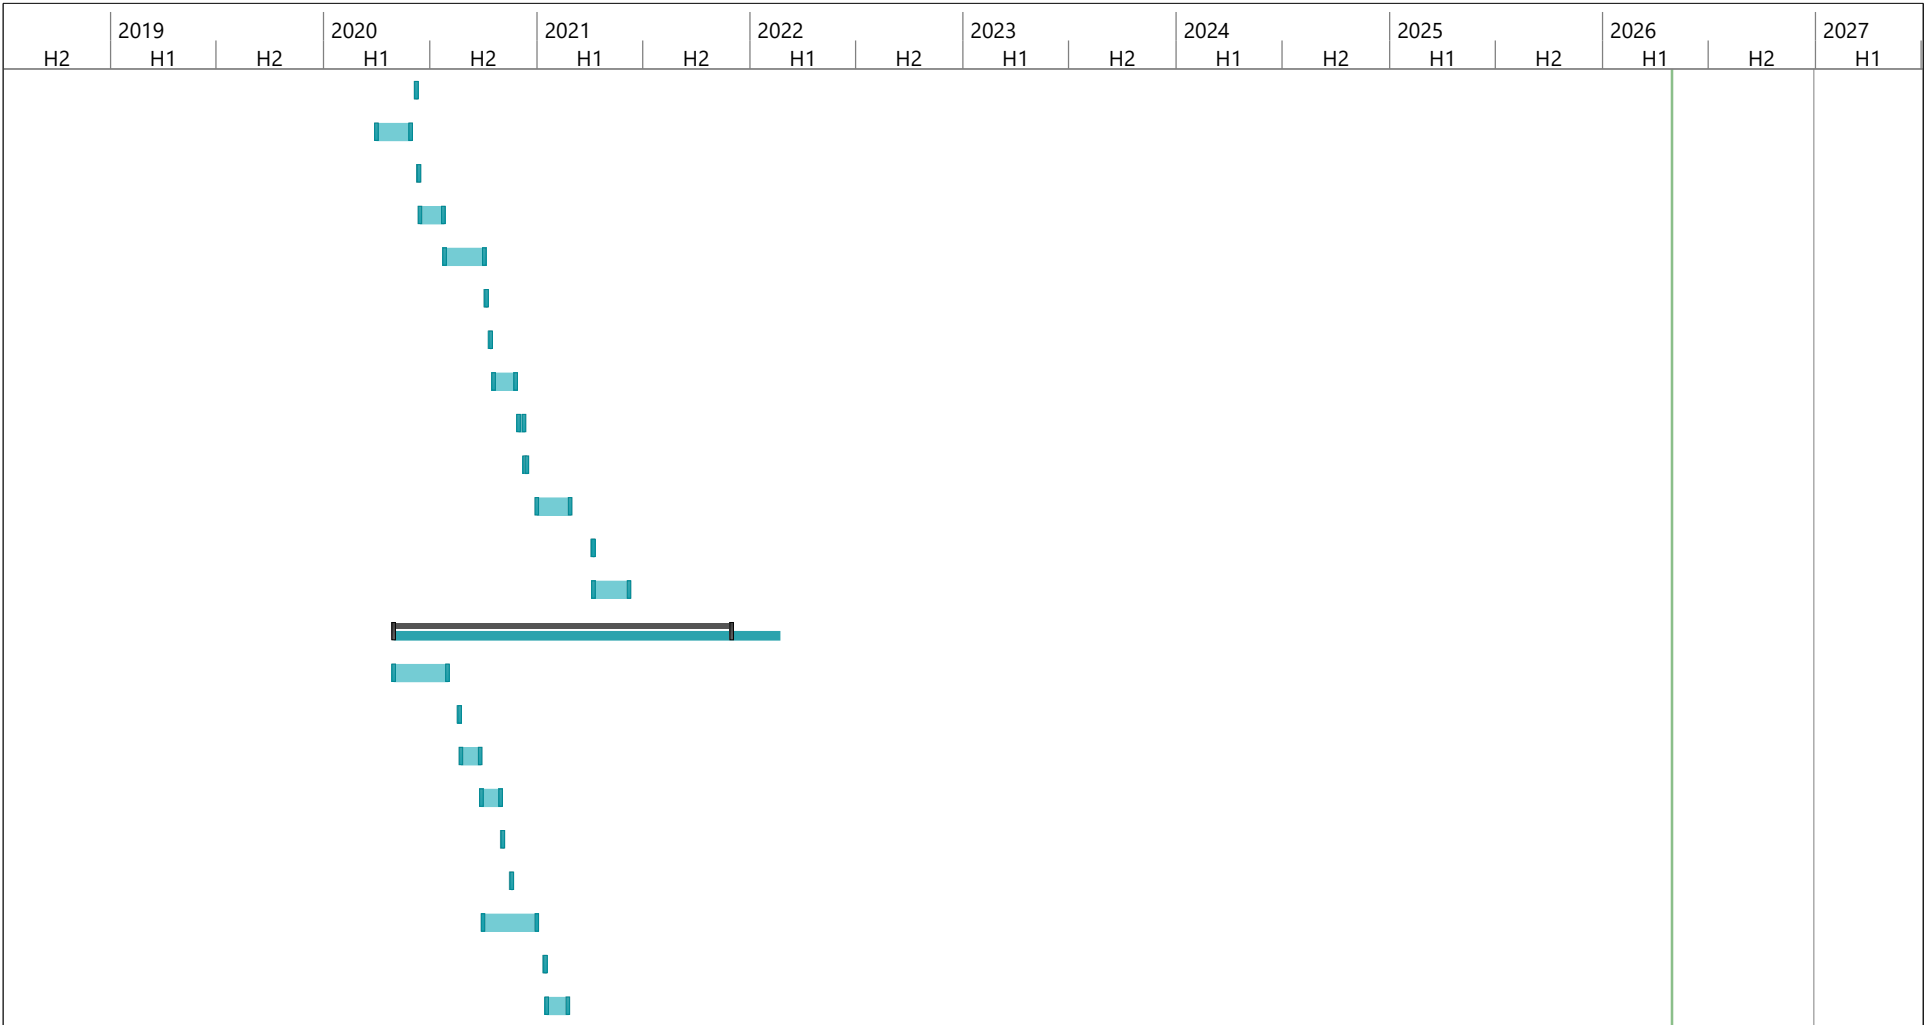


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

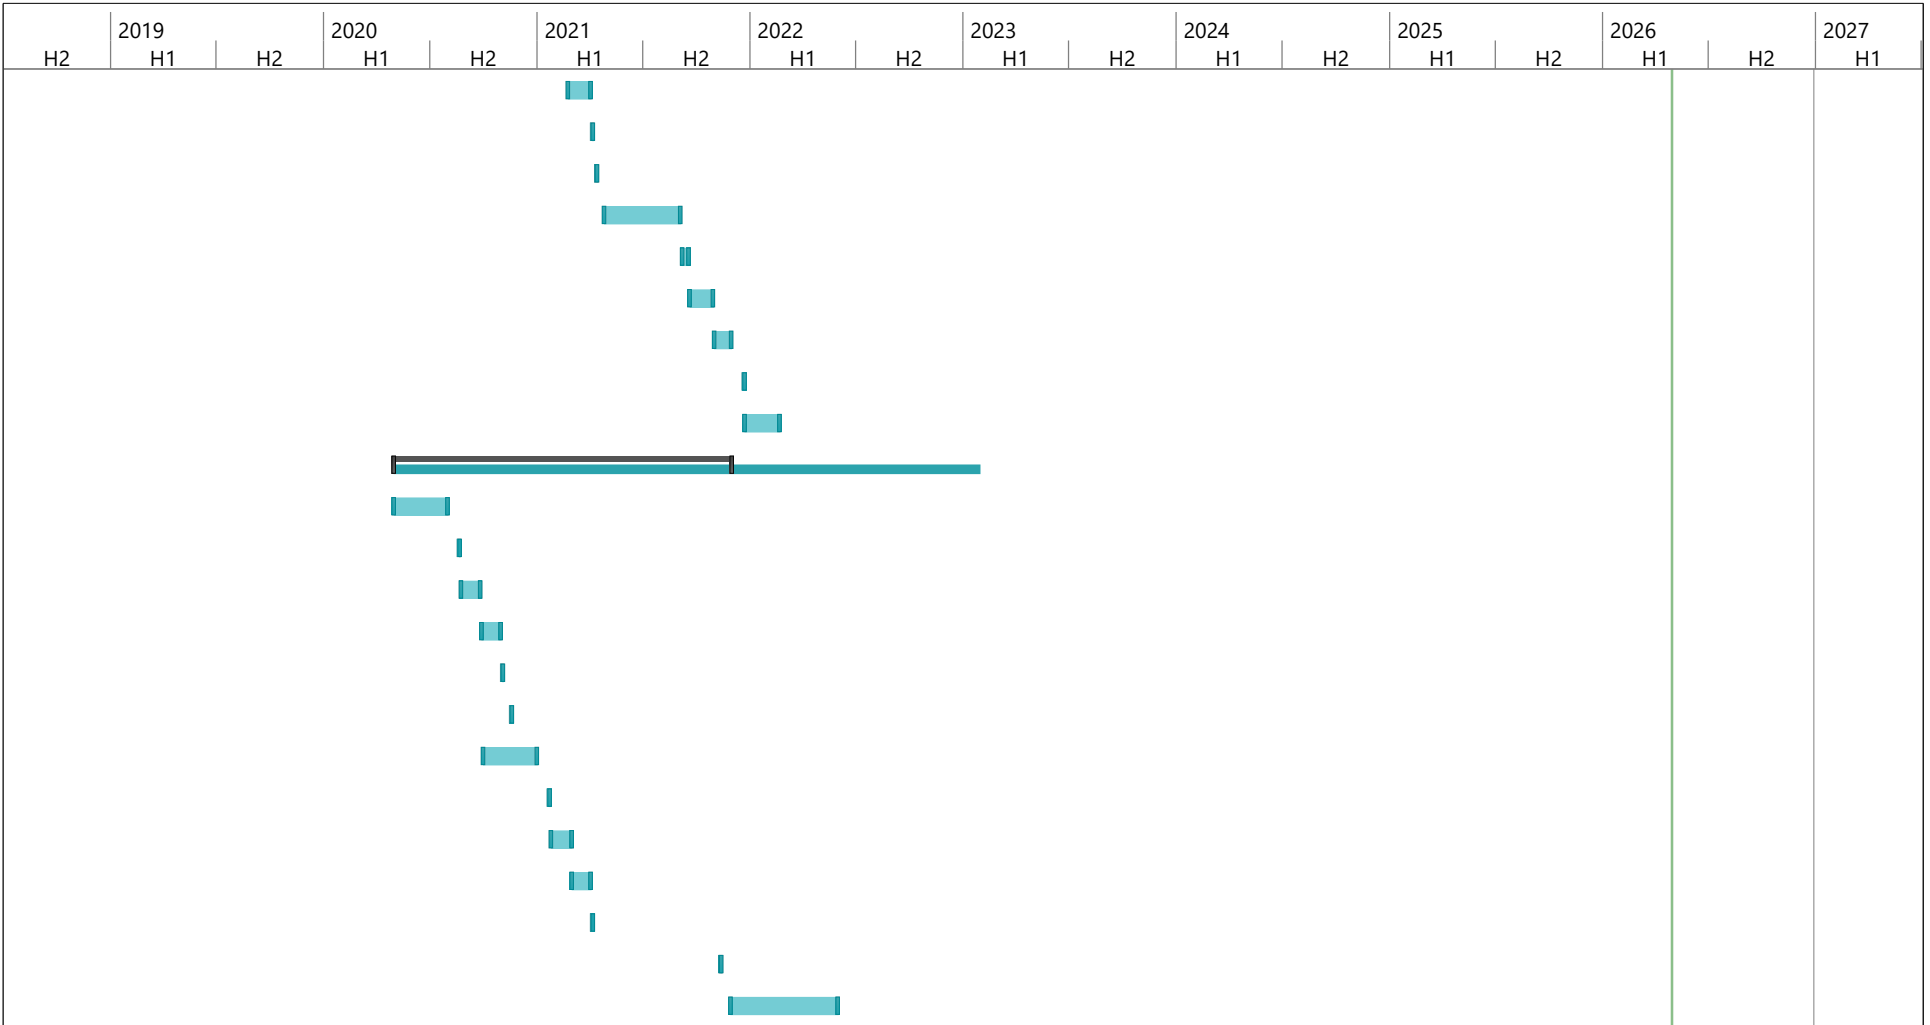


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

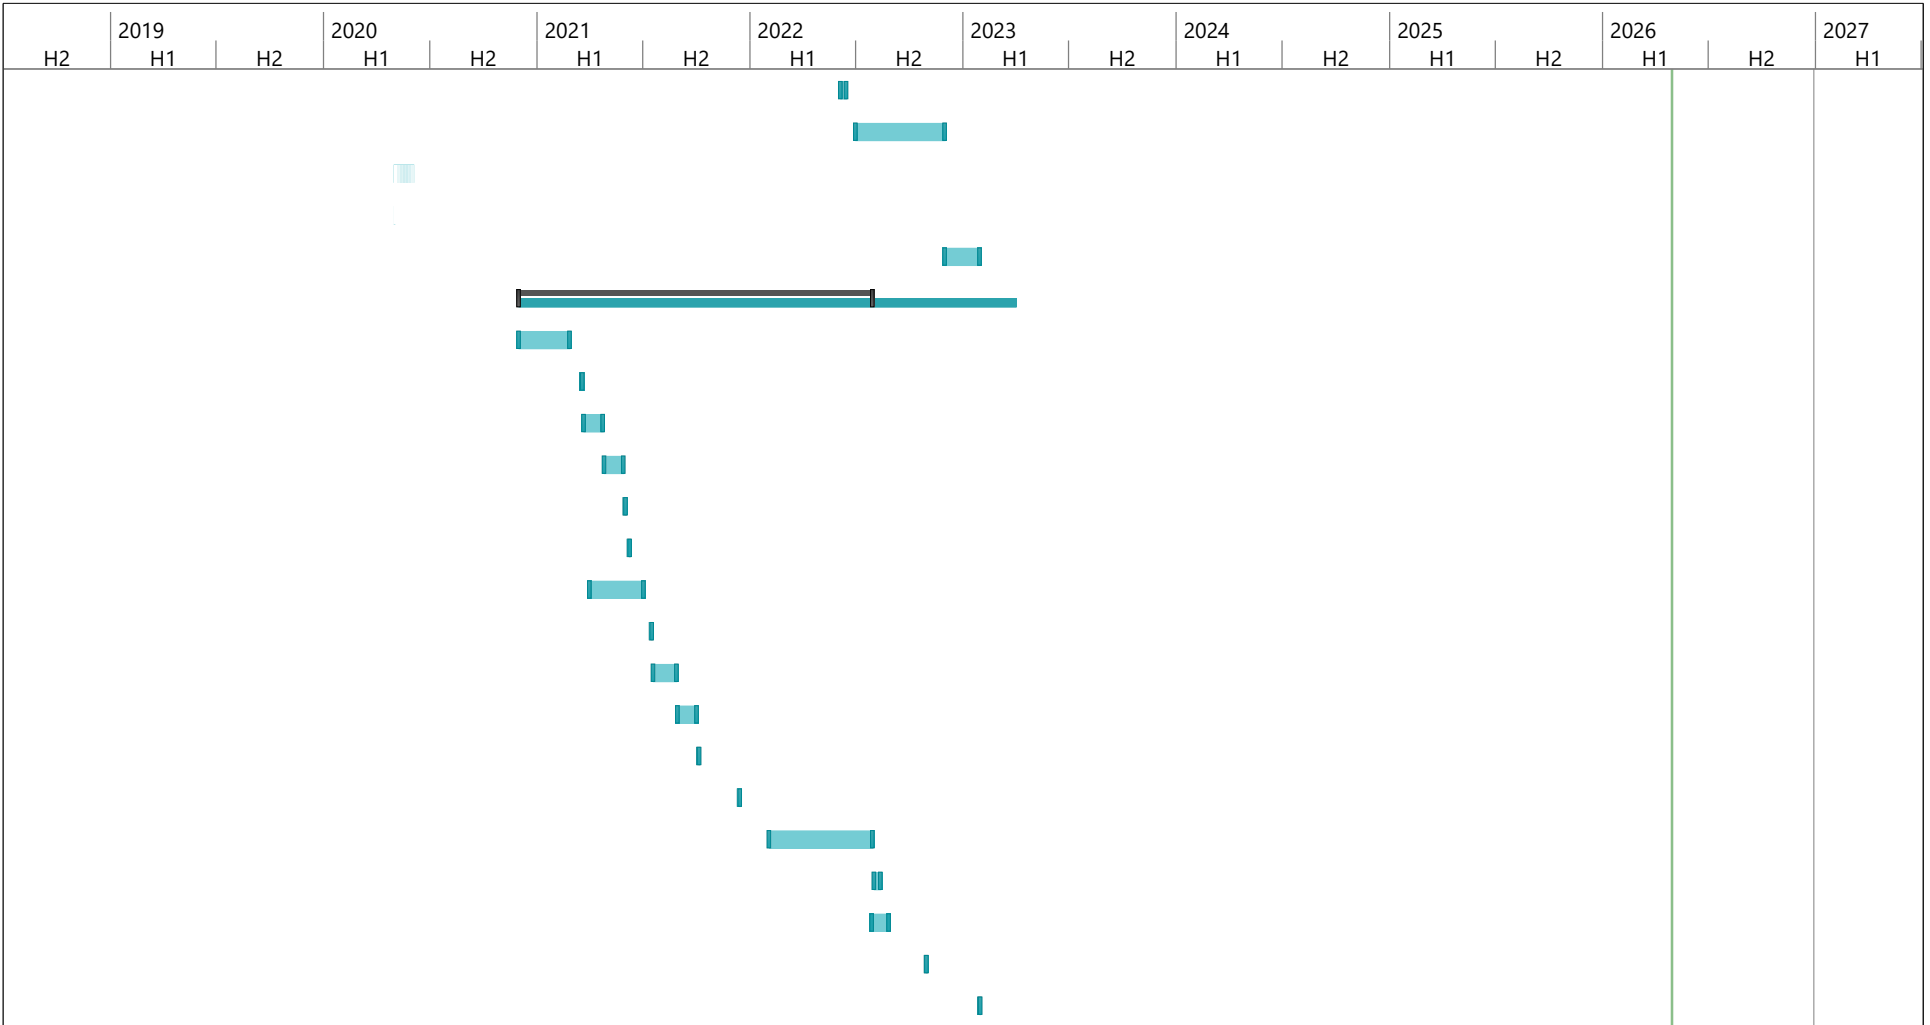


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

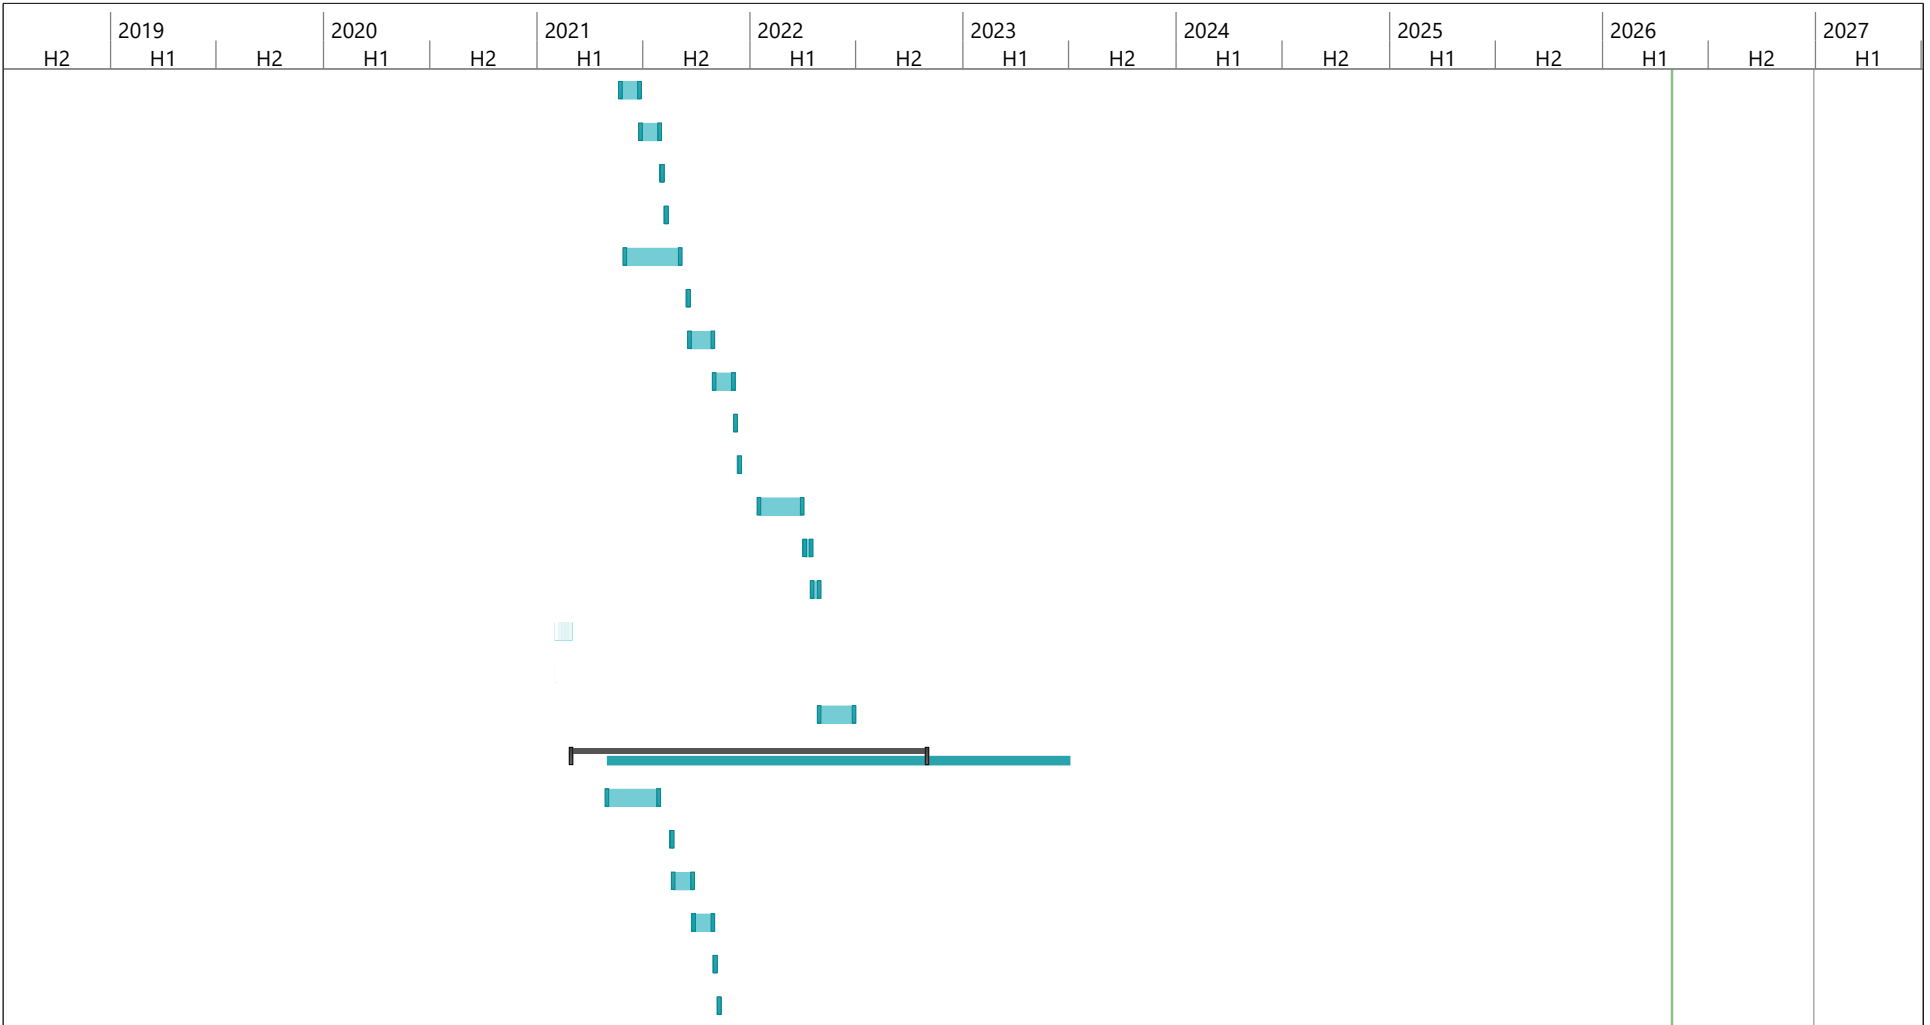


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

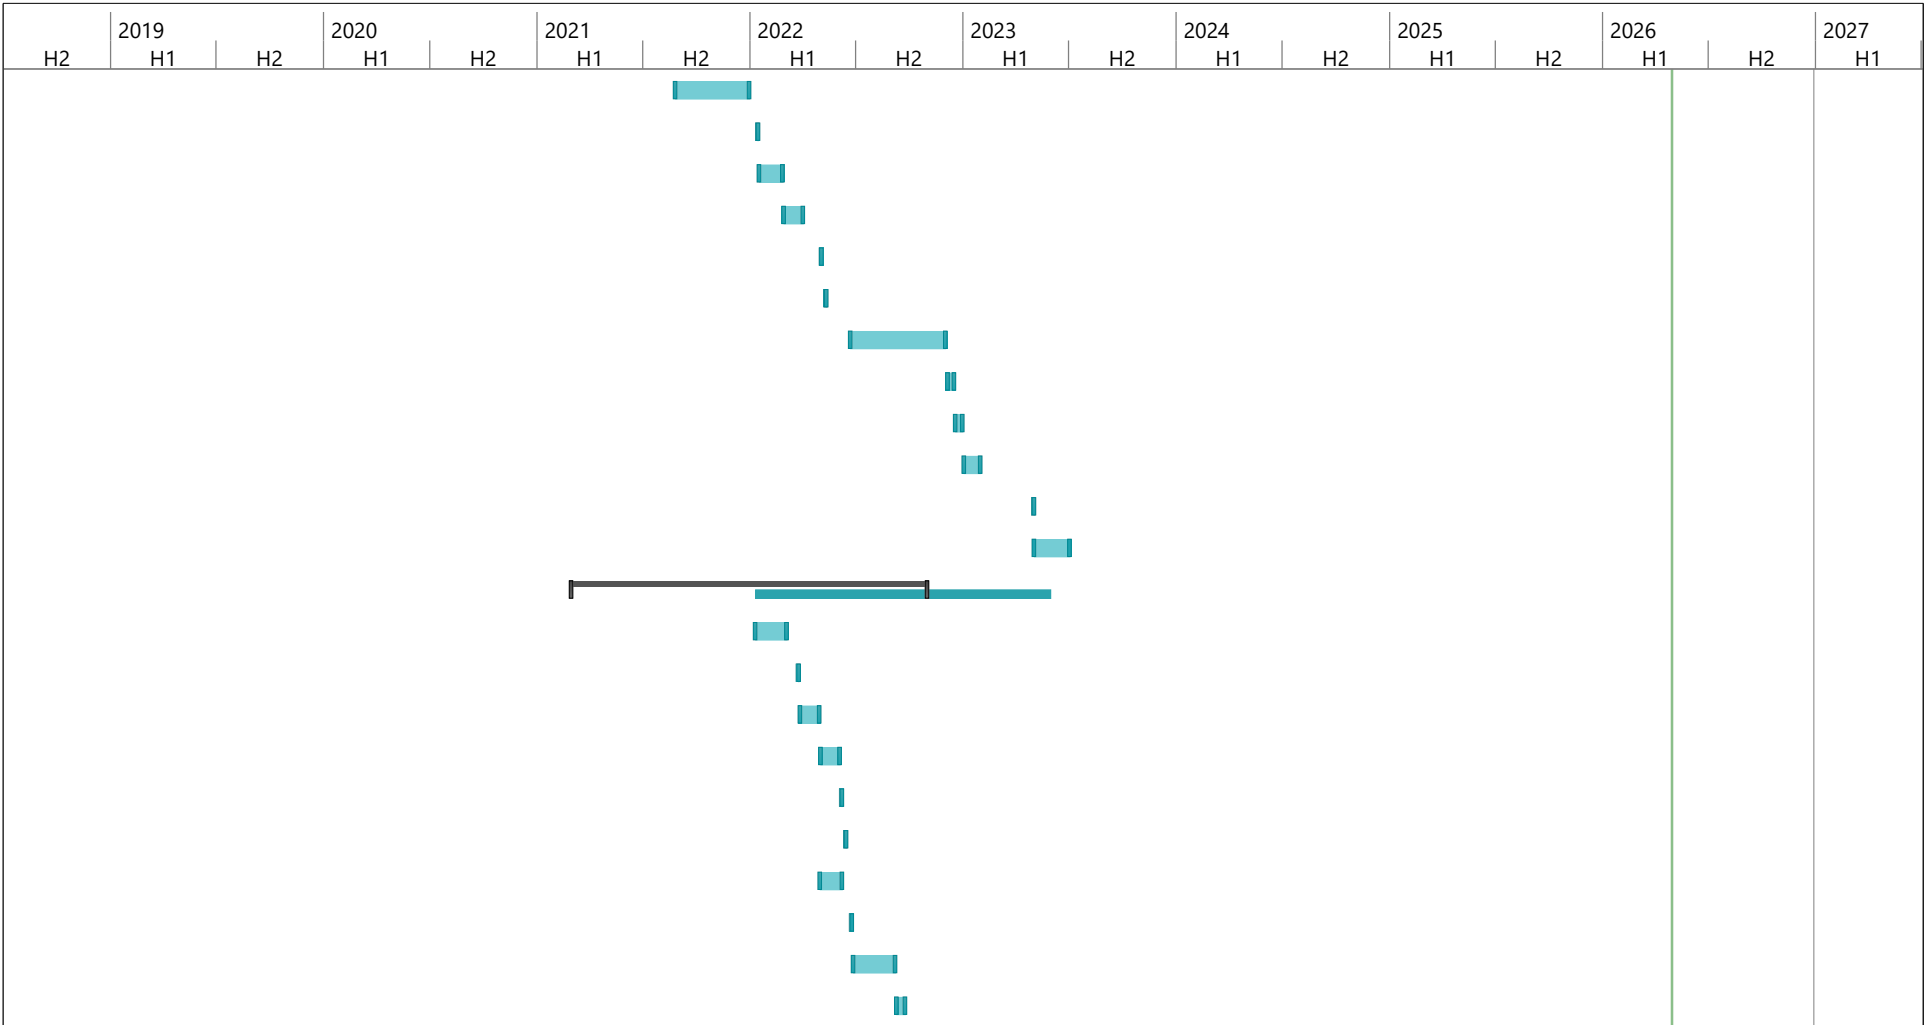


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

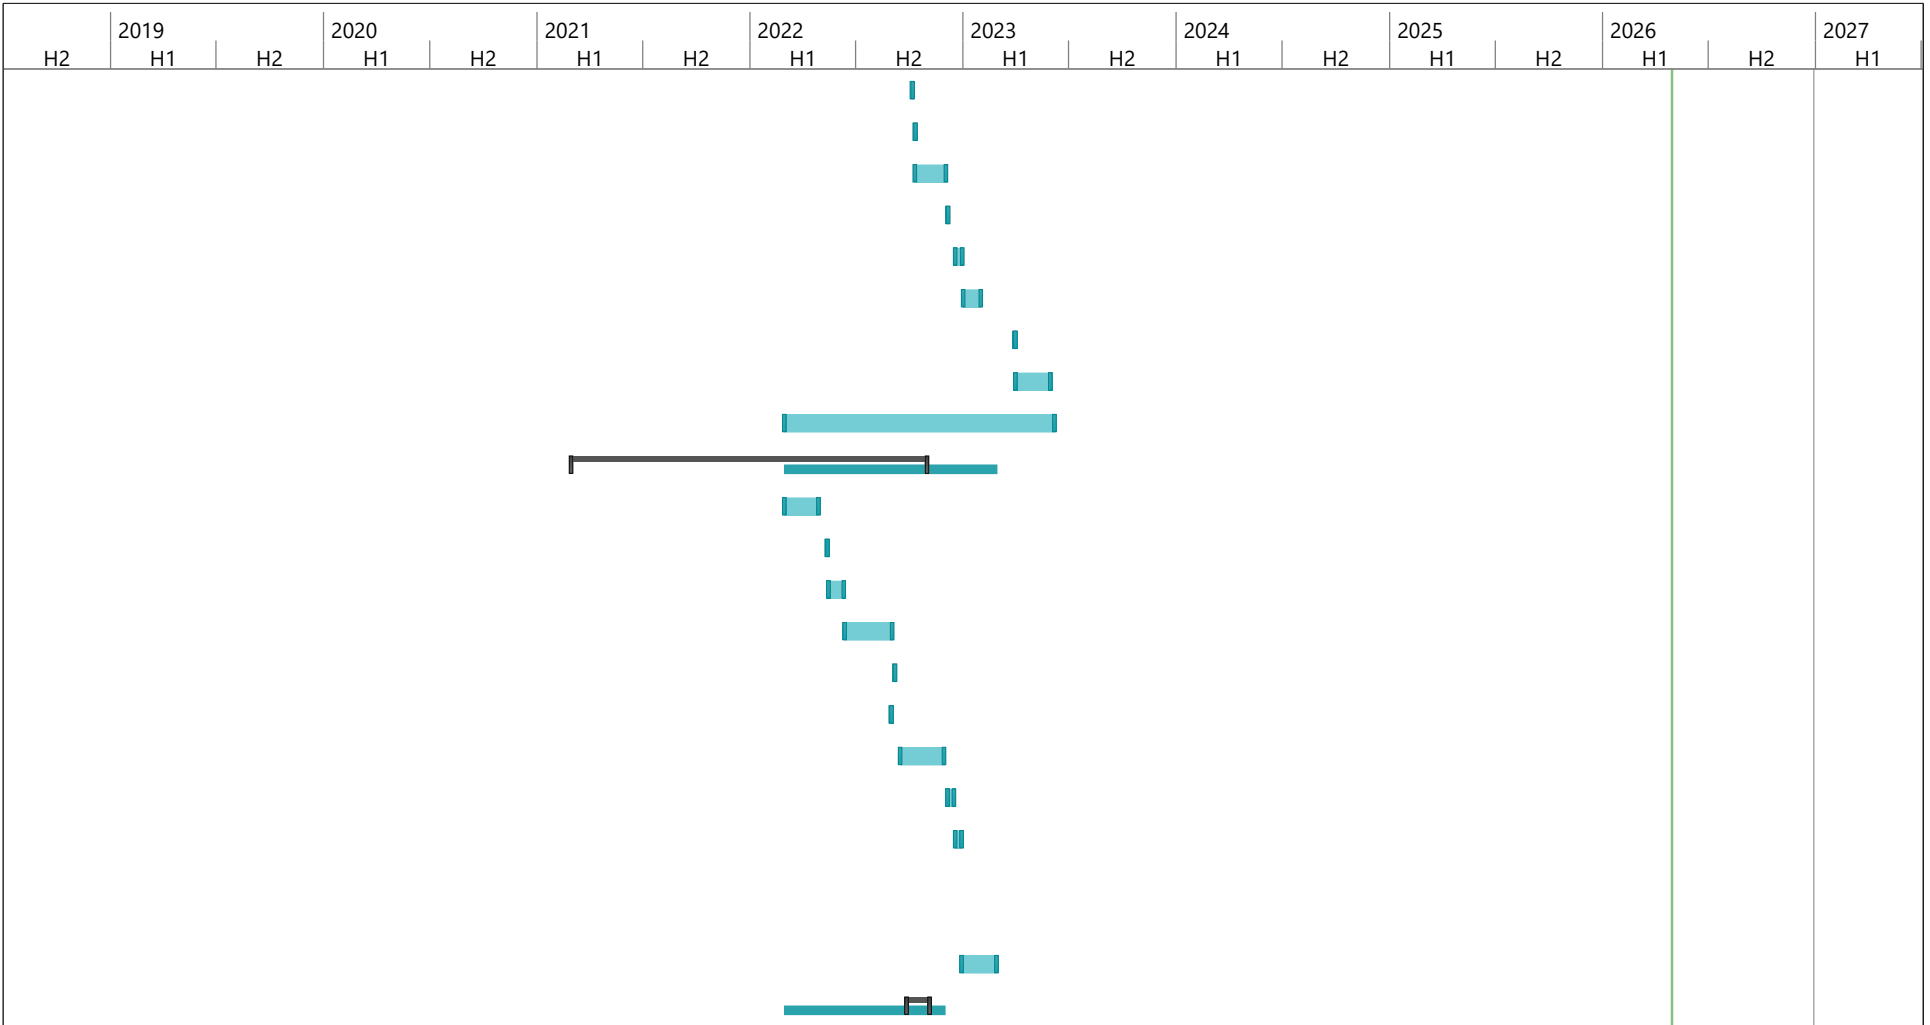


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

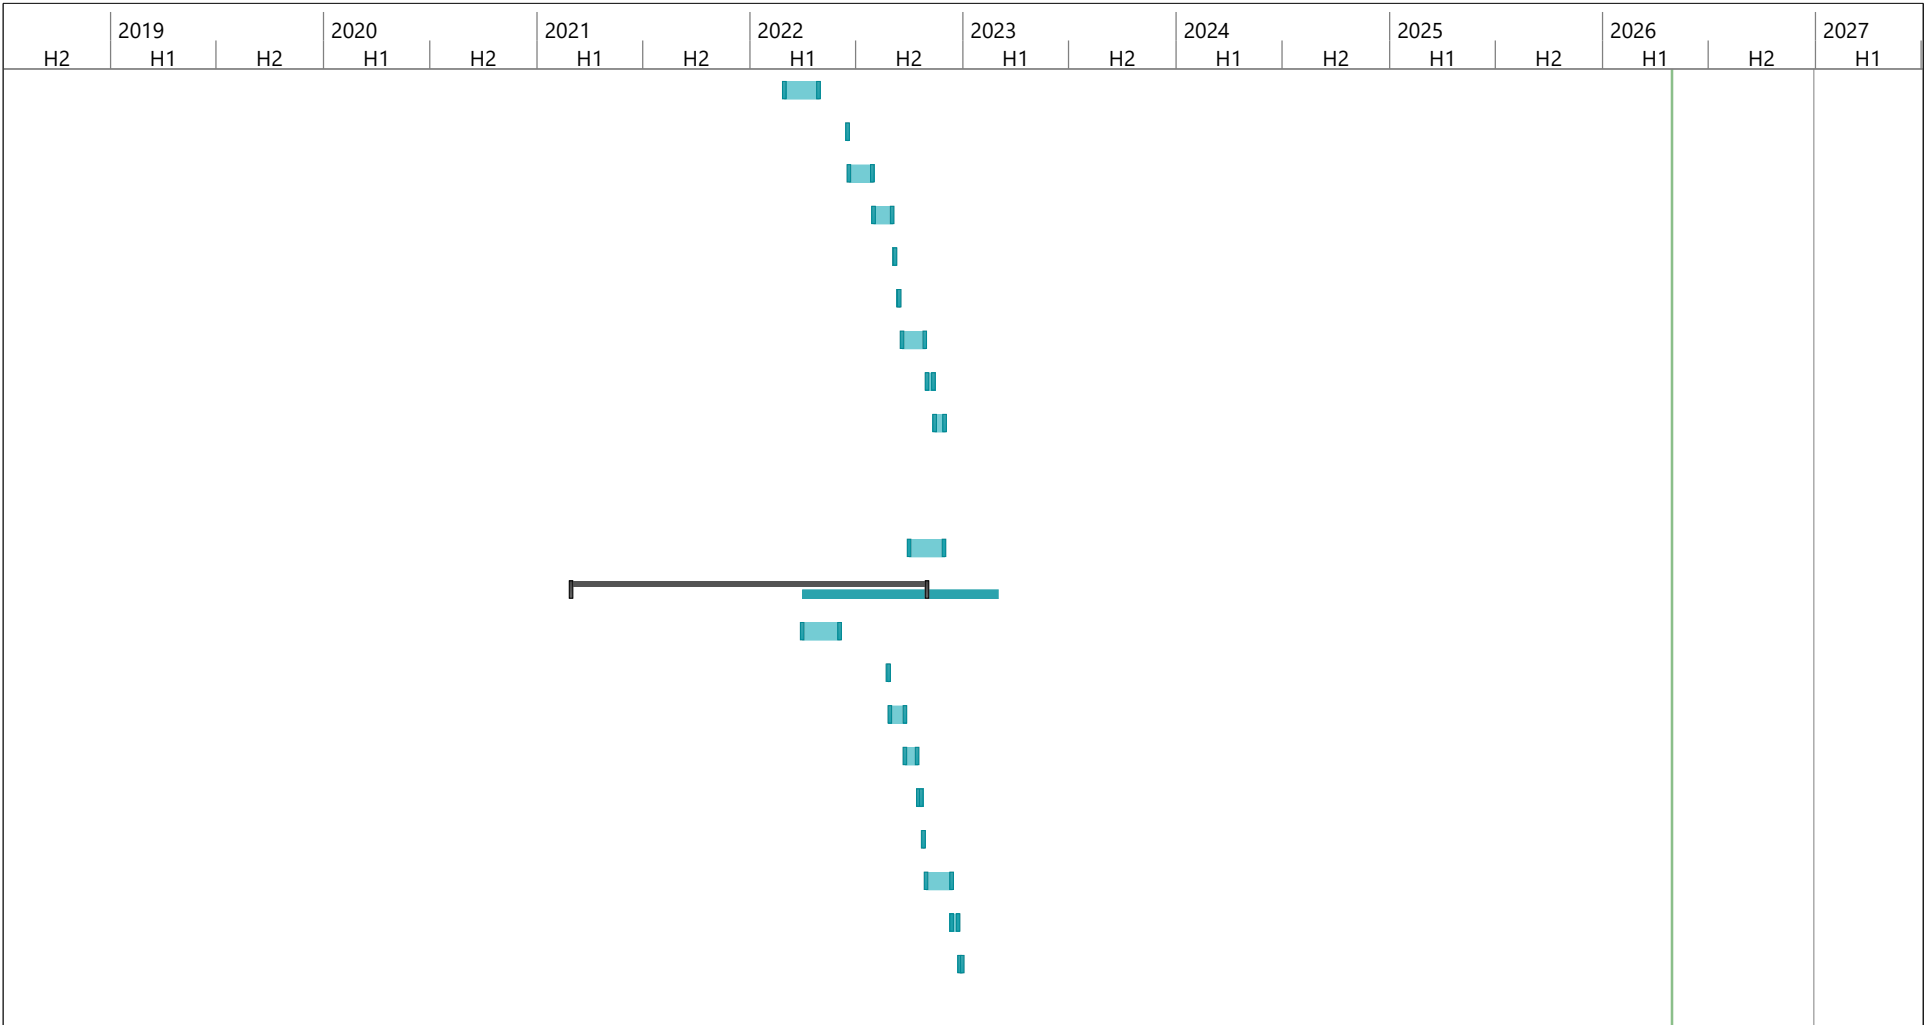


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

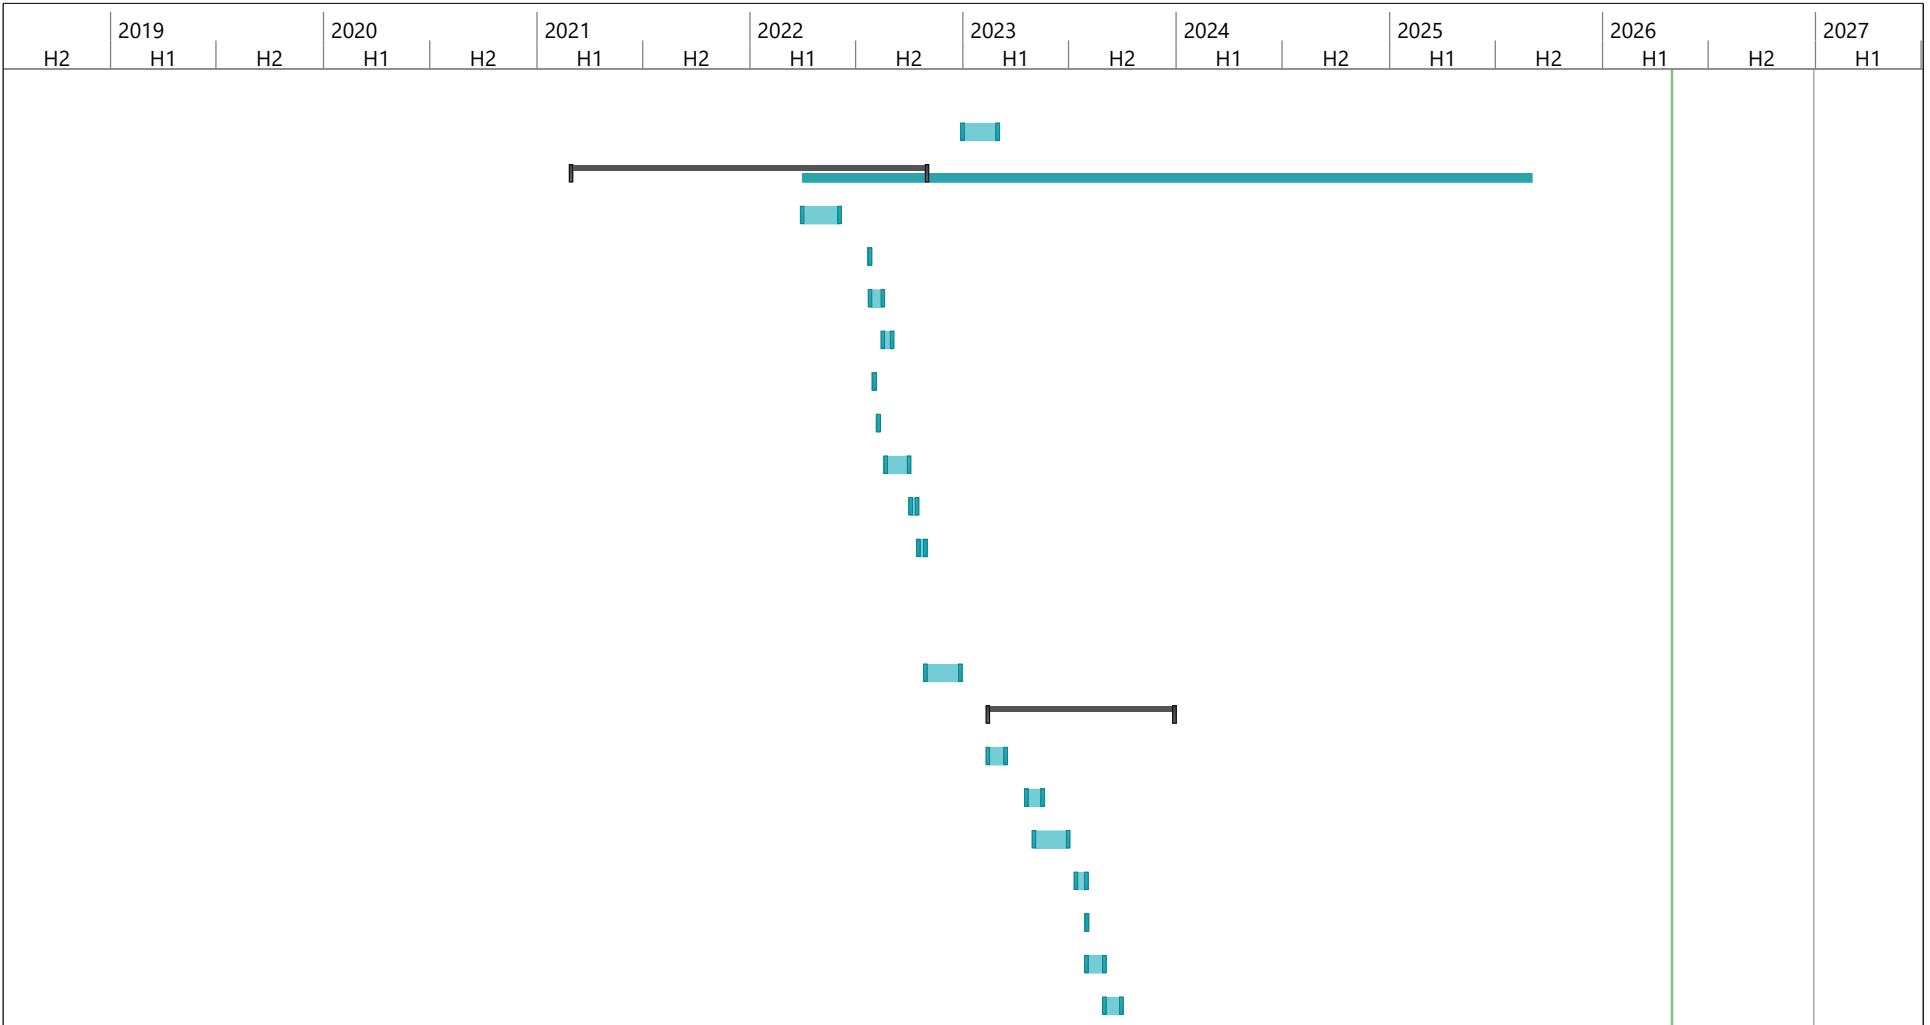


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

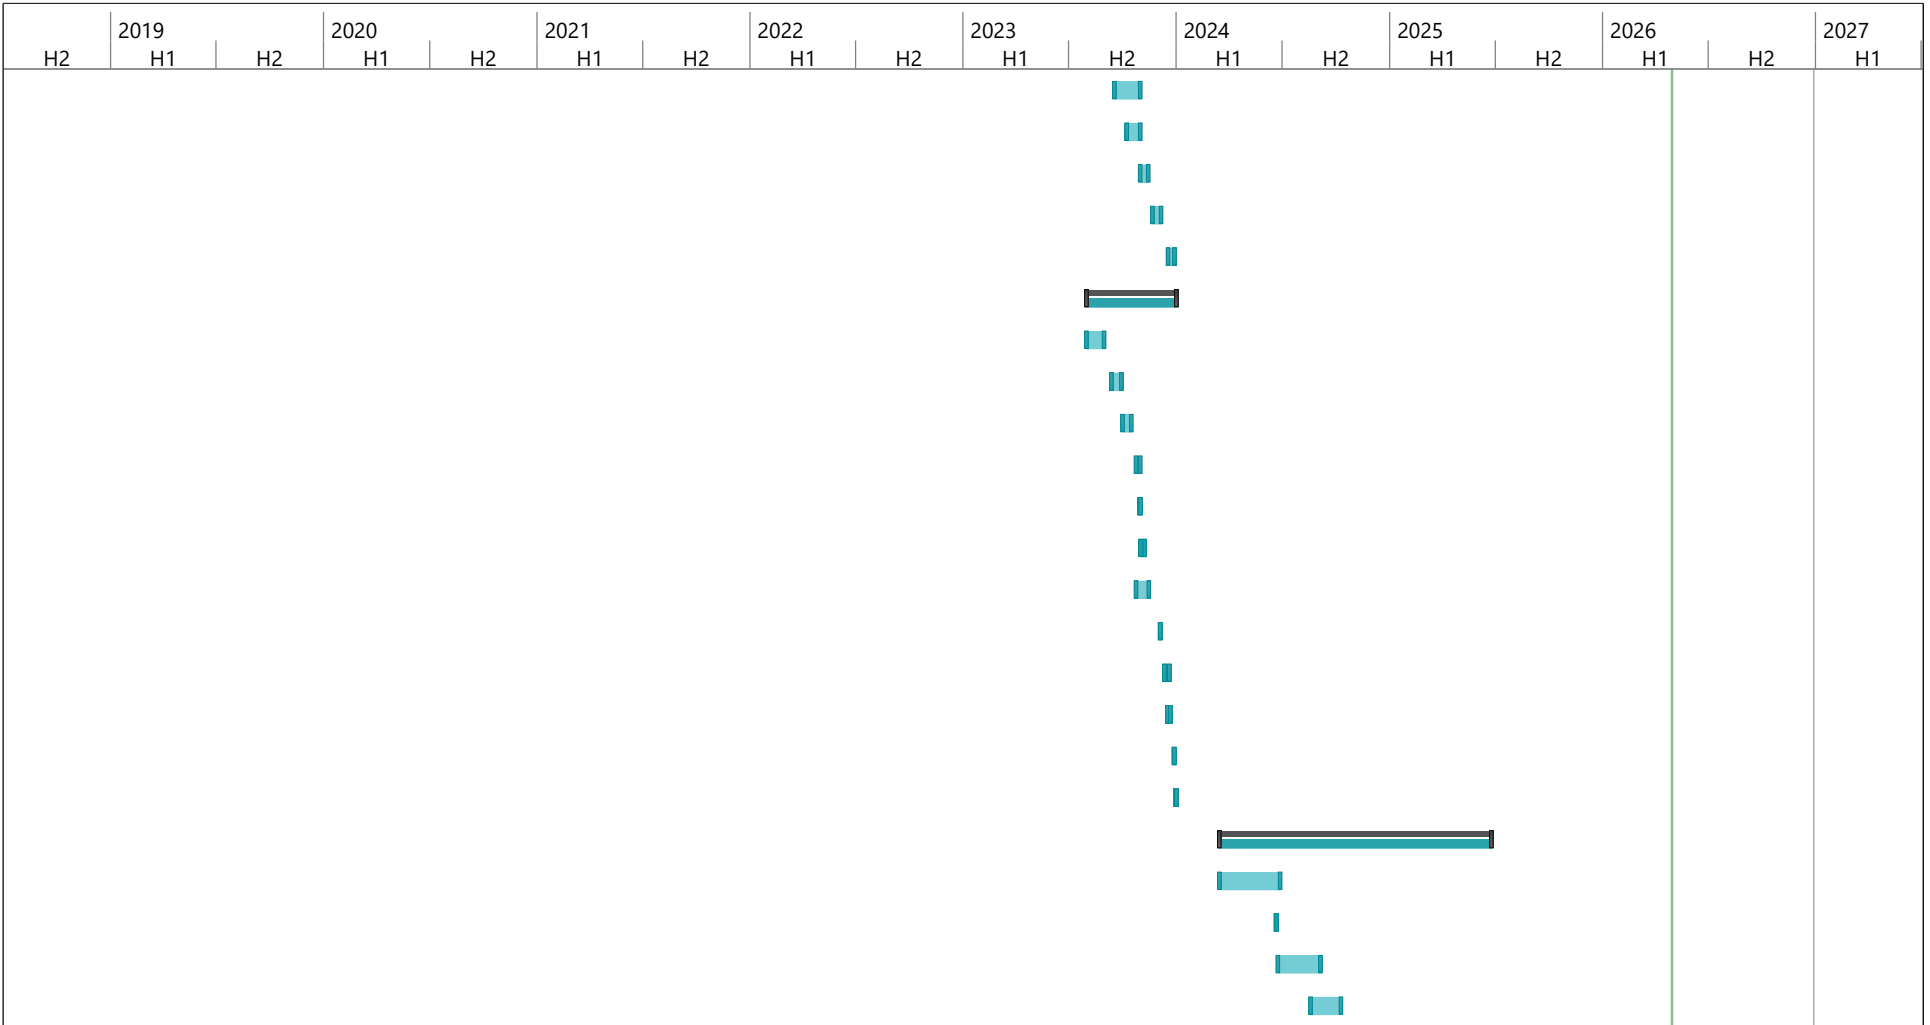


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

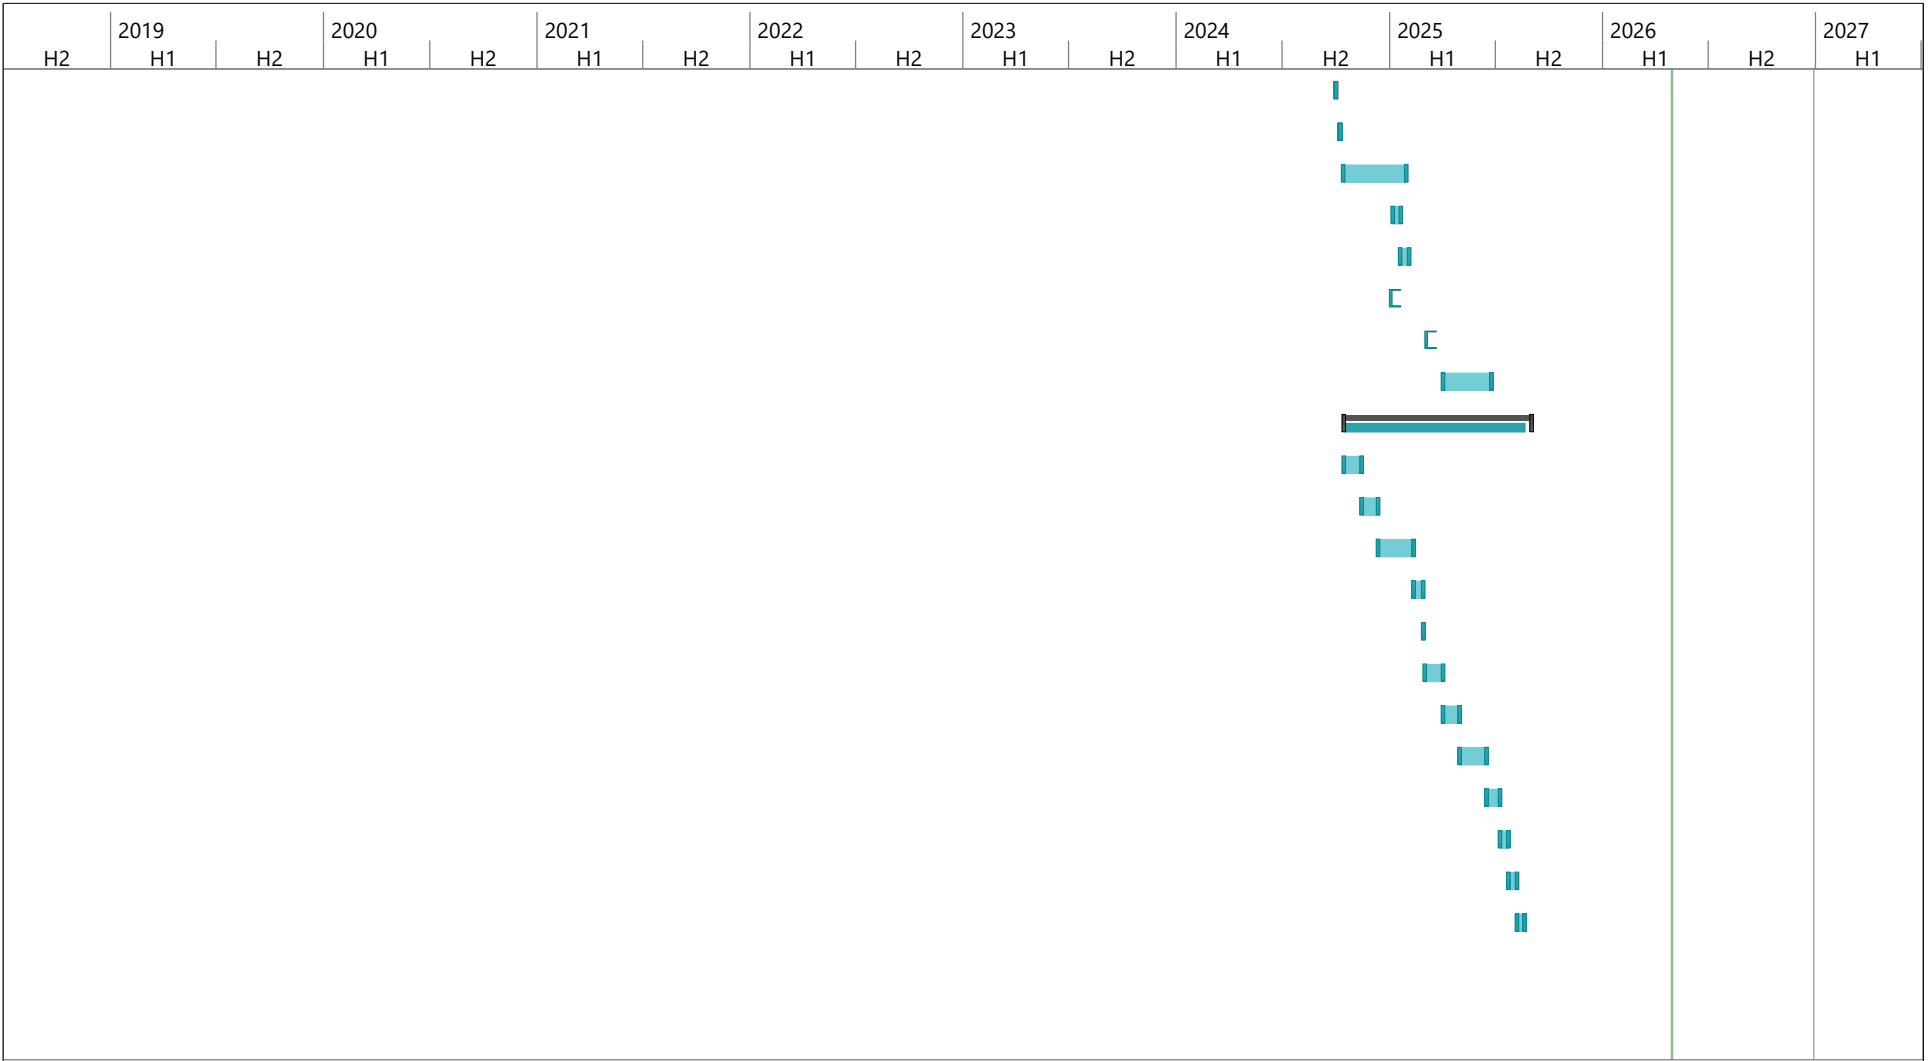


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

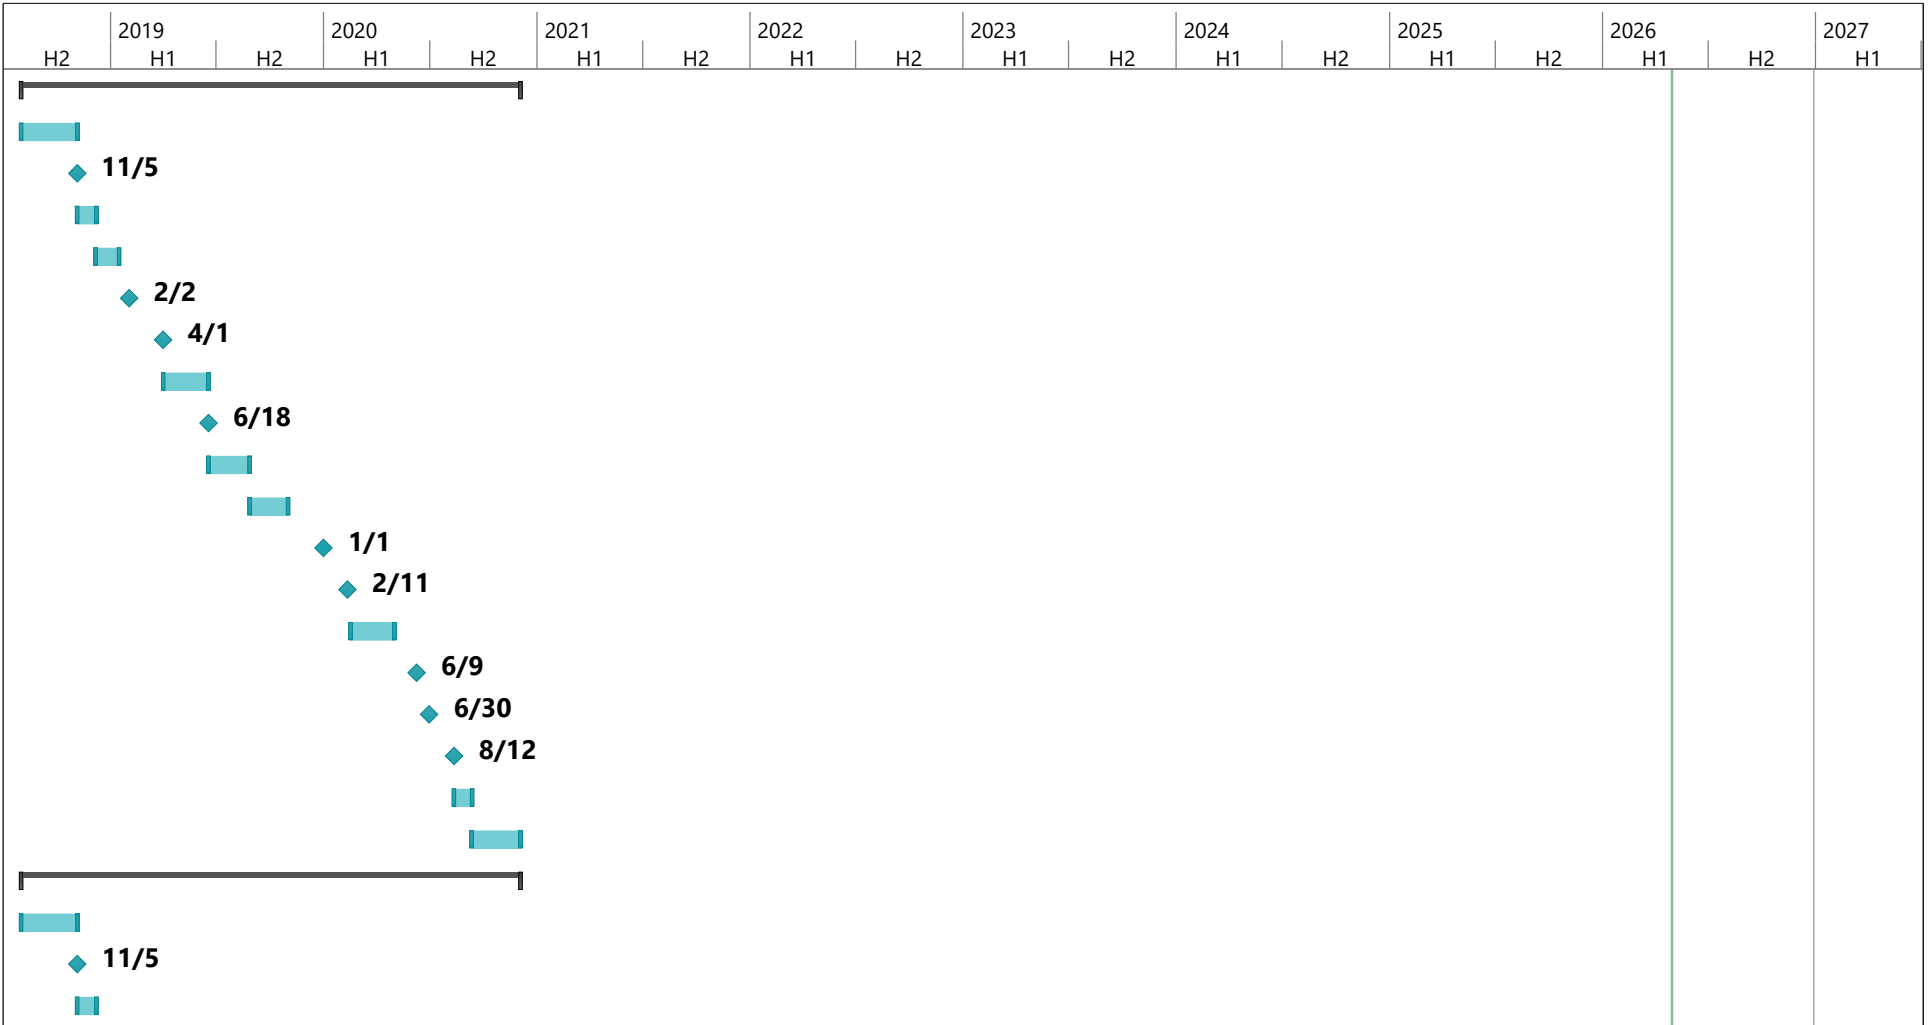


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

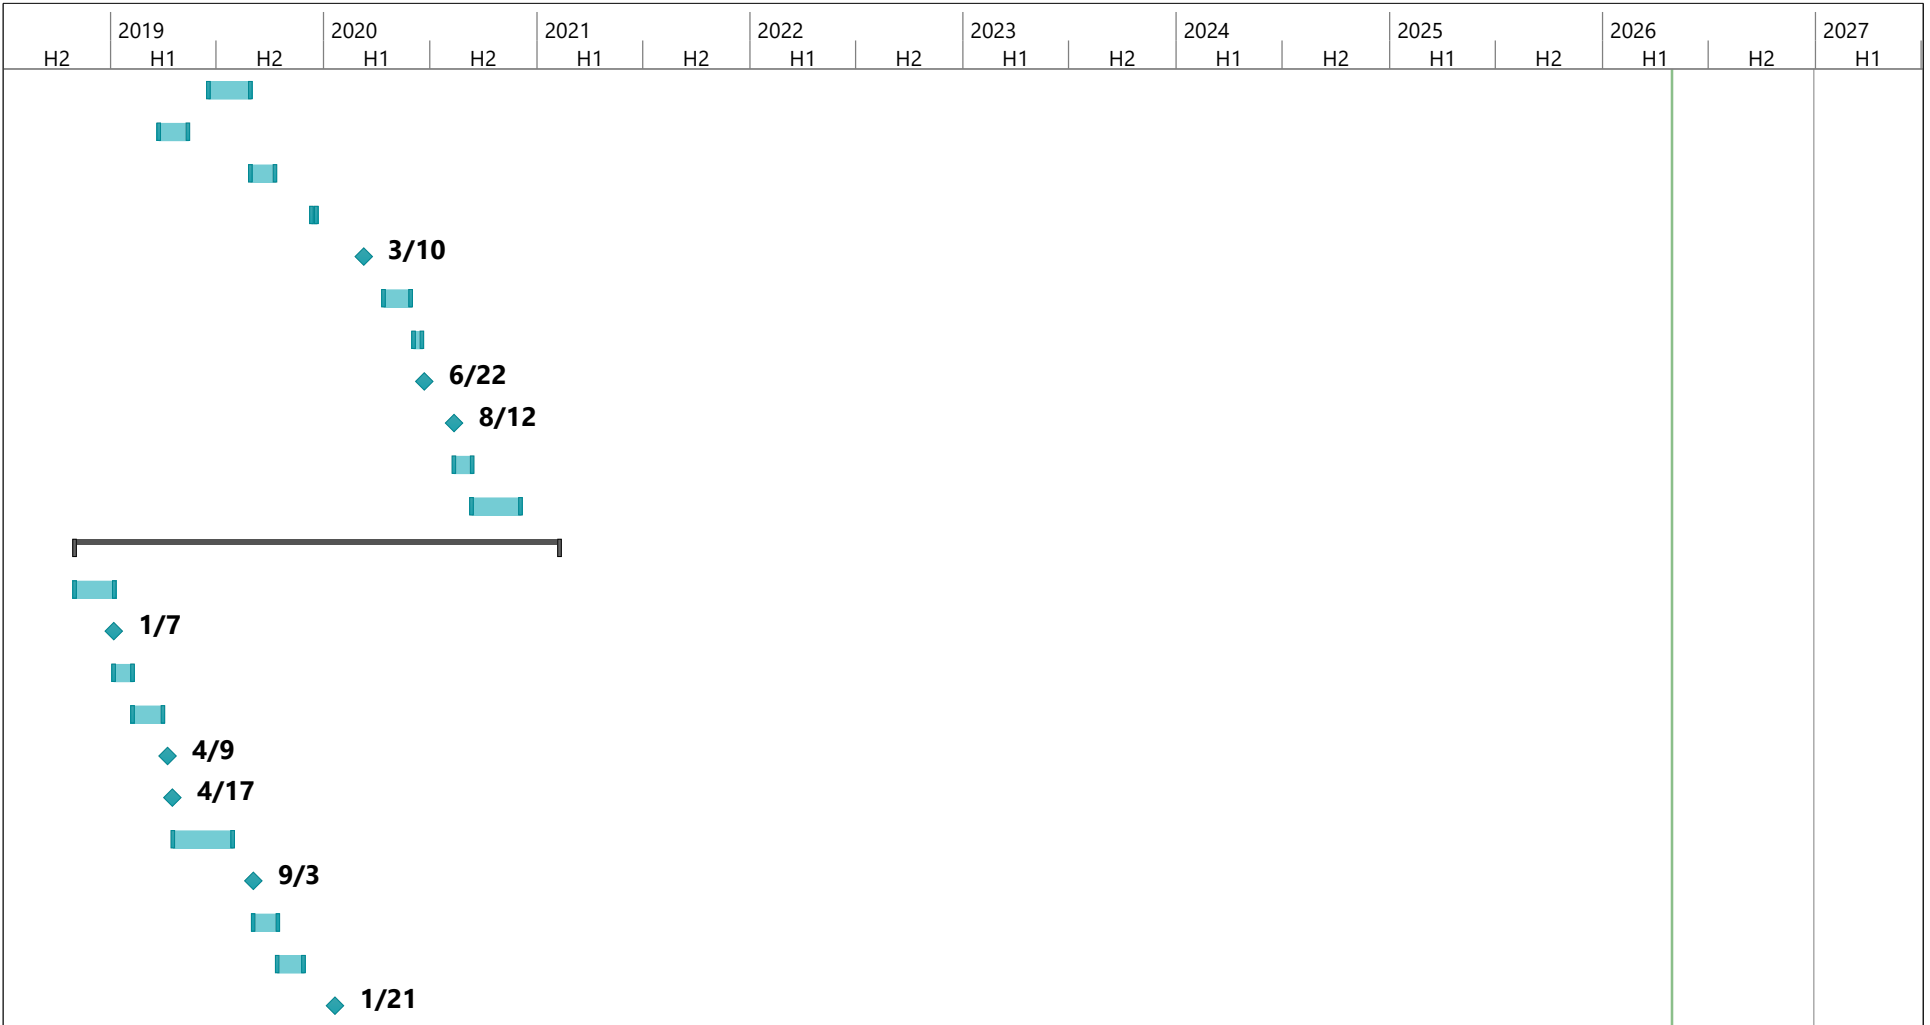


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

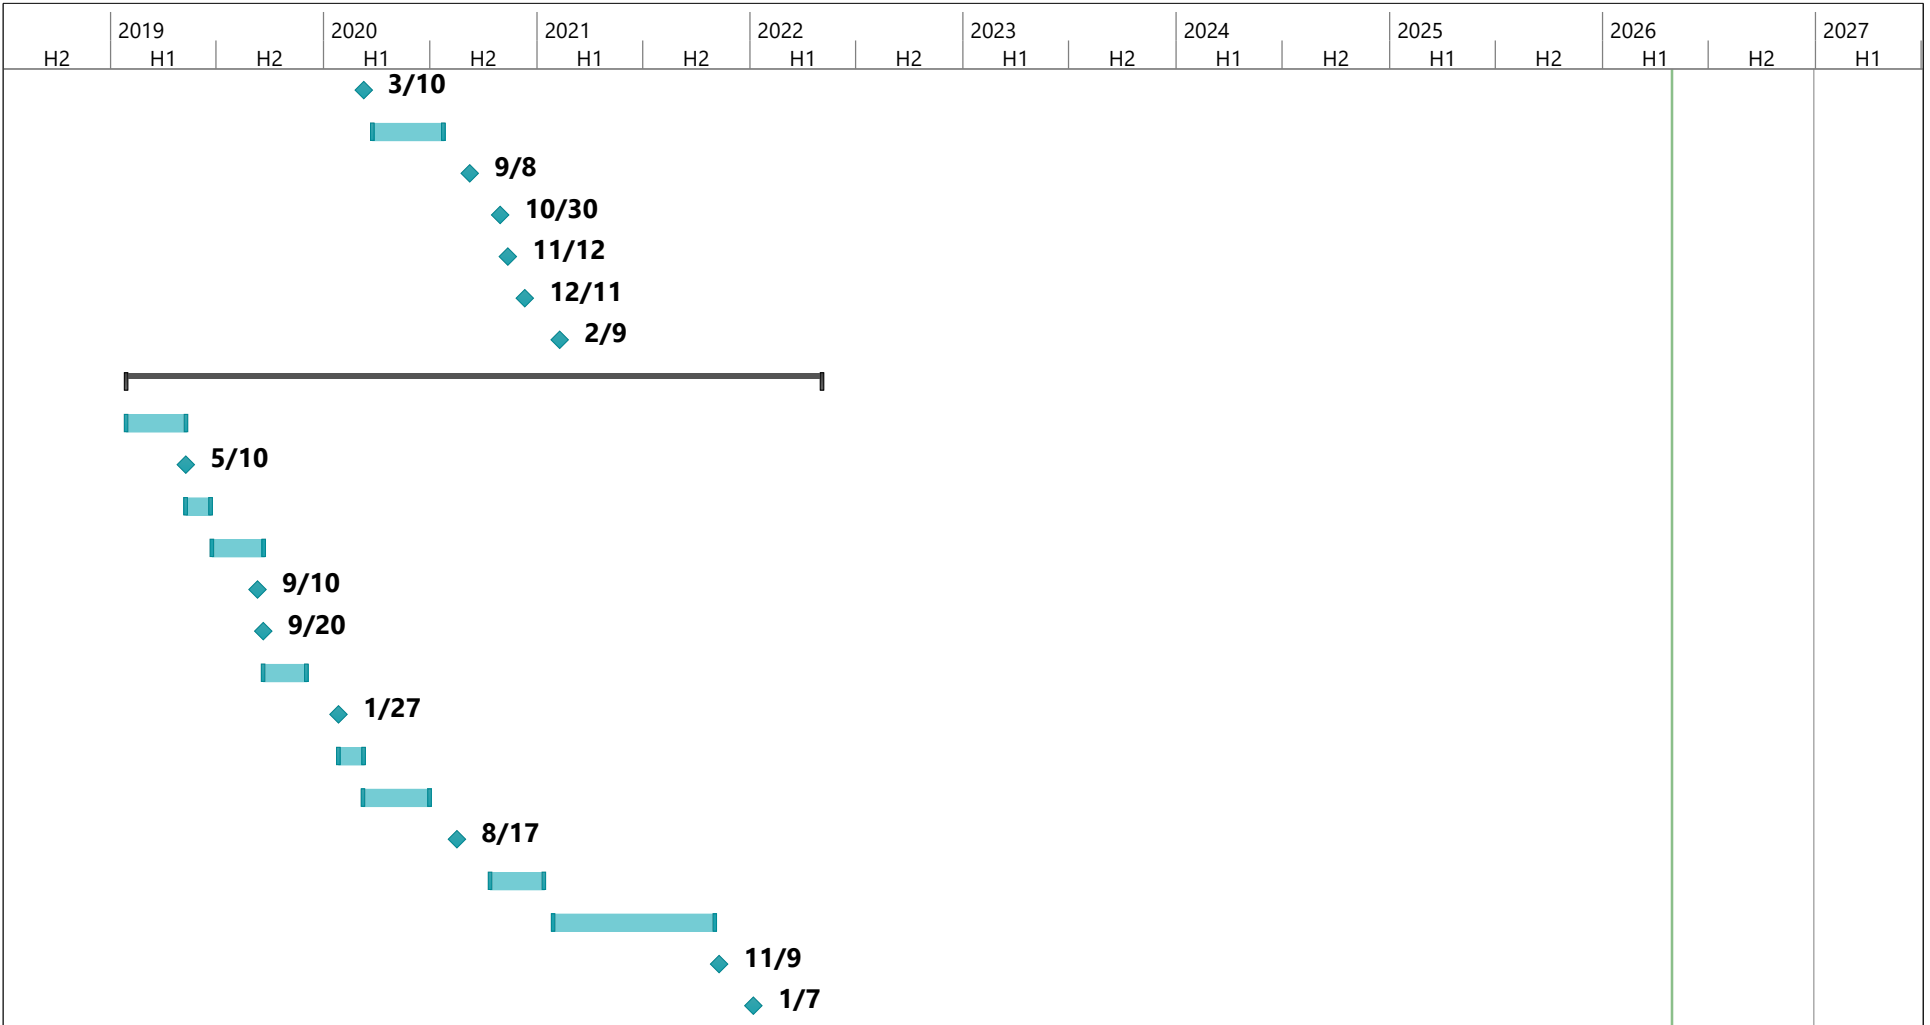


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

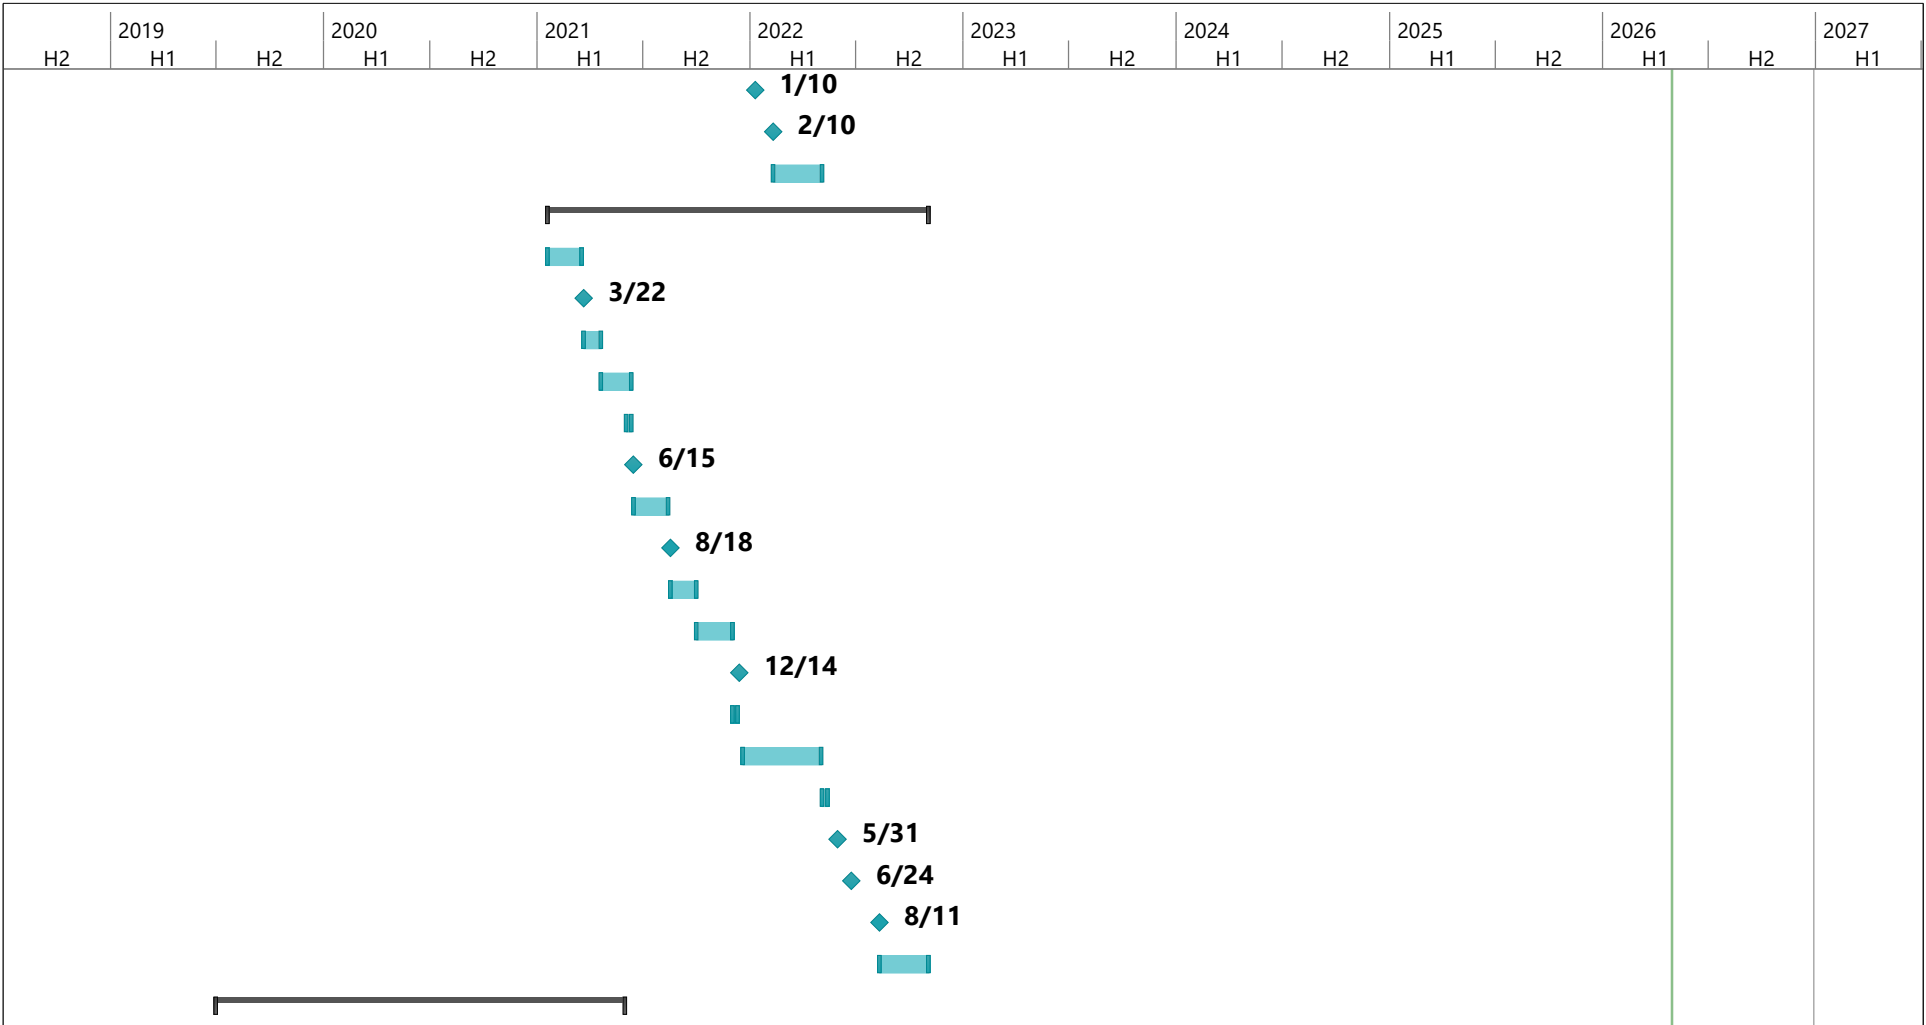


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

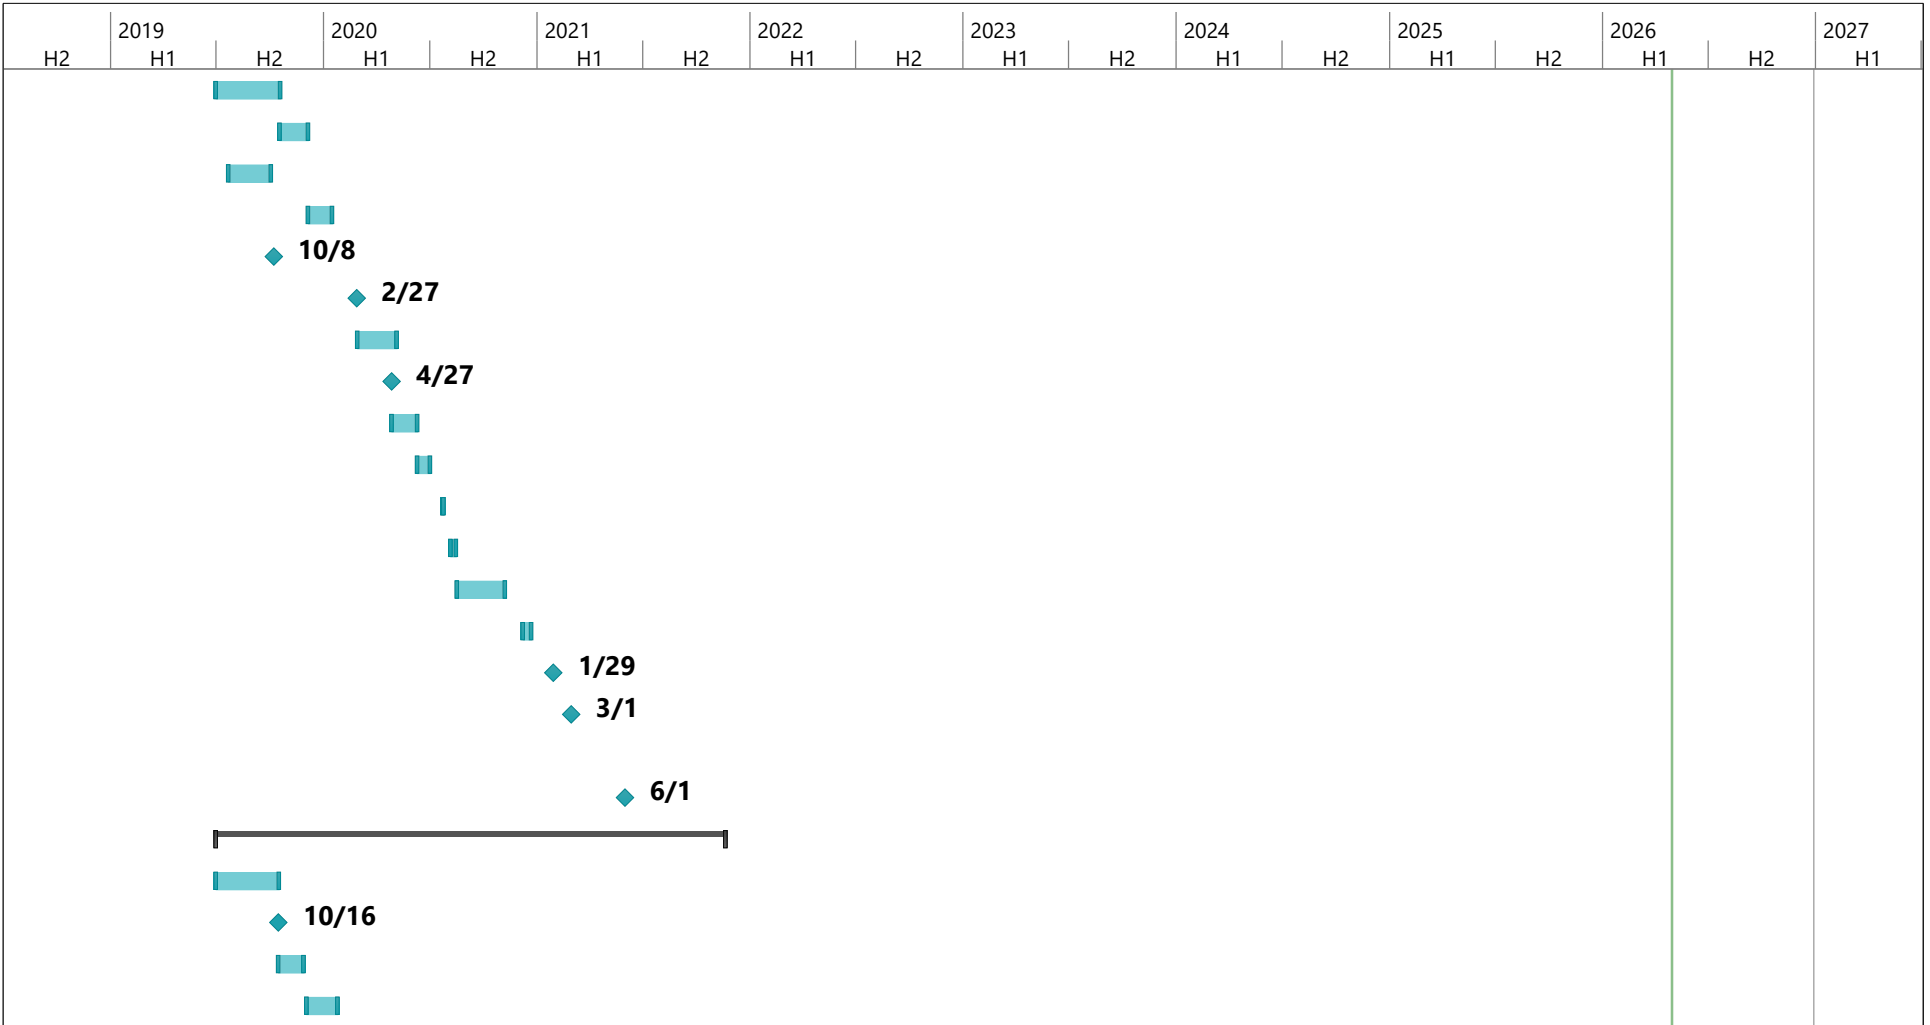


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

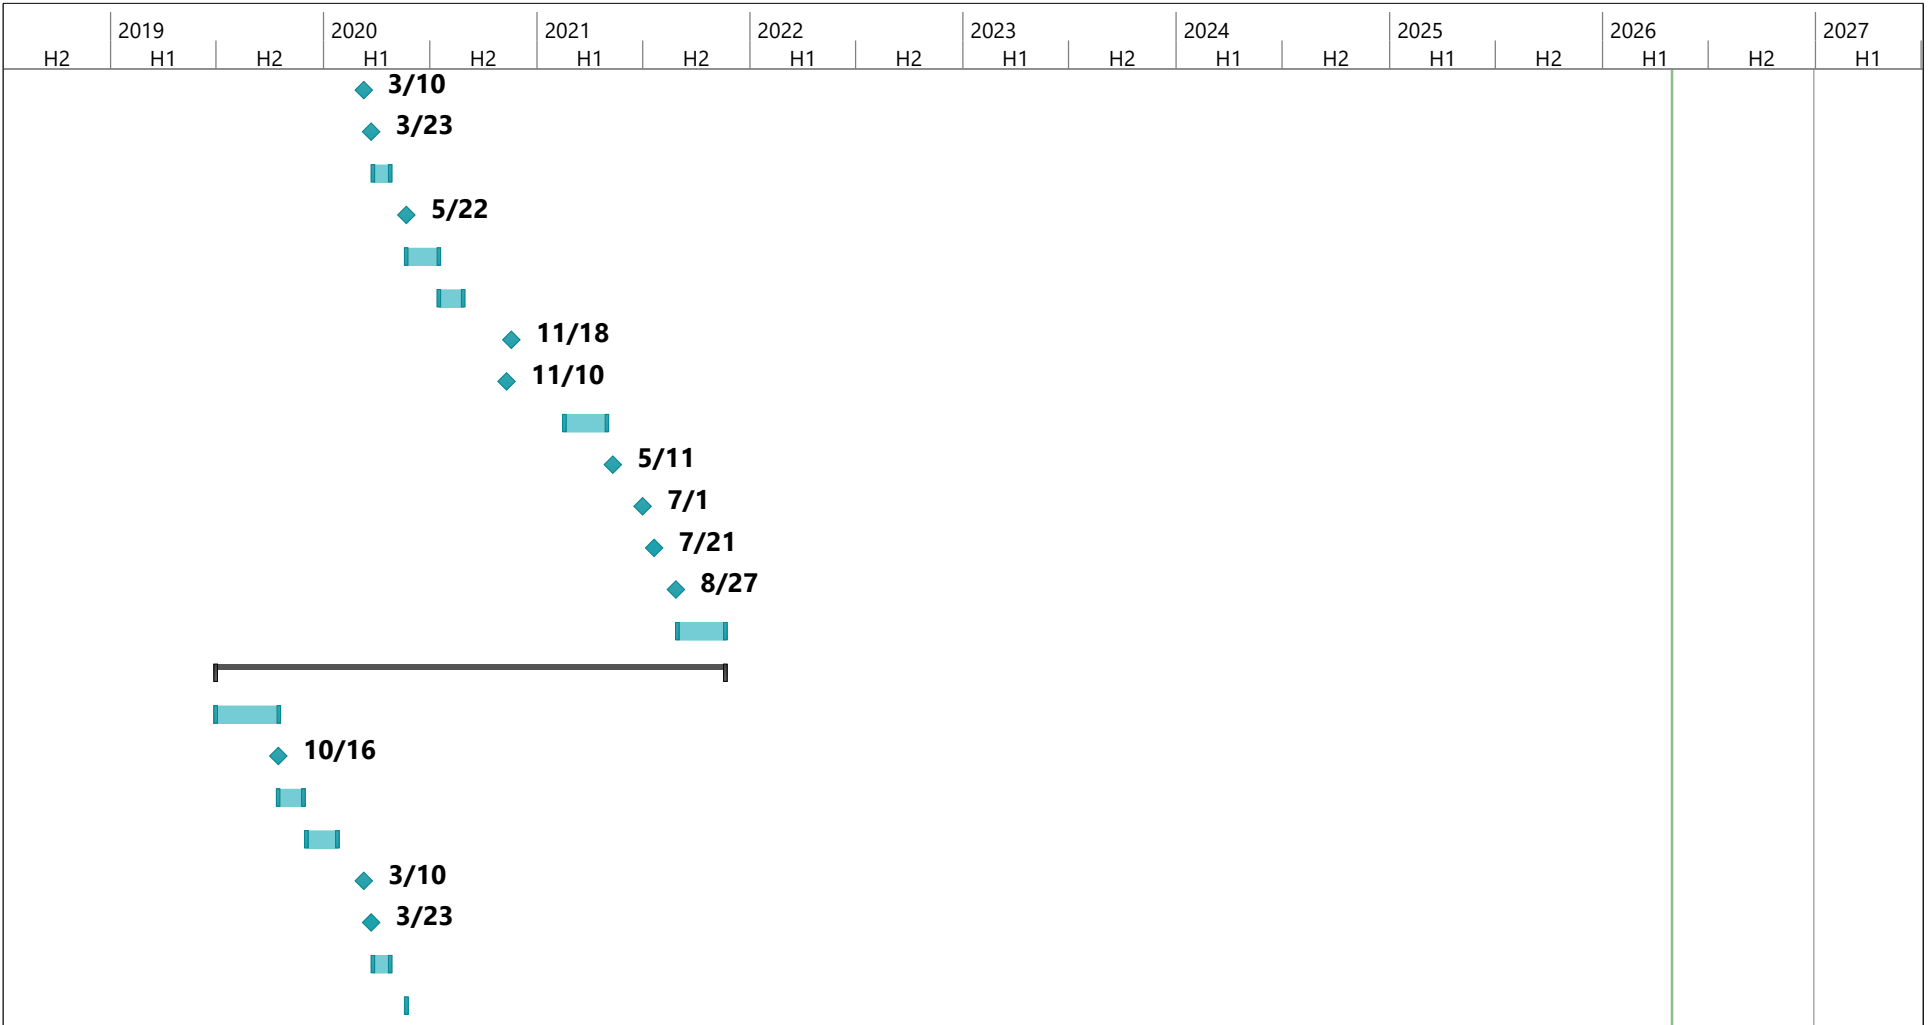


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

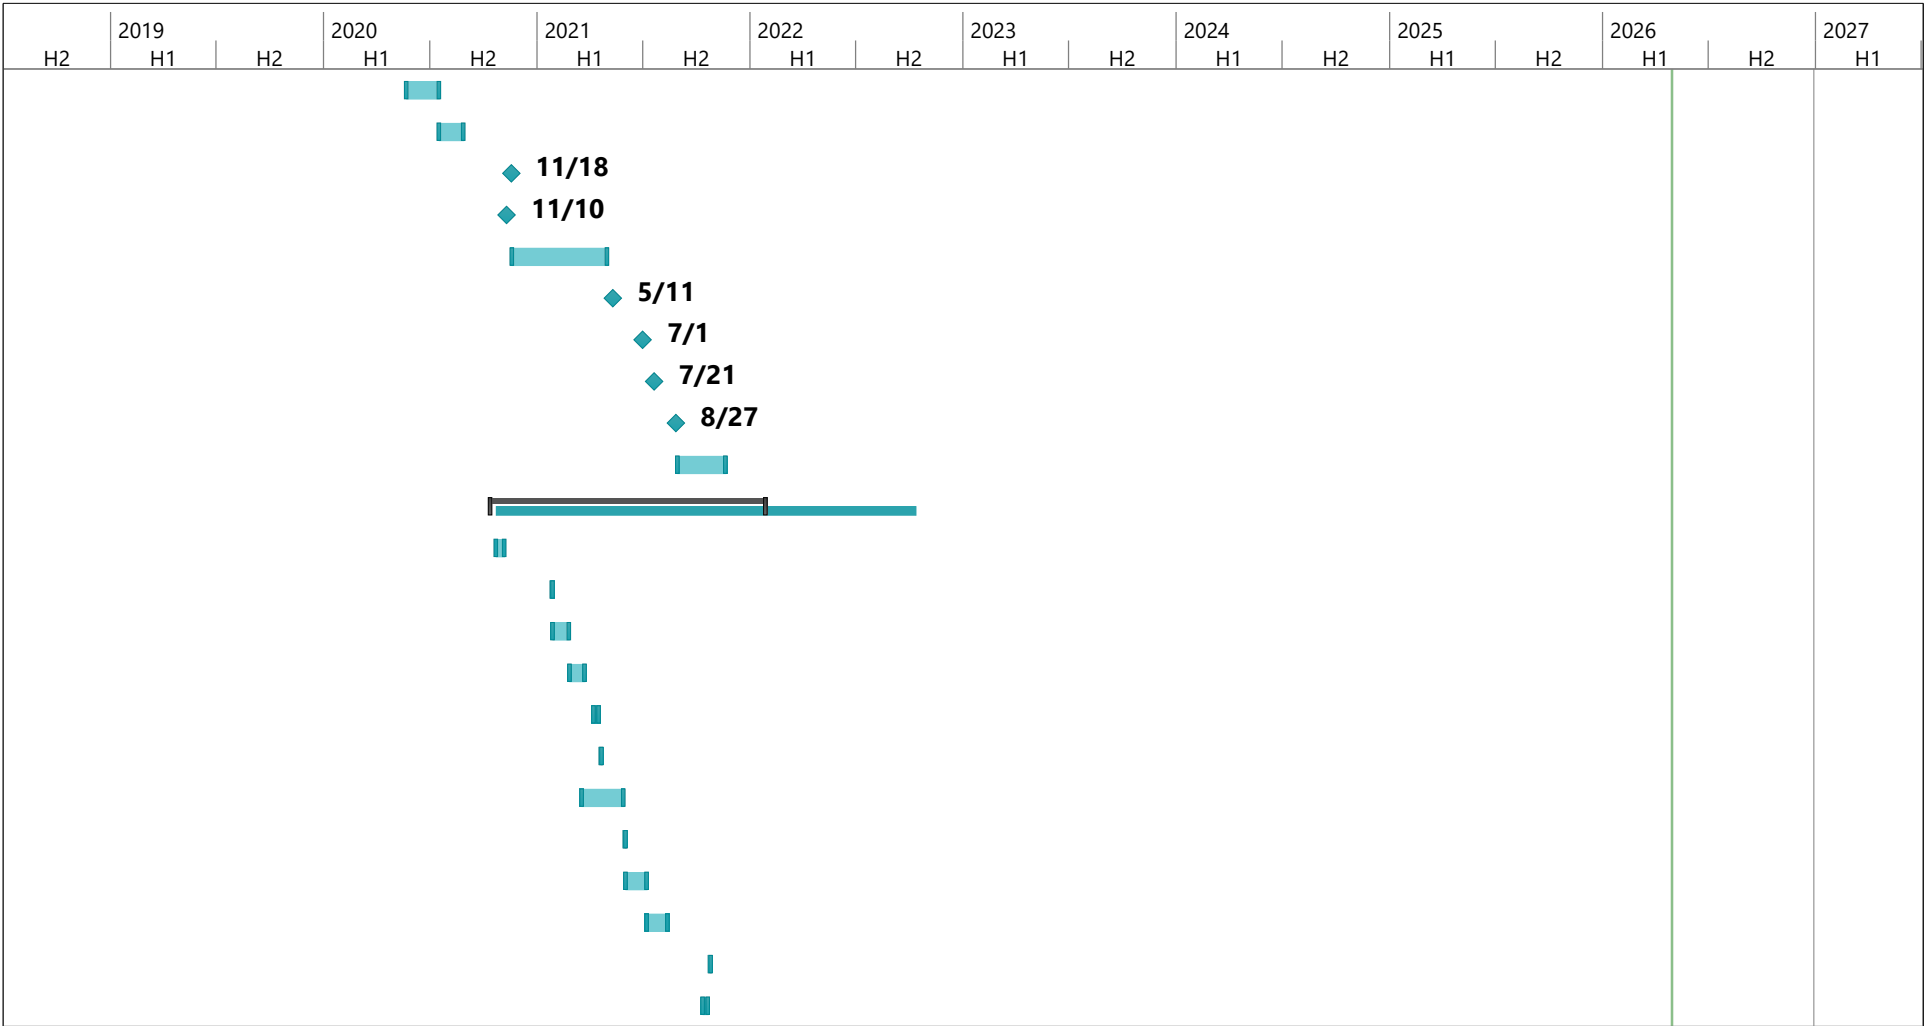


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

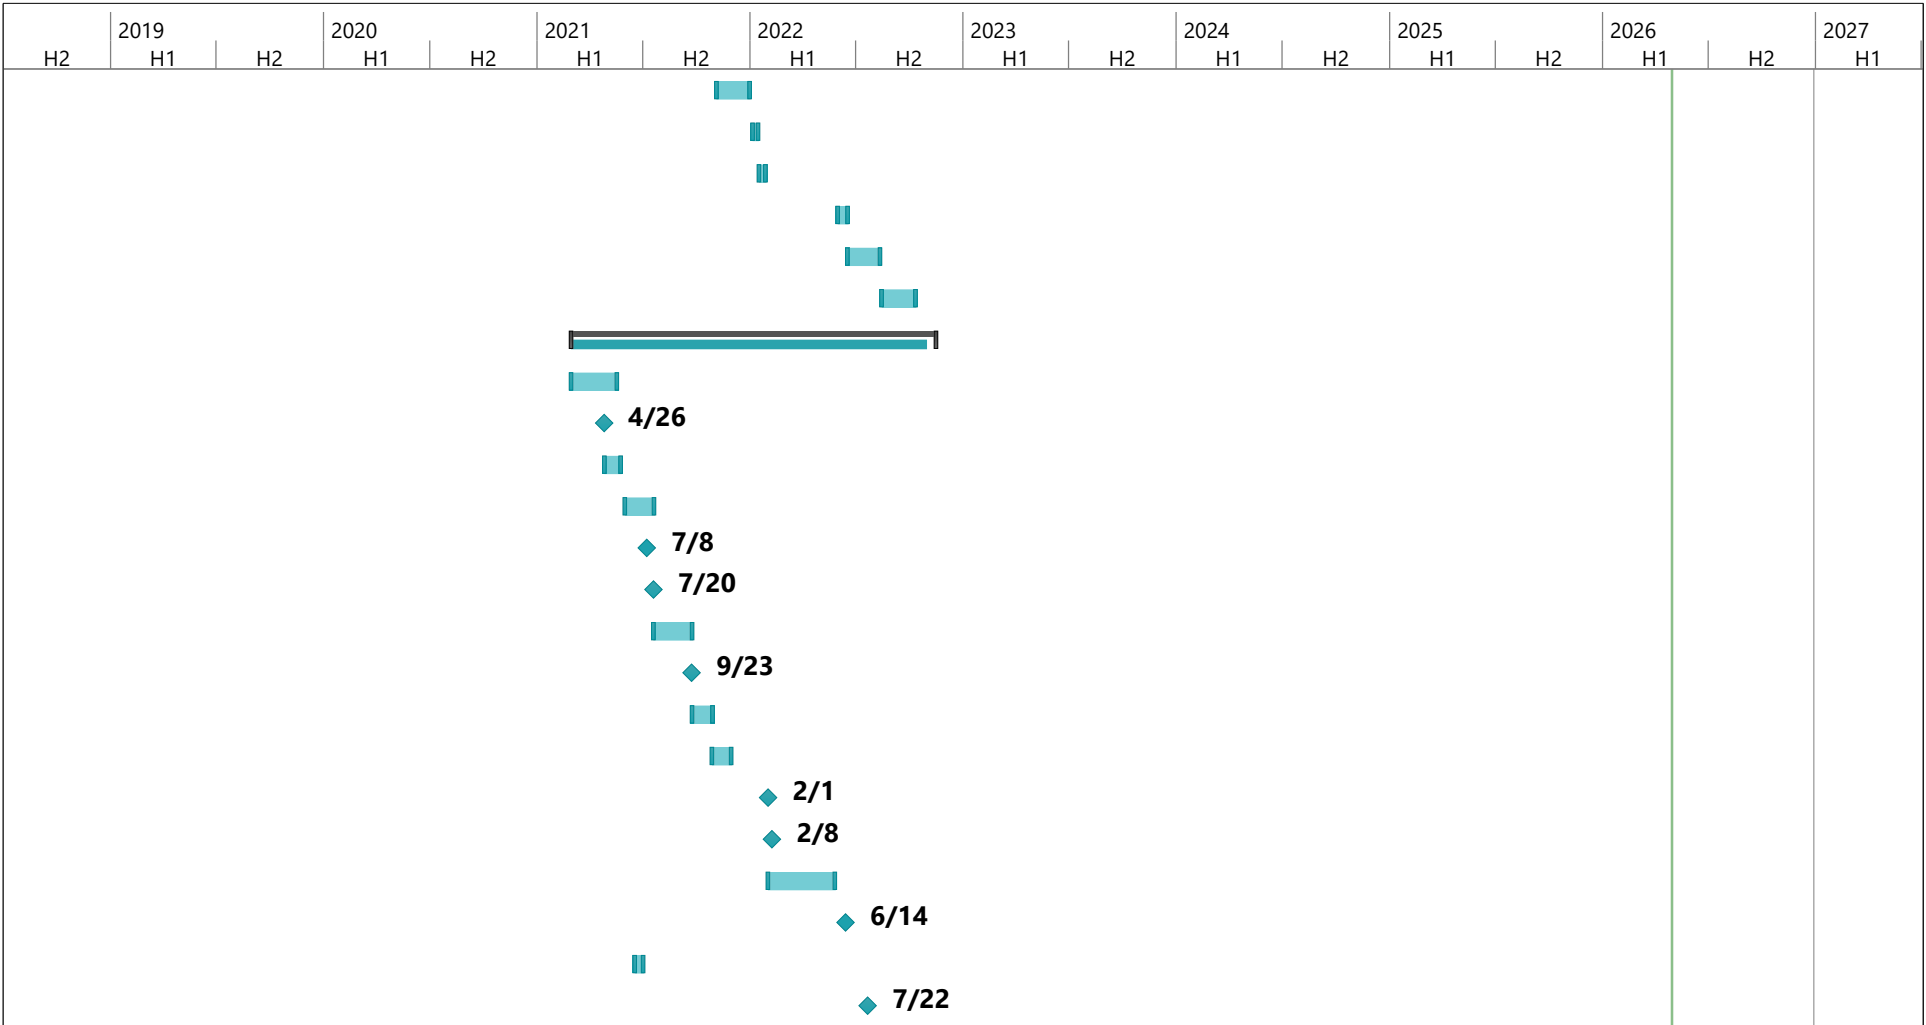


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

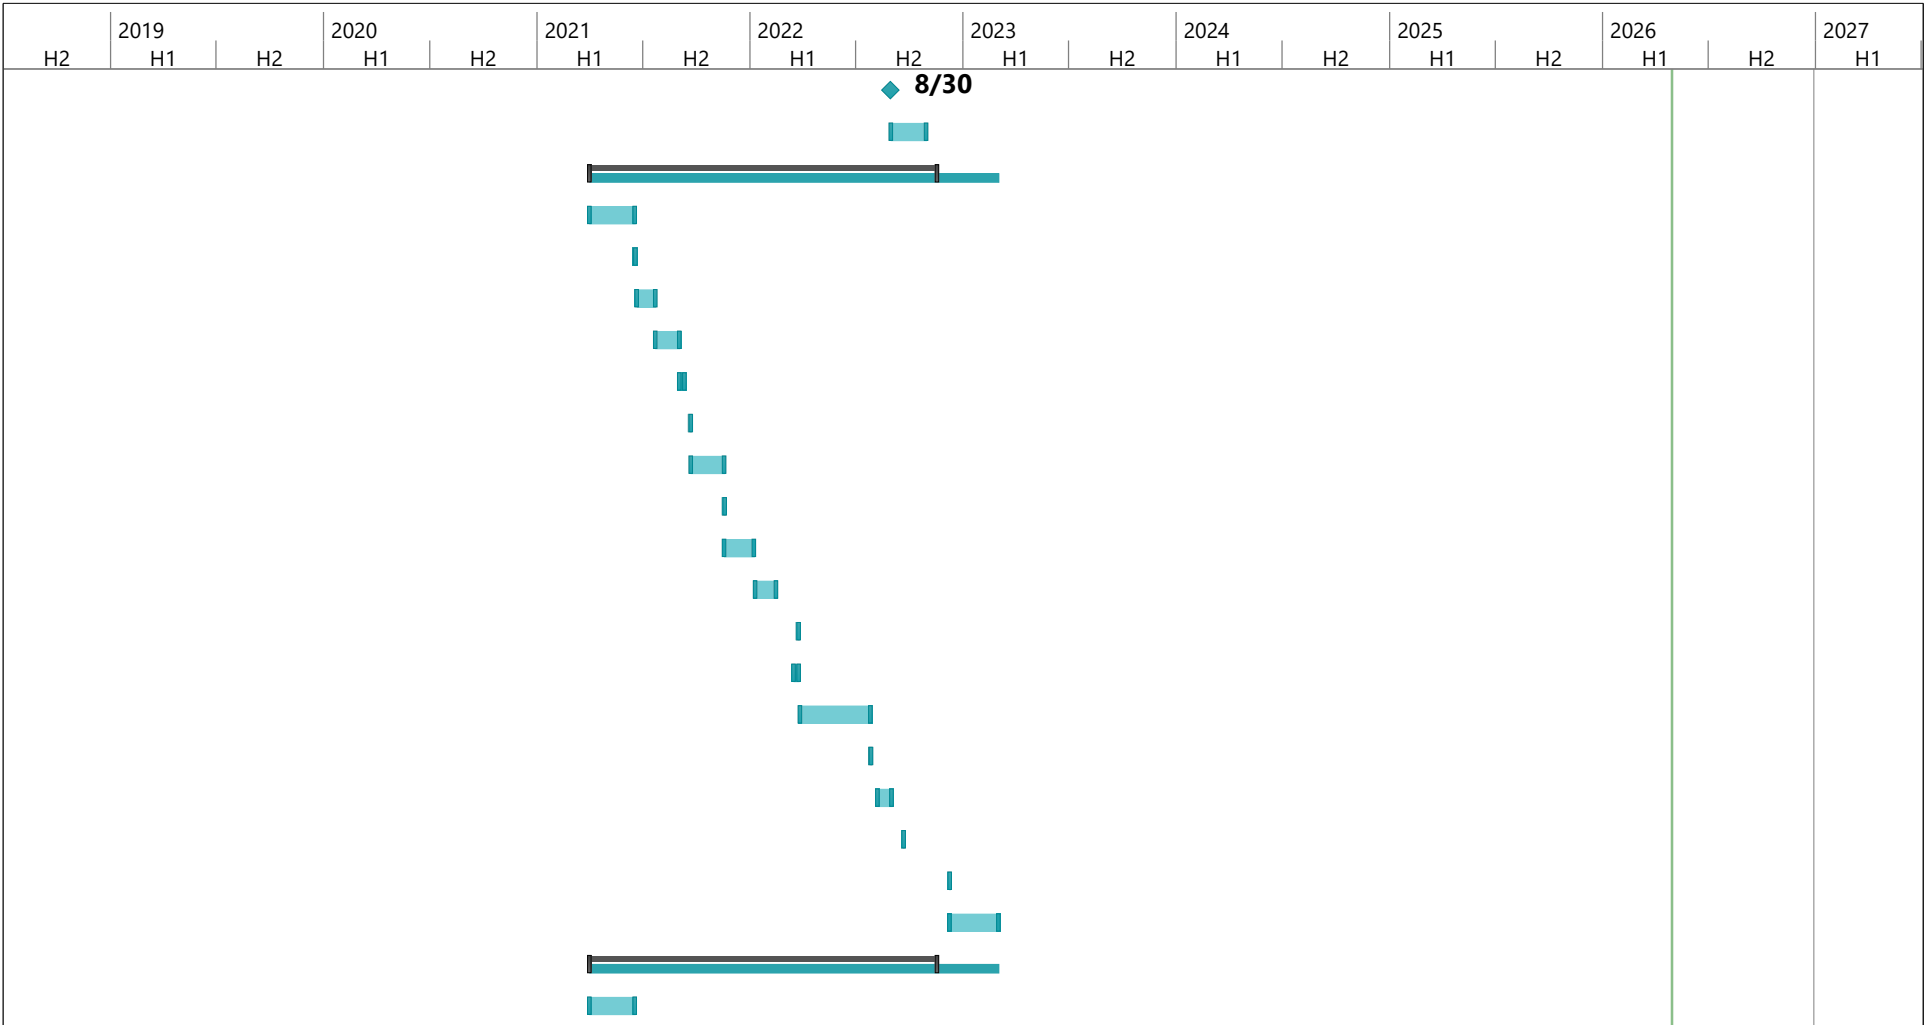


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

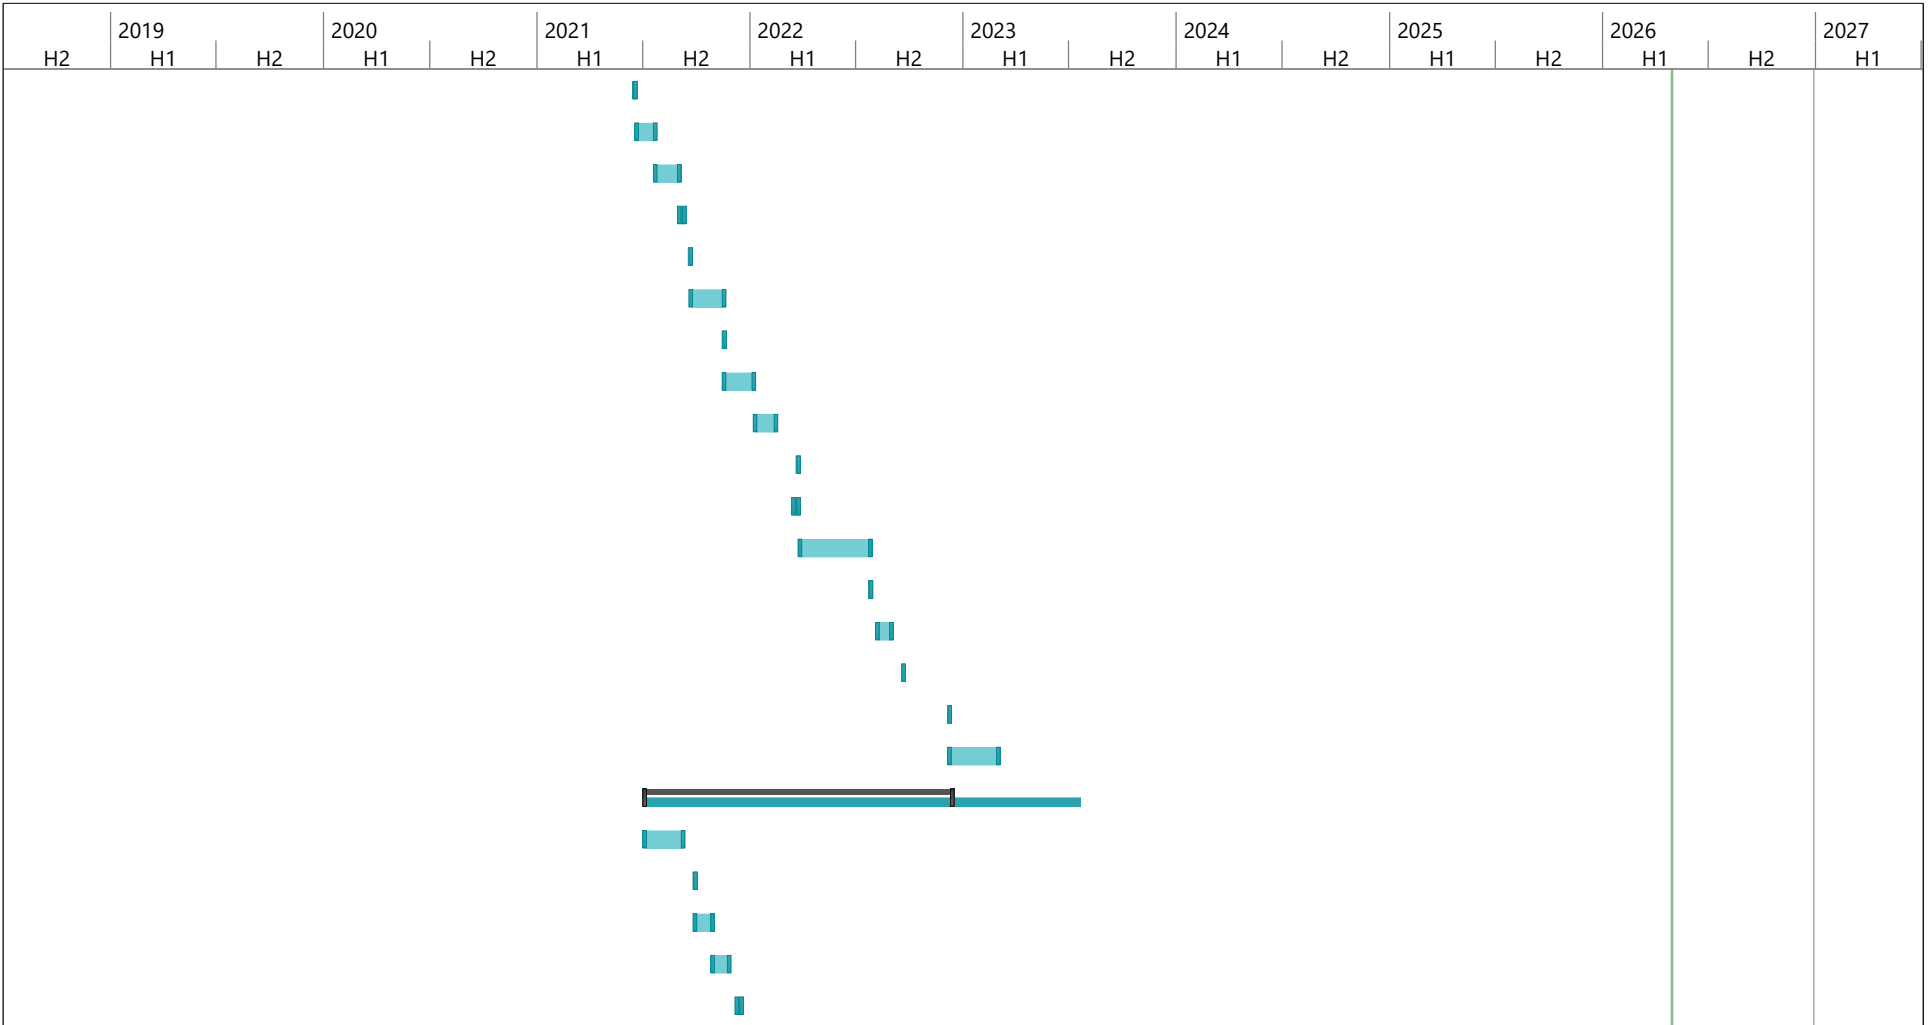


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

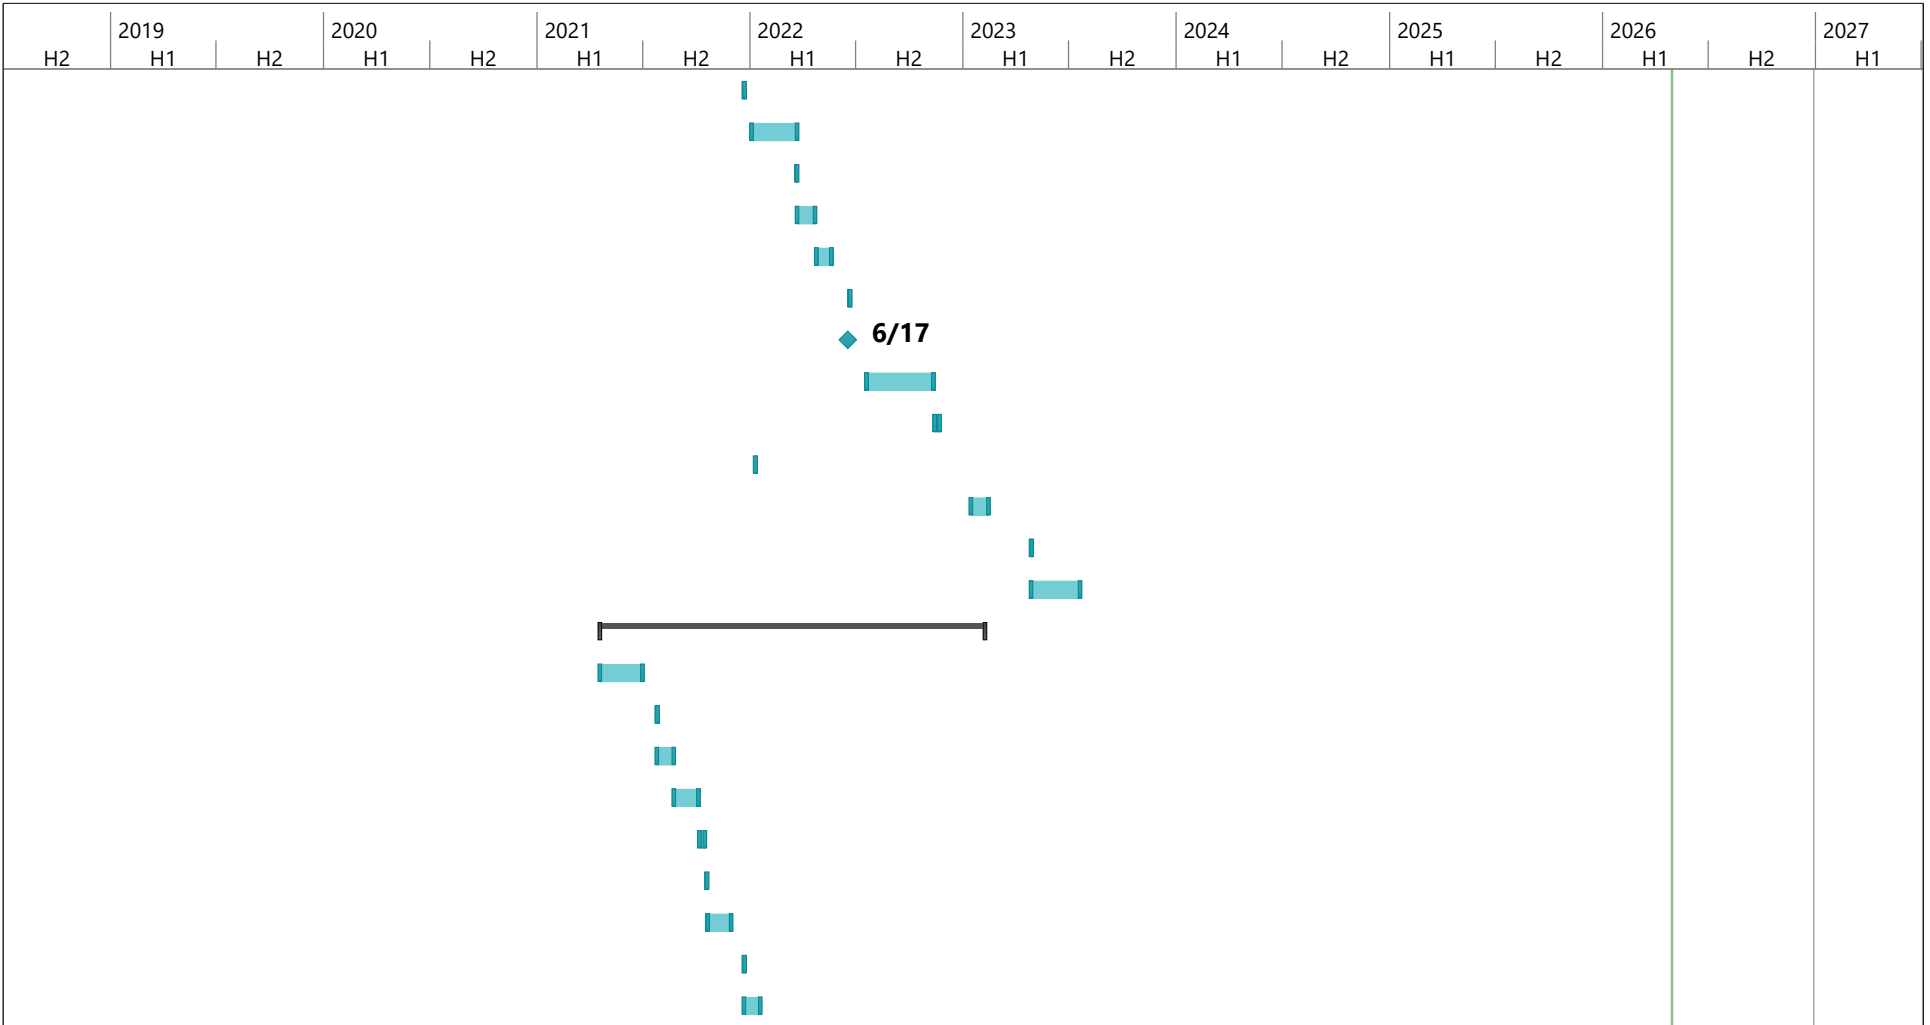


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

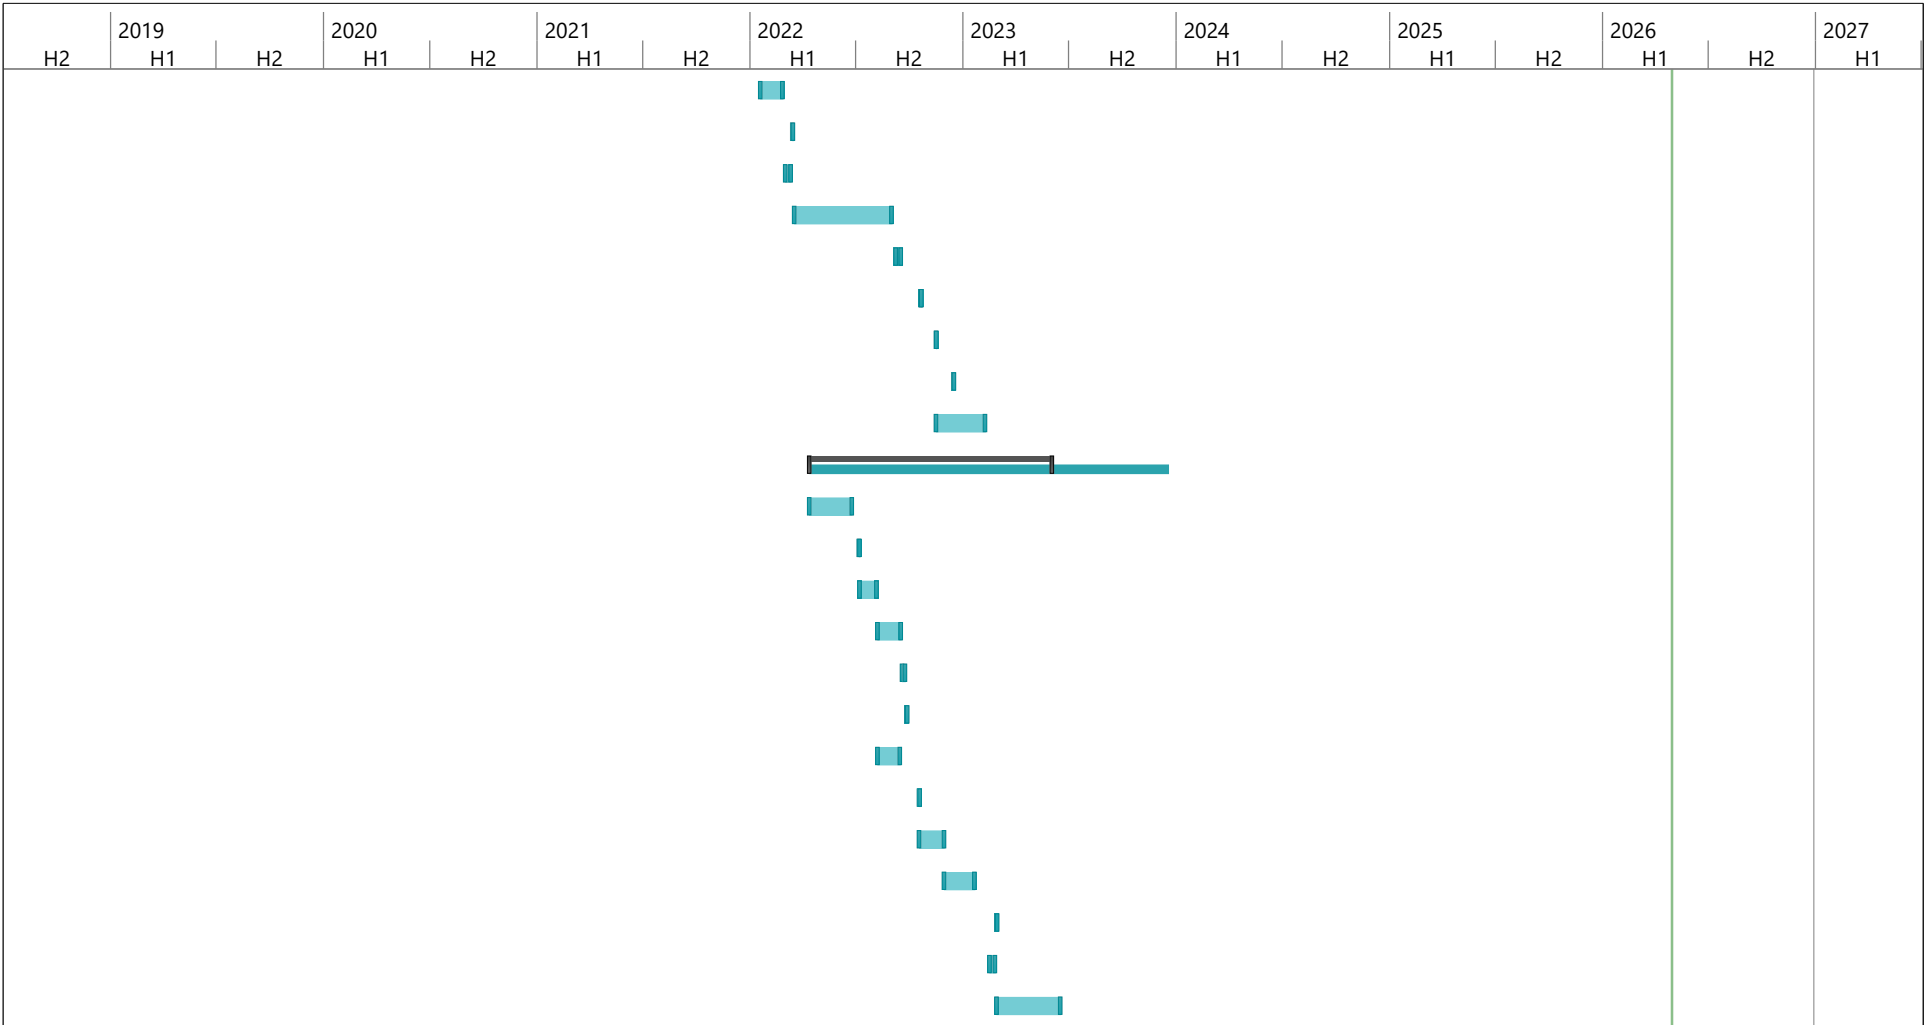


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

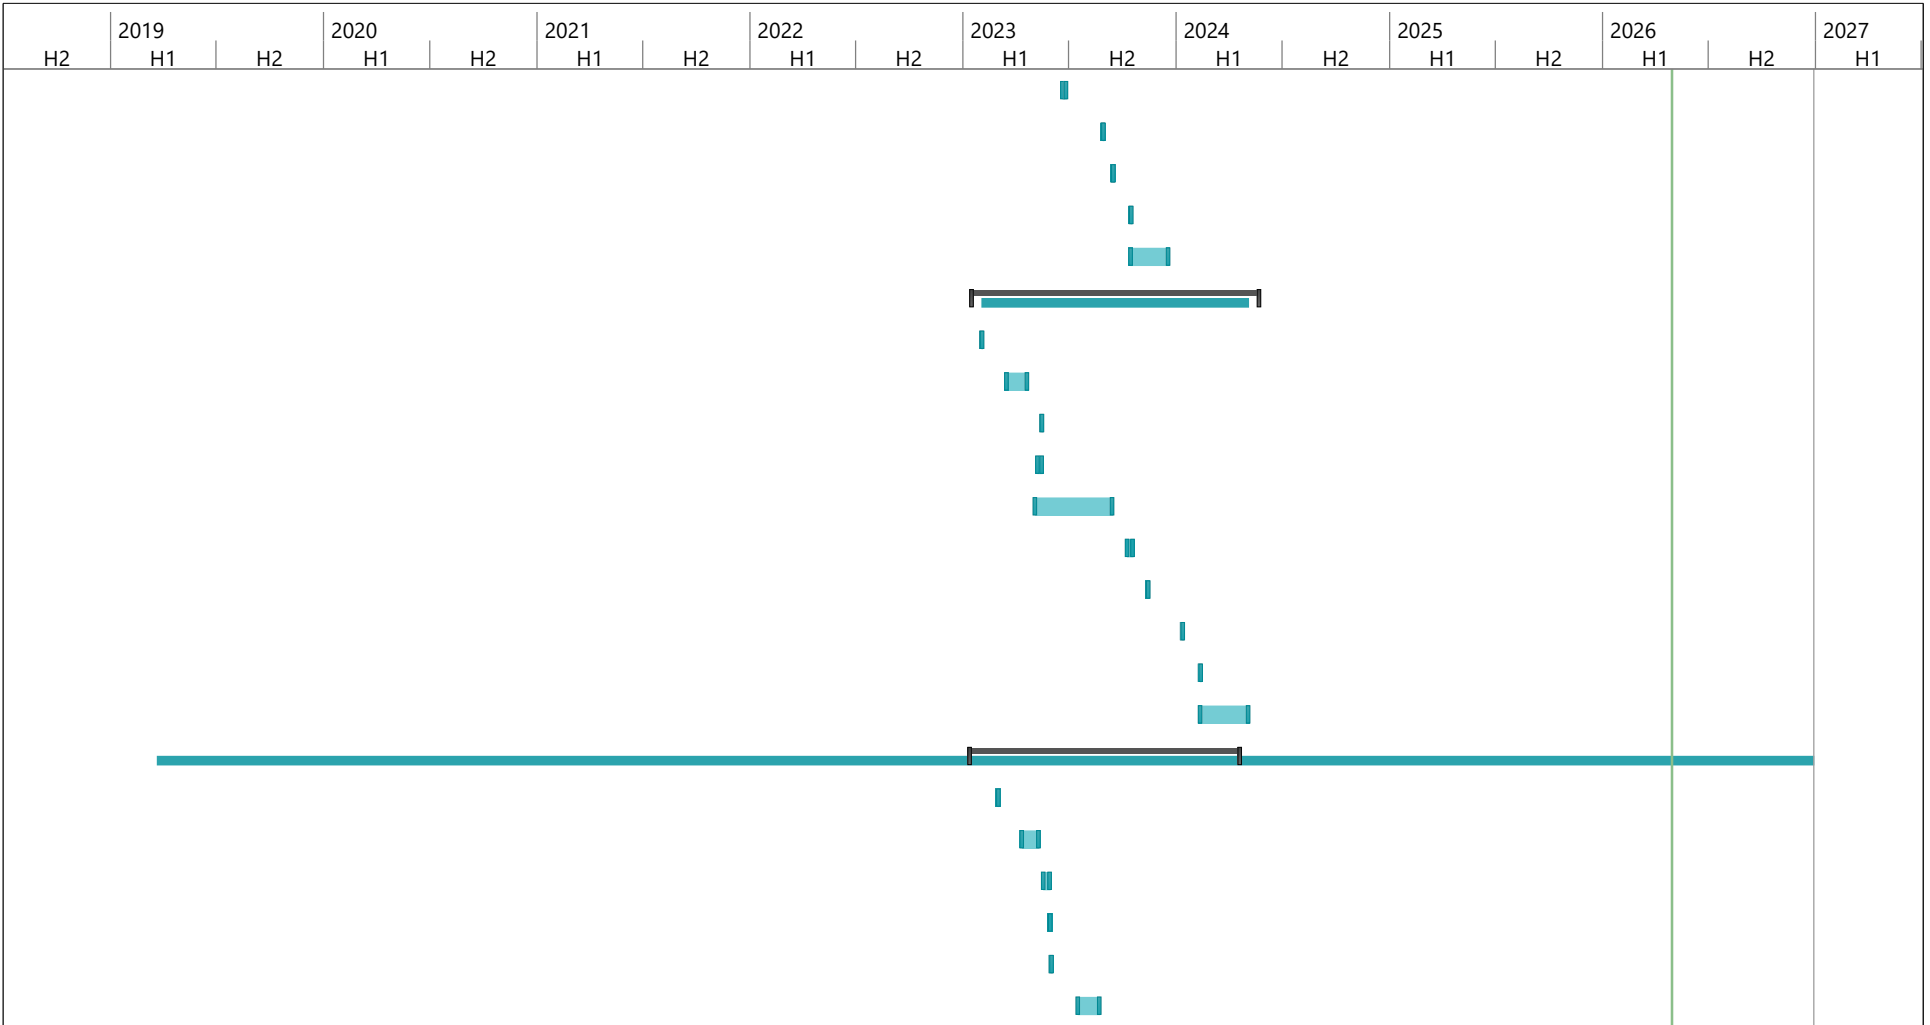


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

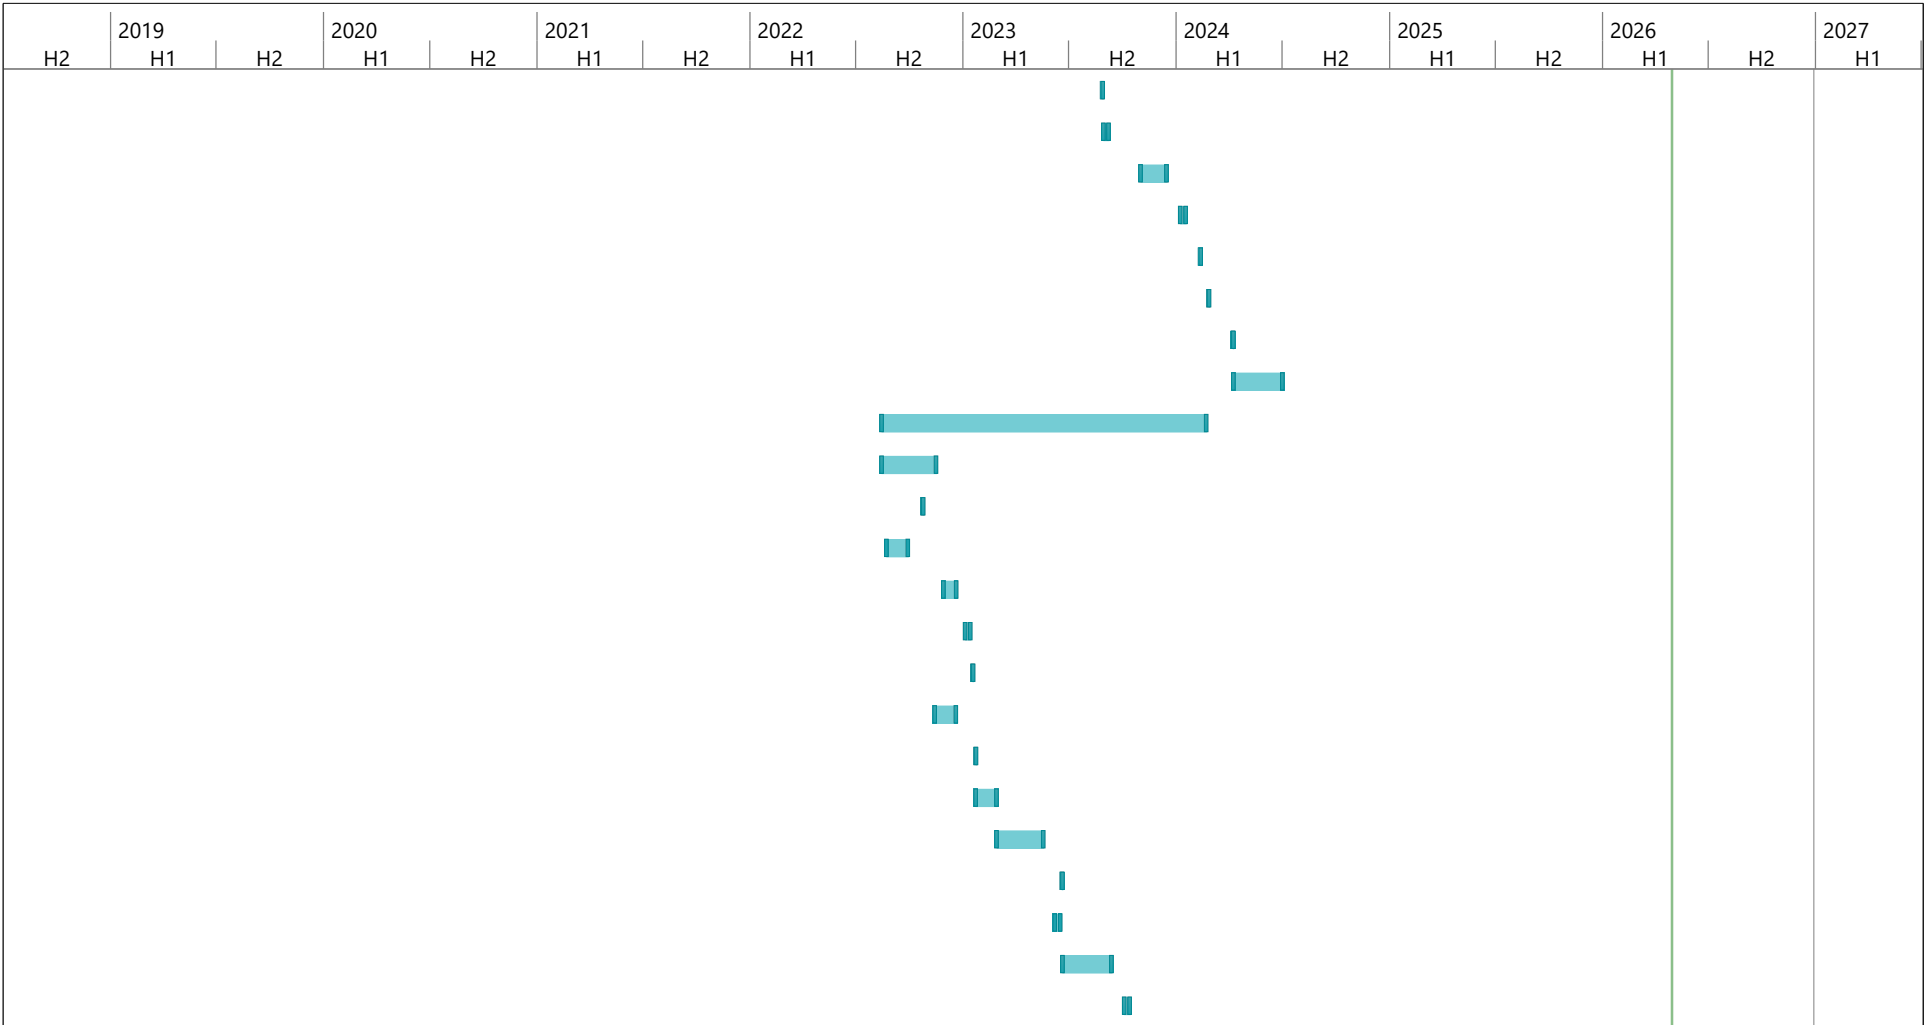


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

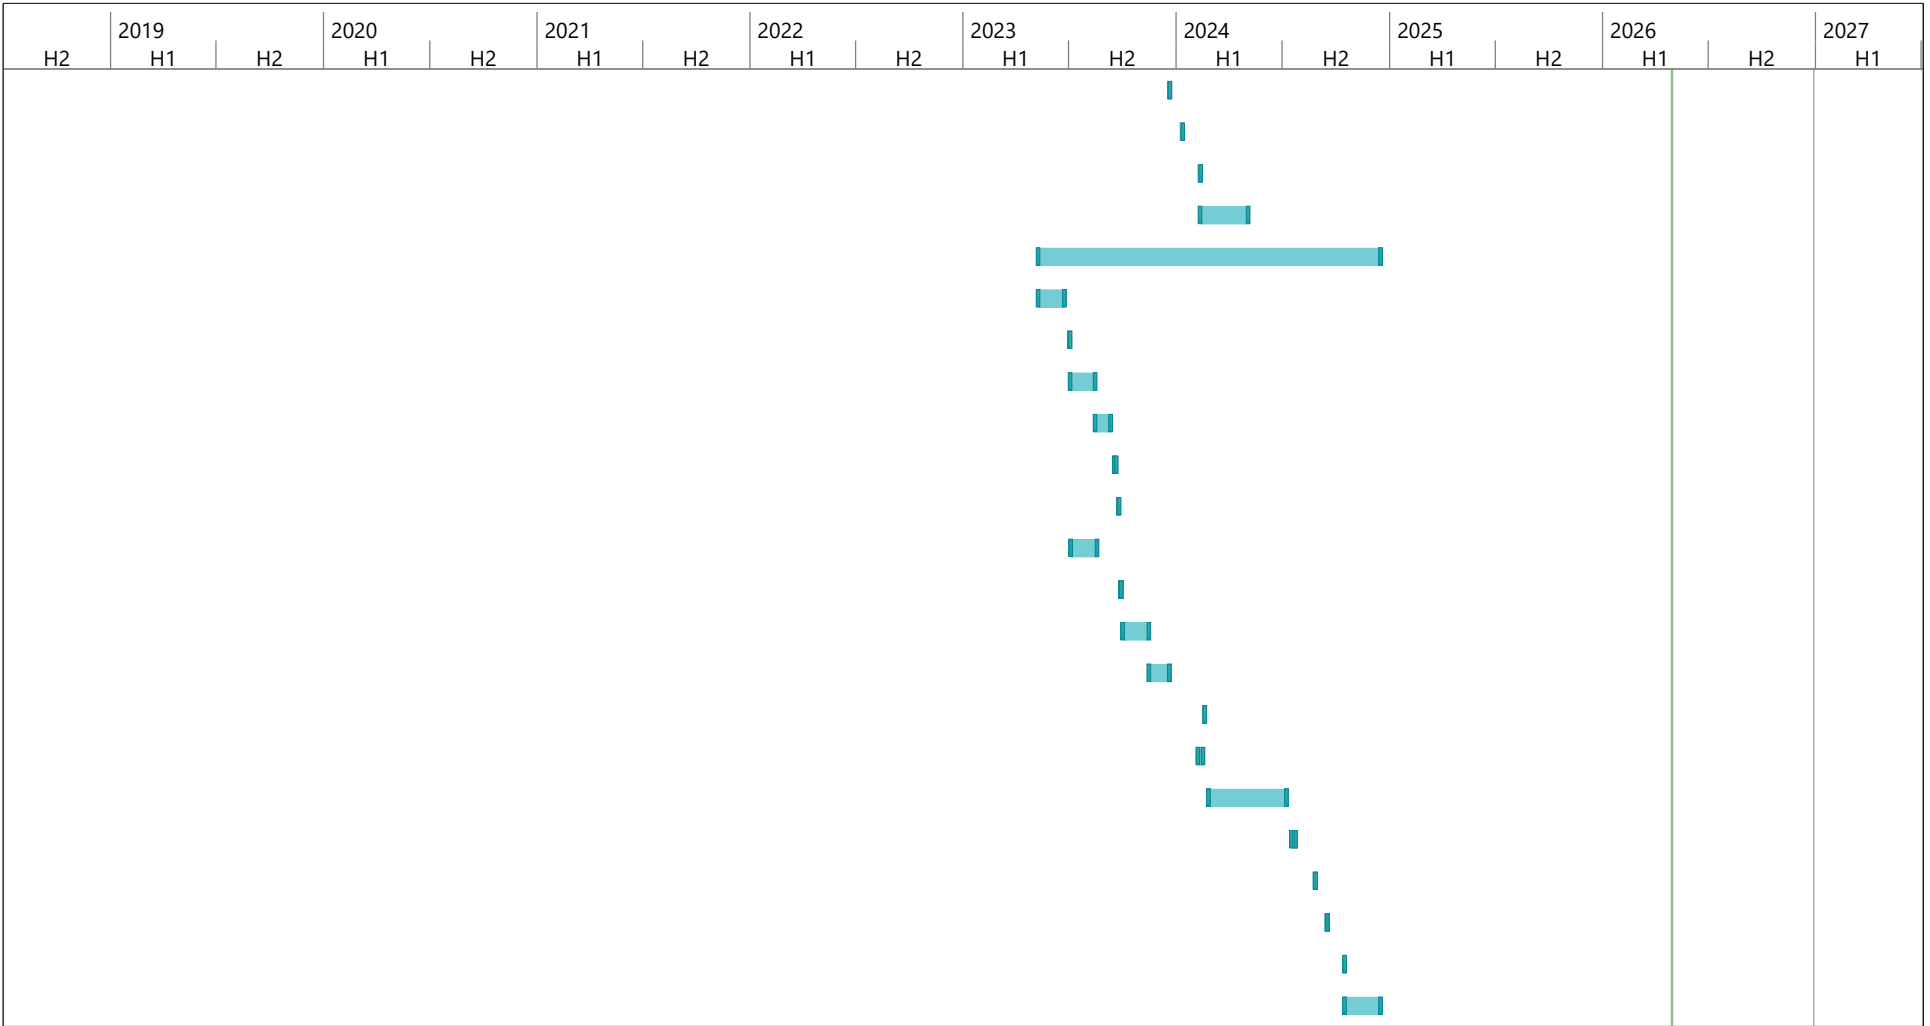


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

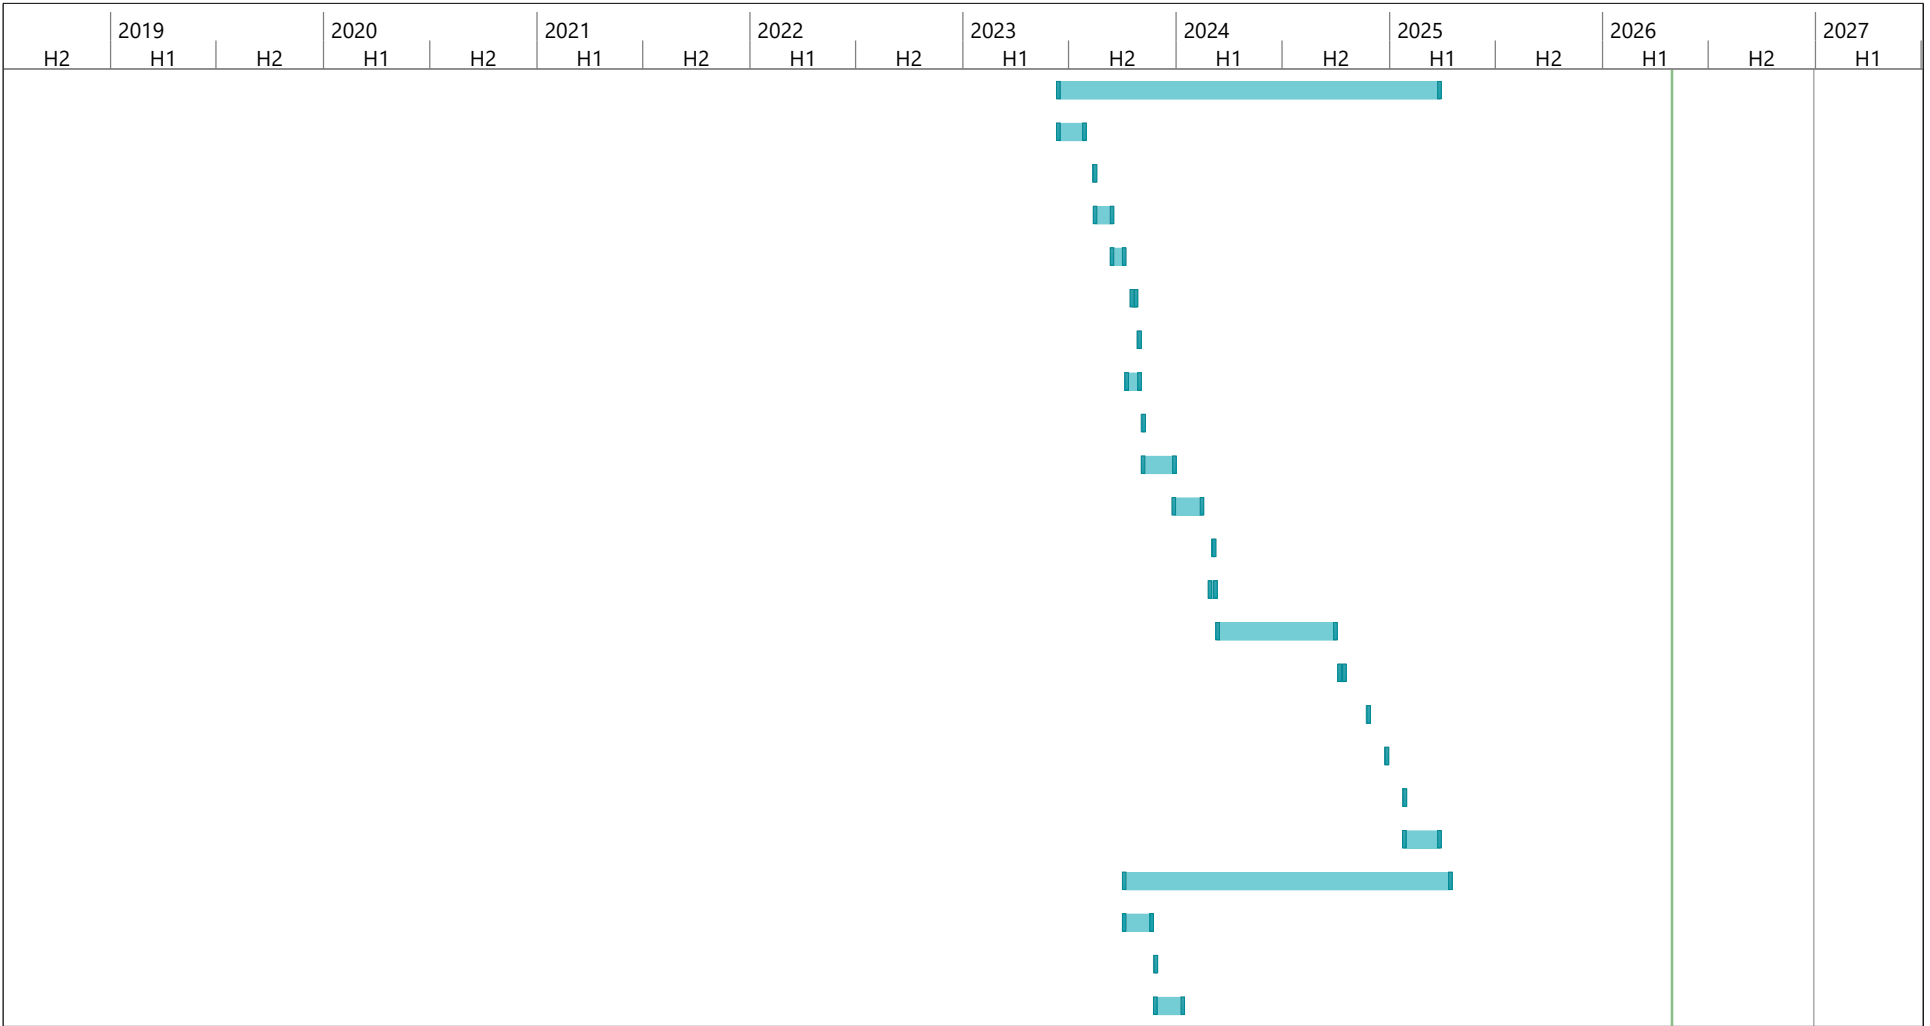


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

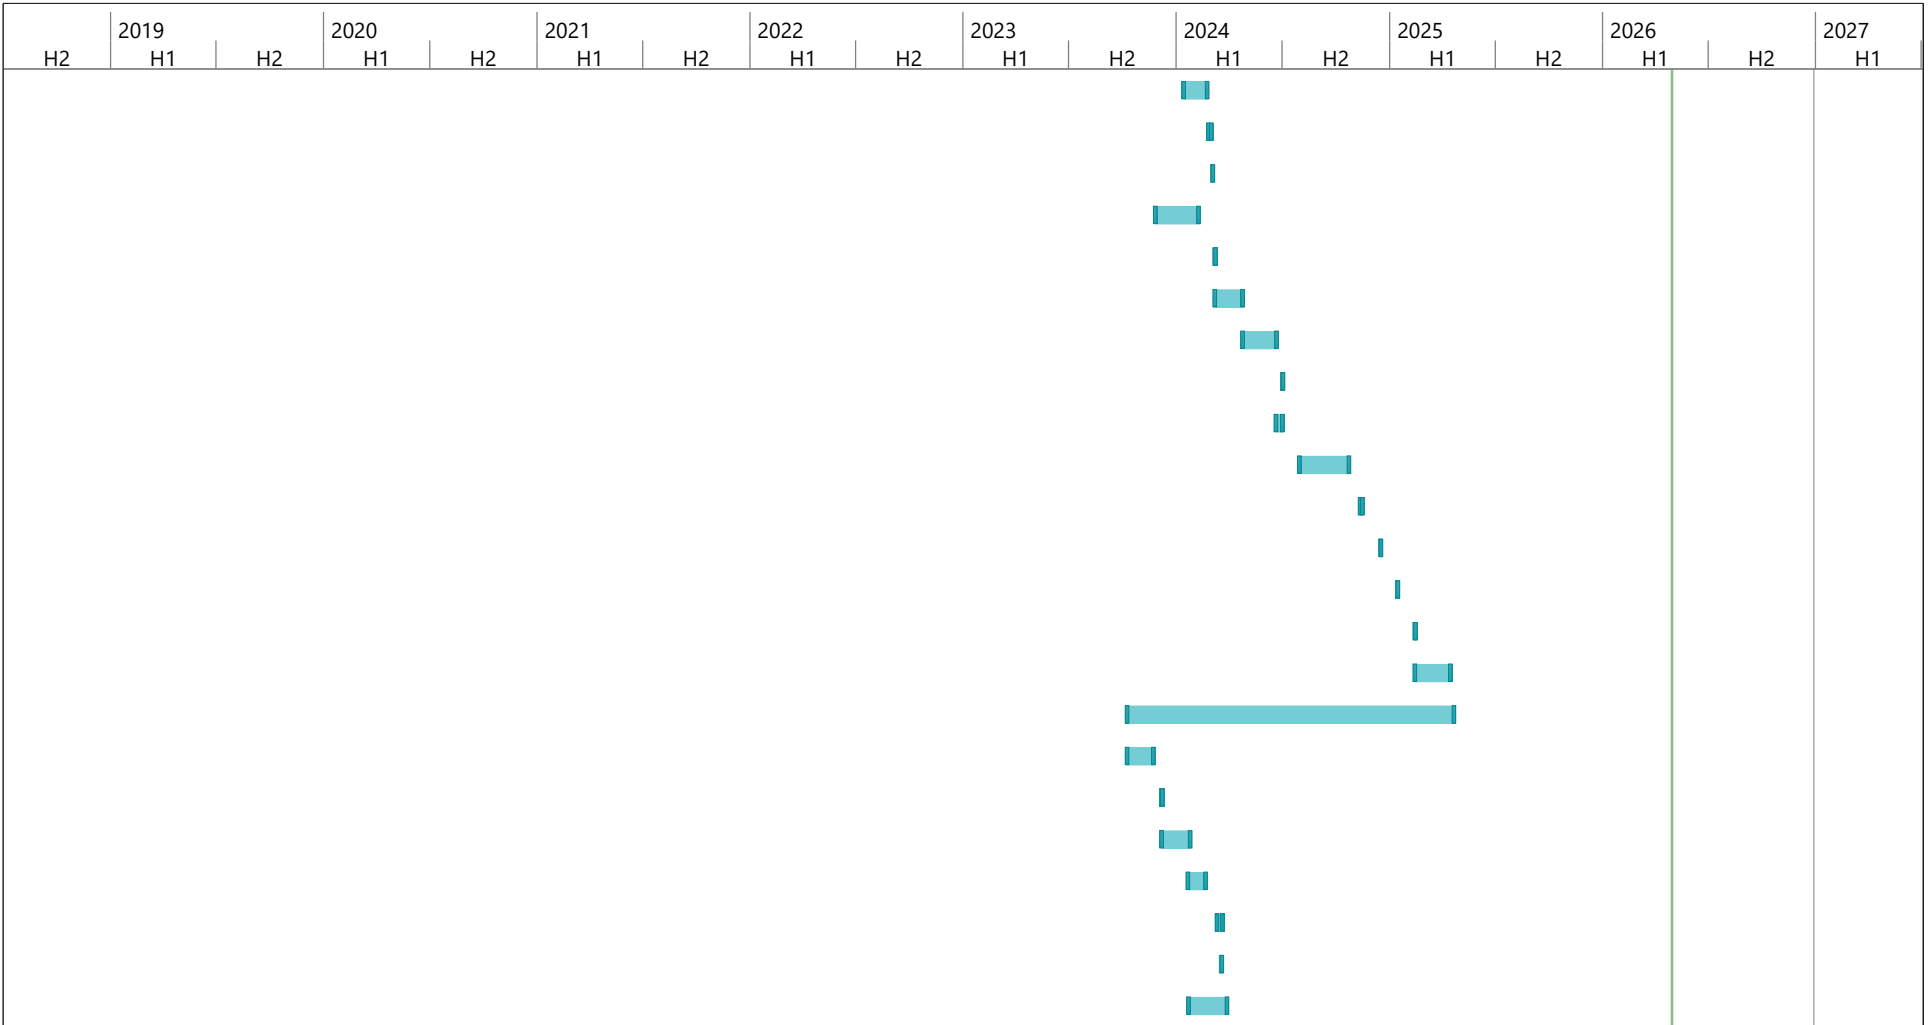

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

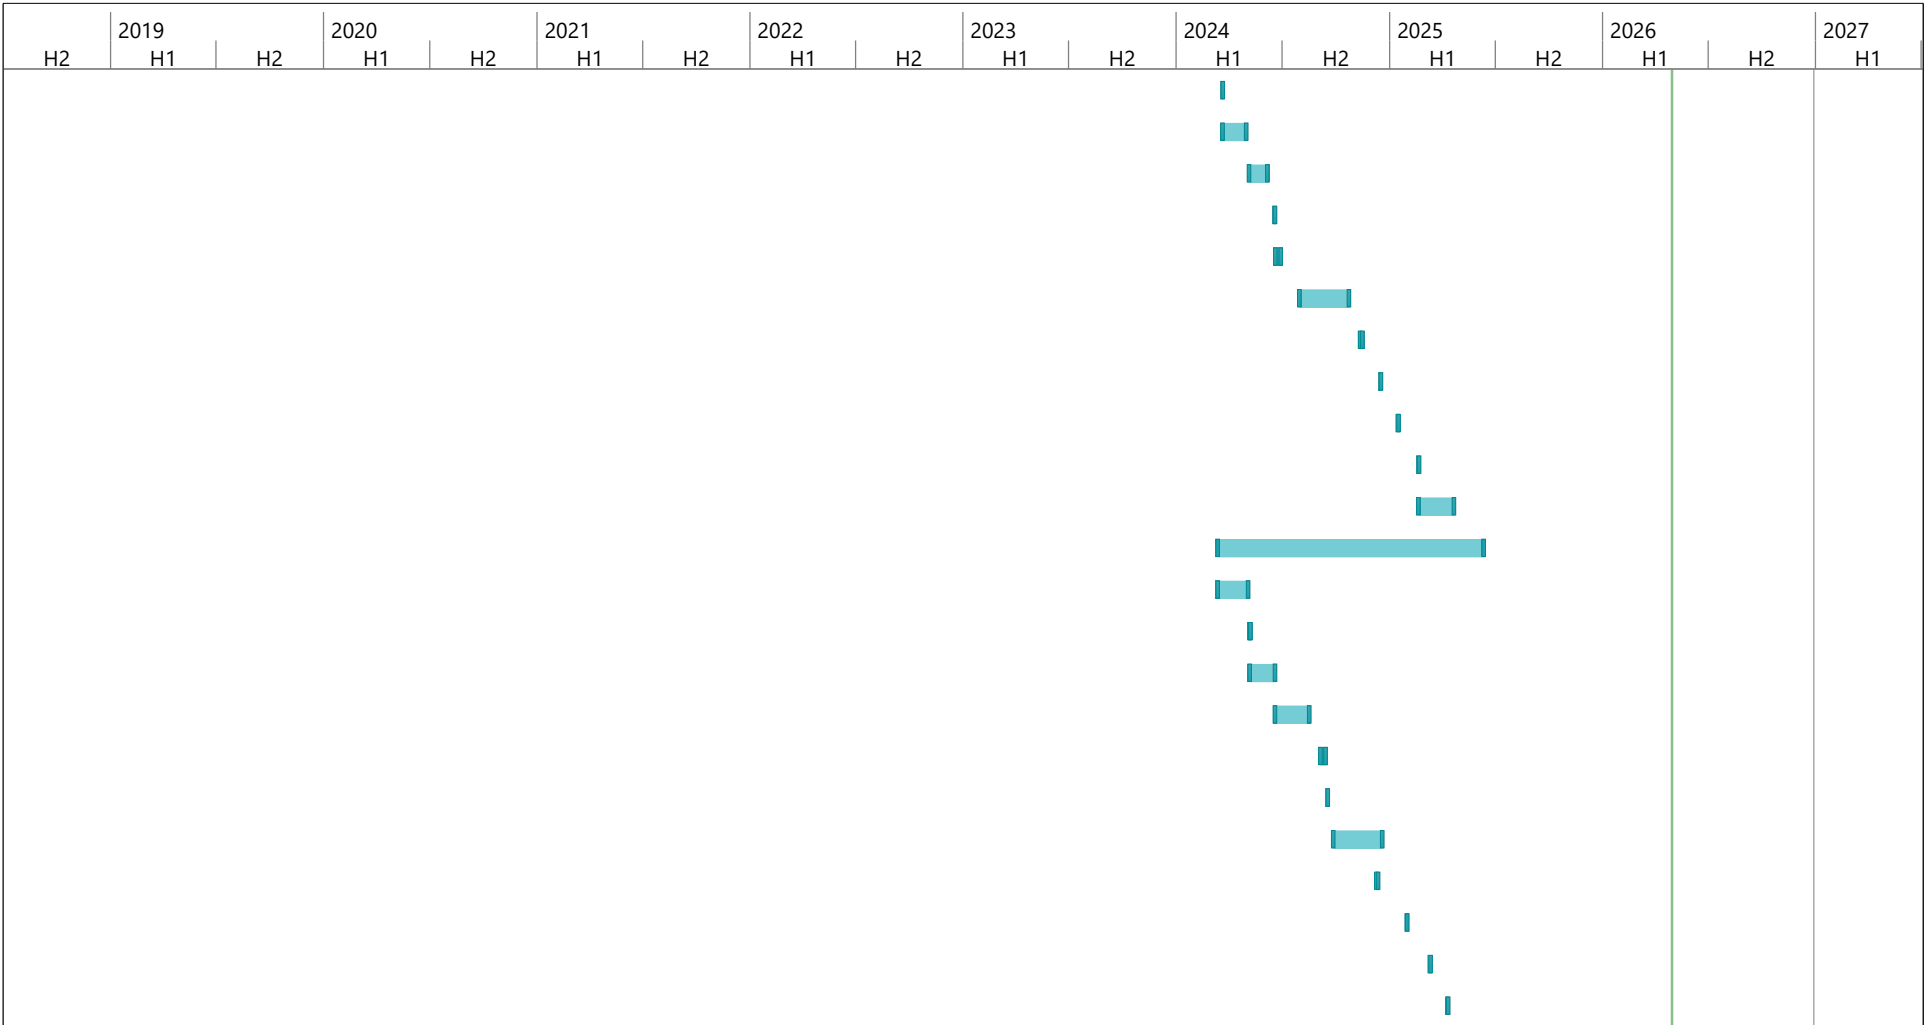


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

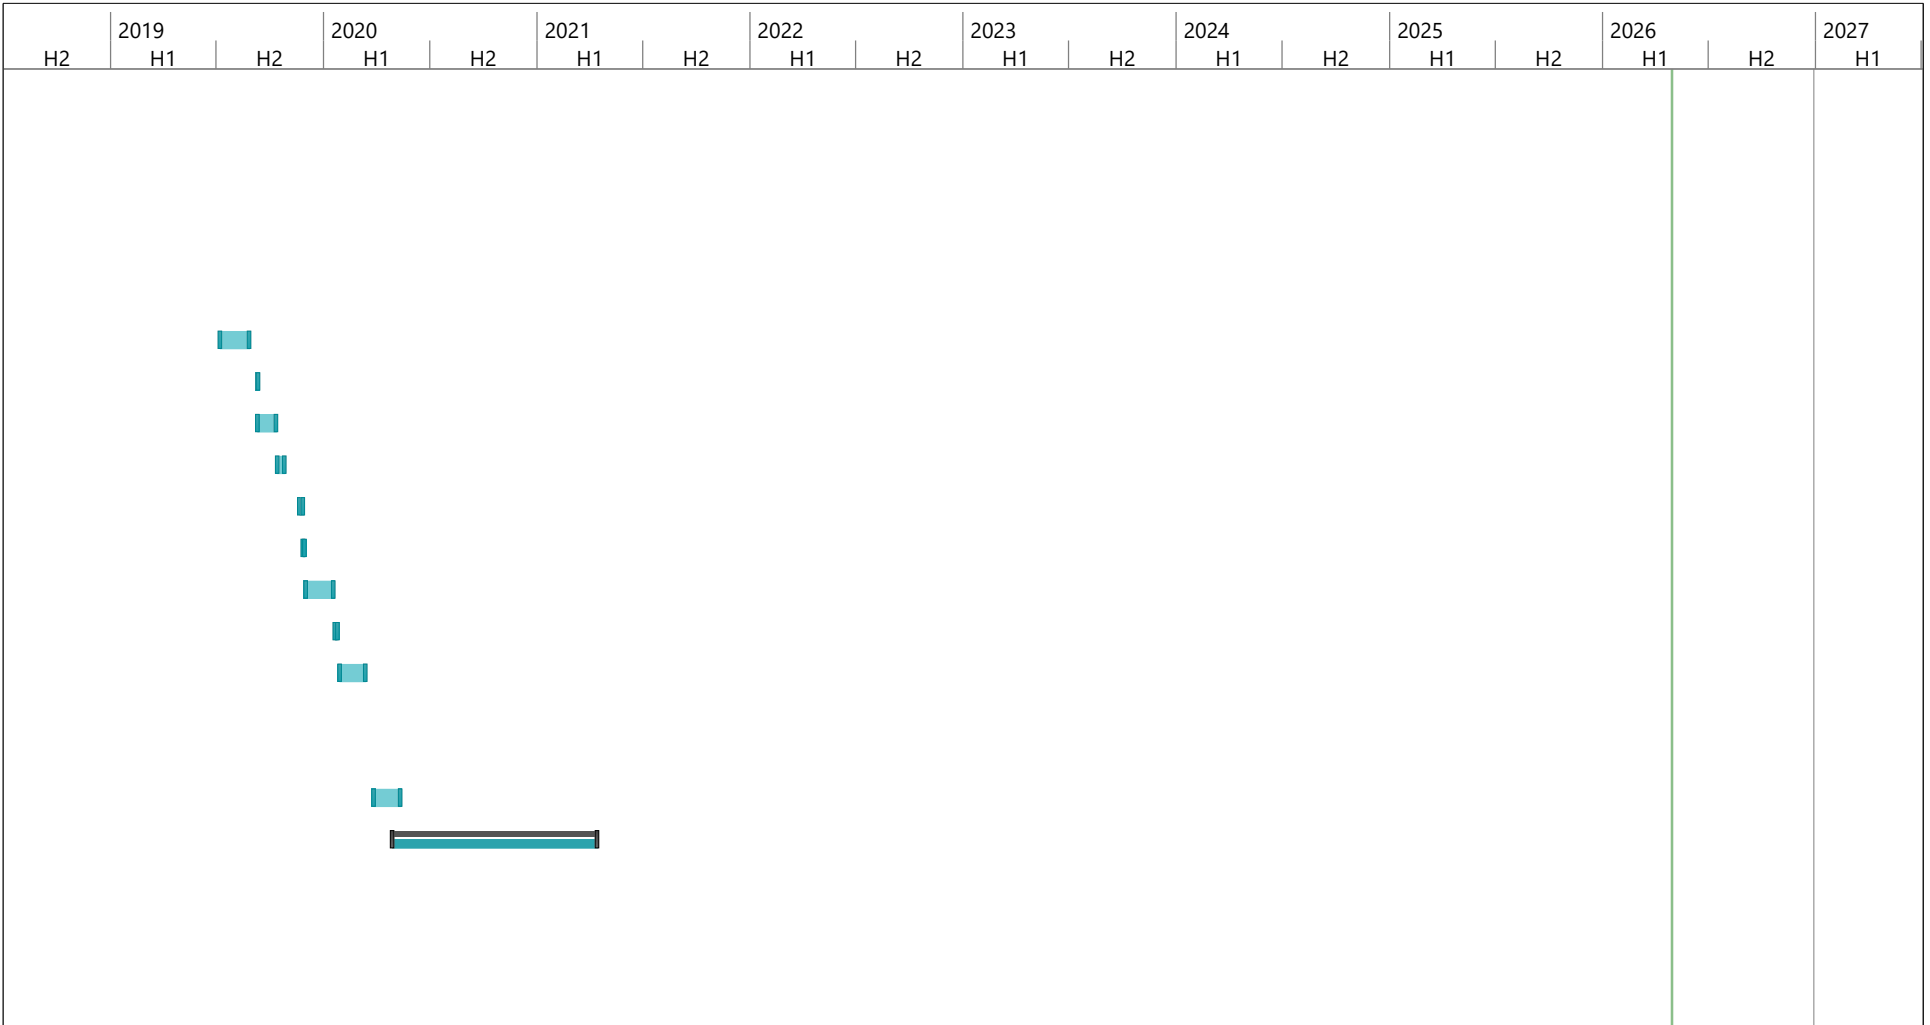


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

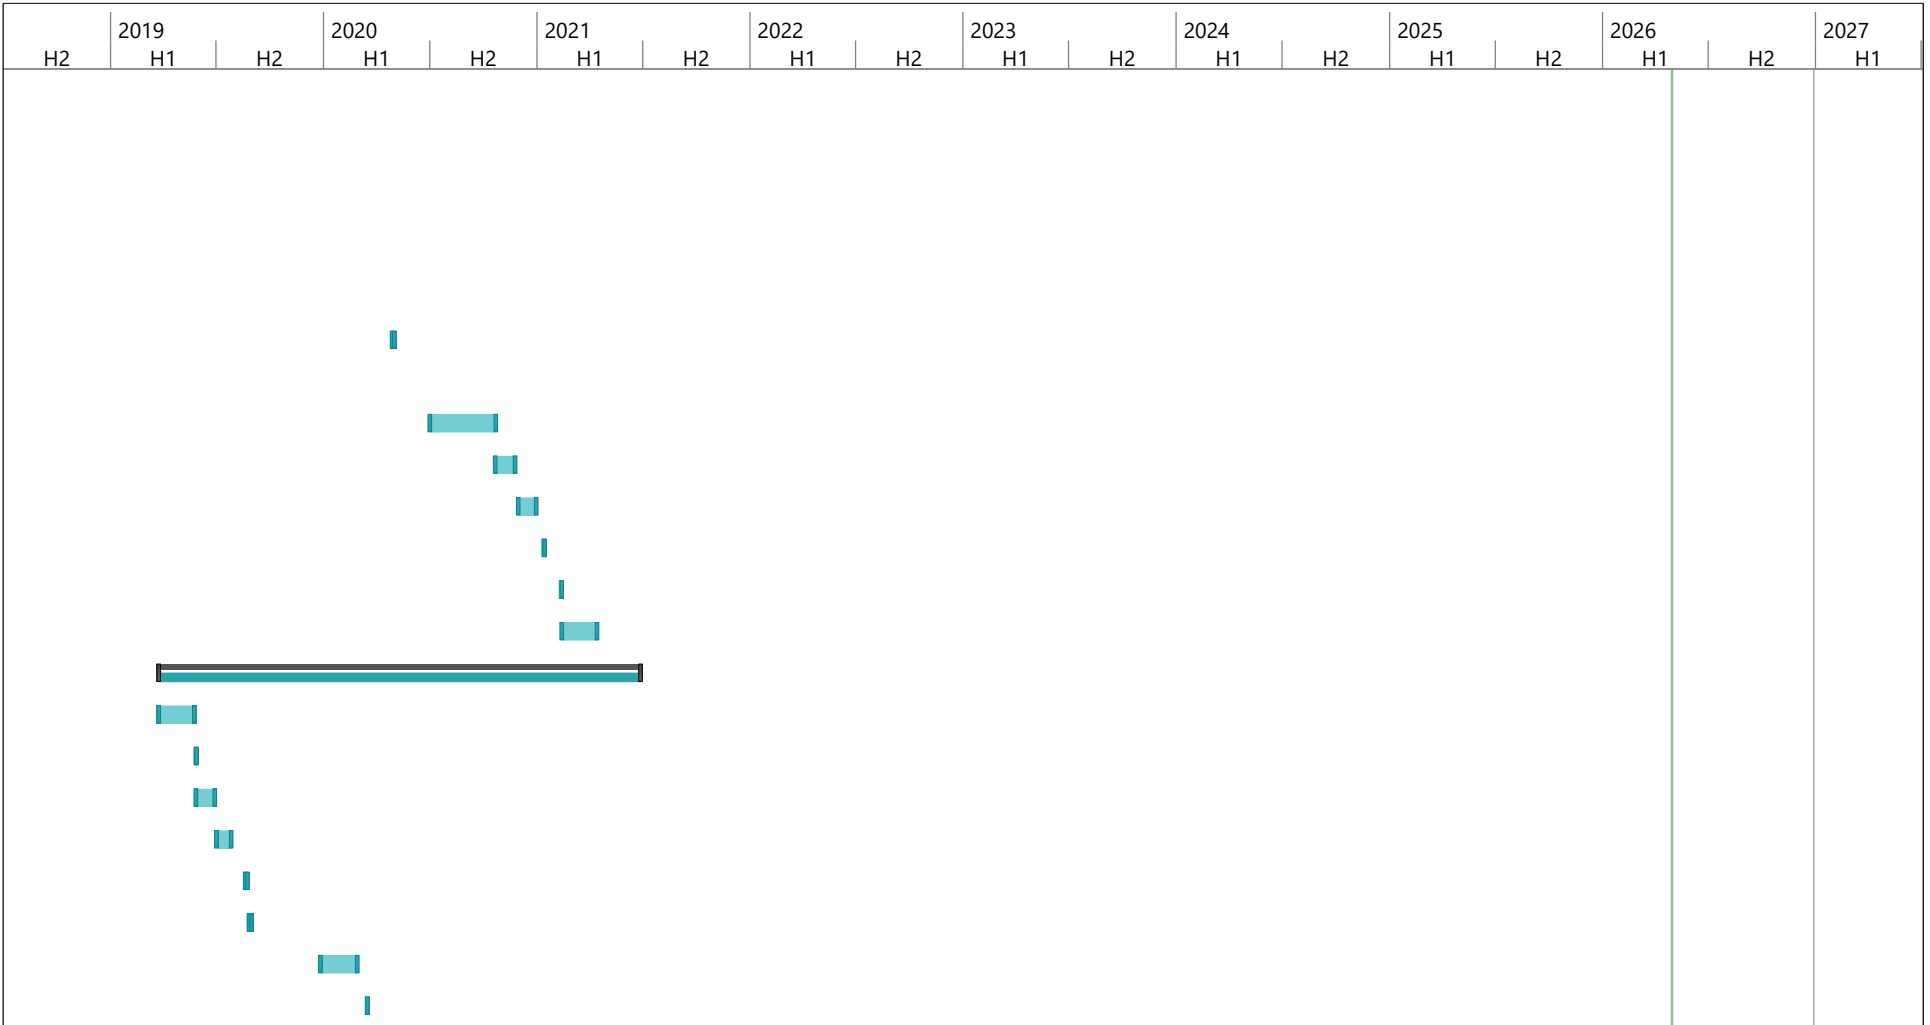


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

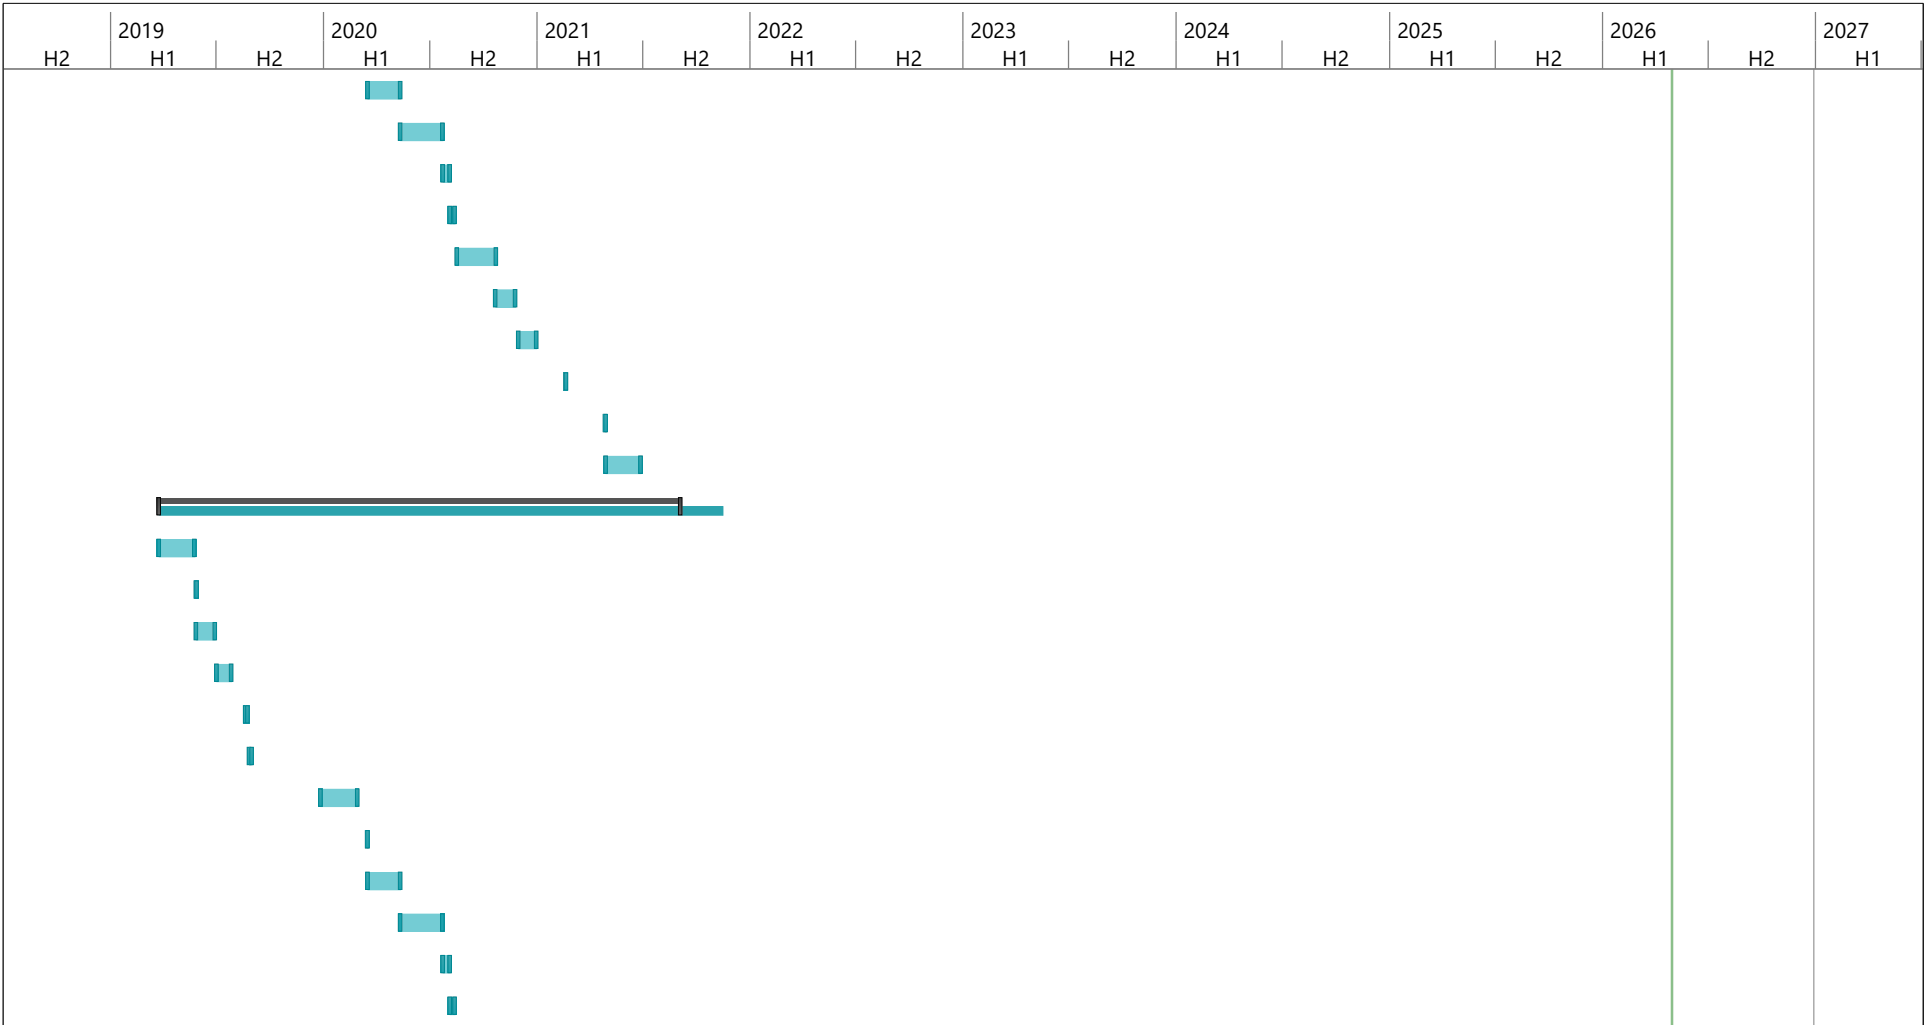


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

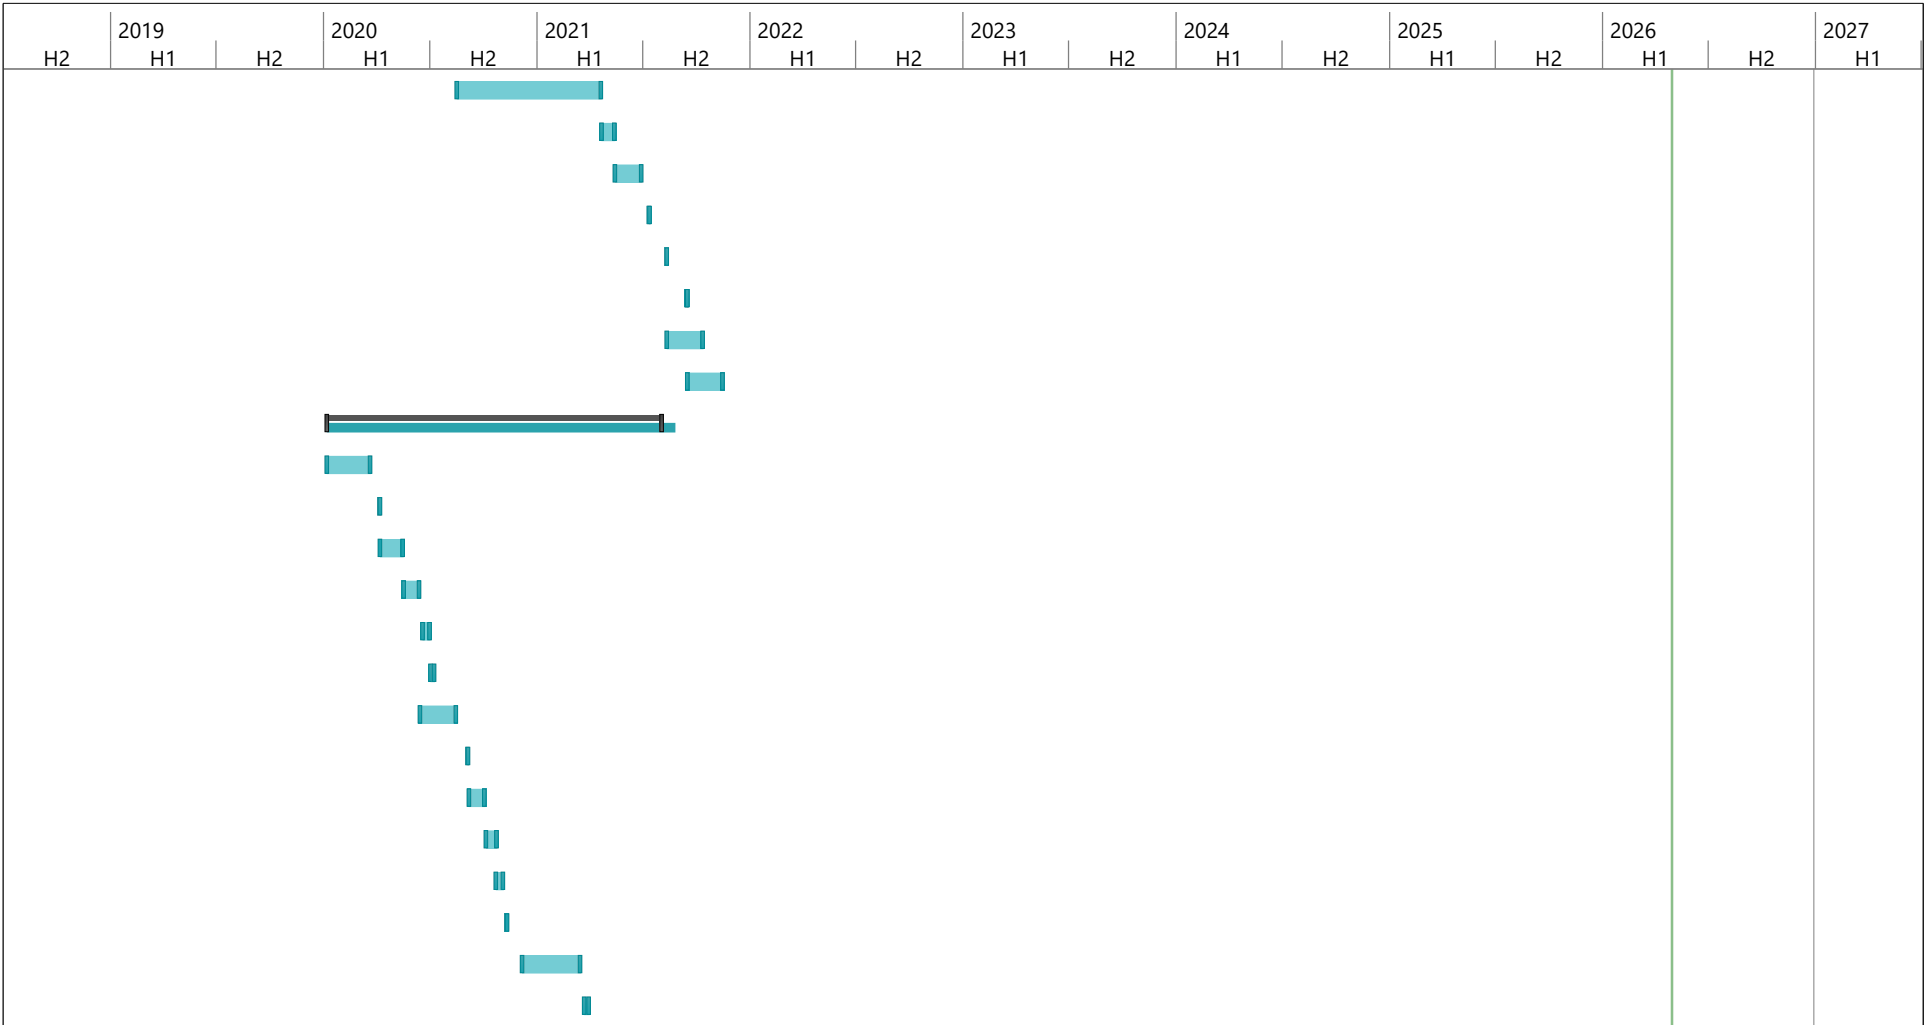


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

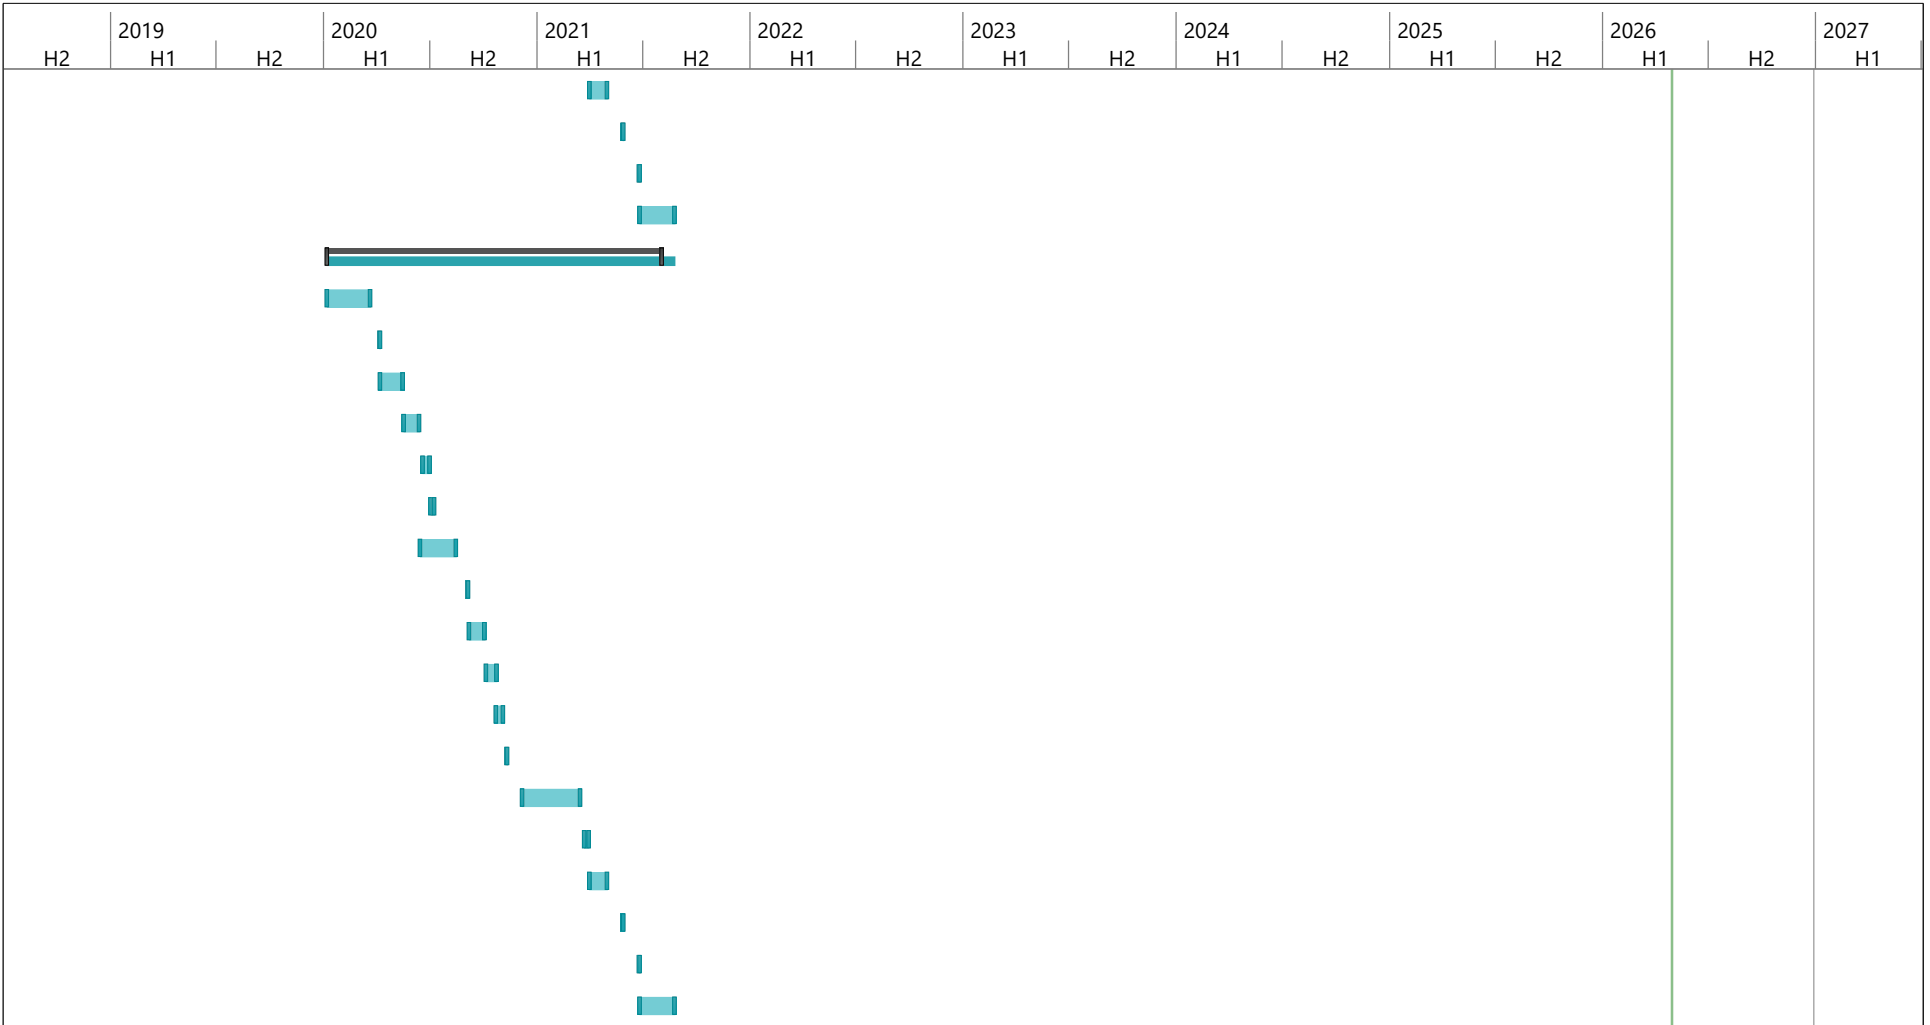


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

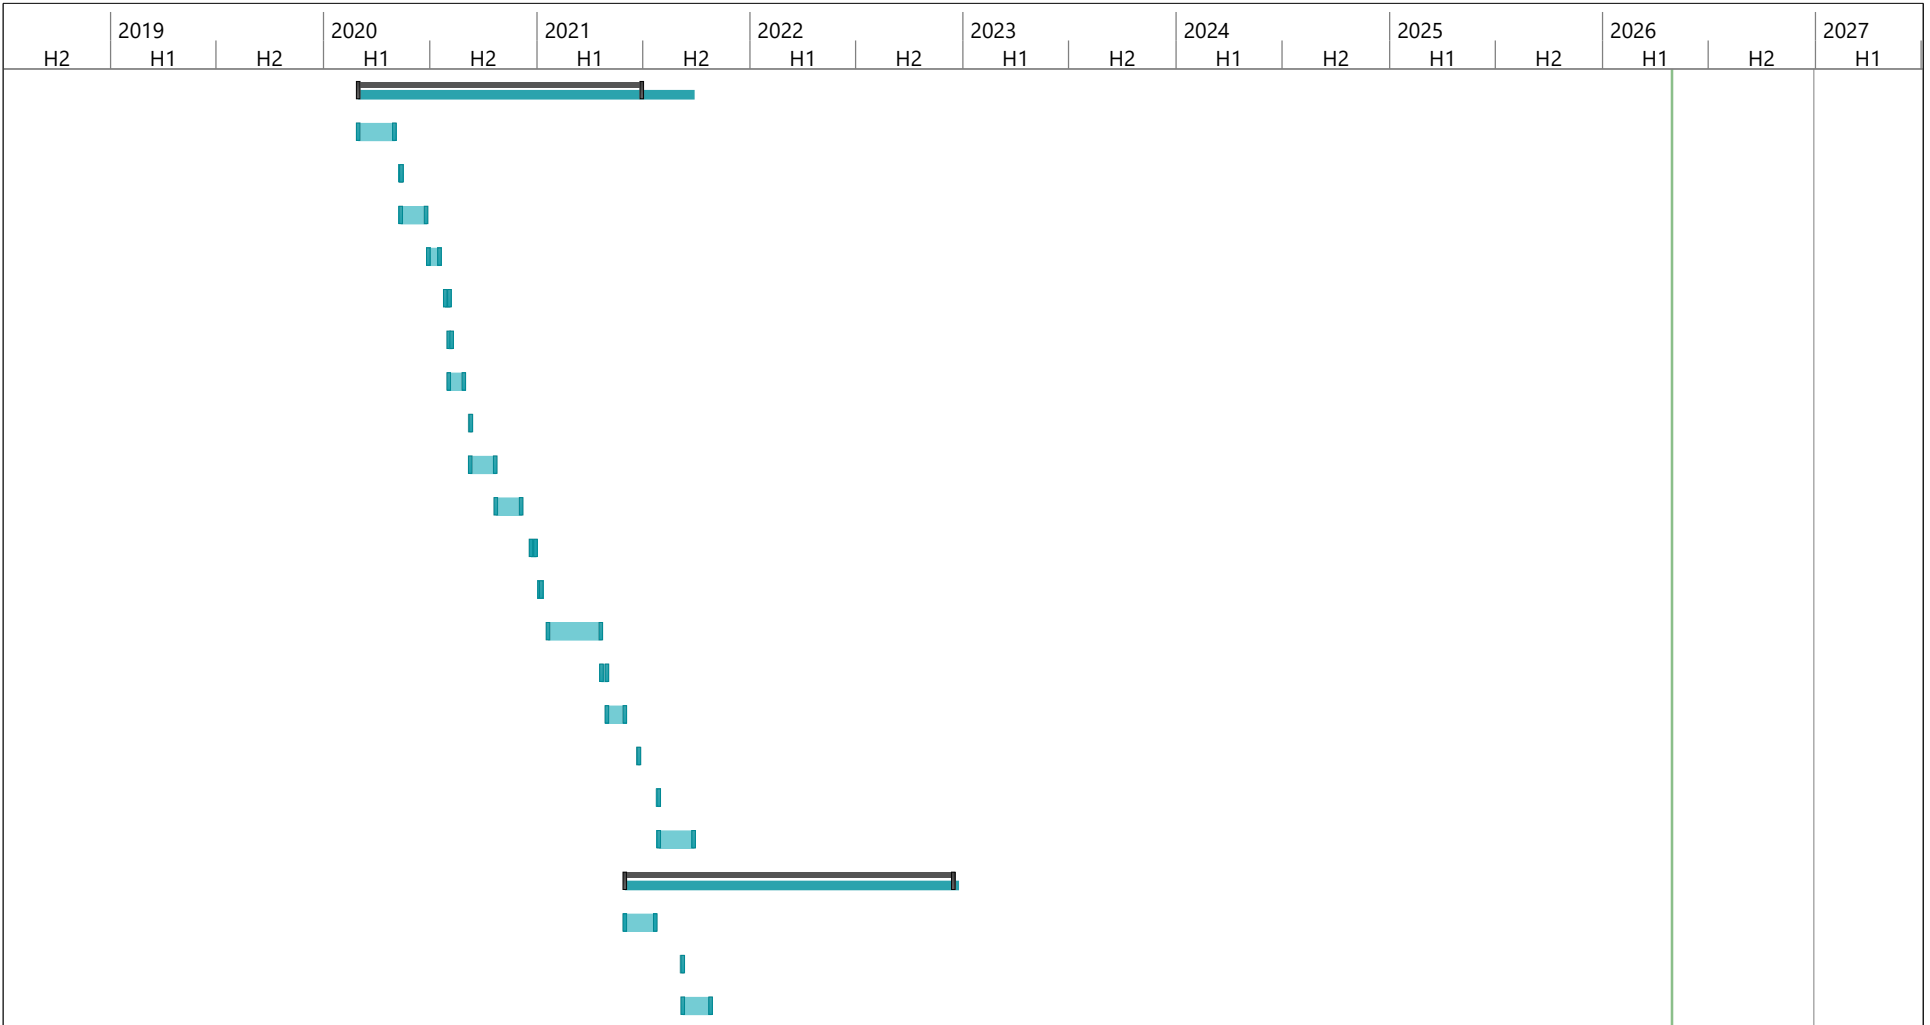


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

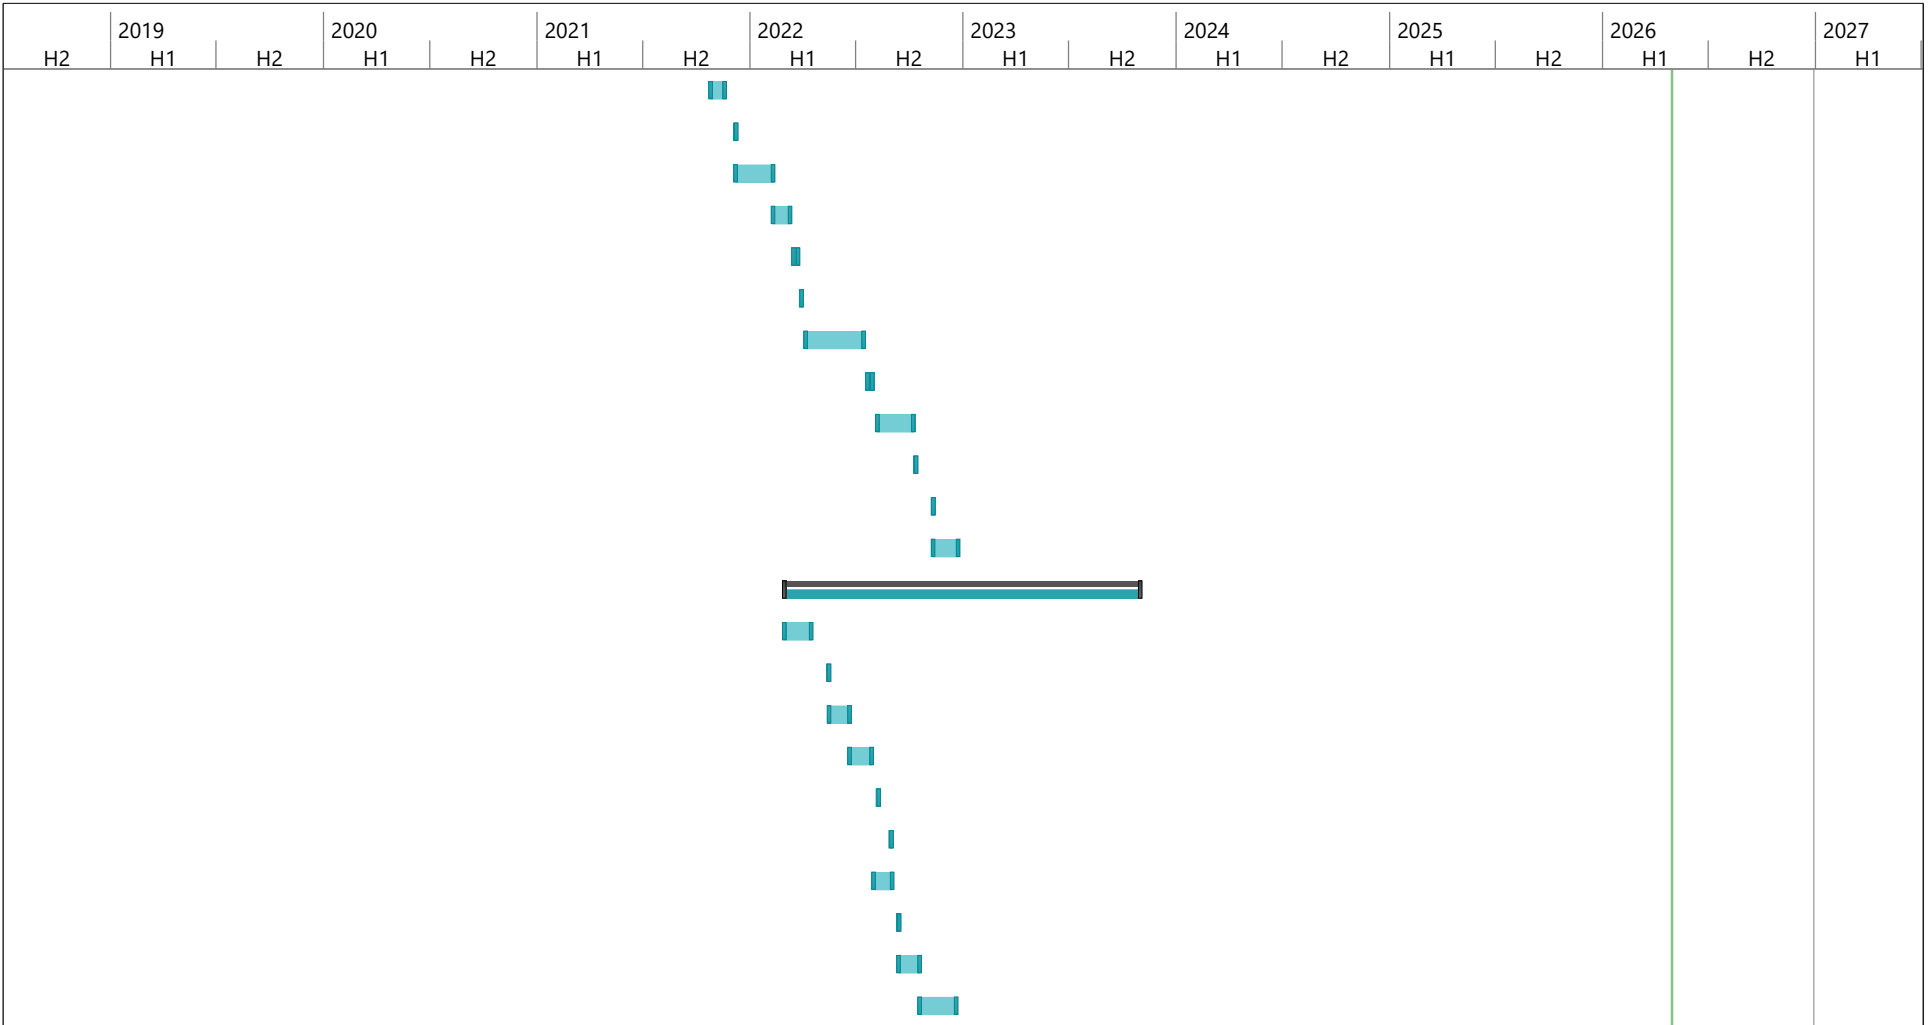


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

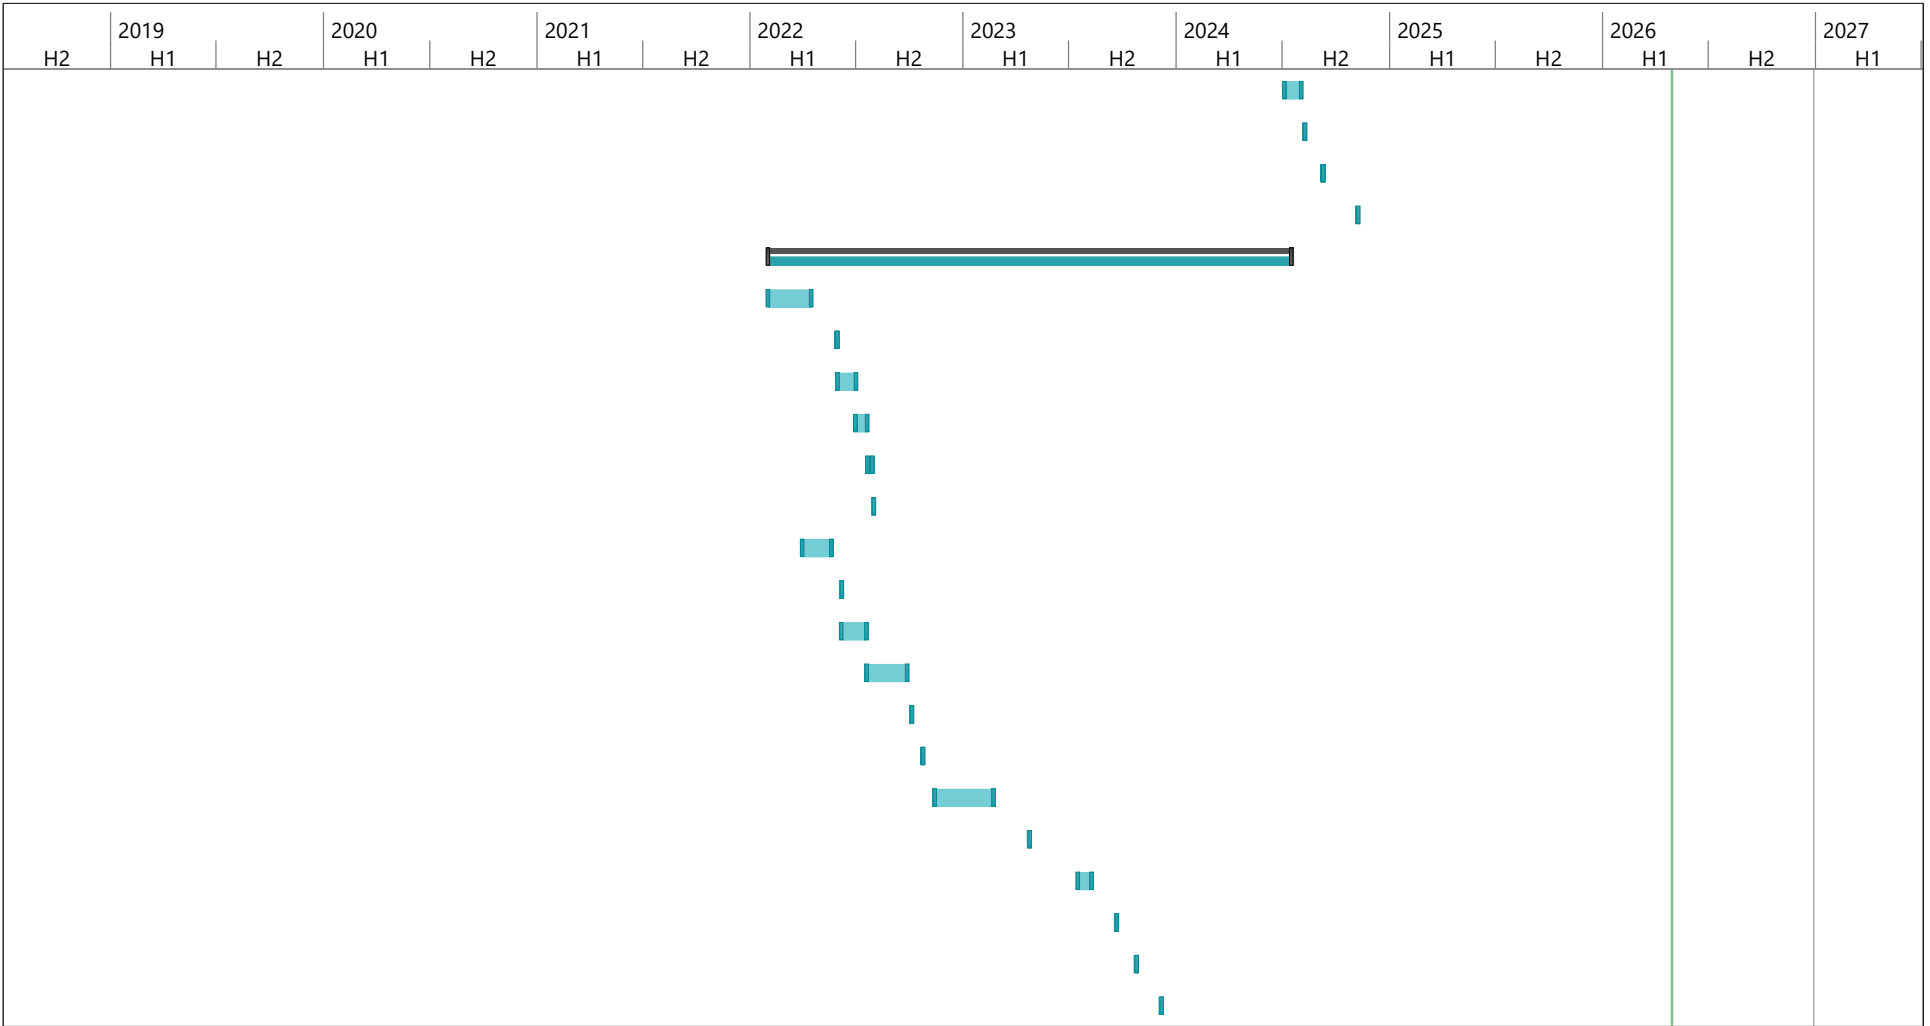


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

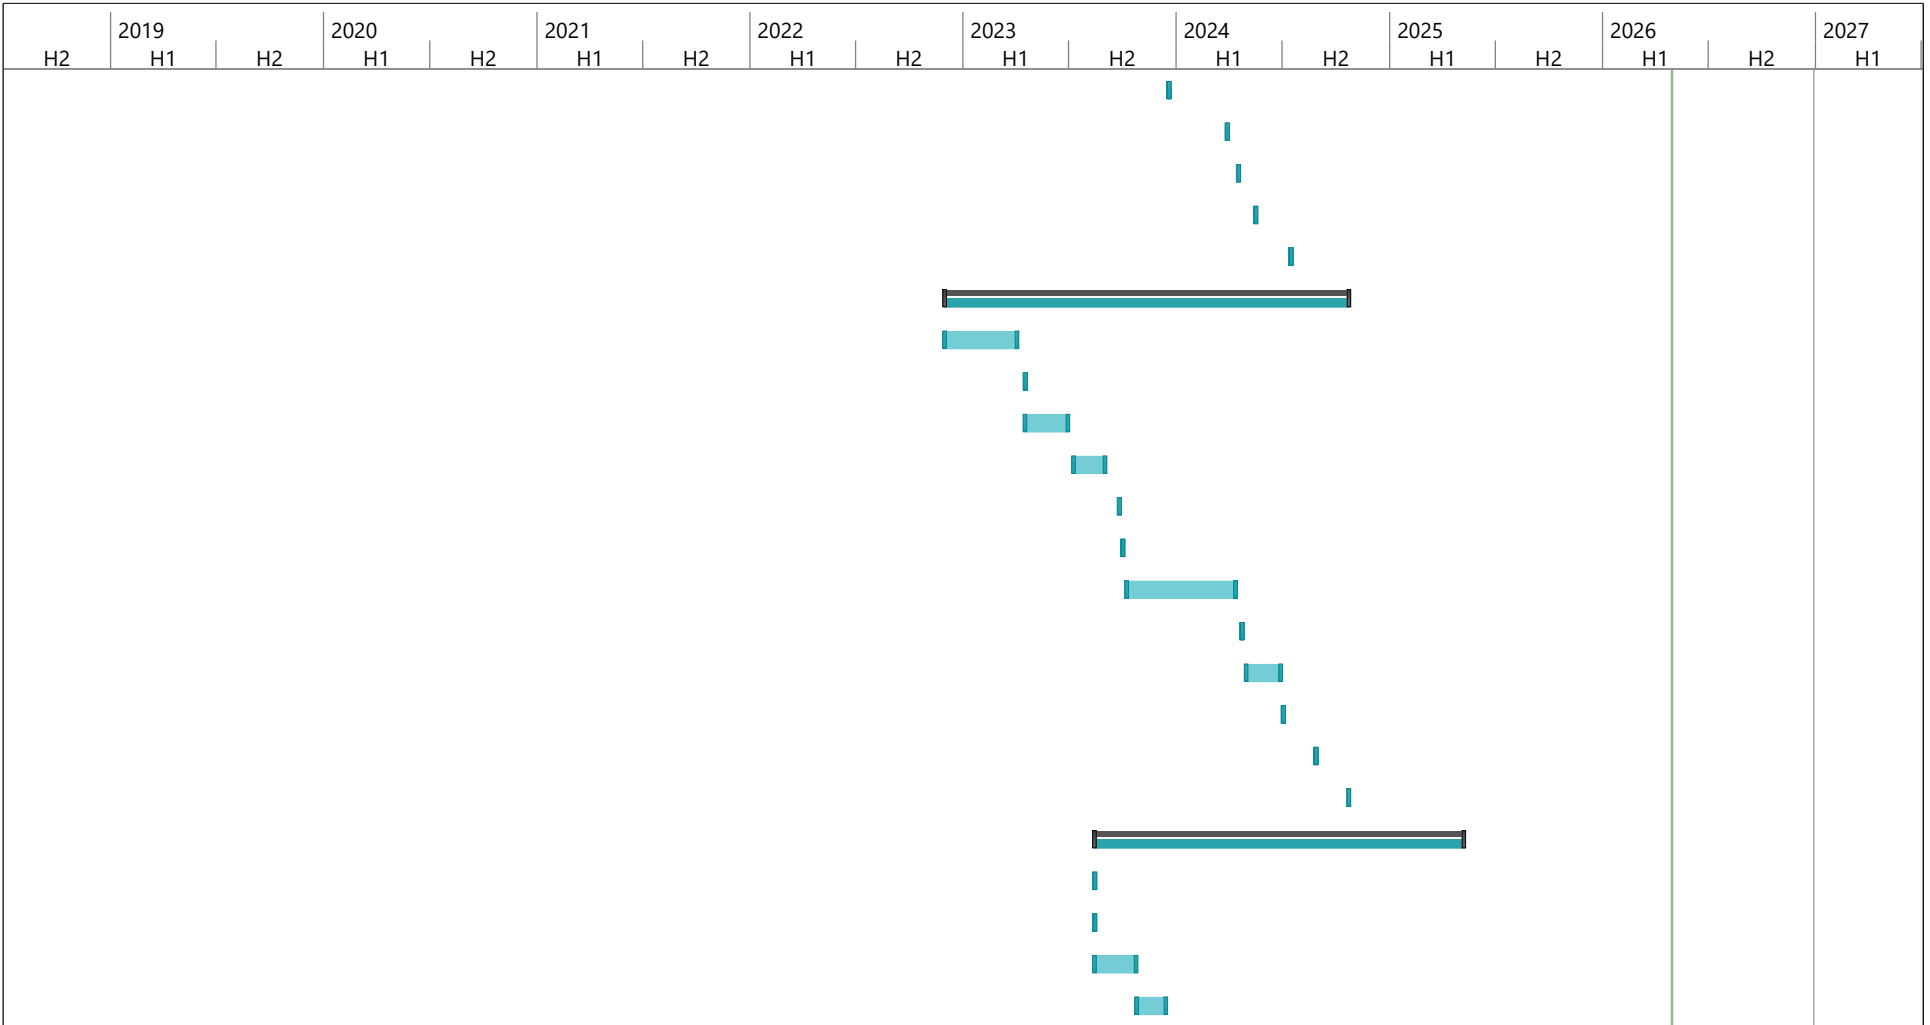


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

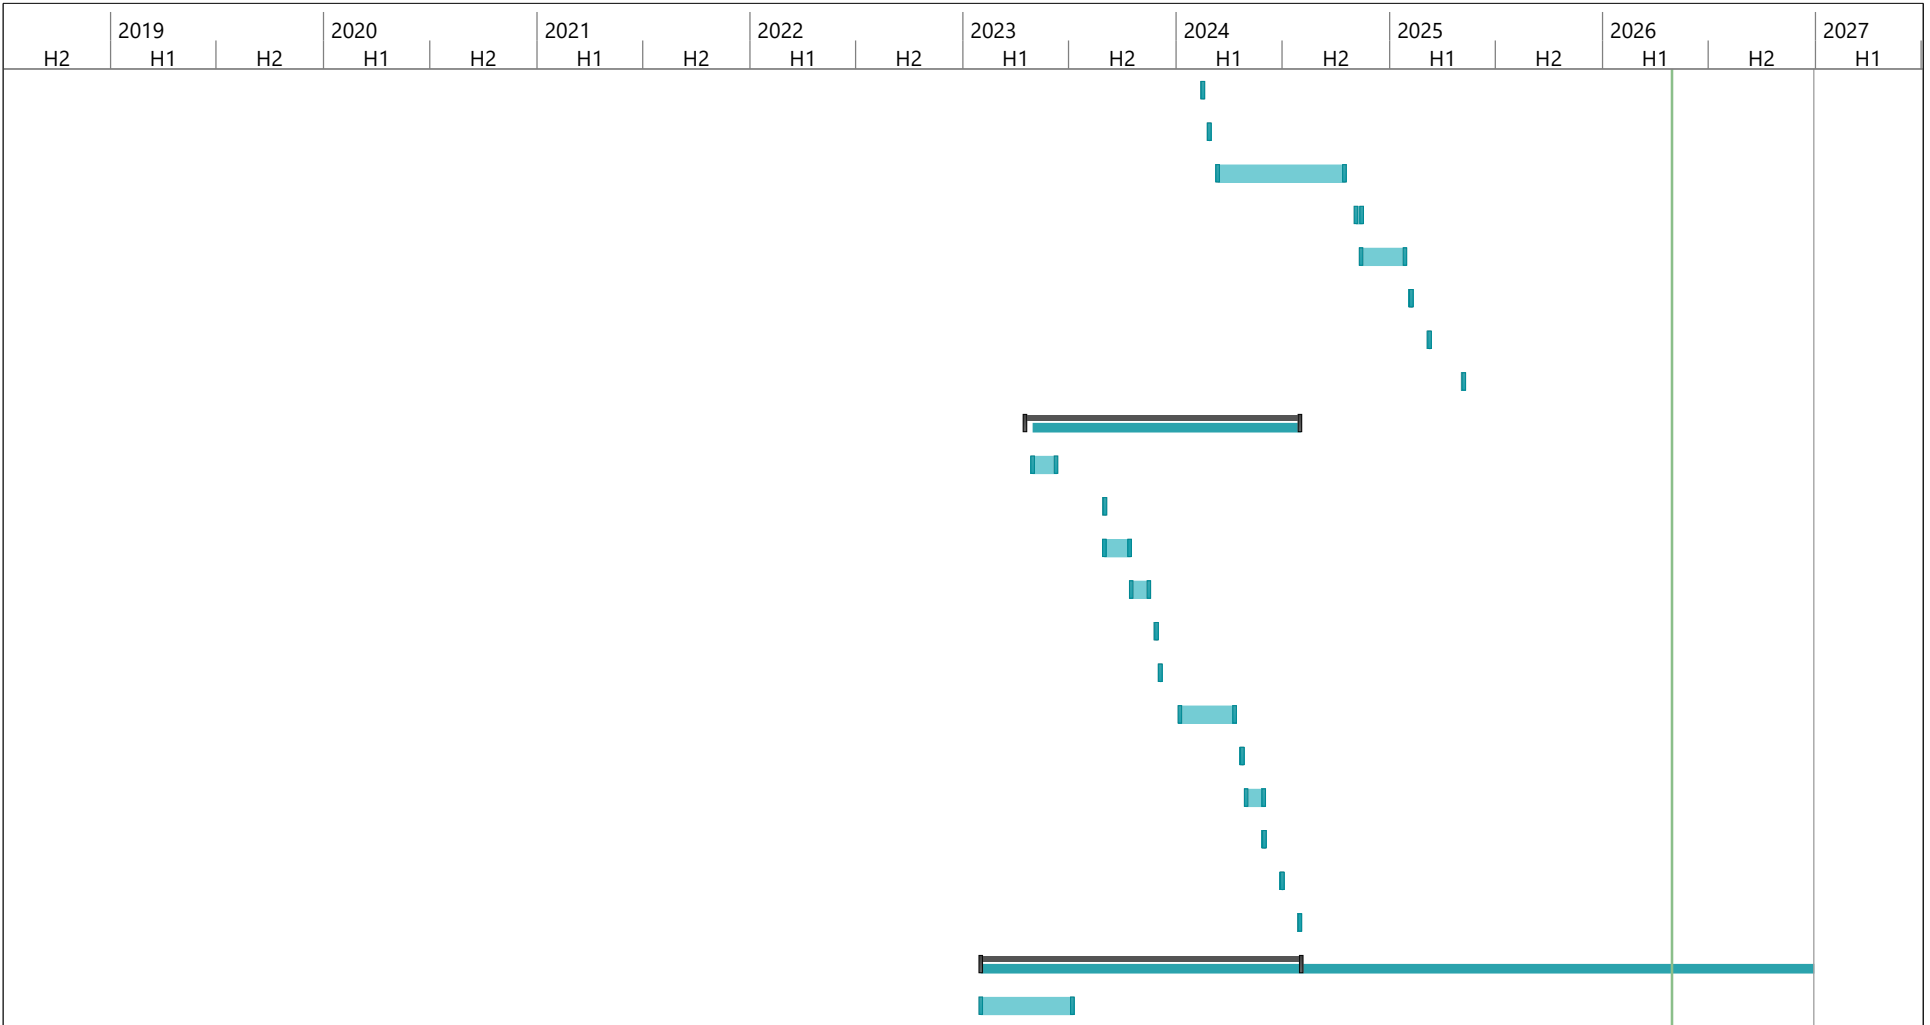


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

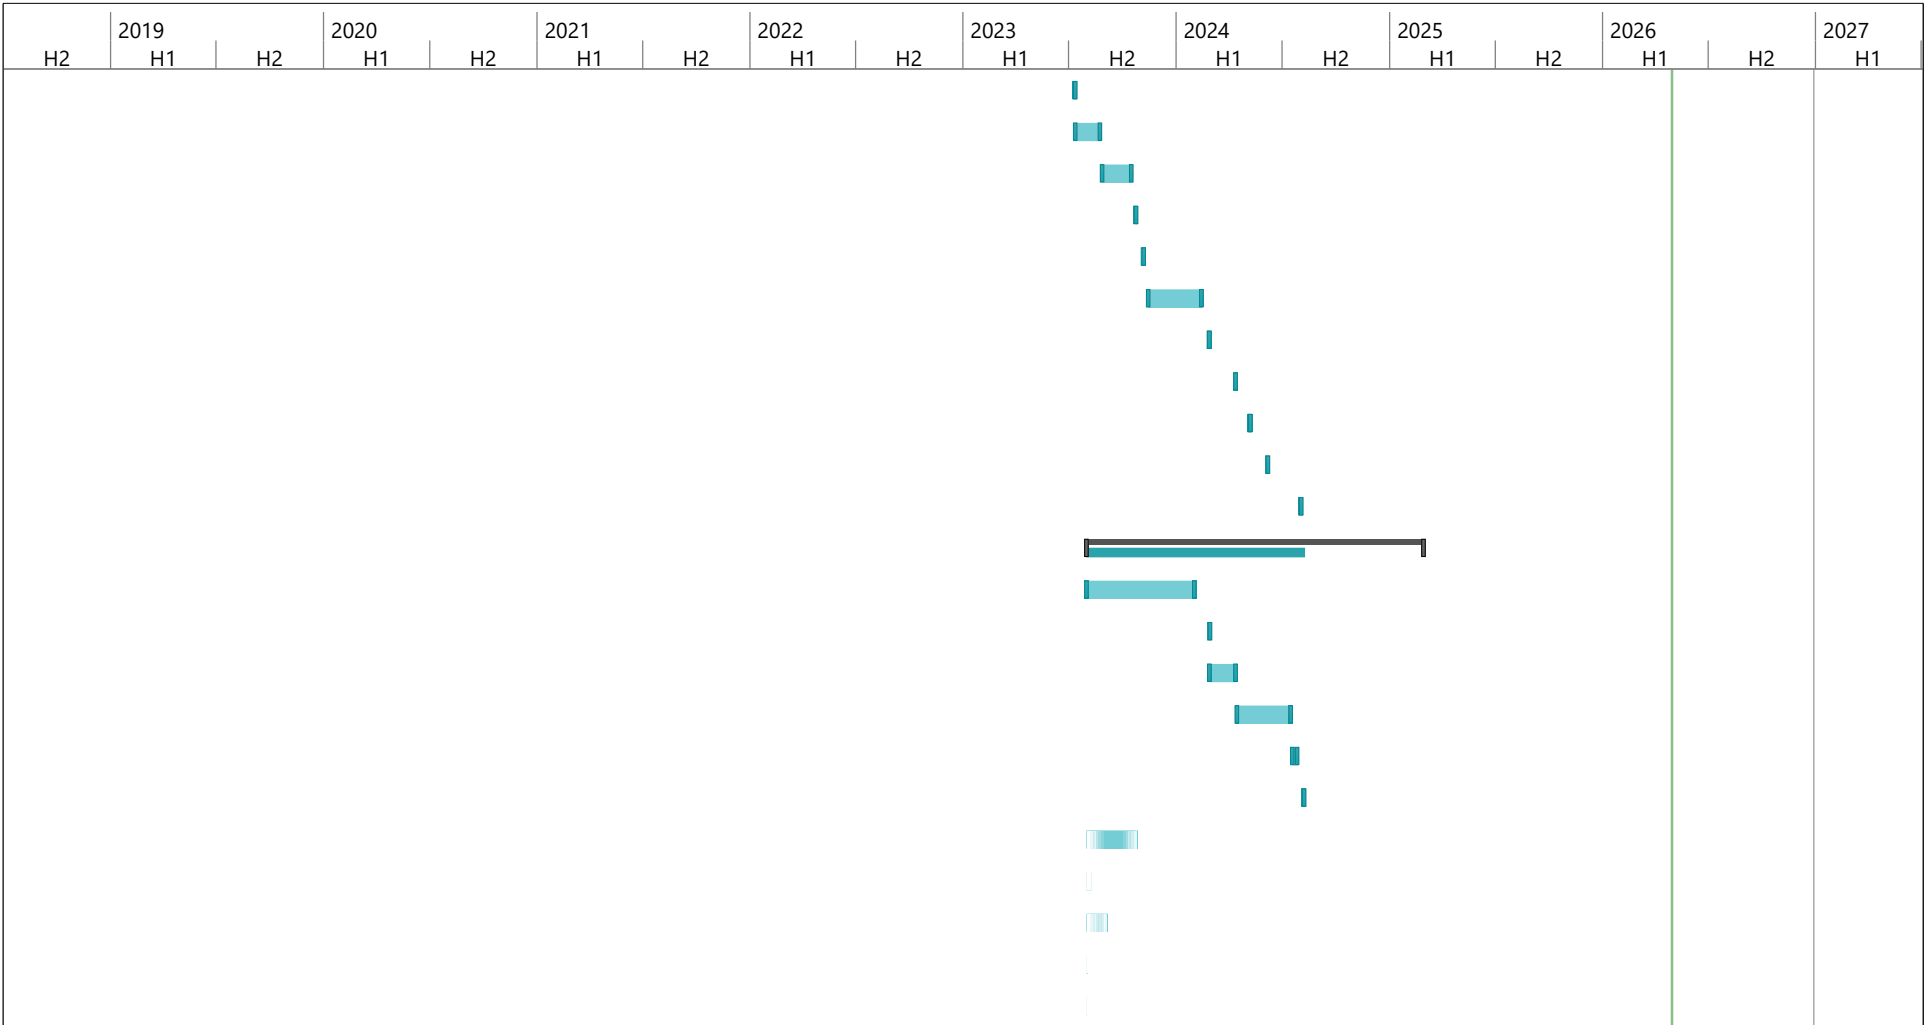


Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

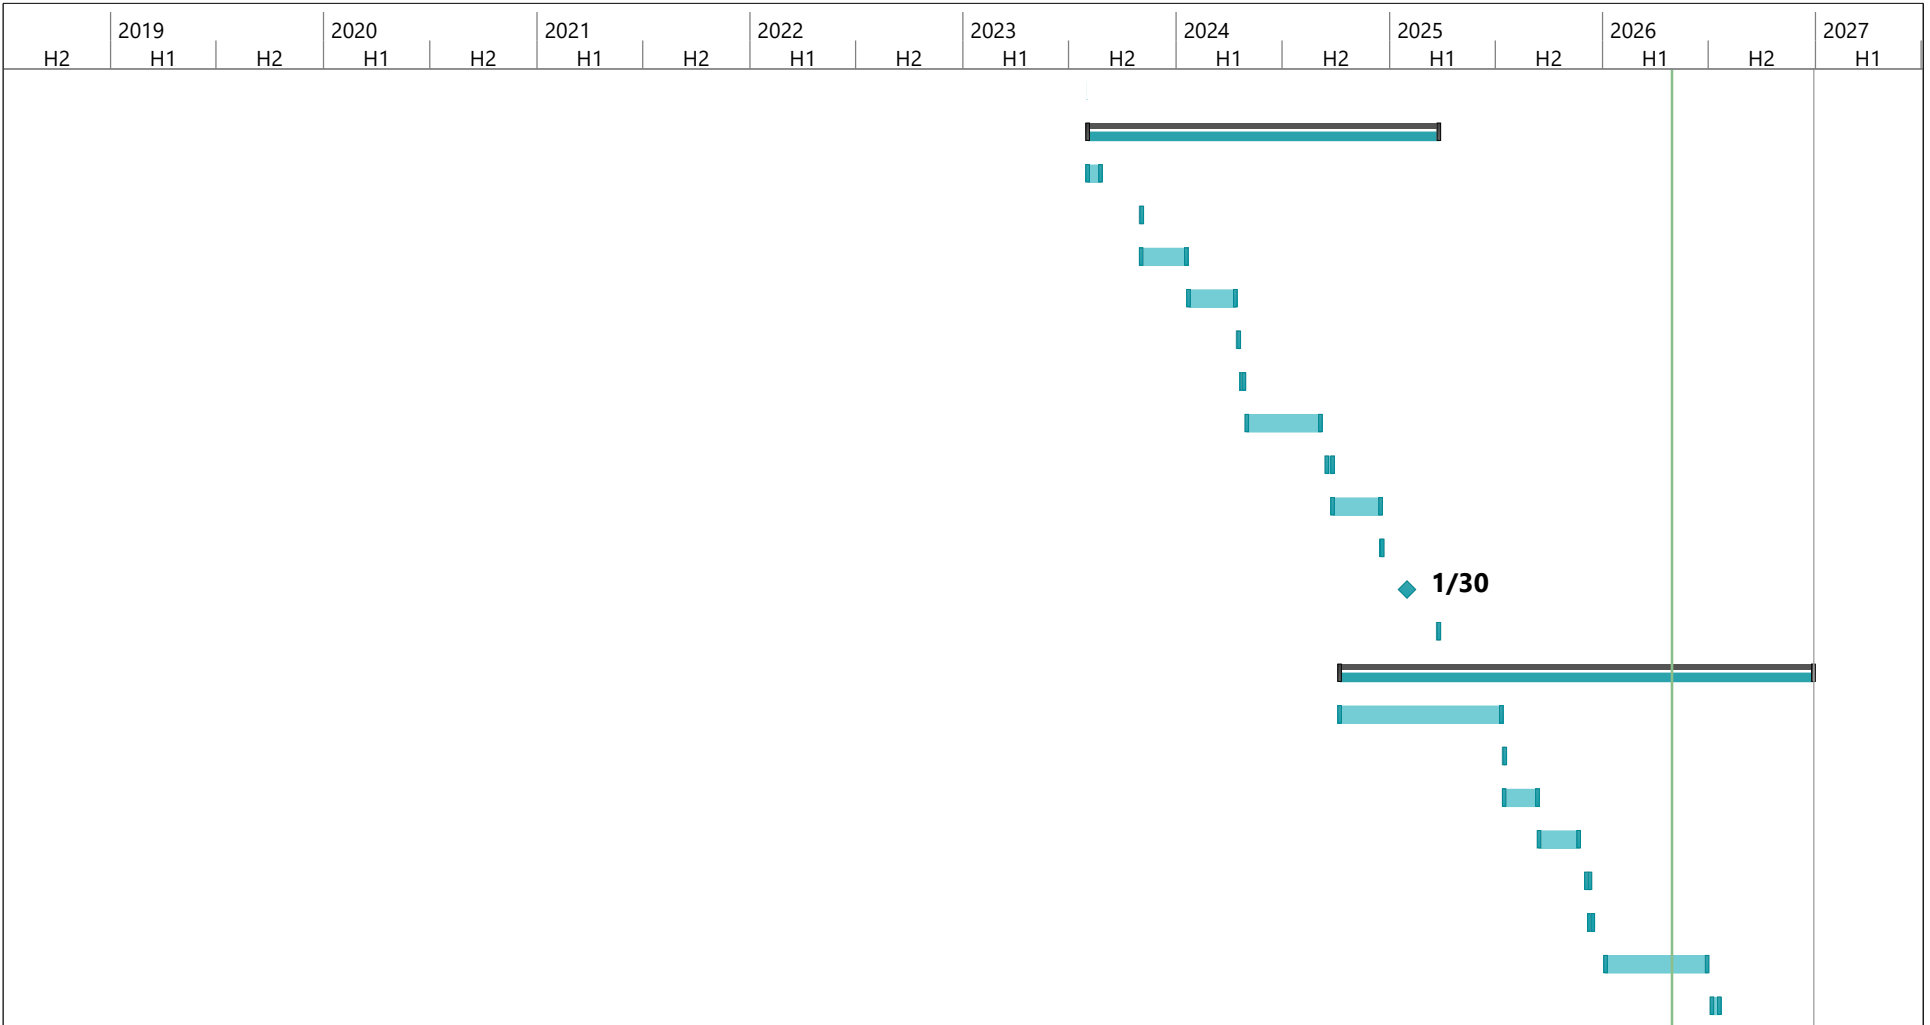

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

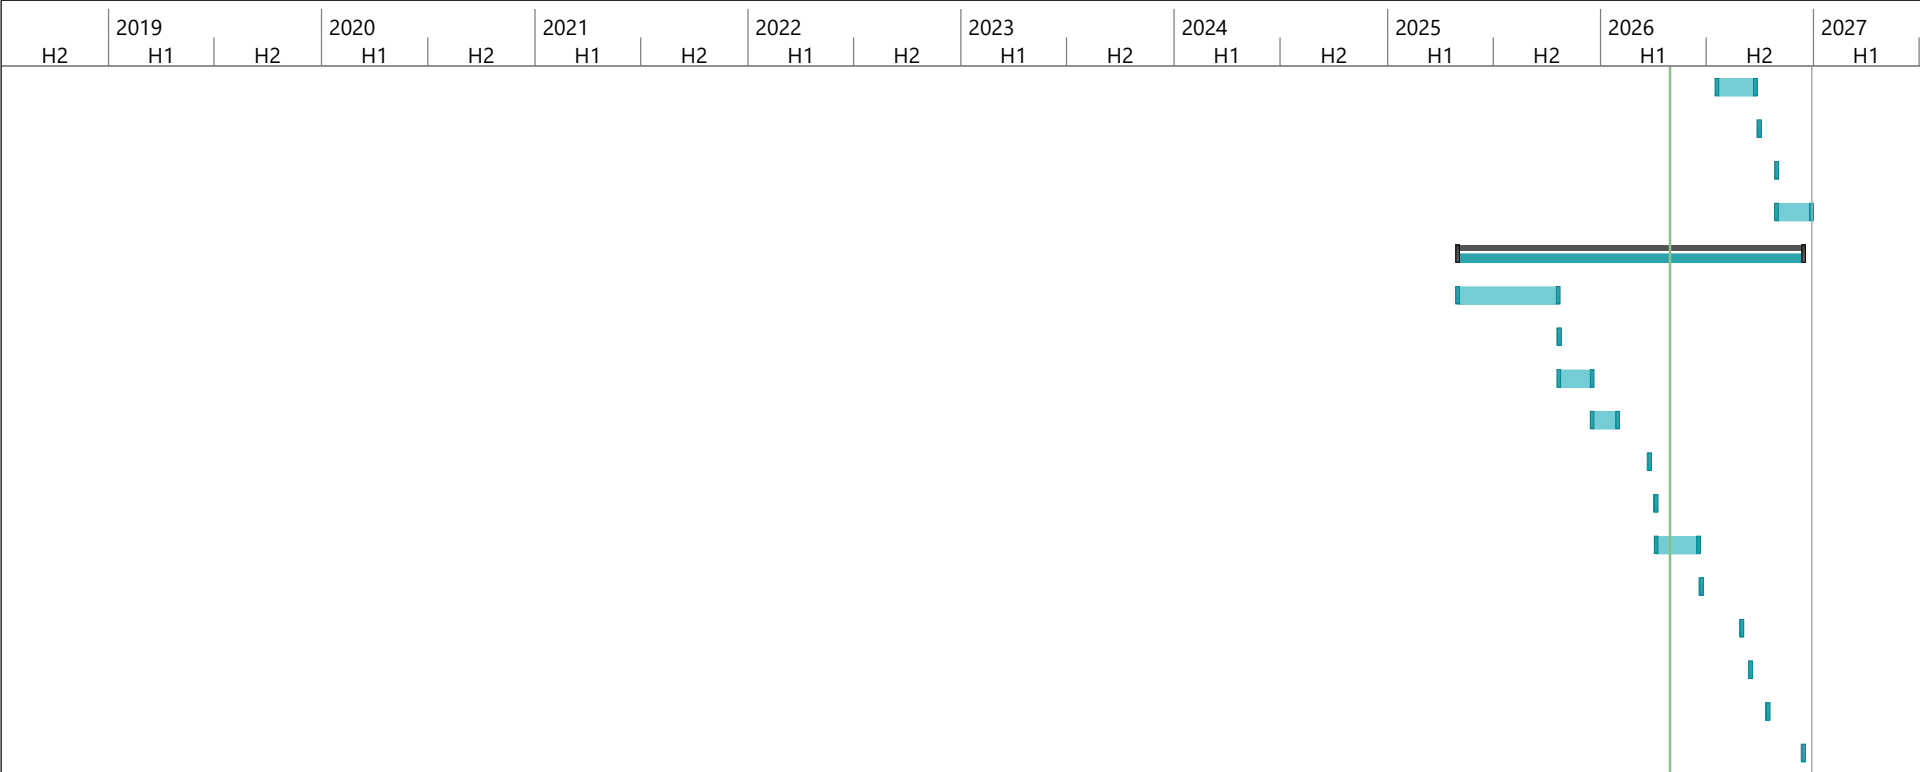

Project: IOU Master Task Timeli
Date: Thu 4/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
