

ID	Task Name	Duration	Start	Finish
1	**UPDATED as of November 1, 2026**			
2	**SCE - Local RCI Solicitation**	**679 days**	**Tue 8/21/18**	**Fri 3/26/21**
3	SCE - RFA Preparation	40 days	Tue 8/21/18	Mon 10/15/18
4	SCE - RFA Release	1 day	Fri 11/9/18	Fri 11/9/18
5	SCE - RFA Abstract Creation Duration	30 days	Sat 11/10/18	Thu 12/20/18
6	SCE - RFA Evaluation	82 days	Fri 12/21/18	Mon 4/15/19
7	SCE - RFA Review with EE PRG	1 day	Tue 4/16/19	Tue 4/16/19
8	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/21/19	Tue 5/21/19
9	SCE - RFP Preparation	175 days	Wed 5/22/19	Tue 1/21/20
10	SCE - RFP Release	1 day	Wed 1/22/20	Wed 1/22/20
11	SCE - RFP Proposal Creation Duration	25 days	Thu 1/23/20	Wed 2/26/20
12	SCE - RFP Evaluation	38 days	Thu 2/27/20	Mon 4/20/20
13	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20
14	SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20
15	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20
16	SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20
17	SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20
18	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20
19	SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20
20	SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21
21	**SCE - SW Lighting**	**518 days**	**Wed 4/3/19**	**Fri 3/26/21**
22	SCE - RFA Preparation	55 days	Wed 4/3/19	Tue 6/18/19
23	SCE - RFA Release	1 day	Tue 7/2/19	Tue 7/2/19

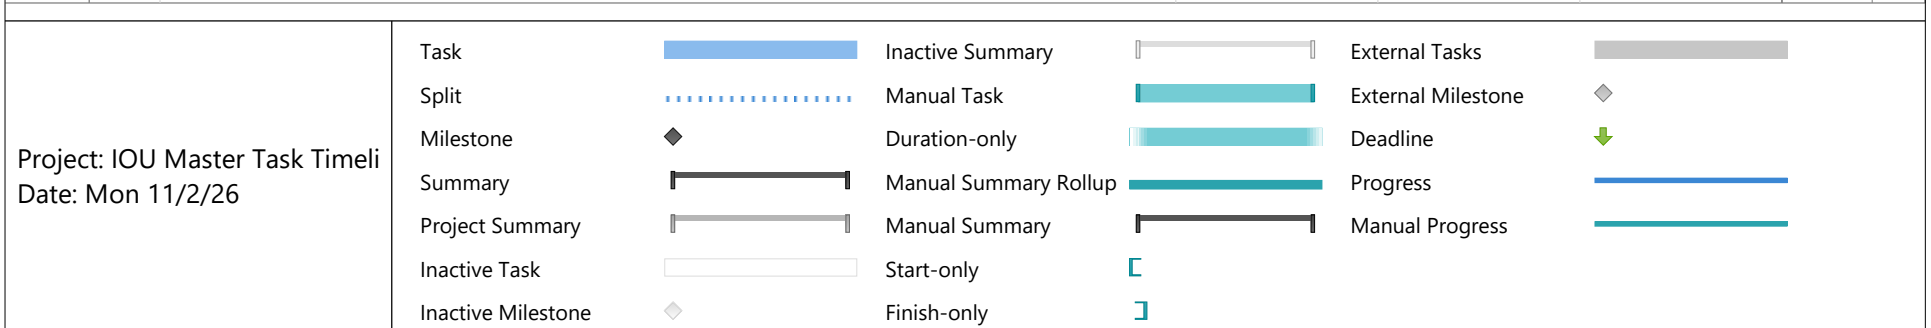


ID	Task Name	Duration	Start	Finish	2018 H1	H2
24	SCE - RFA Abstract Creation Duration	20 days	Wed 7/3/19	Tue 7/30/19		
25	SCE - RFA Evaluation	34 days	Wed 7/31/19	Mon 9/16/19		
26	SCE - RFA Review with EE PRG	1 day	Tue 9/17/19	Tue 9/17/19		
27	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/24/19	Tue 9/24/19		
28	SCE - RFP Preparation	84 days	Wed 9/25/19	Mon 1/20/20		
29	SCE - RFP Release	1 day	Thu 2/6/20	Thu 2/6/20		
30	SCE - RFP Proposal Creation Duration	27 days	Fri 2/7/20	Mon 3/16/20		
31	SCE - RFP Evaluation	25 days	Tue 3/17/20	Mon 4/20/20		
32	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20		
33	SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20		
34	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20		
35	SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20		
36	SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20		
37	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20		
38	SCE - Advice Letter Approved	1 day	Wed 12/23/20	Wed 12/23/20		
39	SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21		
40	**SCE - Local Public Sector Solicitation**	**573 days**	**Mon 8/31/20**	**Wed 11/9/22**		
41	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20		
42	SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20		
43	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20		
44	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21		
45	SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21		
46	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26




ID	Task Name	Duration	Start	Finish	2018 H1	H2
47	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21		
48	SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21		
49	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21		
50	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21		
51	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21		
52	SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21		
53	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21		
54	SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21		
55	SCE - Final Award and Contract Signed	1 day	Tue 12/14/21	Tue 12/14/21		
56	SCE - Submit Advice Letter	37 days	Wed 12/15/21	Thu 2/3/22		
57	SCE - Submit Advice Letter	48 days	Wed 12/15/21	Fri 2/18/22		
58	SCE - Advice Letter Approved	1 day	Thu 8/18/22	Thu 8/18/22		
59	SCE - Implementation Plan	60 days	Thu 8/18/22	Wed 11/9/22		
60	**SCE - Local Agriculture Solicitation**	**512 days**	**Mon 8/31/20**	**Tue 8/16/22**		
61	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20		
62	SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20		
63	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20		
64	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21		
65	SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21		
66	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21		
67	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21		
68	SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21		
69	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26




ID	Task Name	Duration	Start	Finish	2018 H1	H2
70	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21		
71	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21		
72	SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21		
73	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21		
74	SCE - Final Award and Contract Signed	1 day	Mon 12/20/21	Mon 12/20/21		
75	SCE - Submit Advice Letter	33 days	Tue 12/21/21	Thu 2/3/22		
76	SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21		
77	SCE - Final Award and Contract Signed	1 day	Wed 12/15/21	Wed 12/15/21		
78	SCE - Submit Advice Letter	56 days	Thu 12/16/21	Thu 3/3/22		
79	SCE - Advice Letter Approved	1 day	Fri 4/22/22	Fri 4/22/22		
80	SCE - Implementation Plan	60 days	Sat 4/23/22	Thu 7/14/22		
81	**SCE - SW Water/Wastewater Solicitation**	**522 days**	**Mon 11/16/20**	**Tue 11/15/22**		
82	SCE - RFA Preparation	70 days	Mon 11/16/20	Fri 2/19/21		
83	SCE - RFA Release	1 day	Thu 3/4/21	Thu 3/4/21		
84	SCE - RFA Abstract Creation Duration	29 days	Thu 3/4/21	Tue 4/13/21		
85	SCE - RFA Evaluation	20 days	Wed 4/14/21	Tue 5/11/21		
86	SCE - RFA Review with EE PRG	1 day	Tue 5/18/21	Tue 5/18/21		
87	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/27/21	Thu 5/27/21		
88	SCE - RFP Preparation	34 days	Mon 4/19/21	Thu 6/3/21		
89	SCE - RFP Release	1 day	Thu 7/1/21	Thu 7/1/21		
90	SCE - RFP Proposal Creation Duration	25 days	Fri 7/2/21	Thu 8/5/21		
91	SCE - RFP Evaluation	41 days	Fri 8/6/21	Fri 10/1/21		
92	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/26/21	Tue 10/26/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26



ID	Task Name	Duration	Start	Finish	2018 H1	H2
93	SCE - RFP Review with EE PRG	1 day	Tue 10/19/21	Tue 10/19/21		
94	SCE - Contract Negotiation and Development	94 days	Wed 10/27/21	Mon 3/7/22		
95	SCE - Contract Review with EE PRG	1 day	Tue 3/15/22	Tue 3/15/22		
96	SCE - Final Award and Contract Signed	1 day	Tue 4/19/22	Tue 4/19/22		
97	SCE - Submit Advice Letter	40 days	Wed 4/20/22	Tue 6/14/22		
98	SCE - Advice Letter Approved	26 days	Wed 6/15/22	Wed 7/20/22		
99	SCE - Implementation Plan	44 days	Thu 7/21/22	Tue 9/20/22		
100	**SCE - SW ETP Solicitation**	**466 days**	**Fri 5/1/20**	**Fri 2/11/22**		
101	SCE - RFA Preparation	57 days	Fri 5/1/20	Mon 7/20/20		
102	SCE - RFA Release	1 day	Tue 8/4/20	Tue 8/4/20		
103	SCE - RFA Abstract Creation Duration	24 days	Fri 8/7/20	Wed 9/9/20		
104	SCE - RFA Evaluation	16 days	Thu 9/10/20	Thu 10/1/20		
105	SCE - RFA Review with EE PRG	1 day	Tue 10/20/20	Tue 10/20/20		
106	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/27/20	Tue 10/27/20		
107	SCE - RFP Preparation	42 days	Tue 9/8/20	Wed 11/4/20		
108	SCE - RFP Release	1 day	Tue 1/5/21	Tue 1/5/21		
109	SCE - RFP Proposal Creation Duration	37 days	Tue 1/5/21	Wed 2/24/21		
110	SCE - RFP Evaluation	28 days	Wed 2/24/21	Fri 4/2/21		
111	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/27/21	Tue 4/27/21		
112	SCE - RFP Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21		
113	SCE - Contract Negotiation and Development	69 days	Wed 4/21/21	Mon 7/26/21		
114	SCE - Contract Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21		
115	SCE - Final Award and Contract Signed	1 day	Tue 9/14/21	Tue 9/14/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26




ID	Task Name	Duration	Start	Finish	2018 H1	H2
116	SCE - Submit Advice Letter	18 days	Wed 9/15/21	Fri 10/8/21		
117	SCE - Advice Letter Approved	1 day	Tue 11/9/21	Tue 11/9/21		
118	SCE - Implementation Plan	60 days	Wed 11/10/21	Tue 2/1/22		
119	**SCE - SW Higher-Education Solicitation**	**547 days?**	**Thu 10/1/20**	**Fri 11/4/22**		
120	SCE - RFA Preparation	89 days	Thu 10/1/20	Tue 2/2/21		
121	SCE - RFA Release	1 day	Thu 2/4/21	Thu 2/4/21		
122	SCE - RFA Abstract Creation Duration	19 days	Fri 2/5/21	Wed 3/3/21		
123	SCE - RFA Evaluation	31 days	Thu 3/4/21	Thu 4/15/21		
124	SCE - RFA Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21		
125	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 4/29/21	Thu 4/29/21		
126	SCE - RFP Preparation	39 days	Mon 3/22/21	Thu 5/13/21		
127	SCE - RFP Release	1 day	Fri 5/28/21	Fri 5/28/21		
128	SCE - RFP Proposal Creation Duration	24 days	Fri 6/4/21	Wed 7/7/21		
129	SCE - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21		
130	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/30/21	Mon 8/30/21		
131	SCE - RFP Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21		
132	SCE - Contract Negotiation and Development	95 days	Fri 9/3/21	Thu 1/13/22		
133	SCE - Contract Review with EE PRG	1 day	Tue 1/18/22	Tue 1/18/22		
134	SCE - Final Award and Contract Signed	1 day	Sun 3/6/22	Sun 3/6/22		
135	SCE - Submit Advice Letter	1 day	Tue 4/19/22	Tue 4/19/22		
136	SCE - Advice Letter Approved	1 day	Mon 8/15/22	Mon 8/15/22		
137	SCE - Implementation Plan	60 days	Mon 8/15/22	Fri 11/4/22		
138	**SCE - Local Equity Residential and SMB**	**384 days?**	**Tue 2/15/22**	**Fri 8/4/23**		

Project: IOU Master Task Timeli
Date: Mon 11/2/26


Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
139	SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22		
140	SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22		
141	SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22		
142	SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22		
143	SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22		
144	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22		
145	SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22		
146	SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22		
147	SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22		
148	SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22		
149	SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22		
150	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22		
151	SCE - Contract Negotiation and Development	65 days	Wed 11/2/22	Tue 1/31/23		
152	SCE - Contract Review with EE PRG	1 day	Tue 2/21/23	Tue 2/21/23		
153	SCE - Final Award and Contract Signed	1 day	Thu 3/30/23	Thu 3/30/23		
154	SCE - Submit Advice Letter	22 days	Sun 4/3/22	Mon 5/2/22		
155	SCE - Advice Letter Approved	28 days	Tue 5/2/23	Thu 6/8/23		
156	SCE - Implementation Plan	45 days	Thu 6/8/23	Wed 8/9/23		
157						
158	**SCE - Local Equity SMB**	**431 days?**	**Tue 2/15/22**	**Tue 10/10/23**		
159	SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22		
160	SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22		
161	SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

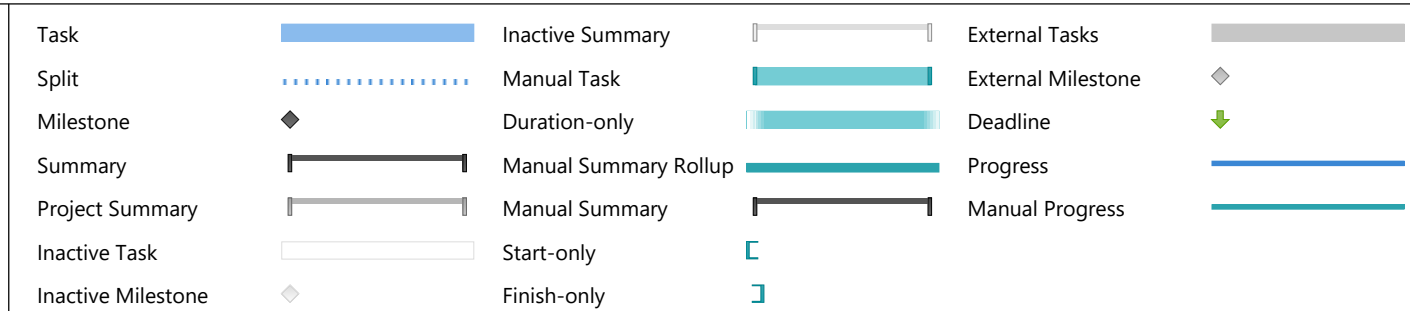


ID	Task Name	Duration	Start	Finish
162	SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22
163	SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22
164	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22
165	SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22
166	SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22
167	SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22
168	SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22
169	SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22
170	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22
171	SCE - Contract Negotiation and Development	108 days	Wed 11/2/22	Fri 3/31/23
172	SCE - Contract Review with EE PRG	1 day	Tue 4/18/23	Tue 4/18/23
173	SCE - Final Award and Contract Signed	1 day	Wed 5/31/23	Wed 5/31/23
174	SCE - Submit Advice Letter	22 days	Mon 6/6/22	Tue 7/5/22
175	SCE - Advice Letter Approved	24 days	Thu 7/6/23	Tue 8/8/23
176	SCE - Implementation Plan	45 days	Wed 8/9/23	Tue 10/10/23
177	**SCE - Local Strategic Energy Management Solicitation**	**372 days?**	**Thu 12/1/22**	**Fri 5/3/24**
178	SCE - RFP Preparation	85 days	Thu 12/1/22	Wed 3/29/23
179	SCE - RFP Release	1 day	Fri 4/7/23	Fri 4/7/23
180	SCE - RFP Proposal Creation Duration	35 days	Fri 4/7/23	Thu 5/25/23
181	SCE - RFP Evaluation	22 days	Thu 6/1/23	Fri 6/30/23
182	SCE - RFP Review with EE PRG	1 day	Tue 7/18/23	Tue 7/18/23
183	SCE - Contract Negotiation and Development	86 days	Tue 8/1/23	Tue 11/28/23
184	SCE - Contract Review with EE PRG	1 day	Tue 12/19/23	Tue 12/19/23



ID	Task Name	Duration	Start	Finish	2018 H1	H2
185	SCE - Final Award and Contract Signed	6 days	Fri 1/19/24	Fri 1/26/24		
186	SCE - Submit Advice Letter	34 days	Wed 1/31/24	Mon 3/18/24		
187	SCE - Advice Letter Approved	40 days	Tue 3/19/24	Mon 5/13/24		
188	**SCE - Local Large Commercial Solicitation**	**488 days?**	**Mon 6/26/23**	**Wed 5/7/25**		
189	SCE - RFP Preparation	35 days	Mon 6/26/23	Fri 8/11/23		
190	SCE - RFP Release	1 day	Thu 8/17/23	Thu 8/17/23		
191	SCE - RFP Proposal Creation Duration	41 days	Thu 8/17/23	Thu 10/12/23		
192	SCE - RFP Paused	1 day	Fri 10/13/23	Fri 10/13/23		
193	**SCE - Residential Multifamily**	**326 days?**	**Fri 9/1/23**	**Fri 11/29/24**		
194	SCE - RFP Preparation	47 days	Fri 9/1/23	Mon 11/6/23		
195	SCE - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23		
196	SCE - RFP Proposal Creation Duration	48 days	Mon 11/6/23	Wed 1/10/24		
197	SCE - RFP Evaluation	25 days	Thu 1/11/24	Wed 2/14/24		
198	SCE - RFP Review with EE PRG	1 day	Tue 2/20/24	Tue 2/20/24		
199	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 2/28/24	Wed 2/28/24		
200	SCE - Contract Negotiation and Development	70 days	Mon 3/4/24	Fri 6/7/24		
201	SCE - Contract Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
202	SCE - Final Award and Contract Signed	15 days	Mon 7/29/24	Fri 8/16/24		
203	SCE - Submit Advice Letter	30 days	Mon 8/19/24	Fri 9/27/24		
204	SCE - Advice Letter Approved	1 day	Mon 10/28/24	Mon 10/28/24		
205	**SCE - Local Large Industrial**	**499 days**	**Fri 11/3/23**	**Wed 10/1/25**		
206	SCE - RFP Preparation	17 days	Fri 11/3/23	Mon 11/27/23		
207	SCE - RFP Release	1 day	Mon 12/11/23	Mon 12/11/23		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

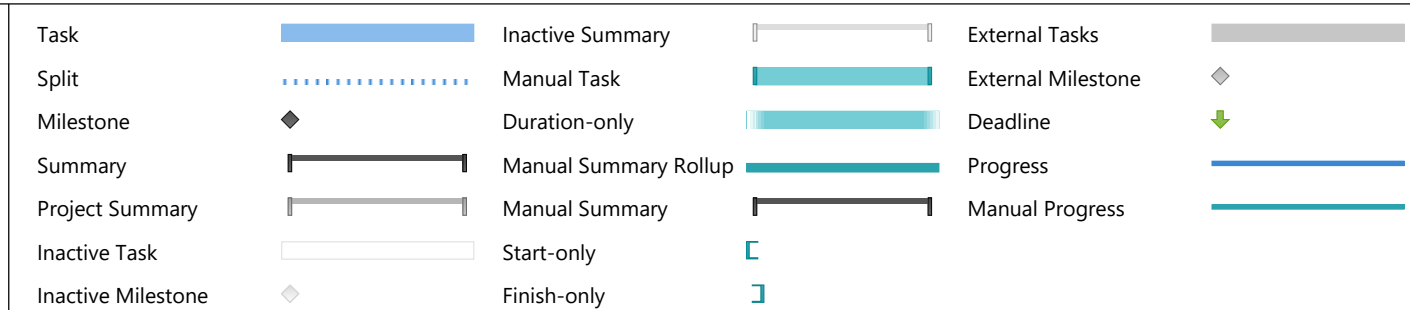

ID	Task Name	Duration	Start	Finish	2018 H1	H2
208	SCE - RFP Proposal Creation Duration	49 days	Mon 12/11/23	Thu 2/15/24		
209	SCE - RFP Evaluation	35 days	Fri 2/16/24	Thu 4/4/24		
210	SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24		
211	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/23/24	Tue 4/23/24		
212	SCE - Contract Negotiation and Development	208 days	Wed 4/24/24	Fri 2/7/25		
213	SCE - Contract Review with EE PRG	1 day	Tue 4/29/25	Tue 4/29/25		
214	SCE - Final Award and Contract Signed	42 days	Thu 5/1/25	Fri 6/27/25		
215	SCE - Submit Advice Letter	35 days	Mon 6/30/25	Fri 8/15/25		
216	SCE - Advice Letter Approved	33 days	Mon 8/18/25	Wed 10/1/25		
217	**SCE - MAP - All Sectors**	**299 days?**	**Mon 11/20/23**	**Thu 1/9/25**		
218	SCE - RFP Preparation	20 days	Mon 11/20/23	Fri 12/15/23		
219	SCE - RFP Release	1 day	Mon 1/8/24	Mon 1/8/24		
220	SCE - RFP Proposal Creation Duration	40 days	Mon 1/8/24	Fri 3/1/24		
221	SCE - RFP Evaluation	30 days	Mon 3/4/24	Fri 4/12/24		
222	SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24		
223	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/24/24	Wed 4/24/24		
224	SCE - Contract Negotiation and Development	108 days	Wed 5/1/24	Fri 9/27/24		
225	SCE - Contract Review with EE PRG	1 day	Tue 10/15/24	Tue 10/15/24		
226	SCE - Final Award and Contract Signed	12 days	Tue 10/29/24	Wed 11/13/24		
227	SCE - Submit Advice Letter	43 days	Wed 11/13/24	Fri 1/10/25		
228	SCE - Advice Letter Approved	22 days	Mon 1/13/25	Tue 2/11/25		
229	**SCE - Residential**	**360 days?**	**Mon 11/20/23**	**Fri 4/4/25**		
230	SCE - RFP Preparation	20 days	Tue 1/16/24	Mon 2/12/24		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
231	SCE - RFP Release	1 day	Thu 3/28/24	Thu 3/28/24		
232	SCE - RFP Proposal Creation Duration	41 days	Thu 3/28/24	Thu 5/23/24		
233	SCE - RFP Evaluation	35 days	Fri 5/24/24	Thu 7/11/24		
234	SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
235	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/5/24	Mon 8/5/24		
236	SCE - Contract Negotiation and Development	80 days	Mon 8/19/24	Fri 12/6/24		
237	SCE - Contract Review with EE PRG	1 day	Tue 12/17/24	Tue 12/17/24		
238	SCE - Final Award and Contract Signed	11 days	Mon 1/13/25	Mon 1/27/25		
239	SCE - Submit Advice Letter	19 days	Mon 2/3/25	Thu 2/27/25		
240	SCE - Advice Letter Approved	1 day	Tue 4/1/25	Tue 4/1/25		
241						
242	**SCE - Local Comprehensive Commercial Solicitation**	**431 days?**	**Mon 11/13/23**	**Mon 7/7/25**		
243	SCE - RFP Preparation	73 days	Mon 11/13/23	Wed 2/21/24		
244	SCE - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24		
245	SCE - RFP Proposal Creation Duration	43 days	Thu 2/29/24	Mon 4/29/24		
246	SCE - RFP Evaluation	54 days	Tue 4/30/24	Fri 7/12/24		
247	SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
248	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Pha	1 day	Mon 7/29/24	Mon 7/29/24		
249	SCE - Contract Negotiation and Development - Phase 1	81 days	Tue 7/30/24	Tue 11/19/24		
250	SCE - Contract Review with EE PRG - Phase 1	1 day	Tue 12/17/24	Tue 12/17/24		
251	SCE - Final Award and Contract Signed - Phase 1	1 day	Tue 1/28/25	Tue 1/28/25		
252	SCE - Submit Advice Letter - Phase 1	23 days	Tue 1/28/25	Thu 2/27/25		
253	SCE - Advice Letter Approved - Phase 1	1 day	Tue 4/1/25	Tue 4/1/25		

Project: IOU Master Task Timeli
Date: Mon 11/2/26


Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
254	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Pha	1 day	Mon 9/30/24	Mon 9/30/24		
255	SCE - Contract Negotiation and Development - Phase 2	80 days	Mon 12/2/24	Fri 3/21/25		
256	SCE - Contract Review with EE PRG - Phase 2	1 day	Tue 4/29/25	Tue 4/29/25		
257	SCE - Final Award and Contract Signed - Phase 2	1 day	Tue 5/20/25	Tue 5/20/25		
258	SCE - Submit Advice Letter - Phase 2	0 days	N/A	N/A		
259	SCE - Advice Letter Approved - Phase 2	0 days	N/A	N/A		
260	**SCE - SW ETP Solicitation**	**505 days**	**Wed 2/25/26**	**Tue 2/1/28**		
261	SCE - RFA Preparation	63 days	Wed 2/25/26	Fri 5/22/26		
262	SCE - RFA Release	1 day	Tue 5/26/26	Tue 5/26/26		
263	SCE - RFA Abstract Creation Duration	34 days	Tue 5/26/26	Fri 7/10/26		
264	SCE - RFA Evaluation	19 days	Tue 7/21/26	Fri 8/14/26		
265	SCE - RFA Review with EE PRG	1 day	Tue 8/18/26	Tue 8/18/26		
266	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/25/26	Tue 8/25/26		
267	SCE - RFP Preparation	42 days	Mon 7/6/26	Tue 9/1/26		
268	SCE - RFP Release	1 day	Mon 11/2/26	Mon 11/2/26		
269	SCE - RFP Proposal Creation Duration	37 days	Mon 11/2/26	Tue 12/22/26		
270	SCE - RFP Evaluation	25 days	Wed 1/6/27	Tue 2/9/27		
271	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/16/27	Tue 2/16/27		
272	SCE - RFP Review with EE PRG	1 day	Tue 2/23/27	Tue 2/23/27		
273	SCE - Contract Negotiation and Development	80 days	Tue 3/2/27	Mon 6/21/27		
274	SCE - Contract Review with EE PRG	1 day	Tue 7/20/27	Tue 7/20/27		
275	SCE - Final Award and Contract Signed	1 day	Wed 7/28/27	Wed 7/28/27		
276	SCE - Submit Advice Letter	23 days	Thu 8/5/27	Mon 9/6/27		


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


ID	Task Name	Duration	Start	Finish
277	SCE - Advice Letter Approved	46 days	Tue 9/7/27	Tue 11/9/27
278	SCE - Implementation Plan	60 days	Wed 11/10/27	Tue 2/1/28
279	**SCE - Statewide Higher Education (2026)**	**303 days?**	**Wed 9/16/26**	**Fri 11/12/27**
280	SCE - RFP Preparation	25 days	Wed 9/16/26	Tue 10/20/26
281	SCE - RFP Release	1 day	Wed 10/21/26	Wed 10/21/26
282	SCE - RFP Proposal Creation Duration	38 days	Wed 10/21/26	Fri 12/11/26
283	SCE - RFP Evaluation	0 days	Sat 12/12/26	Sat 12/12/26
284	SCE - RFP Review with EE PRG	1 day	Tue 2/16/27	Tue 2/16/27
285	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/25/27	Thu 2/25/27
286	SCE - Contract Negotiation and Development	70 days	Wed 3/3/27	Tue 6/8/27
287	SCE - Contract Review with EE PRG	1 day	Tue 6/15/27	Tue 6/15/27
288	SCE - Final Award and Contract Signed	11 days	Wed 7/7/27	Wed 7/21/27
289	SCE - Submit Advice Letter	33 days	Thu 7/22/27	Mon 9/6/27
290	SCE - Advice Letter Approved	47 days	Thu 9/9/27	Fri 11/12/27
291				
292	**SCG - Local Single Family Solicitation**	**660 days**	**Sun 7/1/18**	**Thu 1/7/21**
293	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18
294	SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18
295	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19
296	SCG - RFA Evaluation	39 days	Mon 1/7/19	Thu 2/28/19
297	SCG - RFA Review with EE PRG	1 day	Tue 3/5/19	Tue 3/5/19
298	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19
299	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19




ID	Task Name	Duration	Start	Finish
300	SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19
301	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19
302	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19
303	SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19
304	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20
305	SCG - Contract Negotiation and Development	69 days	Mon 1/27/20	Thu 4/30/20
306	SCG - Contract Review with EE PRG	14 days	Tue 5/5/20	Fri 5/22/20
307	SCG - Final Award and Contract Signed	8 days	Mon 5/25/20	Wed 6/3/20
308	SCG - Submit Advice Letter	96 days	Mon 6/1/20	Mon 10/12/20
309	SCG - Advice Letter Approved	1 day	Thu 11/12/20	Thu 11/12/20
310	SCG - Implementation Plan	41 days	Fri 11/13/20	Fri 1/8/21
311	**SCG - Local Multi-family Solicitation**	**735 days**	**Sun 7/1/18**	**Thu 4/22/21**
312	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18
313	SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18
314	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19
315	SCG - RFA Evaluation	59 days	Mon 1/7/19	Thu 3/28/19
316	SCG - RFA Review with EE PRG	1 day	Tue 4/2/19	Tue 4/2/19
317	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19
318	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19
319	SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19
320	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19
321	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19
322	SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19



ID	Task Name	Duration	Start	Finish
323	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20
324	SCG - Contract Negotiation and Development	155 days	Mon 1/27/20	Fri 8/28/20
325	SCG - Contract Review with EE PRG	99 days	Tue 5/5/20	Fri 9/18/20
326	SCG - Final Award and Contract Signed	8 days	Mon 9/21/20	Wed 9/30/20
327	SCG - Submit Advice Letter	37 days	Thu 10/1/20	Fri 11/20/20
328	SCG - Advice Letter Approved	1 day	Sun 5/2/21	Sun 5/2/21
329	SCG - Implementation Plan	51 days	Mon 5/3/21	Mon 7/12/21
330	**SCG - Local Small/Medium Commercial Solicitation**	**641 days**	**Tue 9/4/18**	**Tue 2/16/21**
331	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19
332	SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19
333	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19
334	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19
335	SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19
336	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19
337	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19
338	SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19
339	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19
340	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19
341	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19
342	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20
343	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20
344	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20
345	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20

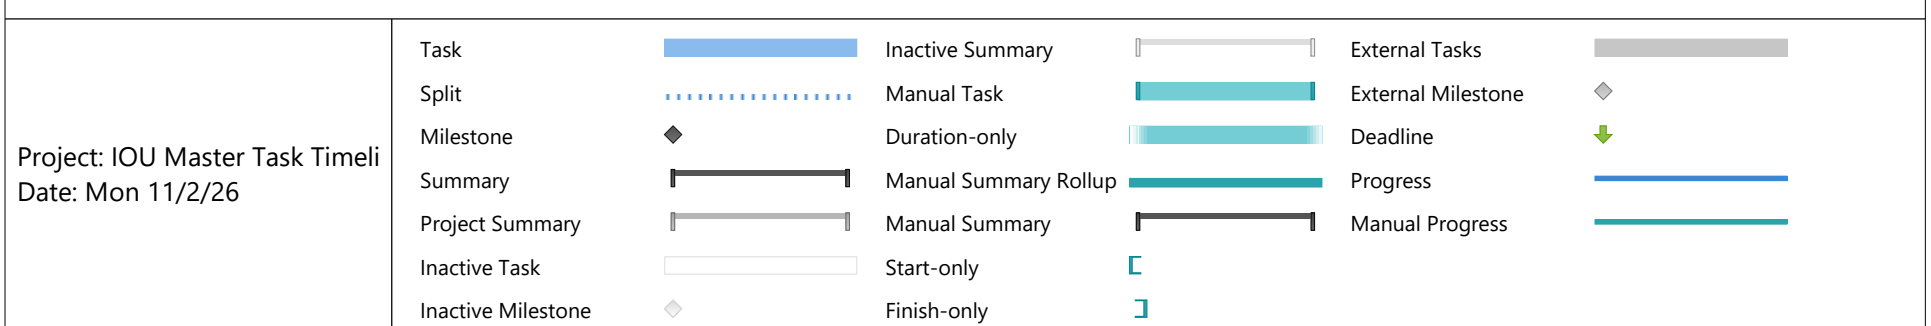

ID	Task Name	Duration	Start	Finish
346	SCG - Submit Advice Letter	59 days	Tue 9/1/20	Fri 11/20/20
347	SCG - Advice Letter Approved	1 day	Fri 12/18/20	Fri 12/18/20
348	SCG - Implementation Plan	43 days	Sat 12/19/20	Tue 2/16/21
349	**SCG - Local Small/Medium Public Solicitation**	**631 days**	**Tue 9/4/18**	**Tue 2/2/21**
350	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19
351	SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19
352	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19
353	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19
354	SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19
355	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19
356	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19
357	SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19
358	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19
359	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19
360	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19
361	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20
362	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20
363	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20
364	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20
365	SCG - Submit Advice Letter	49 days	Tue 9/1/20	Fri 11/6/20
366	SCG - Advice Letter Approved	1 day	Fri 12/4/20	Fri 12/4/20
367	SCG - Implementation Plan	43 days	Sat 12/5/20	Tue 2/2/21
368	**SCG - Statewide POS Food Service Solicitation**	**605 days**	**Mon 1/21/19**	**Fri 5/14/21**




ID	Task Name	Duration	Start	Finish	2018 H1	H2
369	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19		
370	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19		
371	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19		
372	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19		
373	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19		
374	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20		
375	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19		
376	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20		
377	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20		
378	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20		
379	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20		
380	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20		
381	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20		
382	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20		
383	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20		
384	SCG - Submit Advice Letter	32 days	Mon 11/2/20	Tue 12/15/20		
385	SCG - Advice Letter Approved	1 day	Thu 1/14/21	Thu 1/14/21		
386	SCG - Implementation Plan	42 days	Fri 1/15/21	Mon 3/15/21		
387	**SCG - Statewide Midstream Water Heating Solicitation**	**597 days**	**Mon 1/21/19**	**Tue 5/4/21**		
388	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19		
389	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19		
390	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19		
391	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
392	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19		
393	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20		
394	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19		
395	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20		
396	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20		
397	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20		
398	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20		
399	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20		
400	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20		
401	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20		
402	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20		
403	SCG - Submit Advice Letter	25 days	Mon 11/2/20	Fri 12/4/20		
404	SCG - Advice Letter Approved	1 day	Thu 3/18/21	Thu 3/18/21		
405	SCG - Implementation Plan	22 days	Fri 3/19/21	Mon 4/19/21		
406	**SCG - Statewide Gas Emerging Technology Solicitation**	**738 days**	**Wed 1/2/19**	**Fri 10/29/21**		
407	SCG - RFA Preparation	283 days	Wed 1/2/19	Fri 1/31/20		
408	SCG - RFA Release	1 day	Wed 2/12/20	Wed 2/12/20		
409	SCG - RFA Abstract Creation Duration	30 days	Thu 2/13/20	Wed 3/25/20		
410	SCG - RFA Evaluation	26 days	Thu 3/26/20	Thu 4/30/20		
411	SCG - RFA Review with EE PRG	1 day	Tue 5/5/20	Tue 5/5/20		
412	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 5/15/20	Fri 5/15/20		
413	SCG - RFP Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
414	SCG - RFP Release	1 day	Fri 8/21/20	Fri 8/21/20		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

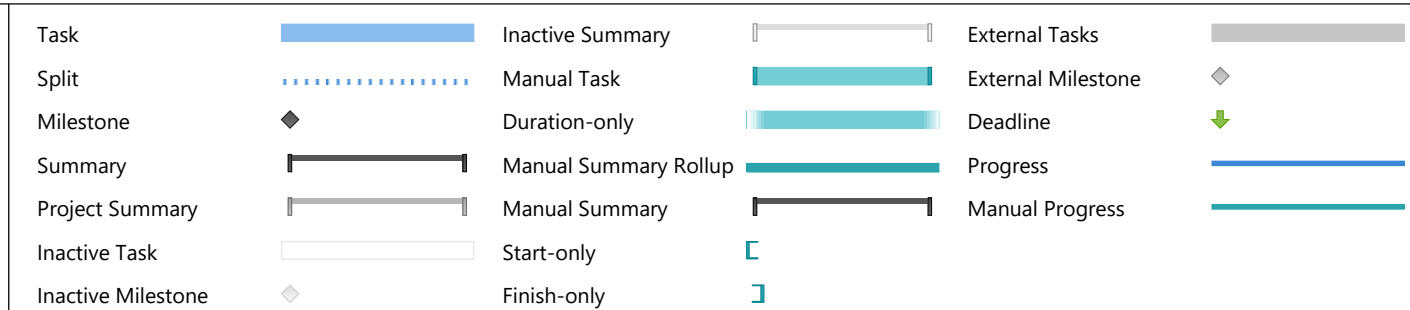


ID	Task Name	Duration	Start	Finish	2018 H1	H2
415	SCG - RFP Proposal Creation Duration	30 days	Mon 8/24/20	Fri 10/2/20		
416	SCG - RFP Evaluation	38 days	Mon 10/5/20	Wed 11/25/20		
417	SCG - RFP Review with EE PRG	1 day	Tue 12/1/20	Tue 12/1/20		
418	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 12/7/20	Mon 12/7/20		
419	SCG - Contract Negotiation and Development	85 days	Mon 1/4/21	Fri 4/30/21		
420	SCG - Contract Review with EE PRG	9 days	Tue 5/4/21	Fri 5/14/21		
421	SCG - Final Award and Contract Signed	29 days	Mon 5/17/21	Thu 6/24/21		
422	SCG - Submit Advice Letter	23 days	Sun 6/27/21	Tue 7/27/21		
423	SCG - Advice Letter Approved	1 day	Tue 8/24/21	Tue 8/24/21		
424	SCG - Implementation Plan	44 days	Wed 8/25/21	Sat 10/23/21		
425	**SCG - Local Manufactured Housing Solicitation**	**341 days**	**Fri 11/1/19**	**Fri 2/19/21**		
426	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		
427	SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20		
428	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
429	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
430	SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20		
431	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20		
432	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
433	SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20		
434	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
435	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
436	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
437	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


ID	Task Name	Duration	Start	Finish	2018 H1	H2
438	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
439	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
440	SCG - Final Award and Contract Signed	9 days	Thu 12/10/20	Tue 12/22/20		
441	SCG - Submit Advice Letter	0 days	N/A	N/A		
442	SCG - Advice Letter Approved	0 days	N/A	N/A		
443	SCG - Implementation Plan	44 days	Tue 12/22/20	Fri 2/19/21		
444	**SCG - Local Large Commercial Solicitation**	**434 days**	**Fri 11/1/19**	**Wed 6/30/21**		
445	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		
446	SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20		
447	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
448	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
449	SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20		
450	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20		
451	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
452	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20		
453	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
454	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
455	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
456	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
457	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
458	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
459	SCG - Final Award and Contract Signed	10 days	Thu 12/10/20	Wed 12/23/20		
460	SCG - Submit Advice Letter	64 days	Fri 1/1/21	Wed 3/31/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26



ID	Task Name	Duration	Start	Finish	2018 H1	H2
461	SCG - Advice Letter Approved	1 day	Fri 6/4/21	Fri 6/4/21		
462	SCG - Implementation Plan	43 days	Sat 6/5/21	Tue 8/3/21		
463	**SCG - Local Agricultural Solicitation**	**434 days**	**Fri 11/1/19**	**Wed 6/30/21**		
464	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		
465	SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20		
466	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
467	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
468	SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20		
469	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20		
470	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
471	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20		
472	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
473	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
474	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
475	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
476	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
477	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
478	SCG - Final Award and Contract Signed	2 days	Fri 12/11/20	Mon 12/14/20		
479	SCG - Submit Advice Letter	41 days	Fri 1/1/21	Fri 2/26/21		
480	SCG - Advice Letter Approved	1 day	Wed 4/7/21	Wed 4/7/21		
481	SCG - Implementation Plan	43 days	Thu 4/8/21	Mon 6/7/21		
482	**SCG - Local Behavioral Solicitation - Residential**	**413 days?**	**Fri 5/1/20**	**Tue 11/30/21**		
483	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20		

Project: IOU Master Task Timeli
Date: Mon 11/2/26




ID	Task Name	Duration	Start	Finish	2018 H1	H2
484	SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20		
485	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20		
486	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20		
487	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20		
488	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20		
489	SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20		
490	SCG - RFP Release	1 day	Fri 1/15/21	Fri 1/15/21		
491	SCG - RFP Proposal Creation Duration	26 days	Mon 1/18/21	Mon 2/22/21		
492	SCG - RFP Evaluation	29 days	Tue 2/23/21	Fri 4/2/21		
493	SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21		
494	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/13/21	Tue 4/13/21		
495	SCG - Contract Negotiation and Development	95 days	Mon 4/26/21	Fri 9/3/21		
496	SCG - Contract Review with EE PRG	9 days	Tue 9/7/21	Fri 9/17/21		
497	SCG - Final Award and Contract Signed	30 days	Mon 9/20/21	Fri 10/29/21		
498	SCG - Submit Advice Letter	21 days	Mon 11/1/21	Mon 11/29/21		
499	SCG - Advice Letter Approved	1 day	Wed 12/22/21	Wed 12/22/21		
500	SCG - Implementation Plan	43 days	Thu 12/23/21	Sun 2/20/22		
501	**SCG - Local Behavioral Solicitation - Commercial**	**413 days?**	**Fri 5/1/20**	**Tue 11/30/21**		
502	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
503	SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20		
504	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20		
505	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20		
506	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
507	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20		
508	SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20		
509	SCG - RFP Release	1 day	Fri 1/22/21	Fri 1/22/21		
510	SCG - RFP Proposal Creation Duration	26 days	Mon 1/25/21	Mon 3/1/21		
511	SCG - RFP Evaluation	24 days	Tue 3/2/21	Fri 4/2/21		
512	SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21		
513	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 11/12/21	Fri 11/12/21		
514	SCG - Contract Negotiation and Development	132 days	Mon 11/29/21	Tue 5/31/22		
515	SCG - Contract Review with EE PRG	8 days	Sun 6/5/22	Tue 6/14/22		
516	SCG - Final Award and Contract Signed	109 days	Fri 7/1/22	Wed 11/30/22		
517	SCG - Submit Advice Letter	23 days	N/A	N/A		
518	SCG - Advice Letter Approved	1 day	N/A	N/A		
519	SCG - Implementation Plan	43 days	Thu 12/1/22	Sun 1/29/23		
520	**SCG - Local Industrial Solicitation**	**434 days?**	**Tue 12/1/20**	**Fri 7/29/22**		
521	SCG - RFA Preparation	63 days?	Tue 12/1/20	Thu 2/25/21		
522	SCG - RFA Release	1 day?	Fri 3/19/21	Fri 3/19/21		
523	SCG - RFA Abstract Creation Duration	25 days?	Mon 3/22/21	Fri 4/23/21		
524	SCG - RFA Evaluation	25 days?	Mon 4/26/21	Fri 5/28/21		
525	SCG - RFA Review with EE PRG	1 day?	Tue 6/1/21	Tue 6/1/21		
526	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 6/8/21	Tue 6/8/21		
527	SCG - RFP Preparation	67 days?	Thu 4/1/21	Fri 7/2/21		
528	SCG - RFP Release	1 day?	Fri 7/16/21	Fri 7/16/21		
529	SCG - RFP Proposal Creation Duration	30 days?	Mon 7/19/21	Fri 8/27/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26



ID	Task Name	Duration	Start	Finish	2018 H1	H2
530	SCG - RFP Evaluation	25 days?	Mon 8/30/21	Fri 10/1/21		
531	SCG - RFP Review with EE PRG	1 day?	Tue 10/5/21	Tue 10/5/21		
532	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 12/14/21	Tue 12/14/21		
533	SCG - Contract Negotiation and Development	127 days?	Thu 2/3/22	Fri 7/29/22		
534	SCG - Contract Review with EE PRG	9 days?	Tue 8/2/22	Fri 8/12/22		
535	SCG - Final Award and Contract Signed	21 days?	Fri 7/29/22	Fri 8/26/22		
536	SCG - Submit Advice Letter	1 day?	Sun 10/30/22	Sun 10/30/22		
537	SCG - Advice Letter Approved	1 day?	Mon 1/30/23	Mon 1/30/23		
538	SCG - Implementation Plan	45 days?	Tue 1/31/23	Sat 4/1/23		
539	**SCG - Large Public Sector Solicitation (re-Bid)**	**412 days**	**Mon 1/4/21**	**Tue 8/2/22**		
540	SCG - RFA Preparation	65 days	Mon 1/4/21	Fri 4/2/21		
541	SCG - RFA Release	1 day	Fri 7/16/21	Fri 7/16/21		
542	SCG - RFA Abstract Creation Duration	20 days	Mon 7/19/21	Fri 8/13/21		
543	SCG - RFA Evaluation	15 days	Mon 8/16/21	Fri 9/3/21		
544	SCG - RFA Review with EE PRG	1 day	Tue 9/7/21	Tue 9/7/21		
545	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/14/21	Tue 9/14/21		
546	SCG - RFP Preparation	35 days	Mon 9/13/21	Fri 10/29/21		
547	SCG - RFP Release	1 day	Mon 11/8/21	Mon 11/8/21		
548	SCG - RFP Proposal Creation Duration	29 days	Tue 11/9/21	Fri 12/17/21		
549	SCG - RFP Evaluation	30 days	Mon 12/20/21	Fri 1/28/22		
550	SCG - RFP Review with EE PRG	1 day	Tue 2/1/22	Tue 2/1/22		
551	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/8/22	Tue 3/8/22		
552	SCG - Contract Negotiation and Development	79 days	Mon 3/14/22	Thu 6/30/22		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
553	SCG - Contract Review with EE PRG	9 days	Tue 7/5/22	Fri 7/15/22		
554	SCG - Final Award and Contract Signed	63 days	Mon 7/18/22	Wed 10/12/22		
555	SCG - Submit Advice Letter	23 days	N/A	N/A		
556	SCG - Advice Letter Approved	1 day	N/A	N/A		
557	SCG - Implementation Plan	44 days	Wed 10/12/22	Sat 12/10/22		
558	**SCG - Outreach Solicitation**	**434 days**	**Mon 2/1/21**	**Thu 9/29/22**		
559	SCG - RFA Preparation	65 days	Mon 2/1/21	Fri 4/30/21		
560	SCG - RFA Release	1 day	Fri 5/21/21	Fri 5/21/21		
561	SCG - RFA Abstract Creation Duration	25 days	Mon 5/24/21	Fri 6/25/21		
562	SCG - RFA Evaluation	25 days	Mon 6/28/21	Fri 7/30/21		
563	SCG - RFA Review with EE PRG	1 day	Tue 8/3/21	Tue 8/3/21		
564	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/10/21	Tue 8/10/21		
565	SCG - RFP Preparation	69 days	Tue 6/1/21	Fri 9/3/21		
566	SCG - RFP Release	1 day	Fri 9/17/21	Fri 9/17/21		
567	SCG - RFP Proposal Creation Duration	30 days	Mon 9/20/21	Fri 10/29/21		
568	SCG - RFP Evaluation	25 days	Mon 11/1/21	Fri 12/3/21		
569	SCG - RFP Review with EE PRG	1 day	Tue 12/7/21	Tue 12/7/21		
570	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 12/14/21	Tue 12/14/21		
571	SCG - Contract Negotiation and Development	54 days	Mon 1/17/22	Thu 3/31/22		
572	SCG - Contract Review with EE PRG	9 days	Tue 4/5/22	Fri 4/15/22		
573	SCG - Final Award and Contract Signed	10 days	Mon 4/18/22	Fri 4/29/22		
574	SCG - Submit Advice Letter	21 days	N/A	N/A		
575	SCG - Advice Letter Approved	1 day	N/A	N/A		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone

Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only

External Tasks
External Milestone
Deadline
Progress
Manual Progress

ID	Task Name	Duration	Start	Finish	2018 H1	H2
576	SCG - Implementation Plan	43 days	Sat 4/30/22	Tue 6/28/22		
577	**SCG - Marketplace Solicitation**	**436 days?**	**Mon 3/1/21**	**Mon 10/31/22**		
578	SCG - RFA Preparation	64 days	Sat 5/1/21	Wed 7/28/21		
579	SCG - RFA Release	1 day	Fri 8/20/21	Fri 8/20/21		
580	SCG - RFA Abstract Creation Duration	25 days	Mon 8/23/21	Fri 9/24/21		
581	SCG - RFA Evaluation	25 days	Mon 9/27/21	Fri 10/29/21		
582	SCG - RFA Review with EE PRG	1 day	Tue 11/2/21	Tue 11/2/21		
583	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/9/21	Tue 11/9/21		
584	SCG - RFP Preparation	91 days	Thu 8/26/21	Thu 12/30/21		
585	SCG - RFP Release	1 day	Fri 1/14/22	Fri 1/14/22		
586	SCG - RFP Proposal Creation Duration	30 days	Mon 1/17/22	Fri 2/25/22		
587	SCG - RFP Evaluation	25 days	Mon 2/28/22	Fri 4/1/22		
588	SCG - RFP Review with EE PRG	1 day	Tue 5/3/22	Tue 5/3/22		
589	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 5/11/22	Wed 5/11/22		
590	SCG - Contract Negotiation and Development	117 days	Wed 6/22/22	Thu 12/1/22		
591	SCG - Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22		
592	SCG - Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22		
593	SCG - Submit Advice Letter	20 days	Tue 1/3/23	Mon 1/30/23		
594	SCG - Advice Letter Approved	1 day	Tue 5/2/23	Tue 5/2/23		
595	SCG - Implementation Plan	44 days	Wed 5/3/23	Sun 7/2/23		
596	**SCG - Residential Multi-Family - Whole Building**	**436 days?**	**Mon 3/1/21**	**Mon 10/31/22**		
597	RFA Preparation	40 days	Mon 1/10/22	Fri 3/4/22		
598	RFA Release	1 day	Fri 3/25/22	Fri 3/25/22		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	2018 H1	H2
599	RFA Abstract Creation Duration	25 days	Mon 3/28/22	Fri 4/29/22		
600	RFA Evaluation	25 days	Mon 5/2/22	Fri 6/3/22		
601	RFA Review with EE PRG	1 day	Tue 6/7/22	Tue 6/7/22		
602	RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/14/22	Tue 6/14/22		
603	RFP Preparation	28 days	Sun 5/1/22	Tue 6/7/22		
604	RFP Release	1 day	Fri 6/24/22	Fri 6/24/22		
605	RFP Proposal Creation Duration	52 days	Mon 6/27/22	Tue 9/6/22		
606	RFP Evaluation	11 days	Fri 9/9/22	Fri 9/23/22		
607	RFP Review with EE PRG	1 day	Thu 10/6/22	Thu 10/6/22		
608	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/11/22	Tue 10/11/22		
609	Contract Negotiation and Development	39 days	Tue 10/11/22	Fri 12/2/22		
610	Contract Review with EE PRG	1 day	Tue 12/6/22	Tue 12/6/22		
611	Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22		
612	Submit Advice Letter	22 days	Mon 1/2/23	Tue 1/31/23		
613	Advice Letter Approved	1 day	Fri 3/31/23	Fri 3/31/23		
614	Implementation Plan	43 days	Sat 4/1/23	Tue 5/30/23		
615	~~SCG - Youth Education Outreach Solicitation~~	~~331 days~~	~~Tue 3/1/22~~	~~Tue 6/6/23~~		
616	**SCG - HERS Rater Training Solicitation**	**436 days?**	**Mon 3/1/21**	**Mon 10/31/22**		
617	RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22		
618	RFP Release	1 day	Fri 5/13/22	Fri 5/13/22		
619	RFP Proposal Creation Duration	20 days	Mon 5/16/22	Fri 6/10/22		
620	RFP Evaluation	59 days	Mon 6/13/22	Thu 9/1/22		
621	RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
622	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 8/31/22	Wed 8/31/22		
623	Contract Negotiation and Development	53 days	Fri 9/16/22	Tue 11/29/22		
624	Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22		
625	Final Award and Contract Signed	9 days	Mon 12/19/22	Thu 12/29/22		
626	Submit Advice Letter	N/A	N/A	N/A		
627	Advice Letter Approved	N/A	N/A	N/A		
628	Implementation Plan	42 days	Fri 12/30/22	Mon 2/27/23		
629	**SCG - Retail Partnering Solicitation**	**29 days?**	Tue 9/27/22	Fri 11/4/22		
630	RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22		
631	RFP Release	1 day	Fri 6/17/22	Fri 6/17/22		
632	RFP Proposal Creation Duration	30 days	Mon 6/20/22	Fri 7/29/22		
633	RFP Evaluation	24 days	Mon 8/1/22	Thu 9/1/22		
634	RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22		
635	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/13/22	Tue 9/13/22		
636	Contract Negotiation and Development	29 days	Mon 9/19/22	Thu 10/27/22		
637	Contract Review with EE PRG	9 days	Tue 11/1/22	Fri 11/11/22		
638	Final Award and Contract Signed	13 days	Mon 11/14/22	Wed 11/30/22		
639	Submit Advice Letter	N/A	N/A	N/A		
640	Advice Letter Approved	N/A	N/A	N/A		
641	Implementation Plan	43 days	Sat 10/1/22	Tue 11/29/22		
642	**SCG - Non-Residential EE Advisor Solicitation**	**436 days?**	**Mon 3/1/21**	**Mon 10/31/22**		
643	RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22		
644	RFP Release	1 day	Fri 8/26/22	Fri 8/26/22		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
645	RFP Proposal Creation Duration	20 days	Mon 8/29/22	Fri 9/23/22		
646	RFP Evaluation	16 days	Sat 9/24/22	Fri 10/14/22		
647	RFP Review with EE PRG	5 days	Mon 10/17/22	Fri 10/21/22		
648	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/25/22	Tue 10/25/22		
649	Contract Negotiation and Development	32 days	Sun 10/30/22	Mon 12/12/22		
650	Contract Review with EE PRG	9 days	Tue 12/13/22	Fri 12/23/22		
651	Final Award and Contract Signed	4 days	Tue 12/27/22	Fri 12/30/22		
652	Submit Advice Letter	N/A	N/A	N/A		
653	Advice Letter Approved	N/A	N/A	N/A		
654	Implementation Plan	44 days	Sun 1/1/23	Wed 3/1/23		
655	**SCG - Residential EE Kits Solicitation**	**436 days?**	**Mon 3/1/21**	**Mon 10/31/22**		
656	RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22		
657	RFP Release	1 day	Mon 7/25/22	Mon 7/25/22		
658	RFP Proposal Creation Duration	16 days	Tue 7/26/22	Tue 8/16/22		
659	RFP Evaluation	12 days	Wed 8/17/22	Thu 9/1/22		
660	RFP Review with EE PRG	1 day	Tue 8/2/22	Tue 8/2/22		
661	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/9/22	Tue 8/9/22		
662	Contract Negotiation and Development	30 days	Mon 8/22/22	Fri 9/30/22		
663	Contract Review with EE PRG	9 days	Tue 10/4/22	Fri 10/14/22		
664	Final Award and Contract Signed	10 days	Mon 10/17/22	Fri 10/28/22		
665	Submit Advice Letter	N/A	N/A	N/A		
666	Advice Letter Approved	N/A	N/A	N/A		
667	Implementation Plan	43 days	Sat 10/29/22	Tue 12/27/22		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
668	**SCG - IDEEA 365**	**230 days**	**Mon 2/13/23**	**Fri 12/29/23**		
669	RFP Preparation	23 days	Mon 2/13/23	Wed 3/15/23		
670	RFP Release	20 days	Thu 4/20/23	Wed 5/17/23		
671	RFP Proposal Creation Duration	43 days	Wed 5/3/23	Fri 6/30/23		
672	RFP Evaluation	12 days	Fri 7/14/23	Mon 7/31/23		
673	RFP Review with EE PRG	1 day	Tue 8/1/23	Tue 8/1/23		
674	RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Tue 8/1/23	Thu 8/31/23		
675	Contract Negotiation and Development	21 days	Fri 9/1/23	Fri 9/29/23		
676	Contract Review with EE PRG	32 days	Mon 9/18/23	Tue 10/31/23		
677	Final Award and Contract Signed	17 days	Mon 10/9/23	Tue 10/31/23		
678	Submit Advice Letter	10 days	Wed 11/1/23	Tue 11/14/23		
679	Advice Letter Approved	11 days	Wed 11/22/23	Wed 12/6/23		
680	Implementation Plan	9 days	Tue 12/19/23	Fri 12/29/23		
681	**SCG - Commercial SEM**	**110 days?**	**Tue 8/1/23**	**Mon 1/1/24**		
682	RFP Preparation	22 days	Tue 8/1/23	Wed 8/30/23		
683	RFP Release	13 days	Wed 9/13/23	Fri 9/29/23		
684	RFP Proposal Creation Duration	11 days	Mon 10/2/23	Mon 10/16/23		
685	RFP Evaluation	5 days	Wed 10/25/23	Tue 10/31/23		
686	RFP Review with EE PRG	2 days	Tue 10/31/23	Wed 11/1/23		
687	RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Thu 11/2/23	Wed 11/8/23		
688	Contract Negotiation and Development	16 days	Wed 10/25/23	Wed 11/15/23		
689	Contract Review with EE PRG	1 day	Tue 12/5/23	Tue 12/5/23		
690	Final Award and Contract Signed	6 days	Wed 12/13/23	Wed 12/20/23		

Project: IOU Master Task Timeli
Date: Mon 11/2/26


Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
691	Submit Advice Letter	5 days	Mon 12/18/23	Fri 12/22/23		
692	Advice Letter Approved	1 day	Fri 12/29/23	Fri 12/29/23		
693	Implementation Plan	1 day	Mon 1/1/24	Mon 1/1/24		
694	**SCG - Market Access Program**	**333 days?**	**Sat 3/16/24**	**Tue 6/24/25**		
695	RFP Preparation	75 days	Sat 3/16/24	Thu 6/27/24		
696	RFP Release	1 day	Fri 6/21/24	Fri 6/21/24		
697	RFP Proposal Creation Duration	53 days	Mon 6/24/24	Wed 9/4/24		
698	RFP Evaluation	38 days	Mon 8/19/24	Wed 10/9/24		
699	RFP Review with EE PRG	1 day	Tue 10/1/24	Tue 10/1/24		
700	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/8/24	Tue 10/8/24		
701	Contract Negotiation and Development	78 days	Mon 10/14/24	Wed 1/29/25		
702	Contract Review with EE PRG	10 days	Tue 1/7/25	Mon 1/20/25		
703	Final Award and Contract Signed	11 days	Mon 1/20/25	Mon 2/3/25		
704	Submit Advice Letter	N/A	Wed 1/1/25			
705	Advice Letter Approved	N/A	Mon 3/3/25			
706	Implementation Plan	59 days	Thu 4/3/25	Tue 6/24/25		
707	**SCG - IDEEA 365 (Round 3)**	**230 days?**	**Tue 10/15/24**	**Mon 9/1/25**		
708	RFP Preparation	23 days	Tue 10/15/24	Thu 11/14/24		
709	RFP Release	20 days	Fri 11/15/24	Thu 12/12/24		
710	RFP Proposal Creation Duration	43 days	Fri 12/13/24	Tue 2/11/25		
711	RFP Evaluation	12 days	Wed 2/12/25	Thu 2/27/25		
712	RFP Review with EE PRG	1 day	Fri 2/28/25	Fri 2/28/25		
713	RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Mon 3/3/25	Wed 4/2/25		


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


ID	Task Name	Duration	Start	Finish
714	Contract Negotiation and Development	21 days	Thu 4/3/25	Thu 5/1/25
715	Contract Review with EE PRG	32 days	Fri 5/2/25	Mon 6/16/25
716	Final Award and Contract Signed	17 days	Tue 6/17/25	Wed 7/9/25
717	Submit Advice Letter	10 days	Thu 7/10/25	Wed 7/23/25
718	Advice Letter Approved	11 days	Thu 7/24/25	Thu 8/7/25
719	Implementation Plan	9 days	Fri 8/8/25	Wed 8/20/25
720				
721	***Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change***			
722	**SDG&E - Small Commercial (<20kW) Solicitation**	**612 days**	**Wed 8/1/18**	**Thu 12/3/20**
723	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18
724	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18
725	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18
726	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19
727	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19
728	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19
729	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19
730	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19
731	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19
732	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19
733	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20
734	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20
735	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20
736	SDG&E - Contract Review with EE PRG	0 days	Tue 6/9/20	Tue 6/9/20



ID	Task Name	Duration	Start	Finish
737	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20
738	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20
739	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20
740	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20
741	**SDG&E - Large Commercial (>20kW) Solicitation**	**612 days**	**Wed 8/1/18**	**Thu 12/3/20**
742	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18
743	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18
744	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18
745	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19
746	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19
747	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19
748	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19
749	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19
750	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19
751	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19
752	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20
753	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20
754	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20
755	SDG&E - Contract Review with EE PRG	0 days	Tue 5/12/20	Tue 5/12/20
756	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20
757	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20
758	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20
759	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20



ID	Task Name	Duration	Start	Finish
760	**SDG&E - Residential Multi-Family Solicitation**	**586 days**	**Thu 9/6/18**	**Thu 12/3/20**
761	SDG&E - RFA Preparation	64 days	Thu 9/6/18	Tue 12/4/18
762	SDG&E - RFA Release	23 days	Tue 12/4/18	Thu 1/3/19
763	SDG&E - RFA Abstract Creation Duration	49 days	Tue 9/11/18	Fri 11/16/18
764	SDG&E - RFA Evaluation	21 days	Mon 1/7/19	Mon 2/4/19
765	SDG&E - RFA Review with EE PRG	0 days	Tue 11/13/18	Tue 11/13/18
766	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 3/20/19	Wed 3/20/19
767	SDG&E - RFP Preparation	63 days	Fri 3/22/19	Tue 6/18/19
768	SDG&E - RFP Release	52 days	Tue 6/18/19	Wed 8/28/19
769	SDG&E - RFP Proposal Creation Duration	36 days	Mon 3/25/19	Mon 5/13/19
770	SDG&E - RFP Evaluation	30 days	Thu 8/29/19	Wed 10/9/19
771	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Thu 12/12/19	Thu 12/19/19
772	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20
773	SDG&E - Contract Negotiation and Development	35 days	Mon 4/13/20	Fri 5/29/20
774	SDG&E - Contract Review with EE PRG	10 days	Thu 6/4/20	Wed 6/17/20
775	SDG&E - Final Award and Contract Signed	0 days	Mon 6/22/20	Mon 6/22/20
776	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20
777	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20
778	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20
779	**SDG&E - SW HVAC Solicitation**	**593 days**	**Thu 11/1/18**	**Tue 2/9/21**
780	SDG&E - RFA Preparation	48 days	Thu 11/1/18	Mon 1/7/19
781	SDG&E - RFA Release	0 days	Mon 1/7/19	Mon 1/7/19
782	SDG&E - RFA Abstract Creation Duration	24 days	Mon 1/7/19	Thu 2/7/19




ID	Task Name	Duration	Start	Finish	2018 H1	H2
783	SDG&E - RFA Evaluation	37 days	Fri 2/8/19	Sun 3/31/19		
784	SDG&E - RFA Review with EE PRG	0 days	Tue 4/9/19	Tue 4/9/19		
785	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 4/17/19	Wed 4/17/19		
786	SDG&E - RFP Preparation	73 days	Thu 4/18/19	Mon 7/29/19		
787	SDG&E - RFP Release	0 days	Tue 9/3/19	Tue 9/3/19		
788	SDG&E - RFP Proposal Creation Duration	30 days	Tue 9/3/19	Mon 10/14/19		
789	SDG&E - RFP Evaluation	33 days	Mon 10/14/19	Wed 11/27/19		
790	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20		
791	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
792	SDG&E - Contract Negotiation and Development	88 days	Wed 3/25/20	Fri 7/24/20		
793	SDG&E - Contract Review with EE PRG	0 days	Tue 9/8/20	Tue 9/8/20		
794	SDG&E - Final Award and Contract Signed	0 days	Fri 10/30/20	Fri 10/30/20		
795	SDG&E - Submit Advice Letter	0 days	Thu 11/12/20	Thu 11/12/20		
796	SDG&E - Advice Letter Approved	0 days	Fri 12/11/20	Fri 12/11/20		
797	SDG&E - Implementation Plan	0 days	Tue 2/9/21	Tue 2/9/21		
798	**SDG&E - SW PLA Solicitation**	**853 days**	**Mon 1/28/19**	**Wed 5/4/22**		
799	SDG&E - RFA Preparation	75 days	Mon 1/28/19	Fri 5/10/19		
800	SDG&E - RFA Release	0 days	Fri 5/10/19	Fri 5/10/19		
801	SDG&E - RFA Abstract Creation Duration	31 days	Fri 5/10/19	Fri 6/21/19		
802	SDG&E - RFA Evaluation	65 days	Mon 6/24/19	Fri 9/20/19		
803	SDG&E - RFA Review with EE PRG	0 days	Tue 9/10/19	Tue 9/10/19		
804	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 9/20/19	Fri 9/20/19		
805	SDG&E - RFP Preparation	52 days	Fri 9/20/19	Mon 12/2/19		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


ID	Task Name	Duration	Start	Finish	2018 H1	H2
806	SDG&E - RFP Release	0 days	Mon 1/27/20	Mon 1/27/20		
807	SDG&E - RFP Proposal Creation Duration	31 days	Mon 1/27/20	Mon 3/9/20		
808	SDG&E - RFP Evaluation	82 days	Mon 3/9/20	Tue 6/30/20		
809	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/17/20	Mon 8/17/20		
810	SDG&E - Selection Review with EE PRG	66 days	Tue 10/13/20	Tue 1/12/21		
811	SDG&E - Contract Negotiation and Development	197 days	Fri 1/29/21	Mon 11/1/21		
812	SDG&E - Contract Review with EE PRG	0 days	Tue 11/9/21	Tue 11/9/21		
813	SDG&E - Final Award and Contract Signed	0 days	Fri 1/7/22	Fri 1/7/22		
814	SDG&E - Submit Advice Letter	0 days	Mon 1/10/22	Mon 1/10/22		
815	SDG&E - Advice Letter Approved	0 days	Thu 2/10/22	Thu 2/10/22		
816	SDG&E - Implementation Plan	60 days	Thu 2/10/22	Wed 5/4/22		
817	**SDG&E - Residential Single-Family 2.0 Solicitation**	**467 days**	**Tue 1/19/21**	**Wed 11/2/22**		
818	SDG&E - RFA Preparation	43 days	Tue 1/19/21	Thu 3/18/21		
819	SDG&E - RFA Release	0 days	Mon 3/22/21	Mon 3/22/21		
820	SDG&E - RFA Abstract Creation Duration	22 days	Mon 3/22/21	Tue 4/20/21		
821	SDG&E - RFA Evaluation	38 days	Wed 4/21/21	Fri 6/11/21		
822	SDG&E - RFA Review with EE PRG	7 days	Thu 6/3/21	Fri 6/11/21		
823	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 6/15/21	Tue 6/15/21		
824	SDG&E - RFP Preparation	43 days	Wed 6/16/21	Fri 8/13/21		
825	SDG&E - RFP Release	0 days	Wed 8/18/21	Wed 8/18/21		
826	SDG&E - RFP Proposal Creation Duration	32 days	Wed 8/18/21	Thu 9/30/21		
827	SDG&E - RFP Evaluation	44 days	Fri 10/1/21	Wed 12/1/21		
828	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 12/14/21	Tue 12/14/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26




ID	Task Name	Duration	Start	Finish	2018 H1	H2
829	SDG&E - Selection Review with EE PRG	7 days	Thu 12/2/21	Fri 12/10/21		
830	SDG&E - Contract Negotiation and Development	96 days	Mon 12/20/21	Mon 5/2/22		
831	SDG&E - Contract Review with EE PRG	7 days	Thu 5/5/22	Fri 5/13/22		
832	SDG&E - Final Award and Contract Signed	0 days	Tue 5/31/22	Tue 5/31/22		
833	SDG&E - Submit Advice Letter	0 days	Fri 6/24/22	Fri 6/24/22		
834	SDG&E - Advice Letter Approved	0 days	Thu 8/11/22	Thu 8/11/22		
835	SDG&E - Implementation Plan	60 days	Thu 8/11/22	Wed 11/2/22		
836	**SDG&E - Residential Single-Family Solicitation**	**501 days**	**Mon 7/1/19**	**Tue 6/1/21**		
837	SDG&E - RFA Preparation	80 days	Mon 7/1/19	Fri 10/18/19		
838	SDG&E - RFA Release	35 days	Fri 10/18/19	Thu 12/5/19		
839	SDG&E - RFA Abstract Creation Duration	53 days	Mon 7/22/19	Wed 10/2/19		
840	SDG&E - RFA Evaluation	29 days	Fri 12/6/19	Wed 1/15/20		
841	SDG&E - RFA Review with EE PRG	0 days	Tue 10/8/19	Tue 10/8/19		
842	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 2/27/20	Thu 2/27/20		
843	SDG&E - RFP Preparation	48 days	Fri 2/28/20	Tue 5/5/20		
844	SDG&E - RFP Release	0 days	Mon 4/27/20	Mon 4/27/20		
845	SDG&E - RFP Proposal Creation Duration	32 days	Mon 4/27/20	Tue 6/9/20		
846	SDG&E - RFP Evaluation	16 days	Wed 6/10/20	Wed 7/1/20		
847	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 7/23/20	Fri 7/24/20		
848	SDG&E - Selection Review with EE PRG	7 days	Thu 8/6/20	Fri 8/14/20		
849	SDG&E - Contract Negotiation and Development	60 days	Mon 8/17/20	Fri 11/6/20		
850	SDG&E - Contract Review with EE PRG	10 days	Tue 12/8/20	Mon 12/21/20		
851	SDG&E - Final Award and Contract Signed	0 days	Fri 1/29/21	Fri 1/29/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26



ID	Task Name	Duration	Start	Finish	2018 H1	H2
852	SDG&E - Submit Advice Letter	0 days	Mon 3/1/21	Mon 3/1/21		
853	SDG&E - Advice Letter Approved					
854	SDG&E - Implementation Plan	0 days	Tue 6/1/21	Tue 6/1/21		
855	**SDG&E - Public Sector: Federal Solicitation**	**625 days**	**Mon 7/1/19**	**Fri 11/19/21**		
856	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19		
857	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19		
858	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19		
859	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20		
860	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
861	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20		
862	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20		
863	SDG&E - RFP Release	0 days	Fri 5/22/20	Fri 5/22/20		
864	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20		
865	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20		
866	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20		
867	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20		
868	SDG&E - Contract Negotiation and Development	53 days	Wed 2/17/21	Fri 4/30/21		
869	SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21		
870	SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21		
871	SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21		
872	SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21		
873	SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21		
874	**SDG&E - Public Sector: K-12 Solicitation**	**625 days**	**Mon 7/1/19**	**Fri 11/19/21**		

Project: IOU Master Task Timeli
Date: Mon 11/2/26




ID	Task Name	Duration	Start	Finish	2018 H1	H2
875	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19		
876	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19		
877	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19		
878	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20		
879	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
880	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20		
881	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20		
882	SDG&E - RFP Release	1 day	Fri 5/22/20	Fri 5/22/20		
883	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20		
884	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20		
885	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20		
886	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20		
887	SDG&E - Contract Negotiation and Development	117 days	Thu 11/19/20	Fri 4/30/21		
888	SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21		
889	SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21		
890	SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21		
891	SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21		
892	SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21		
893	**SDG&E - Public Sector: Local Government Solicitation**	**338 days**	Tue 10/13/20	**Thu 1/27/22**		
894	SDG&E - RFA Preparation	10 days	Fri 10/23/20	Thu 11/5/20		
895	SDG&E - RFA Release	1 day	Wed 1/27/21	Wed 1/27/21		
896	SDG&E - RFA Abstract Creation Duration	20 days	Thu 1/28/21	Wed 2/24/21		
897	SDG&E - RFA Evaluation	18 days	Fri 2/26/21	Tue 3/23/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


ID	Task Name	Duration	Start	Finish	2018 H1	H2
898	SDG&E - RFA Review with EE PRG	7 days	Thu 4/8/21	Fri 4/16/21		
899	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/21/21	Wed 4/21/21		
900	SDG&E - RFP Preparation	51 days	Fri 3/19/21	Fri 5/28/21		
901	SDG&E - RFP Release	1 day	Tue 6/1/21	Tue 6/1/21		
902	SDG&E - RFP Proposal Creation Duration	26 days	Wed 6/2/21	Wed 7/7/21		
903	SDG&E - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21		
904	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/25/21	Mon 10/25/21		
905	SDG&E - Selection Review with EE PRG	7 days	Tue 10/12/21	Wed 10/20/21		
906	SDG&E - Contract Negotiation and Development	41 days	Fri 11/5/21	Fri 12/31/21		
907	SDG&E - Contract Review with EE PRG	7 days	Thu 1/6/22	Fri 1/14/22		
908	SDG&E - Final Award and Contract Signed	9 days	Mon 1/17/22	Thu 1/27/22		
909	SDG&E - Submit Advice Letter	13 days	Wed 6/1/22	Fri 6/17/22		
910	SDG&E - Advice Letter Approved	40 days	Fri 6/17/22	Thu 8/11/22		
911	SDG&E - Implementation Plan	42 days	Mon 8/15/22	Tue 10/11/22		
912	**SDG&E - Agricultural Sector: Local Agriculture Solicitation**	**447 days**	**Mon 3/1/21**	**Tue 11/15/22**		
913	SDG&E - RFA Preparation	56 days	Mon 3/1/21	Mon 5/17/21		
914	SDG&E - RFA Release	0 days	Mon 4/26/21	Mon 4/26/21		
915	SDG&E - RFA Abstract Creation Duration	20 days	Tue 4/27/21	Mon 5/24/21		
916	SDG&E - RFA Evaluation	36 days	Tue 6/1/21	Tue 7/20/21		
917	SDG&E - RFA Review with EE PRG	0 days	Thu 7/8/21	Thu 7/8/21		
918	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 7/20/21	Tue 7/20/21		
919	SDG&E - RFP Preparation	48 days	Tue 7/20/21	Thu 9/23/21		
920	SDG&E - RFP Release	0 days	Thu 9/23/21	Thu 9/23/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26




ID	Task Name	Duration	Start	Finish	2018 H1	H2
921	SDG&E - RFP Proposal Creation Duration	25 days	Fri 9/24/21	Thu 10/28/21		
922	SDG&E - RFP Evaluation	23 days	Thu 10/28/21	Mon 11/29/21		
923	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 2/1/22	Tue 2/1/22		
924	SDG&E - Selection Review with EE PRG	0 days	Tue 2/8/22	Tue 2/8/22		
925	SDG&E - Contract Negotiation and Development	83 days	Tue 2/1/22	Thu 5/26/22		
926	SDG&E - Contract Review with EE PRG	0 days	Tue 6/14/22	Tue 6/14/22		
927	SDG&E - Final Award and Contract Signed	10 days	Fri 6/18/21	Thu 7/1/21		
928	SDG&E - Submit Advice Letter	0 days	Fri 7/22/22	Fri 7/22/22		
929	SDG&E - Advice Letter Approved	0 days	Tue 8/30/22	Tue 8/30/22		
930	SDG&E - Implementation Plan	44 days	Wed 8/31/22	Sat 10/29/22		
931	***SDG&E - Industrial Solicitation**	**426 days**	**Thu 4/1/21**	**Thu 11/17/22**		
932	SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21		
933	SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21		
934	SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21		
935	SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21		
936	SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21		
937	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21		
938	SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21		
939	SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21		
940	SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22		
941	SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22		
942	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22		
943	SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22		

Project: IOU Master Task Timeli
Date: Mon 11/2/26




ID	Task Name	Duration	Start	Finish	2018 H1	H2
944	SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22		
945	SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22		
946	SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22		
947	SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22		
948	SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22		
949	SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23		
950	***SDG&E - Industrial-Port Tenants Solicitation**	**426 days**	**Thu 4/1/21**	**Thu 11/17/22**		
951	SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21		
952	SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21		
953	SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21		
954	SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21		
955	SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21		
956	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21		
957	SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21		
958	SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21		
959	SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22		
960	SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22		
961	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22		
962	SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22		
963	SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22		
964	SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22		
965	SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22		
966	SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22		

Project: IOU Master Task Timeli
Date: Mon 11/2/26



ID	Task Name	Duration	Start	Finish	2018 H1	H2
967	SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22		
968	SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23		
969	***SDG&E - SW Residential HVAC QI/QM Solicitation**	**377 days**	**Mon 7/5/21**	**Tue 12/13/22**		
970	SDG&E - RFA Preparation	48 days	Mon 7/5/21	Wed 9/8/21		
971	SDG&E - RFA Release	1 day	Wed 9/29/21	Wed 9/29/21		
972	SDG&E - RFA Abstract Creation Duration	22 days	Wed 9/29/21	Thu 10/28/21		
973	SDG&E - RFA Evaluation	21 days	Fri 10/29/21	Fri 11/26/21		
974	SDG&E - RFA Review with EE PRG	6 days	Fri 12/10/21	Fri 12/17/21		
975	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 12/22/21	Wed 12/22/21		
976	SDG&E - RFP Preparation	56 days	Tue 1/4/22	Tue 3/22/22		
977	SDG&E - RFP Release	1 day	Tue 3/22/22	Tue 3/22/22		
978	SDG&E - RFP Proposal Creation Duration	23 days	Wed 3/23/22	Fri 4/22/22		
979	SDG&E - RFP Evaluation	20 days	Mon 4/25/22	Fri 5/20/22		
980	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/21/22	Tue 6/21/22		
981	SDG&E - Selection Review with EE PRG	0 days	Fri 6/17/22	Fri 6/17/22		
982	SDG&E - Contract Negotiation and Development	83 days	Wed 7/20/22	Fri 11/11/22		
983	SDG&E - Contract Review with EE PRG	6 days	Mon 11/14/22	Mon 11/21/22		
984	SDG&E - Final Award and Contract Signed	1 day	Mon 1/10/22	Mon 1/10/22		
985	SDG&E - Submit Advice Letter	22 days	Sun 1/15/23	Mon 2/13/23		
986	SDG&E - Advice Letter Approved	1 day	Fri 4/28/23	Fri 4/28/23		
987	SDG&E - Implementation Plan	60 days	Fri 4/28/23	Thu 7/20/23		
988	***SDG&E - Local/Residential Behavioral Solicitation**	**472 days**	**Mon 4/19/21**	**Tue 2/7/23**		
989	SDG&E - RFA Preparation	53 days	Mon 4/19/21	Wed 6/30/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26



ID	Task Name	Duration	Start	Finish	2018 H1	H2
990	SDG&E - RFA Release	1 day	Mon 7/26/21	Mon 7/26/21		
991	SDG&E - RFA Abstract Creation Duration	21 days	Mon 7/26/21	Mon 8/23/21		
992	SDG&E - RFA Evaluation	30 days	Tue 8/24/21	Mon 10/4/21		
993	SDG&E - RFA Review with EE PRG	7 days	Thu 10/7/21	Fri 10/15/21		
994	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/19/21	Tue 10/19/21		
995	SDG&E - RFP Preparation	28 days	Thu 10/21/21	Mon 11/29/21		
996	SDG&E - RFP Release	1 day	Wed 12/22/21	Wed 12/22/21		
997	SDG&E - RFP Proposal Creation Duration	20 days	Wed 12/22/21	Tue 1/18/22		
998	SDG&E - RFP Evaluation	28 days	Wed 1/19/22	Fri 2/25/22		
999	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/15/22	Tue 3/15/22		
1000	SDG&E - Selection Review with EE PRG	7 days	Thu 3/3/22	Fri 3/11/22		
1001	SDG&E - Contract Negotiation and Development	119 days	Fri 3/18/22	Wed 8/31/22		
1002	SDG&E - Contract Review with EE PRG	7 days	Thu 9/8/22	Fri 9/16/22		
1003	SDG&E - Final Award and Contract Signed	1 day	Fri 10/21/22	Fri 10/21/22		
1004	SDG&E - Submit Advice Letter	1 day	Wed 11/16/22	Wed 11/16/22		
1005	SDG&E - Advice Letter Approved	1 day	Fri 12/16/22	Fri 12/16/22		
1006	SDG&E - Implementation Plan	60 days	Wed 11/16/22	Tue 2/7/23		
1007	***SDG&E - Small Business Outreach Solicitation**	**298 days?**	**Wed 4/13/22**	**Fri 6/2/23**		
1008	SDG&E - RFA Preparation	53 days	Wed 4/13/22	Fri 6/24/22		
1009	SDG&E - RFA Release	1 day	Thu 7/7/22	Thu 7/7/22		
1010	SDG&E - RFA Abstract Creation Duration	21 days	Fri 7/8/22	Fri 8/5/22		
1011	SDG&E - RFA Evaluation	30 days	Mon 8/8/22	Fri 9/16/22		
1012	SDG&E - RFA Review with EE PRG	5 days	Mon 9/19/22	Fri 9/23/22		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


ID	Task Name	Duration	Start	Finish	2018 H1	H2
1013	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/27/22	Tue 9/27/22		
1014	SDG&E - RFP Preparation	28 days	Mon 8/8/22	Wed 9/14/22		
1015	SDG&E - RFP Release	1 day	Tue 10/18/22	Tue 10/18/22		
1016	SDG&E - RFP Proposal Creation Duration	31 days	Tue 10/18/22	Tue 11/29/22		
1017	SDG&E - RFP Evaluation	38 days	Wed 11/30/22	Fri 1/20/23		
1018	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/28/23	Tue 2/28/23		
1019	SDG&E - Selection Review with EE PRG	7 days	Thu 2/16/23	Fri 2/24/23		
1020	SDG&E - Contract Negotiation and Development	79 days	Tue 2/28/23	Fri 6/16/23		
1021	SDG&E - Contract Review with EE PRG	4 days	Wed 6/21/23	Mon 6/26/23		
1022	SDG&E - Final Award and Contract Signed	1 day	Tue 8/29/23	Tue 8/29/23		
1023	SDG&E - Submit Advice Letter	1 day	Fri 9/15/23	Fri 9/15/23		
1024	SDG&E - Advice Letter Approved	1 day	Mon 10/16/23	Mon 10/16/23		
1025	SDG&E - Implementation Plan	46 days	Mon 10/16/23	Mon 12/18/23		
1026	***SDG&E - Workforce Education & Training /Integrated Energy Education Solicitatic**	**353 days?**	**Mon 1/16/23**	**Wed 5/22/24**		
1027	SDG&E - RFP Release	1 day?	Thu 2/2/23	Thu 2/2/23		
1028	SDG&E - RFP Evaluation	25 days	Fri 3/17/23	Thu 4/20/23		
1029	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/16/23	Tue 5/16/23		
1030	SDG&E - Selection Review with EE PRG	5 days	Tue 5/9/23	Mon 5/15/23		
1031	SDG&E - Contract Negotiation and Development	94 days	Fri 5/5/23	Wed 9/13/23		
1032	SDG&E - Contract Review with EE PRG	7 days	Tue 10/10/23	Wed 10/18/23		
1033	SDG&E - Final Award and Contract Signed	1 day	Tue 11/14/23	Tue 11/14/23		
1034	SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24		
1035	SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


ID	Task Name	Duration	Start	Finish	2018 H1	H2
1036	SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24		
1037	***SDG&E - Residential Equity Education & Outreach Solicitation**	**331 days?**	**Fri 1/13/23**	**Fri 4/19/24**		
1038	SDG&E - RFA Release	1 day	Thu 3/2/23	Thu 3/2/23		
1039	SDG&E - RFA Evaluation	21 days	Wed 4/12/23	Wed 5/10/23		
1040	SDG&E - RFA Review with EE PRG	7 days	Fri 5/19/23	Mon 5/29/23		
1041	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/30/23	Tue 5/30/23		
1042	SDG&E - RFP Release	1 day	Thu 6/1/23	Thu 6/1/23		
1043	SDG&E - RFP Evaluation	27 days	Mon 7/17/23	Tue 8/22/23		
1044	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/28/23	Mon 8/28/23		
1045	SDG&E - Selection Review with EE PRG	7 days	Wed 8/30/23	Thu 9/7/23		
1046	SDG&E - Contract Negotiation and Development	32 days	Thu 11/2/23	Fri 12/15/23		
1047	SDG&E - Contract Review with EE PRG	7 days	Tue 1/9/24	Wed 1/17/24		
1048	SDG&E - Final Award and Contract Signed	1 day	Mon 2/12/24	Mon 2/12/24		
1049	SDG&E - Submit Advice Letter	1 day	Mon 2/26/24	Mon 2/26/24		
1050	SDG&E - Advice Letter Approved	1 day	Mon 4/8/24	Mon 4/8/24		
1051	SDG&E - Implementation Plan	60 days	Tue 4/9/24	Mon 7/1/24		
1052	***SDG&E - Non-Residential Behavioral Solicitation**	**398 days**	**Mon 8/15/22**	**Wed 2/21/24**		
1053	SDG&E - RFA Preparation	67 days	Mon 8/15/22	Tue 11/15/22		
1054	SDG&E - RFA Release	1 day	Mon 10/24/22	Mon 10/24/22		
1055	SDG&E - RFA Abstract Creation Duration	27 days	Tue 8/23/22	Wed 9/28/22		
1056	SDG&E - RFA Evaluation	16 days	Tue 11/29/22	Tue 12/20/22		
1057	SDG&E - RFA Review with EE PRG	7 days	Thu 1/5/23	Fri 1/13/23		
1058	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 1/18/23	Wed 1/18/23		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

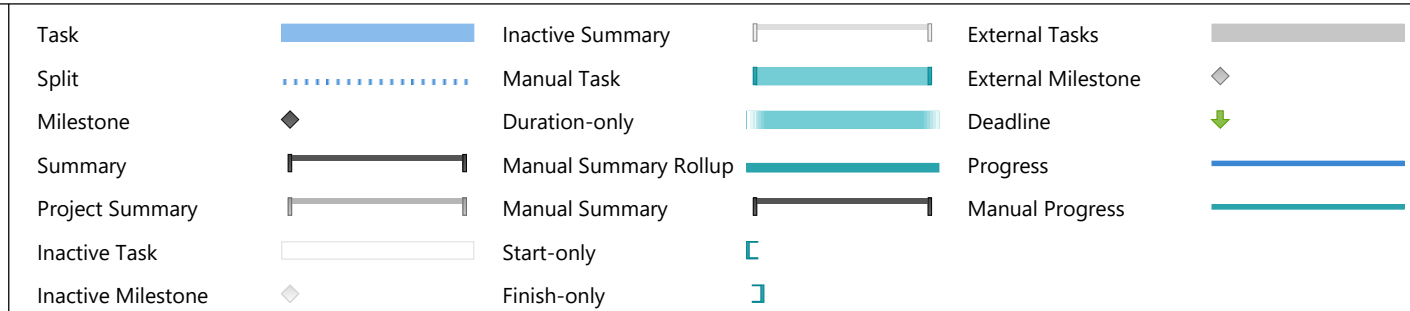

ID	Task Name	Duration	Start	Finish	2018 H1	H2
1059	SDG&E - RFP Preparation	26 days	Mon 11/14/22	Mon 12/19/22		
1060	SDG&E - RFP Release	1 day	Mon 1/23/23	Mon 1/23/23		
1061	SDG&E - RFP Proposal Creation Duration	26 days	Mon 1/23/23	Mon 2/27/23		
1062	SDG&E - RFP Evaluation	58 days	Tue 2/28/23	Thu 5/18/23		
1063	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/20/23	Tue 6/20/23		
1064	SDG&E - Selection Review with EE PRG	7 days	Thu 6/8/23	Fri 6/16/23		
1065	SDG&E - Contract Negotiation and Development	60 days	Wed 6/21/23	Tue 9/12/23		
1066	SDG&E - Contract Review with EE PRG	7 days	Thu 10/5/23	Fri 10/13/23		
1067	SDG&E - Final Award and Contract Signed	1 day	Thu 12/21/23	Thu 12/21/23		
1068	SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24		
1069	SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24		
1070	SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24		
1071	***SDG&E - Retail Offices and Wholesale Solicitation**	**419 days**	**Wed 5/10/23**	**Mon 12/16/24**		
1072	SDG&E - RFA Preparation	33 days	Wed 5/10/23	Fri 6/23/23		
1073	SDG&E - RFA Release	1 day	Mon 7/3/23	Mon 7/3/23		
1074	SDG&E - RFA Abstract Creation Duration	31 days	Tue 7/4/23	Tue 8/15/23		
1075	SDG&E - RFA Evaluation	19 days	Wed 8/16/23	Mon 9/11/23		
1076	SDG&E - RFA Review with EE PRG	3 days	Mon 9/18/23	Wed 9/20/23		
1077	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 9/25/23	Mon 9/25/23		
1078	SDG&E - RFP Preparation	33 days	Wed 7/5/23	Fri 8/18/23		
1079	SDG&E - RFP Release	1 day	Fri 9/29/23	Fri 9/29/23		
1080	SDG&E - RFP Proposal Creation Duration	33 days	Mon 10/2/23	Wed 11/15/23		
1081	SDG&E - RFP Evaluation	25 days	Thu 11/16/23	Wed 12/20/23		

Project: IOU Master Task Timeli
Date: Mon 11/2/26



ID	Task Name	Duration	Start	Finish	2018 H1	H2
1082	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 2/19/24	Mon 2/19/24		
1083	SDG&E - Selection Review with EE PRG	7 days	Thu 2/8/24	Fri 2/16/24		
1084	SDG&E - Contract Negotiation and Development	96 days	Mon 2/26/24	Mon 7/8/24		
1085	SDG&E - Contract Review with EE PRG	6 days	Wed 7/17/24	Wed 7/24/24		
1086	SDG&E - Final Award and Contract Signed	1 day	Tue 8/27/24	Tue 8/27/24		
1087	SDG&E - Submit Advice Letter	1 day	Mon 9/16/24	Mon 9/16/24		
1088	SDG&E - Advice Letter Approved	1 day	Wed 10/16/24	Wed 10/16/24		
1089	SDG&E - Implementation Plan	44 days	Wed 10/16/24	Mon 12/16/24		
1090	***SDG&E - Groceries, Restaurants and Food Storage Solicitation**	**467 days**	**Wed 6/14/23**	**Thu 3/27/25**		
1091	SDG&E - RFA Preparation	33 days	Wed 6/14/23	Fri 7/28/23		
1092	SDG&E - RFA Release	1 day	Tue 8/15/23	Tue 8/15/23		
1093	SDG&E - RFA Abstract Creation Duration	21 days	Wed 8/16/23	Wed 9/13/23		
1094	SDG&E - RFA Evaluation	15 days	Thu 9/14/23	Wed 10/4/23		
1095	SDG&E - RFA Review with EE PRG	5 days	Wed 10/18/23	Tue 10/24/23		
1096	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/30/23	Mon 10/30/23		
1097	SDG&E - RFP Preparation	16 days	Mon 10/9/23	Mon 10/30/23		
1098	SDG&E - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23		
1099	SDG&E - RFP Proposal Creation Duration	40 days	Mon 11/6/23	Fri 12/29/23		
1100	SDG&E - RFP Evaluation	34 days	Fri 12/29/23	Wed 2/14/24		
1101	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 3/6/24	Wed 3/6/24		
1102	SDG&E - Selection Review with EE PRG	7 days	Thu 2/29/24	Fri 3/8/24		
1103	SDG&E - Contract Negotiation and Development	144 days	Wed 3/13/24	Mon 9/30/24		
1104	SDG&E - Contract Review with EE PRG	6 days	Tue 10/8/24	Tue 10/15/24		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
1105	SDG&E - Final Award and Contract Signed	1 day	Tue 11/26/24	Tue 11/26/24		
1106	SDG&E - Submit Advice Letter	1 day	Fri 12/27/24	Fri 12/27/24		
1107	SDG&E - Advice Letter Approved	1 day	Mon 1/27/25	Mon 1/27/25		
1108	SDG&E - Implementation Plan	44 days	Mon 1/27/25	Thu 3/27/25		
1109	***SDG&E - Private Institutions and Healthcare Solicitation**	**399 days**	**Thu 10/5/23**	**Tue 4/15/25**		
1110	SDG&E - RFA Preparation	33 days	Thu 10/5/23	Mon 11/20/23		
1111	SDG&E - RFA Release	1 day	Mon 11/27/23	Mon 11/27/23		
1112	SDG&E - RFA Abstract Creation Duration	35 days	Mon 11/27/23	Fri 1/12/24		
1113	SDG&E - RFA Evaluation	30 days	Mon 1/15/24	Fri 2/23/24		
1114	SDG&E - RFA Review with EE PRG	5 days	Mon 2/26/24	Fri 3/1/24		
1115	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 3/4/24	Mon 3/4/24		
1116	SDG&E - RFP Preparation	54 days	Mon 11/27/23	Thu 2/8/24		
1117	SDG&E - RFP Release	1 day	Fri 3/8/24	Fri 3/8/24		
1118	SDG&E - RFP Proposal Creation Duration	34 days	Fri 3/8/24	Wed 4/24/24		
1119	SDG&E - RFP Evaluation	42 days	Thu 4/25/24	Fri 6/21/24		
1120	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 7/2/24	Tue 7/2/24		
1121	SDG&E - Selection Review with EE PRG	7 days	Fri 6/21/24	Mon 7/1/24		
1122	SDG&E - Contract Negotiation and Development	61 days	Wed 7/31/24	Wed 10/23/24		
1123	SDG&E - Contract Review with EE PRG	4 days	Tue 11/12/24	Fri 11/15/24		
1124	SDG&E - Final Award and Contract Signed	1 day	Tue 12/17/24	Tue 12/17/24		
1125	SDG&E - Submit Advice Letter	1 day	Wed 1/15/25	Wed 1/15/25		
1126	SDG&E - Advice Letter Approved	1 day	Fri 2/14/25	Fri 2/14/25		
1127	SDG&E - Implementation Plan	43 days	Fri 2/14/25	Tue 4/15/25		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


ID	Task Name	Duration	Start	Finish	2018 H1	H2
1128	***SDG&E - Lodging: Hotels/Motels Solicitation**	**400 days**	**Tue 10/10/23**	**Mon 4/21/25**		
1129	SDG&E - RFA Preparation	33 days	Tue 10/10/23	Thu 11/23/23		
1130	SDG&E - RFA Release	1 day	Fri 12/8/23	Fri 12/8/23		
1131	SDG&E - RFA Abstract Creation Duration	35 days	Fri 12/8/23	Thu 1/25/24		
1132	SDG&E - RFA Evaluation	22 days	Mon 1/22/24	Tue 2/20/24		
1133	SDG&E - RFA Review with EE PRG	7 days	Tue 3/12/24	Wed 3/20/24		
1134	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/19/24	Tue 3/19/24		
1135	SDG&E - RFP Preparation	48 days	Tue 1/23/24	Thu 3/28/24		
1136	SDG&E - RFP Release	1 day	Thu 3/21/24	Thu 3/21/24		
1137	SDG&E - RFP Proposal Creation Duration	29 days	Thu 3/21/24	Tue 4/30/24		
1138	SDG&E - RFP Evaluation	23 days	Mon 5/6/24	Wed 6/5/24		
1139	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/18/24	Tue 6/18/24		
1140	SDG&E - Selection Review with EE PRG	7 days	Thu 6/20/24	Fri 6/28/24		
1141	SDG&E - Contract Negotiation and Development	61 days	Wed 7/31/24	Wed 10/23/24		
1142	SDG&E - Contract Review with EE PRG	4 days	Tue 11/12/24	Fri 11/15/24		
1143	SDG&E - Final Award and Contract Signed	1 day	Tue 12/17/24	Tue 12/17/24		
1144	SDG&E - Submit Advice Letter	1 day	Thu 1/16/25	Thu 1/16/25		
1145	SDG&E - Advice Letter Approved	1 day	Thu 2/20/25	Thu 2/20/25		
1146	SDG&E - Implementation Plan	43 days	Thu 2/20/25	Mon 4/21/25		
1147	***SDG&E - Market Access Program (MAP)**	**326 days**	**Wed 3/13/24**	**Wed 6/11/25**		
1148	SDG&E - RFP Preparation	38 days	Wed 3/13/24	Fri 5/3/24		
1149	SDG&E - RFP Release	1 day	Tue 5/7/24	Tue 5/7/24		
1150	SDG&E - RFP Proposal Creation Duration	31 days	Tue 5/7/24	Tue 6/18/24		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
1151	SDG&E - RFP Evaluation	43 days	Wed 6/19/24	Fri 8/16/24		
1152	SDG&E - Selection Review with EE PRG	7 days	Thu 9/5/24	Fri 9/13/24		
1153	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/17/24	Tue 9/17/24		
1154	SDG&E - Contract Negotiation and Development	60 days	Fri 9/27/24	Thu 12/19/24		
1155	SDG&E - Contract Review with EE PRG	3 days	Tue 12/10/24	Thu 12/12/24		
1156	SDG&E - Final Award and Contract Signed	1 day	Fri 1/31/25	Fri 1/31/25		
1157	SDG&E - Submit Advice Letter	1 day	Wed 3/12/25	Wed 3/12/25		
1158	SDG&E - Advice Letter Approved	1 day	Fri 4/11/25	Fri 4/11/25		
1159	SDG&E - Implementation Plan	44 days	Fri 4/11/25	Wed 6/11/25		
1160	Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change					
1161						
1162	**PG&E - Local Government Partnerships (non-resource programs) Solicitation**	**376 days?**	**Fri 3/22/19**	**Fri 8/28/20**		
1163	PG&E - RFA Preparation	42 days	Fri 3/22/19	Mon 5/20/19		
1164	PG&E - RFA Release	1 day	Thu 5/23/19	Thu 5/23/19		
1165	PG&E - RFA Abstract Creation Duration	22 days	Thu 5/23/19	Fri 6/21/19		
1166	PG&E - RFA Evaluation	15 days	Mon 6/24/19	Fri 7/12/19		
1167	PG&E - RFA Review with EE PRG	4 days	Tue 7/23/19	Fri 7/26/19		
1168	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/5/19	Fri 8/9/19		
1169	PG&E - RFP Preparation	45 days	Tue 8/27/19	Mon 10/28/19		
1170	PG&E - RFP Release	1 day	Mon 11/4/19	Mon 11/4/19		
1171	PG&E - RFP Proposal Creation Duration	33 days	Mon 11/4/19	Wed 12/18/19		
1172	PG&E - RFP Evaluation	18 days	Mon 1/6/20	Wed 1/29/20		
1173	PG&E - RFP Review with EE PRG	4 days	Tue 2/25/20	Fri 2/28/20		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

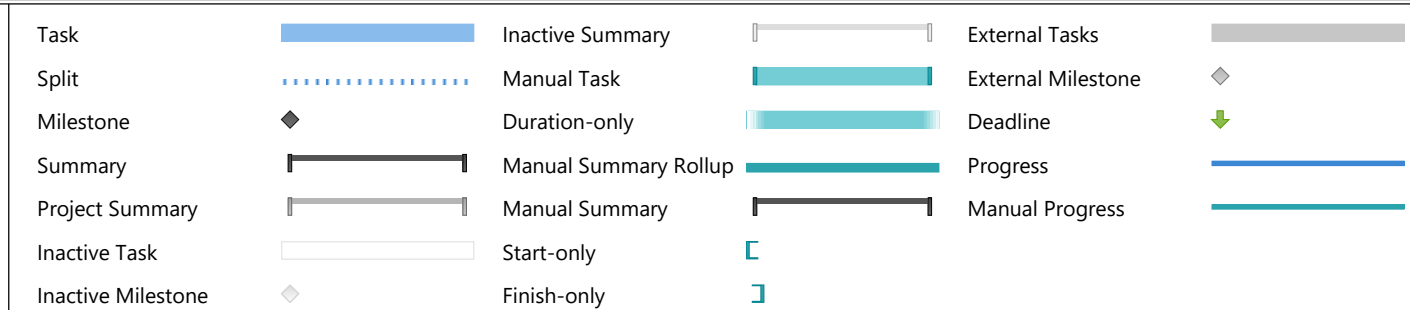


ID	Task Name	Duration	Start	Finish	2018 H1	H2
1174	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/2/20	Fri 3/6/20		
1175	PG&E - Contract Negotiation and Development	58 days	Fri 2/28/20	Tue 5/19/20		
1176	PG&E - Contract Review with EE PRG	7 days	Tue 5/26/20	Wed 6/3/20		
1177	PG&E - Final Award and Contract Signed	22 days	Fri 5/29/20	Mon 6/29/20		
1178	PG&E - Submit Advice Letter		N/A	N/A		
1179	PG&E - Advice Letter Approved					
1180	PG&E - Implementation Plan	24 days	Tue 7/28/20	Fri 8/28/20		
1181	**PG&E - Statewide Codes & Standards (RFP only) Solicitation**	**221 days?**	**Mon 7/8/19**	**Mon 5/11/20**		
1182	PG&E - RFA Preparation		N/A	N/A		
1183	PG&E - RFA Release		N/A	N/A		
1184	PG&E - RFA Abstract Creation Duration		N/A	N/A		
1185	PG&E - RFA Evaluation		N/A	N/A		
1186	PG&E - RFA Review with EE PRG		N/A	N/A		
1187	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A		
1188	PG&E - RFP Preparation	36 days	Mon 7/8/19	Mon 8/26/19		
1189	PG&E - RFP Release	1 day	Tue 9/10/19	Tue 9/10/19		
1190	PG&E - RFP Proposal Creation Duration	24 days	Tue 9/10/19	Fri 10/11/19		
1191	PG&E - RFP Evaluation	10 days	Mon 10/14/19	Fri 10/25/19		
1192	PG&E - RFP Review with EE PRG	4 days	Thu 11/21/19	Tue 11/26/19		
1193	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 11/27/19	Fri 11/29/19		
1194	PG&E - Contract Negotiation and Development	35 days	Mon 12/2/19	Fri 1/17/20		
1195	PG&E - Contract Review with EE PRG	4 days	Tue 1/21/20	Fri 1/24/20		
1196	PG&E - Final Award and Contract Signed	32 days	Wed 1/29/20	Thu 3/12/20		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
1197	PG&E - Submit Advice Letter		N/A	N/A		
1198	PG&E - Advice Letter Approved					
1199	PG&E - Implementation Plan	32 days	Fri 3/27/20	Mon 5/11/20		
1200	**PG&E - Local Multi-Sector (40% outsource) Solicitation**	**251 days?**	**Tue 4/28/20**	**Tue 4/13/21**		
1201	PG&E - RFA Preparation		N/A	N/A		
1202	PG&E - RFA Release		N/A	N/A		
1203	PG&E - RFA Abstract Creation Duration		N/A	N/A		
1204	PG&E - RFA Evaluation		N/A	N/A		
1205	PG&E - RFA Review with EE PRG		N/A	N/A		
1206	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A		
1207	PG&E - RFP Preparation		N/A	N/A		
1208	PG&E - RFP Release		N/A	N/A		
1209	PG&E - RFP Proposal Creation Duration		N/A	N/A		
1210	PG&E - RFP Evaluation		N/A	N/A		
1211	PG&E - RFP Review with EE PRG	4 days	Tue 4/28/20	Fri 5/1/20		
1212	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder					
1213	PG&E - Contract Negotiation and Development	81 days	Thu 7/2/20	Thu 10/22/20		
1214	PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20		
1215	PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20		
1216	PG&E - Submit Advice Letter	1 day	Wed 1/13/21	Wed 1/13/21		
1217	PG&E - Advice Letter Approved	1 day?	Fri 2/12/21	Fri 2/12/21		
1218	PG&E - Implementation Plan	43 days	Sat 2/13/21	Tue 4/13/21		
1219	**PG&E - Statewide New Constructions (Non-Residential) Solicitation**	**591 days**	**Mon 3/25/19**	**Sun 6/27/21**		

Project: IOU Master Task Timeli
Date: Mon 11/2/26



ID	Task Name	Duration	Start	Finish	2018 H1	2018 H2
1220	PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19		
1221	PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19		
1222	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19		
1223	PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19		
1224	PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19		
1225	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19		
1226	PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20		
1227	PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20		
1228	PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20		
1229	PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20		
1230	PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20		
1231	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20		
1232	PG&E - Contract Negotiation and Development	49 days	Mon 8/17/20	Thu 10/22/20		
1233	PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20		
1234	PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20		
1235	PG&E - Submit Advice Letter	1 day	Fri 2/19/21	Fri 2/19/21		
1236	PG&E - Advice Letter Approved	1 day	Wed 4/28/21	Wed 4/28/21		
1237	PG&E - Implementation Plan	43 days	Thu 4/29/21	Sun 6/27/21		
1238	**PG&E - Statewide New Construction (Residential) Solicitation**	**640 days?**	**Mon 3/25/19**	**Fri 9/3/21**		
1239	PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19		
1240	PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19		
1241	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19		
1242	PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	2018 H2
1243	PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19		
1244	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19		
1245	PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20		
1246	PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20		
1247	PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20		
1248	PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20		
1249	PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20		
1250	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20		
1251	PG&E - Contract Negotiation and Development	177 days	Mon 8/17/20	Tue 4/20/21		
1252	PG&E - Contract Review with EE PRG	16 days	Thu 4/22/21	Thu 5/13/21		
1253	PG&E - Final Award and Contract Signed	32 days	Sat 5/15/21	Mon 6/28/21		
1254	PG&E - Submit Advice Letter	1 day	Mon 7/12/21	Mon 7/12/21		
1255	PG&E - Advice Letter Approved (all electric)	1 day	Wed 8/11/21	Wed 8/11/21		
1256	PG&E - Advice Letter Approved (mixed fuel)	1 day	Wed 9/15/21	Wed 9/15/21		
1257	PG&E - Implementation Plan (all electric)	43 days	Thu 8/12/21	Mon 10/11/21		
1258	PG&E - Implementation Plan (mixed fuel)	43 days	Thu 9/16/21	Sun 11/14/21		
1259	**PG&E - Statewide WE&T Career Connections Solicitation**	**410 days?**	**Tue 1/7/20**	**Mon 8/2/21**		
1260	PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20		
1261	PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20		
1262	PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20		
1263	PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20		
1264	PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20		
1265	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks			
Split	Manual Task	External Milestone			
Milestone	Duration-only	Deadline			
Summary	Manual Summary Rollup	Progress			
Project Summary	Manual Summary	Manual Progress			
Inactive Task	Start-only				
Inactive Milestone	Finish-only				


ID	Task Name	Duration	Start	Finish	2018 H1	H2
1266	PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20		
1267	PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20		
1268	PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20		
1269	PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20		
1270	PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20		
1271	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20		
1272	PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21		
1273	PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21		
1274	PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21		
1275	PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21		
1276	PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21		
1277	PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21		
1278	**PG&E - Statewide WE&T Career and Workforce Readiness Solicitation**	**410 days?**	**Tue 1/7/20**	**Mon 8/2/21**		
1279	PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20		
1280	PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20		
1281	PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20		
1282	PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20		
1283	PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20		
1284	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20		
1285	PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20		
1286	PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20		
1287	PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20		
1288	PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


ID	Task Name	Duration	Start	Finish	2018 H1	H2
1289	PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20		
1290	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20		
1291	PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21		
1292	PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21		
1293	PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21		
1294	PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21		
1295	PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21		
1296	PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21		
1297	**PG&E - Statewide State of CA (Dept. of Corrections) Solicitation**	**348 days?**	**Sun 3/1/20**	**Tue 6/29/21**		
1298	PG&E - RFA Preparation	46 days	Sun 3/1/20	Fri 5/1/20		
1299	PG&E - RFA Release	1 day	Wed 5/13/20	Wed 5/13/20		
1300	PG&E - RFA Abstract Creation Duration	31 days	Wed 5/13/20	Wed 6/24/20		
1301	PG&E - RFA Evaluation	15 days	Mon 6/29/20	Fri 7/17/20		
1302	PG&E - RFA Review with EE PRG	5 days	Tue 7/28/20	Mon 8/3/20		
1303	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/3/20	Fri 8/7/20		
1304	PG&E - RFP Preparation	20 days	Mon 8/3/20	Fri 8/28/20		
1305	PG&E - RFP Release	1 day	Wed 9/9/20	Wed 9/9/20		
1306	PG&E - RFP Proposal Creation Duration	31 days	Wed 9/9/20	Wed 10/21/20		
1307	PG&E - RFP Evaluation	31 days	Fri 10/23/20	Fri 12/4/20		
1308	PG&E - RFP Review with EE PRG	6 days	Tue 12/22/20	Tue 12/29/20		
1309	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 1/6/21	Fri 1/8/21		
1310	PG&E - Contract Negotiation and Development	65 days	Wed 1/20/21	Tue 4/20/21		
1311	PG&E - Contract Review with EE PRG	7 days	Thu 4/22/21	Fri 4/30/21		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

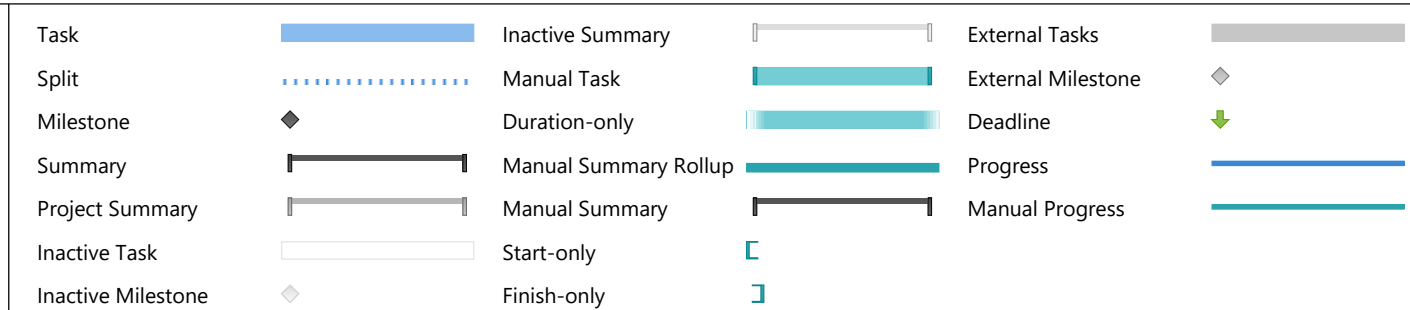

ID	Task Name	Duration	Start	Finish	2018 H1	H2
1312	PG&E - Final Award and Contract Signed	22 days	Sat 5/1/21	Mon 5/31/21		
1313	PG&E - Submit Advice Letter	1 day	Thu 6/24/21	Thu 6/24/21		
1314	PG&E - Advice Letter Approved	1 day	Wed 7/28/21	Wed 7/28/21		
1315	PG&E - Implementation Plan	43 days	Thu 7/29/21	Sun 9/26/21		
1316	**PG&E - Local (Micro and Small Business Equity Program) Solicitation**	**403 days?**	**Tue 6/1/21**	**Thu 12/15/22**		
1317	PG&E - RFA Preparation	38 days	Tue 6/1/21	Thu 7/22/21		
1318	PG&E - RFA Release	1 day	Tue 9/7/21	Tue 9/7/21		
1319	PG&E - RFA Abstract Creation Duration	34 days	Wed 9/8/21	Mon 10/25/21		
1320	PG&E - RFA Evaluation	18 days	Tue 10/26/21	Thu 11/18/21		
1321	PG&E - RFP Release	1 day	Wed 12/8/21	Wed 12/8/21		
1322	PG&E - RFP Proposal Creation Duration	46 days	Wed 12/8/21	Wed 2/9/22		
1323	PG&E - RFP Evaluation	21 days	Thu 2/10/22	Thu 3/10/22		
1324	PG&E - RFP Review with EE PRG	6 days	Thu 3/17/22	Thu 3/24/22		
1325	PG&E - RFP Estimated Bidder Notification	1 day	Wed 3/30/22	Wed 3/30/22		
1326	PG&E - Contract Negotiation and Development	71 days	Thu 4/7/22	Thu 7/14/22		
1327	PG&E - Contract Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22		
1328	PG&E - Final Award and Contract Signed	45 days	Mon 8/8/22	Fri 10/7/22		
1329	PG&E - Submit Advice Letter	1 day	Wed 10/12/22	Wed 10/12/22		
1330	PG&E - Advice Letter Approved	1 day	Fri 11/11/22	Fri 11/11/22		
1331	PG&E - Implementation Plan	31 days	Fri 11/11/22	Fri 12/23/22		
1332	**PG&E - Local (C&S Compliance Improvement) Solicitation**	**436 days**	**Tue 3/1/22**	**Tue 10/31/23**		
1333	PG&E - RFA Preparation	34 days	Tue 3/1/22	Fri 4/15/22		
1334	PG&E - RFA Release	1 day	Mon 5/16/22	Mon 5/16/22		

Project: IOU Master Task Timeli
Date: Mon 11/2/26




ID	Task Name	Duration	Start	Finish	2018 H1	H2
1335	PG&E - RFA Abstract Creation Duration	25 days	Tue 5/17/22	Mon 6/20/22		
1336	PG&E - RFA Evaluation	28 days	Tue 6/21/22	Thu 7/28/22		
1337	PG&E - RFA Review with EE PRG	1 day	Tue 8/9/22	Tue 8/9/22		
1338	PG&E - RFA Estimated Bidder Notification	1 day	Wed 8/31/22	Wed 8/31/22		
1339	PG&E - RFP Preparation	24 days	Mon 8/1/22	Thu 9/1/22		
1340	PG&E - RFP Release	1 day	Tue 9/13/22	Tue 9/13/22		
1341	PG&E - RFP Proposal Creation Duration	26 days	Tue 9/13/22	Tue 10/18/22		
1342	PG&E - RFP Evaluation	45 days	Wed 10/19/22	Tue 12/20/22		
1343	PG&E - RFP Review with EE PRG	1 day	Tue 1/24/23	Tue 1/24/23		
1344	PG&E - RFP Estimated Bidder Notification	1 day	Fri 2/10/23	Fri 2/10/23		
1345	PG&E - Contract Negotiation and Development	47 days	Mon 2/13/23	Tue 4/18/23		
1346	PG&E - Contract Review with EE PRG	26 days	Tue 5/23/23	Tue 6/27/23		
1347	PG&E - Final Award and Contract Signed	48 days	Wed 6/28/23	Fri 9/1/23		
1348	PG&E - Submit Advice Letter		N/A			
1349	PG&E - Advice Letter Approved		N/A			
1350	PG&E - Implementation Plan	1 day	Tue 10/31/23	Tue 10/31/23		
1351	**PG&E - Residential Electrification Equity Program Solicitation**	**595 days**	**Mon 8/1/22**	**Fri 11/8/24**		
1352	PG&E - RFA Preparation	59 days	Mon 8/1/22	Thu 10/20/22		
1353	PG&E - RFA Release	1 day	Tue 11/29/22	Tue 11/29/22		
1354	PG&E - RFA Abstract Creation Duration	46 days	Tue 11/29/22	Tue 1/31/23		
1355	PG&E - RFA Evaluation	17 days	Sun 2/5/23	Sun 2/26/23		
1356	PG&E - RFA Review with EE PRG	6 days	Mon 2/27/23	Mon 3/6/23		
1357	PG&E - RFA Estimated Bidder Notification	3 days	Mon 3/6/23	Wed 3/8/23		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
1358	PG&E - RFP Preparation	46 days	Mon 1/9/23	Mon 3/13/23		
1359	PG&E - RFP Release	1 day	Tue 4/11/23	Tue 4/11/23		
1360	PG&E - RFP Proposal Creation Duration	26 days	Tue 4/11/23	Tue 5/16/23		
1361	PG&E - RFP Evaluation	18 days	Fri 5/19/23	Tue 6/13/23		
1362	PG&E - RFP Review with EE PRG	1 day	Tue 6/27/23	Tue 6/27/23		
1363	PG&E - RFP Estimated Bidder Notification	1 day	Tue 7/11/23	Tue 7/11/23		
1364	PG&E - Contract Negotiation and Development	233 days	Tue 8/1/23	Thu 6/20/24		
1365	PG&E - Contract Review with EE PRG	8 days	Fri 6/21/24	Tue 7/2/24		
1366	PG&E - Final Award and Contract Signed	21 days	Fri 7/5/24	Fri 8/2/24		
1367	PG&E - Submit Advice Letter	1 day	Fri 8/9/24	Fri 8/9/24		
1368	PG&E - Advice Letter Approved	1 day	Mon 9/9/24	Mon 9/9/24		
1369	PG&E - Implementation Plan	1 day	Fri 11/8/24	Fri 11/8/24		
1370	**PG&E - Statewide C&S Advocacy Solicitation**	**641 days**	**Tue 2/1/22**	**Tue 7/16/24**		
1371	PG&E - RFA Preparation	54 days	Tue 2/1/22	Fri 4/15/22		
1372	PG&E - RFA Release	1 day	Mon 5/30/22	Mon 5/30/22		
1373	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/31/22	Fri 7/1/22		
1374	PG&E - RFA Evaluation	14 days	Fri 7/1/22	Wed 7/20/22		
1375	PG&E - RFA Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22		
1376	PG&E - RFA Estimated Bidder Notification	1 day	Mon 8/1/22	Mon 8/1/22		
1377	PG&E - RFP Preparation	36 days	Fri 4/1/22	Fri 5/20/22		
1378	PG&E - RFP Release	1 day	Tue 6/7/22	Tue 6/7/22		
1379	PG&E - RFP Proposal Creation Duration	31 days	Tue 6/7/22	Tue 7/19/22		
1380	PG&E - RFP Evaluation	50 days	Wed 7/20/22	Tue 9/27/22		

Project: IOU Master Task Timeli
Date: Mon 11/2/26




ID	Task Name	Duration	Start	Finish	2018 H1	H2
1381	PG&E - RFP Review with EE PRG	1 day	Wed 10/5/22	Wed 10/5/22		
1382	PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/24/22	Mon 10/24/22		
1383	PG&E - Contract Negotiation and Development	73 days	Mon 11/14/22	Wed 2/22/23		
1384	PG&E - Contract Review with EE PRG - Wave 1	1 day	Tue 4/25/23	Tue 4/25/23		
1385	PG&E - Final Award and Contract Signed	18 days	Mon 7/17/23	Wed 8/9/23		
1386	PG&E - Submit Advice Letter (wave 1)	1 day	Thu 9/21/23	Thu 9/21/23		
1387	PG&E - Advice Letter Approved	1 day	Wed 10/25/23	Wed 10/25/23		
1388	PG&E - Implementation Plan	1 day	Thu 12/7/23	Thu 12/7/23		
1389	PG&E - Contract Review with EE PRG - Wave 2	1 day	Wed 12/20/23	Wed 12/20/23		
1390	PG&E - Final Award and Contract Signed	1 day	Fri 3/29/24	Fri 3/29/24		
1391	PG&E - Submit Advice Letter	1 day	Wed 4/17/24	Wed 4/17/24		
1392	PG&E - Advice Letter Approved	1 day	Fri 5/17/24	Fri 5/17/24		
1393	PG&E - Implementation Plan	1 day	Tue 7/16/24	Tue 7/16/24		
1394	**PG&E - Zonal Electrification Solicitation**	**495 days**	**Thu 12/1/22**	**Wed 10/23/24**		
1395	PG&E - RFP Preparation	88 days	Thu 12/1/22	Mon 4/3/23		
1396	PG&E - RFP Release	1 day	Tue 4/18/23	Tue 4/18/23		
1397	PG&E - RFP Proposal Creation Duration	53 days	Tue 4/18/23	Thu 6/29/23		
1398	PG&E - RFP Evaluation (including interviews)	40 days	Mon 7/10/23	Fri 9/1/23		
1399	PG&E - RFP Review with EE PRG	1 day	Tue 9/26/23	Tue 9/26/23		
1400	PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/2/23	Mon 10/2/23		
1401	PG&E - Contract Negotiation and Development	135 days	Mon 10/9/23	Fri 4/12/24		
1402	PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24		
1403	PG&E - Final Award and Contract Signed	43 days	Wed 5/1/24	Fri 6/28/24		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish	2018 H1	H2
1404	PG&E - Submit Advice Letter	1 day	Wed 7/3/24	Wed 7/3/24		
1405	PG&E - Advice Letter Approved	1 day	Wed 8/28/24	Wed 8/28/24		
1406	PG&E - Implementation Plan	1 day	Wed 10/23/24	Wed 10/23/24		
1407	**PG&E - Residential Whole Home Load Management RFP**	**453 days**	**Tue 8/15/23**	**Thu 5/8/25**		
1408	PG&E - RFP Preparation	1 day	Tue 8/15/23	Tue 8/15/23		
1409	PG&E - RFP Release	1 day	Tue 8/15/23	Tue 8/15/23		
1410	PG&E - RFP Proposal Creation Duration	51 days	Tue 8/15/23	Tue 10/24/23		
1411	PG&E - RFP Evaluation	36 days	Thu 10/26/23	Thu 12/14/23		
1412	PG&E - RFP Review with EE PRG	1 day	Fri 2/16/24	Fri 2/16/24		
1413	PG&E - RFP Estimated Bidder Notification	1 day	Tue 2/27/24	Tue 2/27/24		
1414	PG&E - Contract Negotiation and Development	155 days	Wed 3/13/24	Tue 10/15/24		
1415	PG&E - Contract Review with EE PRG	8 days	Tue 11/5/24	Thu 11/14/24		
1416	PG&E - Final Award and Contract Signed	53 days	Thu 11/14/24	Mon 1/27/25		
1417	PG&E - Submit Advice Letter	1 day	Fri 2/7/25	Fri 2/7/25		
1418	PG&E - Advice Letter Approved	1 day	Mon 3/10/25	Mon 3/10/25		
1419	PG&E - Implementation Plan	1 day	Thu 5/8/25	Thu 5/8/25		
1420	**PG&E - 2024 Summer Reliability Platform Administrator RFP**	**337 days?**	**Tue 4/18/23**	**Wed 7/31/24**		
1421	PG&E - RFP Preparation	30 days	Mon 5/1/23	Fri 6/9/23		
1422	PG&E - RFP Release	1 day	Fri 9/1/23	Fri 9/1/23		
1423	PG&E - RFP Proposal Creation Duration	31 days	Fri 9/1/23	Fri 10/13/23		
1424	PG&E - RFP Evaluation	22 days	Tue 10/17/23	Wed 11/15/23		
1425	PG&E - RFP Review with EE PRG	1 day	Tue 11/28/23	Tue 11/28/23		
1426	PG&E - RFP Estimated Bidder Notification	1 day	Tue 12/5/23	Tue 12/5/23		

Project: IOU Master Task Timeli
Date: Mon 11/2/26



ID	Task Name	Duration	Start	Finish	2018 H1	H2
1427	PG&E - Contract Negotiation and Development	68 days	Mon 1/8/24	Wed 4/10/24		
1428	PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24		
1429	PG&E - Final Award and Contract Signed	22 days	Wed 5/1/24	Thu 5/30/24		
1430	PG&E - Submit Advice Letter	1 day	Fri 5/31/24	Fri 5/31/24		
1431	PG&E - Advice Letter Approved	1 day	Mon 7/1/24	Mon 7/1/24		
1432	PG&E - Implementation Plan	1 day	Wed 7/31/24	Wed 7/31/24		
1433	**PG&E - C&S Code Readiness RFP**	**393 days?**	**Wed 2/1/23**	**Fri 8/2/24**		
1434	PG&E - RFP Preparation	113 days	Wed 2/1/23	Fri 7/7/23		
1435	PG&E - RFP Release	1 day	Wed 7/12/23	Wed 7/12/23		
1436	PG&E - RFP Proposal Creation Duration	30 days	Thu 7/13/23	Wed 8/23/23		
1437	PG&E - RFP Evaluation	36 days	Mon 8/28/23	Mon 10/16/23		
1438	PG&E - RFP Review with EE PRG	1 day	Tue 10/24/23	Tue 10/24/23		
1439	PG&E - RFP Estimated Bidder Notification	1 day	Mon 11/6/23	Mon 11/6/23		
1440	PG&E - Contract Negotiation and Development	65 days	Wed 11/15/23	Tue 2/13/24		
1441	PG&E - Contract Review with EE PRG	1 day	Tue 2/27/24	Tue 2/27/24		
1442	PG&E - Final Award and Contract Signed	1 day	Fri 4/12/24	Fri 4/12/24		
1443	PG&E - Submit Advice Letter	1 day	Tue 5/7/24	Tue 5/7/24		
1444	PG&E - Advice Letter Approved	1 day	Thu 6/6/24	Thu 6/6/24		
1445	PG&E - Implementation Plan	1 day	Fri 8/2/24	Fri 8/2/24		
1446	**PG&E - Residential Electrification - Single Point of Contact**	**414 days**	**Tue 8/1/23**	**Fri 2/28/25**		
1447	PG&E - RFP Preparation	133 days	Tue 8/1/23	Thu 2/1/24		
1448	PG&E - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24		
1449	PG&E - RFP Proposal Creation Duration	33 days	Wed 2/28/24	Fri 4/12/24		

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Duration	Start	Finish
1450	PG&E - RFP Evaluation	66 days	Mon 4/15/24	Mon 7/15/24
1451	PG&E - RFP Review with EE PRG	6 days	Fri 7/19/24	Fri 7/26/24
1452	PG&E - RFP Estimated Bidder Notification	1 day	Wed 8/7/24	Wed 8/7/24
1453	PG&E - Contract Negotiation and Development	62 days		
1454	PG&E - Contract Review with EE PRG	6 days		
1455	PG&E - Final Award and Contract Signed	25 days		
1456	PG&E - Submit Advice Letter	1 day		
1457	PG&E - Advice Letter Approved	1 day		
1458	PG&E - Implementation Plan	1 day		
1459	**PG&E - Commercial SEM FP**	**430 days**	**Thu 8/3/23**	**Wed 3/26/25**
1460	PG&E - RFP Preparation	16 days	Thu 8/3/23	Thu 8/24/23
1461	PG&E - RFP Release	1 day	Fri 11/3/23	Fri 11/3/23
1462	PG&E - RFP Proposal Creation Duration	55 days	Fri 11/3/23	Thu 1/18/24
1463	PG&E - RFP Evaluation	58 days	Tue 1/23/24	Thu 4/11/24
1464	PG&E - RFP Review with EE PRG	1 day	Wed 4/17/24	Wed 4/17/24
1465	PG&E - RFP Estimated Bidder Notification	4 days	Tue 4/23/24	Fri 4/26/24
1466	PG&E - Contract Negotiation and Development	90 days	Thu 5/2/24	Wed 9/4/24
1467	PG&E - Contract Review with EE PRG	8 days	Mon 9/16/24	Wed 9/25/24
1468	PG&E - Final Award and Contract Signed	58 days	Thu 9/26/24	Mon 12/16/24
1469	PG&E - Submit Advice Letter	1 day	Thu 12/19/24	Thu 12/19/24
1470	PG&E - Advice Letter Approved	0 days	Thu 1/30/25	Thu 1/30/25
1471	PG&E - Implementation Plan	1 day	Wed 3/26/25	Wed 3/26/25
1472	**PG&E - SW WE&T Career & Workforce Readiness**	**630 days**	**Tue 10/8/24**	**Sun 3/7/27**


2018
H1 H2

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress


ID	Task Name	Duration	Start	Finish	2018 H1	H2
1473	PG&E - RFP Preparation	199 days	Tue 10/8/24	Fri 7/11/25		
1474	PG&E - RFP Release	1 day	Thu 7/17/25	Thu 7/17/25		
1475	PG&E - RFP Proposal Creation Duration	41 days	Thu 7/17/25	Thu 9/11/25		
1476	PG&E - RFP Evaluation	50 days	Mon 9/15/25	Fri 11/21/25		
1477	PG&E - RFP Review with EE PRG	4 days	Fri 12/5/25	Wed 12/10/25		
1478	PG&E - RFP Estimated Bidder Notification	4 days	Wed 12/10/25	Mon 12/15/25		
1479	PG&E - Contract Negotiation and Development	157 days	Wed 1/7/26	Thu 8/13/26		
1480	PG&E - Contract Review with EE PRG	6 days	Fri 9/18/26	Fri 9/25/26		
1481	PG&E - Final Award and Contract Signed	42 days	Fri 9/25/26	Mon 11/23/26		
1482	PG&E - Submit Advice Letter	1 day	Tue 12/8/26	Tue 12/8/26		
1483	PG&E - Advice Letter Approved	1 day	Thu 1/7/27	Thu 1/7/27		
1484	PG&E - Implementation Plan	43 days	Thu 1/7/27	Sun 3/7/27		
1485	**PG&E - Statewide HVAC**	**532 days**	**Fri 5/2/25**	**Sat 5/15/27**		
1486	PG&E - RFP Preparation	122 days	Fri 5/2/25	Mon 10/20/25		
1487	PG&E - RFP Release	1 day	Wed 10/22/25	Wed 10/22/25		
1488	PG&E - RFP Proposal Creation Duration	41 days	Wed 10/22/25	Wed 12/17/25		
1489	PG&E - RFP Evaluation	32 days	Thu 12/18/25	Fri 1/30/26		
1490	PG&E - RFP Review with EE PRG	1 day	Thu 3/26/26	Thu 3/26/26		
1491	PG&E - RFP Estimated Bidder Notification	1 day	Mon 4/6/26	Mon 4/6/26		
1492	PG&E - Contract Negotiation and Development	130 days	Tue 4/7/26	Mon 10/5/26		
1493	PG&E - Contract Review with EE PRG	9 days	Tue 10/20/26	Fri 10/30/26		
1494	PG&E - Final Award and Contract Signed	1 day	Fri 2/5/27	Fri 2/5/27		
1495	PG&E - Submit Advice Letter	1 day	Mon 2/15/27	Mon 2/15/27		


Project: IOU Master Task Timeli
Date: Mon 11/2/26

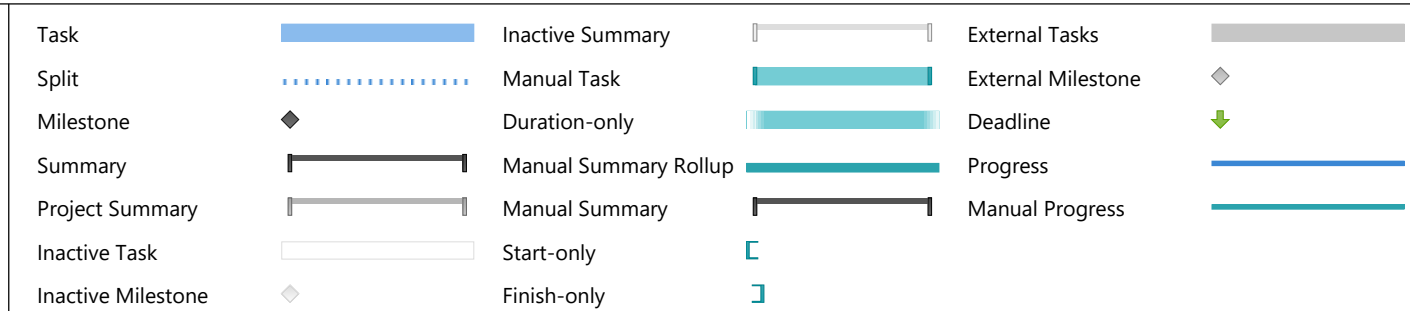

ID	Task Name	Duration	Start	Finish	2018 H1	H2
1496	PG&E - Advice Letter Approved	1 day	Mon 3/15/27	Mon 3/15/27		
1497	PG&E - Implementation Plan	1 day	Sat 5/15/27	Sat 5/15/27		


Project: IOU Master Task Timeli
Date: Mon 11/2/26



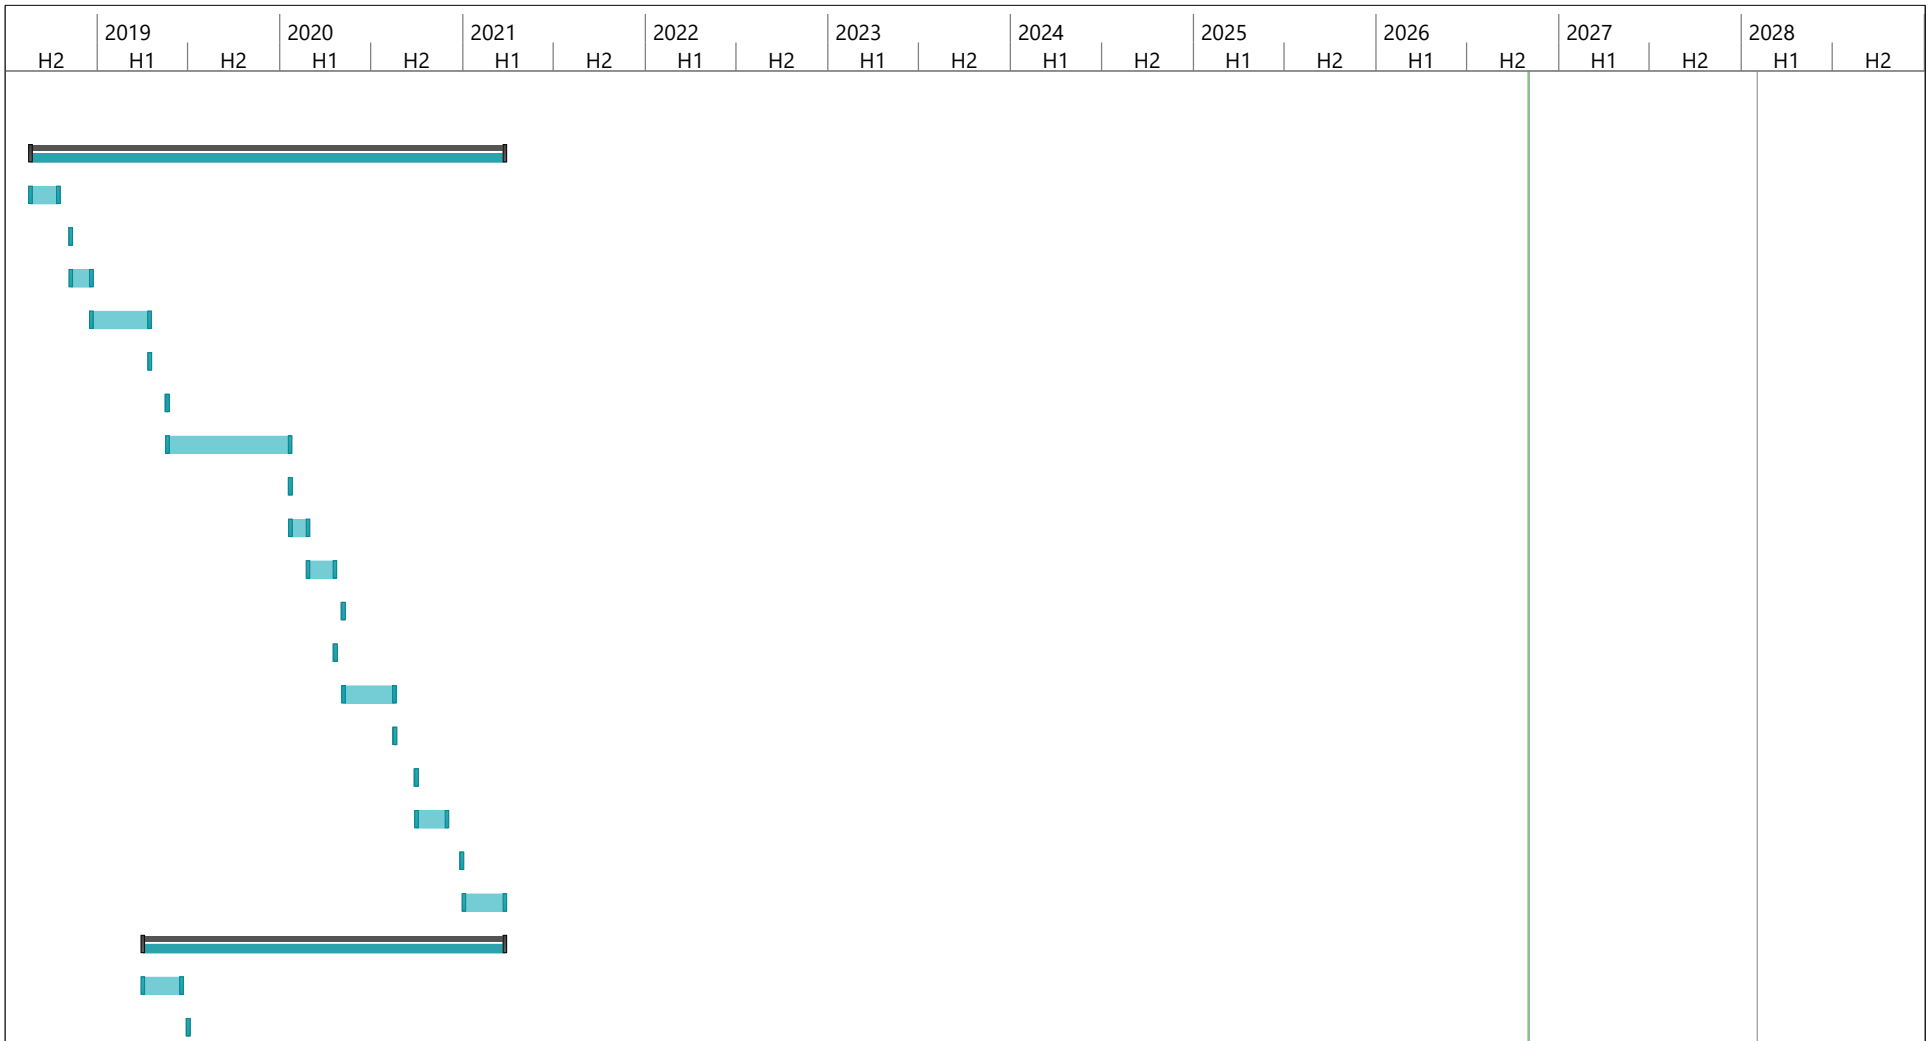


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

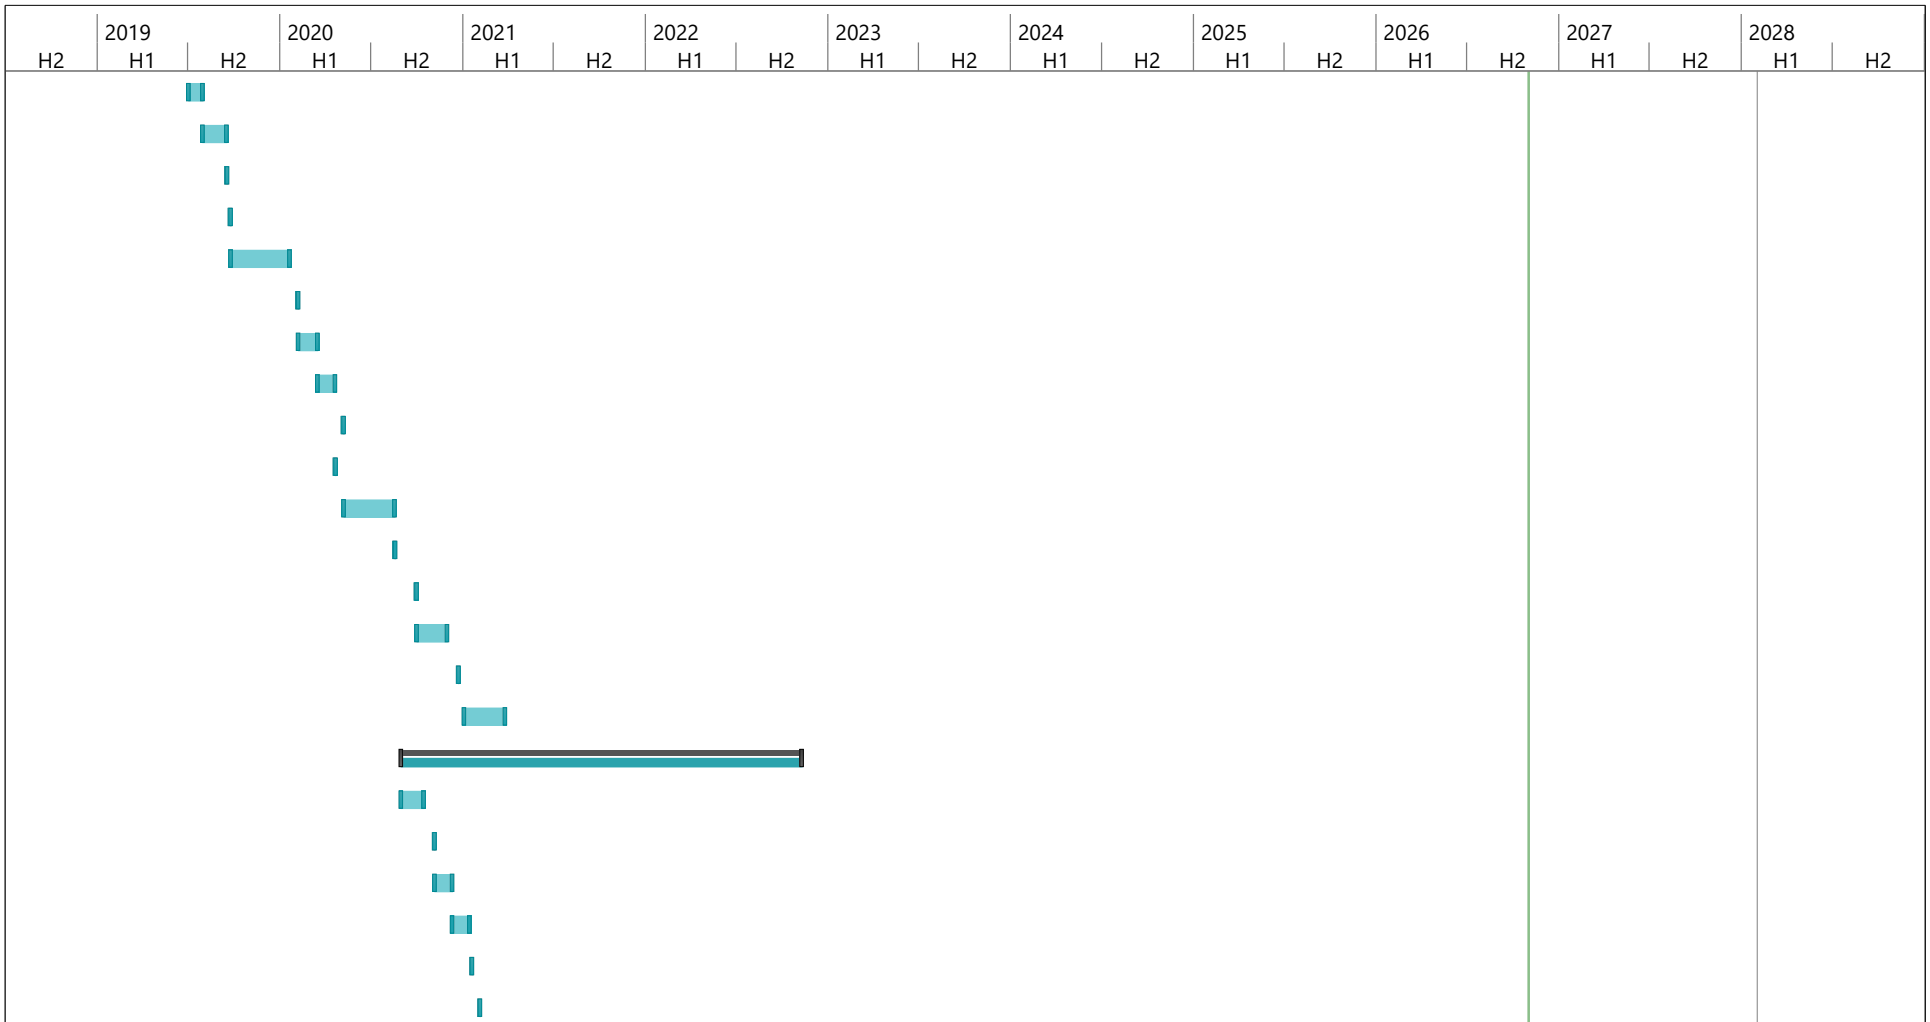


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

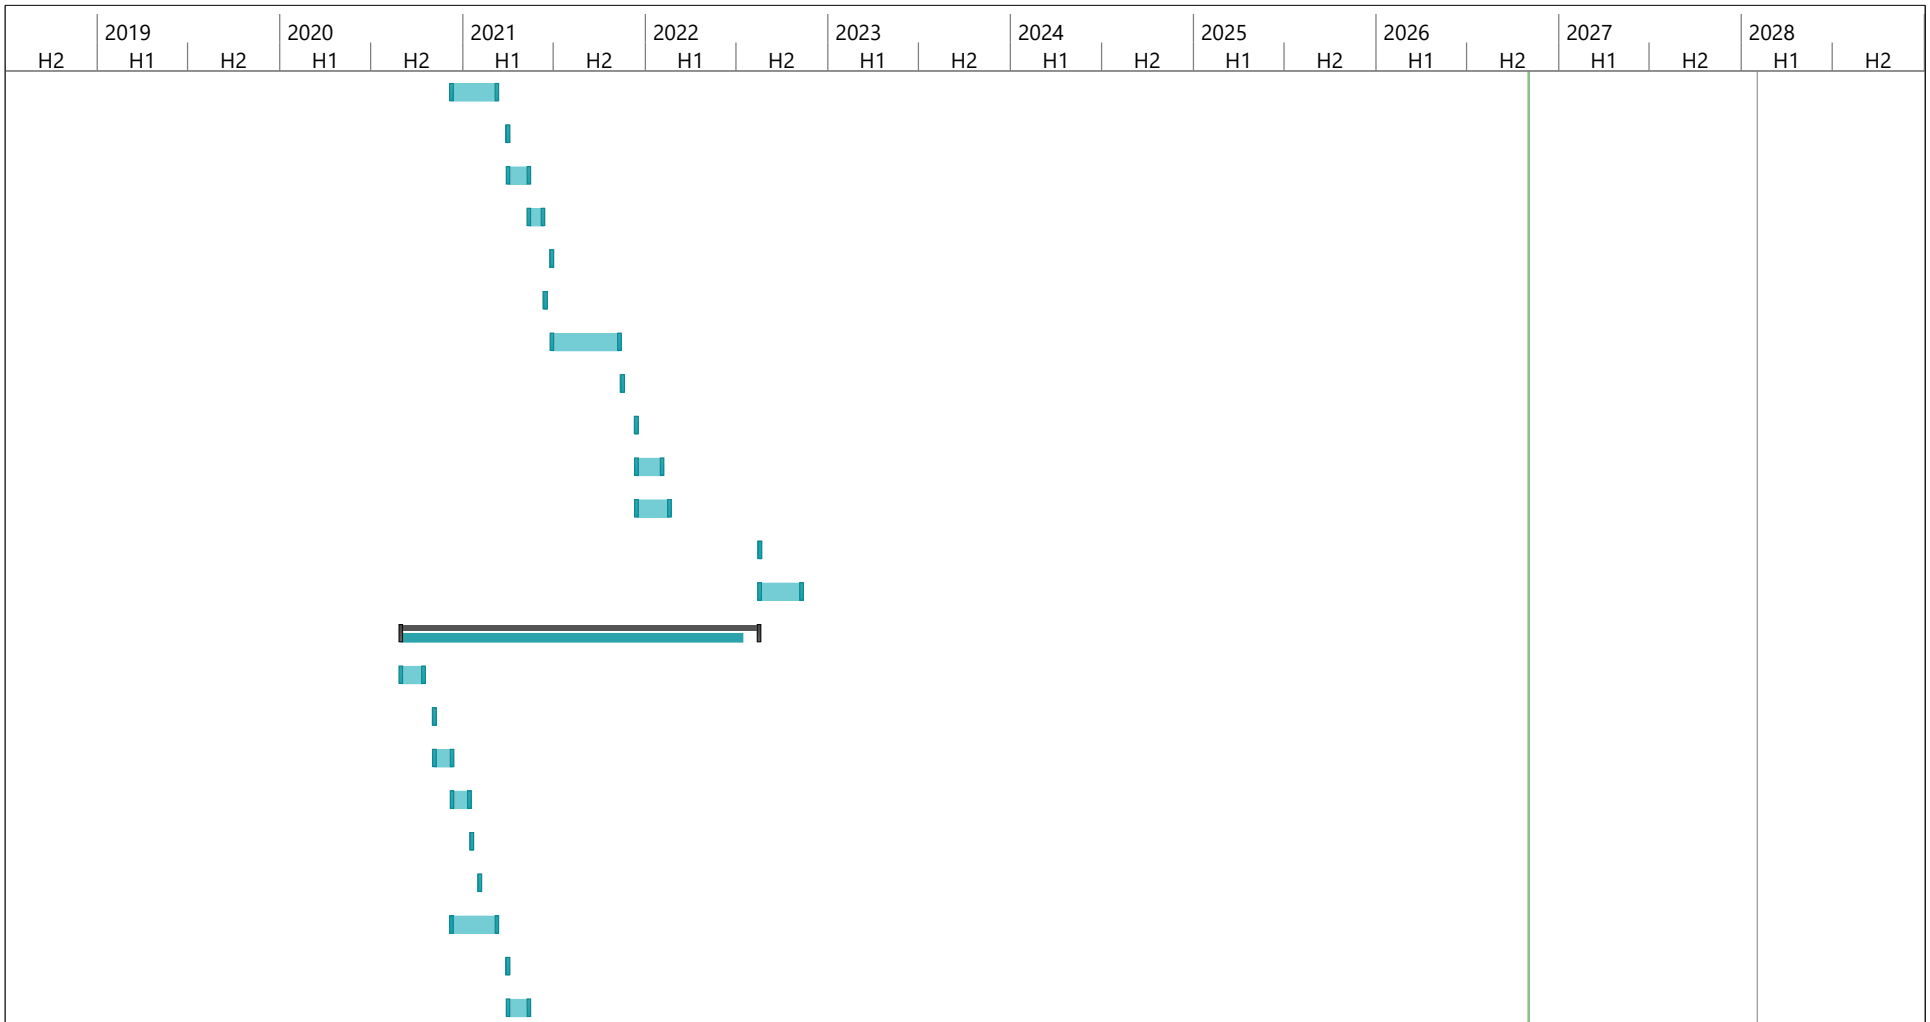


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

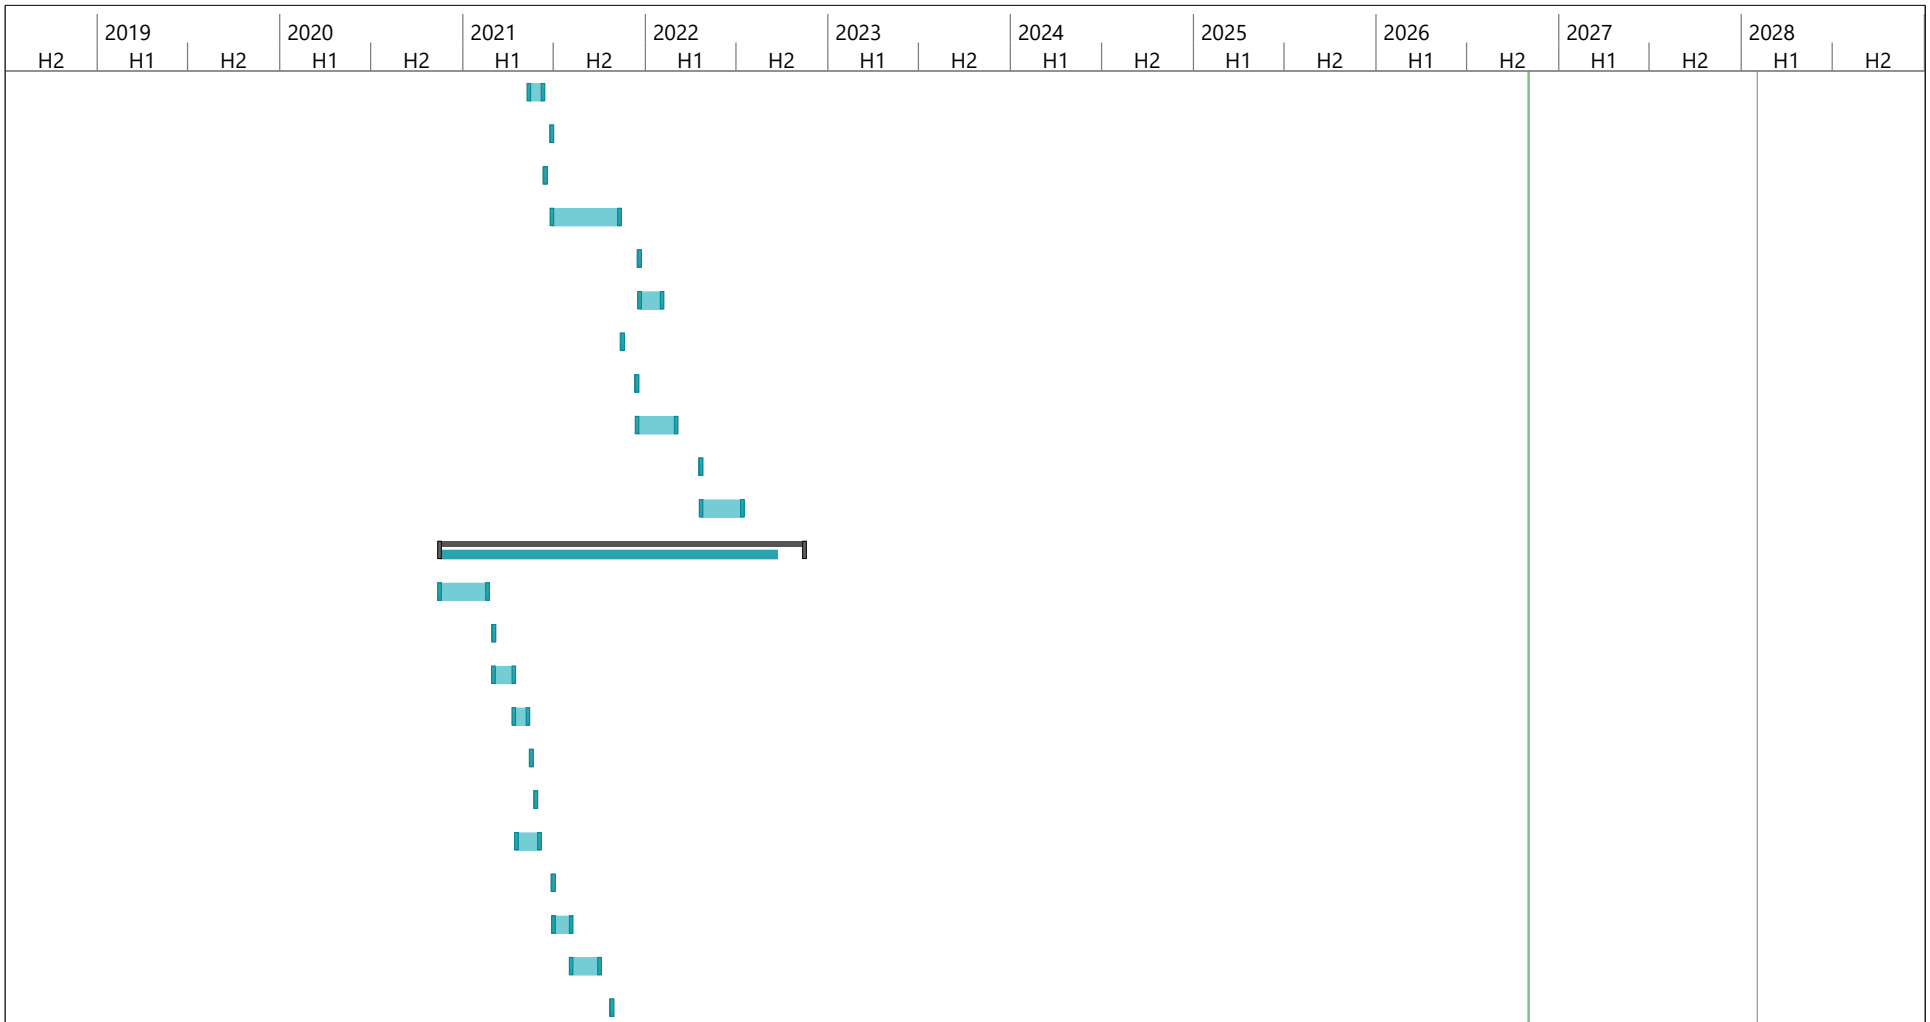


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

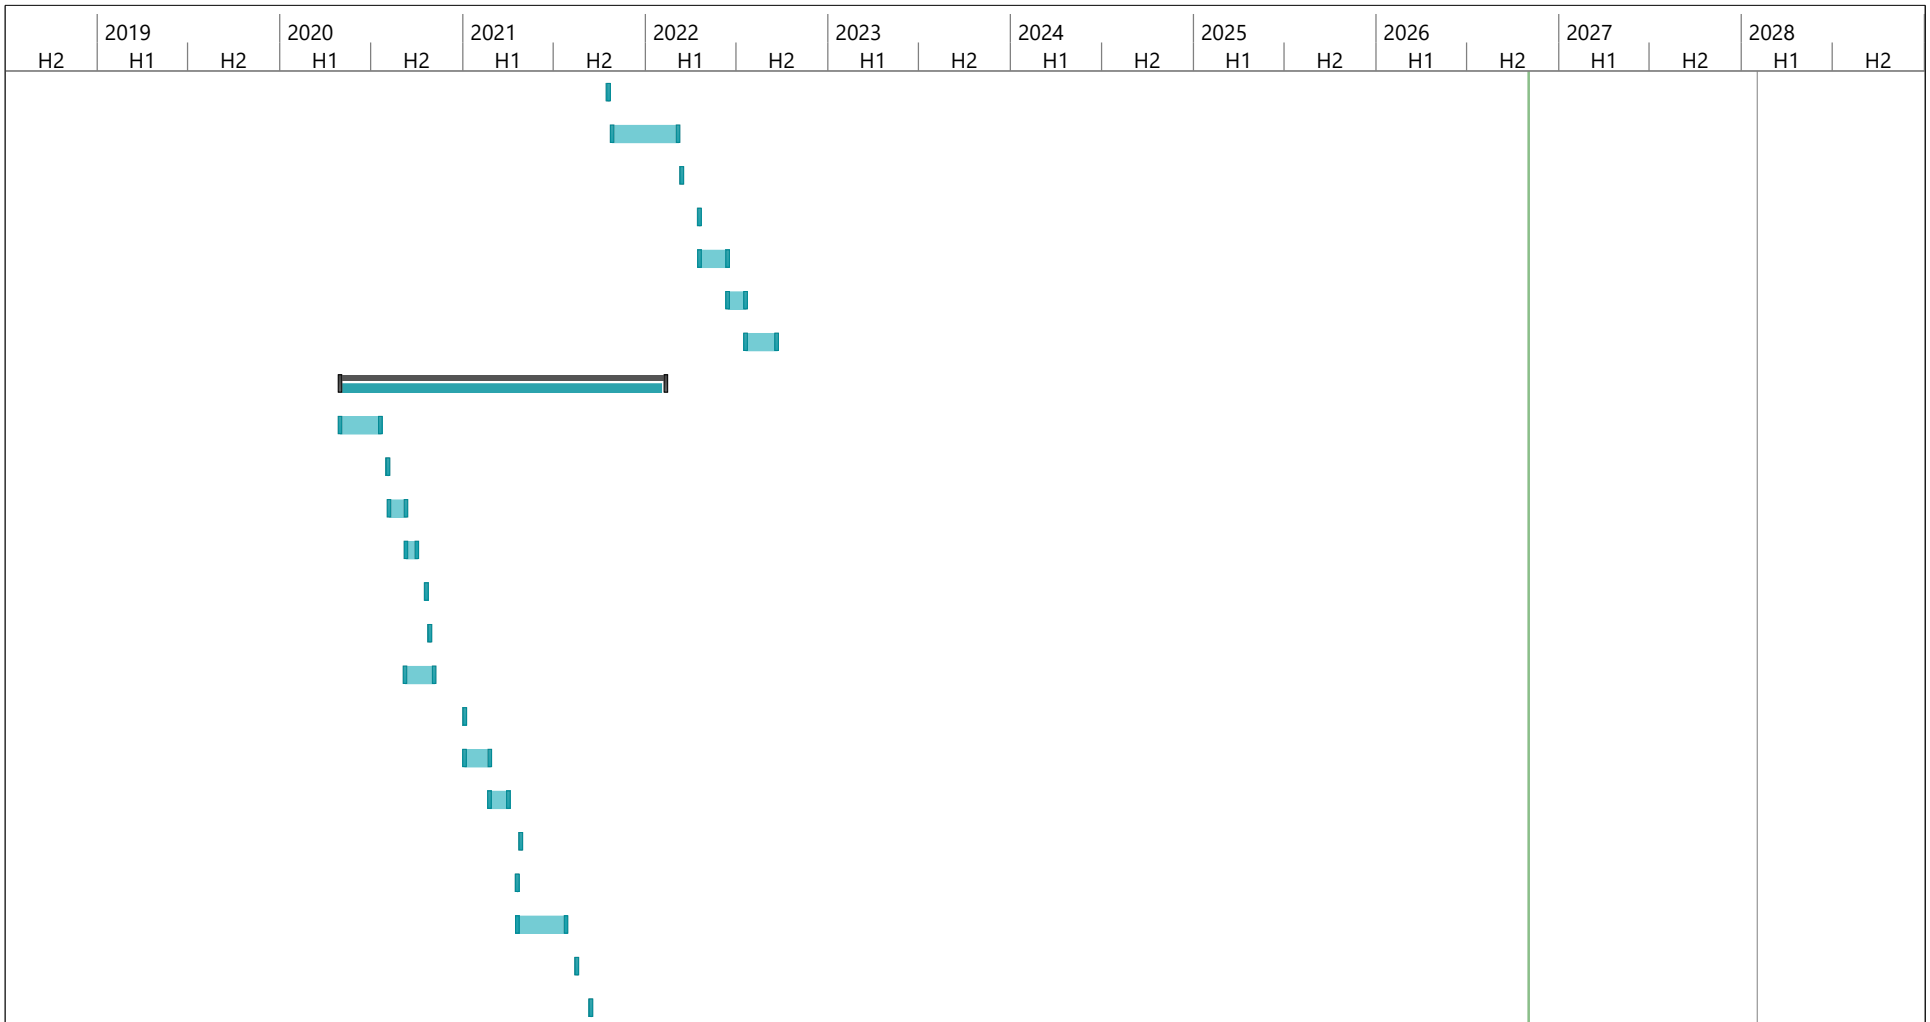


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

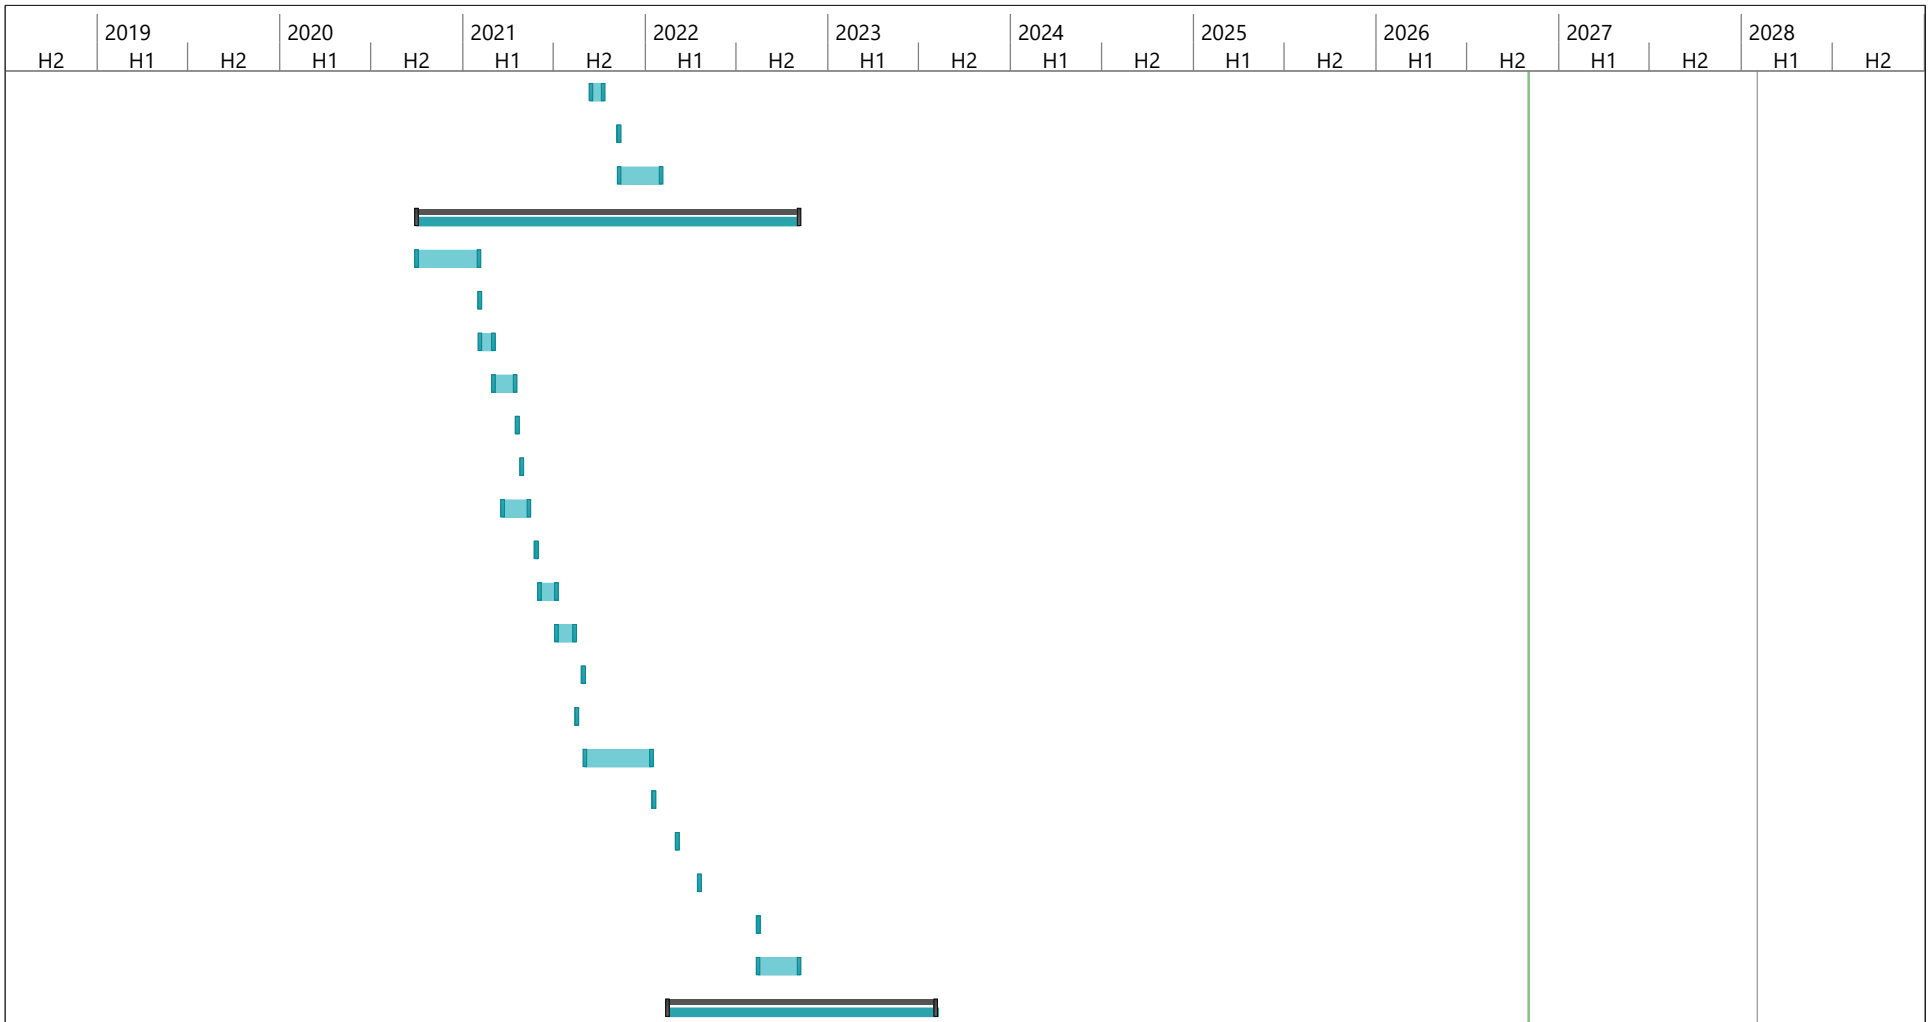


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

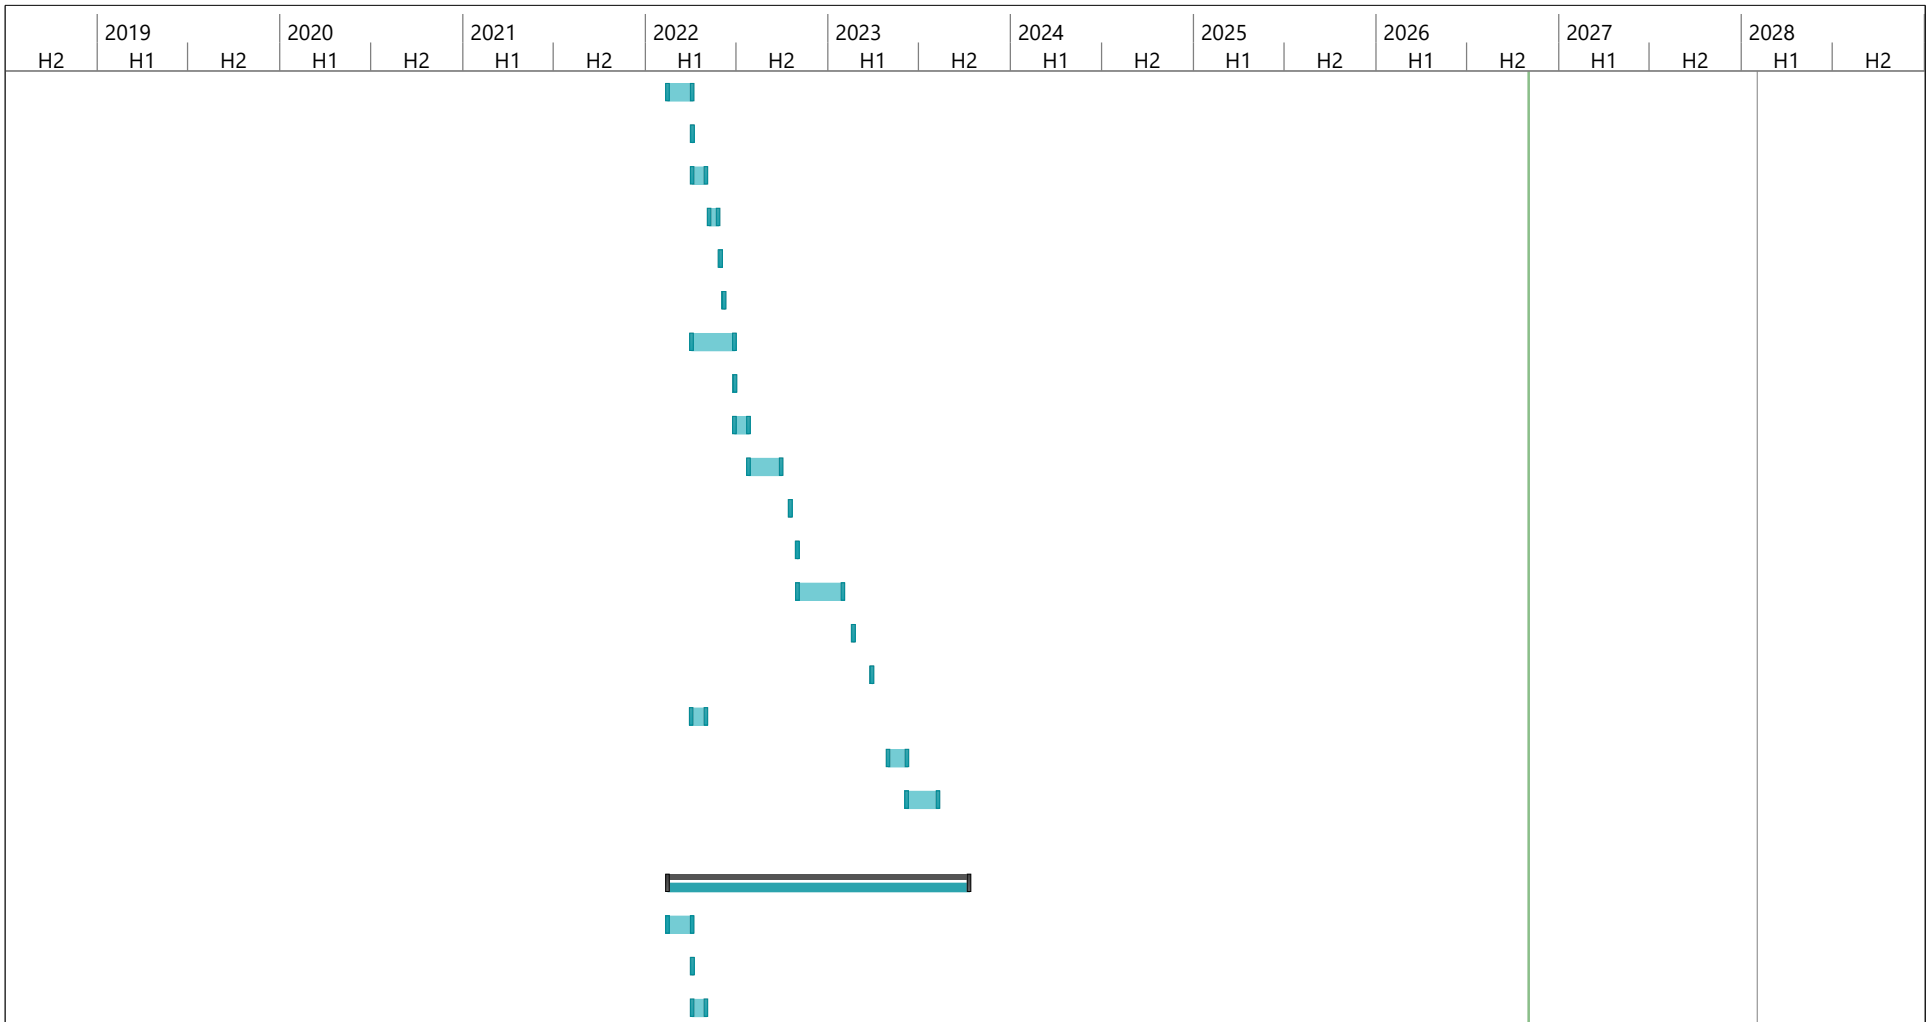


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

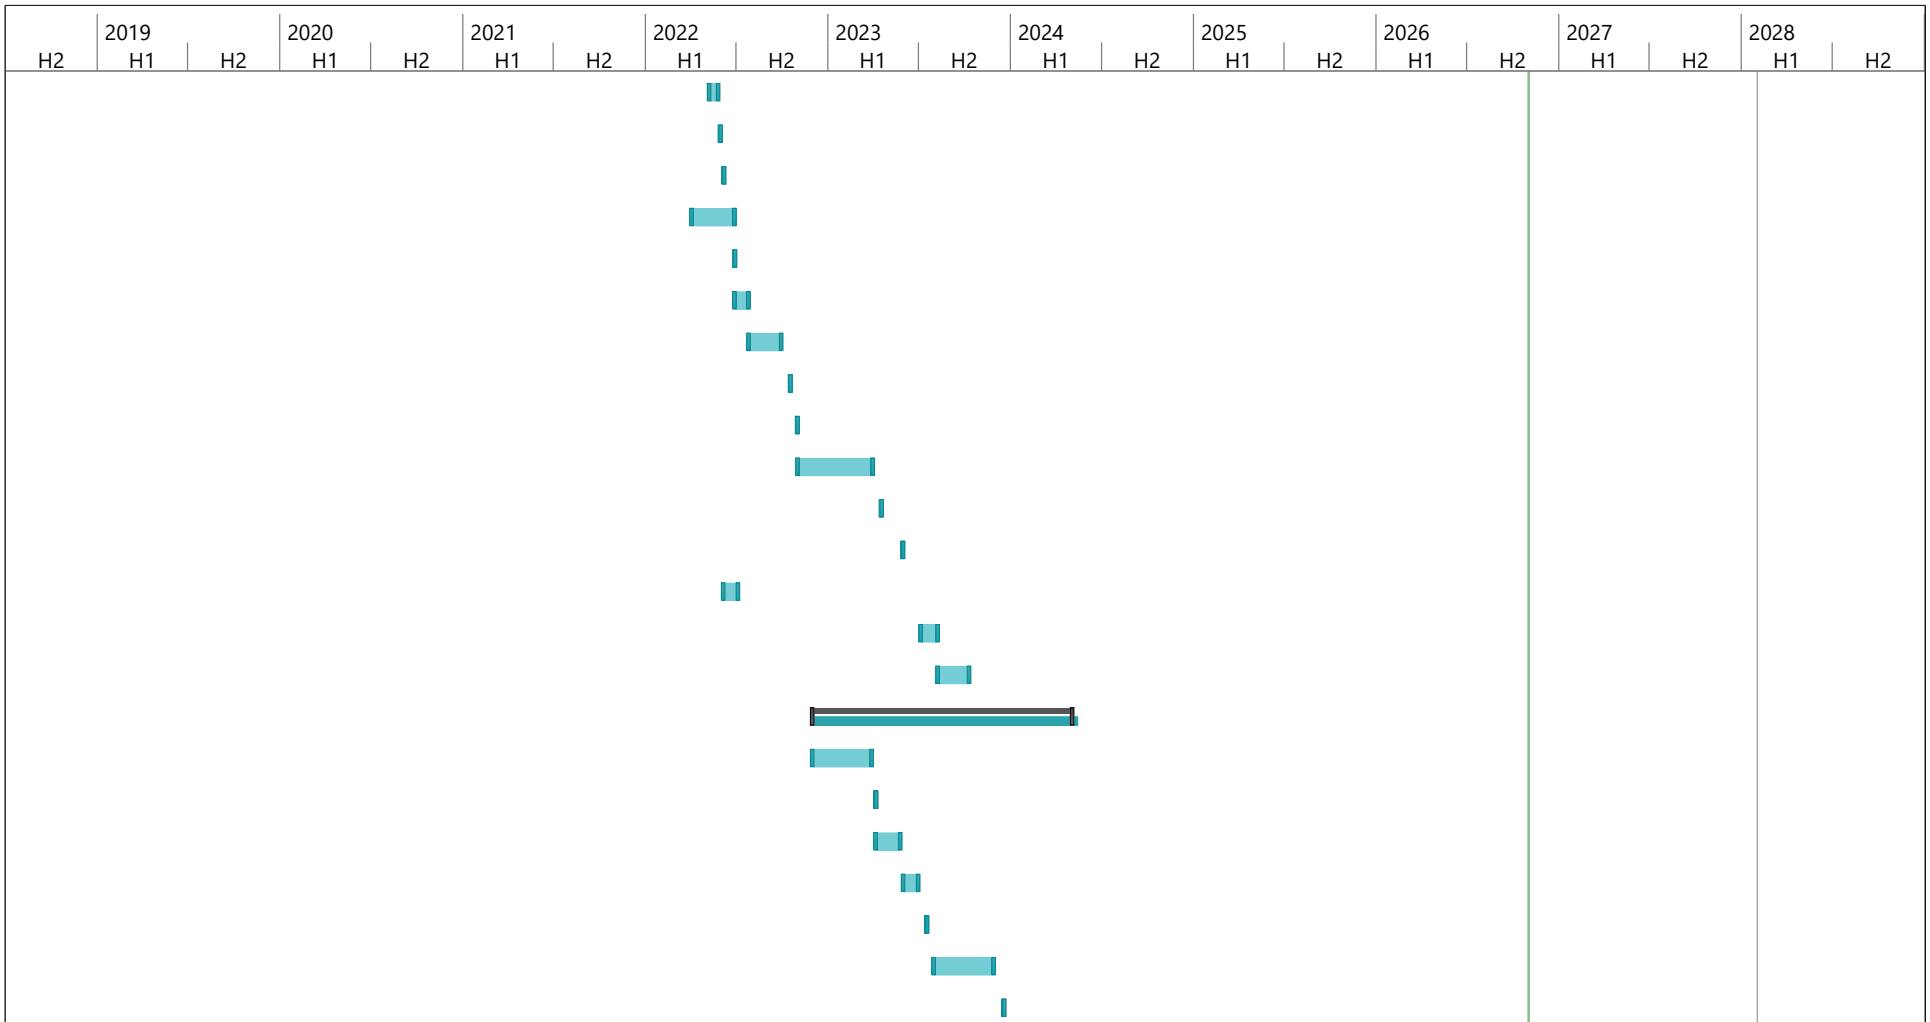


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

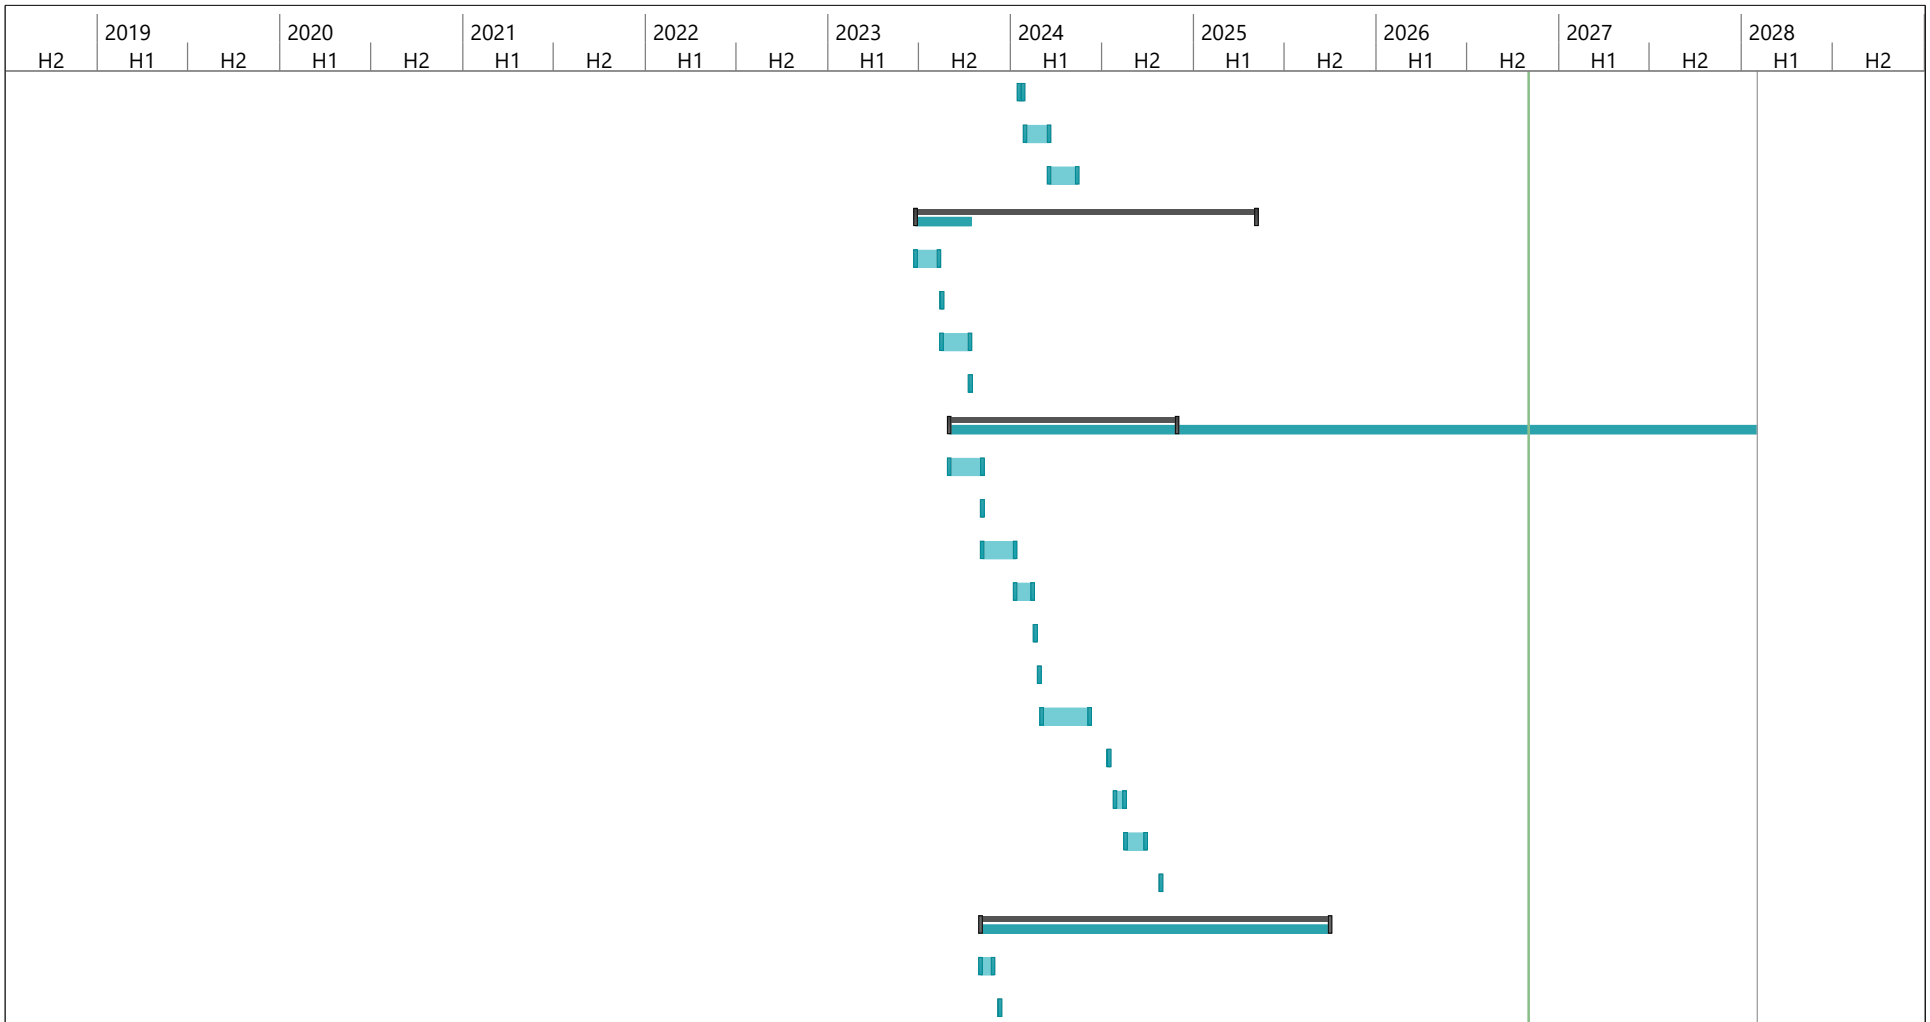


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

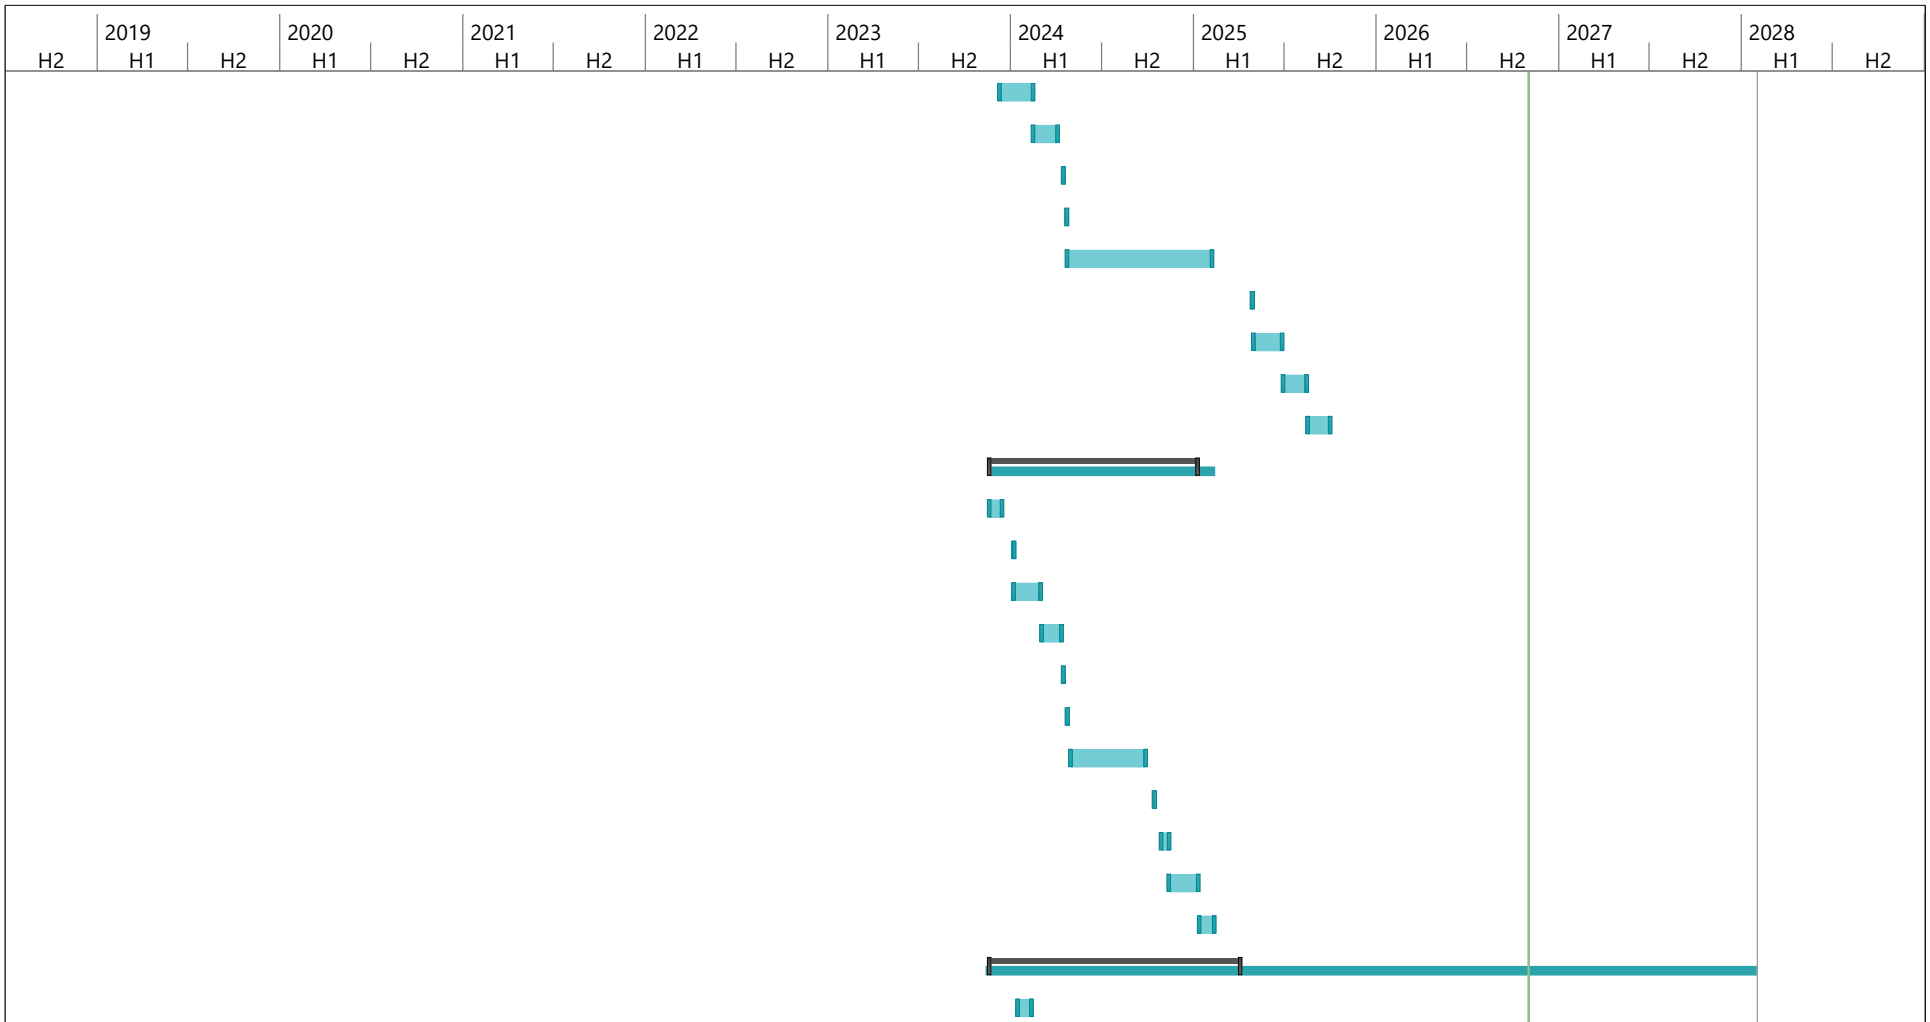


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

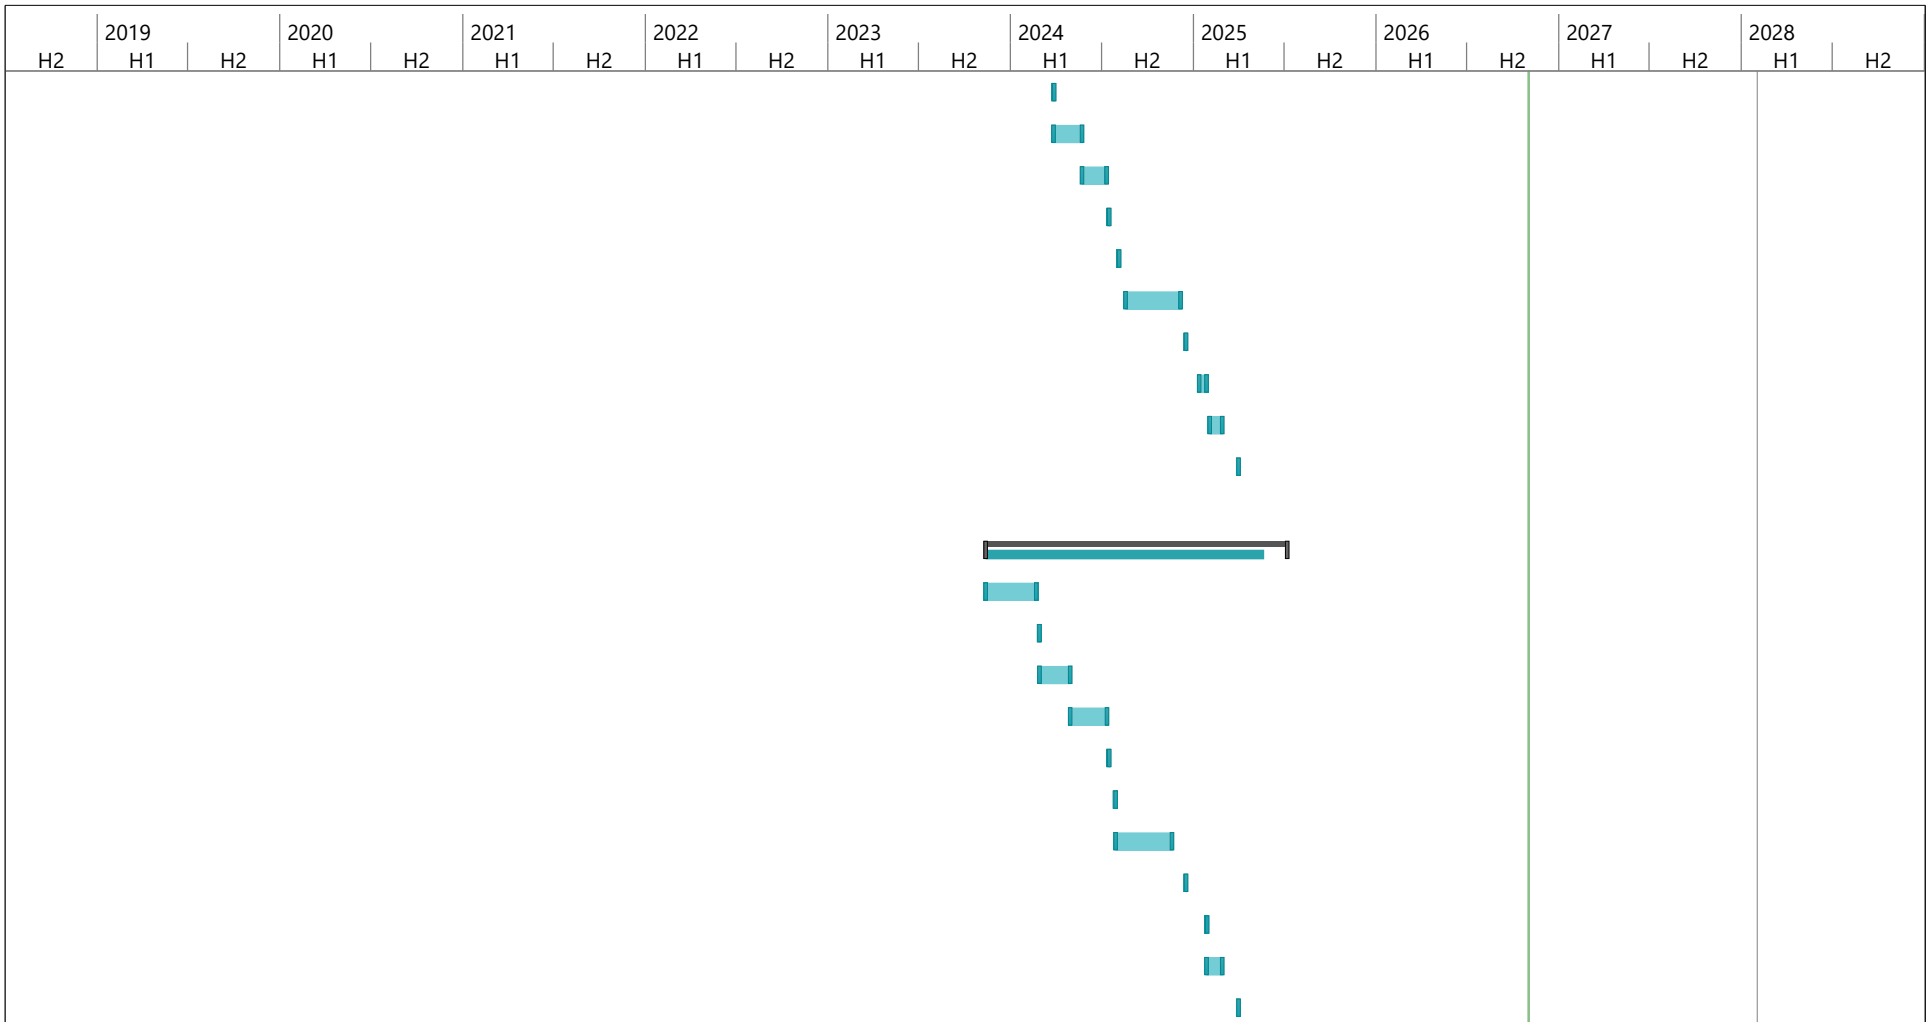


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

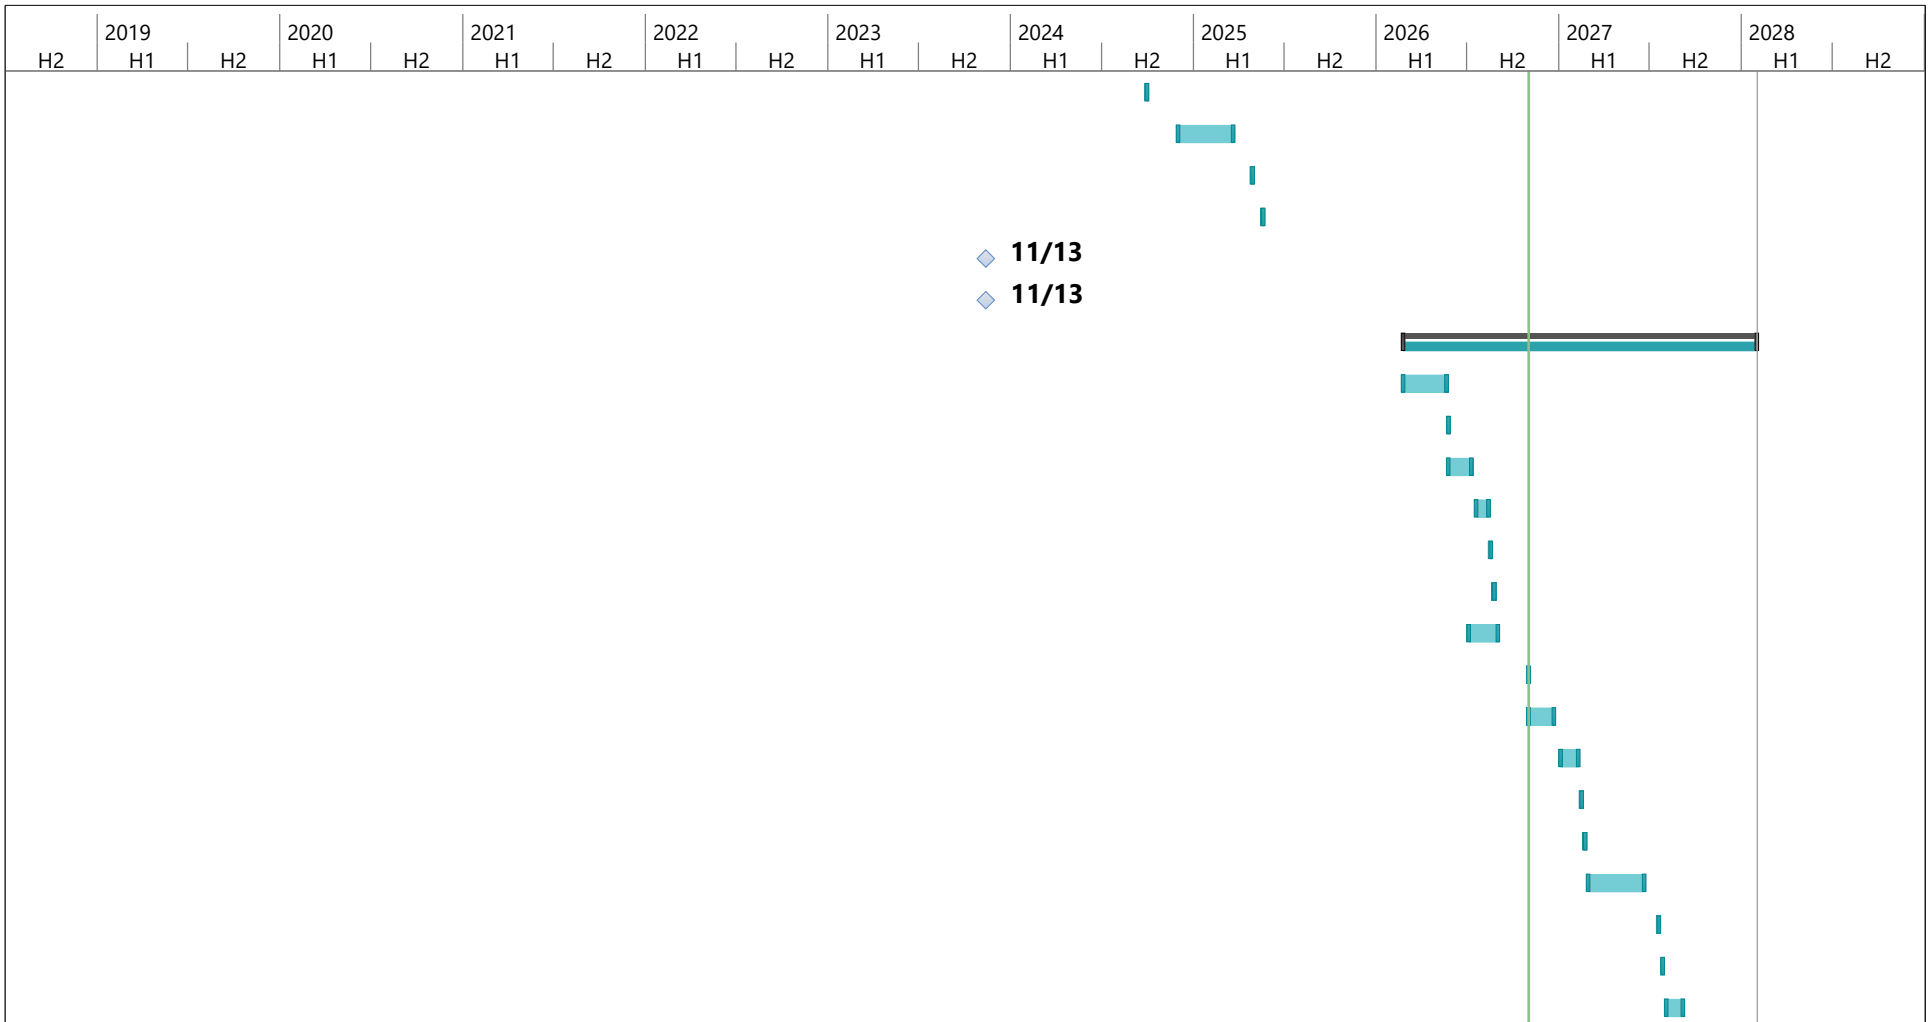


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

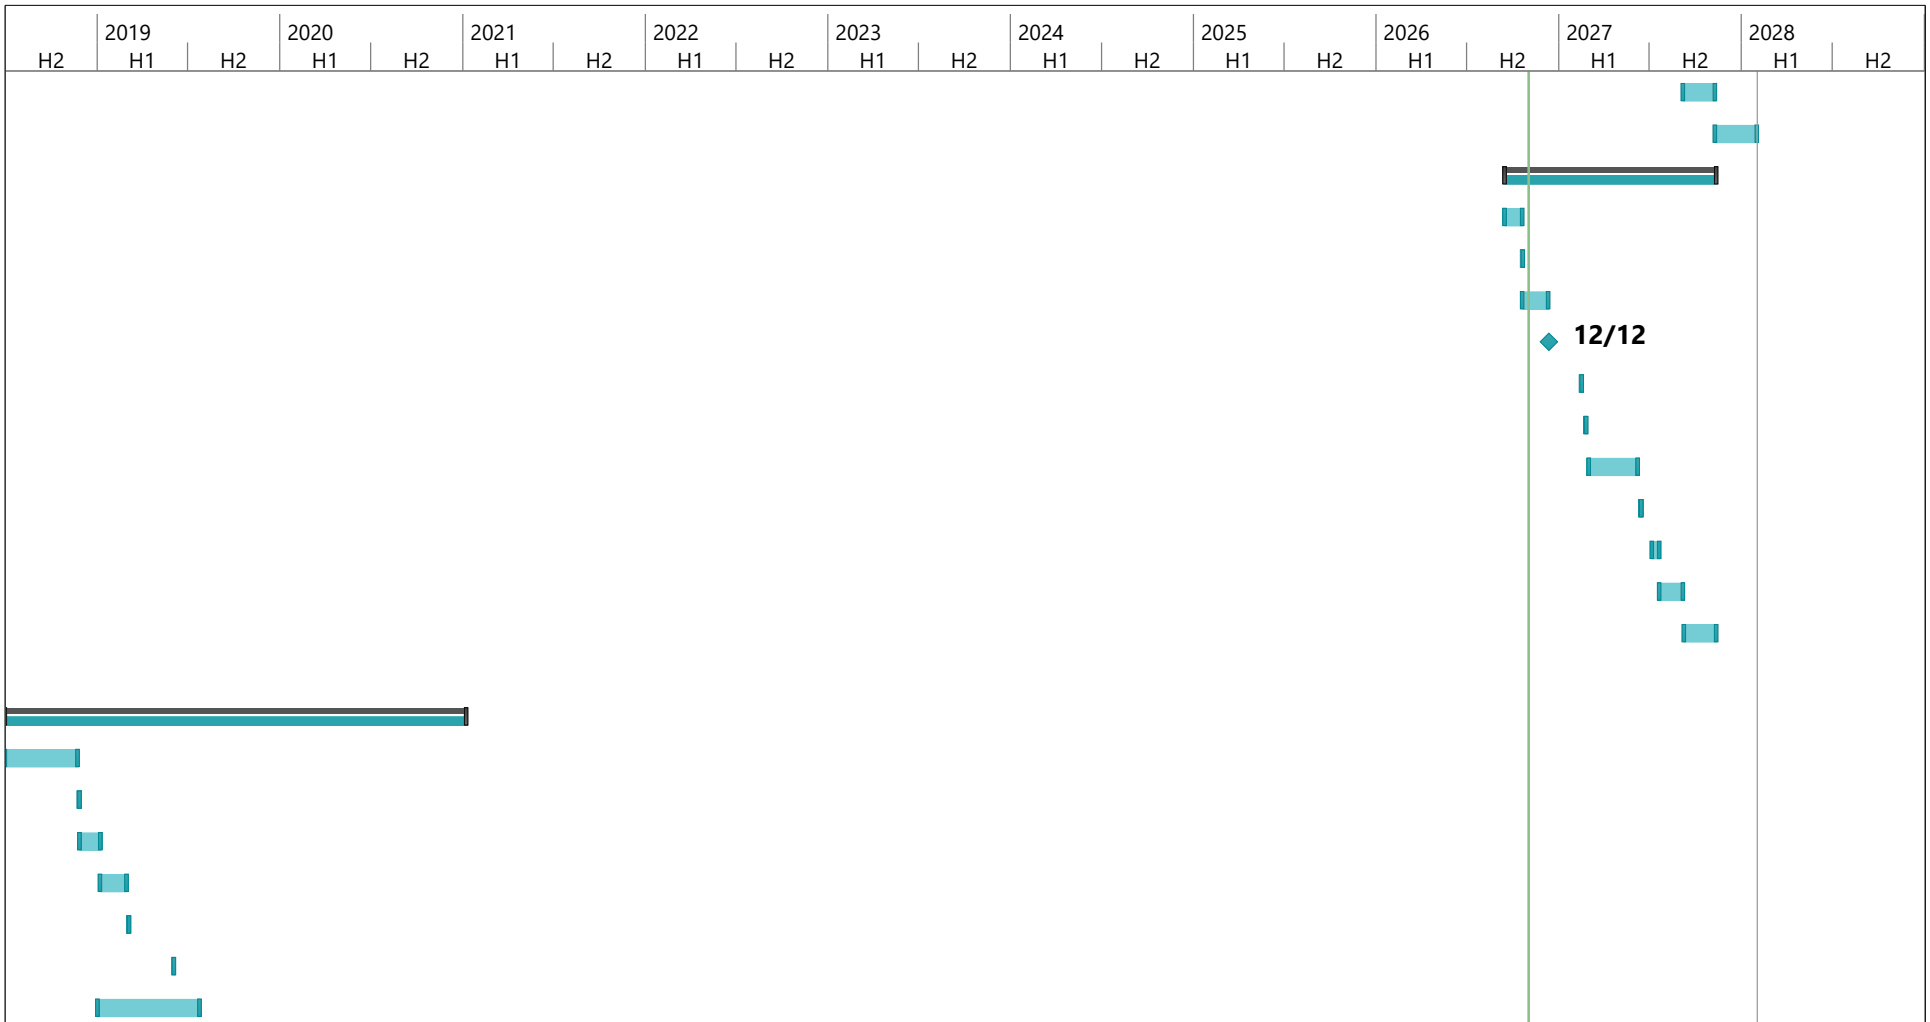


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

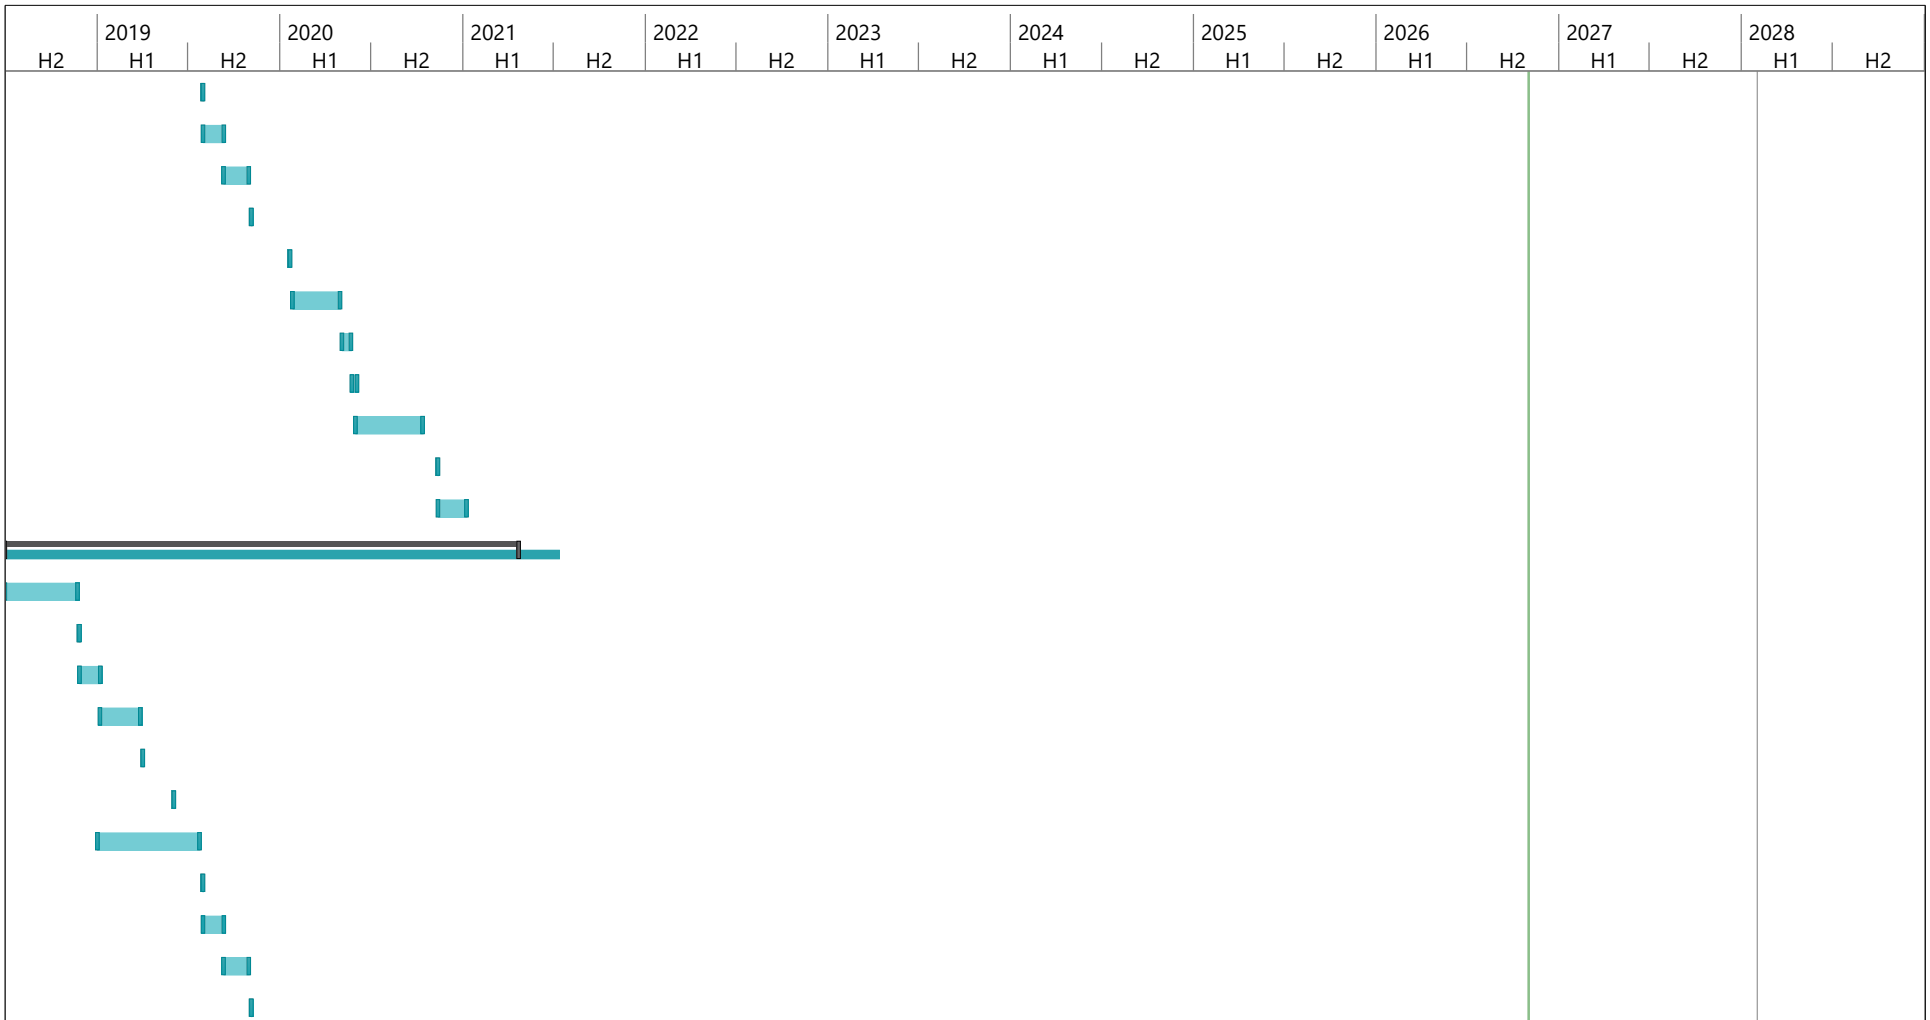


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

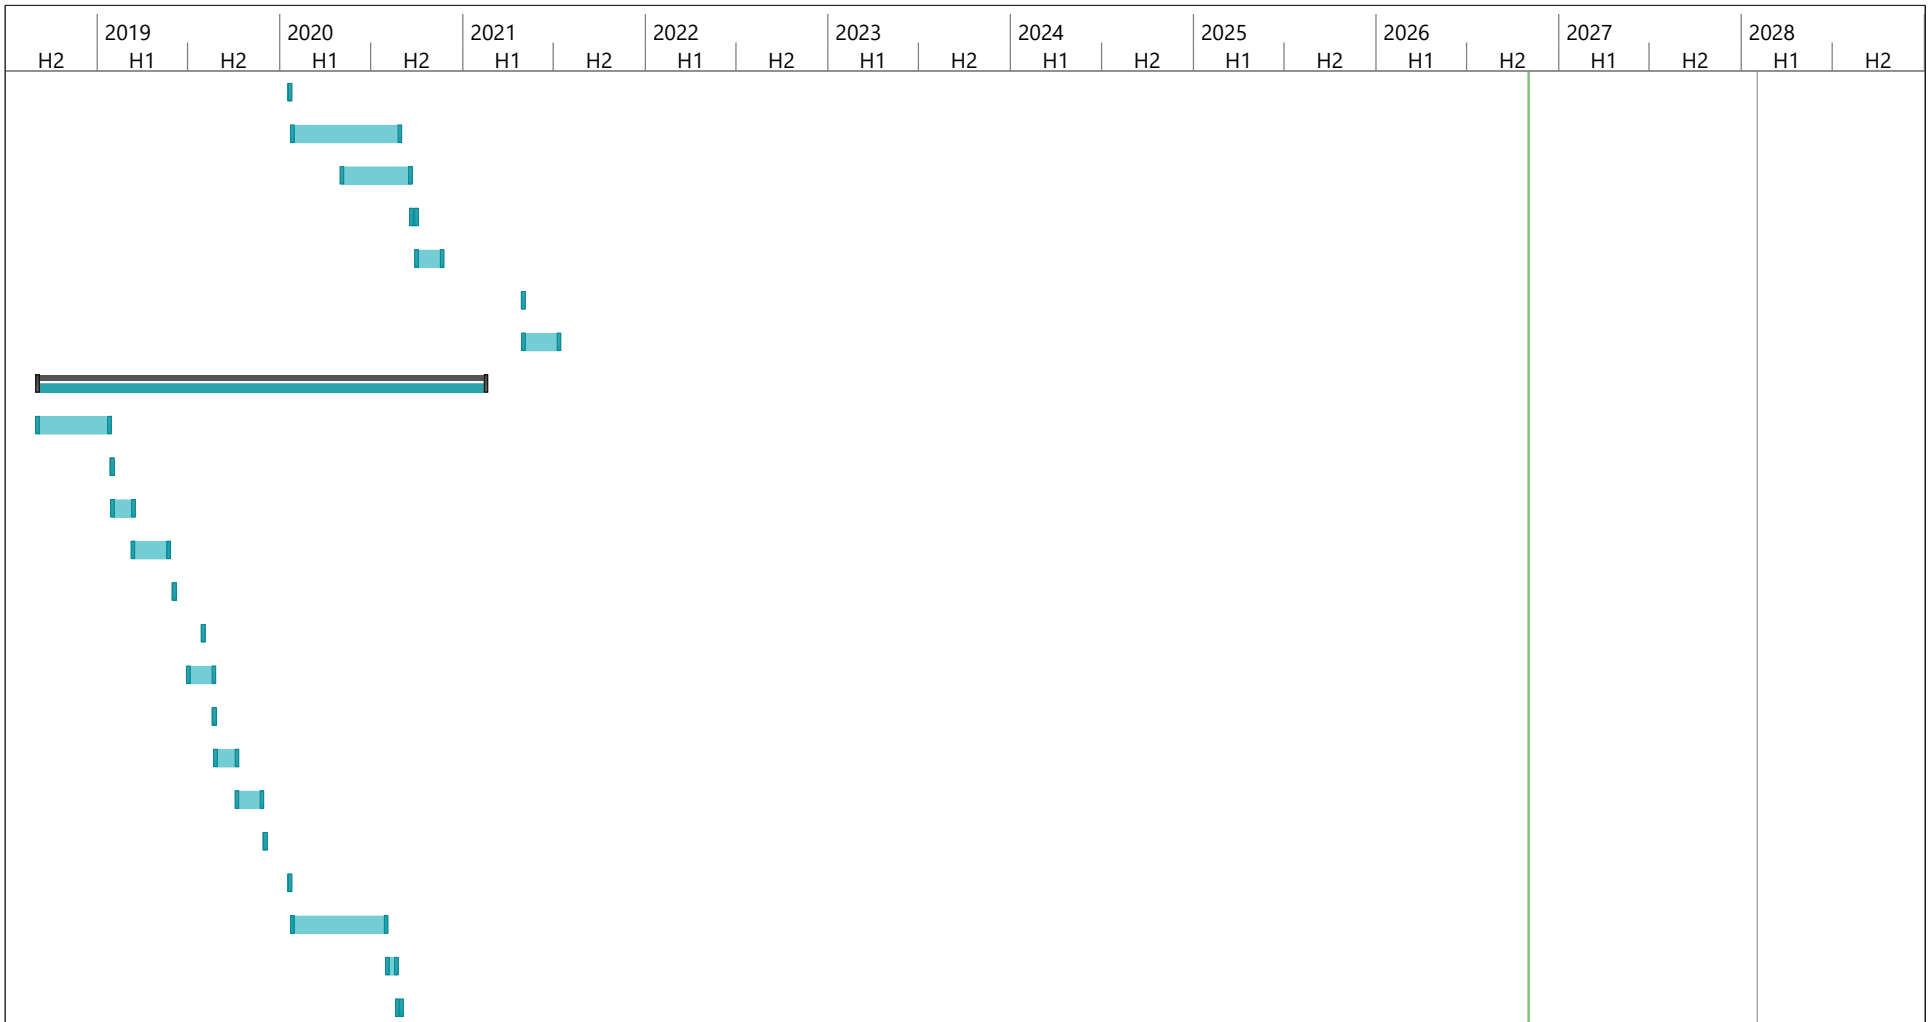


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

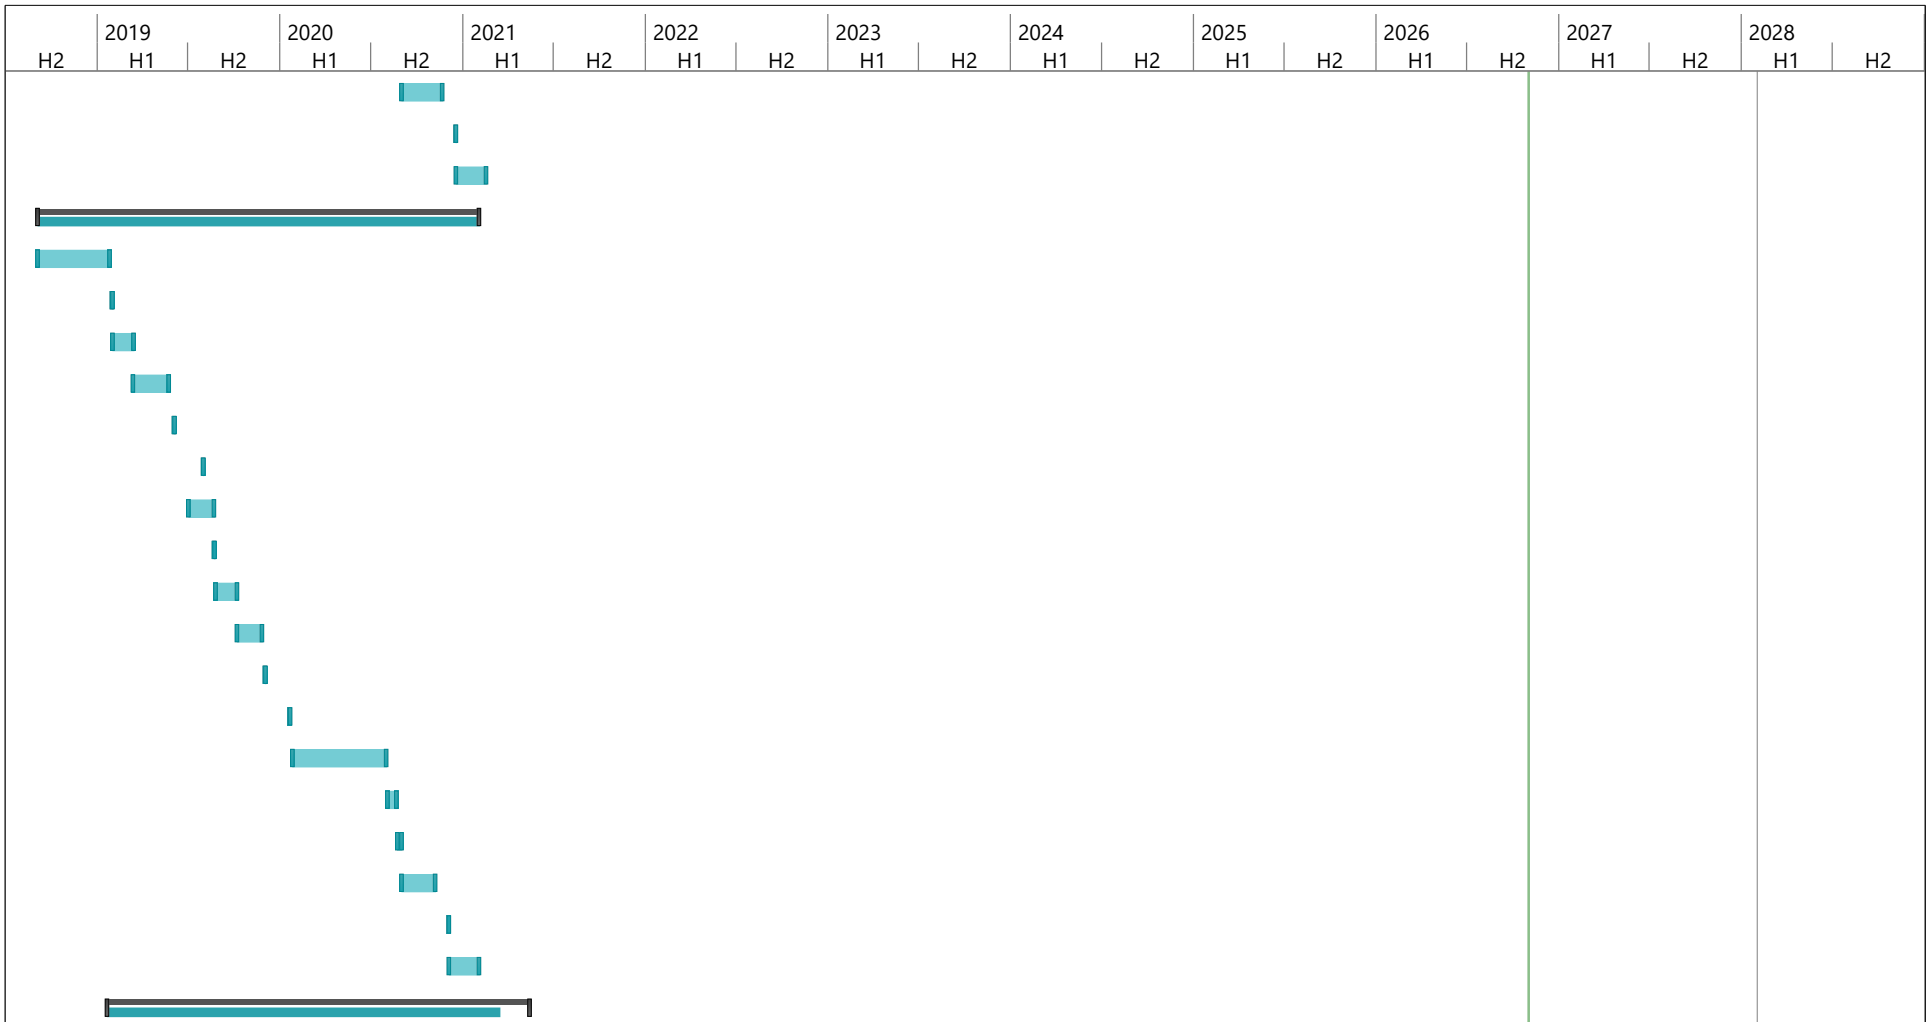


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

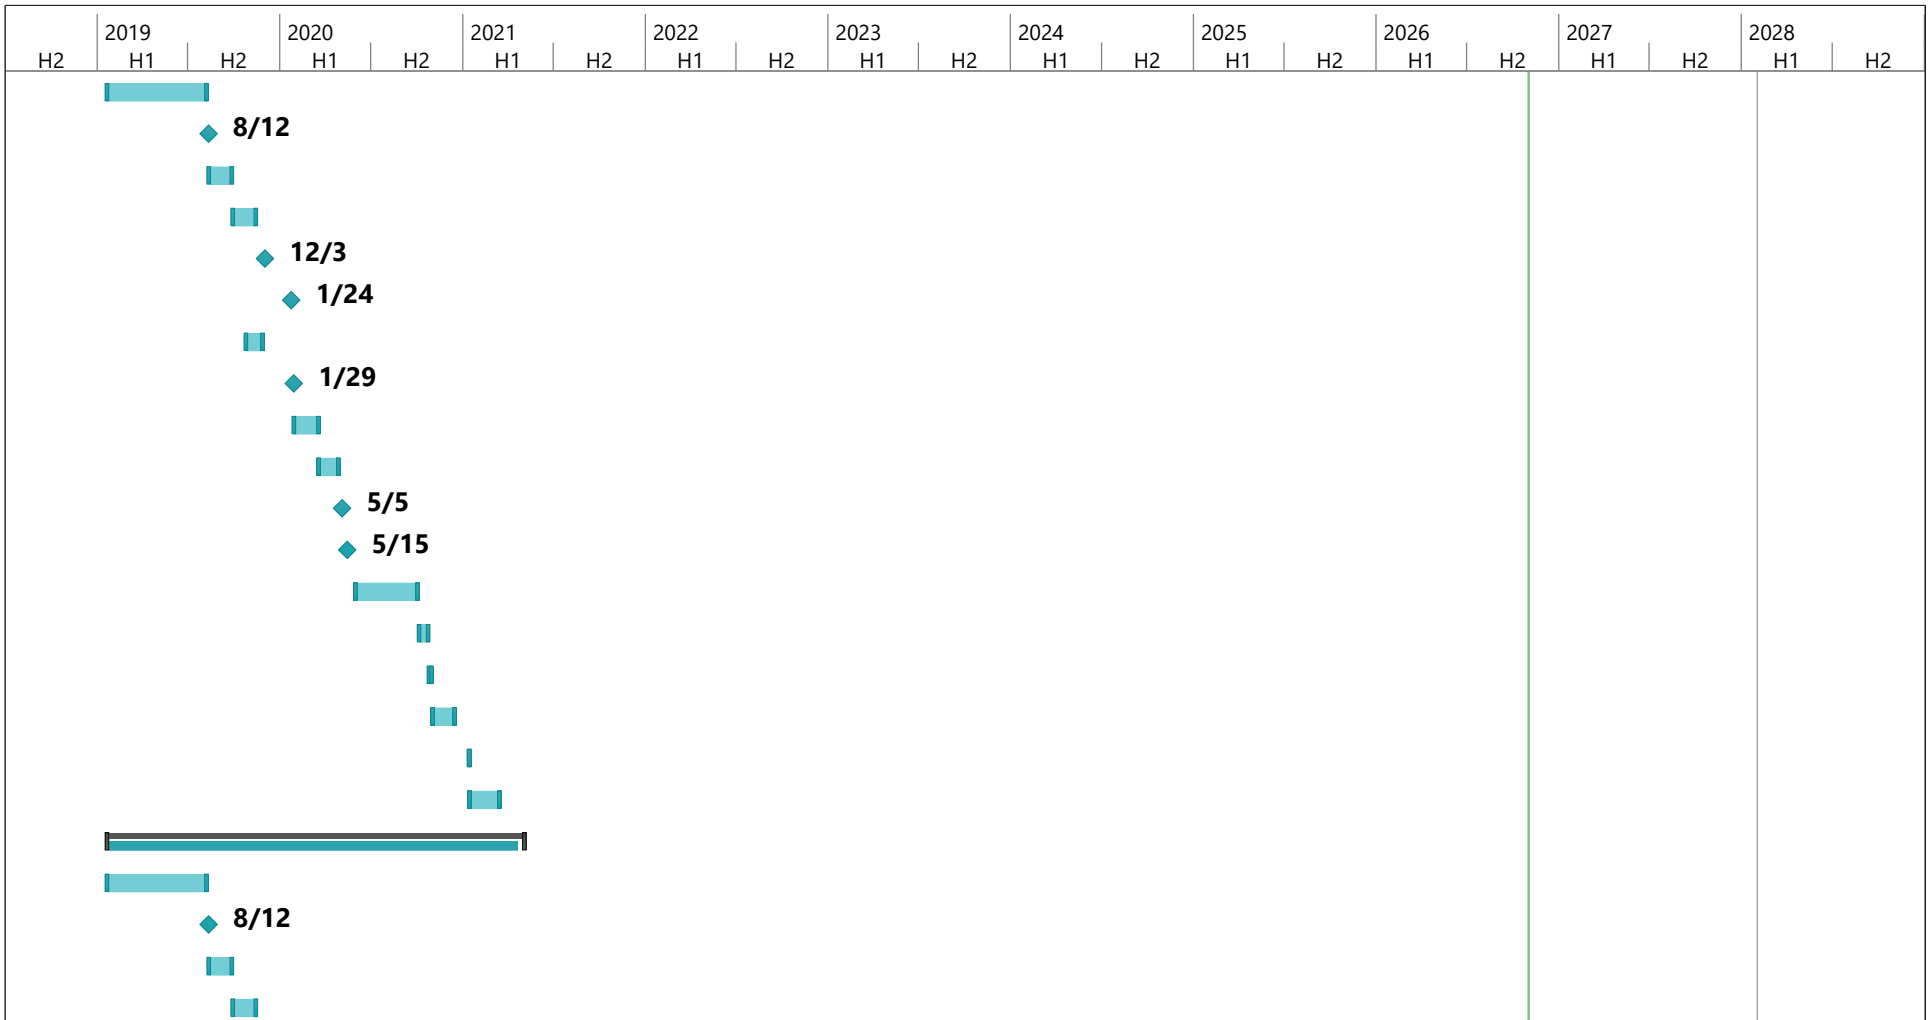


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

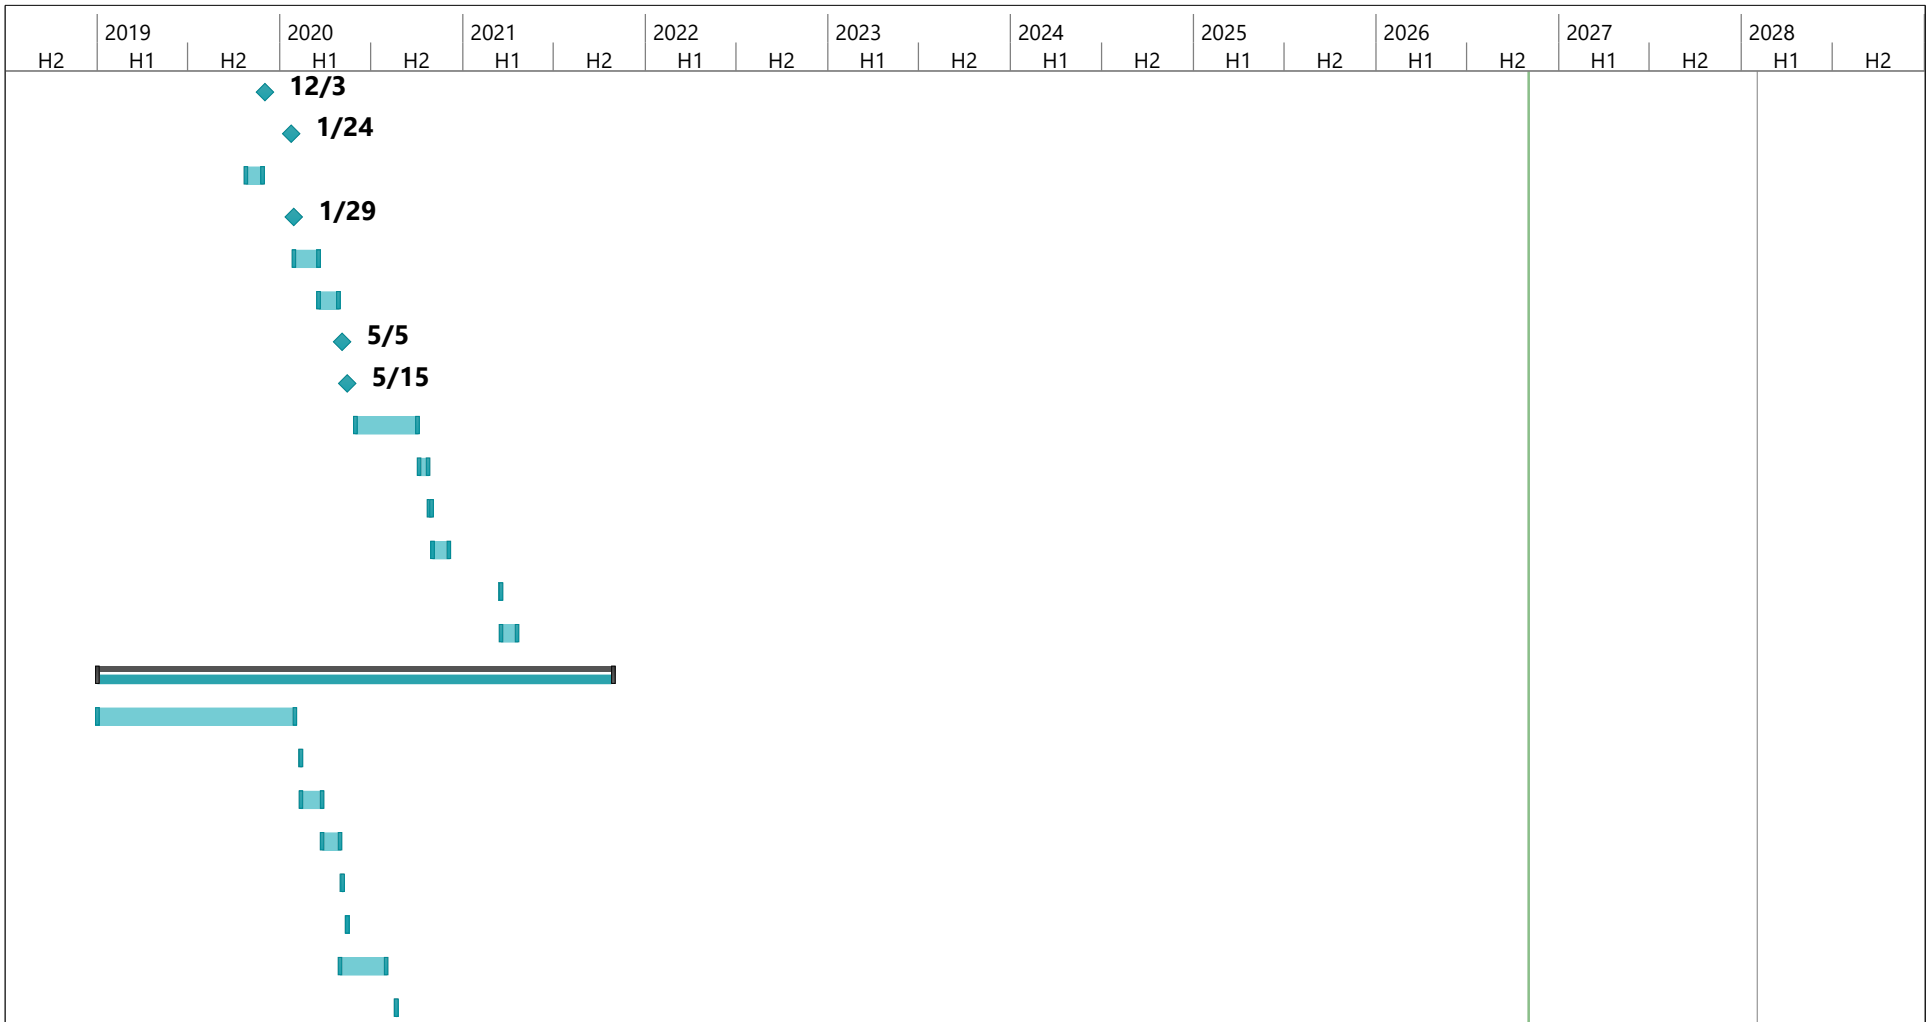

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

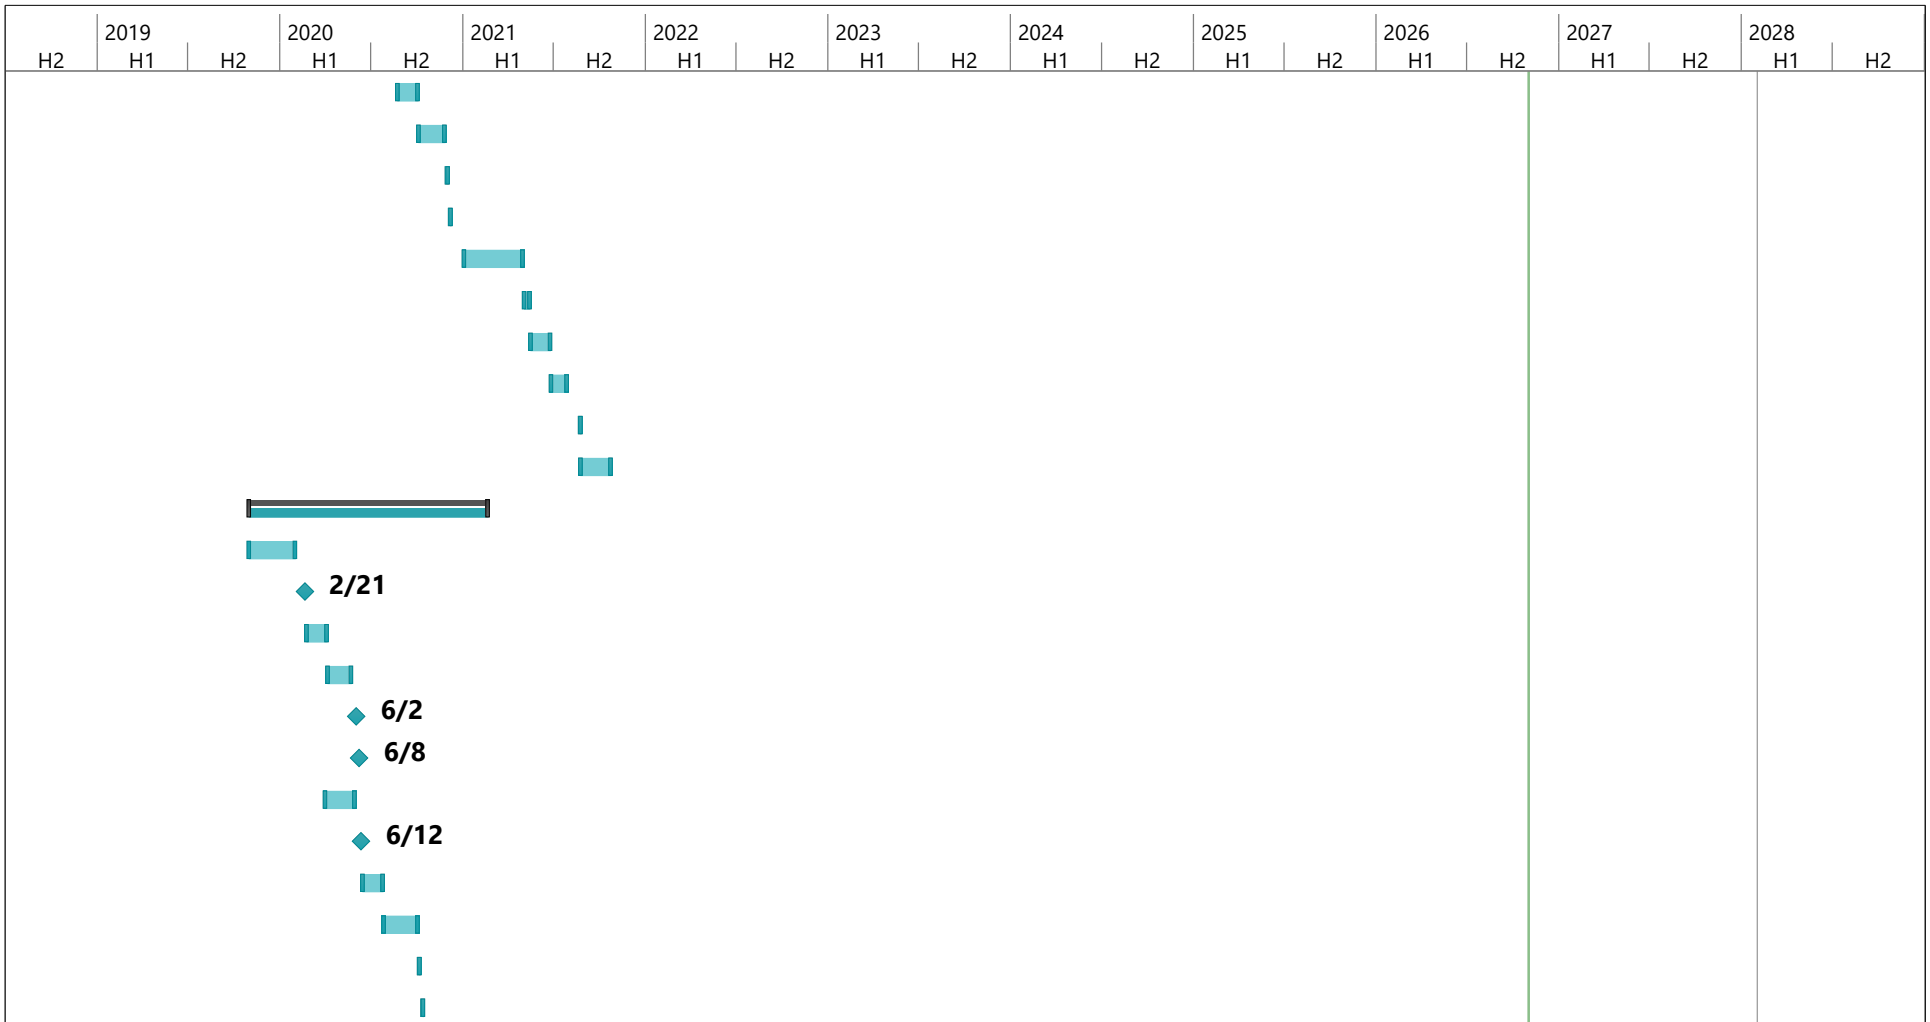


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

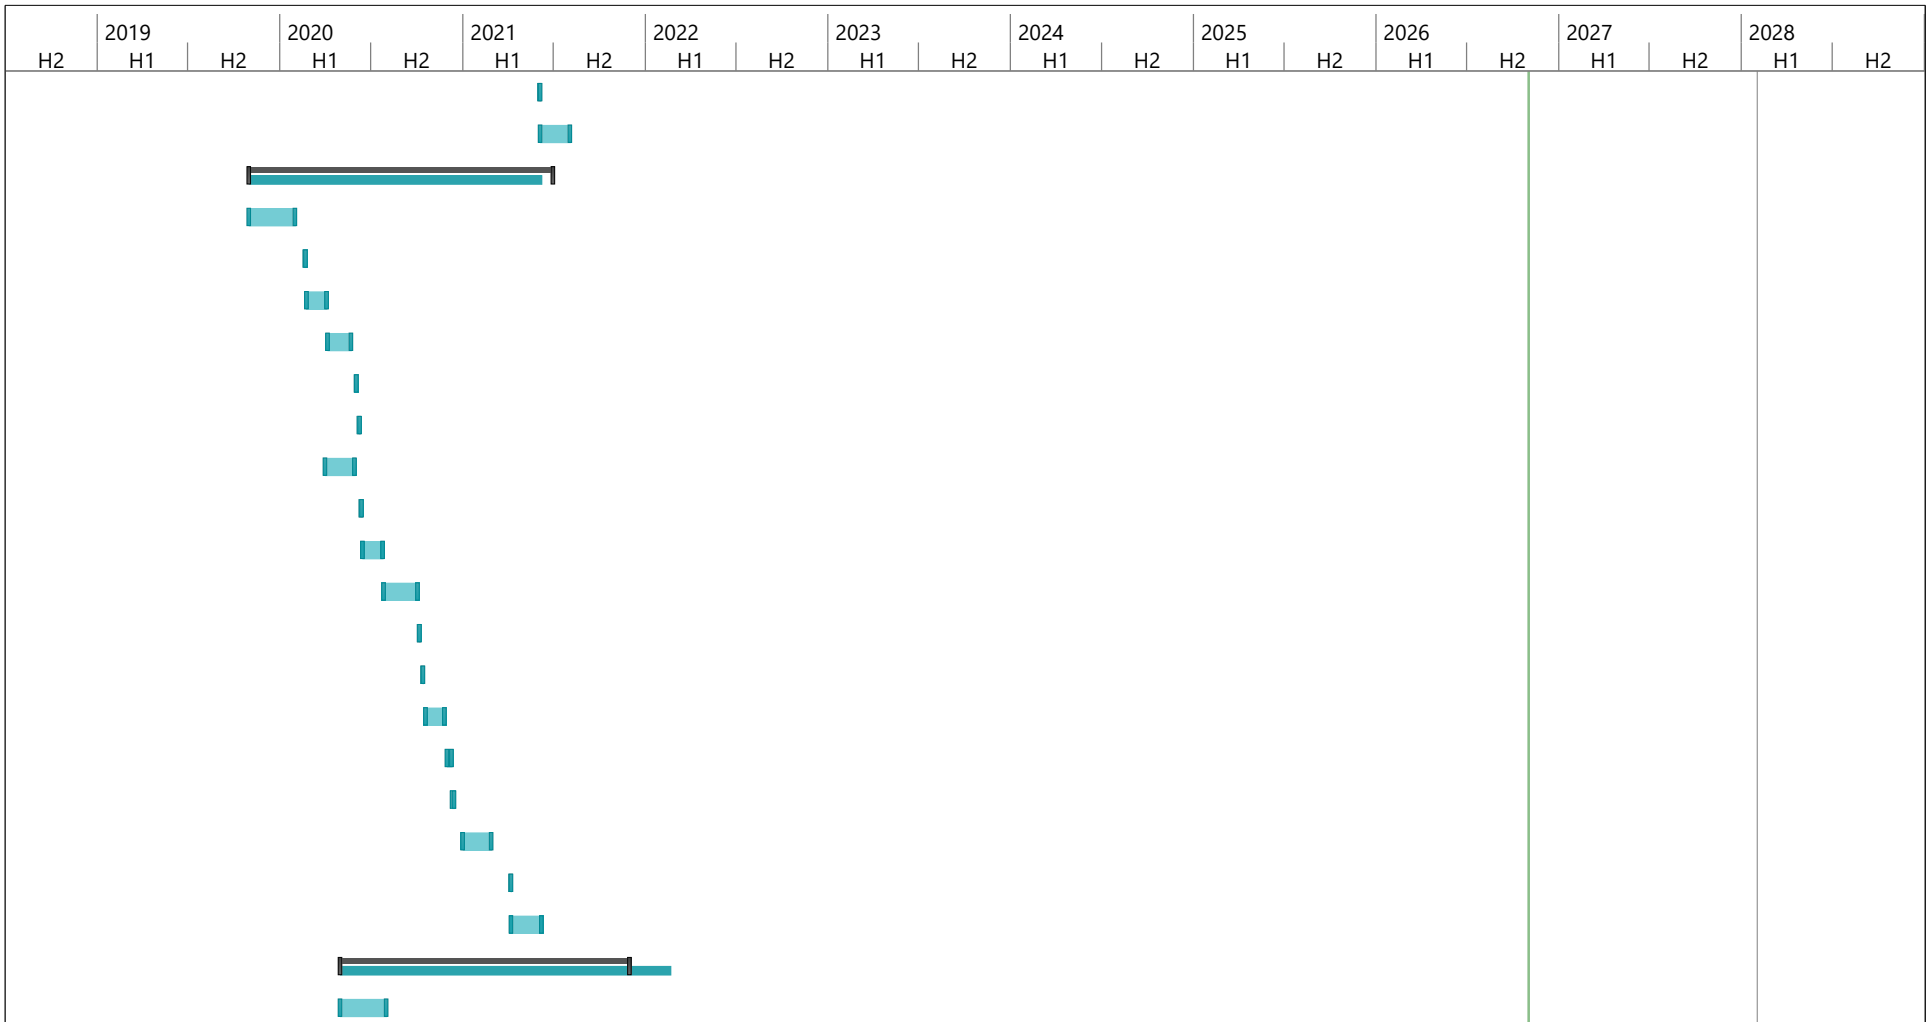


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

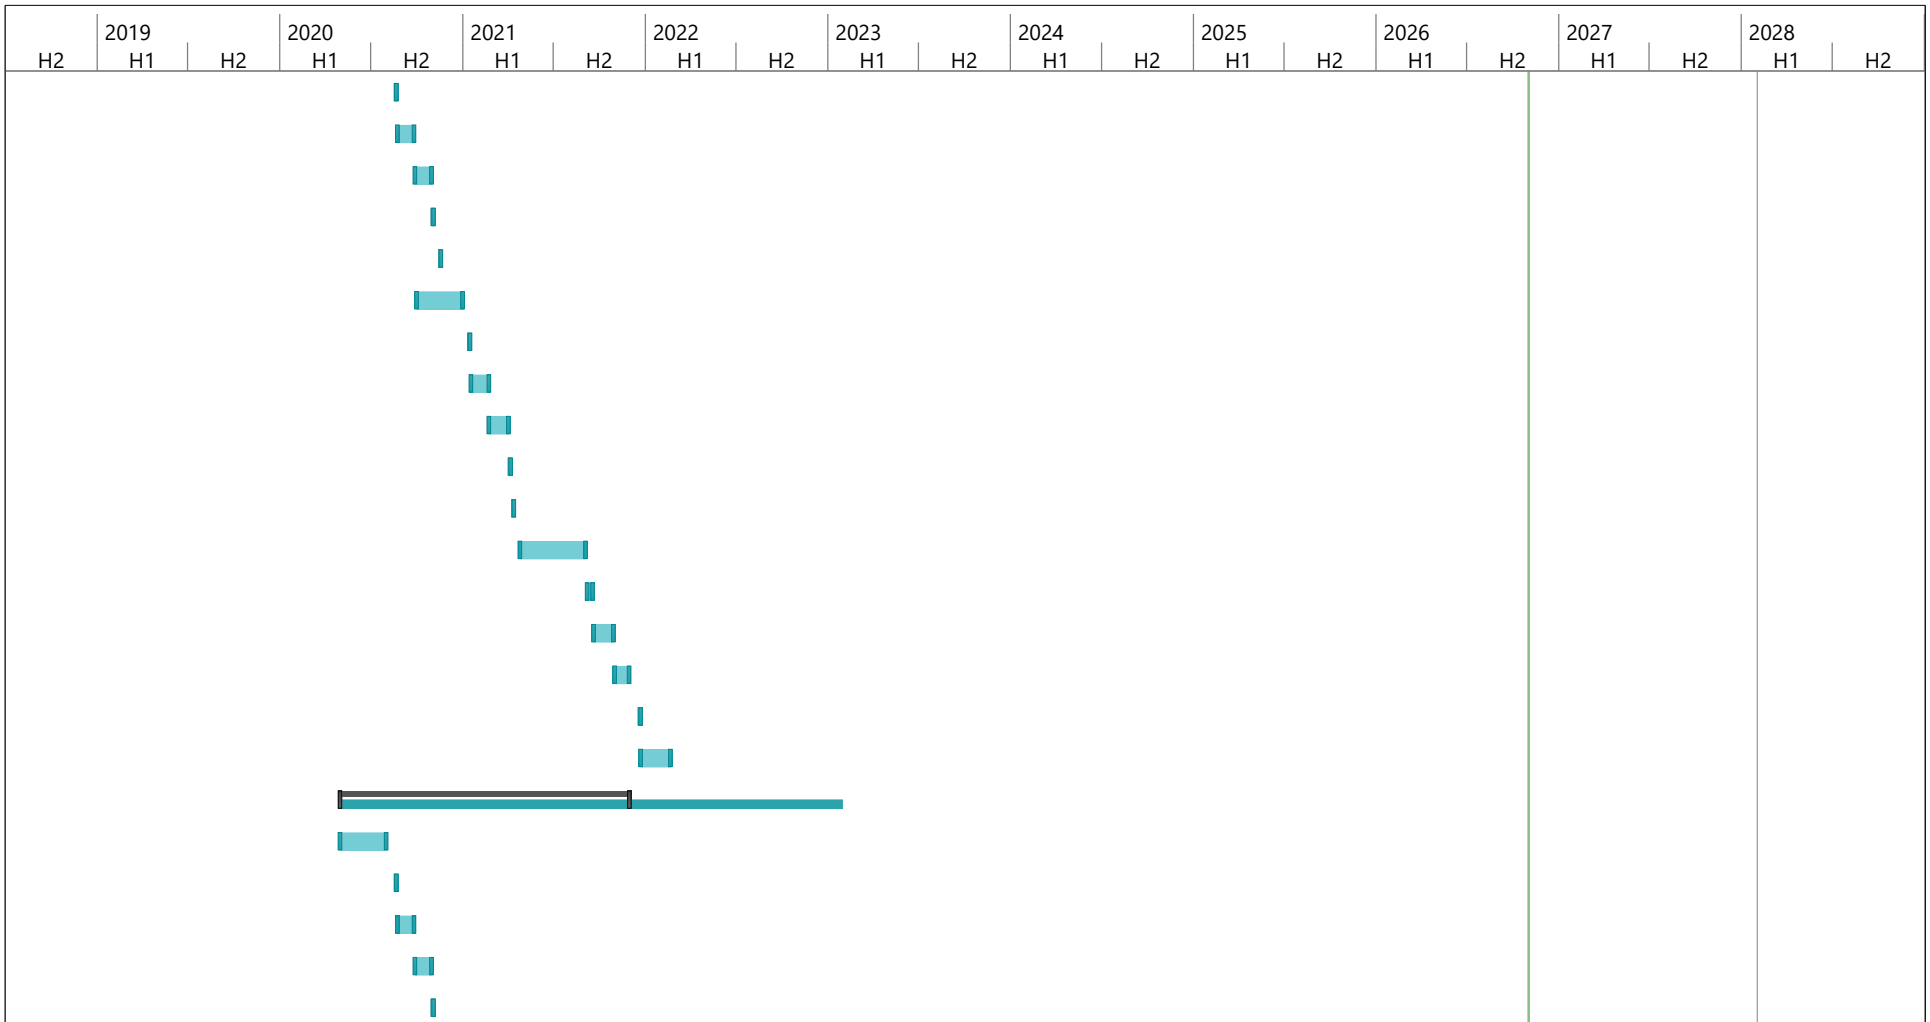


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

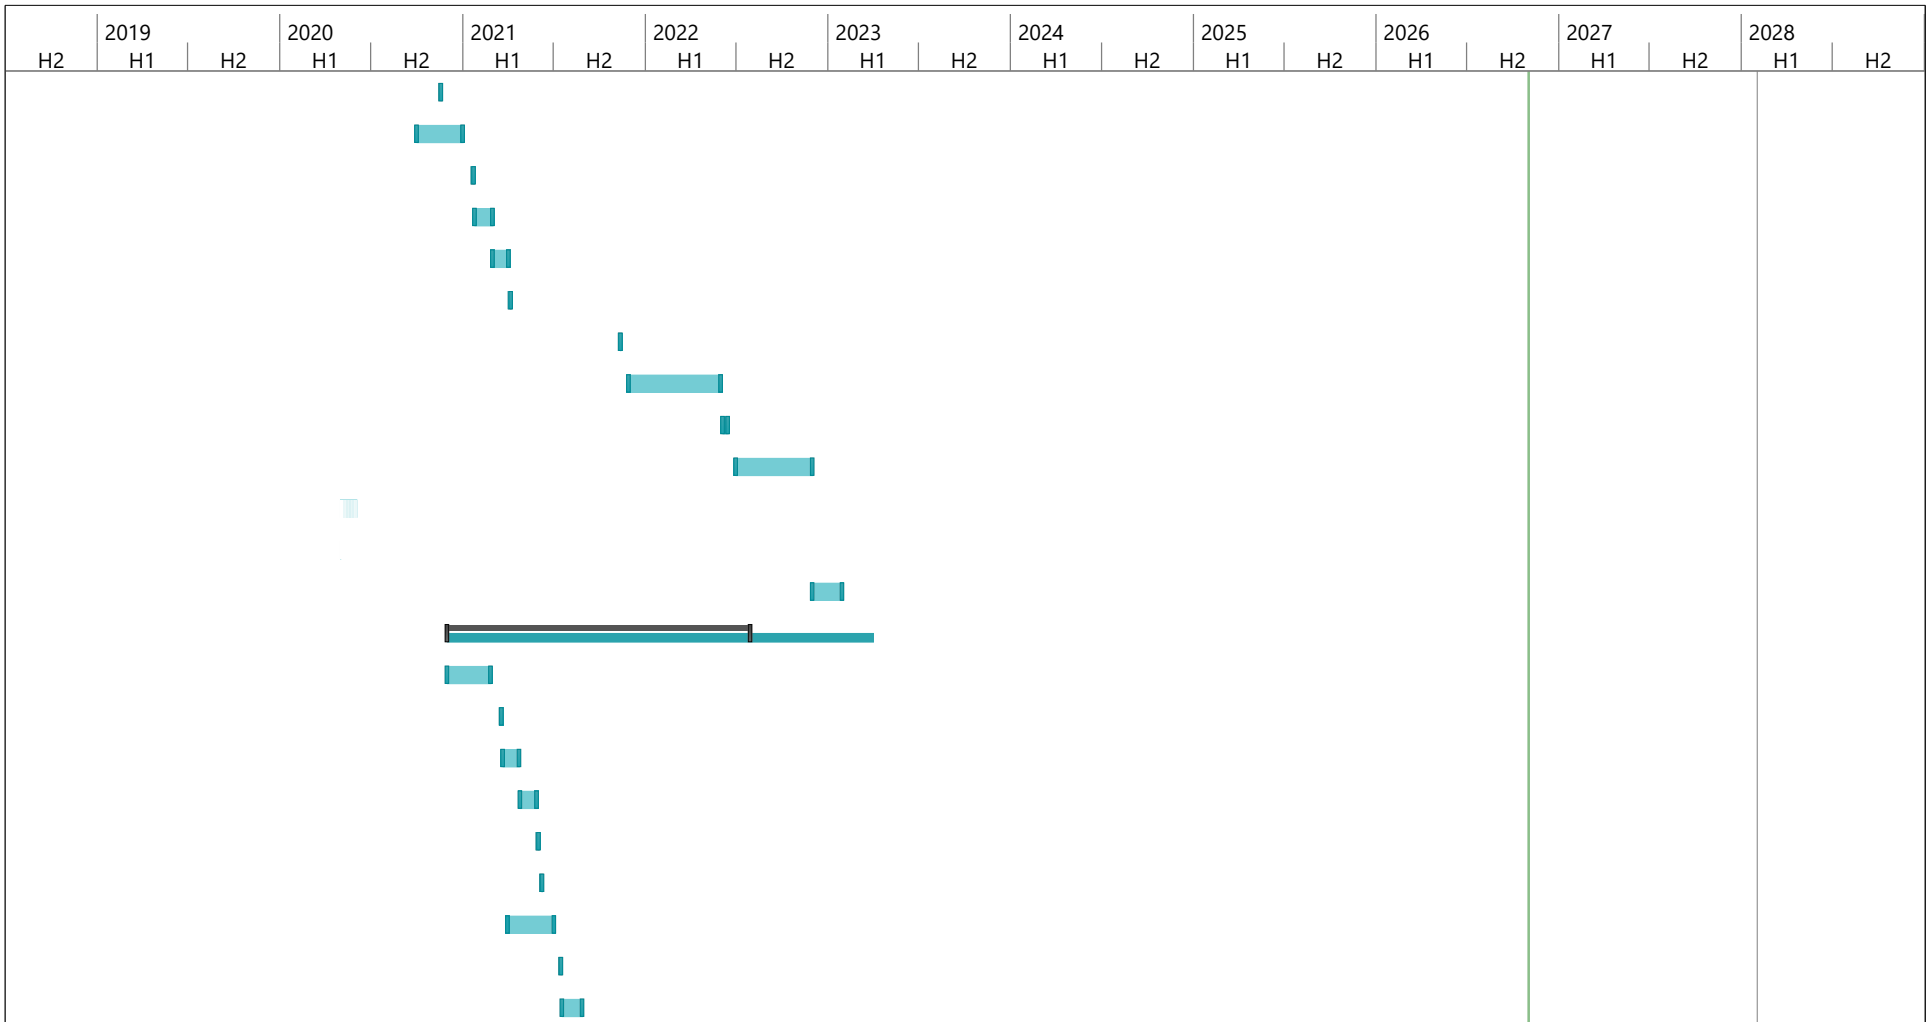


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

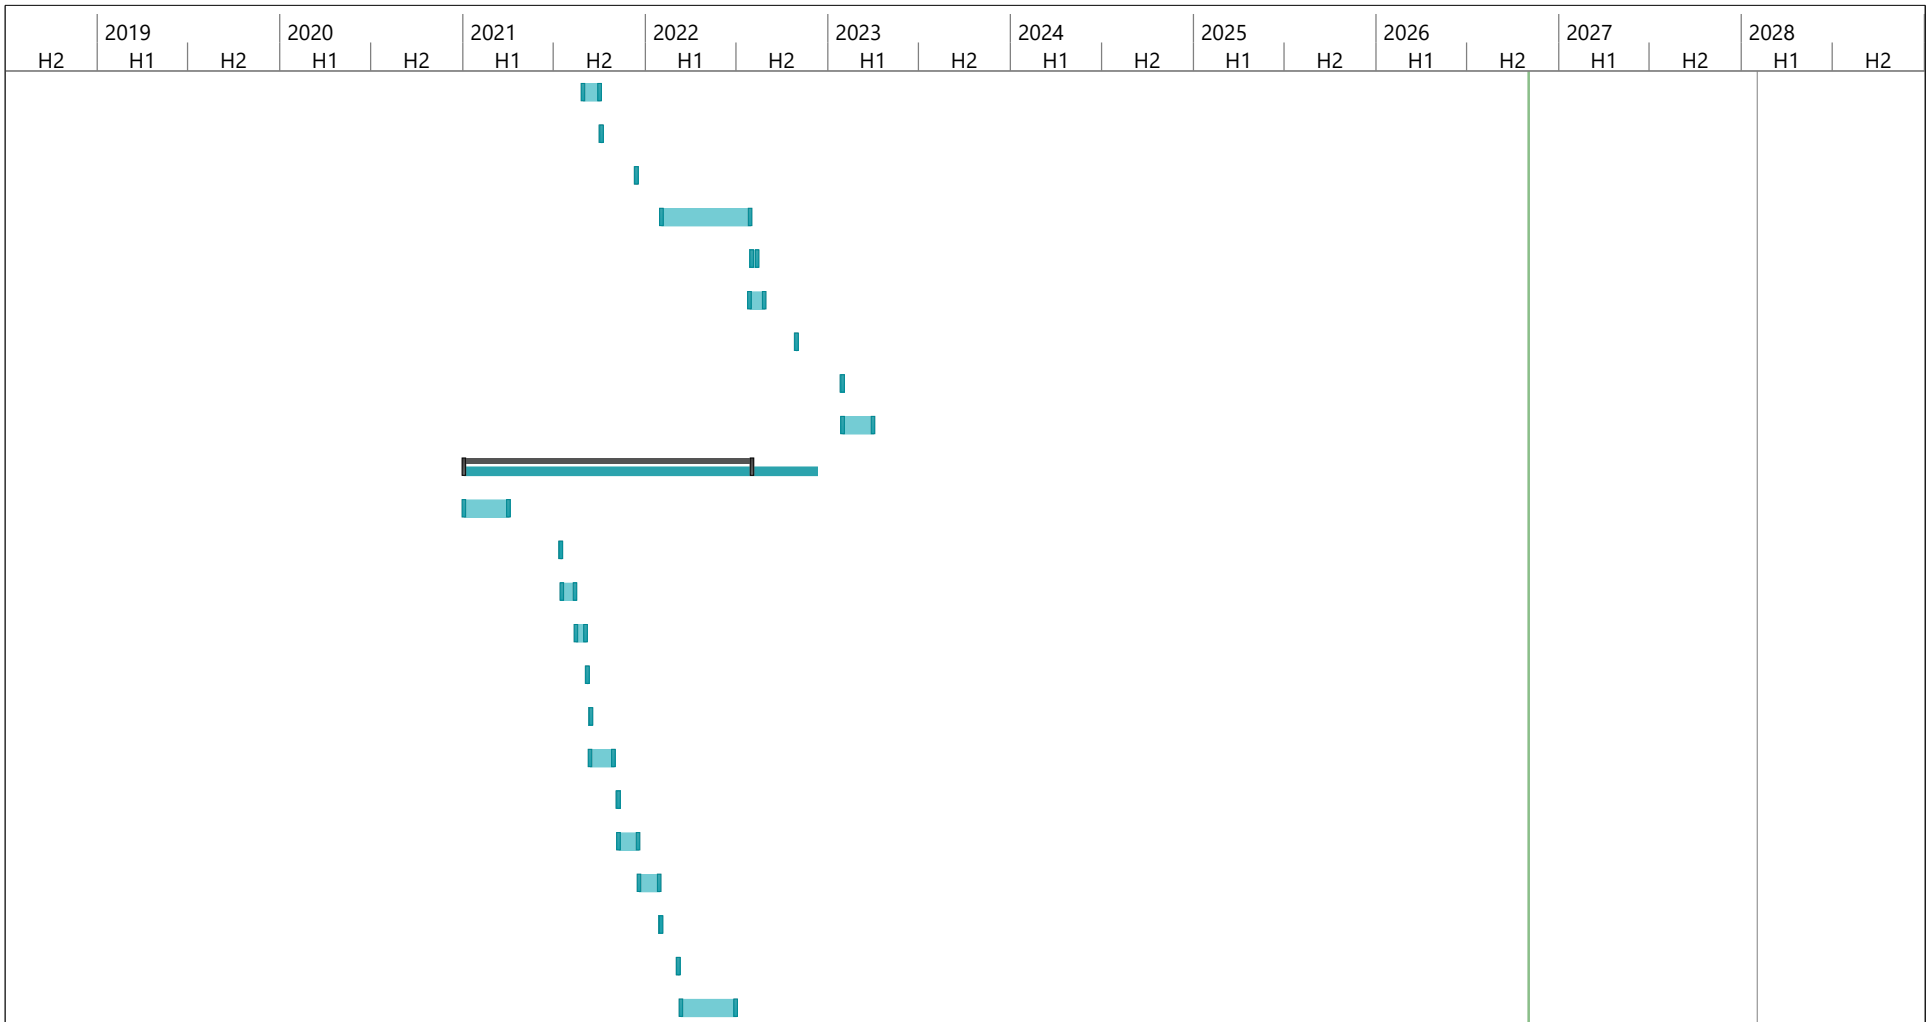


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

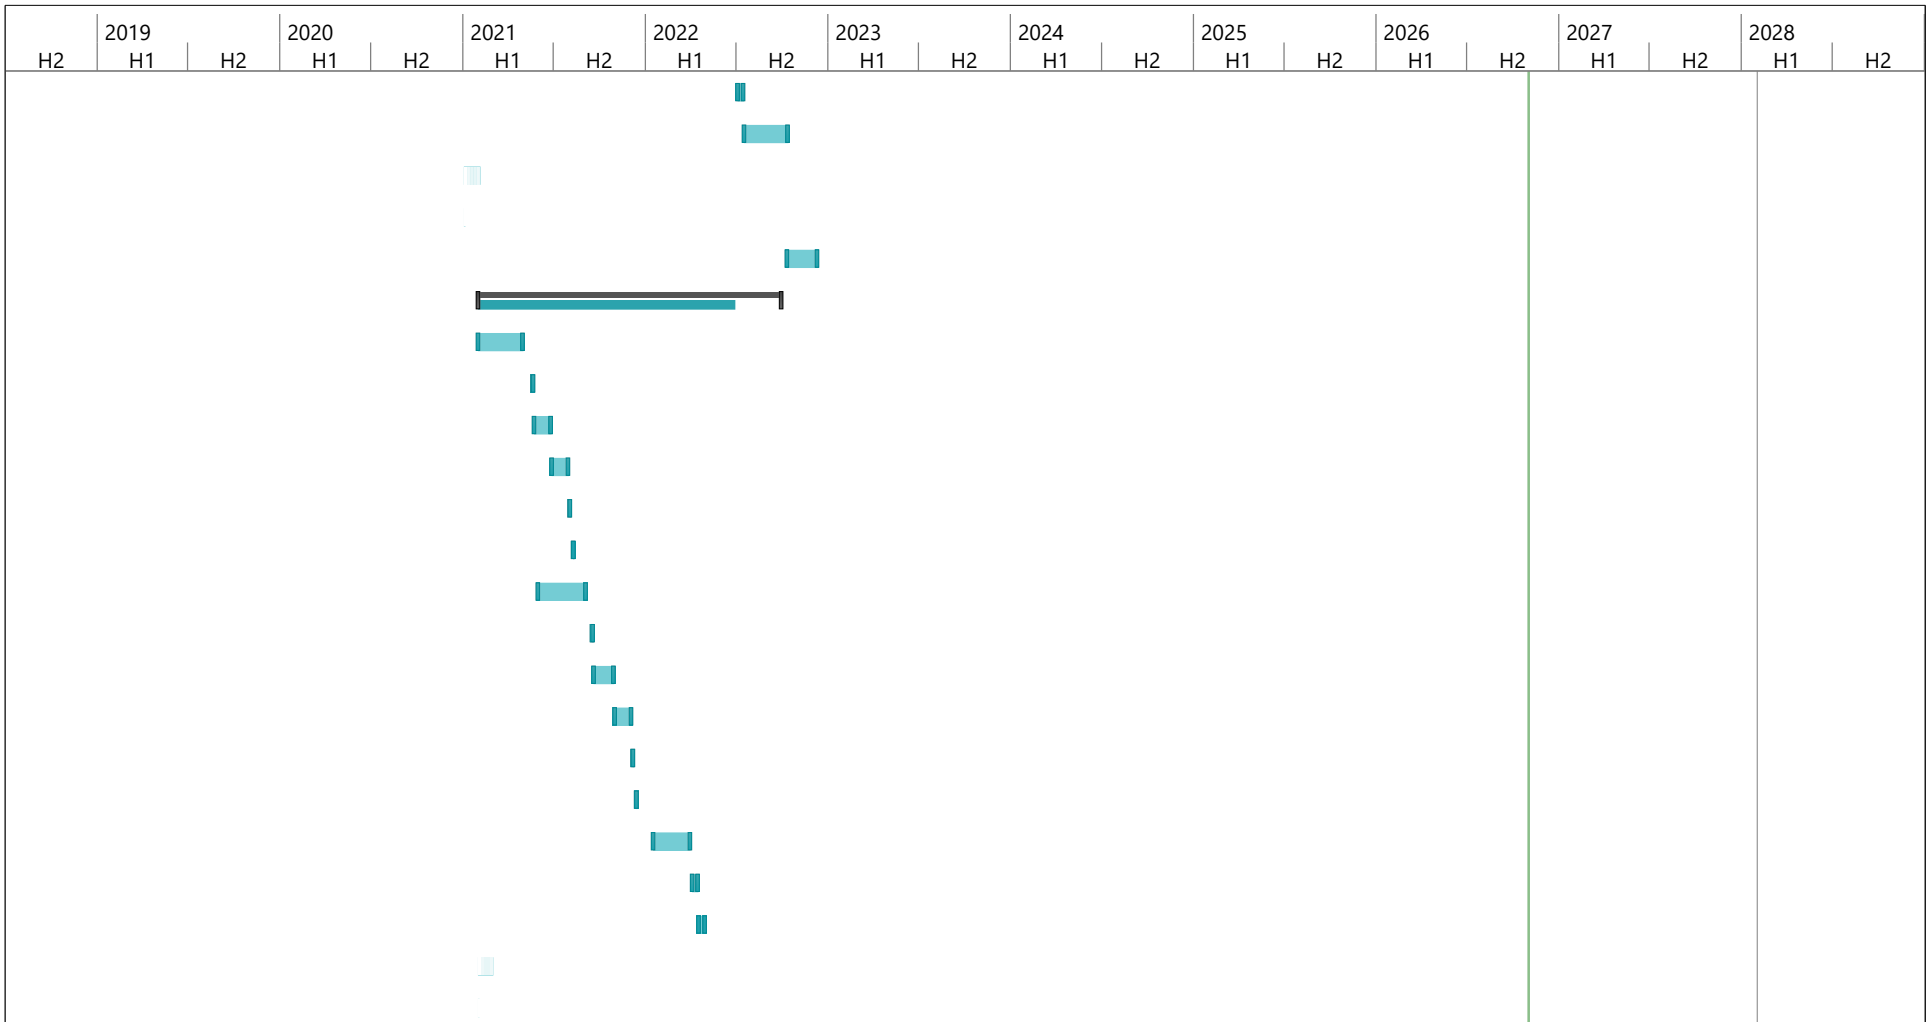


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

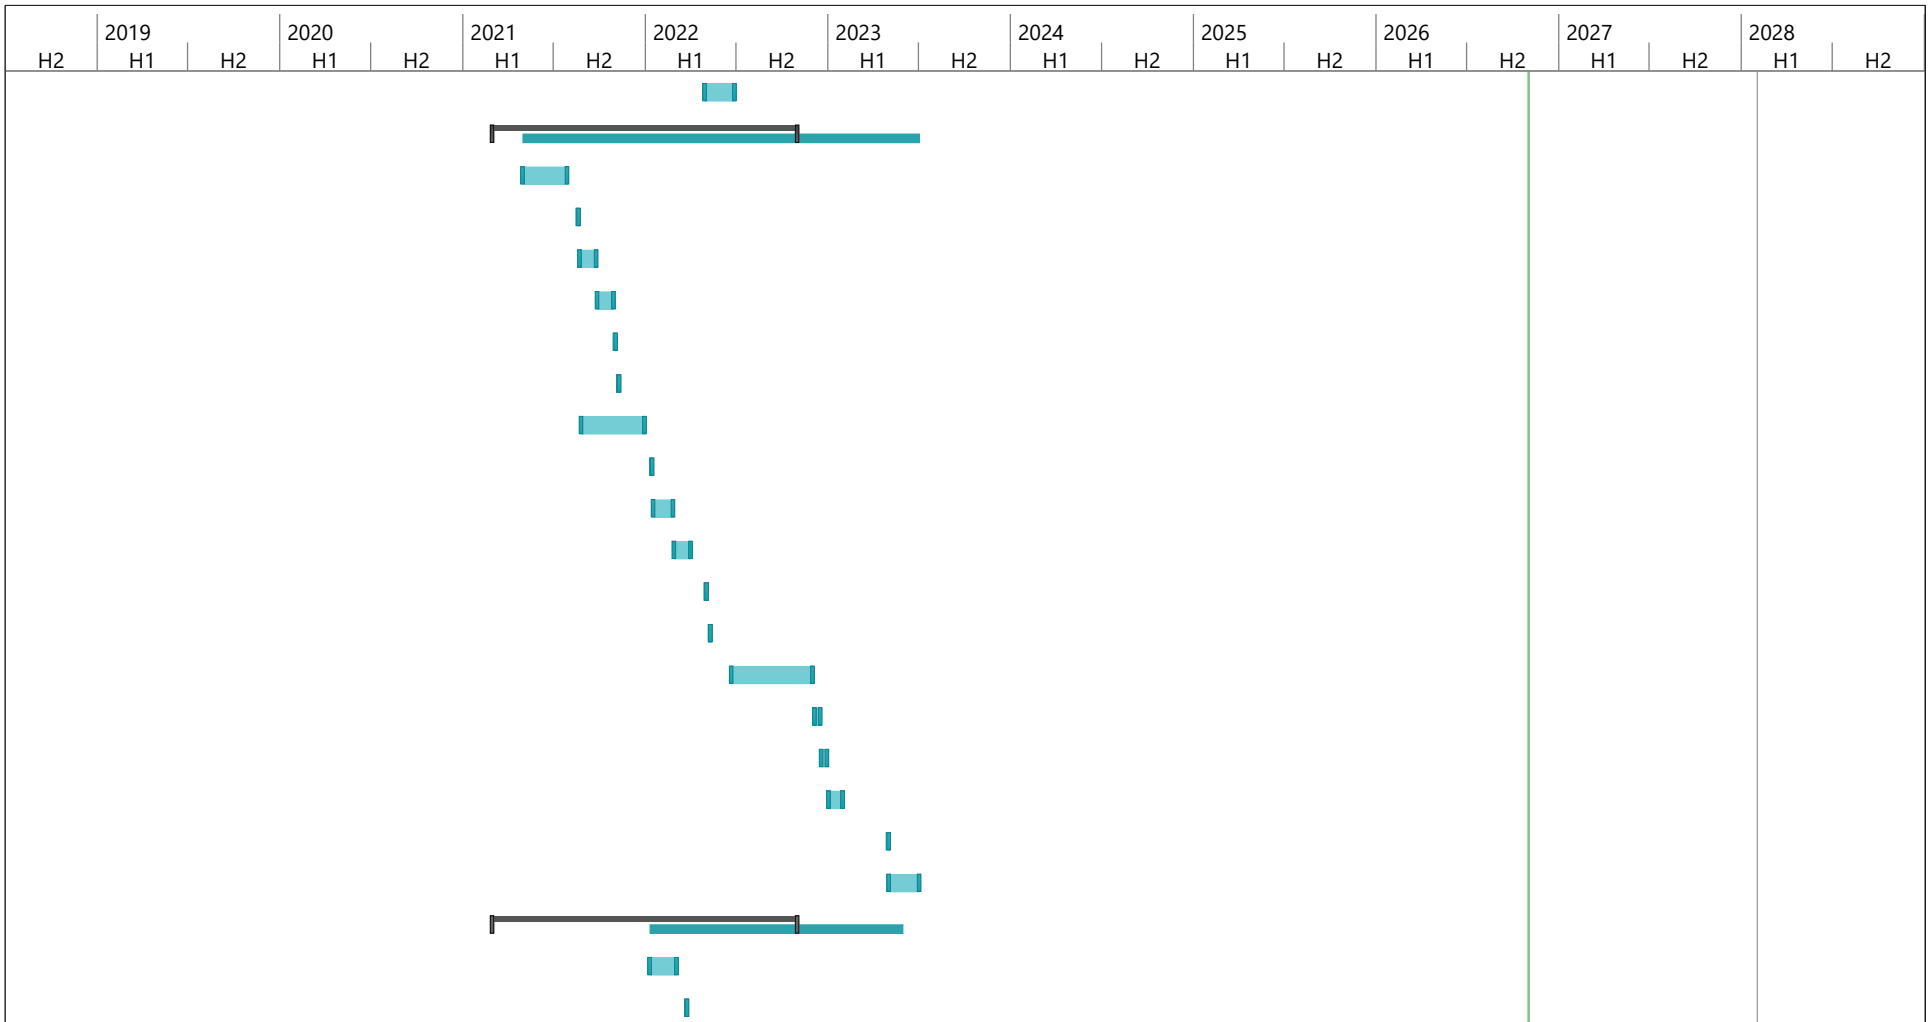


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

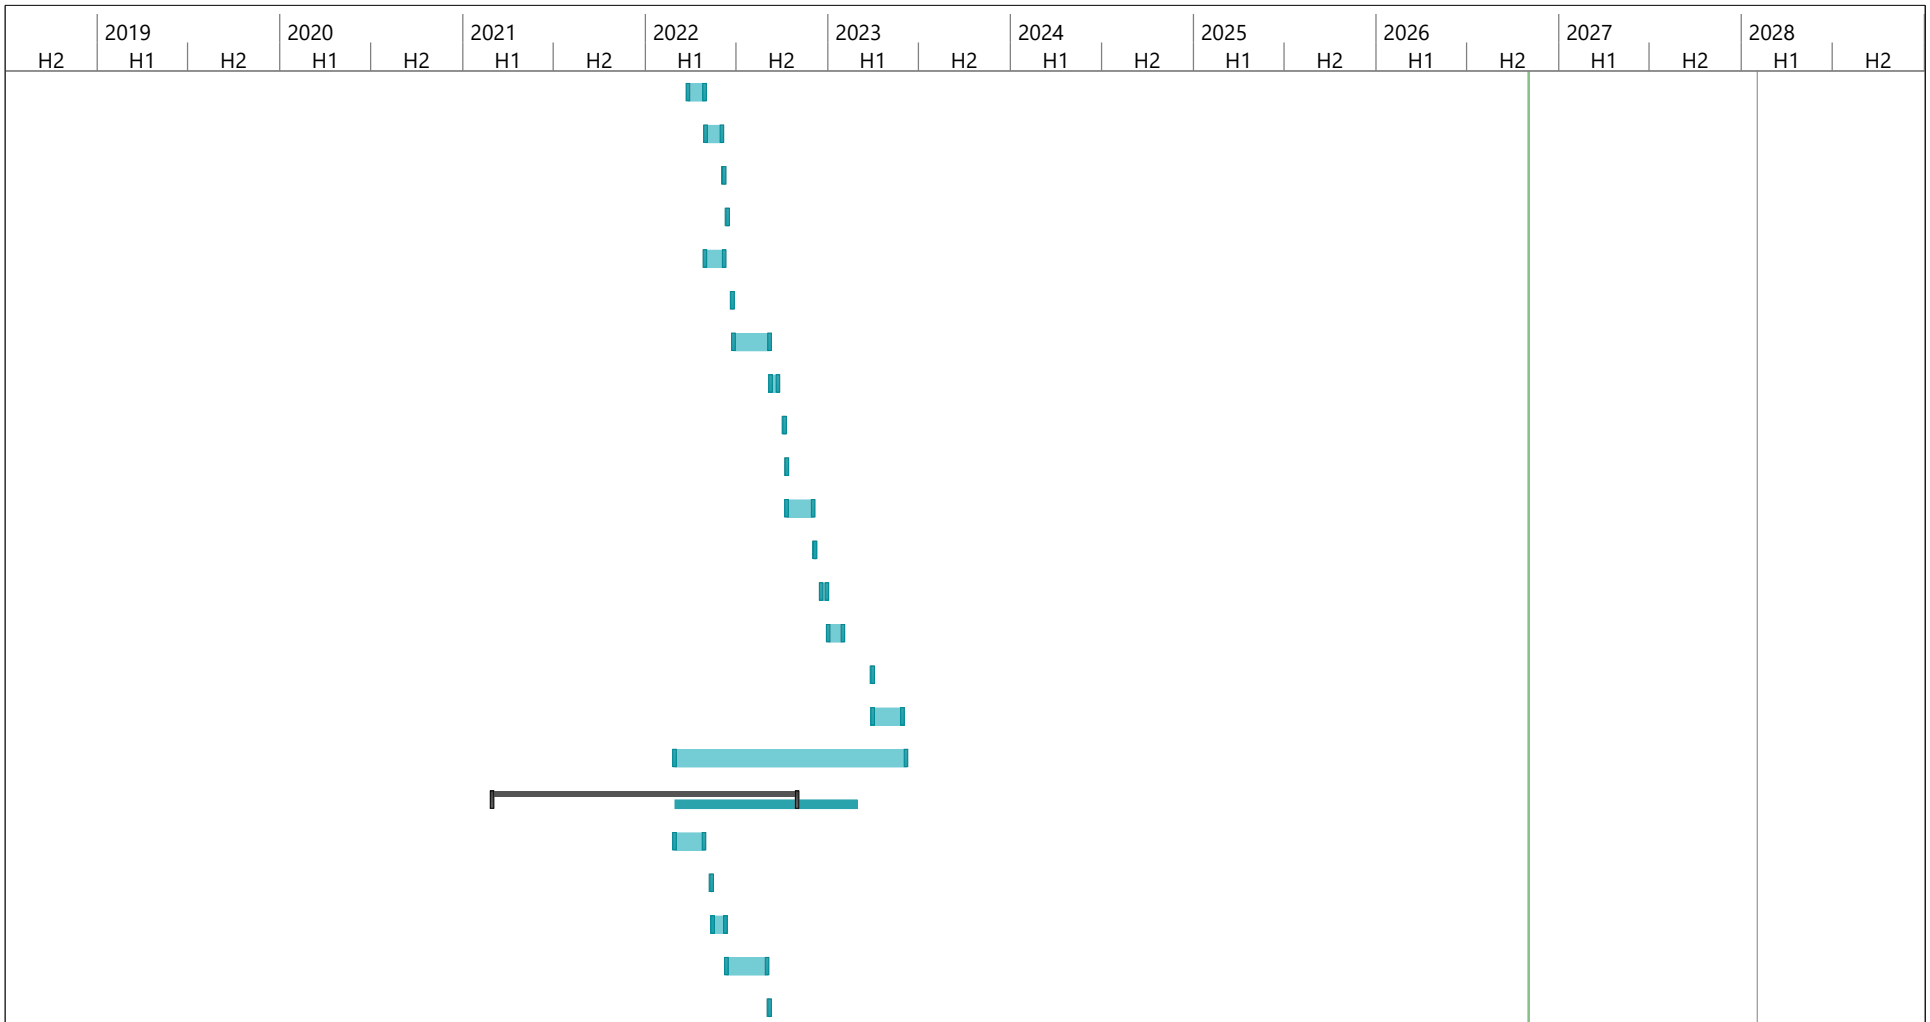


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

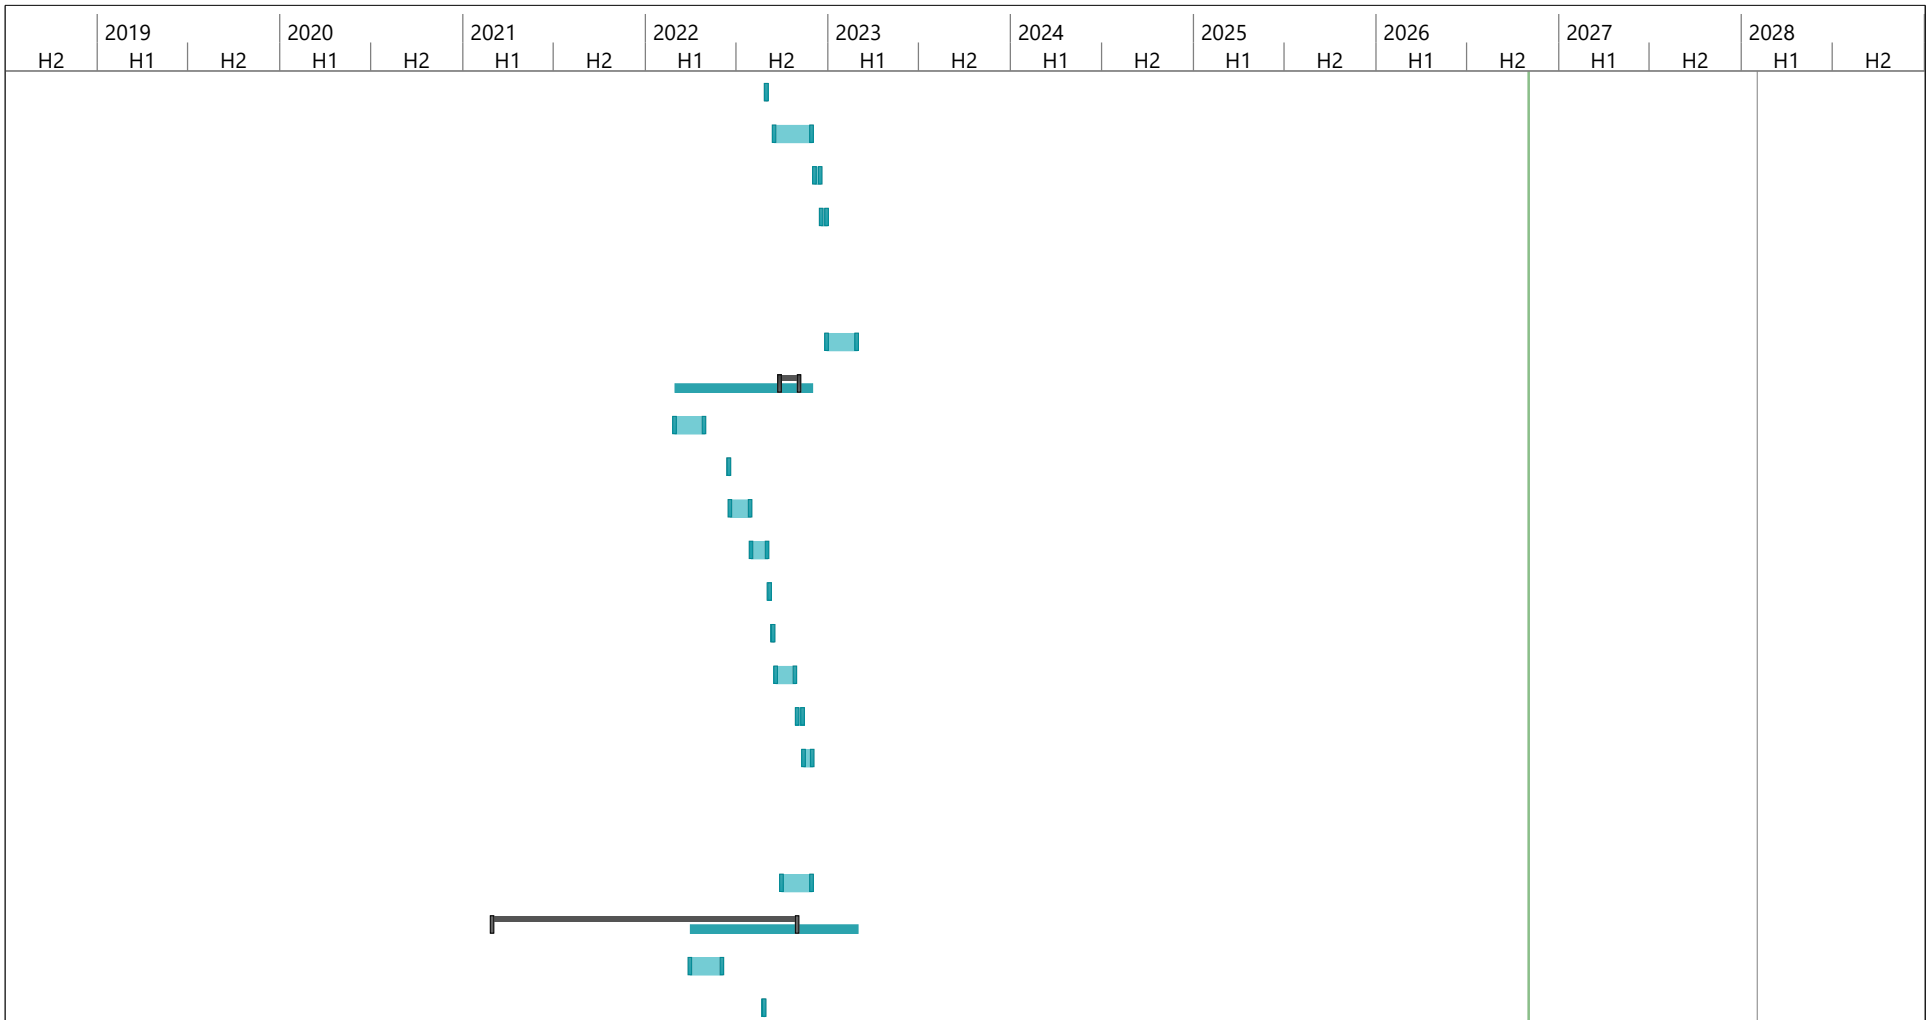


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

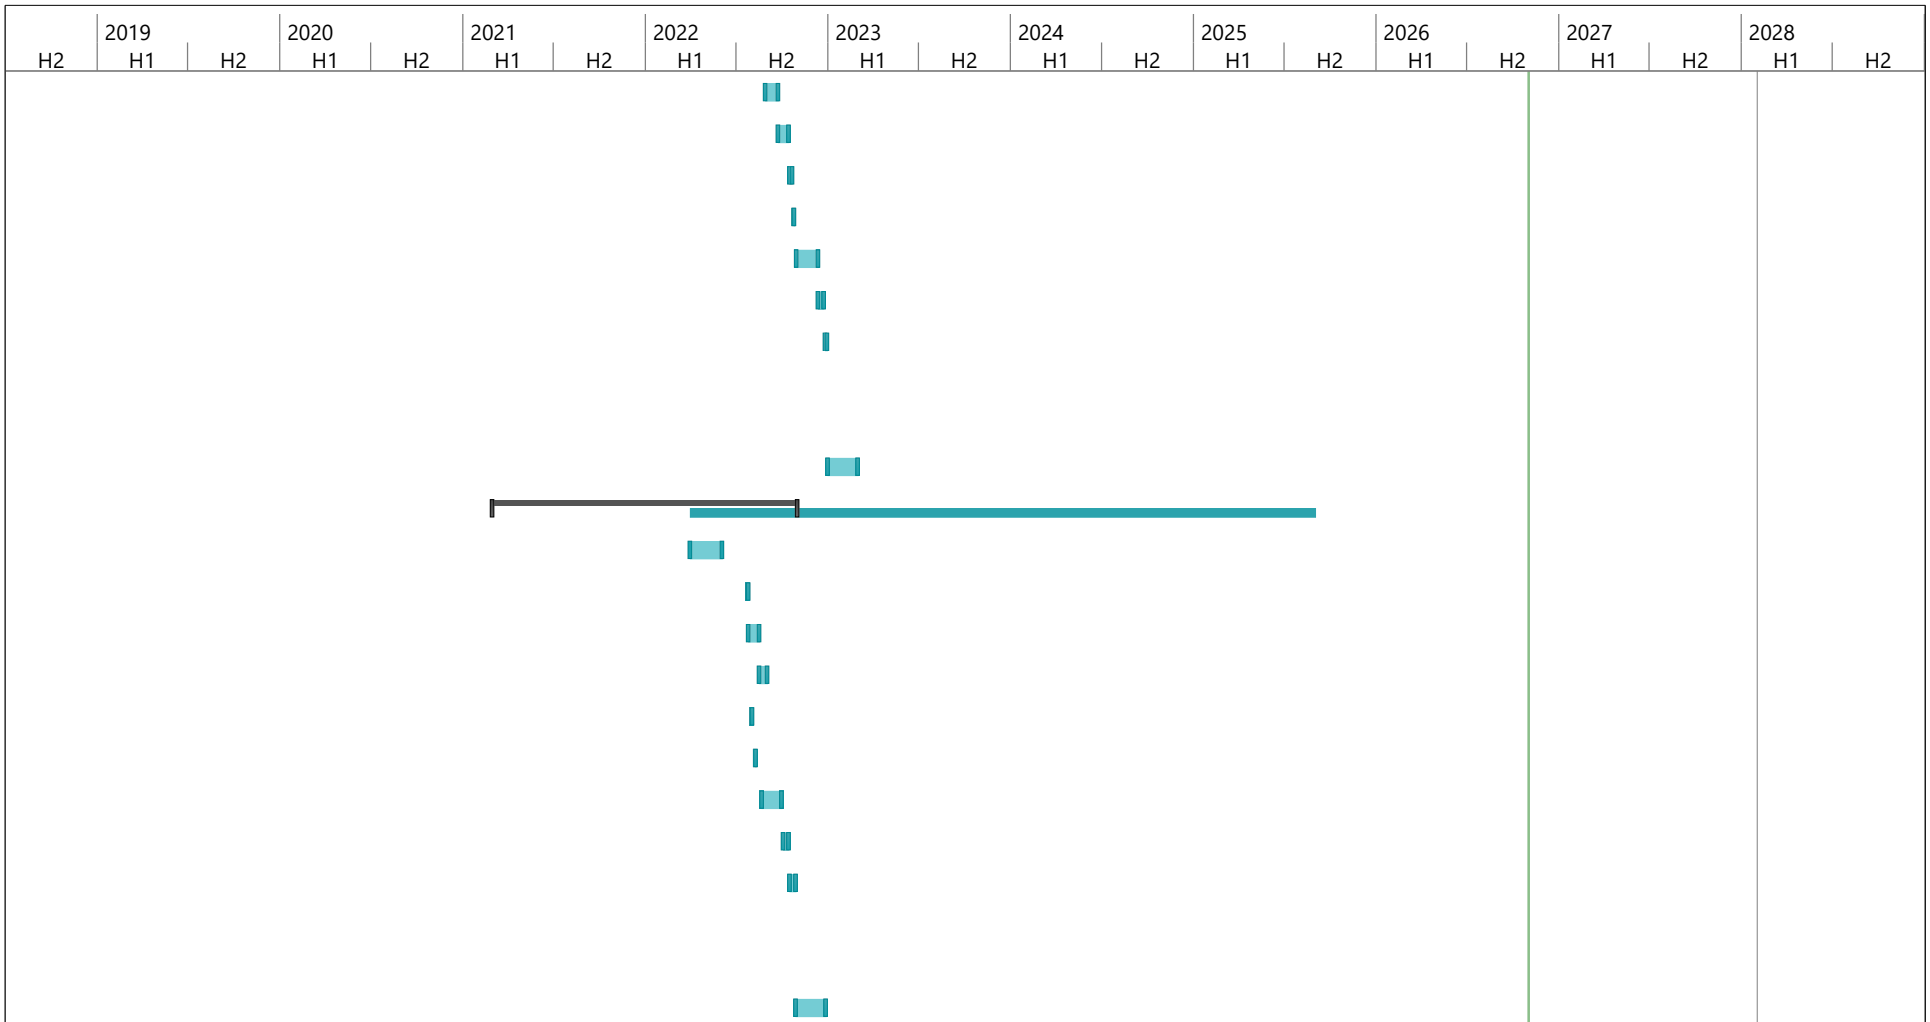


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

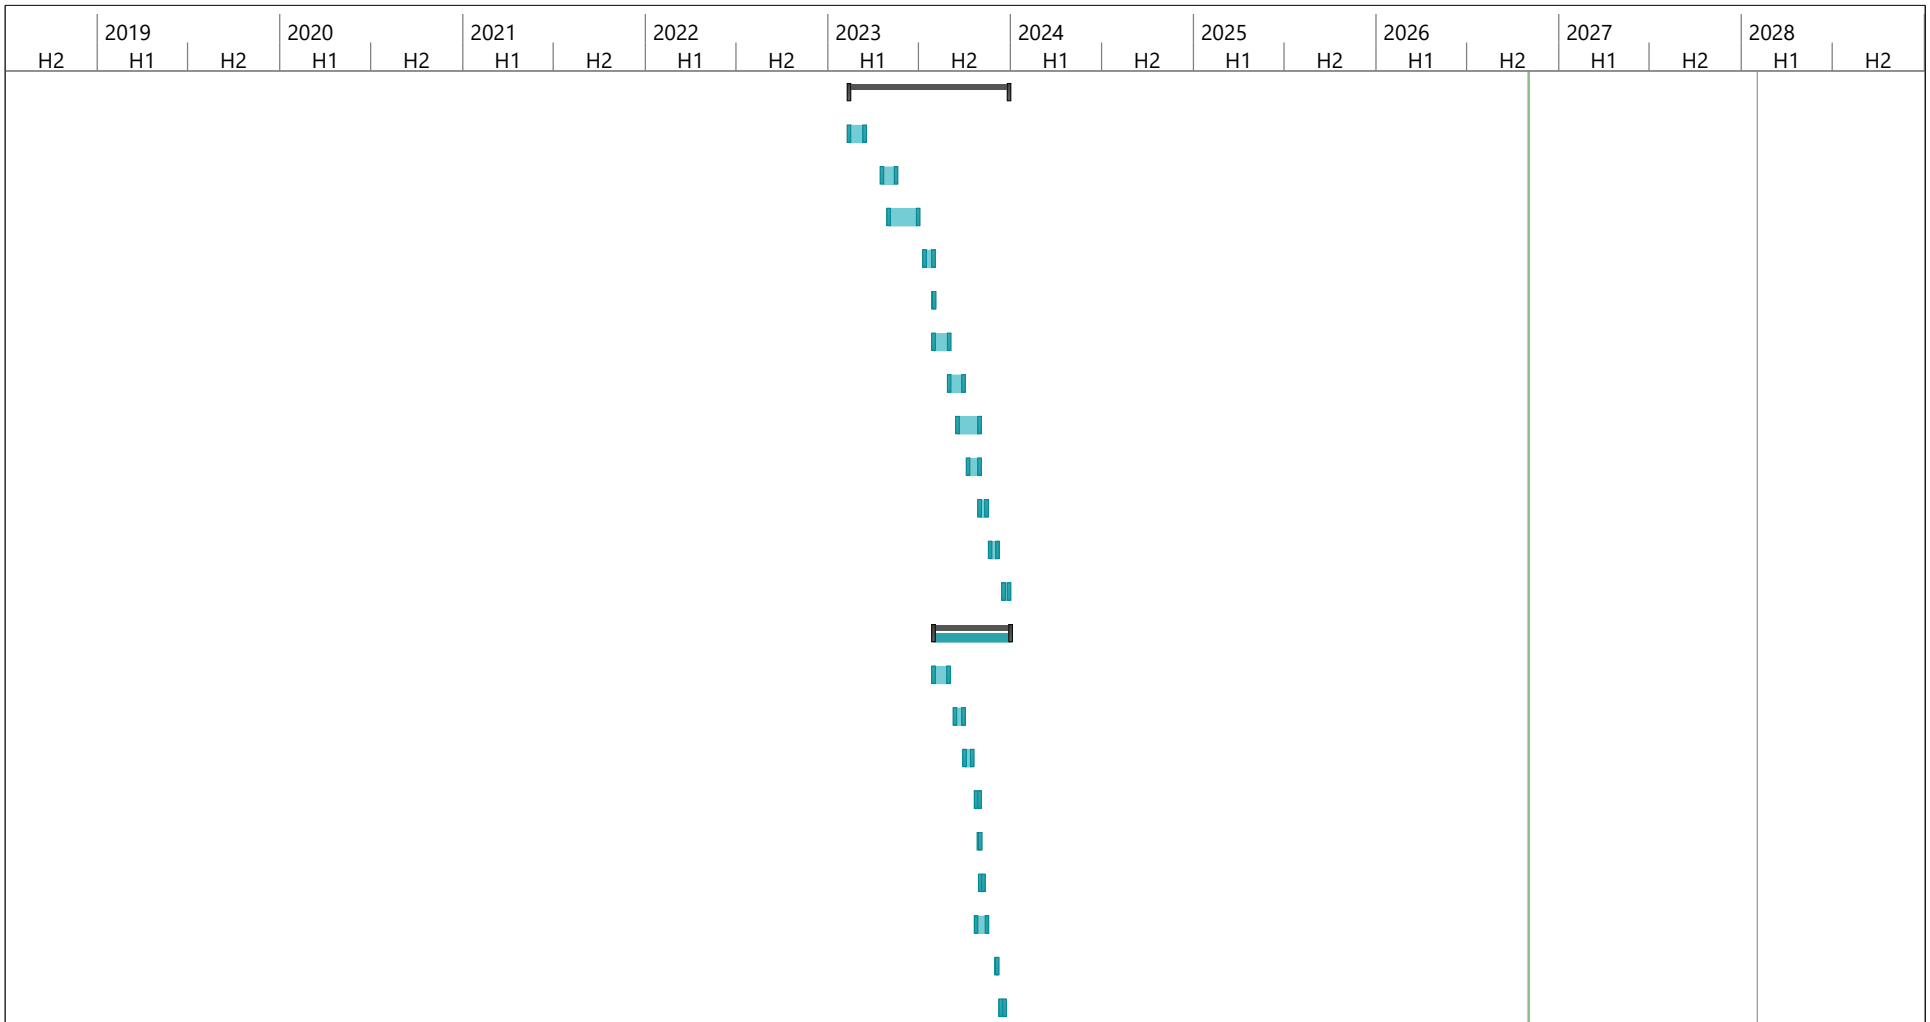


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

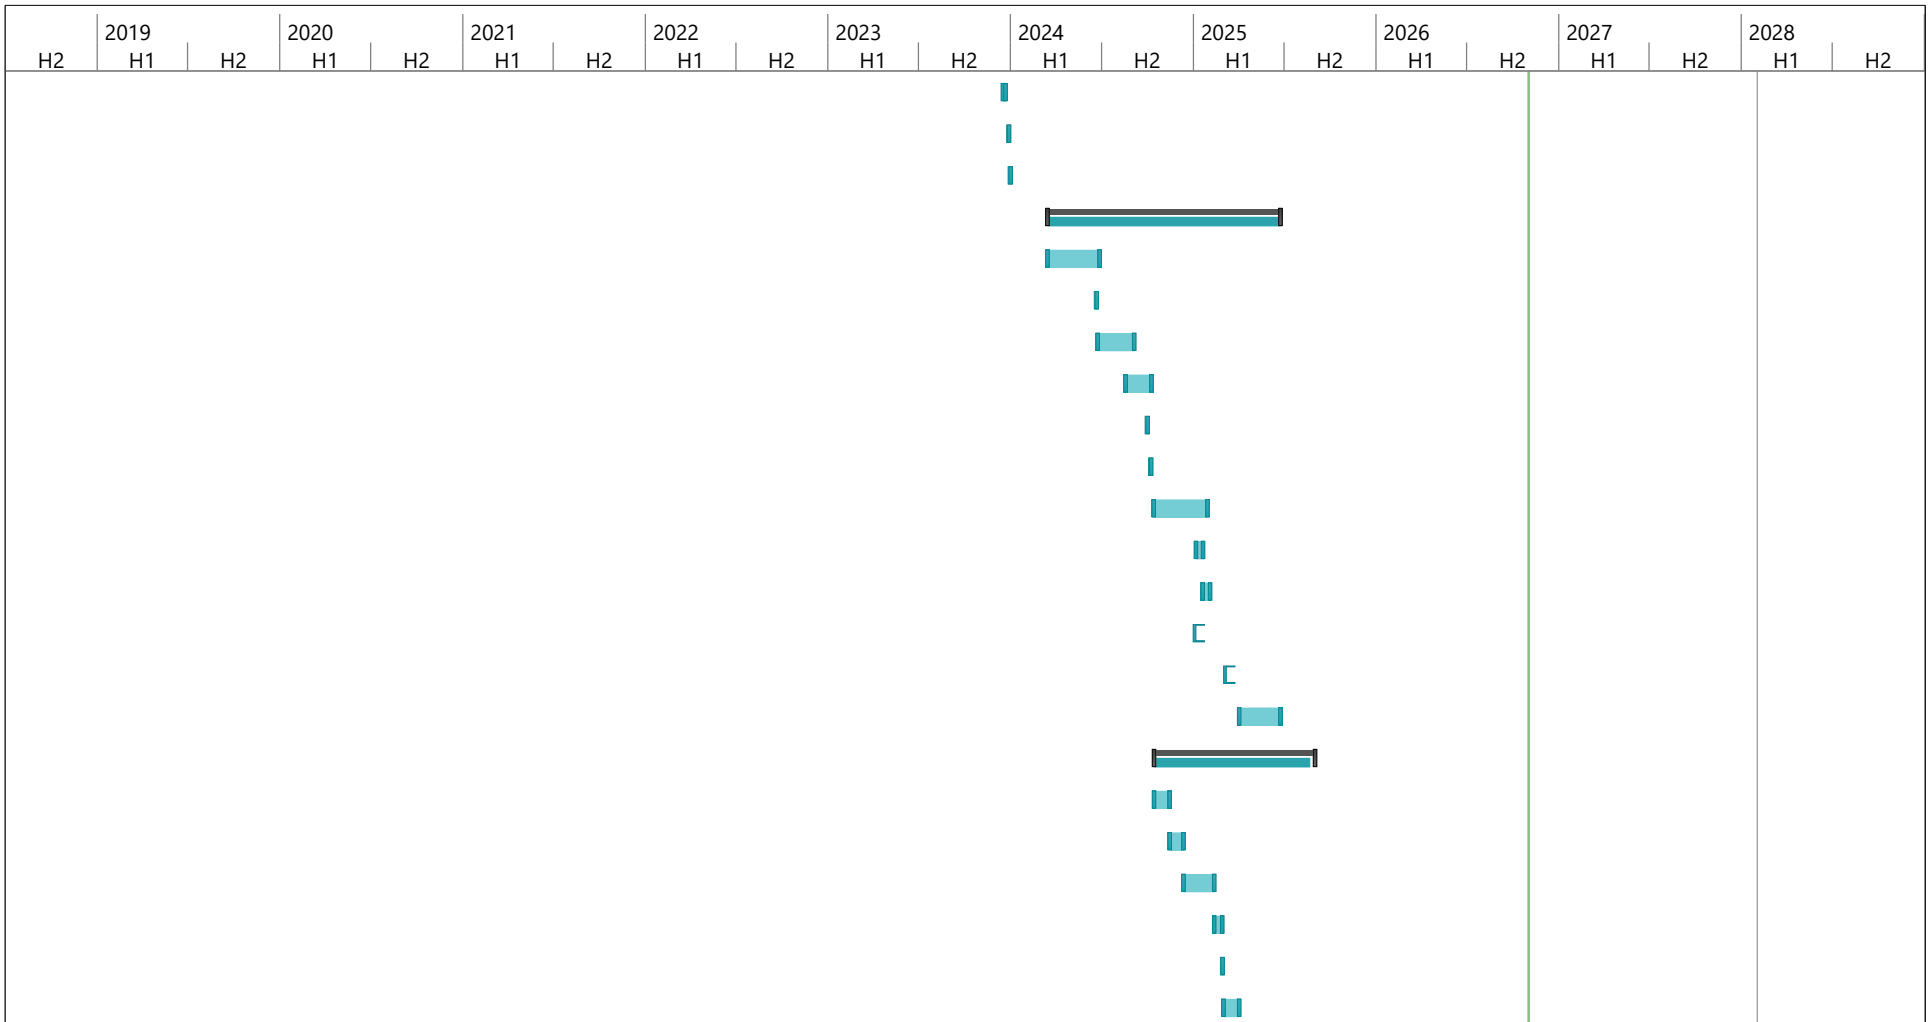


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

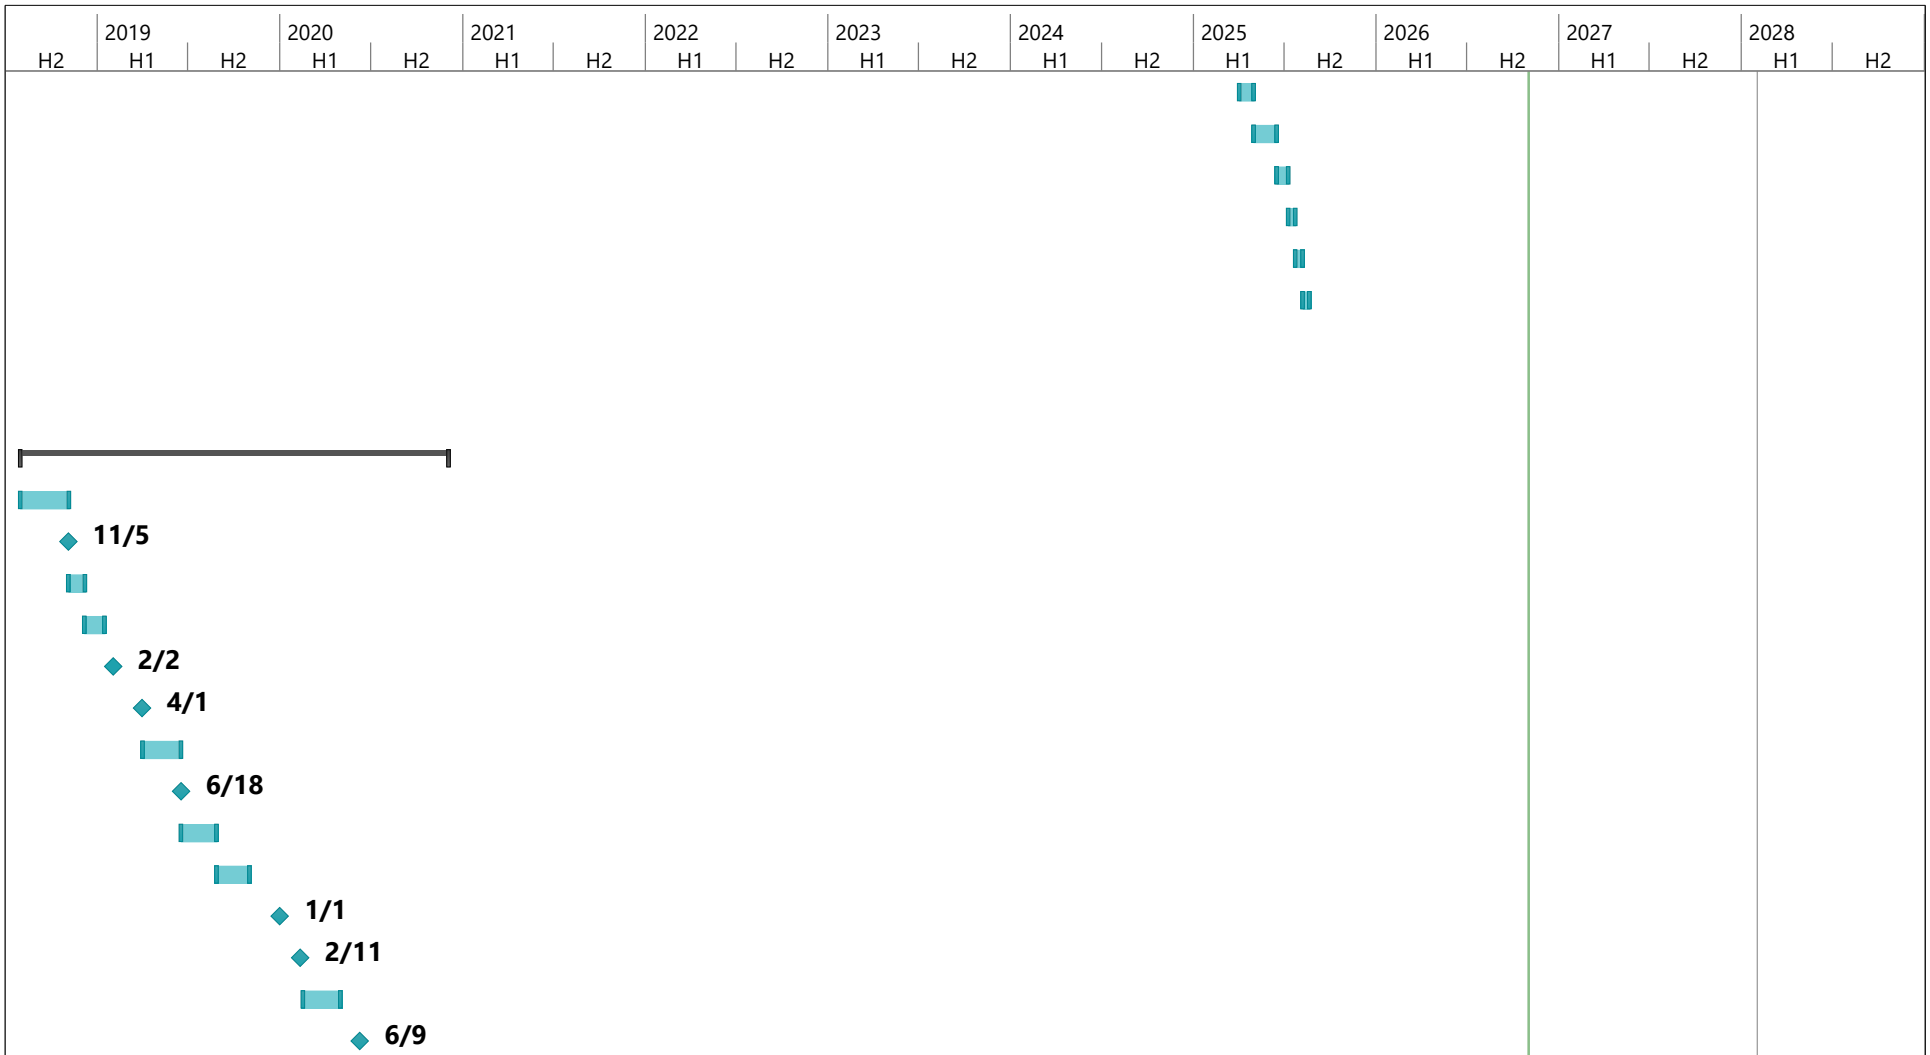


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

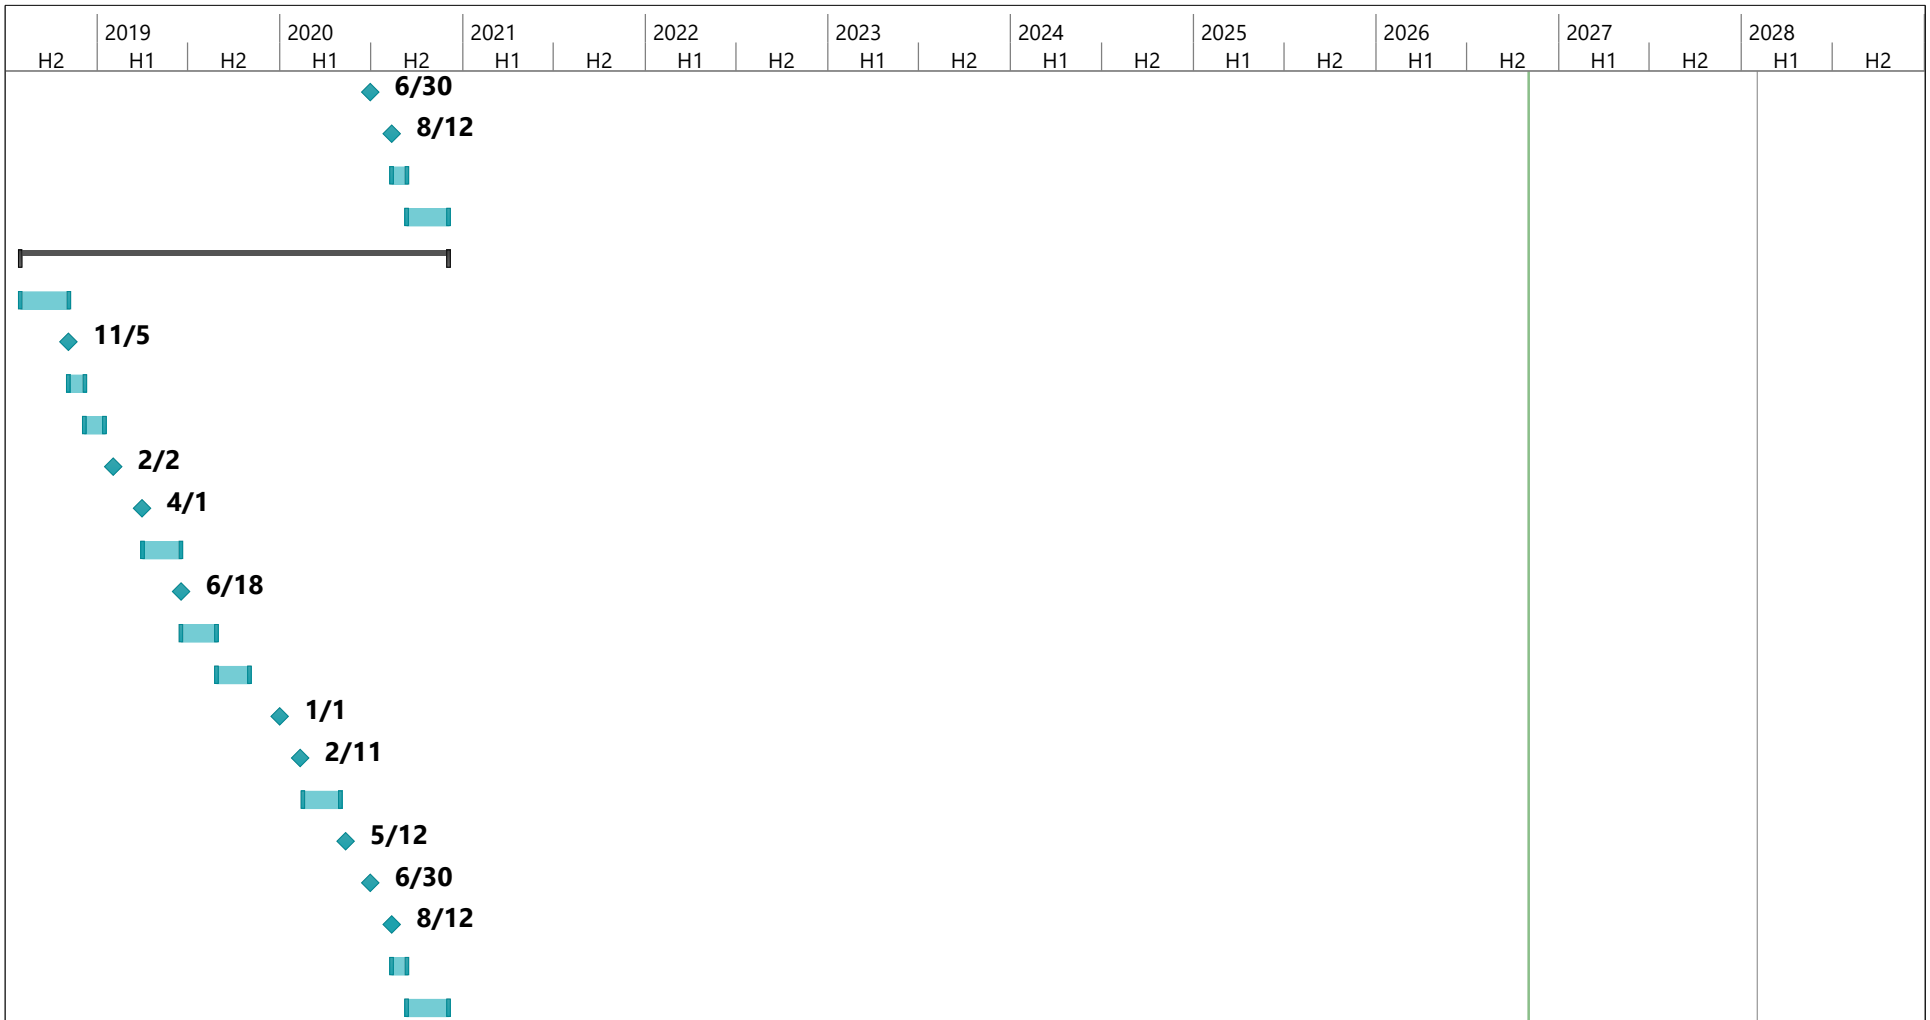


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

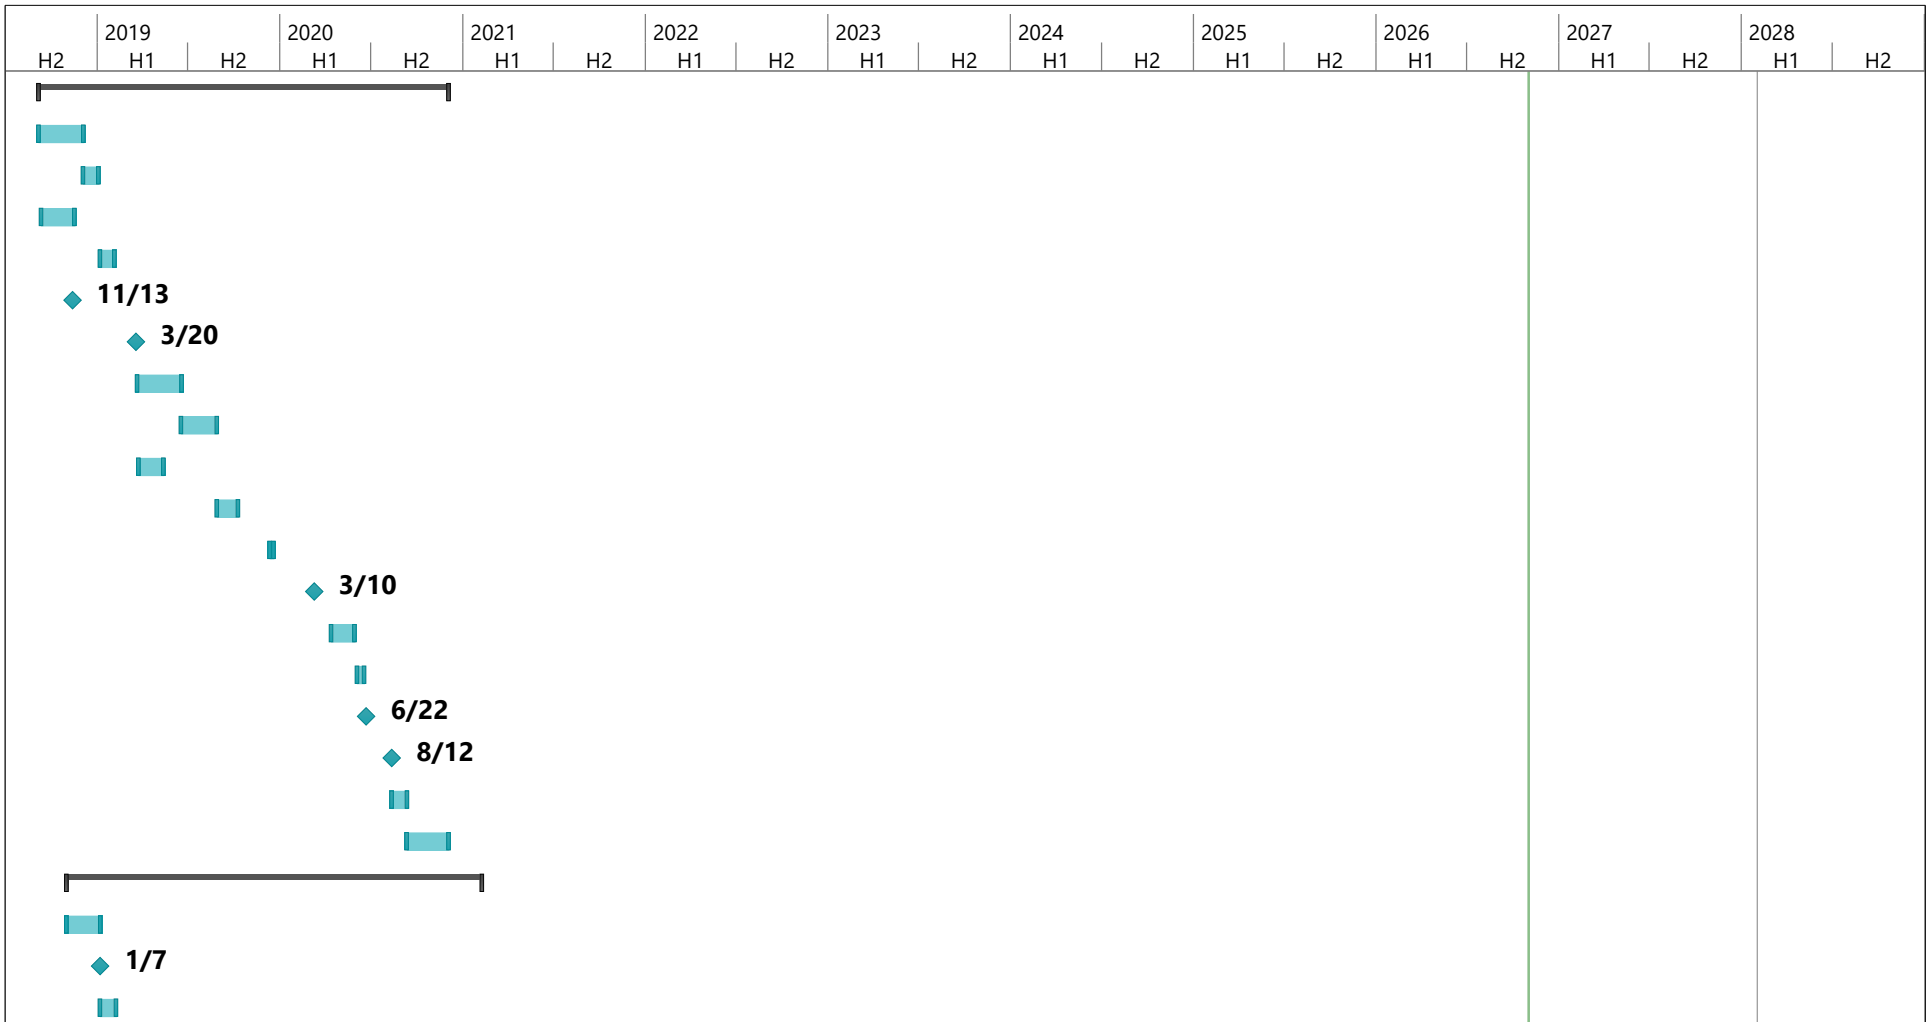


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

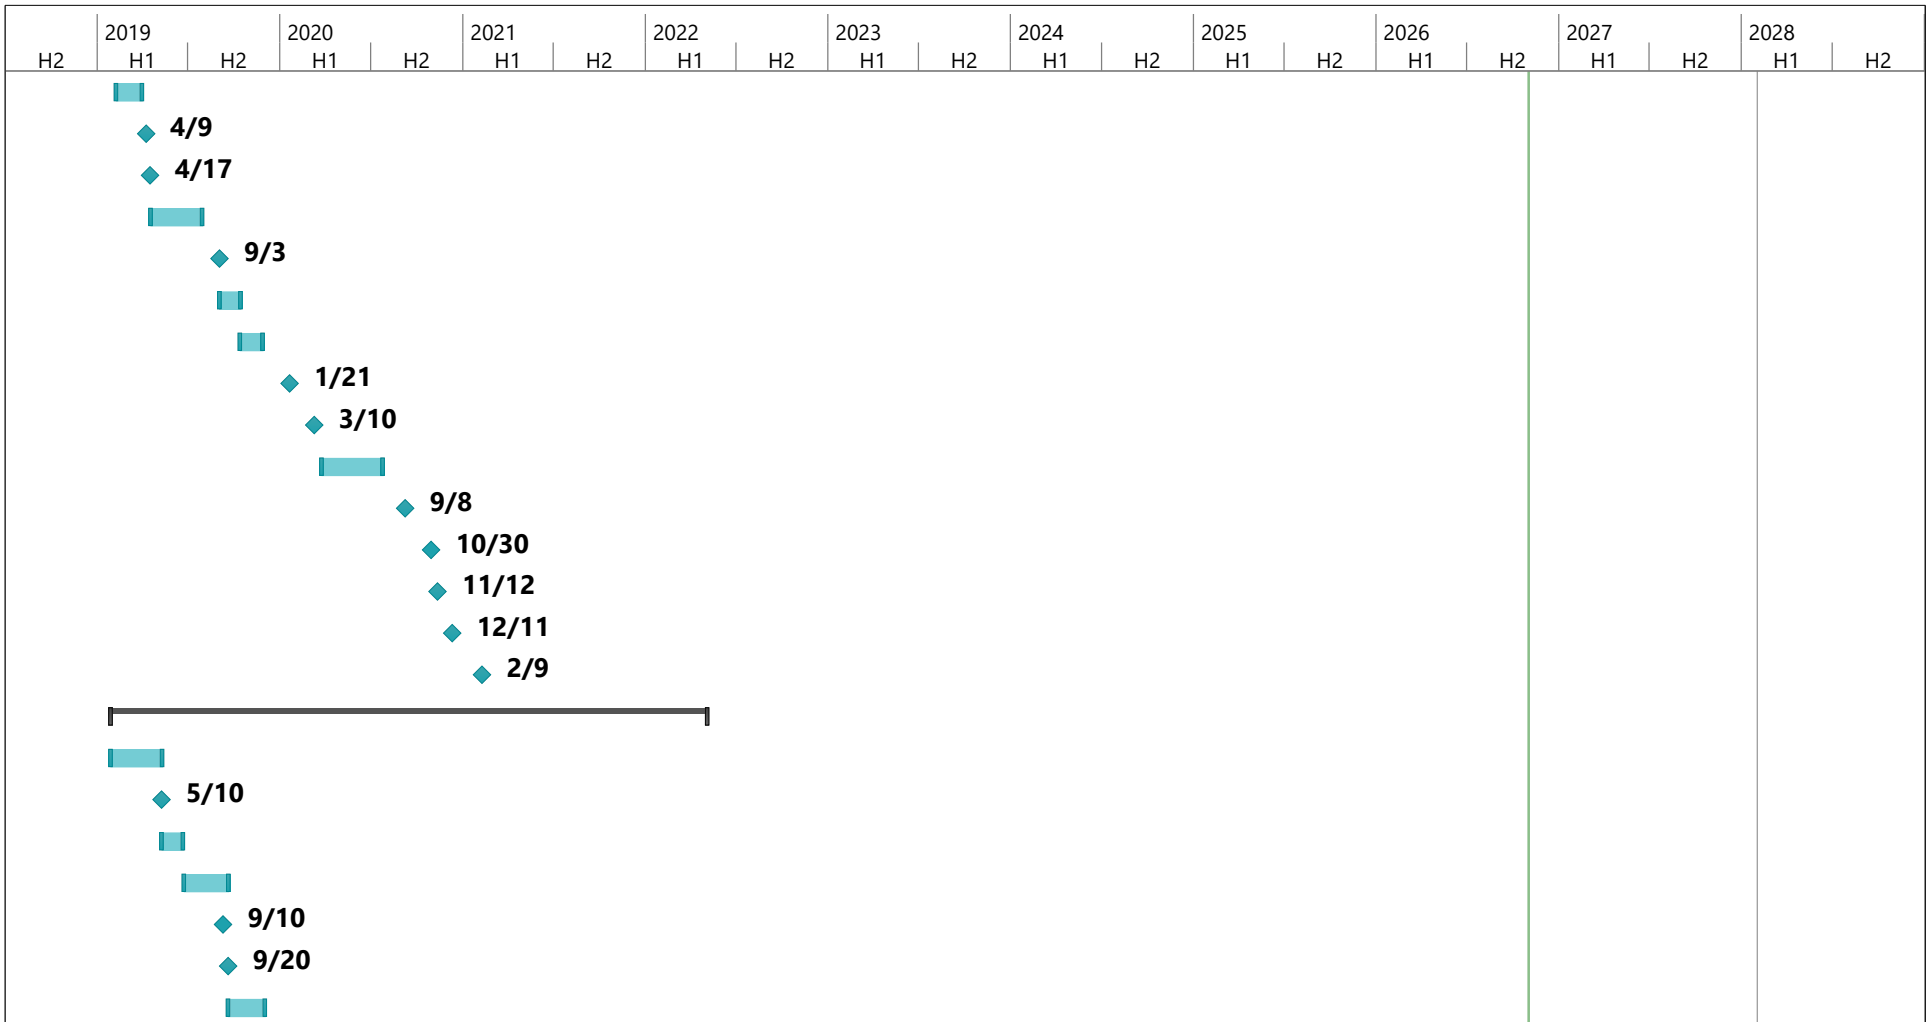


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

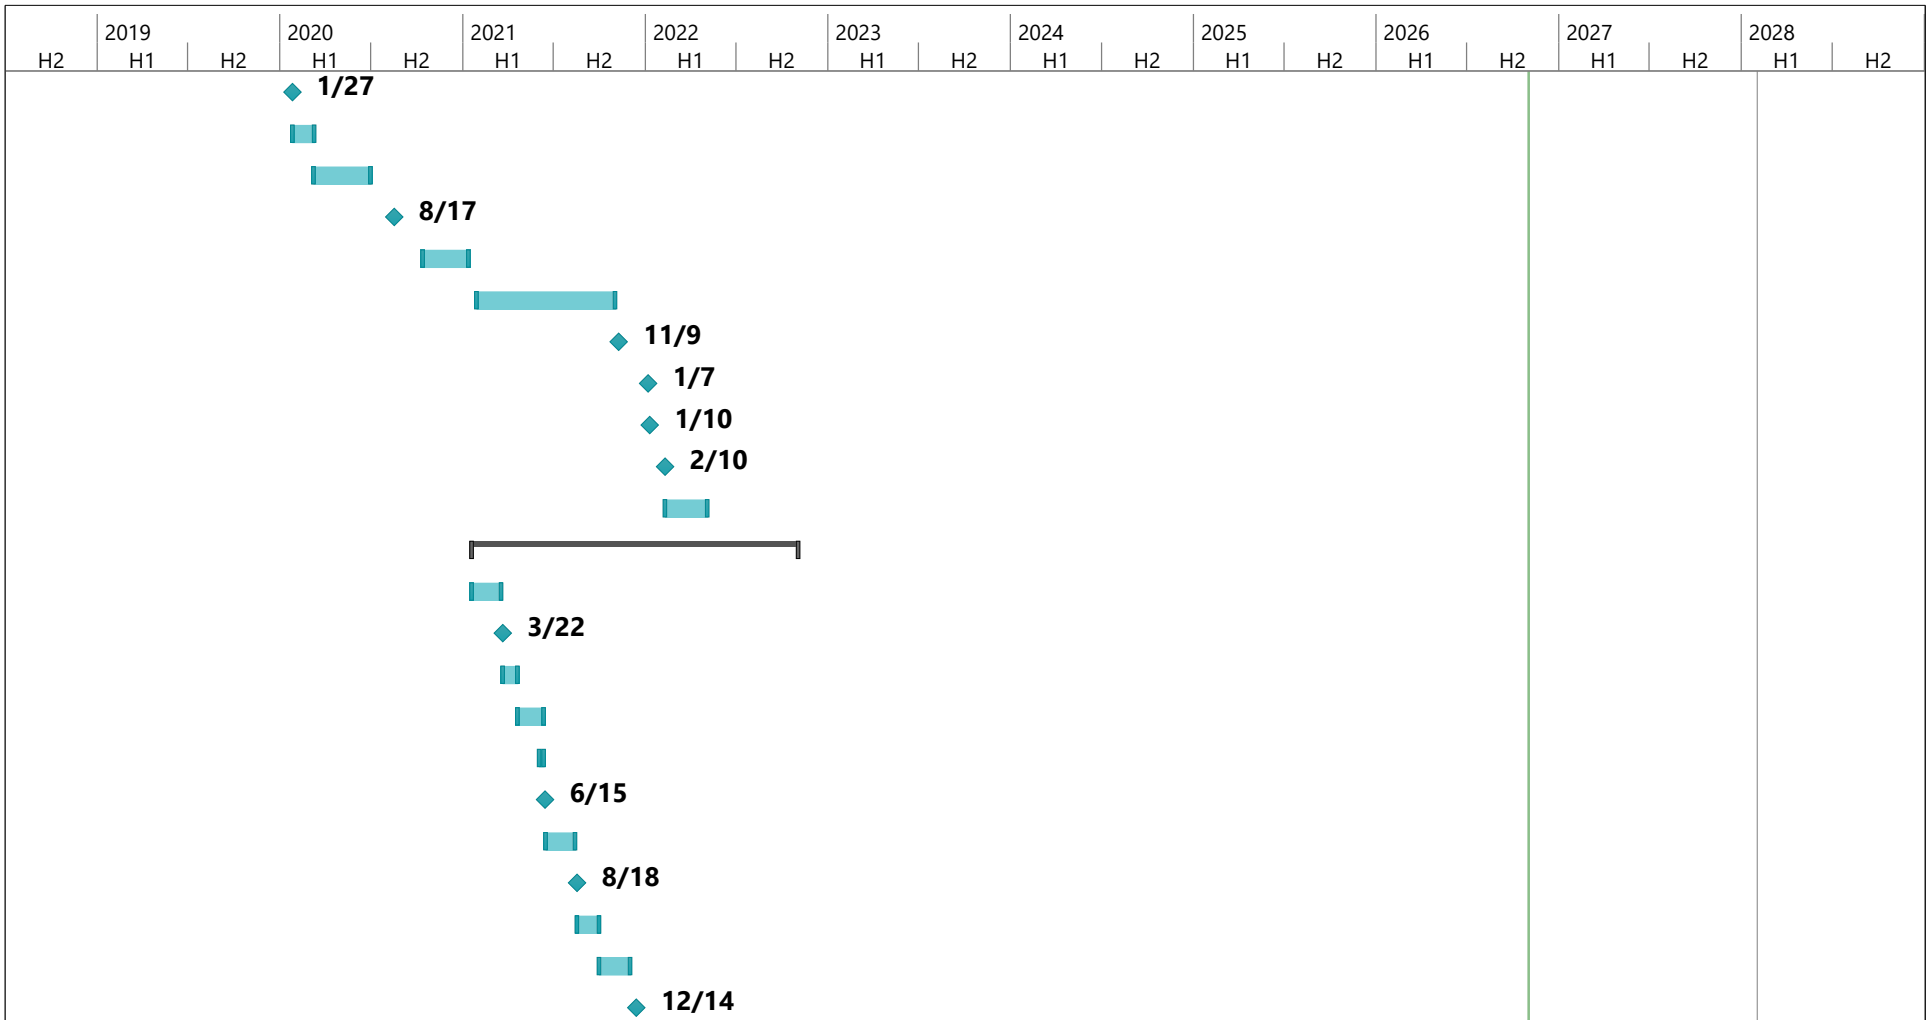


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

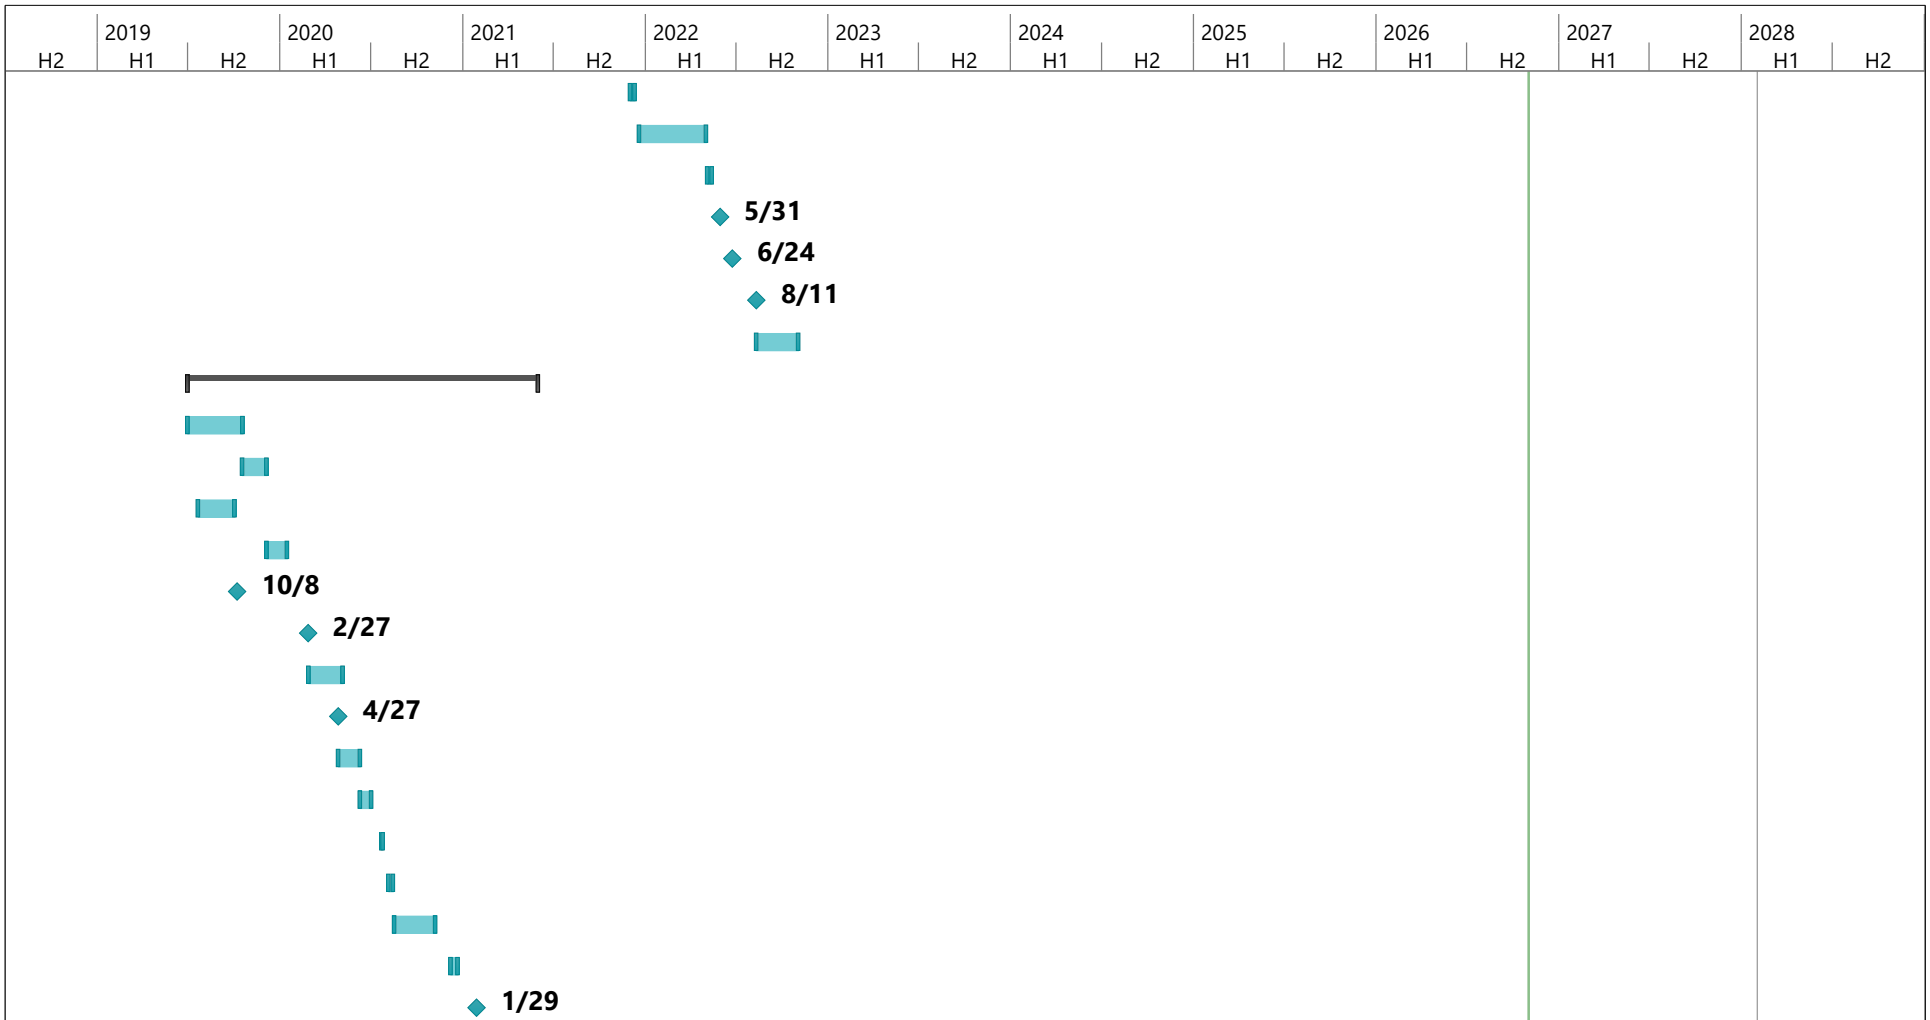


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

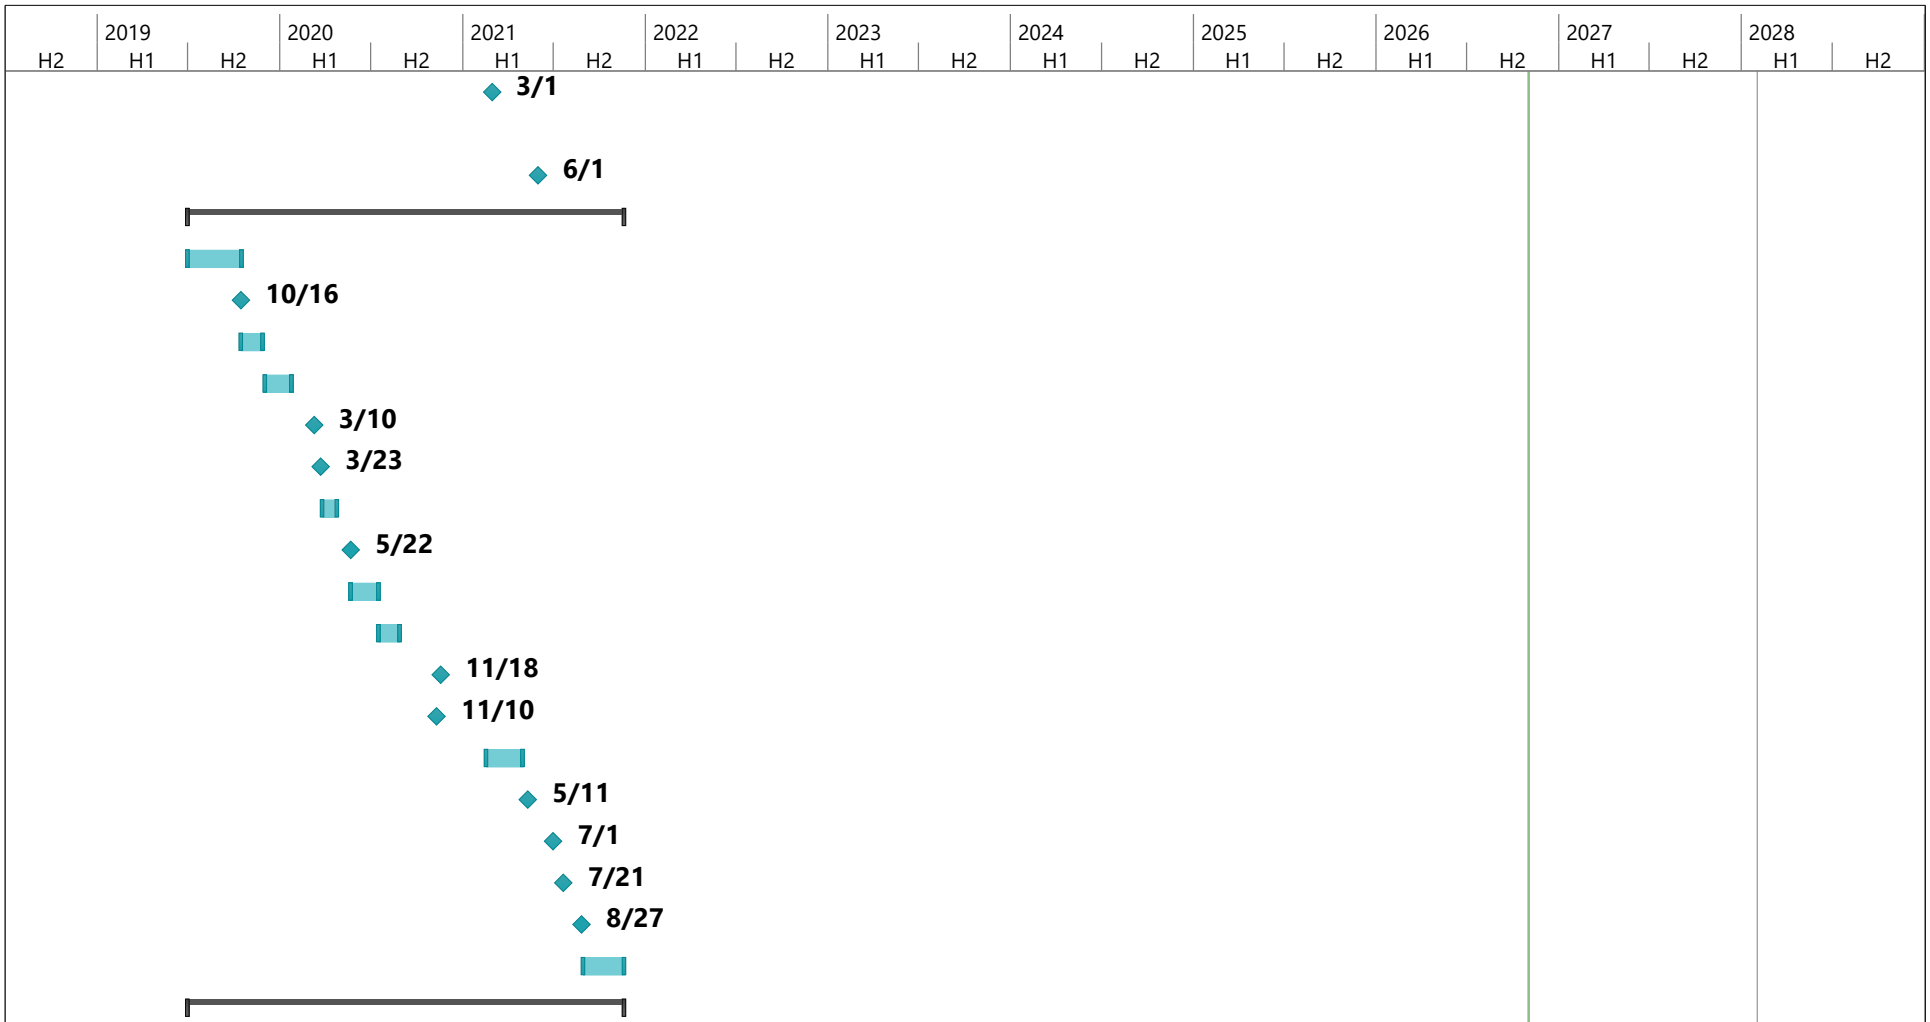


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

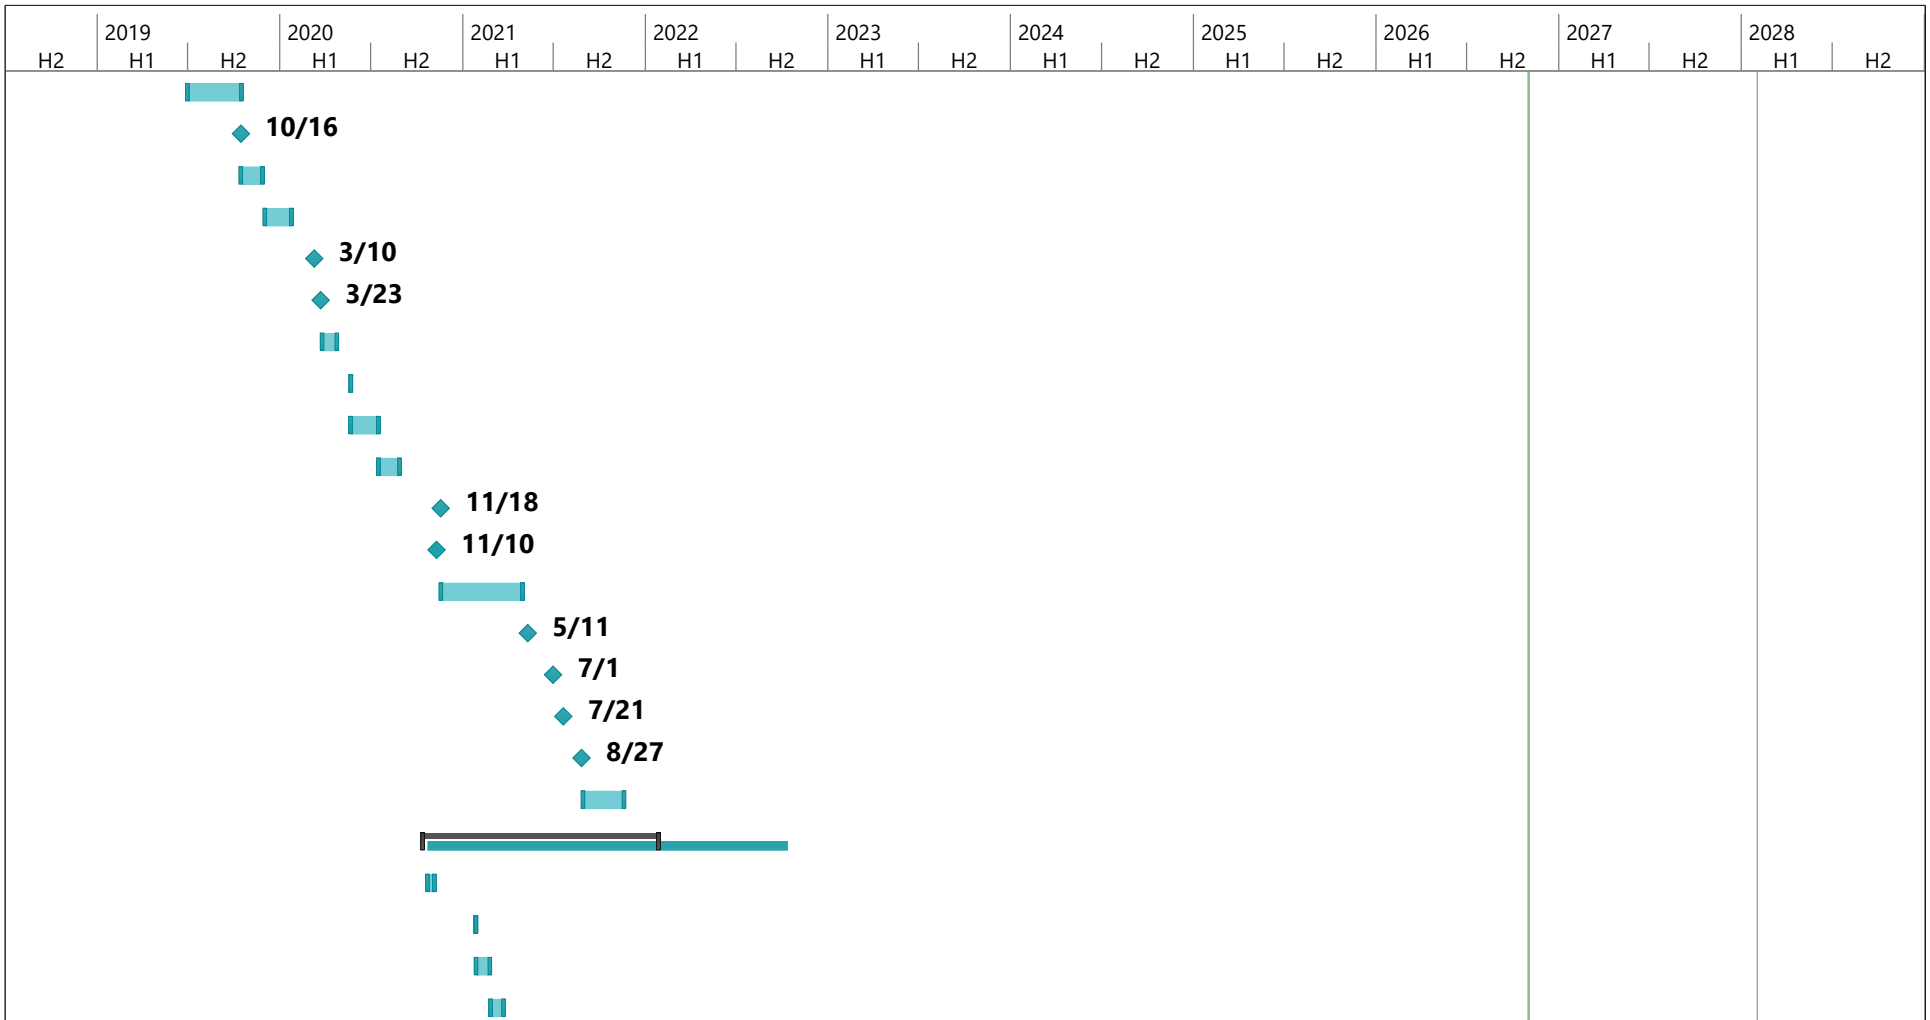


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

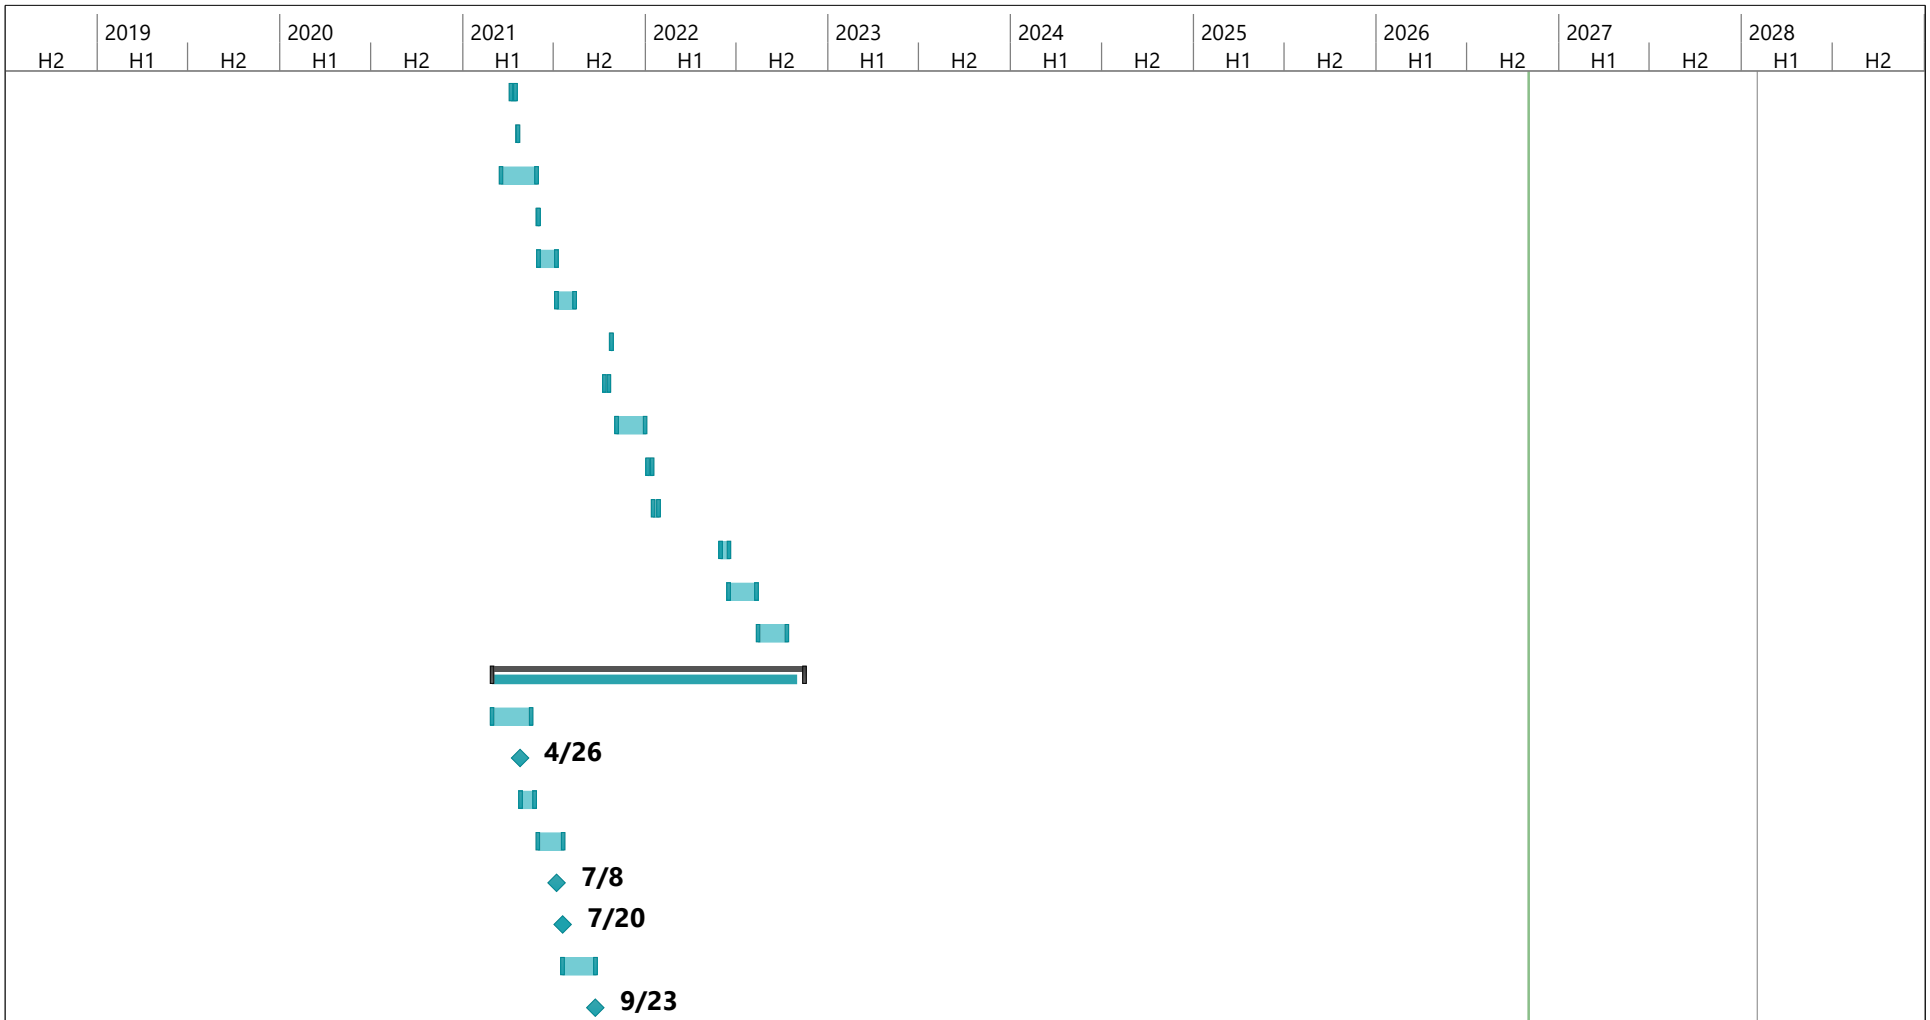


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

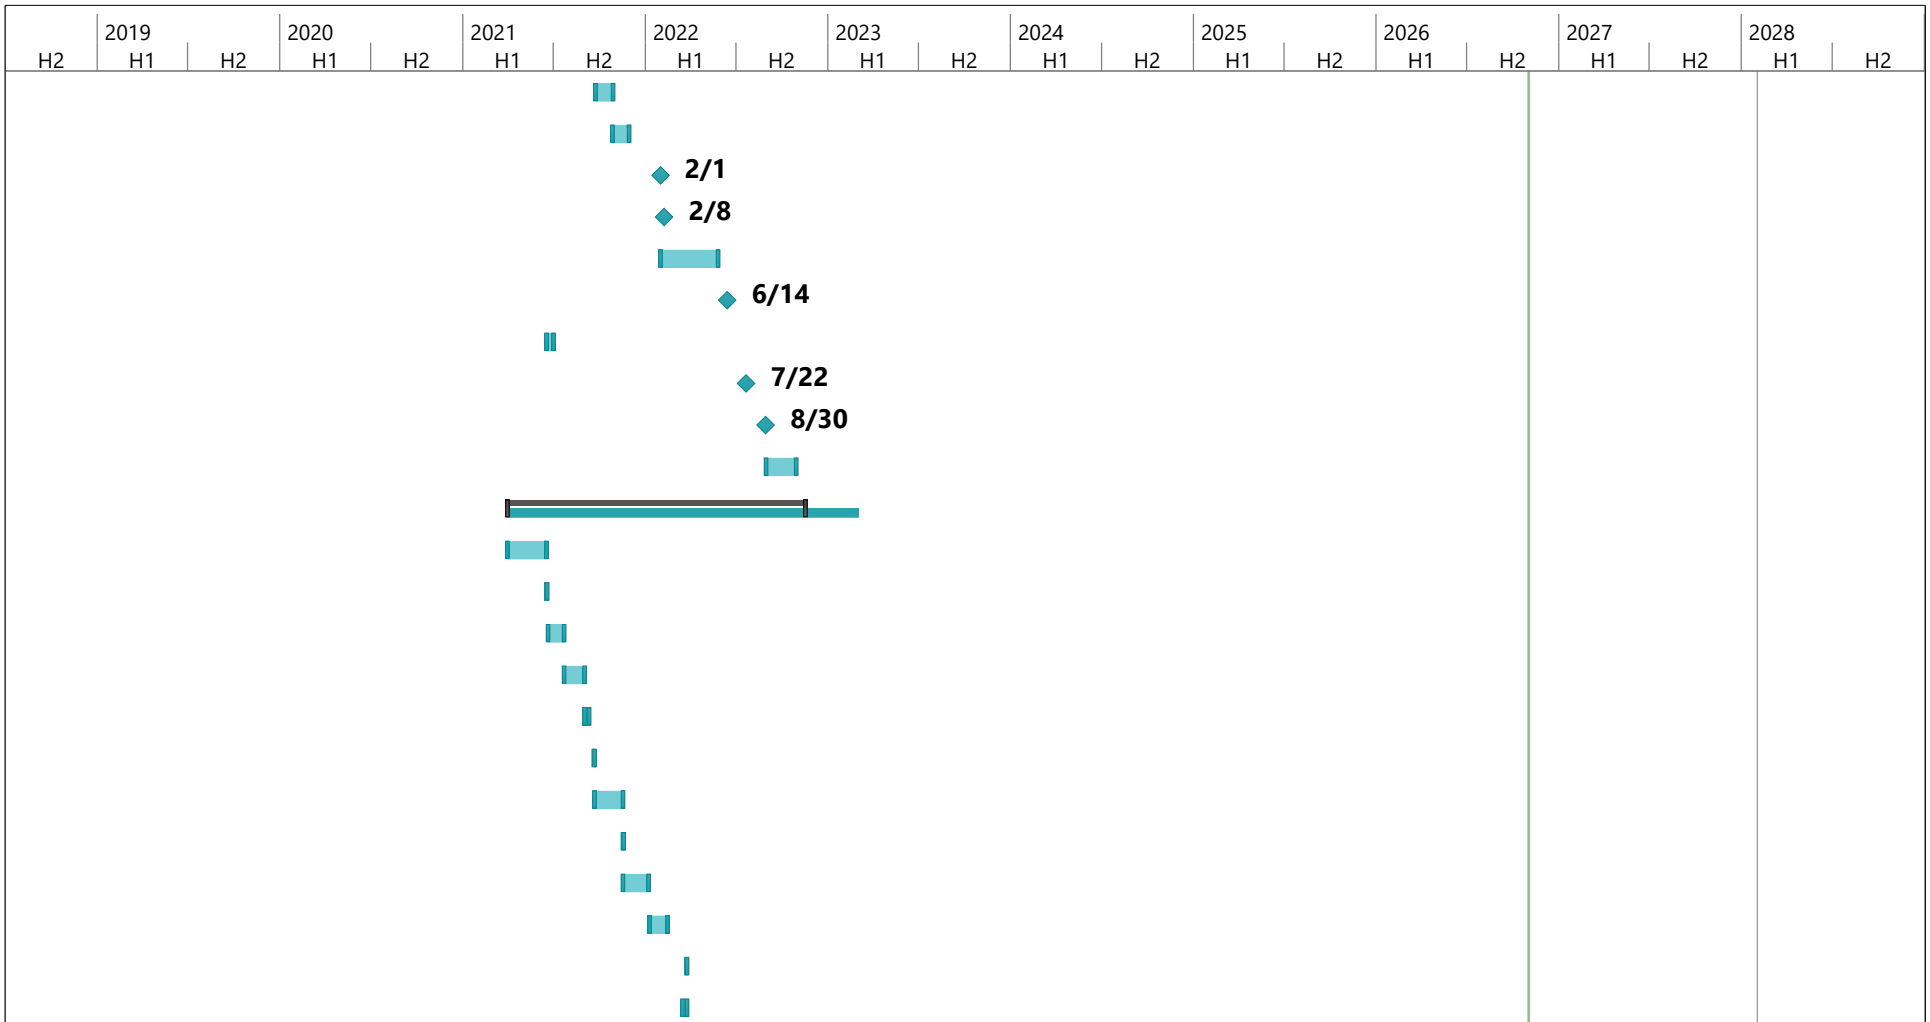


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

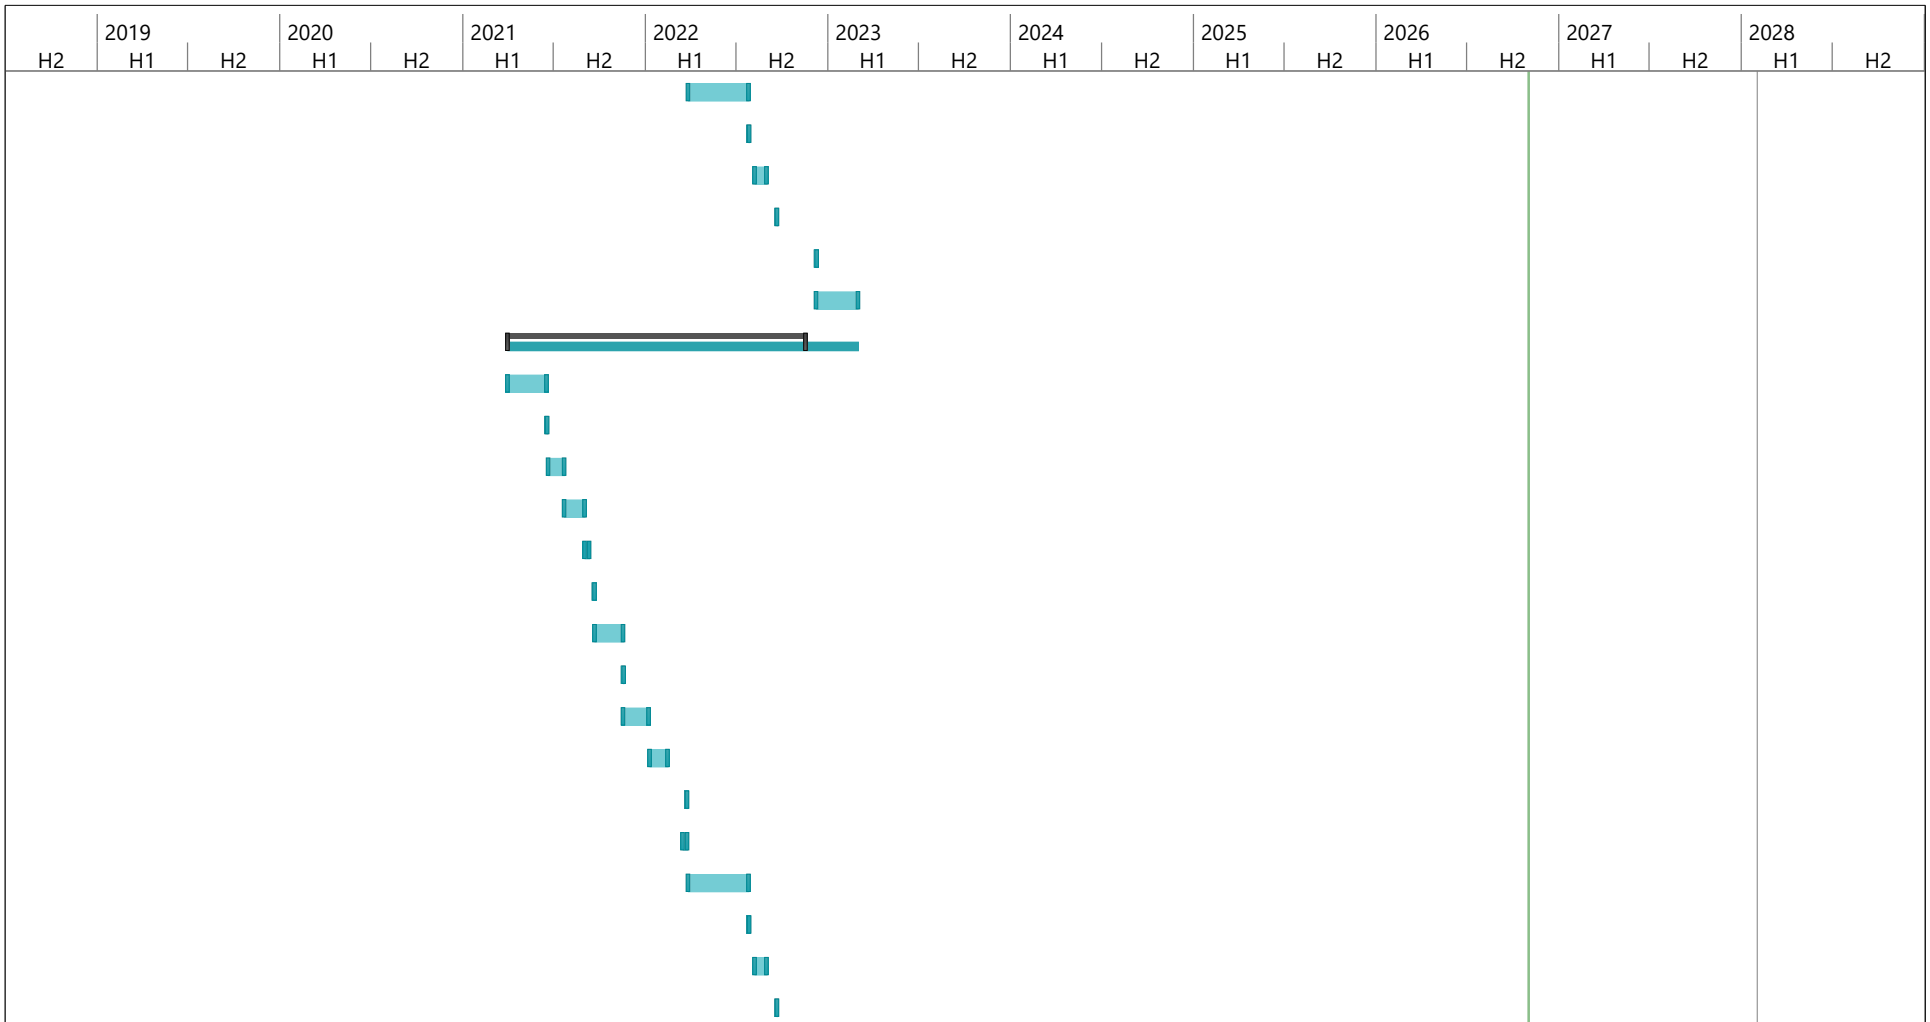


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

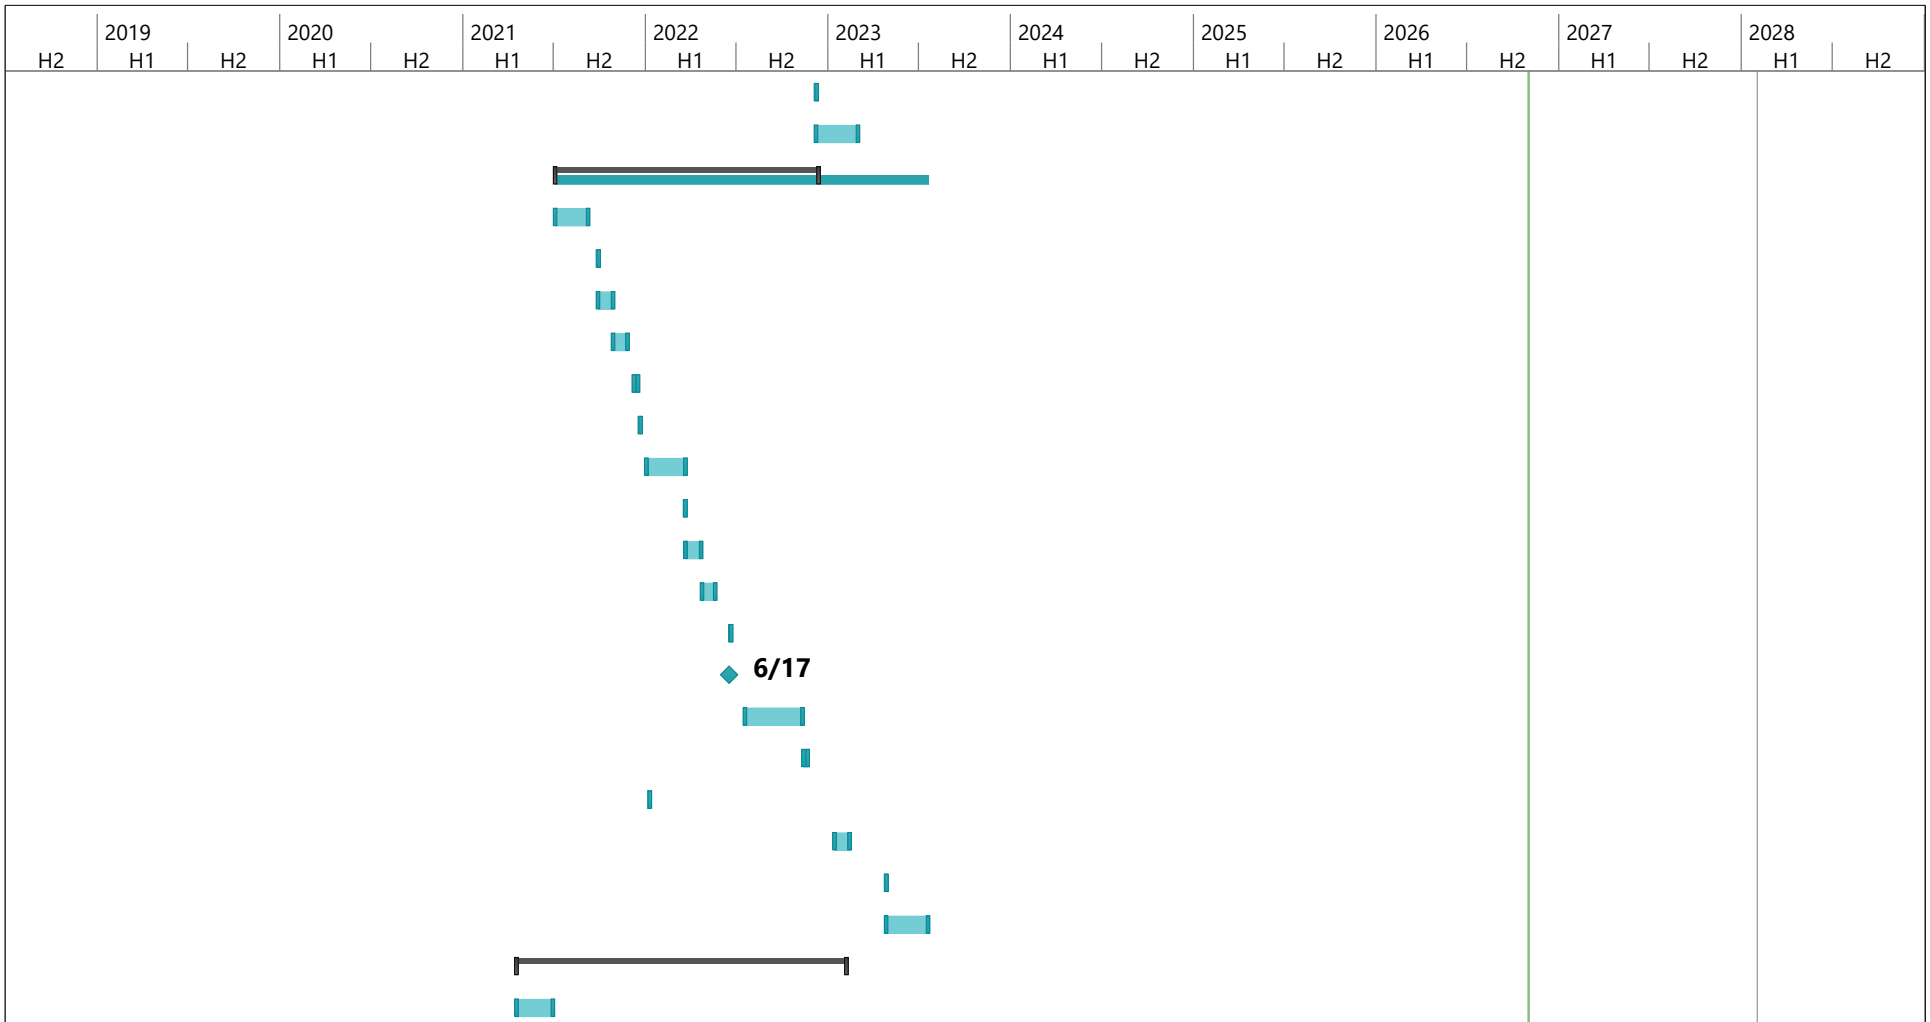


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

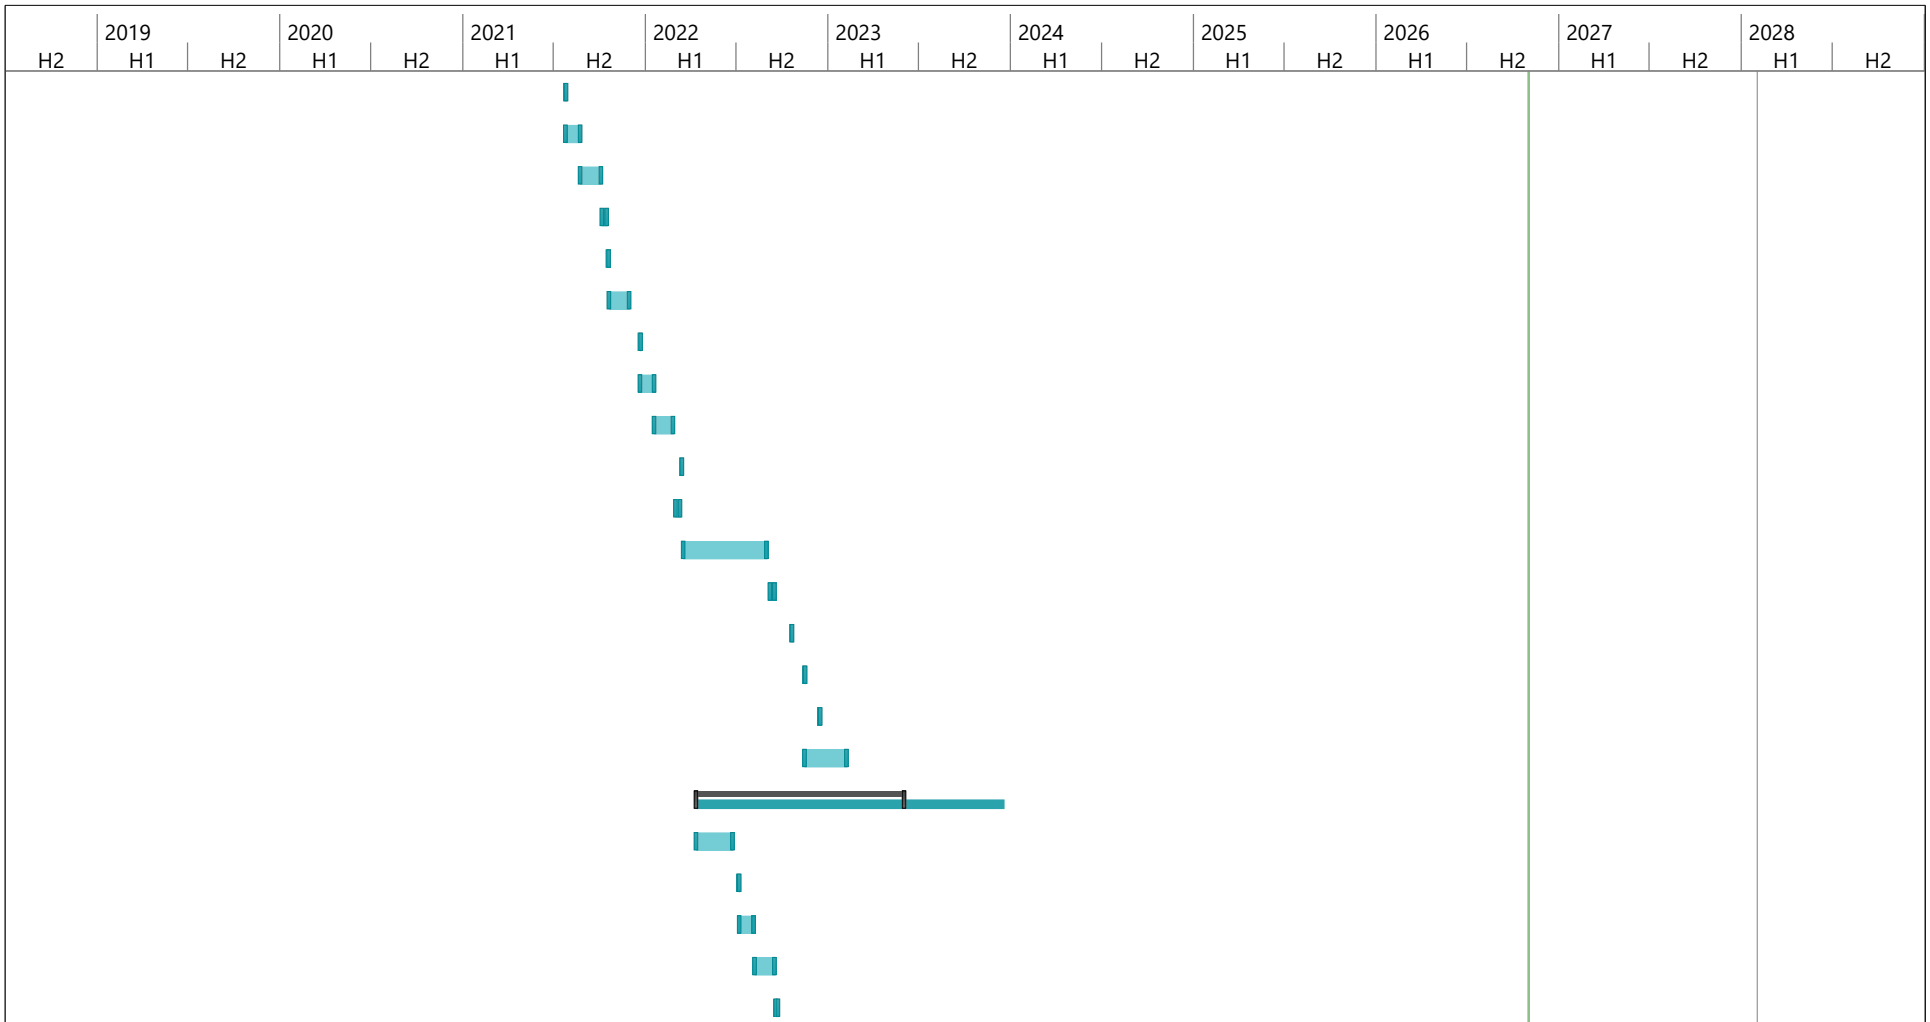


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

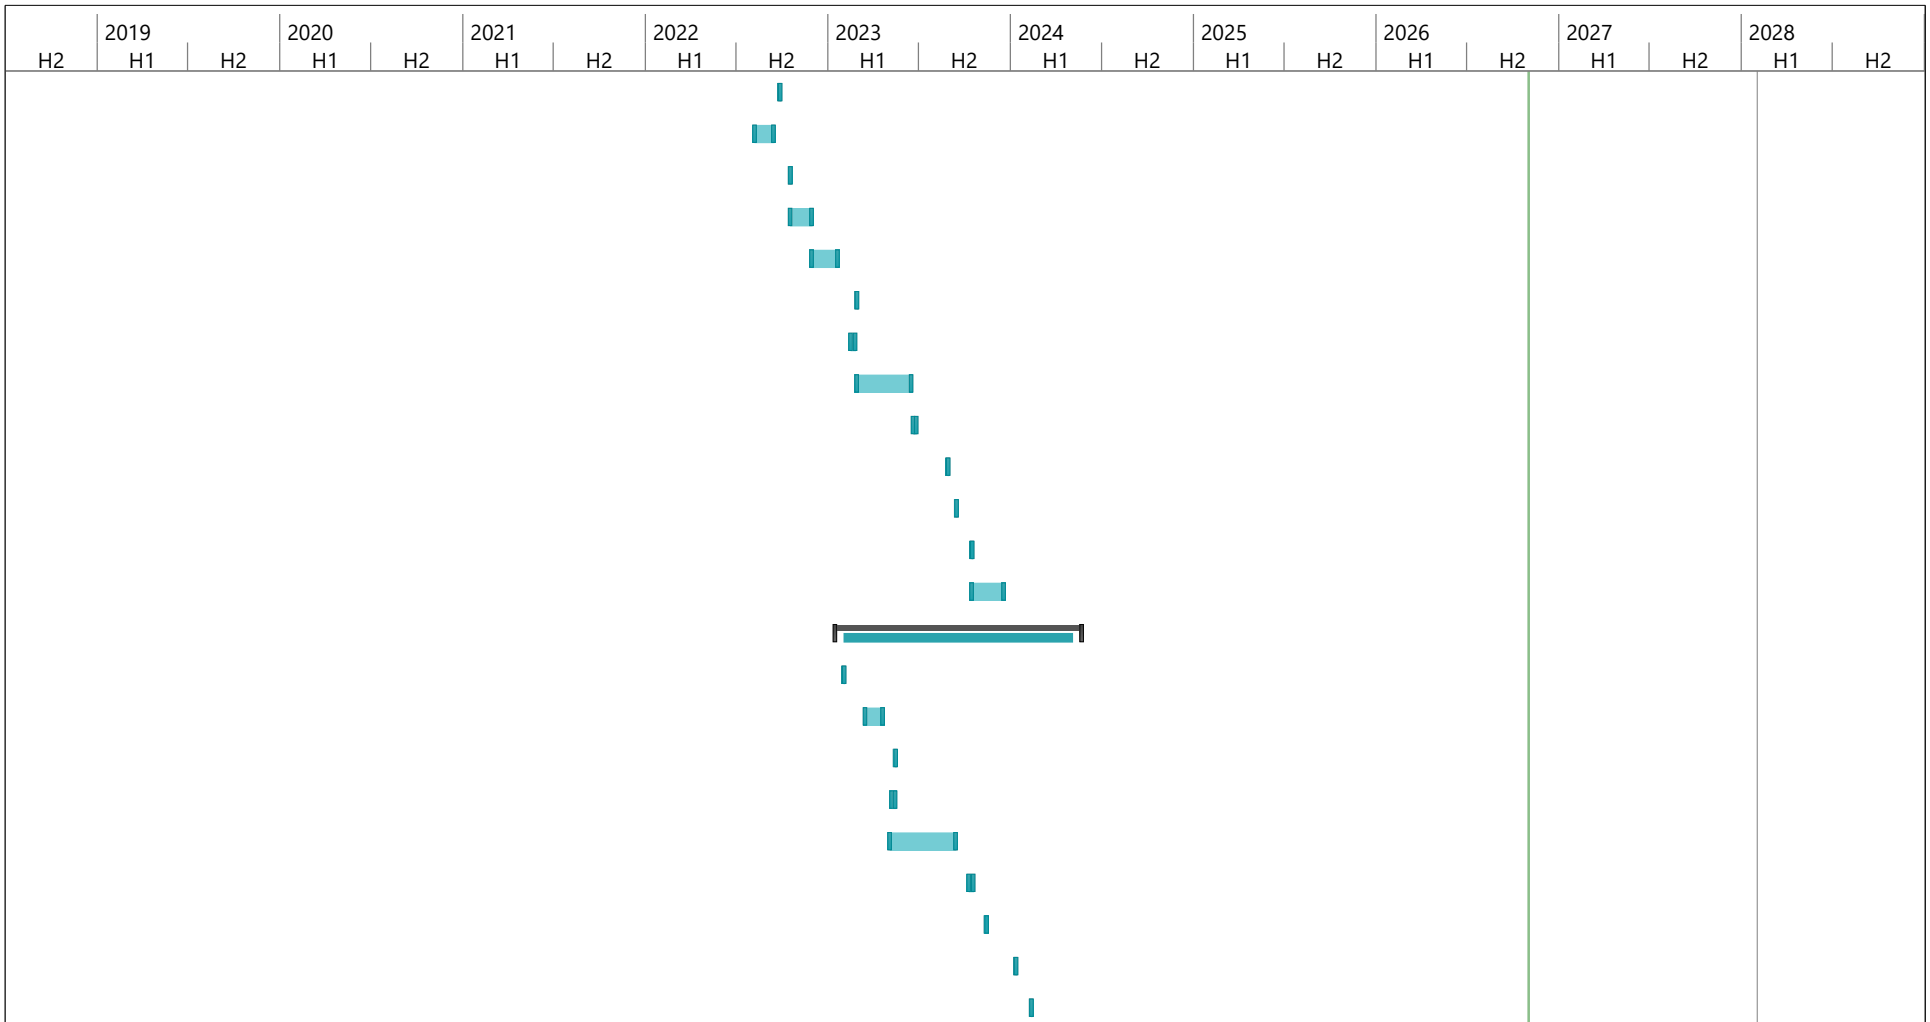


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

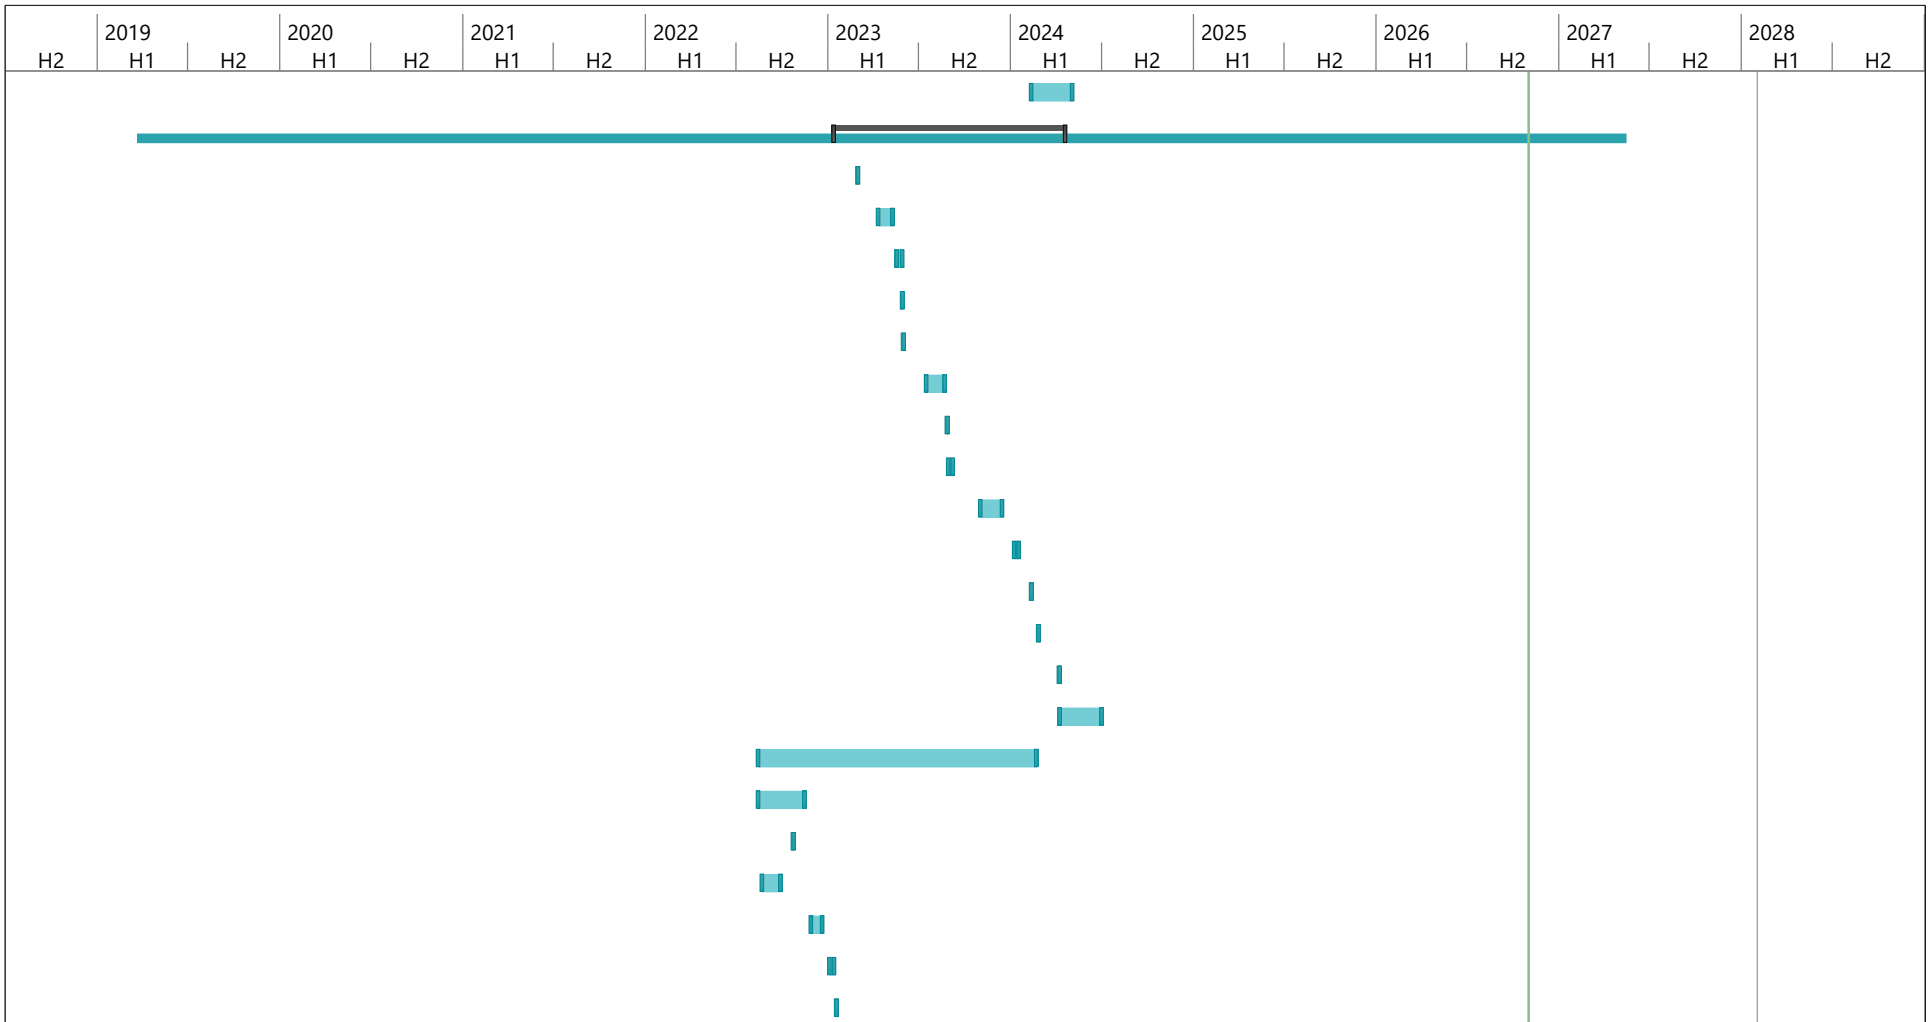


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

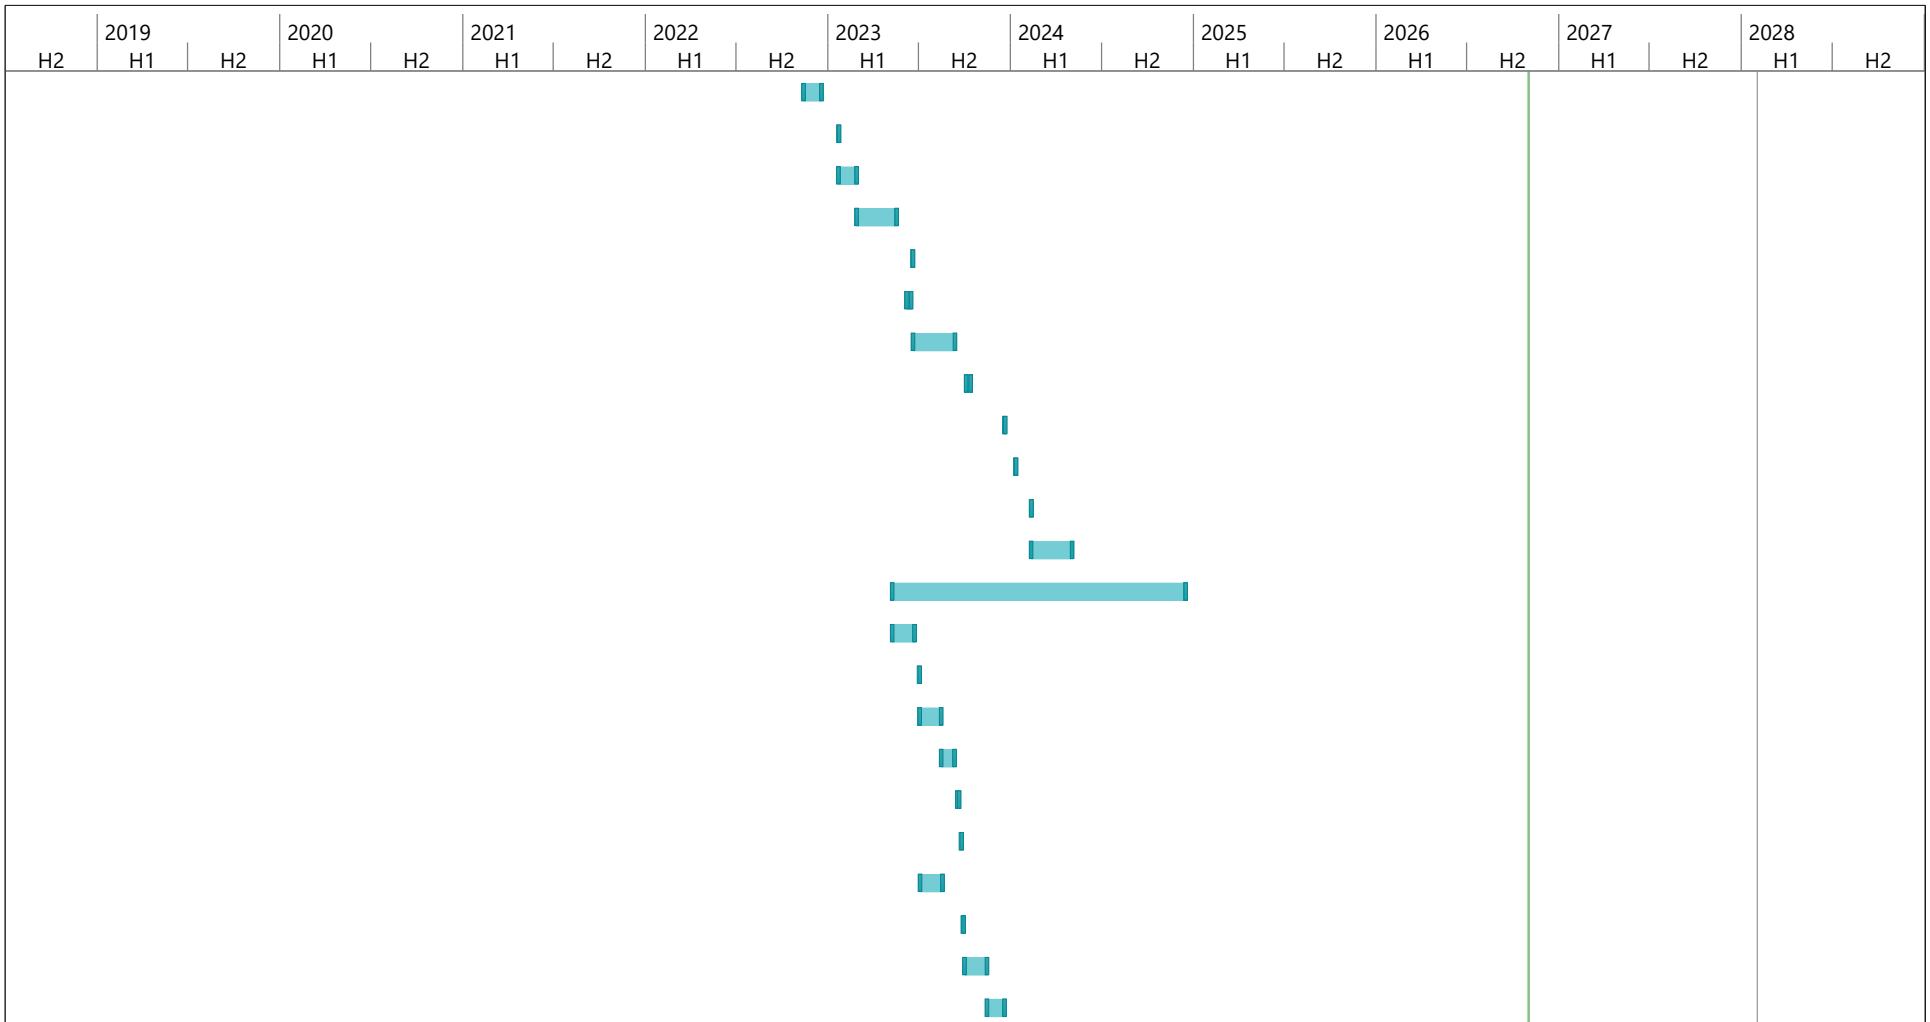


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

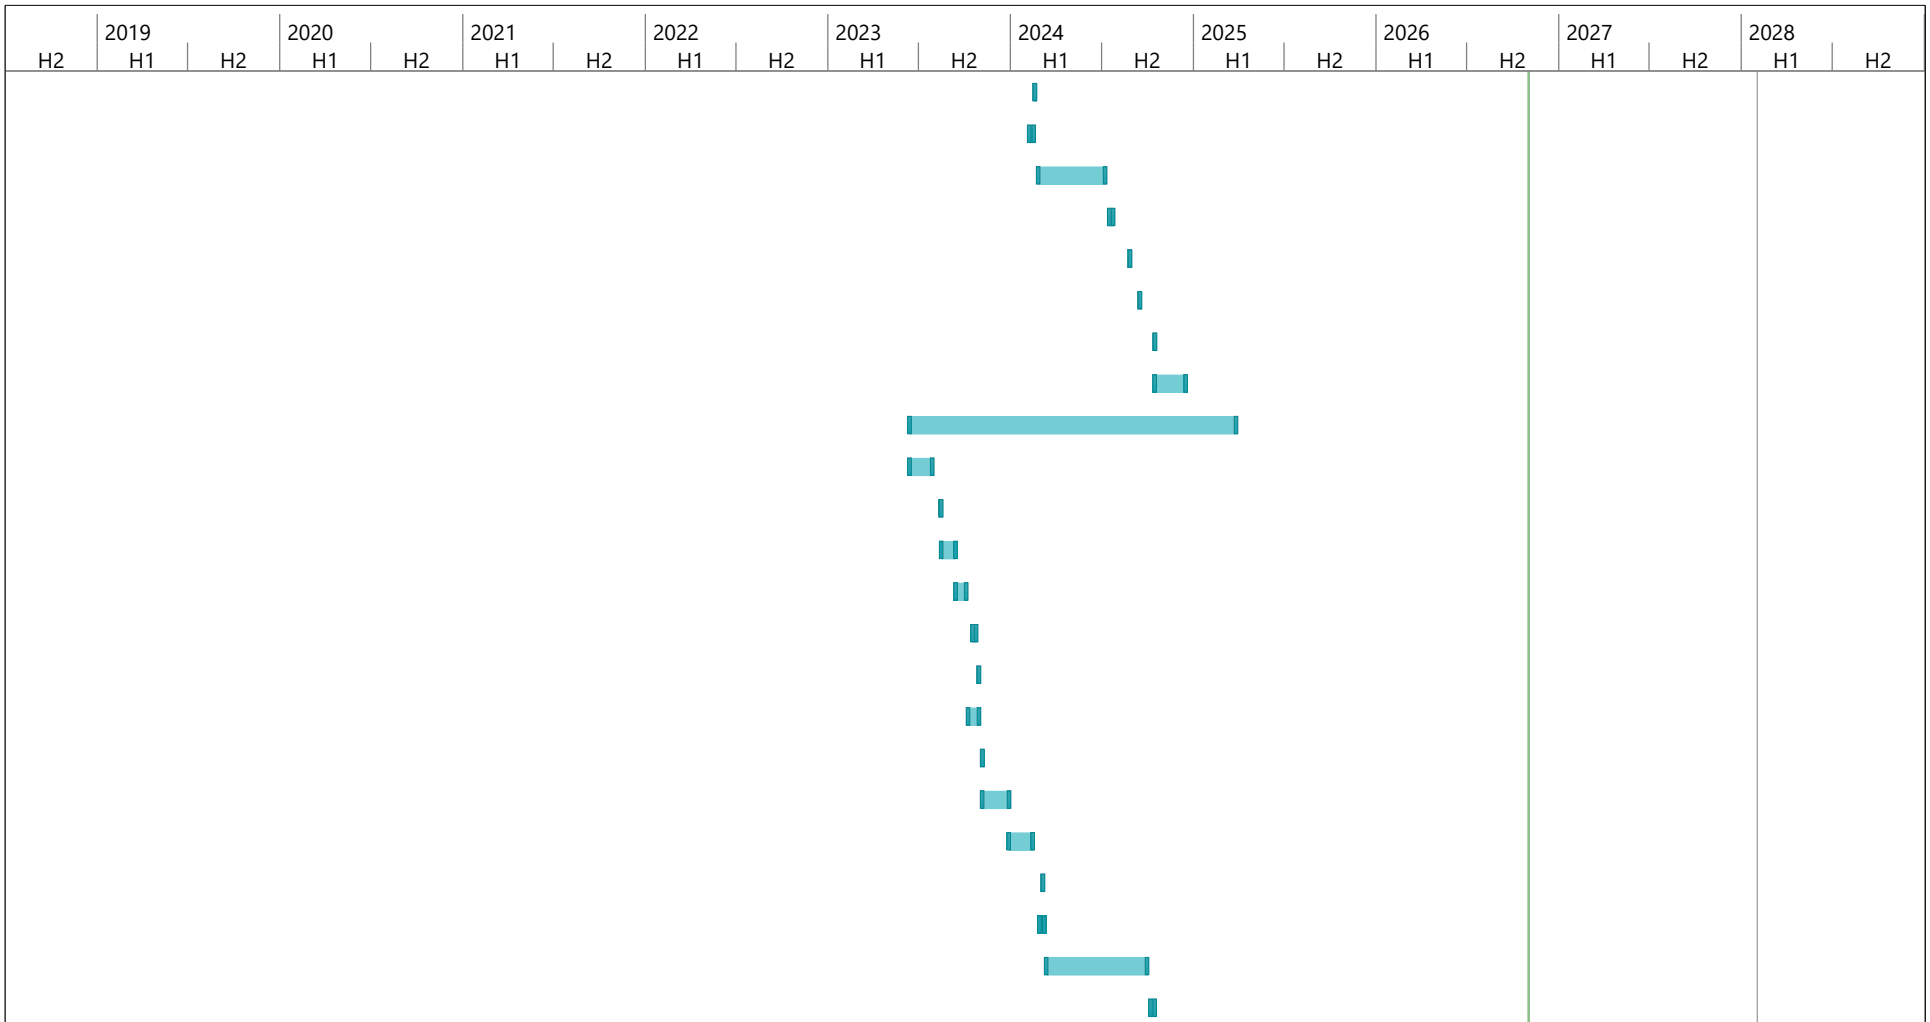


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

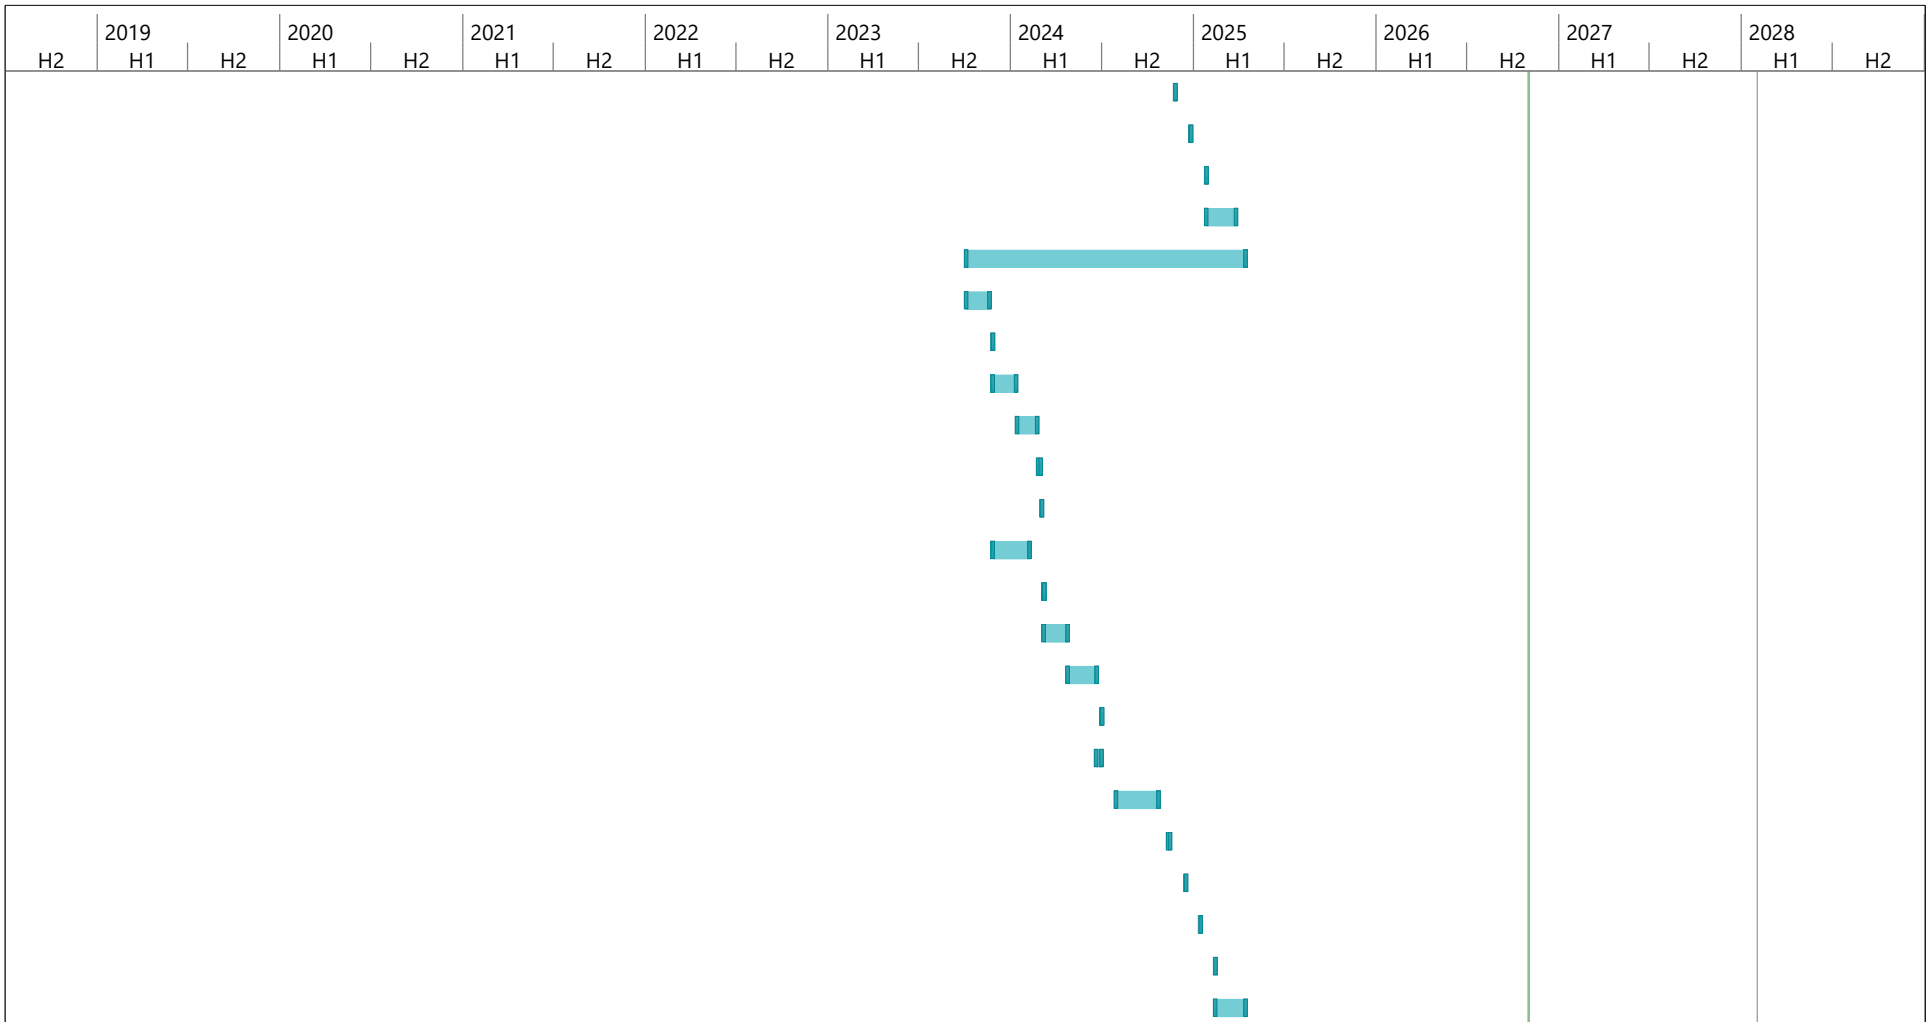


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

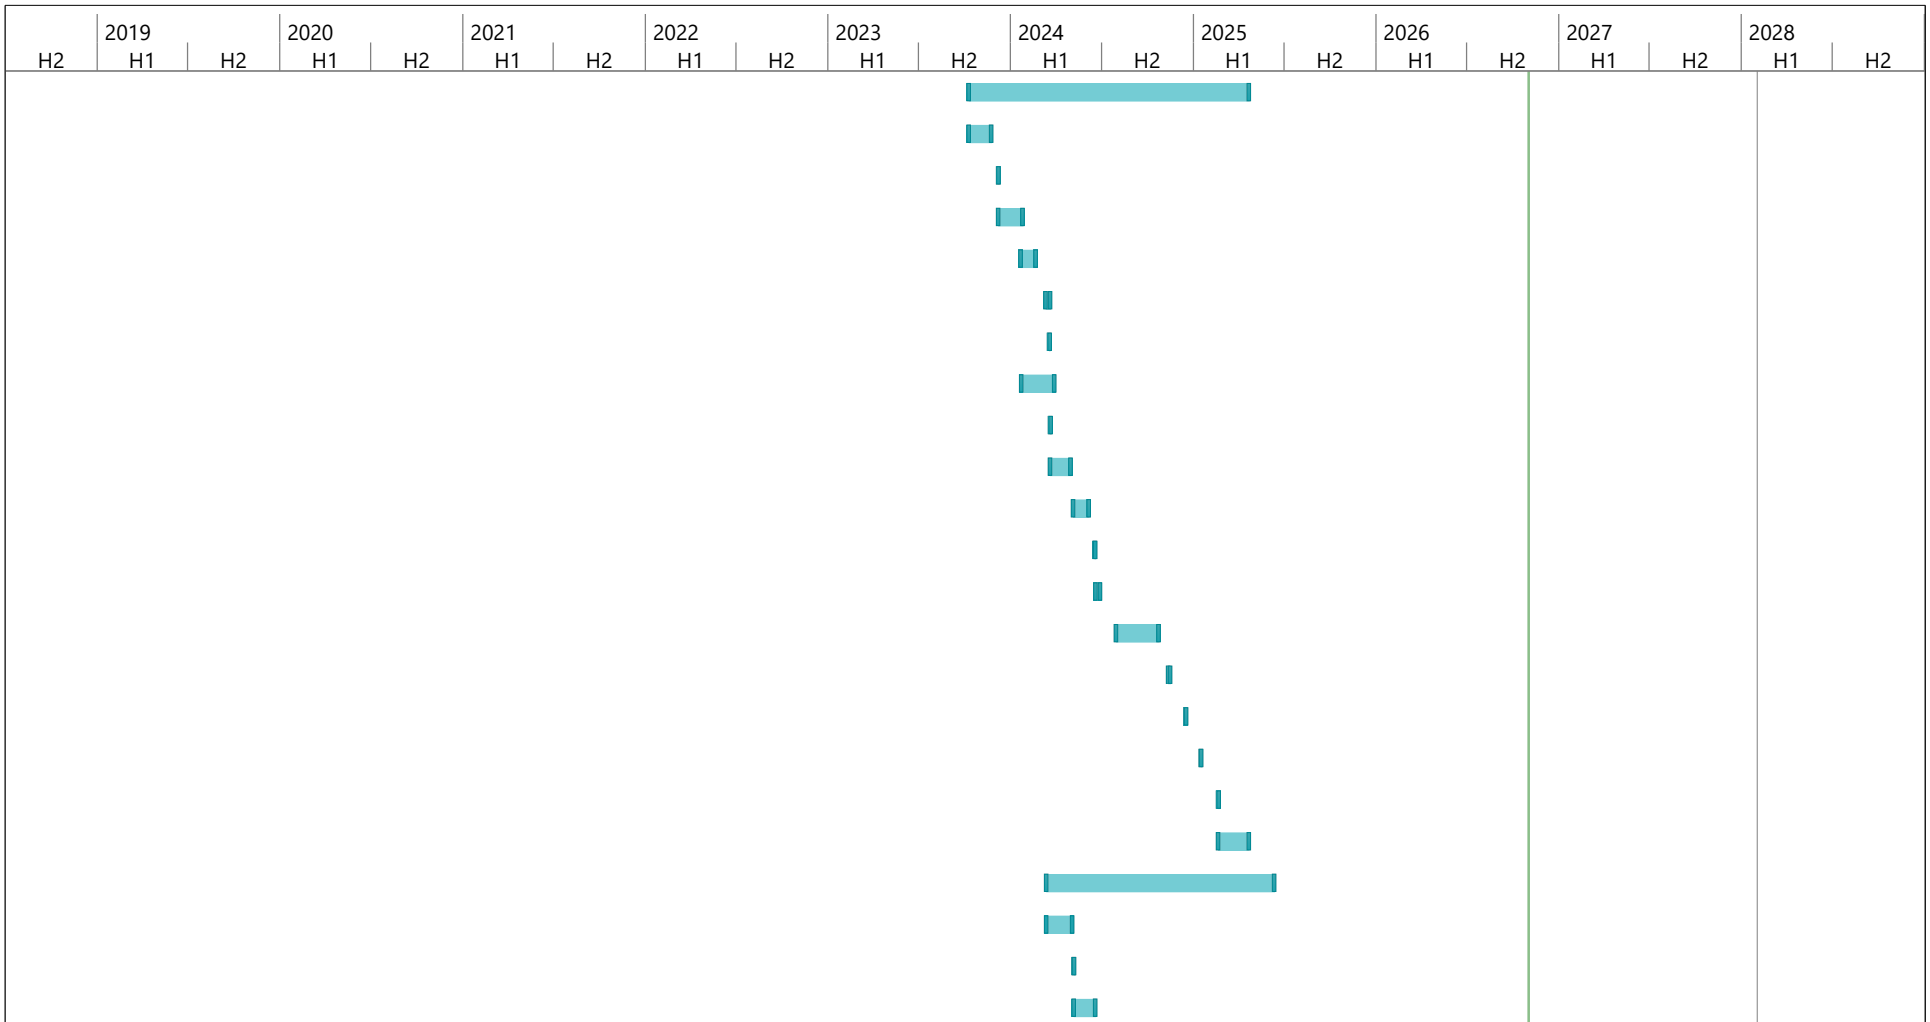


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

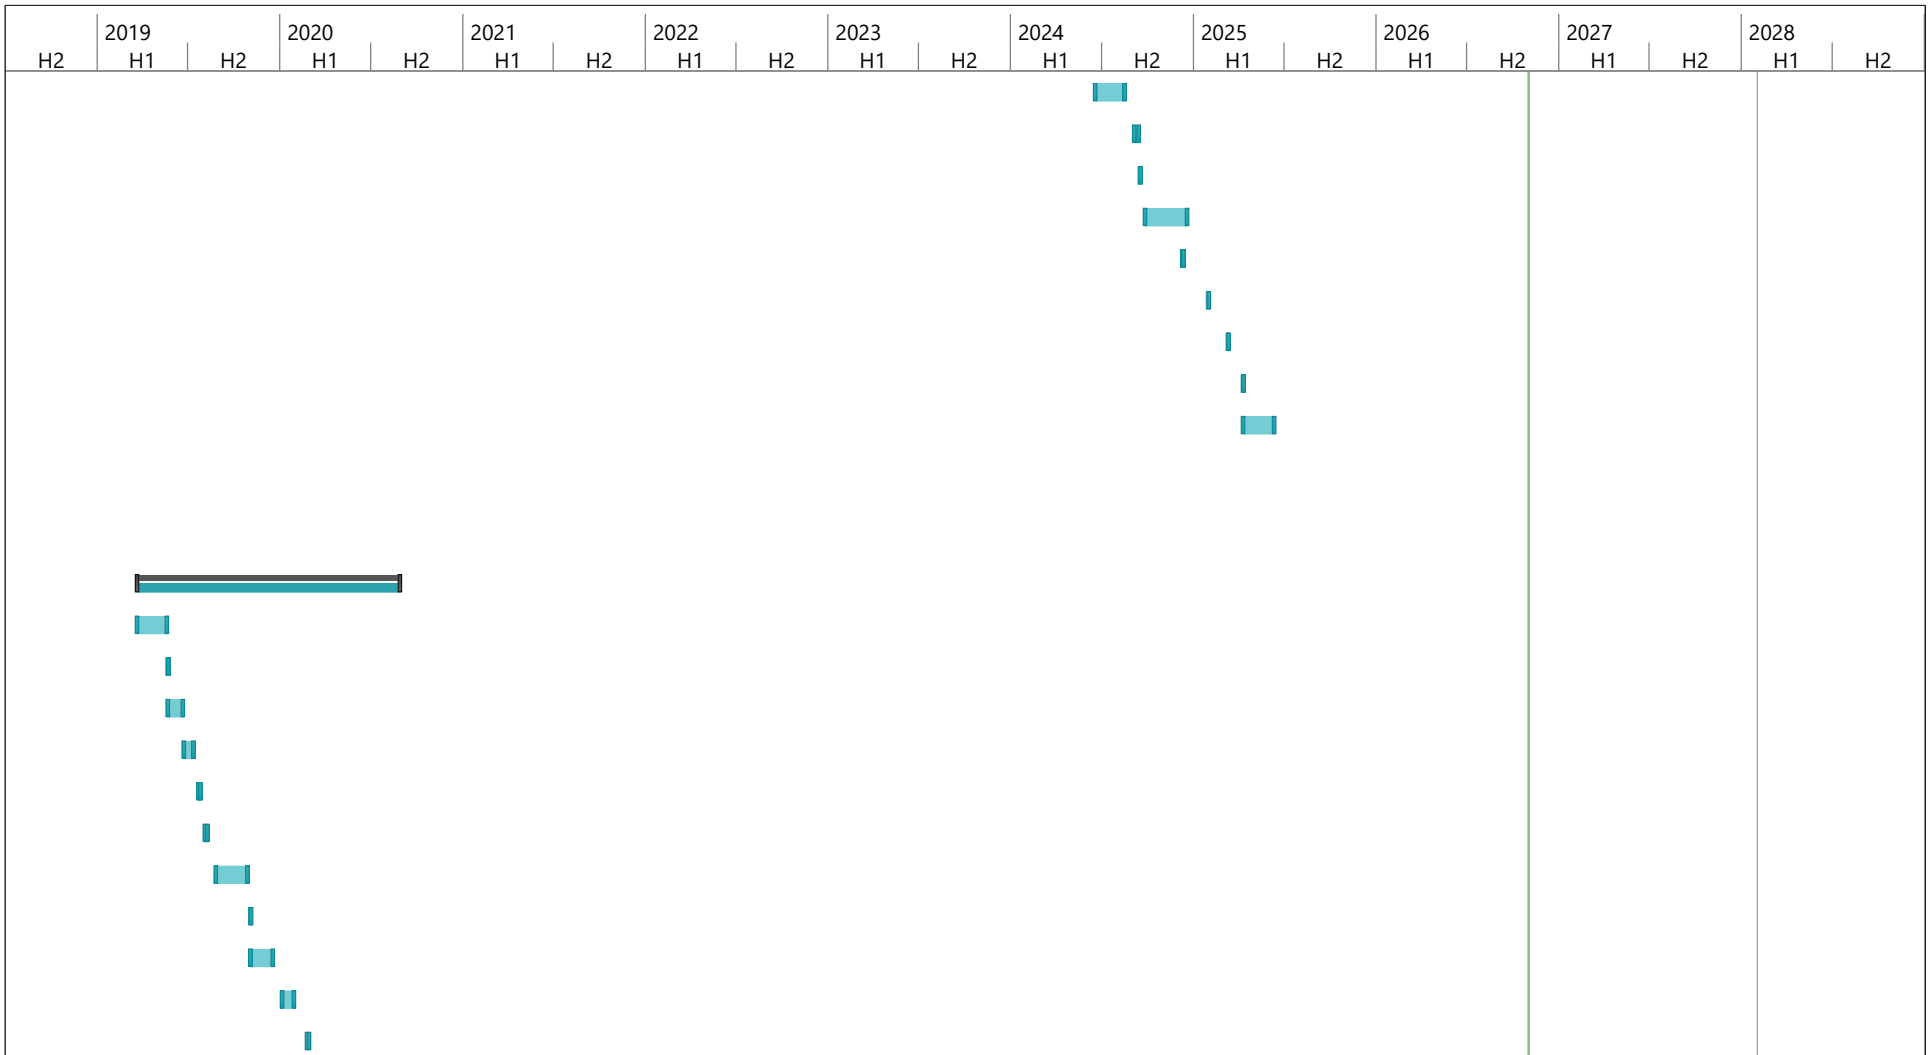


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

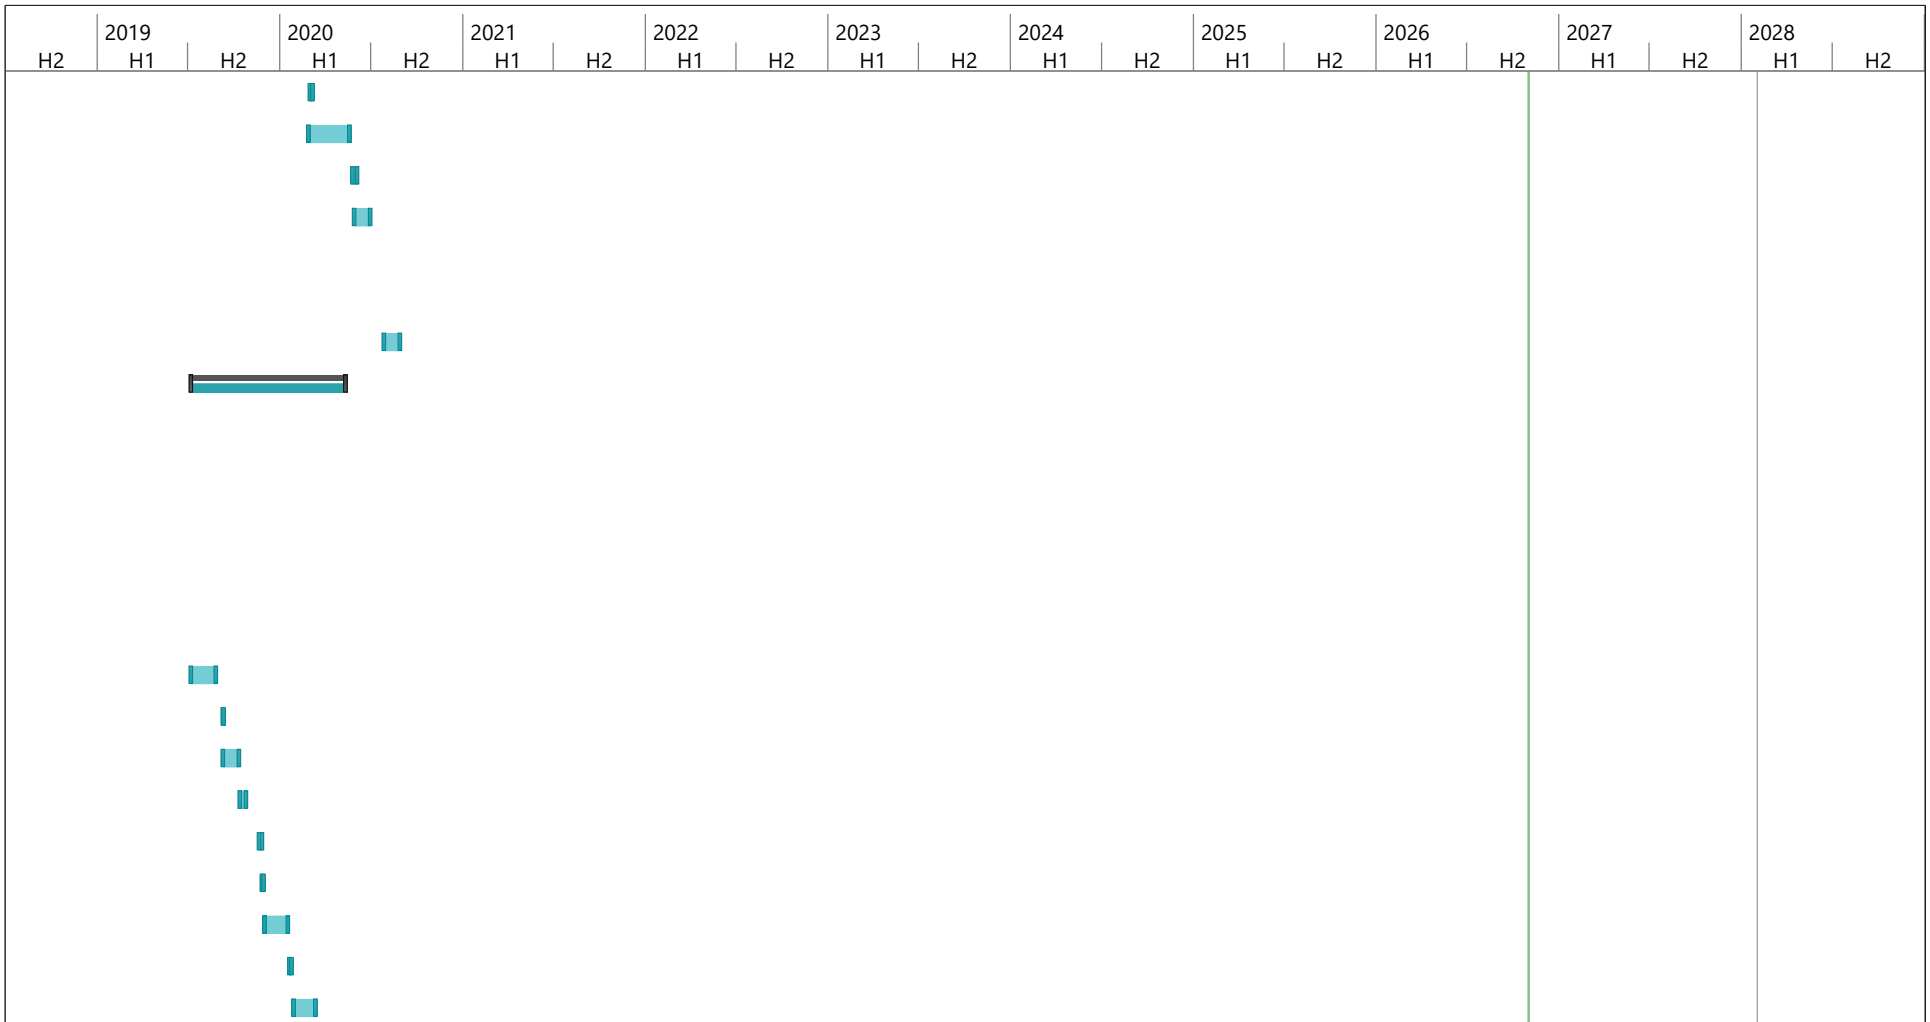


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

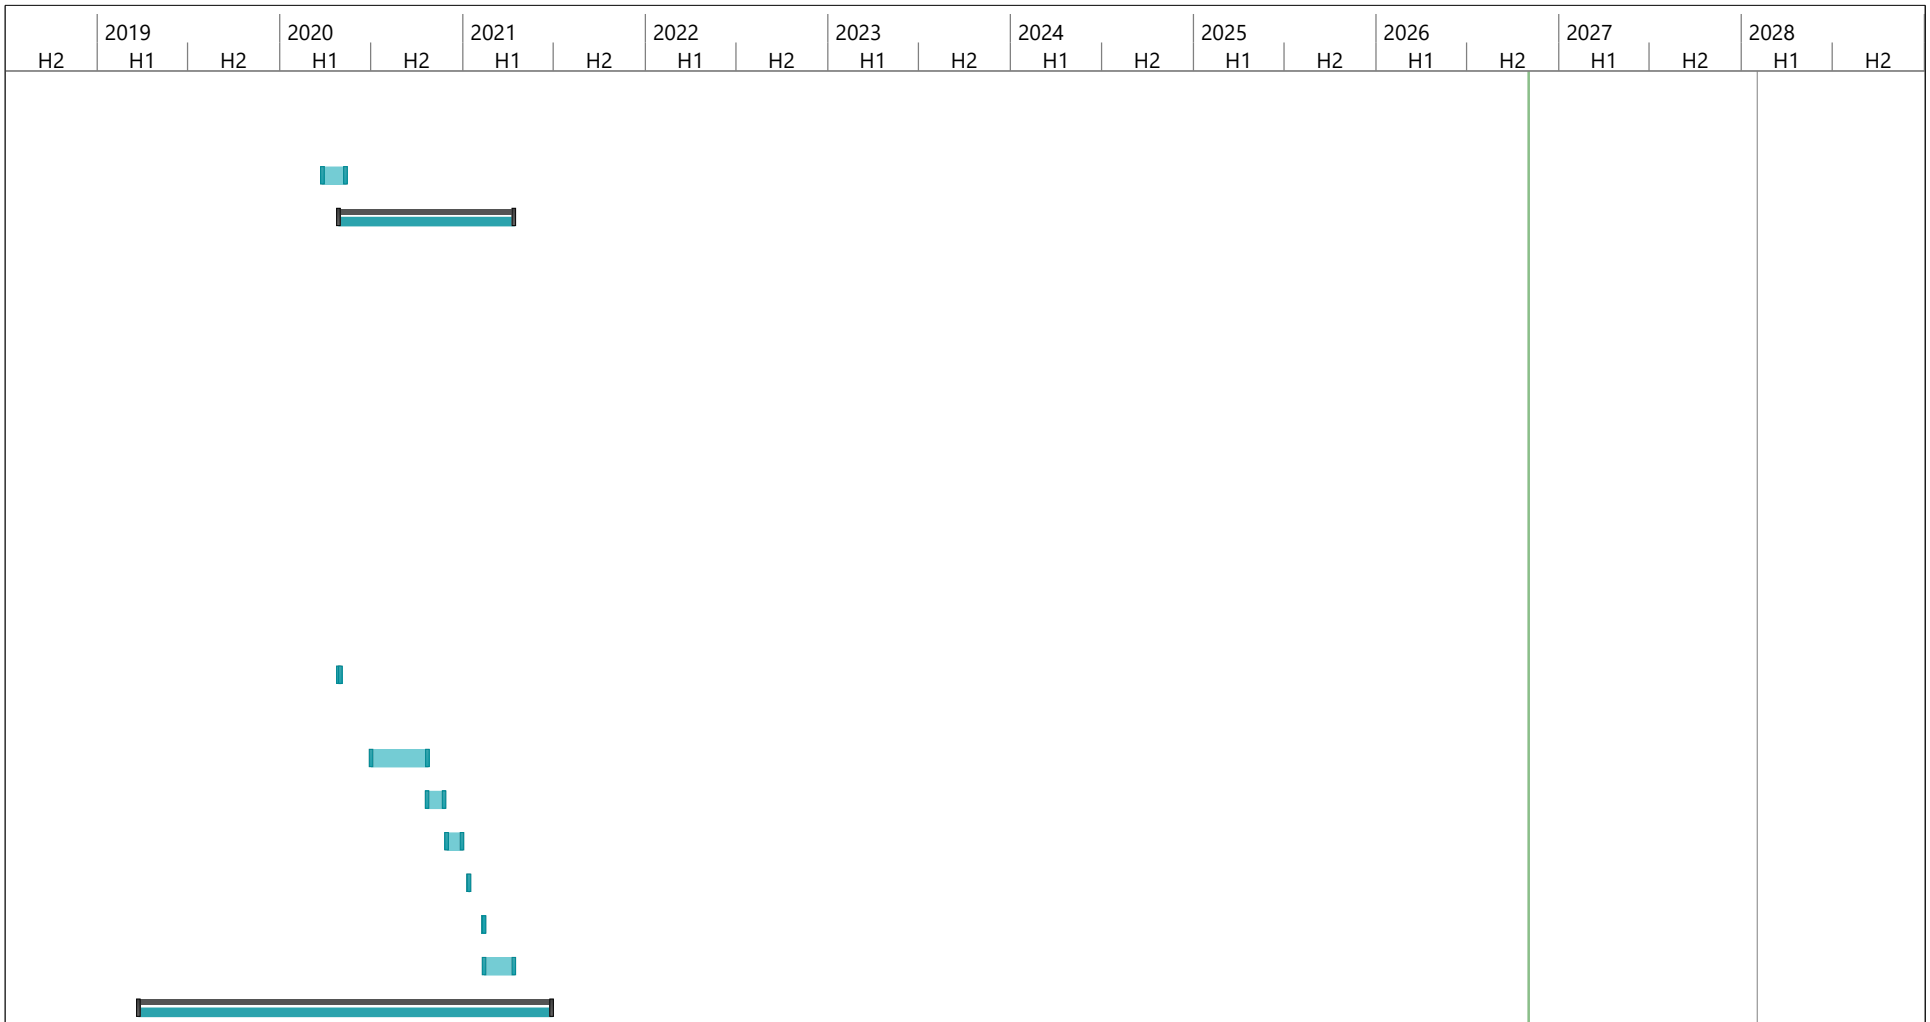


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

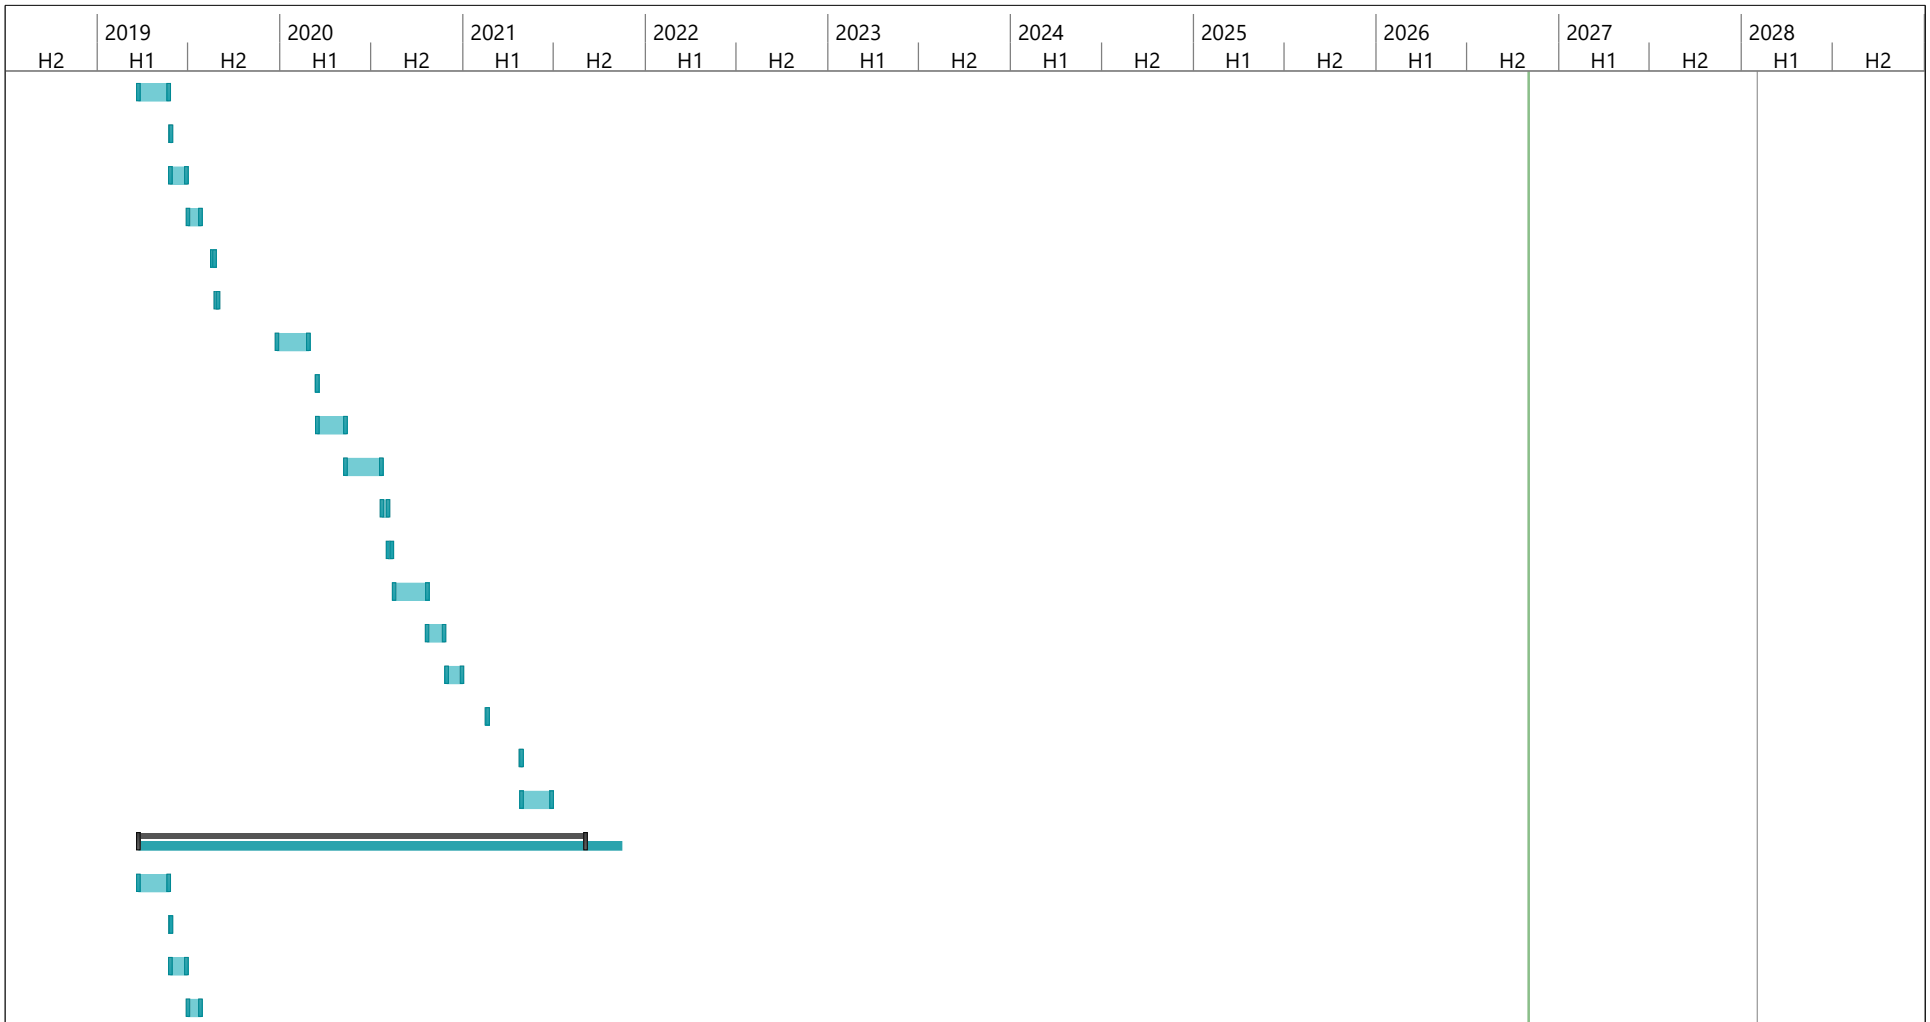


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

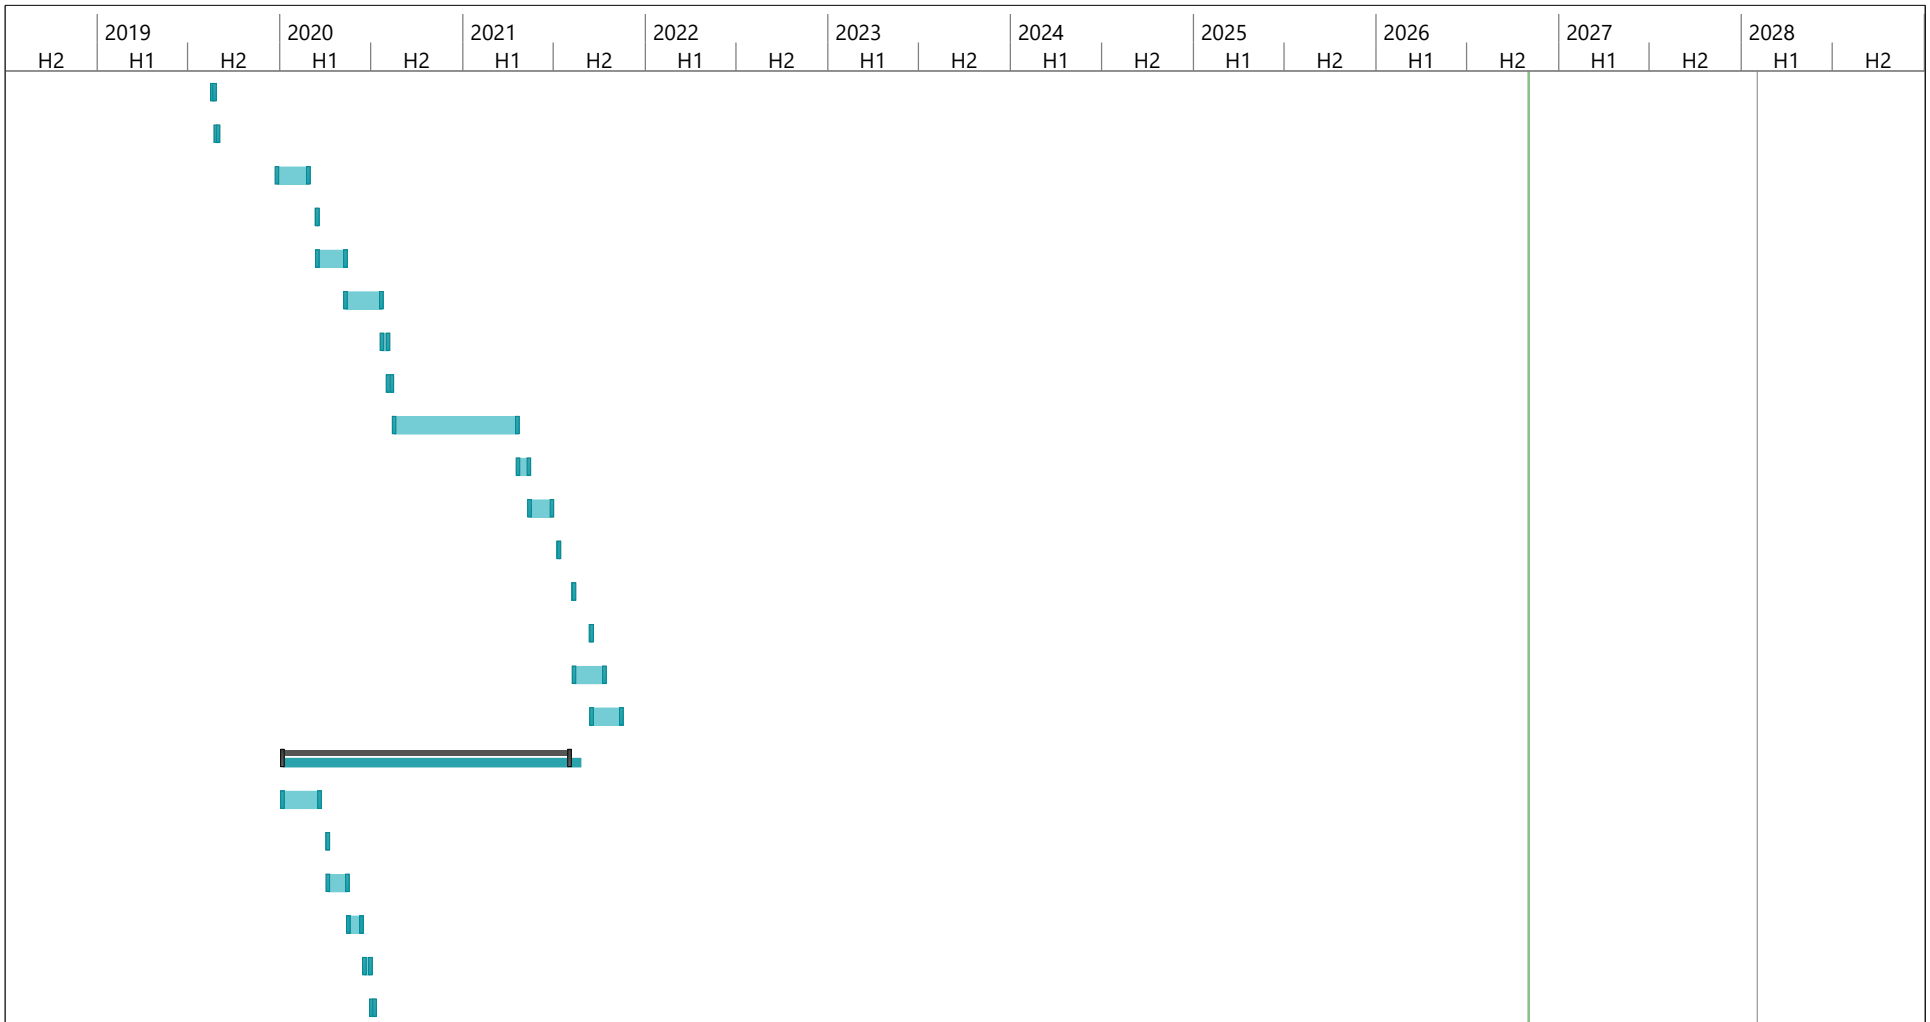


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

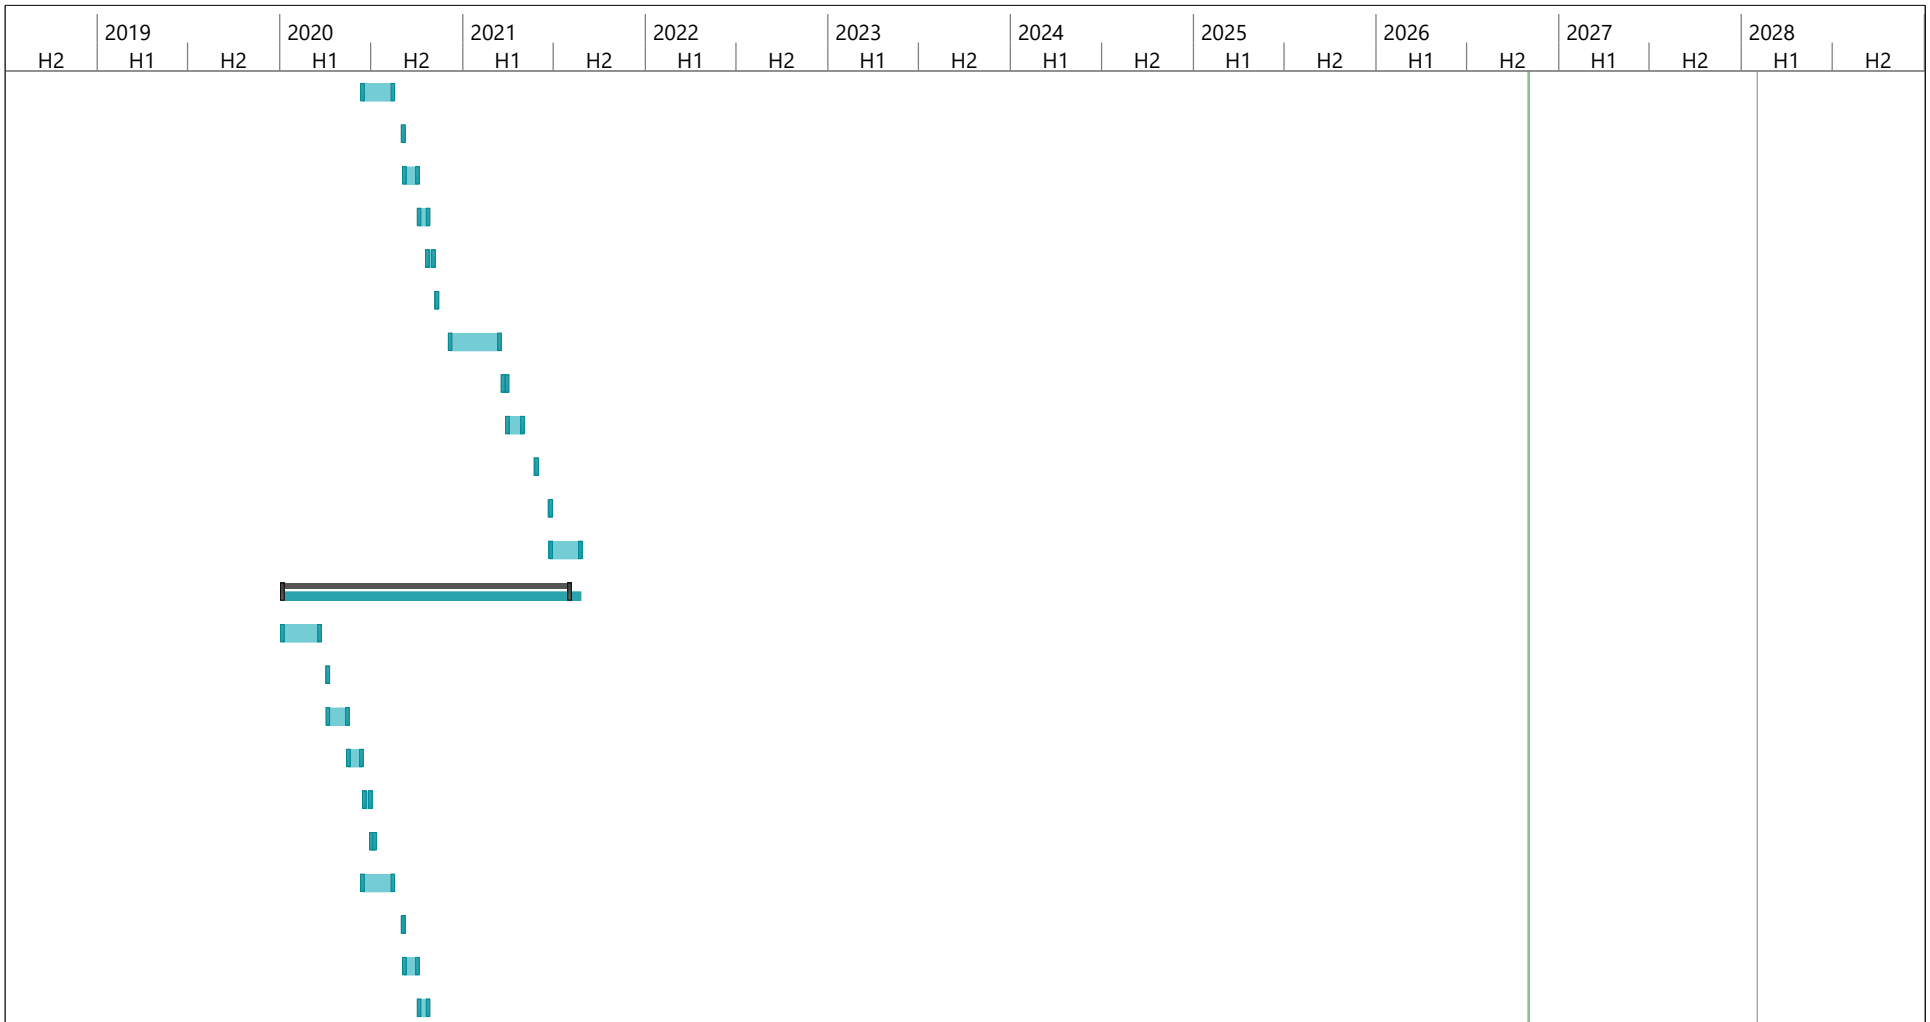


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

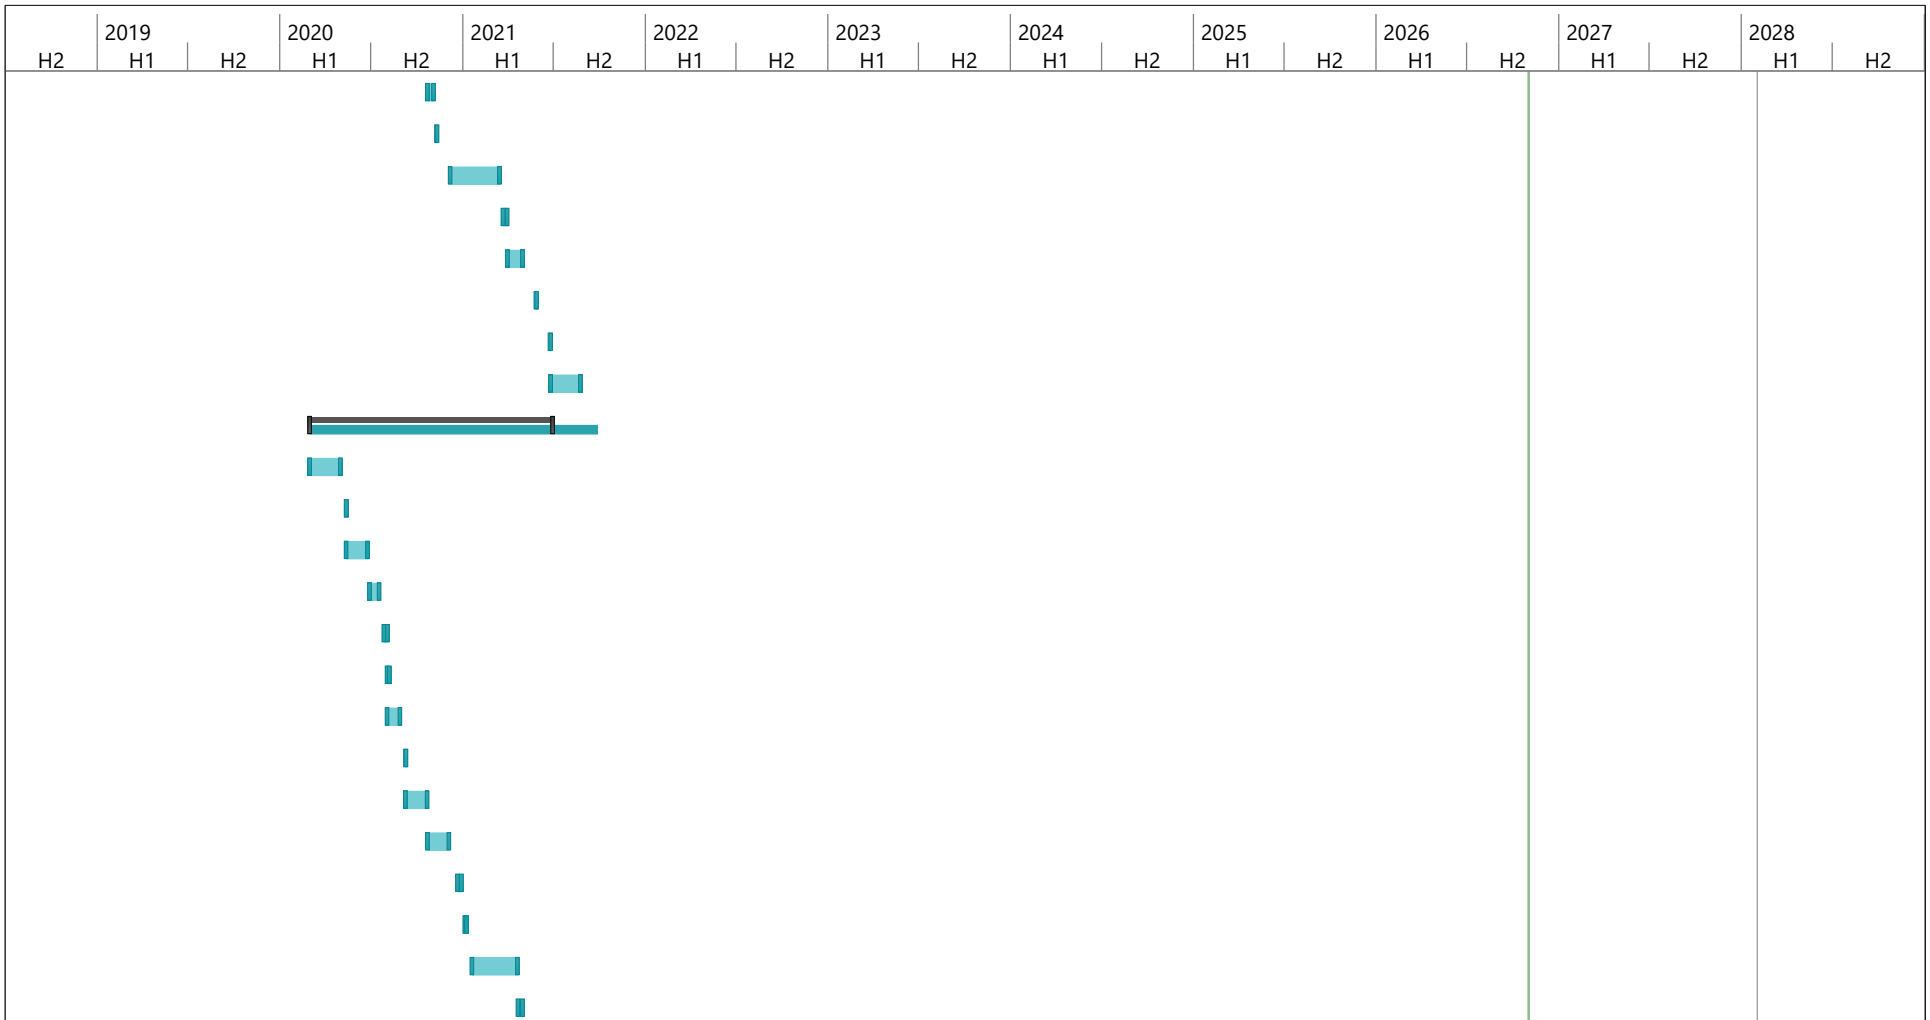


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

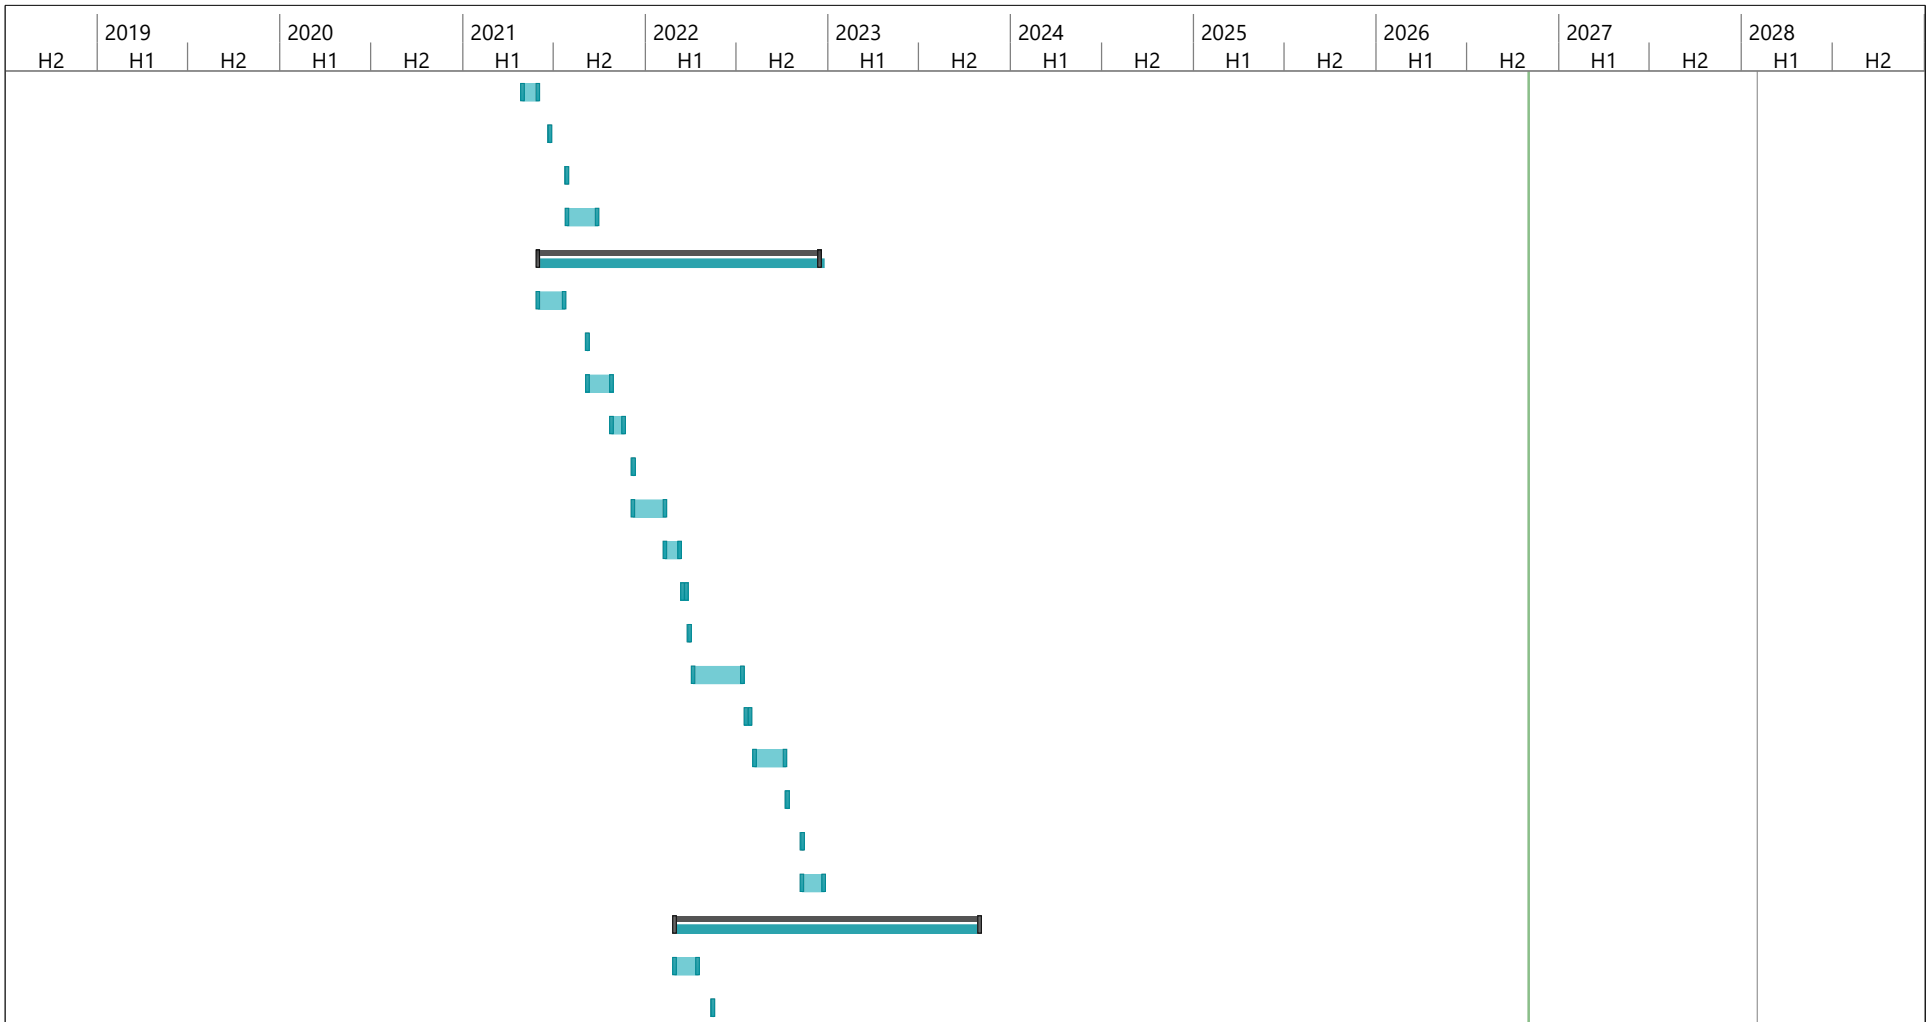


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

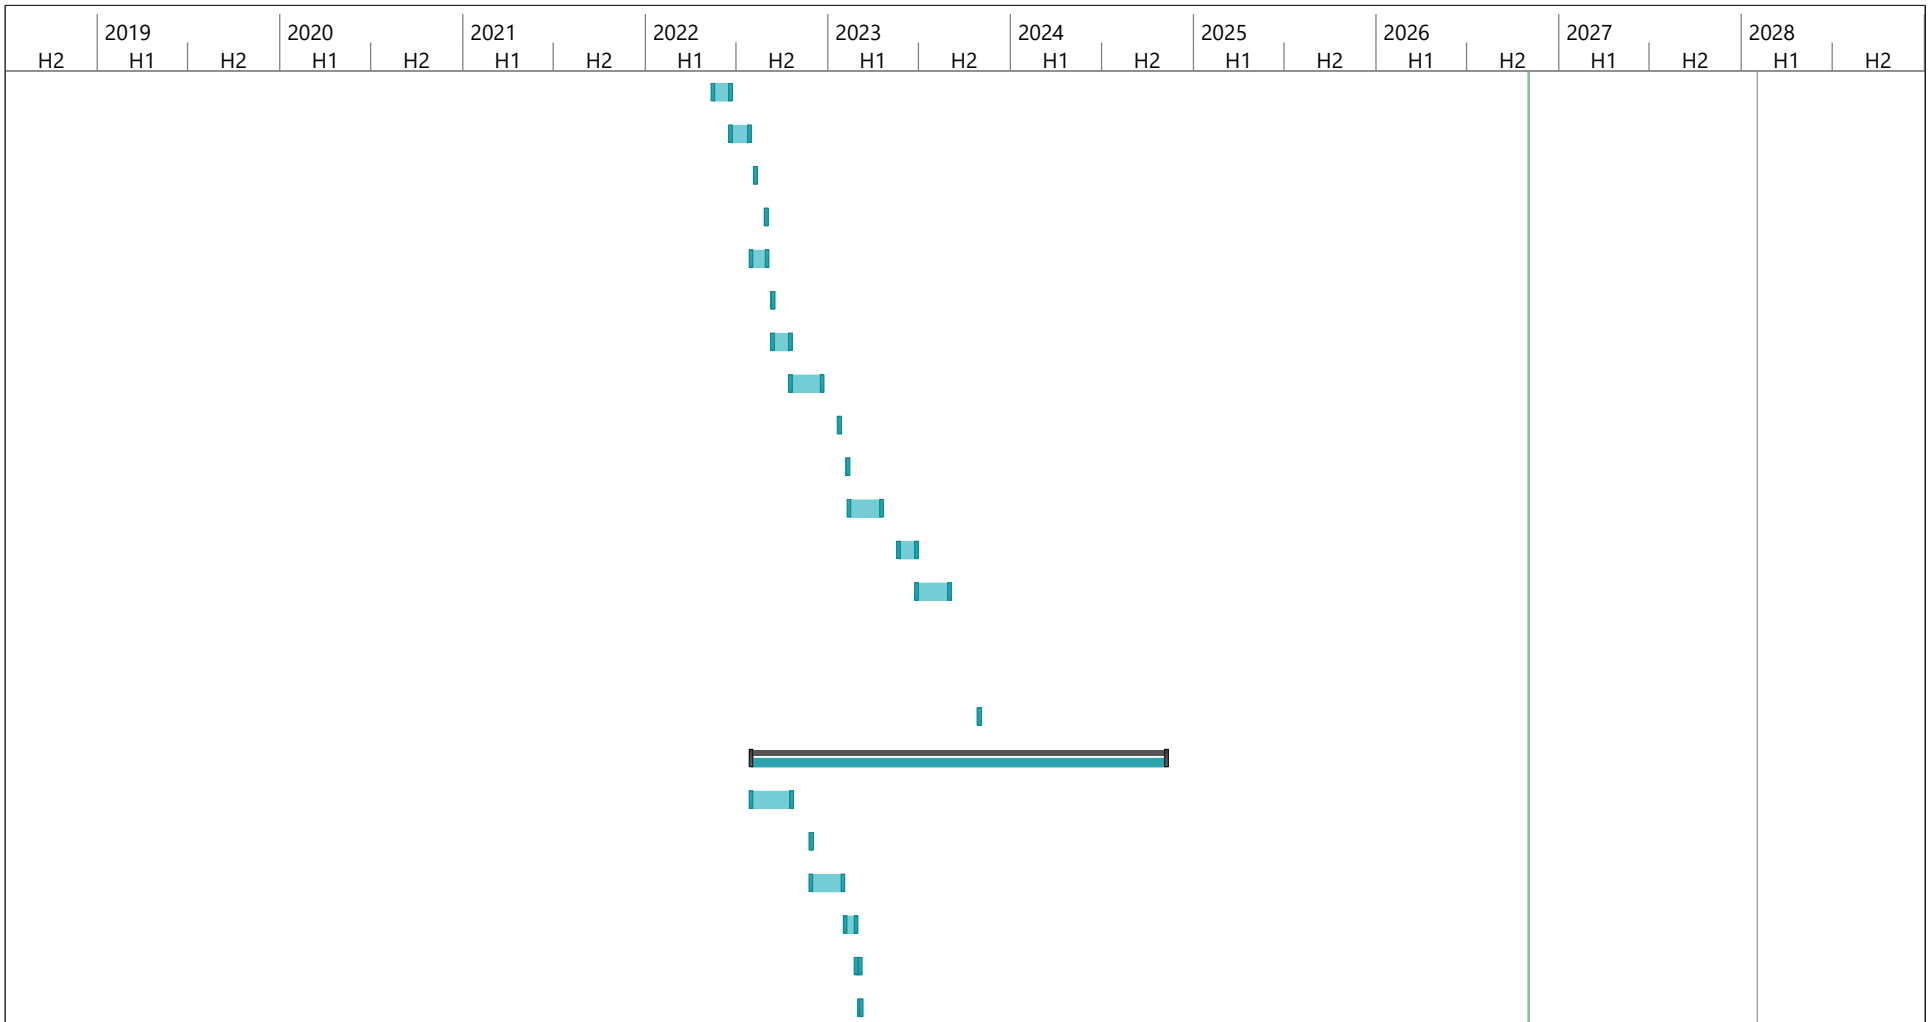


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

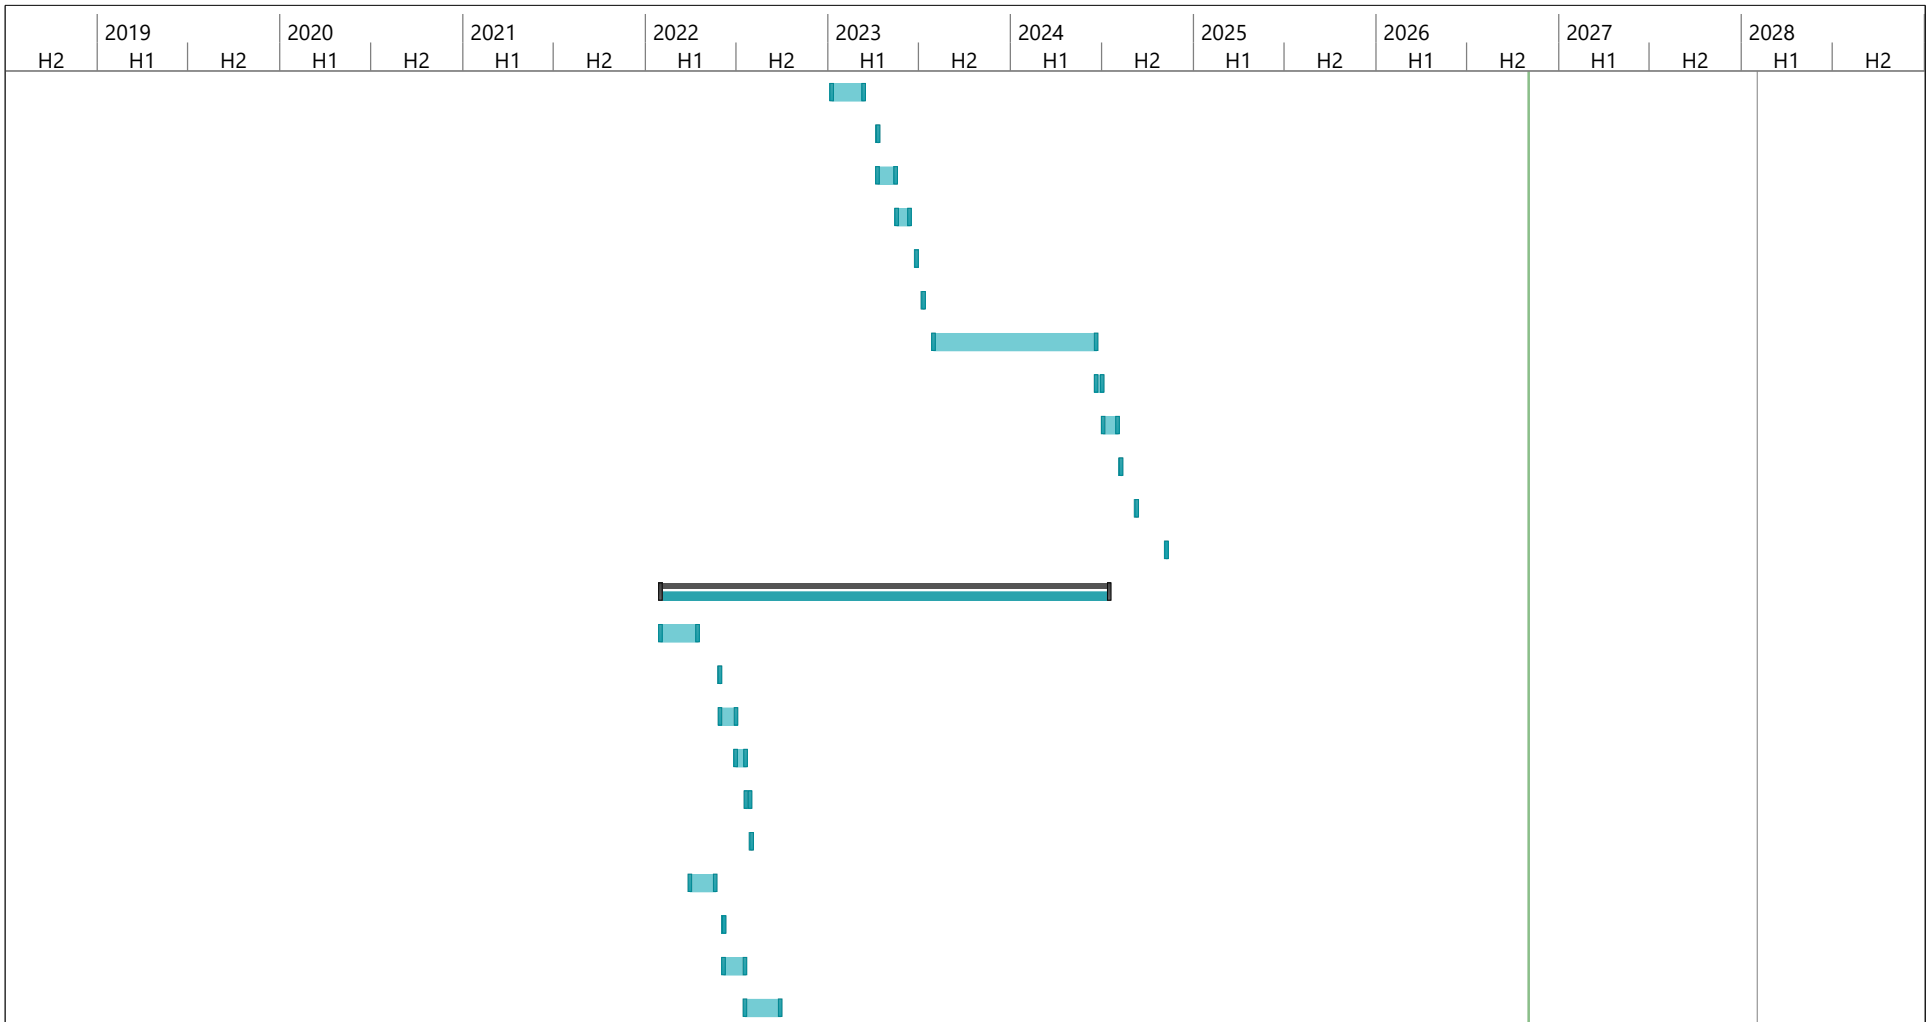


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

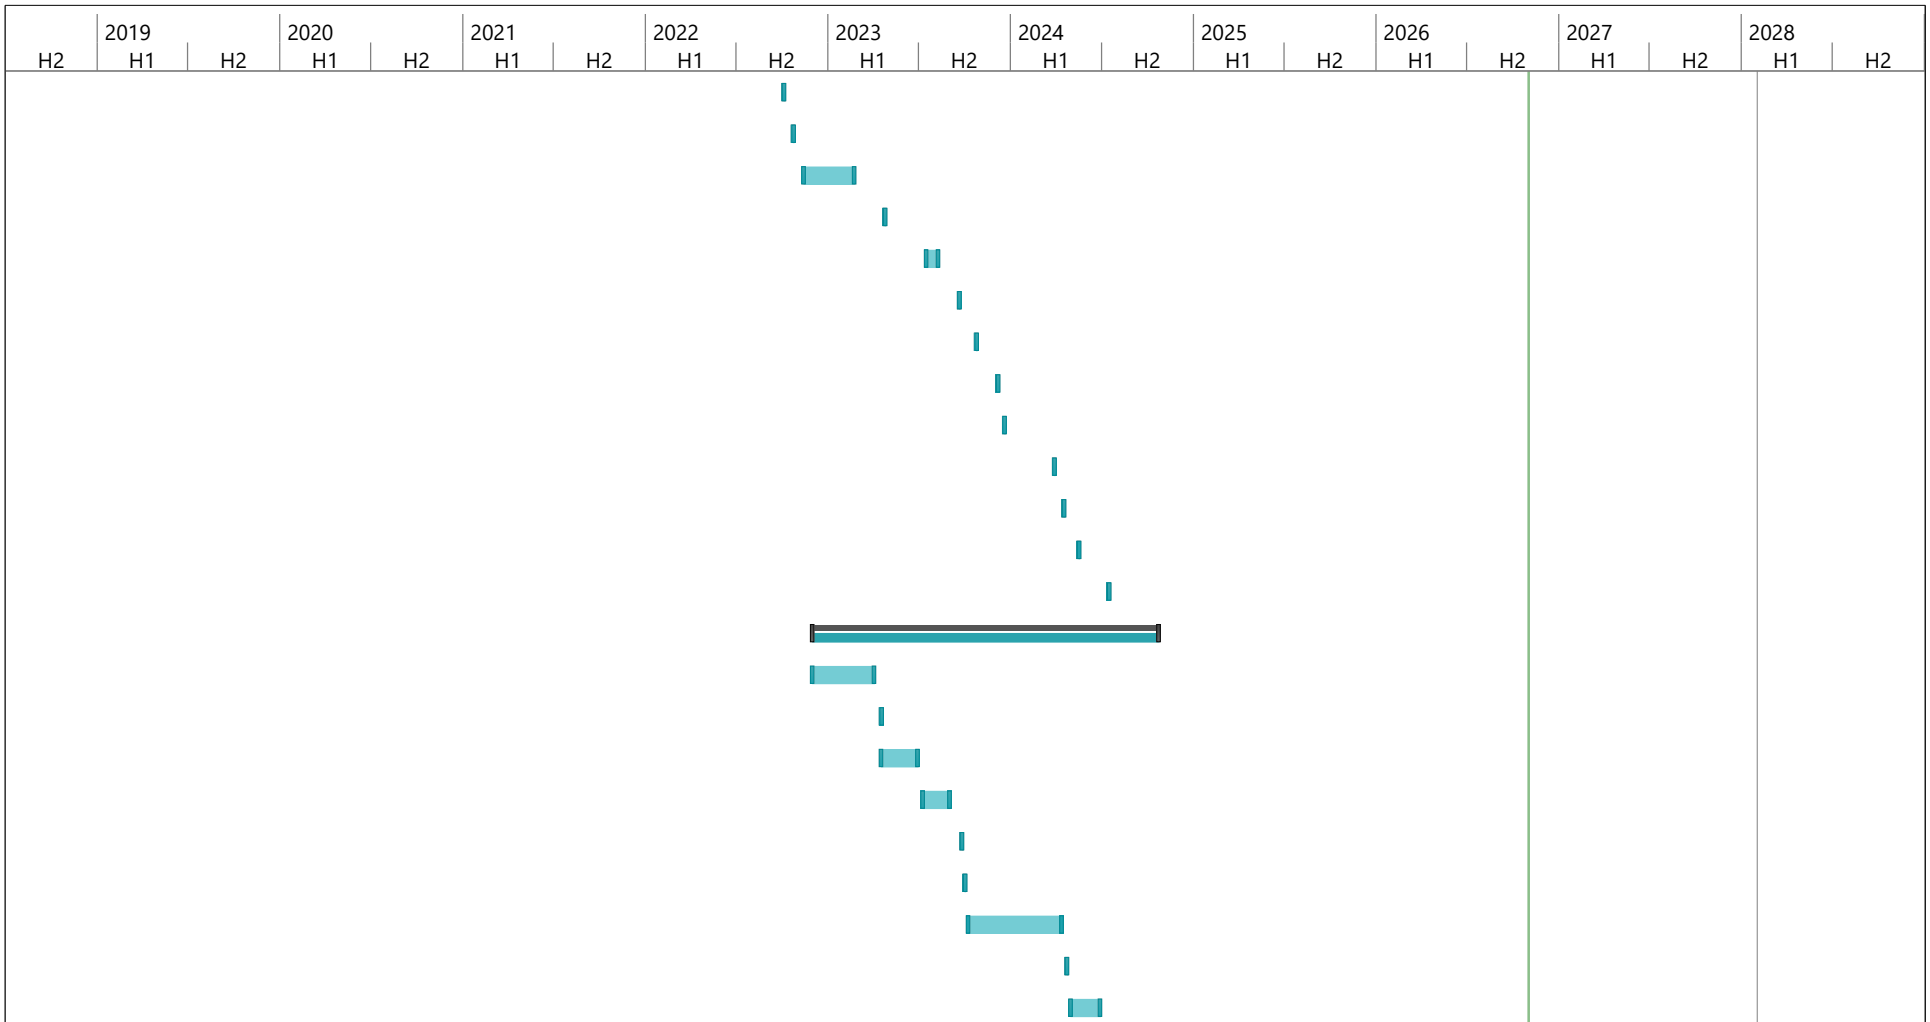

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

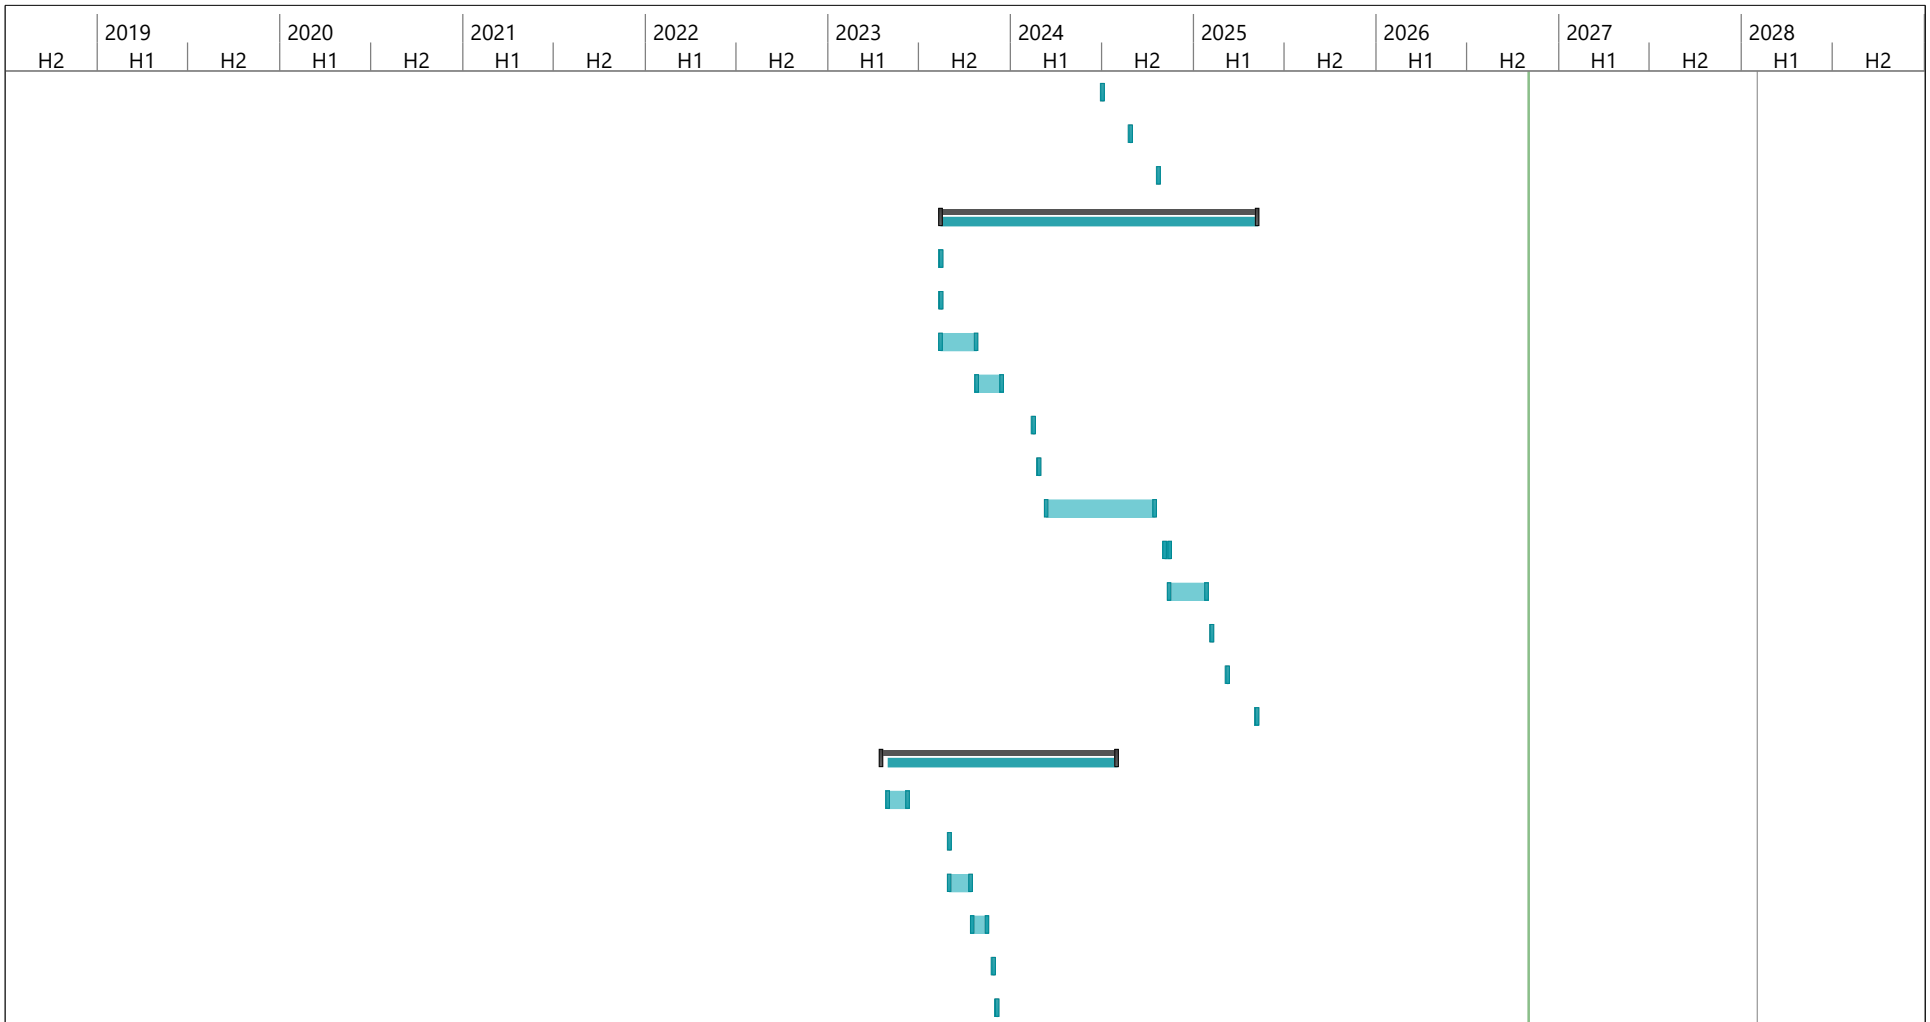


Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	




Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

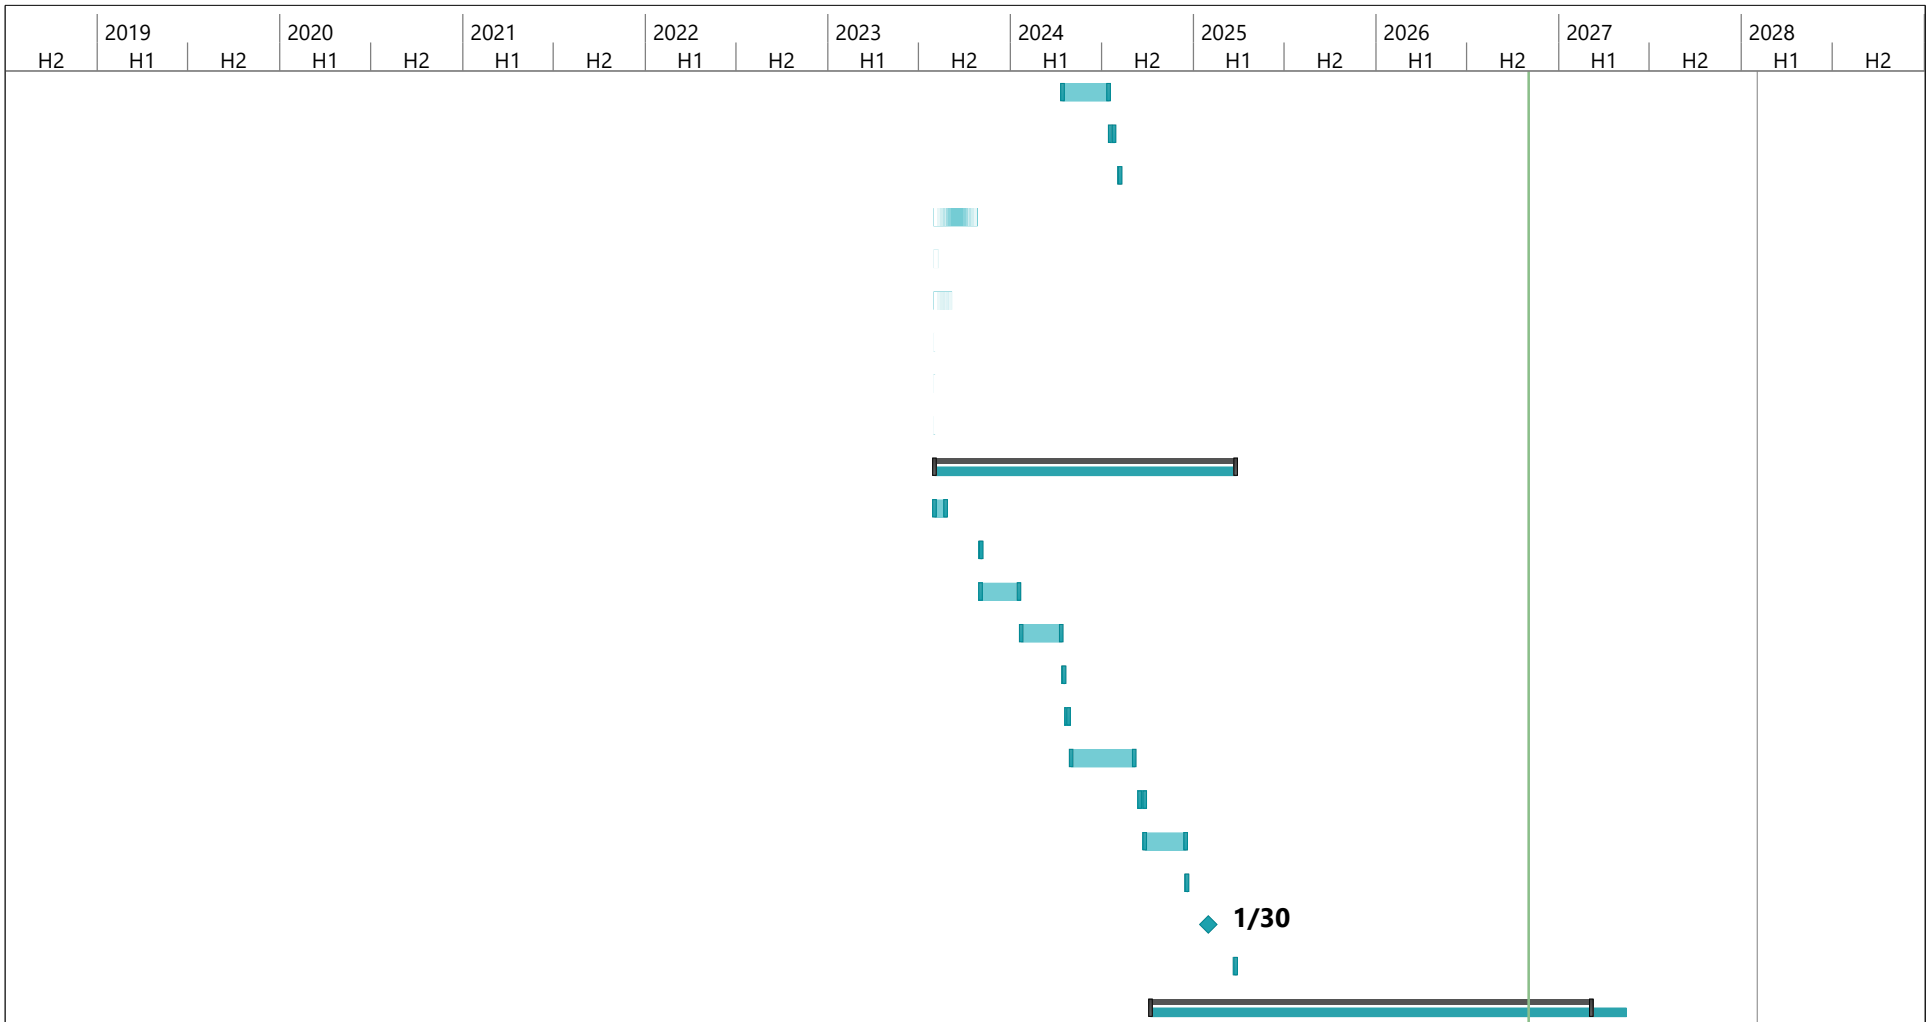

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

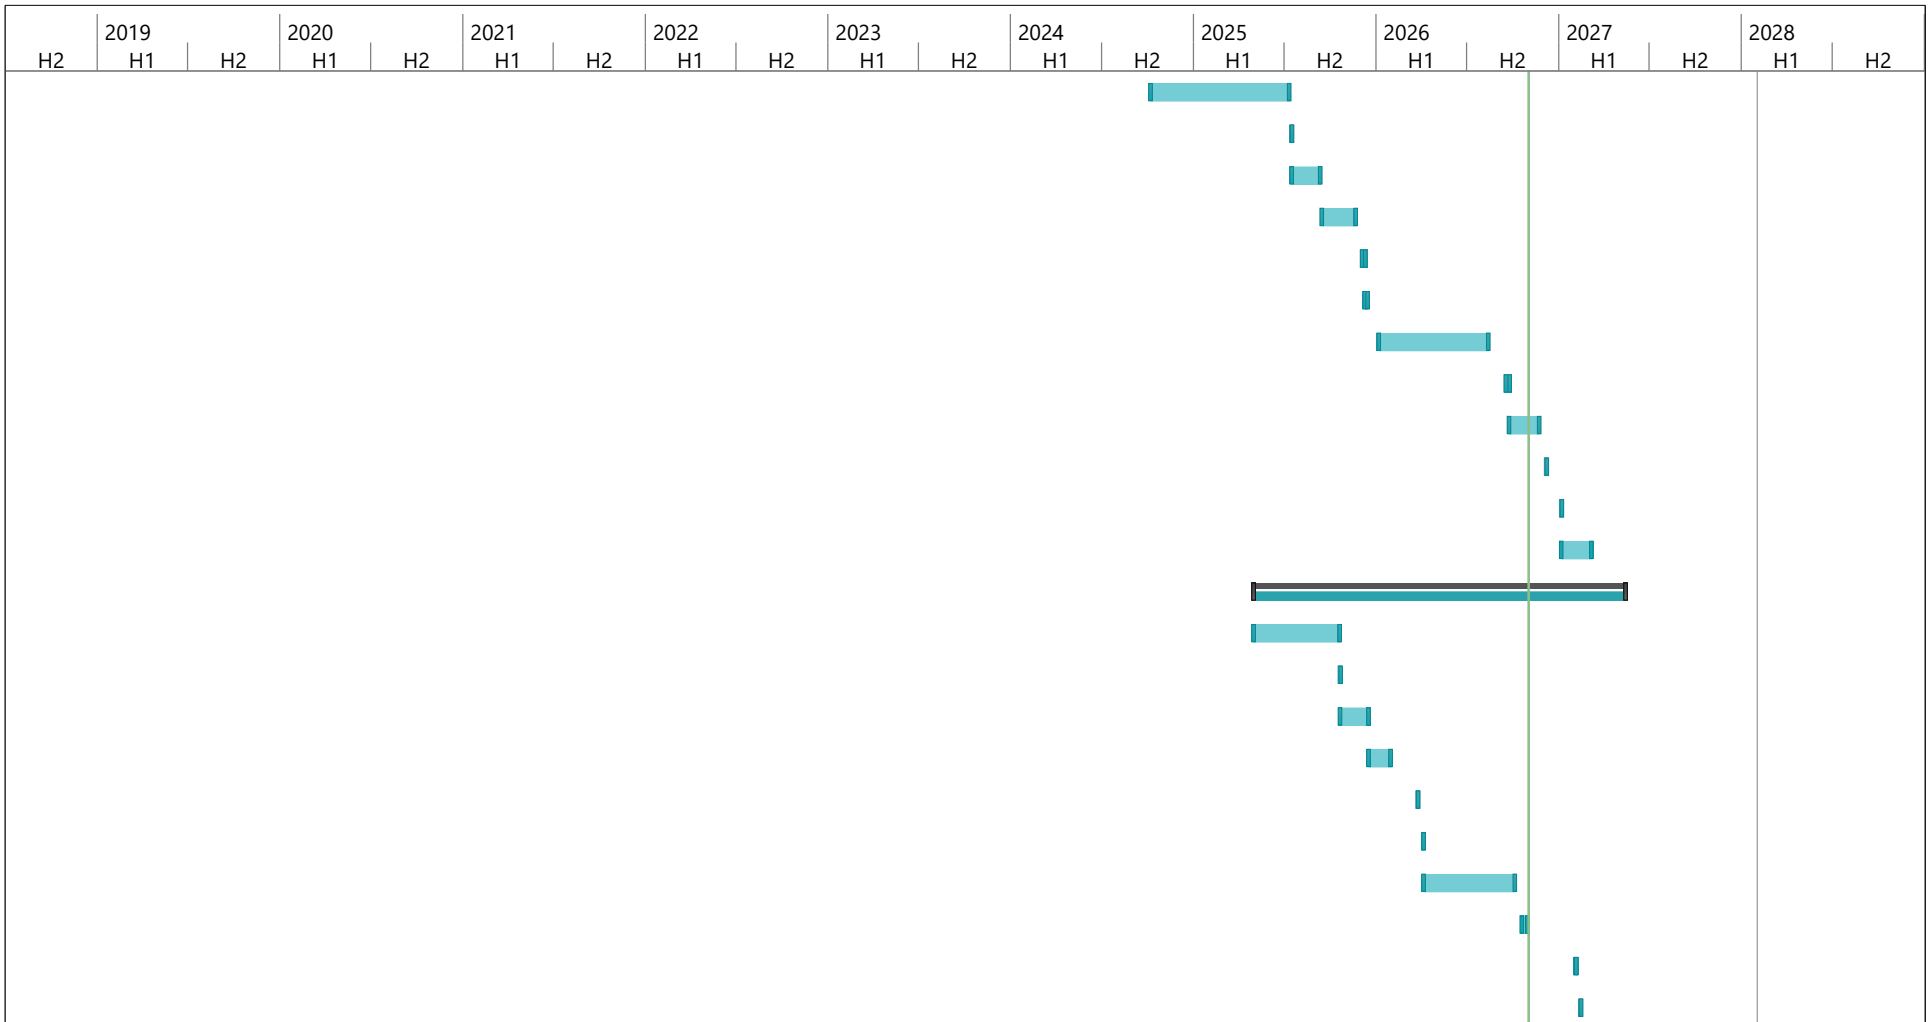

Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Mon 11/2/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
